

Sengupta, Abhijit

From: Williams, Charles R. [Charles.Williams@pgnmail.com]
Sent: Thursday, January 14, 2010 7:16 AM
To: Lake, Louis; Thomas, George
Subject: FW: 01-14-10 Containment Repair Project Level 3 schedule
Attachments: 01-14-10 Level 3 Rev D - 11x17.pdf - 12 pages

FYI

From: Goering, Calvin
Sent: Wednesday, January 13, 2010 7:19 PM
To: Fagan, Paul; Dyksterhouse, Don; Williams, Charles R.; Ortalan, Emin; Miller, Garry; Bell, Robert; Tobin, Larry; Pugh, C-Glenn; Mallner, Aaron; McEwan, Ken
Subject: 01-14-10 Containment Repair Project Level 3 schedule


Please find attached a copy of the Containment Repair Project Level 3 schedule as of this morning for your information.

Also, please note that this schedule is now in Progress Reporter and that progress should be reported each day prior to 14:00. If you need to make significant changes or changes that will impact a deliverable, please let Paul Fagan know so he can be prepared to discuss them at the morning schedule review meeting with the Project team.

Please notify me of any changes that need to be made as soon they are determined, thanks.


Cal Goering
CR3 CRT Project Scheduler
352-563-2943 Ext 4186

CR3 NPC Outage Containment Repair Project - Level 3 Schedule

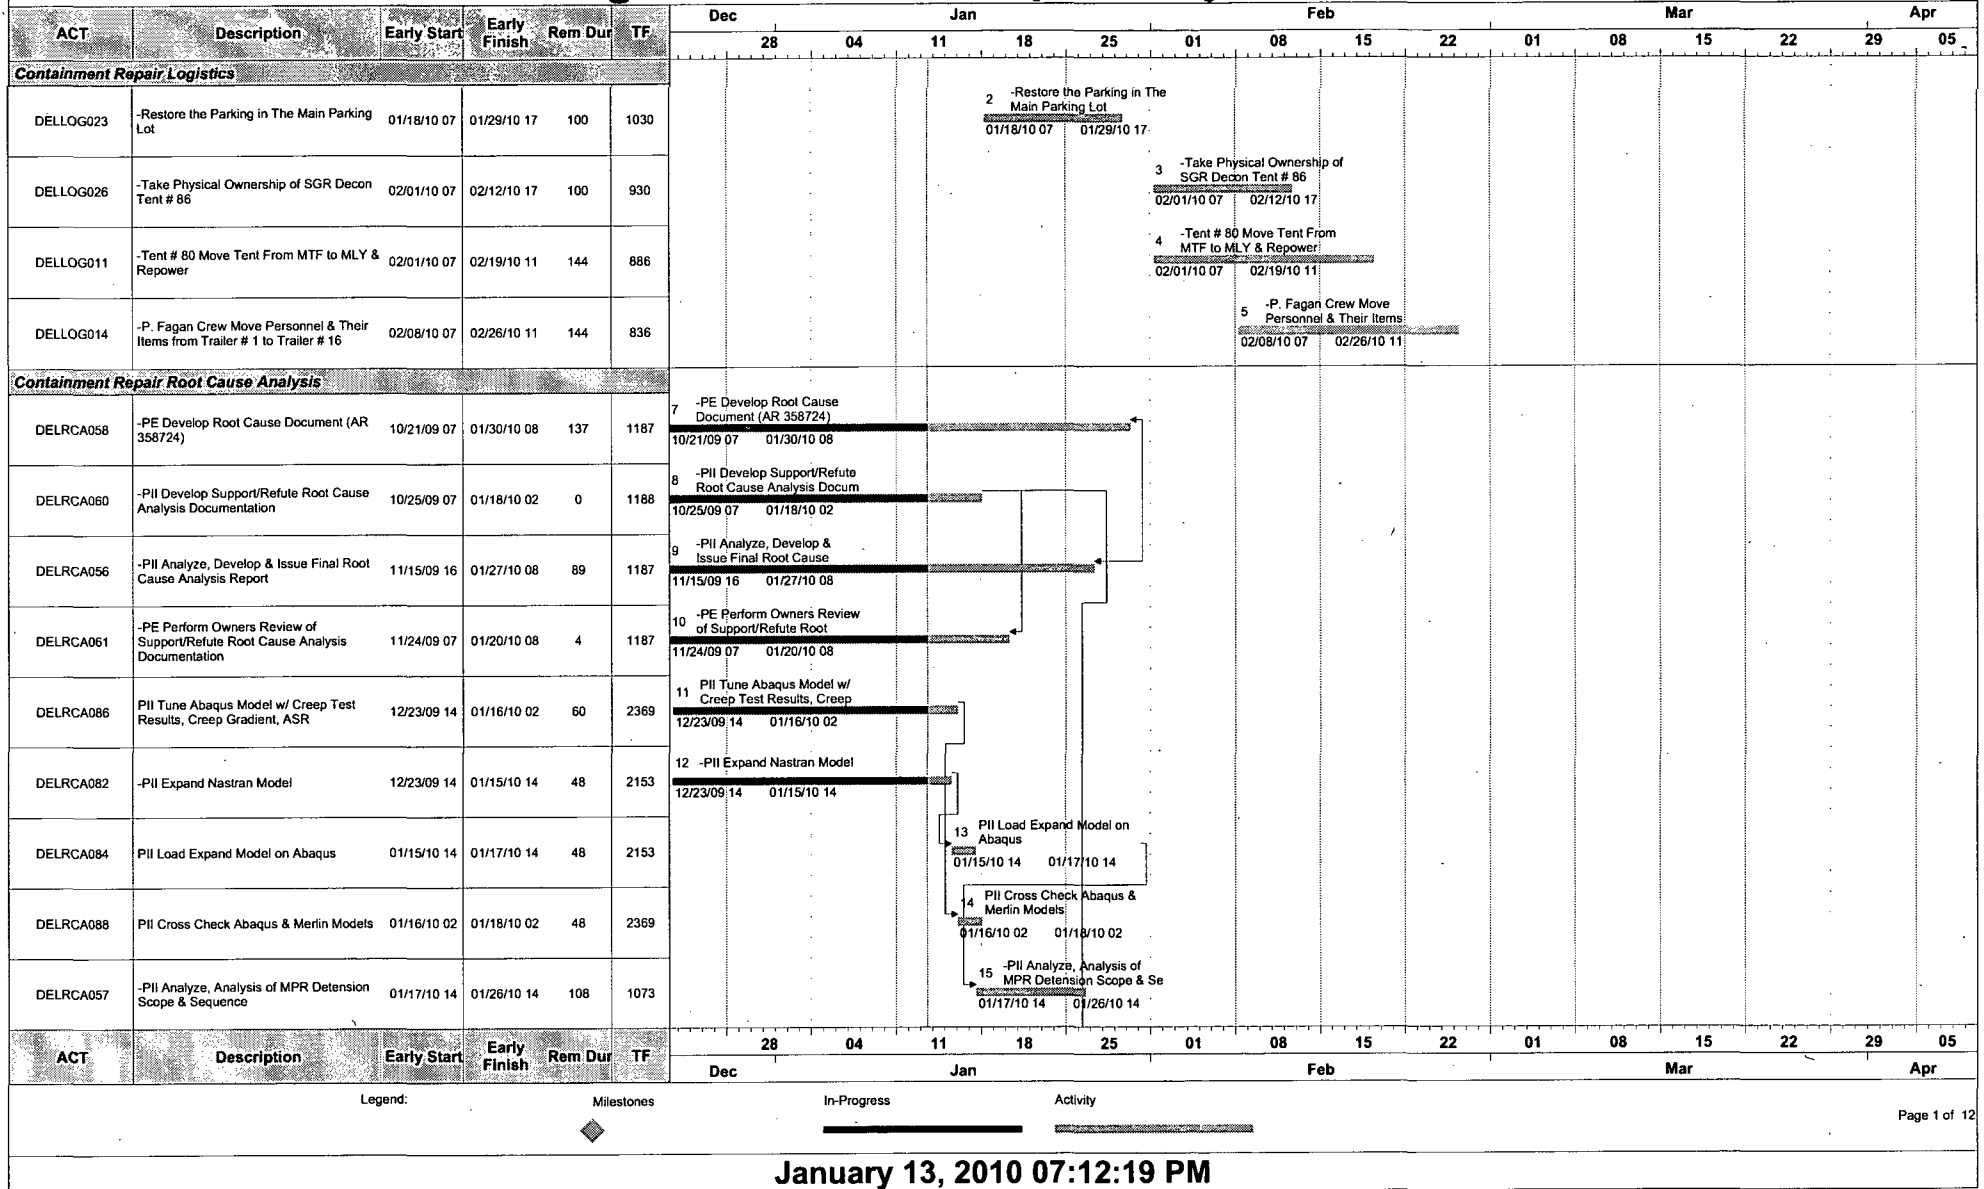

January 13, 2010 07:12:19 PM

CR3 NPC Outage Containment Repair Project - Level 3 Schedule

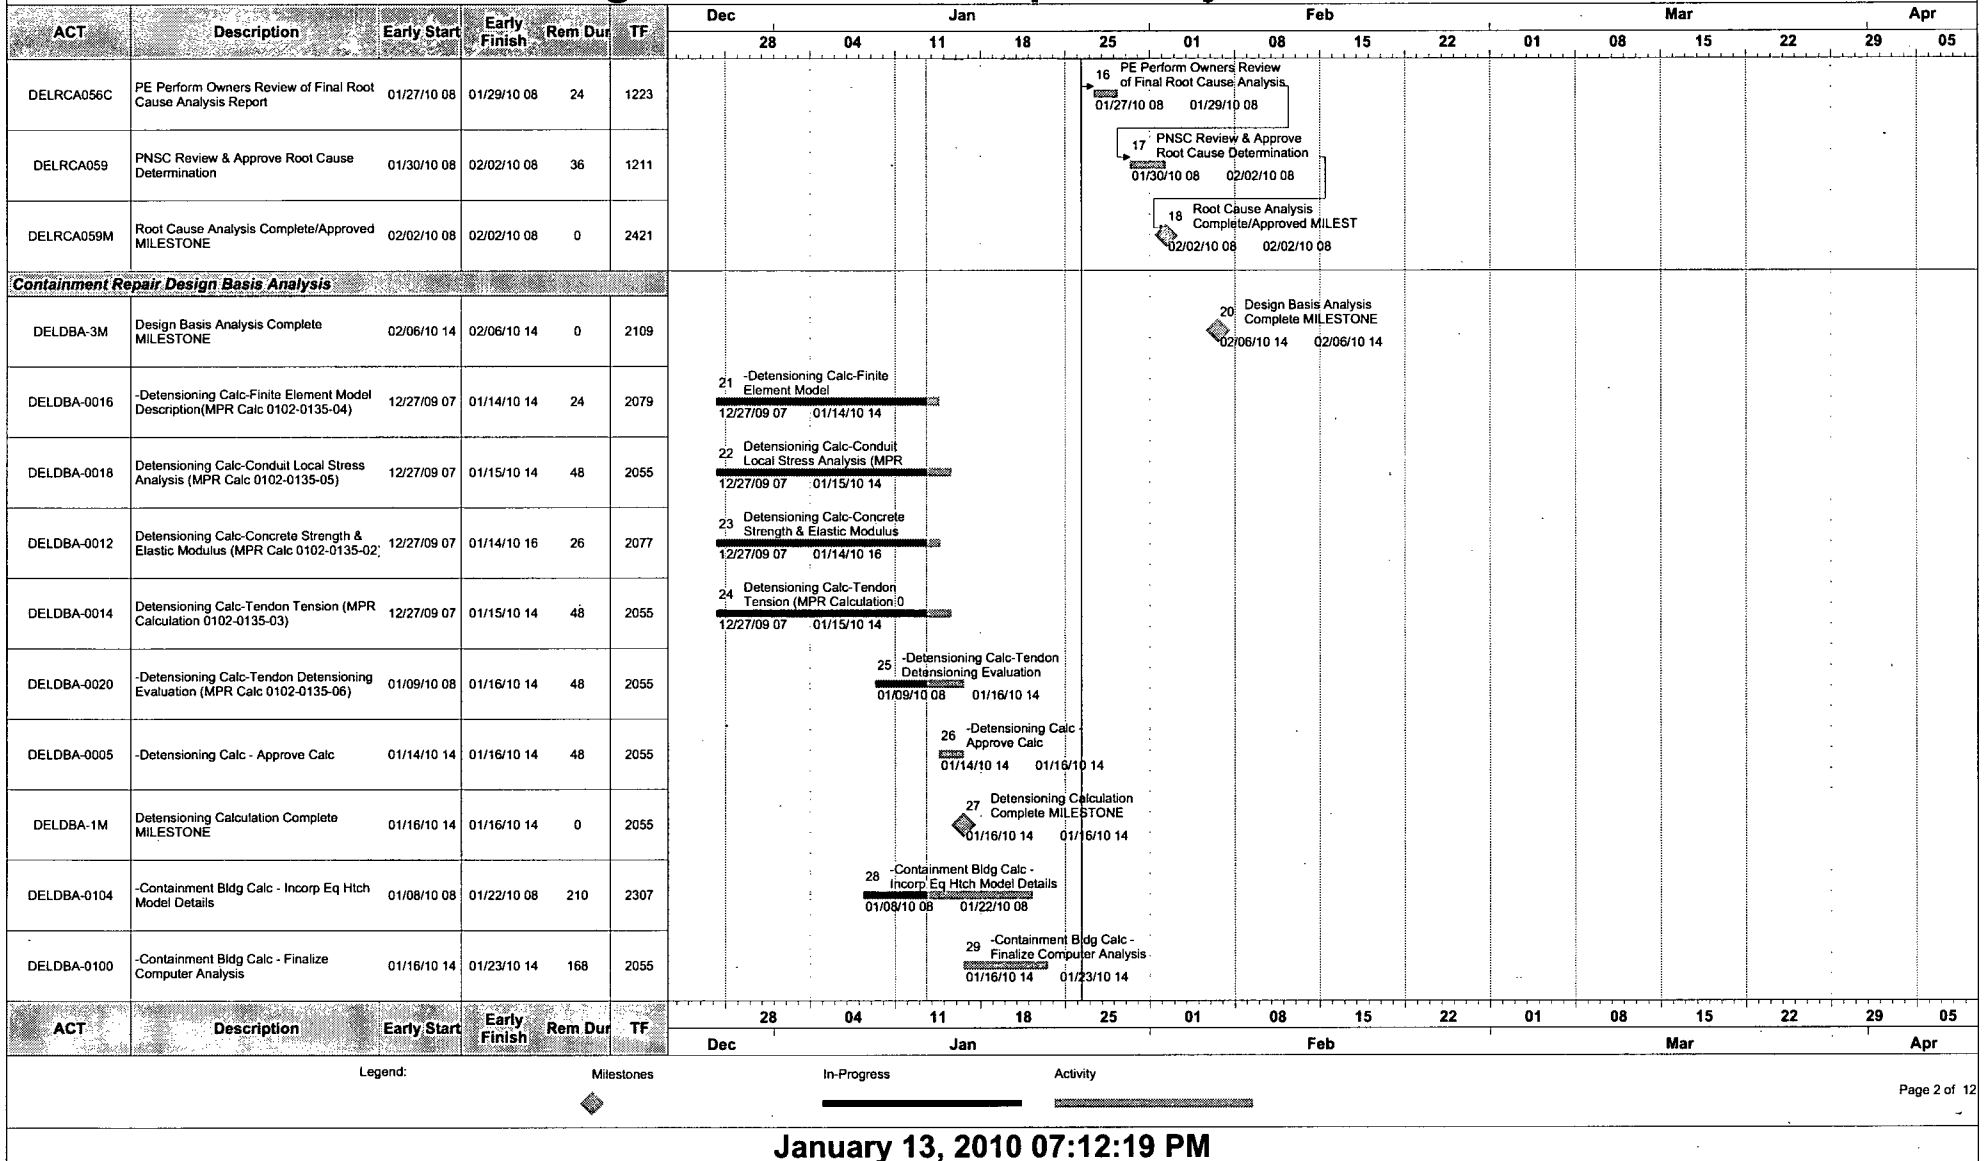

CR3 NPC Outage Containment Repair Project - Level 3 Schedule

ACT	Description	Early Start	Early Finish	Rem Dur	TF	Dec	Jan	Feb	Mar	Apr
DELDDBA-0101	-Containment Bldg Calc - Compile Calc to be Ready for Review/Verification	01/23/10 14	01/30/10 14	168	2055			30 - Containment Bldg Calc - Compile Calc to be Ready 01/23/10 14 01/30/10 14		
DELDDBA-0102	-Containment Bldg Calc - Owners Review/Verification	01/30/10 14	02/04/10 14	120	2109			31 - Containment Bldg Calc - Owners Review/Verification 01/30/10 14 02/04/10 14		
DELDDBA-0103	-Containment Bldg Calc - Incorporate Review Comments & Approve	02/04/10 14	02/06/10 14	48	2109			32 - Containment Bldg Calc - Incorporate Review 02/04/10 14 02/06/10 14		
DELDDBA-2M	Containment Bldg Calc Compl MILESTONE	02/06/10 14	02/06/10 14	0	2109			33 - Containment Bldg Calc Compl MILESTONE 02/06/10 14 02/06/10 14		
Containment Repair Implementation Design										
DELDES1M	EC Implementation Design Complete MILESTONE	02/15/10 08	02/15/10 08	0	2651			35 - EC Implementation Design Complete MILESTONE 02/15/10 08 02/15/10 08		
DELDES11710	-EC 75000 PH 1 Concrete Cut: Planning Prepare W/O 01652765 Packages Complete	12/26/09 10	01/15/10 07	41	2086	36 - EC 75000 PH 1 Concrete Cut: Planning Prepare W/O 12/26/09 10 01/15/10 07				
DELDES2111M	-EC 75218 PH 2 Detension: Develop Final EC "Pkg for final DRB"	01/13/10 07	01/14/10 07	17	2249		37 - EC 75218 PH 2 Detension: Develop Final EC "Pkg for 01/13/10 07 01/14/10 07			
DELDES2115M	-EC 75218 PH 2 Detension: Mech / Struc - DV	01/14/10 07	01/16/10 07	48	2249		38 - EC 75218 PH 2 Detension: Mech / Struc - DV 01/14/10 07 01/16/10 07			
DELDES2120	-EC 75218 PH 2 Detension: Inter-Departmental Reviews	01/14/10 07	01/16/10 07	48	2249		39 - EC 75218 PH 2 Detension: Inter-Departmental Reviews 01/14/10 07 01/16/10 07			
DELDES2123	-EC 75218 PH 2 Detension: Incorp Review Comments	01/16/10 07	01/17/10 07	24	2249		40 - EC 75218 PH 2 Detension: Incorp Review Comments 01/16/10 07 01/17/10 07			
DELDES2117	-EC 75218 PH 2 Detension: Incorp Verification Comments	01/16/10 07	01/17/10 07	24	2249		41 - EC 75218 PH 2 Detension: Incorp Verification Comments 01/16/10 07 01/17/10 07			
DELDES2125	EC 75218 PH 2 Detension: Supv Review Prior to Final DRB	01/17/10 07	01/17/10 11	4	2249		42 - EC 75218 PH 2 Detension: Supv Review Prior to Final D 01/17/10 07 01/17/10 11			
DELDES2125D	EC 75218 PH 2 Detension: Distrib Final DRB Pkg for Review	01/17/10 11	01/17/10 12	1	2249		43 - EC 75218 PH 2 Detension: Distrib Final DRB Pkg for Re 01/17/10 11 01/17/10 12			

Legend: Milestones In-Progress Activity

January 13, 2010 07:12:19 PM

Page 3 of 12

CR3 NPC Outage Containment Repair Project - Level 3 Schedule

ACT	Description	Early Start	Early Finish	Rem Dur	TF	Dec												Jan												Feb												Mar												Apr																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																		
						28	04	11	18	25	01	08	15	22	01	08	15	22	29	05	01	08	15	22	29	05	01	08	15	22	29	05																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																								
DELDES2125R	-EC 75218 PH 2 Detension: Review Final DRB Pkg	01/17/10 12	01/18/10 12	24	2249																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																																			</

CR3 NPC Outage Containment Repair Project - Level 3 Schedule

ACT	Description	Early Start	Early Finish	Rem Dur	TF	Dec	28	04	11	18	25	01	08	15	22	01	08	15	22	29	05	Apr
DELDES3120	-EC 75219 PH 3 Removal: Inter-Departmental Reviews	01/18/10 19	01/22/10 19	96	2371					58 -EC 75219 PH 3 Removal: Inter-Departmental Reviews												
DELDES3123	-EC 75219 PH 3 Removal: Incorp Review Comments	01/22/10 19	01/23/10 21	26	2381					59 -EC 75219 PH 3 Removal: Incorp Review Comments												
DELDES3117	-EC 75219 PH 3 Removal: Incorp Verification Comments	01/22/10 19	01/24/10 07	36	2371					60 -EC 75219 PH 3 Removal: Incorp Verification Comment												
DELDES3125	EC 75219 PH 3 Removal: Supv Review Prior to Final DRB	01/24/10 07	01/24/10 11	4	2371					61 EC 75219 PH 3 Removal: Supv Review Prior to Final D												
DELDES3125D	EC 75219 PH 3 Removal: Distrib Final DRB Pkg for Review	01/24/10 11	01/24/10 12	1	2371					62 EC 75219 PH 3 Removal: Distrib Final DRB Pkg for Re												
DELDES3125R	-EC 75219 PH 3 Removal: Review Final DRB Pkg	01/24/10 12	01/26/10 06	42	2371					63 -EC 75219 PH 3 Removal: Review Final DRB Pkg												
DELDES31205	EC 75219 PH 3 Removal: Final DRB Meeting	01/26/10 06	01/26/10 08	2	2371					64 EC 75219 PH 3 Removal: Final DRB Meeting												
DELDES31215	-EC 75219 PH 3 Removal: Incorporate Final DRB Comments	01/26/10 08	01/27/10 08	24	2371					65 -EC 75219 PH 3 Removal: Incorporate Final DRB Com												
DELDES3130Z	EC 75219 PH 3 Removal: MILESTONE - All Reviews Complete	01/27/10 08	01/27/10 08	0	2371					66 EC 75219 PH 3 Removal: MILESTONE - All Reviews C												
DELDES31220	EC 75219 PH 3 Removal: Obtain Supervisor Approval	01/27/10 08	01/27/10 10	2	2371					67 EC 75219 PH 3 Removal: Obtain Supervisor Approval												
DELDES31225	-EC 75219 PH 3 Removal: Obtain PGM Approval	01/27/10 10	01/28/10 10	24	2371					68 -EC 75219 PH 3 Removal: Obtain PGM Approval												
DELDES3140Z	EC 75219 PH 3 Removal: MILESTONE - PGM Approval	01/28/10 10	01/28/10 10	0	2371					69 EC 75219 PH 3 Removal: MILESTONE - PGM Approv												
DELDES31710	-EC 75219 PH 3 Removal: Planning Prepare EC Work Packages	01/28/10 10	01/31/10 10	72	2371					70 -EC 75219 PH 3 Removal: Planning Prepare EC Work P												
DELDES4111M	-EC 75220 PH 4 Replacement: Develop 70% EC *Pkg for Design Challenge	01/13/10 10	01/23/10 16	212	2252					71 -EC 75220 PH 4 Replacement: Develop 70%												

Legend:

Milestones

In-Progress

Activity

Page 5 of 12

January 13, 2010 07:12:19 PM

CR3 NPC Outage Containment Repair Project - Level 3 Schedule

ACT	Description	Early Start	Early Finish	Rem Dur	TF	Dec		Jan			Feb			Mar			Apr			
						28	04	11	18	25	01	08	15	22	01	08	15	22	29	05
DELDES4-0006	EC 75220 PH 4 Replacement: AREVA Design Radial Reinforcement	01/15/10 09	01/20/10 23	134	2607					72 EC 75220 PH 4 Replacement: AREVA										
										01/15/10 09 01/20/10 23										
DELDES4-0004	EC 75220 PH 4 Replacement: AREVA Revise Concrete Spec CR3-C-0003&Verify Mix Dsn	01/15/10 09	01/20/10 23	134	2486					73 EC 75220 PH 4 Replacement: AREVA										
										01/15/10 09 01/20/10 23										
DELDES4-0008	EC 75220 PH 4 Replacement: AREVA Design Additional Reinforcement for Delan Area	01/15/10 09	01/20/10 23	134	2607					74 EC 75220 PH 4 Replacement: AREVA										
										01/15/10 09 01/20/10 23										
DELDES4-0001	EC 75220 PH 4 Replacement: SGT Revist Formwork Calc S08-0021	01/15/10 09	02/02/10 23	446	2174					75 EC 75220 PH 4 Replacement: SGT Revise										
										01/15/10 09 02/02/10 23										
DELDES41008B	EC 75220 PH 4 Replacement: Receive Design Input on Form Work from SGT	01/15/10 09	01/15/10 09	0	2174					76 EC 75220 PH 4 Replacement: Receive										
										01/15/10 09 01/15/10 09										
DELDES4-0002	EC 75220 PH 4 Replacement: SGT Revist Formwork Spec CR3-C-0002	01/15/10 09	02/02/10 23	446	2174					77 EC 75220 PH 4 Replacement: SGT Revise										
										01/15/10 09 02/02/10 23										
DELDES4-0013	EC 75220 PH 4 Replacement: Void Calc S09-0025	01/15/10 09	02/03/10 23	470	2174					78 EC 75220 PH 4 Replacement: Void Calc S09										
										01/15/10 09 02/03/10 23										
DELDES4-0011	EC 75220 PH 4 Replacement: AREVA Review & Revise Calc S06-0007 for Liner Plate	01/15/10 09	01/31/10 23	398	2198					79 EC 75220 PH 4 Replacement: AREVA										
										01/15/10 09 01/31/10 23										
DELDES4-0024	EC 75220 PH 4 Replacement: MPR Revise Calc S09-0044	01/15/10 09	01/31/10 23	398	2246					80 EC 75220 PH 4 Replacement: MPR Revise										
										01/15/10 09 01/31/10 23										
DELDES4-0010	EC 75220 PH 4 Replacement: AREVA Issue Reinforcement Calc/Dwgs	01/15/10 09	01/31/10 23	398	2198					81 EC 75220 PH 4 Replacement: AREVA Issue										
										01/15/10 09 01/31/10 23										
DELDES4-0009	EC 75220 PH 4 Replacement: AREVA Revise Existing & Create New Reinforcement Dwgs	01/15/10 09	01/20/10 23	134	2607					82 EC 75220 PH 4 Replacement: AREVA										
										01/15/10 09 01/20/10 23										
DELDES4-0005	EC 75220 PH 4 Replacement: Owner Accept Revised Concrete Spec CR3-C-0003	01/20/10 23	01/21/10 23	24	2486					83 EC 75220 PH 4 Replacement: Owner Accept										
										01/20/10 23 01/21/10 23										
DELDES4111M3	EC 75220 PH 4 Replacement: Receive Preliminary MPR Analysis Input	01/23/10 14	01/23/10 16	2	2252					84 EC 75220 PH 4 Replacement: Receive										
										01/23/10 14 01/23/10 16										
DELDES4115M	-EC 75220 PH 4 Replacement: Mech / Struc - 70% DV	01/23/10 16	01/28/10 14	118	2422					85 EC 75220 PH 4 Replacement: Mech / Struc										
										01/23/10 16 01/28/10 14										
ACT	Description	Early Start	Early Finish	Rem Dur	TF	28	04	11	18	25	01	08	15	22	01	08	15	22	29	05
						Dec		Jan		Feb			Mar		Apr					

Legend:

Milestones

In-Progress

Activity

Page 6 of 12

January 13, 2010 07:12:19 PM

Rev D

CR3 NPC Outage Containment Repair Project - Level 3 Schedule

ACT	Description	Early Start	Early Finish	Rem Dur	TF	Dec		Jan		Feb		Mar		Apr						
						28	04	11	18	25	01	08	15	22	01	08	15	22	29	05
DELDES4190Z	EC 75220 PH 4 Replacement: Milestone - Issued for 70% Review	01/23/10 16	01/23/10 16	0	2542					86	EC 75220 PH 4 Replacement: Milestone -									
										01/23/10 16	01/23/10 16									
DELDES4120	-EC 75220 PH 4 Replacement: Inter-Departmental 70% Reviews	01/23/10 16	01/28/10 14	118	2422					87	-EC 75220 PH 4 Replacement:									
										01/23/10 16	01/28/10 14									
DELDES4-0000	EC 75220 PH 4 Replacement: Receive Design Input from PII Root Cause Analysis	01/27/10 08	01/27/10 10	2	2539					88	EC 75220 PH 4 Replacement: Receive									
										01/27/10 08	01/27/10 10									
DELDES41207	EC 75220 PH 4 Replacement: 70% Design Challenge Meeting	01/28/10 14	01/28/10 16	2	2422					89	EC 75220 PH 4 Replacement: 70% Design									
										01/28/10 14	01/28/10 16									
DELDES4117	-EC 75220 PH 4 Replacement: Incorporate 70% Verification Comments	01/28/10 14	01/29/10 14	24	2424					90	-EC 75220 PH 4 Replacement: Incorporate 70%									
										01/28/10 14	01/29/10 14									
DELDES4123	-EC 75220 PH 4 Replacement: Incorporate 70% Review Comments	01/28/10 16	01/29/10 16	24	2422					91	-EC 75220 PH 4 Replacement: Incorporate 70%									
										01/28/10 16	01/29/10 16									
DELDES4111M2	-EC 75220 PH 4 Replacement: Develop Final EC "Pkg for final DRB"	01/29/10 15	02/06/10 16	193	2109					92	-EC 75220 PH 4 Replacement: Develop Final									
										01/29/10 15	02/06/10 16									
DELDES4-0007	EC 75220 PH 4 Replacement: Owner Accept New Reinforcement Design/Calc	01/31/10 23	02/02/10 23	48	2198					93	EC 75220 PH 4 Replacement: Owner Accept									
										01/31/10 23	02/02/10 23									
DELDES4-0012	EC 75220 PH 4 Replacement: Owner Accept Revised Calc S06-0007 for Liner Plate	01/31/10 23	02/02/10 23	48	2198					94	EC 75220 PH 4 Replacement: Owner Accept									
										01/31/10 23	02/02/10 23									
DELDES4-0003	EC 75220 PH 4 Replacement: Owner Accept Formwork Spec CR3-C-0002 & Calc S08-0021	02/02/10 23	02/03/10 23	24	2174					95	EC 75220 PH 4 Replacement: Owner Accept									
										02/02/10 23	02/03/10 23									
DELDES4111M1	EC 75220 PH 4 Replacement: Receive Approved MPR Analysis Input	02/06/10 14	02/06/10 16	2	2109					96	EC 75220 PH 4 Replacement: Receive									
										02/06/10 14	02/06/10 16									
DELDES4120A	-EC 75220 PH 4 Replacement: Final Inter-Departmental Reviews	02/06/10 16	02/10/10 17	97	2113					97	-EC 75220 PH 4 Replacement: Final									
										02/06/10 16	02/10/10 17									
DELDES4115M1	-EC 75220 PH 4 Replacement: Final Mech / Struc - DV	02/06/10 16	02/10/10 17	97	2109					98	-EC 75220 PH 4 Replacement: Final Mech /									
										02/06/10 16	02/10/10 17									
DELDES4123A	-EC 75220 PH 4 Replacement: Incorporate Final Review Comments	02/10/10 17	02/11/10 17	24	2113					99	-EC 75220 PH 4 Replacement: Incorporate Final									
										02/10/10 17	02/11/10 17									
ACT	Description	Early Start	Early Finish	Rem Dur	TF	Dec		Jan		Feb		Mar		Apr						
						28	04	11	18	25	01	08	15	22	01	08	15	22	29	05

Legend:

Milestones

In-Progress

Activity

Page 7 of 12

January 13, 2010 07:12:19 PM

Rev D

CR3 NPC Outage Containment Repair Project - Level 3 Schedule									
--	--	--	--	--	--	--	--	--	--

ACT	Description	Early Start	Early Finish	Rem Dur	TF	Dec		Jan		Feb		Mar		Apr						
						28	04	11	18	25	01	08	15	22	01	08	15	22	29	05
DELDES4117F	-EC 75220 PH 4 Replacement: Incorp Final Verification Comments	02/10/10 17	02/11/10 17	24	2109							100 EC 75220 PH 4 Replacement: Incorp Final								
DELDES4125	EC 75220 PH 4 Replacement: Supv Review Prior to Final DRB	02/11/10 17	02/11/10 21	4	2109							101 EC 75220 PH 4 Replacement: Supv Review								
DELDES4125D	EC 75220 PH 4 Replacement: Distrib Final DRB Pkg for Review	02/11/10 21	02/11/10 22	1	2109							102 EC 75220 PH 4 Replacement: Distrib Final								
DELDES4125R	-EC 75220 PH 4 Replacement: Review Final DRB Pkg	02/11/10 22	02/12/10 22	24	2109							103 EC 75220 PH 4 Replacement: Review Final								
DELDES41205	EC 75220 PH 4 Replacement: Final DRB Meeting	02/12/10 22	02/13/10 00	2	2109							104 EC 75220 PH 4 Replacement: Final DRB Meeting								
DELDES41215	-EC 75220 PH 4 Replacement: Incorporate Final DRB Comments	02/13/10 00	02/14/10 00	24	2109							105 EC 75220 PH 4 Replacement: Incorporate								
DELDES4130Z	EC 75220 PH 4 Replacement: MILESTONE - All Reviews Complete	02/14/10 00	02/14/10 00	0	2109							106 EC 75220 PH 4 Replacement: MILESTONE -								
DELDES41220	EC 75220 PH 4 Replacement: Obtain Supervisor Approval	02/14/10 00	02/14/10 08	8	2109							107 EC 75220 PH 4 Replacement: Obtain								
DELDES41225	-EC 75220 PH 4 Replacement: Obtain PGM Approval	02/14/10 08	02/15/10 08	24	2109							108 EC 75220 PH 4 Replacement: Obtain PGM Approval								
DELDES41710	EC 75220 PH 4 Replacement: Planning Prepare EC Work Packages	02/15/10 08	02/18/10 08	72	2109							109 EC 75220 PH 4 Replacement: Planning								
DELDES4140Z	EC 75220 Replacement MILESTONE - PGM Approval	02/15/10 08	02/15/10 08	0	2109							110 EC 75220 Replacement: MILESTONE - PGM Approval								
DELDES510Z	EC 75221 PH 5 Retension: MILESTONE - Start Project	01/15/10 07	01/15/10 07	0	2890															
DELDES51005	EC 75221 PH 5 Retension: Prep / Cplt Validation Plan w/Supv	01/15/10 07	01/15/10 09	2	2890															
DELDES51008	EC 75221 PH 5 Retension: Develop Project Tm / Kick-Off Mtg	01/15/10 09	01/15/10 11	2	2890															
ACT	Description	Early Start	Early Finish	Rem Dur	TF	28	04	11	18	25	01	08	15	22	01	08	15	22	29	05
						Dec		Jan				Feb			Mar				Apr	

Milestones

Activity

January 13, 2010 07:12:19 PM

Rev D

CR3 NPC Outage Containment Repair Project - Level 3 Schedule

ACT	Description	Early Start	Early Finish	Rem Dur	TF	Dec		Jan			Feb			Mar			Apr	
						28	04	11	18	25	01	08	15	22	01	08	15	22
DELDES51020M	-EC 75221 PH 5 Retension: Develop Draft Pkg for Conceptual DRB	01/15/10 11	01/19/10 17	102	2890					114 -EC 75221 PH 5 Retension: Develop Draft Pkg for 01/15/10 11 01/19/10 17								
DELDES51025	EC 75221 PH 5 Retension: Distribute Conceptual 70% Pkg for Review	01/19/10 17	01/19/10 18	1	2983					115 EC 75221 PH 5 Retension: Distribute Conceptual 70% 01/19/10 17 01/19/10 18								
DELDES5111M	-EC 75221 PH 5 Retension: Develop 70% EC "Pkg"	01/19/10 17	01/22/10 17	72	2890					116 -EC 75221 PH 5 Retension: Develop 70% EC "Pkg" 01/19/10 17 01/22/10 17								
DELDES51027	-EC 75221 PH 5 Retension: Review Conceptual 70% Pkg	01/19/10 18	01/22/10 18	72	2983					117 -EC 75221 PH 5 Retension: Review Conceptual 70% Pkg 01/19/10 18 01/22/10 18								
DELDES51030	EC 75221 PH 5 Retension: Conceptual DRB Meeting	01/22/10 16	01/22/10 18	2	2985					118 EC 75221 PH 5 Retension: Conceptual DRB Meeting 01/22/10 16 01/22/10 18								
DELDES5120	-EC 75221 PH 5 Retension: Inter-Departmental Reviews	01/22/10 17	01/26/10 17	96	2890					119 -EC 75221 PH 5 Retension: Inter-Departmental Reviews 01/22/10 17 01/26/10 17								
DELDES5115M	-EC 75221 PH 5 Retension: Mech / Struc - DV	01/22/10 17	01/26/10 17	96	2890					120 -EC 75221 PH 5 Retension: Mech / Struc - DV 01/22/10 17 01/26/10 17								
DELDES5190Z	EC 75221 PH 5 Retension: Milestone - Issued for 70% Review	01/22/10 18	01/22/10 18	0	2985					121 EC 75221 PH 5 Retension: Milestone - Issued for 70% R 01/22/10 18 01/22/10 18								
DELDES5120Z	EC 75221 PH 5 Retension: MILESTONE - Conceptual DRB Mtg Cplt / Waived	01/22/10 18	01/22/10 18	0	2985					122 EC 75221 PH 5 Retension: MILESTONE - Conceptual 01/22/10 18 01/22/10 18								
DELDES5122	-EC 75221 PH 5 Retension: 70% Design Challenge Mgt	01/22/10 18	01/22/10 20	2	2983					123 -EC 75221 PH 5 Retension: 70% Design Challenge Mgt 01/22/10 18 01/22/10 20								
DELDES5117	-EC 75221 PH 5 Retension: Incorp 70% Comments	01/26/10 17	01/29/10 18	73	2890					124 -EC 75221 PH 5 Retension: Incorp 70% Comments 01/26/10 17 01/29/10 18								
DELDES5123	-EC 75221 PH 5 Retension: Incorp Review Comments	01/26/10 17	01/29/10 18	73	2890					125 -EC 75221 PH 5 Retension: Incorp Review Comments 01/26/10 17 01/29/10 18								
DELDES5125	EC 75221 PH 5 Retension: Supv Review Prior to Final DRB	01/29/10 18	01/29/10 22	4	2890					126 EC 75221 PH 5 Retension: Supv Review Prior to Final D 01/29/10 18 01/29/10 22								
DELDES5125D	EC 75221 PH 5 Retension: Distrib Final DRB Pkg for Review	01/29/10 22	01/29/10 23	1	2890					127 EC 75221 PH 5 Retension: Distrib Final DRB Pkg for Re 01/29/10 22 01/29/10 23								
ACT	Description	Early Start	Early Finish	Rem Dur	TF	Dec	Jan	Feb	Mar	Apr								

Legend:

Milestones

In-Progress

Activity

Page 9 of 12

January 13, 2010 07:12:19 PM

Rev D

CR3 NPC Outage Containment Repair Project - Level 3 Schedule									
--	--	--	--	--	--	--	--	--	--

ACT	Description	Early Start	Early Finish	Rem Dur	TF	Dec 28 04 11 18 25 01 08 15 22 01 08 15 22 29 05											
DELDES5125R	-EC 75221 PH 5 Retension: Review Final DRB Pkg	01/29/10 23	01/30/10 23	24	2890	128 EC 75221 PH 5 Retension: Review Final DRB Pkg 01/29/10 23 01/30/10 23											
DELDES51205	EC 75221 PH 5 Retension: Final DRB Meeting	01/30/10 23	01/31/10 01	2	2890	129 EC 75221 PH 5 Retension: Final DRB Meeting 01/30/10 23 01/31/10 01											
DELDES51215	-EC 75221 PH 5 Retension: Incorporate Final DRB Comments	01/31/10 01	02/01/10 01	24	2890	130 EC 75221 PH 5 Retension: Incorporate Final DRB Comments 01/31/10 01 02/01/10 01											
DELDES51220	EC 75221 PH 5 Retension: Obtain Supervisor Approval	02/01/10 01	02/01/10 09	8	2890	131 EC 75221 PH 5 Retension: Obtain Supervisor Approval 02/01/10 01 02/01/10 09											
DELDES5130Z	EC 75221 PH 5 Retension: MILESTONE - All Reviews Complete	02/01/10 01	02/01/10 01	0	2890	132 EC 75221 PH 5 Retension: MILESTONE - All Reviews Complete 02/01/10 01 02/01/10 01											
DELDES51225	-EC 75221 PH 5 Retension: Obtain PGM Approval	02/01/10 09	02/02/10 09	24	2890	133 EC 75221 PH 5 Retension: Obtain PGM Approval 02/01/10 09 02/02/10 09											
DELDES5140Z	EC 75221 PH 5 Retension: MILESTONE - PGM Approval	02/02/10 09	02/02/10 09	0	2890	134 EC 75221 PH 5 Retension: MILESTONE - PGM Approval 02/02/10 09 02/02/10 09											
DELDES51710	EC 75221 PH 5 Retension: Planning Prepare EC Work Packages	02/02/10 09	02/05/10 09	72	2890	135 EC 75221 PH 5 Retension: Planning Prepare EC Work Packages 02/02/10 09 02/05/10 09											
Containment Repair Contracting / Subcontracting / Procurement																	
DELCON1M	Contracting/Subcontracting/Procurement Complete MILESTONE	02/08/10 17	02/08/10 17	0	2810	137 Contracting/Subcontracting/Procurement Complete MILESTONE 02/08/10 17 02/08/10 17											
Containment Repair Subcontracting																	
DELCON09	-Award Hydro-Demolition Contract	12/04/09 19	01/15/10 17	51	2748	139 Award Hydro-Demolition Contract 12/04/09 19 01/15/10 17											
DELCON09M	Award Hydro-Demolition Contract Compl MILESTONE	01/15/10 17	01/15/10 17	0	2748	140 Award Hydro-Demolition Contract Compl MILESTONE 01/15/10 17 01/15/10 17											
DELCON11	-Award Batch Plant Contract	12/04/09 19	02/08/10 17	627	2532	141 Award Batch Plant Contract 12/04/09 19 02/08/10 17											
DELCON11M	Award Batch Plant Contract Compl MILESTONE	02/08/10 17	02/08/10 17	0	2532	142 Award Batch Plant Contract Compl MILESTONE 02/08/10 17 02/08/10 17											
Containment Repair Long Lead Procurement																	
ACT	Description	Early Start	Early Finish	Rem Dur	TF	Dec 28 04 11 18 25 01 08 15 22 01 08 15 22 29 05											
						Dec Jan Feb Mar Apr											

Legend:

Milestones


In-Progress

Activity

Page 10 of 12

January 13, 2010 07:12:19 PM

CR3 NPC Outage Containment Repair Project - Level 3 Schedule

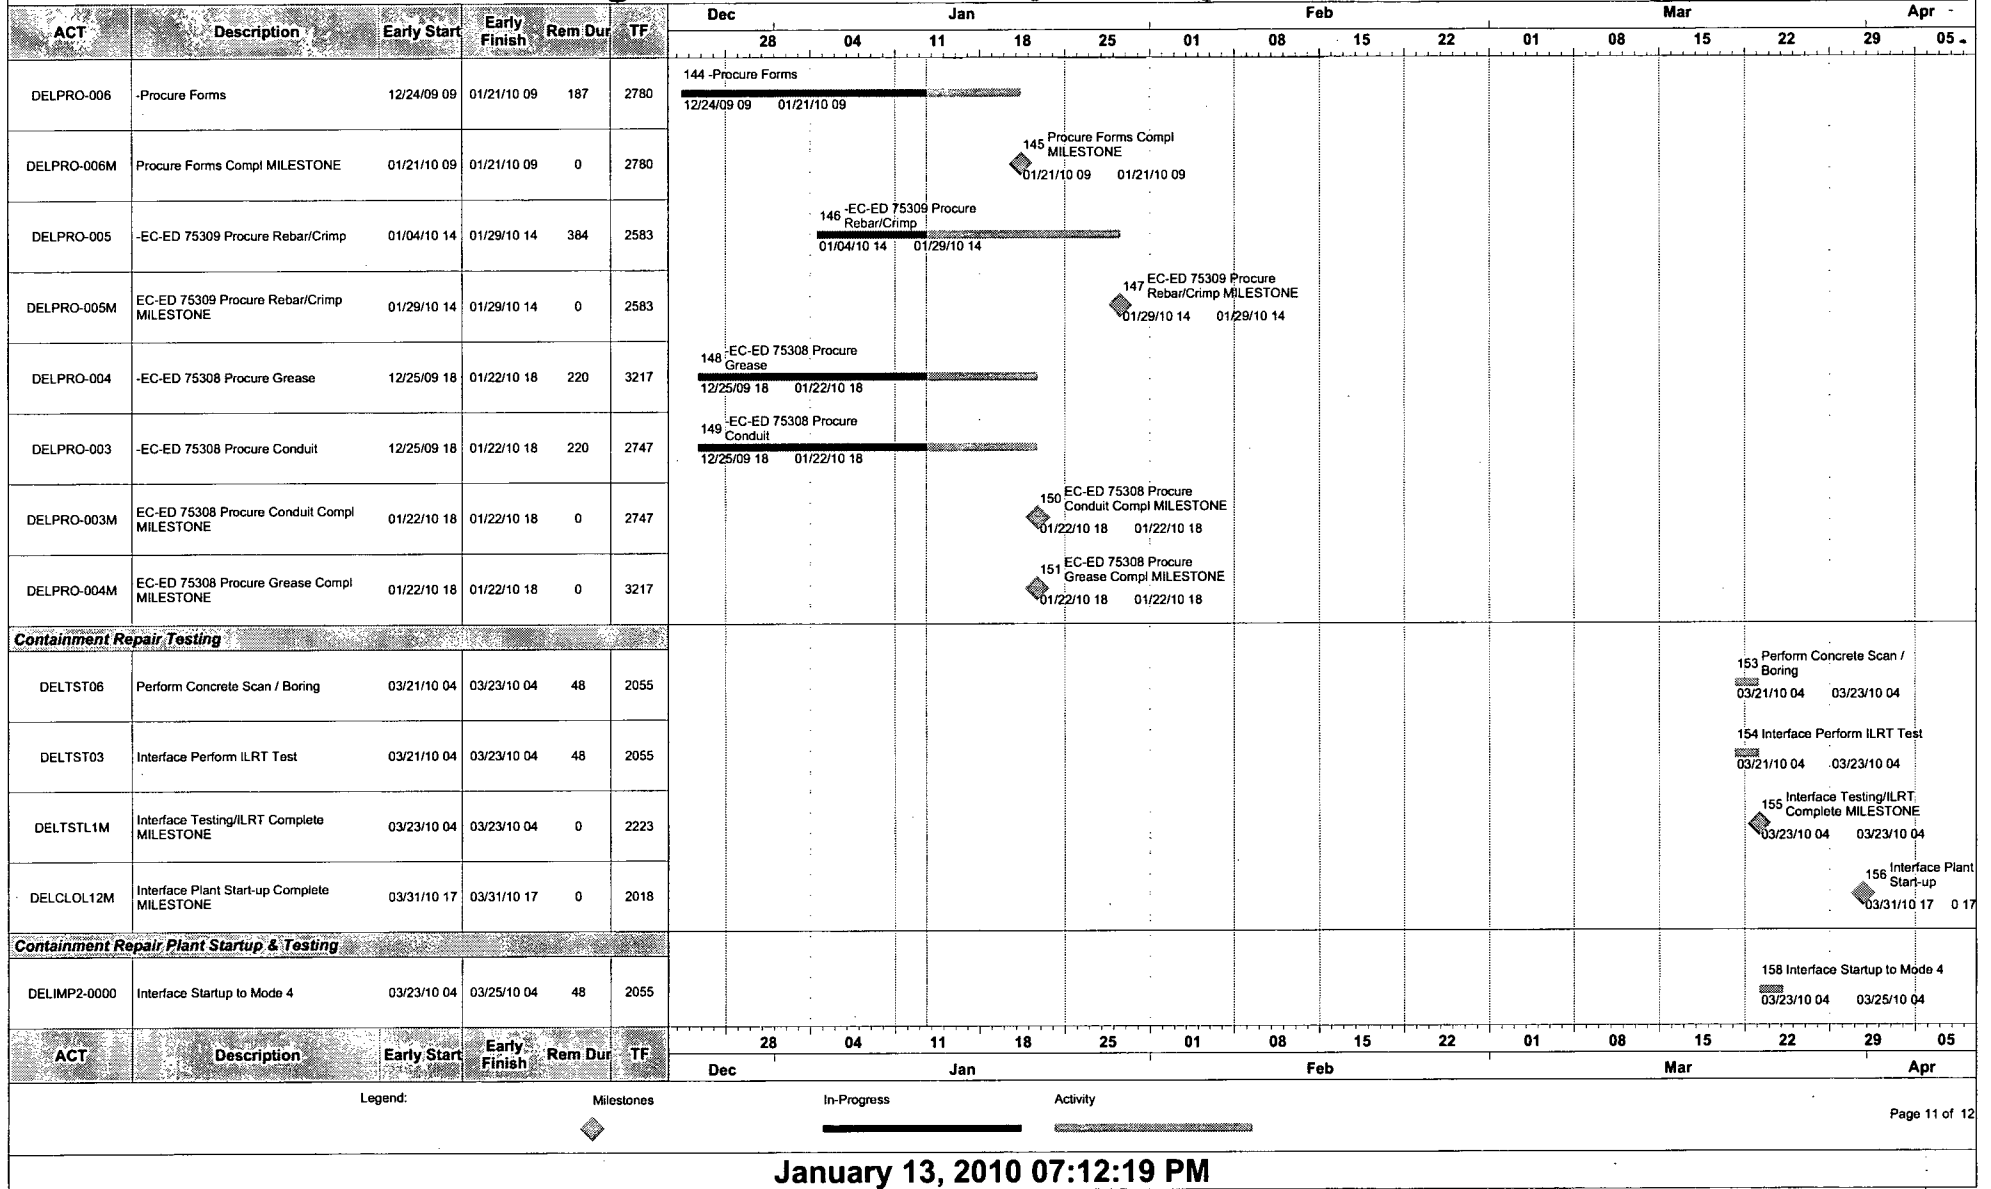

CR3 NPC Outage Containment Repair Project - Level 3 Schedule

ACT	Description	Early Start	Early Finish	Rem Dur	TF	Dec Jan Feb Mar Apr														
						28	04	11	18	25	01	08	15	22	01	08	15	22	29	05
DELCLO0-0000	Interface Startup to Mode 1/On-line	03/25/10 04	03/30/10 04	120	2055													159 Interface Startup to Mode 1/On-line 03/25/10 04 03/30/10 04		
ACT	Description	Early Start	Early Finish	Rem Dur	TF	Dec Jan Feb Mar Apr														
						28	04	11	18	25	01	08	15	22	01	08	15	22	29	05
Legend:						Milestones In-Progress Activity														
						 														
Page 12 of 12																				
January 13, 2010 07:12:19 PM																				
