

ACCELERATED DISTRIBUTION DEMONSTRATION SYSTEM

REGULATORY INFORMATION DISTRIBUTION SYSTEM (RIDS)

ACCESSION NBR: 8911160048 DOC.DATE: 89/11/03 NOTARIZED: NO DOCKET #
 FACIL: 50-331 Duane Arnold Energy Center, Iowa Electric Light & Pow 05000331
 AUTH.NAME AUTHOR AFFILIATION
 MINECK, D.L. Iowa Electric Light & Power Co.
 RECIP.NAME RECIPIENT AFFILIATION
 MURLEY, T.E. Office of Nuclear Reactor Regulation, Director (Post 870411)

SUBJECT: Provides semiannual rept for plan for integrated scheduling of plant mods for DAEC.

DISTRIBUTION CODE: A001D COPIES RECEIVED: LTR 1 ENCL 1 SIZE: 14
 TITLE: OR Submittal: General Distribution

NOTES:

	RECIPIENT ID CODE/NAME	COPIES	L	T	ENCL	RECIPIENT ID CODE/NAME	COPIES	L	T	ENCL
	PD3-3 LA	1			1	PD3-3 PD	1			1
	HALL, J.R.	5			5					
INTERNAL:	ACRS	6			6	NRR/DEST/ADS 7E	1			1
	NRR/DEST/ESB 8D	1			1	NRR/DEST/ICSB	1			1
	NRR/DEST/MTB 9H	1			1	NRR/DEST/RSB 8E	1			1
	NRR/DOEA/TSB 11	1			1	NUDOCS-ABSTRACT	1			1
	OC/LEMB	1			0	OGC/HDS2	1			0
	<u>REG FILE 01</u>	1			1	RES/DSIR/EIB	1			1
EXTERNAL:	LPDR	1			1	NRC PDR	1			1
	NSIC	1			1					

NOTE TO ALL "RIDS" RECIPIENTS:

PLEASE HELP US TO REDUCE WASTE! CONTACT THE DOCUMENT CONTROL DESK,
 ROOM P1-37 (EXT. 20079) TO ELIMINATE YOUR NAME FROM DISTRIBUTION
 LISTS FOR DOCUMENTS YOU DON'T NEED!

TOTAL NUMBER OF COPIES REQUIRED: LTR 27 ENCL 25



R
I
D
S
/
A
D
D
S

R
I
D
S
/
A
D
D
S

Iowa Electric Light and Power Company

November 3, 1989

NG-89-2786

Dr. Thomas E. Murley, Director
Office of Nuclear Reactor Regulation
U. S. Nuclear Regulatory Commission
Attn: Document Control Desk
Washington, DC 20555

Subject: Duane Arnold Energy Center
Docket No: 50-331
Op. License No: DPR-49
Semi-annual Report for the "Plan for the
Integrated Scheduling of Plant Modifications
for the Duane Arnold Energy Center"
Reference: D. Mineck letter to T. Murley dated May 3, 1989,
NG-89-1189
File: A-117, A-278

Dear Dr. Murley:

This letter and attachments provide the semi-annual report required by Section V.A. of the "Plan for the Integrated Scheduling of Plant Modifications for the Duane Arnold Energy Center" (the Plan). This report summarizes our progress in implementing Schedule A and B items, identifies the changes since the last report, summarizes the reasons for schedule changes, and provides updated schedules.

Attachment 1 is a summary of progress in implementing the items listed in Schedules A and B. It lists the four items which have been completed since the last update (referenced above).

Attachment 2 identifies the changes since the last report. These revisions include changes to the Item Descriptions of three items, the revision of four Schedule commitment dates, the addition of ten new Schedule B items and the deletion of three Schedule B items. The reasons for the schedule changes are stated in Attachment 3.

Updated Schedules A and B are included as Attachment 4. For each item listed, the specific implementation date is stated and reference to the NRC correspondence supporting this date is identified. When available, references to NRC correspondence are cited for IELP-initiated items listed in Schedule B.

8911160048 891103
PDR ADOCK 05000331
R PIC

AD01
||

Dr. Thomas Murley
NG-89-2786
November 3, 1989
Page

Please inform us if you have any questions or comments concerning this
submittal.

Very truly yours,



Daniel L. Mineck
Manager, Nuclear Division

DLM/PLB/pjv+

Attachments: 1. Summary of Progress in Implementing Schedule A and B Items
2. Changes in Schedules
3. Summary of Reasons for Schedule Changes
4. Updated Schedules A and B

cc: P. Bell
L. Liu
L. Root
R. McGaughy
J. R. Hall (NRC-NRR)
A. Bert Davis (Region III)
NRC Resident Office
Commitment Control: 830308, 840308, 840309, 860391, 880433, 880434,
880436, 880437

Summary of Progress in Implementing Schedule A and B Items

The following items, as listed on the Schedules A and B transmitted with the May 3, 1989 semiannual report, have been completed during this reporting period:

Schedule A

None

Schedule B

Instrument/Service Air Improvements

Training Simulator

Post Event Reconstruction (GL 83-28, Item 1.2)
Upgrade Recorder Power Supplies

Verification of Single Failure Assumption in ECCS Analysis

Changes in Schedules

Changes to the Schedules fall into four categories: revised descriptions of items, revised completion dates, addition of new items and deletion of items. Item descriptions are sometimes revised to better reflect the current IELP project titles.

I. Item Descriptions

<u>Current Item Description</u>	<u>Revised Item Description</u>
<u>Schedule A</u>	
None	
<u>Schedule B</u>	
Security System Upgrades	Security Systems Upgrades <ul style="list-style-type: none">•Perimeter Intrusion Detection System Upgrade•Security Computer System Upgrade•Access Control Upgrade
Containment Performance Improvements	Containment Performance Improvements <ul style="list-style-type: none">•Hardened Wetwell Vent (GL 89-16)•Other Containment Performance Improvements
Individual Plant Examination	Individual Plant Examination <ul style="list-style-type: none">•Initial Level I PRA•Containment Performance Analysis•Report Submittal

II. Schedule Changes

<u>Description</u>	<u>Current Completion Date</u>	<u>Revised Completion Date</u>
<u>Schedule A</u>		
None		
<u>Schedule B</u>		
Security System Upgrades	Schedule not yet certain	NA
• Perimeter Intrusion Detection System Upgrade	NA	March 31, 1990
• Security Computer System Upgrade	NA	December 31, 1992
• Access Control Upgrade	NA	December 31, 1992
Individual Plant Examination	Schedule not yet certain	NA
• Initial Level I PRA	NA	June 30, 1991
• Containment Performance Analysis	NA	June 30, 1992
• Report Submittal	NA	August 31, 1992
Additional 161 kV Service Breaker	Prior to Cycle 11 Startup	Prior to Cycle 12 Startup
Containment Performance Improvements	Schedule not yet certain	NA
• Hardened Wetwell Vent (GL 89-16)	NA	December 31, 1992
• Other Containment Performance Improvements	NA	Schedule not yet certain

III. New Items

<u>Description</u>	<u>Completion Date</u>
<u>Schedule A</u>	
None	
<u>Schedule B</u>	
Drill/Exercise Utilization of Control Room Simulator	
•Initial Use of Simulator	Full Scale Drill I. (Fall 1990)
•Permanent Use of Simulator	January 31, 1991
Emergency Diesel Generator Reliability Program	August 31, 1990
Emergency Response Data System (GL 89-15)	Schedule not yet certain, awaiting promulgation of NRC requirement/guidance
HPCI Availability Improvements	
•Component Modifications/Upgrades	Prior to Cycle 11 Startup
•System/Component Assessment Study	Prior to Cycle 12 Startup
MSIV Internals Improvements	Prior to Cycle 11 Startup
Power Systems Analysis	December 31, 1991
Safety-Related MOV-Operability/Testing (GL 89-10)	Prior to Cycle 13 Startup
Safety-Related Service Water Program (GL 89-13)	Prior to Cycle 11 Startup
Safety System Functional Inspection	December 31, 1990
Steam Leak Detection System Upgrades	Prior to Cycle 11 Startup

IV. Items Deleted

Description

Schedule A

None

Schedule B

Fire Protection (ANI Annual Projects)

Low Level Radwaste Processing and Storage Facility Improvements
(Annual Projects)

Plant Initiated Modifications (Annual Projects)


Summary of Reasons for Schedule Changes

<u>Item Description</u>	<u>Change</u>	<u>Explanation</u>
<u>Schedule A</u>		
None		
<u>Schedule B</u>		
Security System Upgrades <ul style="list-style-type: none"> • Perimeter Intrusion Detection System Upgrade • Security Computer System Upgrade • Access Control Upgrade 	Schedule B from IELP Initiative to NRC Items/ Completion Date/ Item Description	Made commitment by our response to a Notice of Violation
Additional 161 kV Service Breaker	Completion Date	Budgetary constraints
Containment Performance Improvements <ul style="list-style-type: none"> • Hardened Wetwell Vent (GL 89-16) • Other Containment Performance Improvements 	Completion Date/ Item Description	Issuance of GL 89-16
Individual Plant Examination <ul style="list-style-type: none"> • Initial Level I PRA • Containment Performance Analysis • Report Submittal 	Completion Date/ Item Description	Issuance of GL 88-20, Supplement 1
Drill/Exercise Utilization of Control Room Simulator <ul style="list-style-type: none"> • Initial Use of Simulator • Permanent Use of Simulator 	New Item	Increased realism of drills/ exercises and effectiveness of emergency response capabilities
Emergency Diesel Generator Reliability Program	New Item	Maintain current level of EDG reliability
Emergency Response Data System (GL 89-15)	New Item	Issuance of GL 89-15
HPCI Availability Improvements <ul style="list-style-type: none"> • Component Modifications/ Upgrades • System/Component Assessment Study 	New Item	Upgrade system availability through hardware modifications and changes in procedure and preventive maintenance programs


Summary of Reasons for Schedule Changes

<u>Item Description</u>	<u>Change</u>	<u>Explanation</u>
<u>Schedule B (Continued)</u>		
MSIV Internals Improvements	New Item	Improve local leak rate performance
Power Systems Analysis	New Item	Added per GL 88-15, SSFI finding, IN 88-45
Safety-Related MOV Operability/Testing (GL 89-10)	New Item	Issuance of GL 89-10
Safety-Related Service Water Program (GL 89-13)	New Item	Issuance of GL 89-13
Safety System Functional Inspection	New Item	IELP self-initiated item
Steam Leak Detection System Upgrades	New Item	Improve system operation and increase availability of related safety systems
Fire Protection (ANI Annual Projects)	Deleted Item	See Note
Low Level Radwaste Processing and Storage Facility Improvements (Annual Projects)	Deleted Item	See Note
Plant Initiated Modification (Annual Projects)	Deleted Item	See Note


Note: Deleted from the Schedule due to nature of "Annual Projects" items. This item consists of numerous small projects grouped together which, individually, are not significant enough to list on the schedule. Because of the continuous nature of these projects and the difficulty involved in defining the scope, we have elected to delete this item from the schedule.

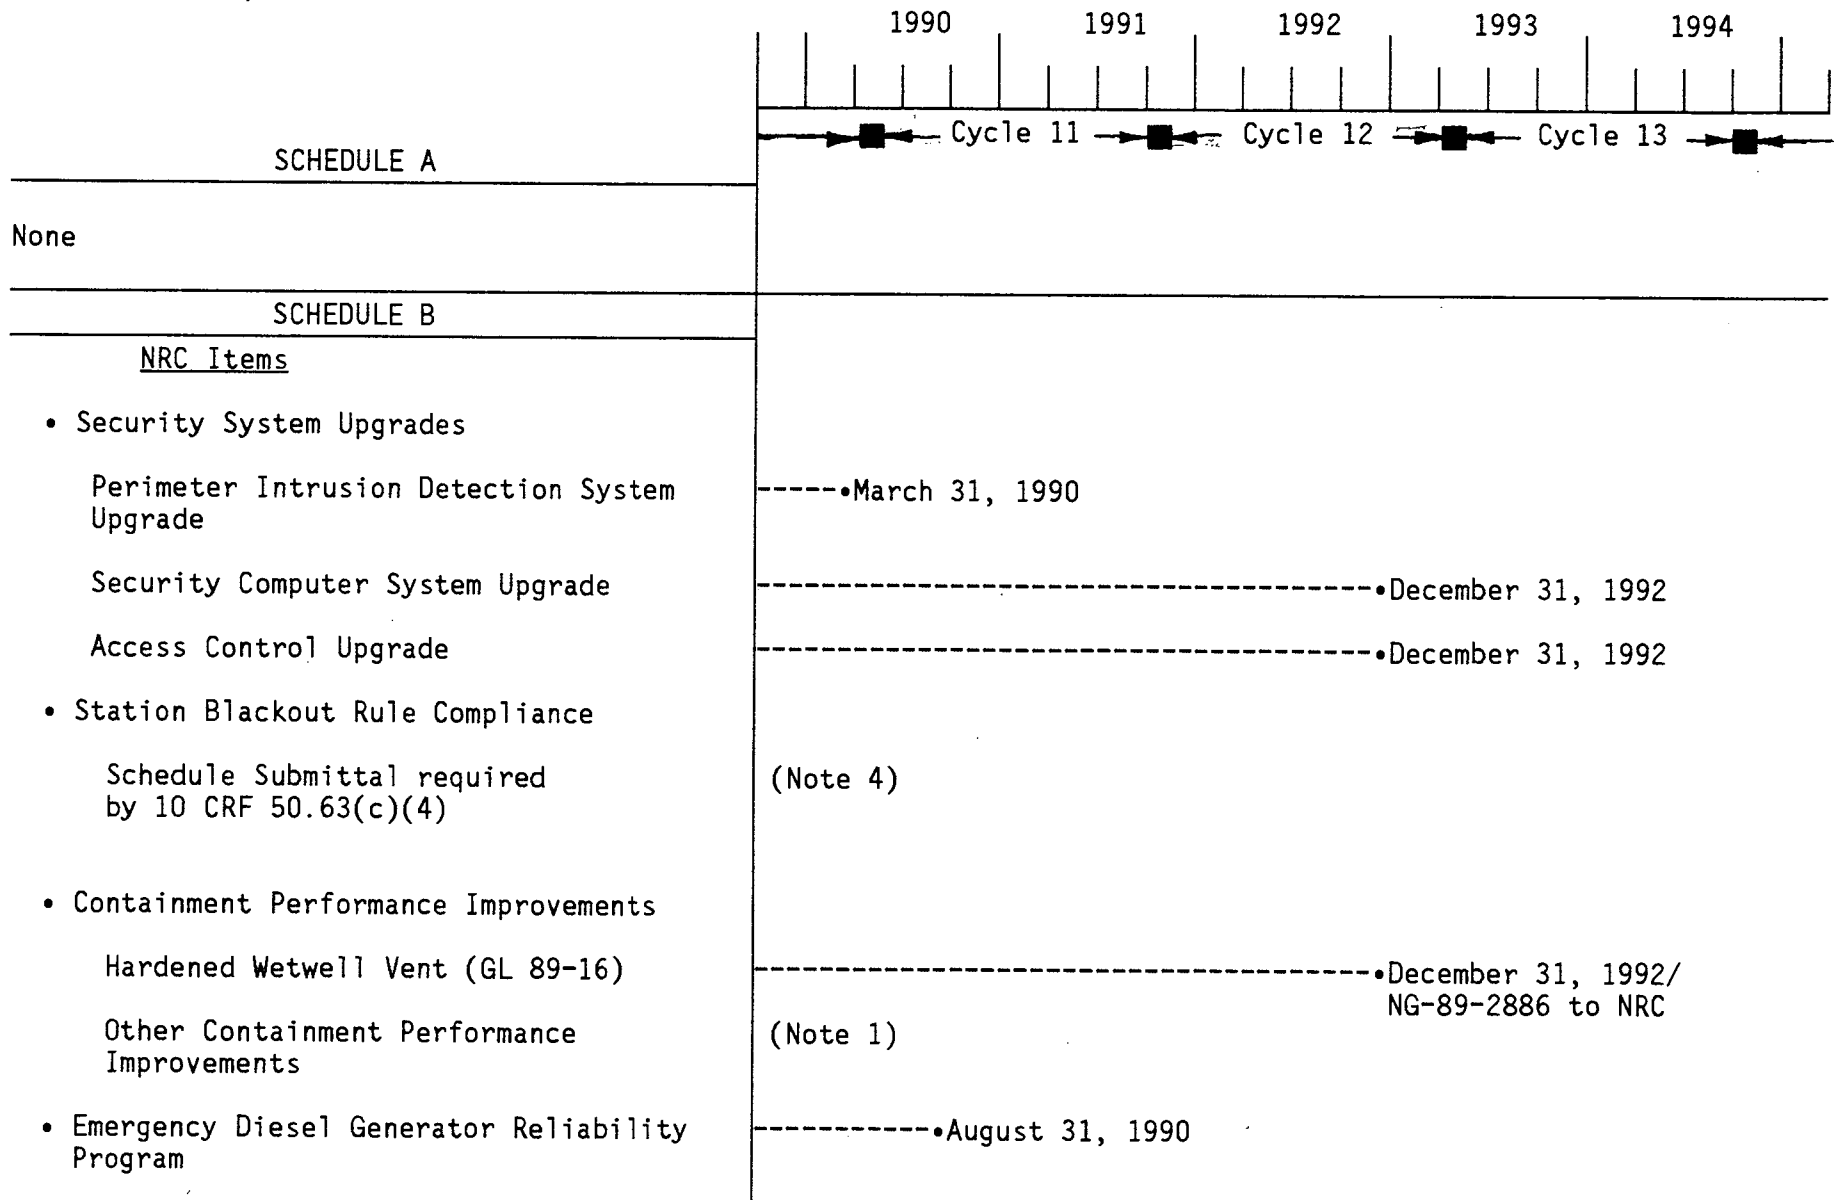


SCHEDULE B (Continued)

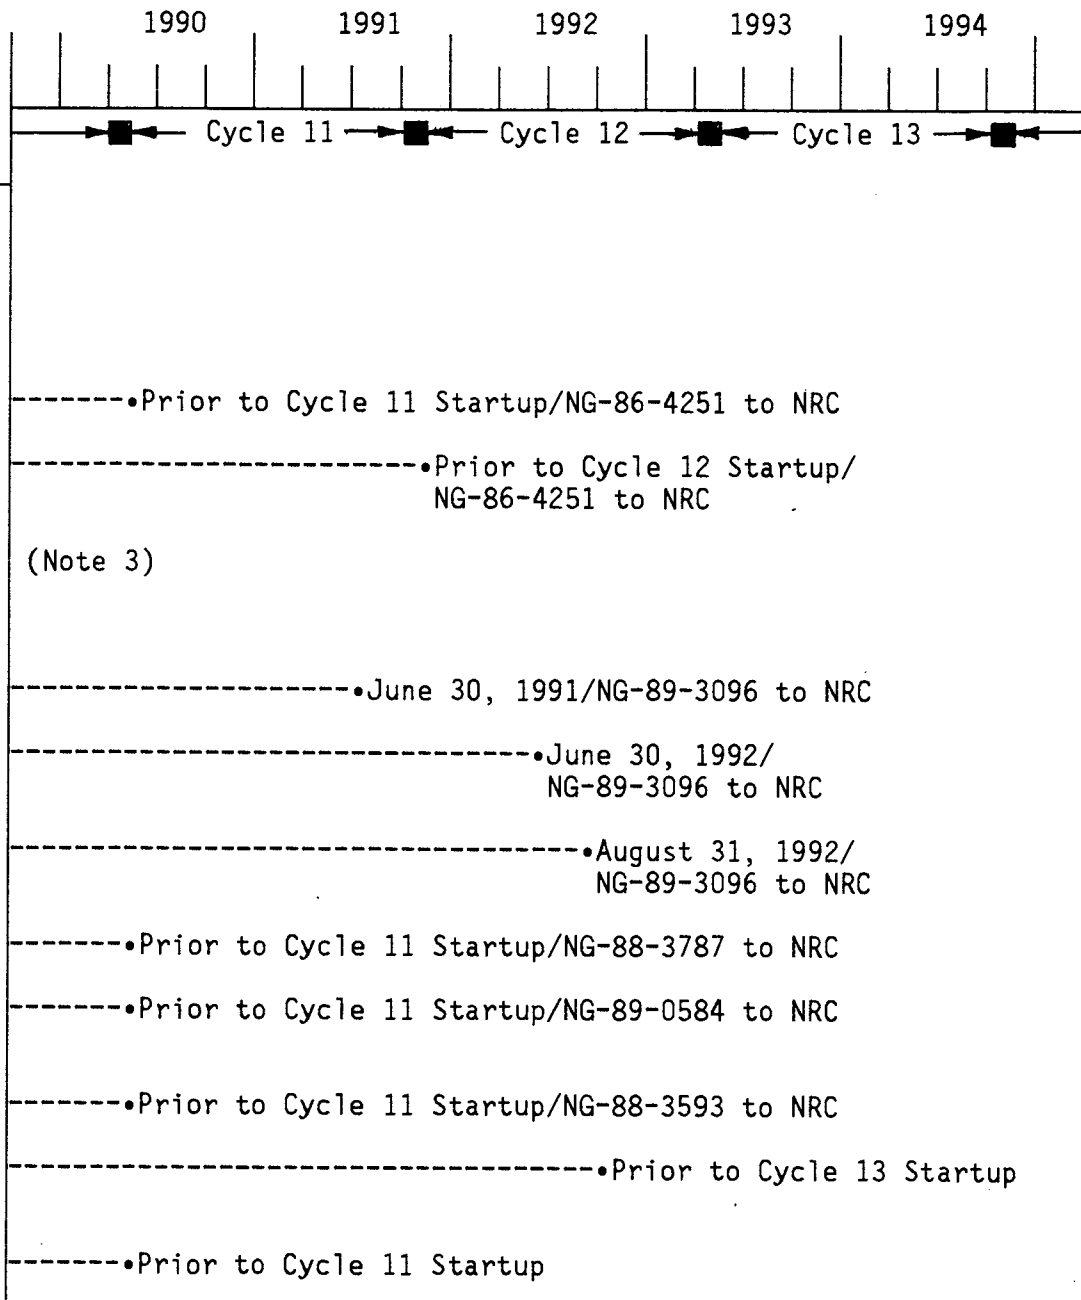

SCHEDULE B (Continued)

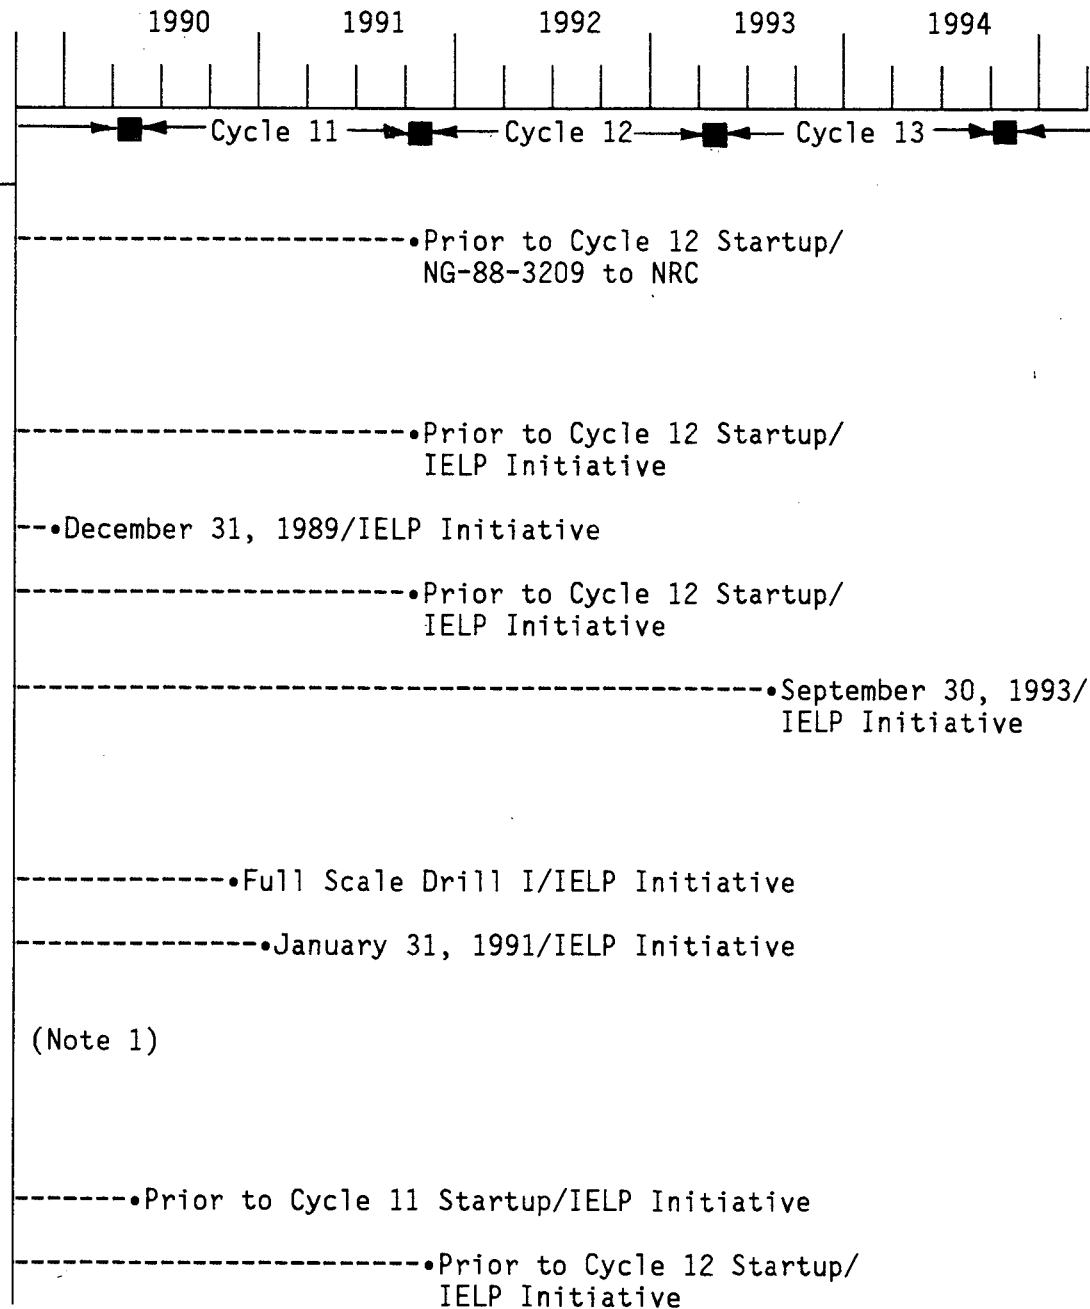

SCHEDULE B (Continued)

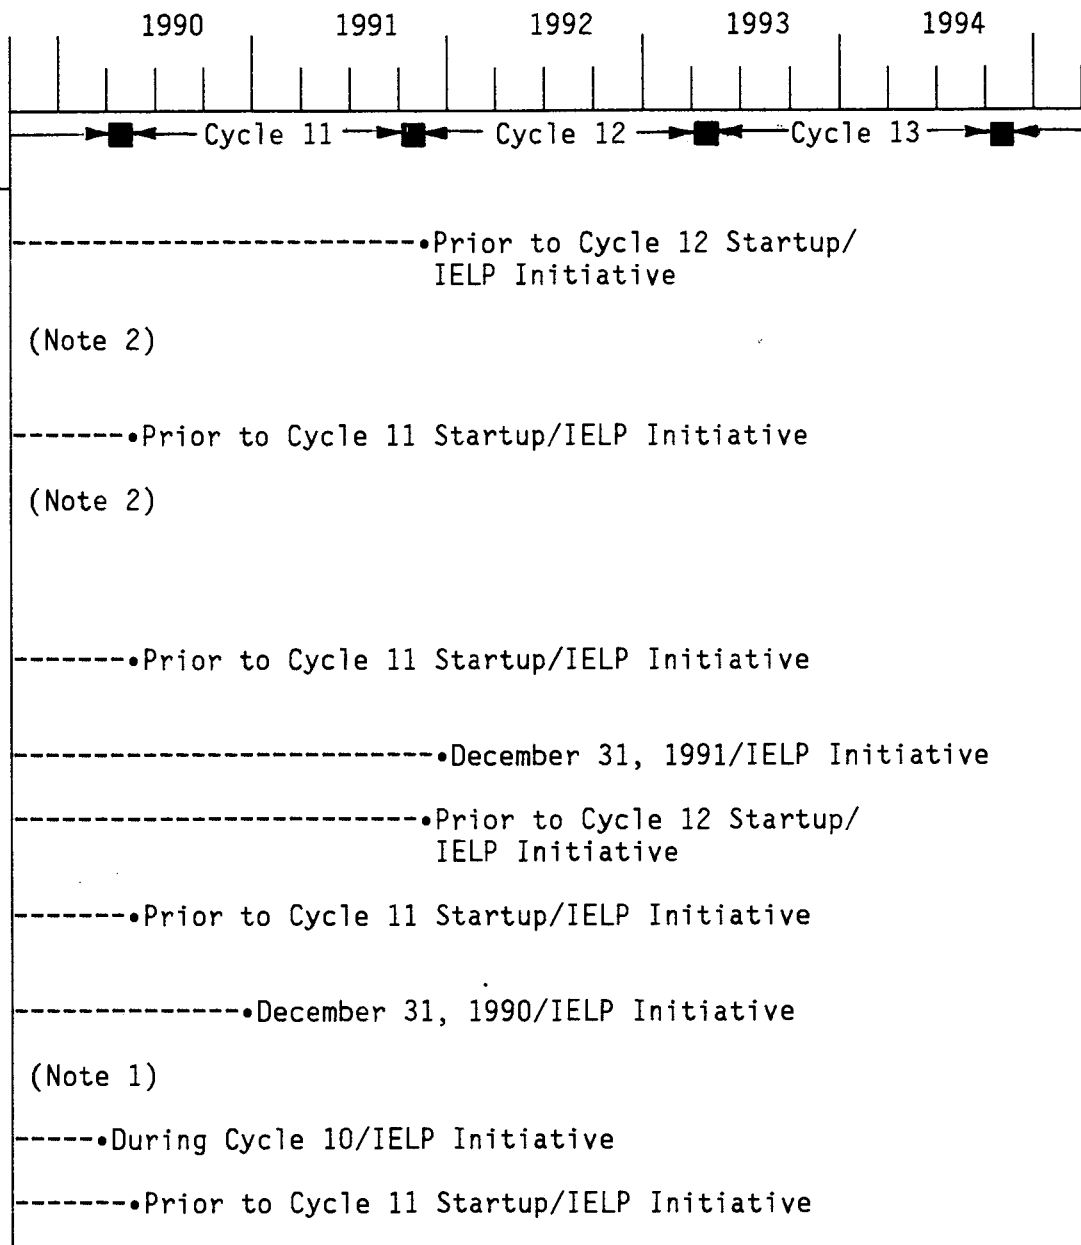

- Hydrogen Water Chemistry for Vessel Internals

•Prior to Cycle 12 Startup/
 IELP Initiative

- Hydrogen Water Chemistry Oxygen/Hydrogen Generator

(Note 2)

- MSIV Internals Improvement

•Prior to Cycle 11 Startup/IELP Initiative

- Plant Life Extension

(Note 2)

- Post Event Reconstruction (GL 83-28, Item 1.2)

- Verify Completion of Containment Isolation

•Prior to Cycle 11 Startup/IELP Initiative

- Power Systems Analysis

•December 31, 1991/IELP Initiative

- Recirc Pump Shaft Replacement (Both Pumps)

•Prior to Cycle 12 Startup/
 IELP Initiative

- Replacement of Extraction Steam Pipe to 3A/3B Feedwater Heaters

•Prior to Cycle 11 Startup/IELP Initiative

- Safety System Functional Inspection

•December 31, 1990/IELP Initiative

- Severe Accident Management


(Note 1)

- SPDS Enhancements

•During Cycle 10/IELP Initiative

- Steam Leak Detection System Upgrades

•Prior to Cycle 11 Startup/IELP Initiative

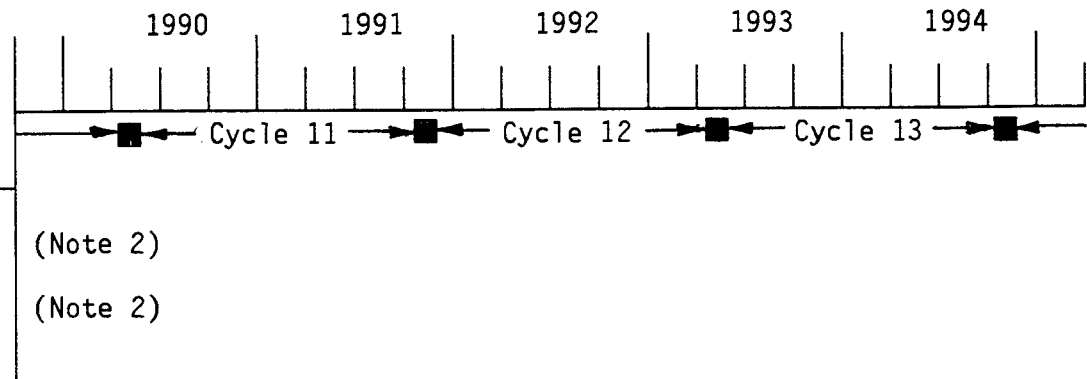

SCHEDULE B (Continued)

- Technical Specifications Improvement
- Zinc Injection

(Note 2)

(Note 2)

Note 1: Schedule not yet certain, awaiting promulgation of NRC requirements/guidance.
Note 2: Potential IELP initiative item. Schedule not yet certain.
Note 3: Schedule not yet certain, evaluation of scope in progress, (NG-89-0057).
Note 4: Schedule not yet certain. Due within 30 days of the notification provided in accordance with 1D CFR 50.63(c)(3).
