

memorandum

Idaho Operations Office
West Valley Project Office

M-32

DATE: April 6, 1994
SUBJECT: Waste Tank Farm Processing Schedule
TO: T. W. McIntosh, Program Manager
for West Valley
DOE-HQ, EM-343, 311/TREV

Attached for your information is a Level II Schedule for the major Integrated Radwaste Treatment System (IRTS) activities related to Waste Tank Farm Processing. This schedule will be issued on a biweekly in lieu of a weekly basis, and dates, if any, which have changed by more than ten working days from the previous schedule, are highlighted with a "number." This number corresponds to a brief explanation of the reason for the schedule change. This explanation is contained in an attachment to the schedule.

If you have any questions, please call me at (716) 942-4780, or Dennis H. Lin of my staff at (716) 942-2163.

J. A. Yeazel
Operations, Maintenance, Construction
Program Manager

Attachment: Schedule for Major IRTS Activities

cc: G. C. Comfort, NRC-HQ, w/att.
J. Furia, NRC, Region I, w/att.
P. L. Piciulo, NYSERDA-WV, w/att.
J. Paul, WVNS, MS W, w/o att.

DHL:011:94 - 0036:93:01

DHL/jam

NF13/1

IRTS ACTIVITIES SUMMARY SCHEDULE AS OF 03/28/94


| NOTE | DESCRIPTION | * BARCHART NUMBER | PREVIOUS FORECAST DATE 03/21/94 | NEW FORECAST DATE 03/28/94 |
|------|---|----------------------|--|-------------------------------------|
| | Complete Sludge Wash #1 processing to Tank 8D-2 level of 24 inches | 5 | 05/20/94 | 05/20/94 |
| | Test G-001 pump with new control scheme | 11 | 04/15/94 | 04/15/94 |
| | Issue Revision 2 of the Type I WQR | 12 | 04/29/94 | 04/29/94 |
| | Obtain DOE full release of Type I and Type V recipes, after NRC concurrence | -- | 06/28/94 | 06/28/94 |
| | Complete initial long-term drum testing for Type I and Type V sludge wash drums, issue letter reports | 21 | 04/27/94 | 04/27/94 |
| | Complete modification of WTF Chemical and Water Addition System pump suction line | 26 | 03/29/94 | 03/31/94 |
| | Complete installation of STS underdrain piping/equipment | 62 | 07/29/94 | 08/04/94 |

* See attached barchart schedule


NOTES AND EXPLANATION OF FORECAST CHANGES GREATER THAN 10 WORKING DAYS
=====

No forecast shown above has changed by greater than ten (10) working days since the previous update. Note, however, that the delivery of the drum grabber (Bar #57) has been reforecast to 6/30/94.

SCHEDULE OF MAJOR IRTS ACTIVITIES

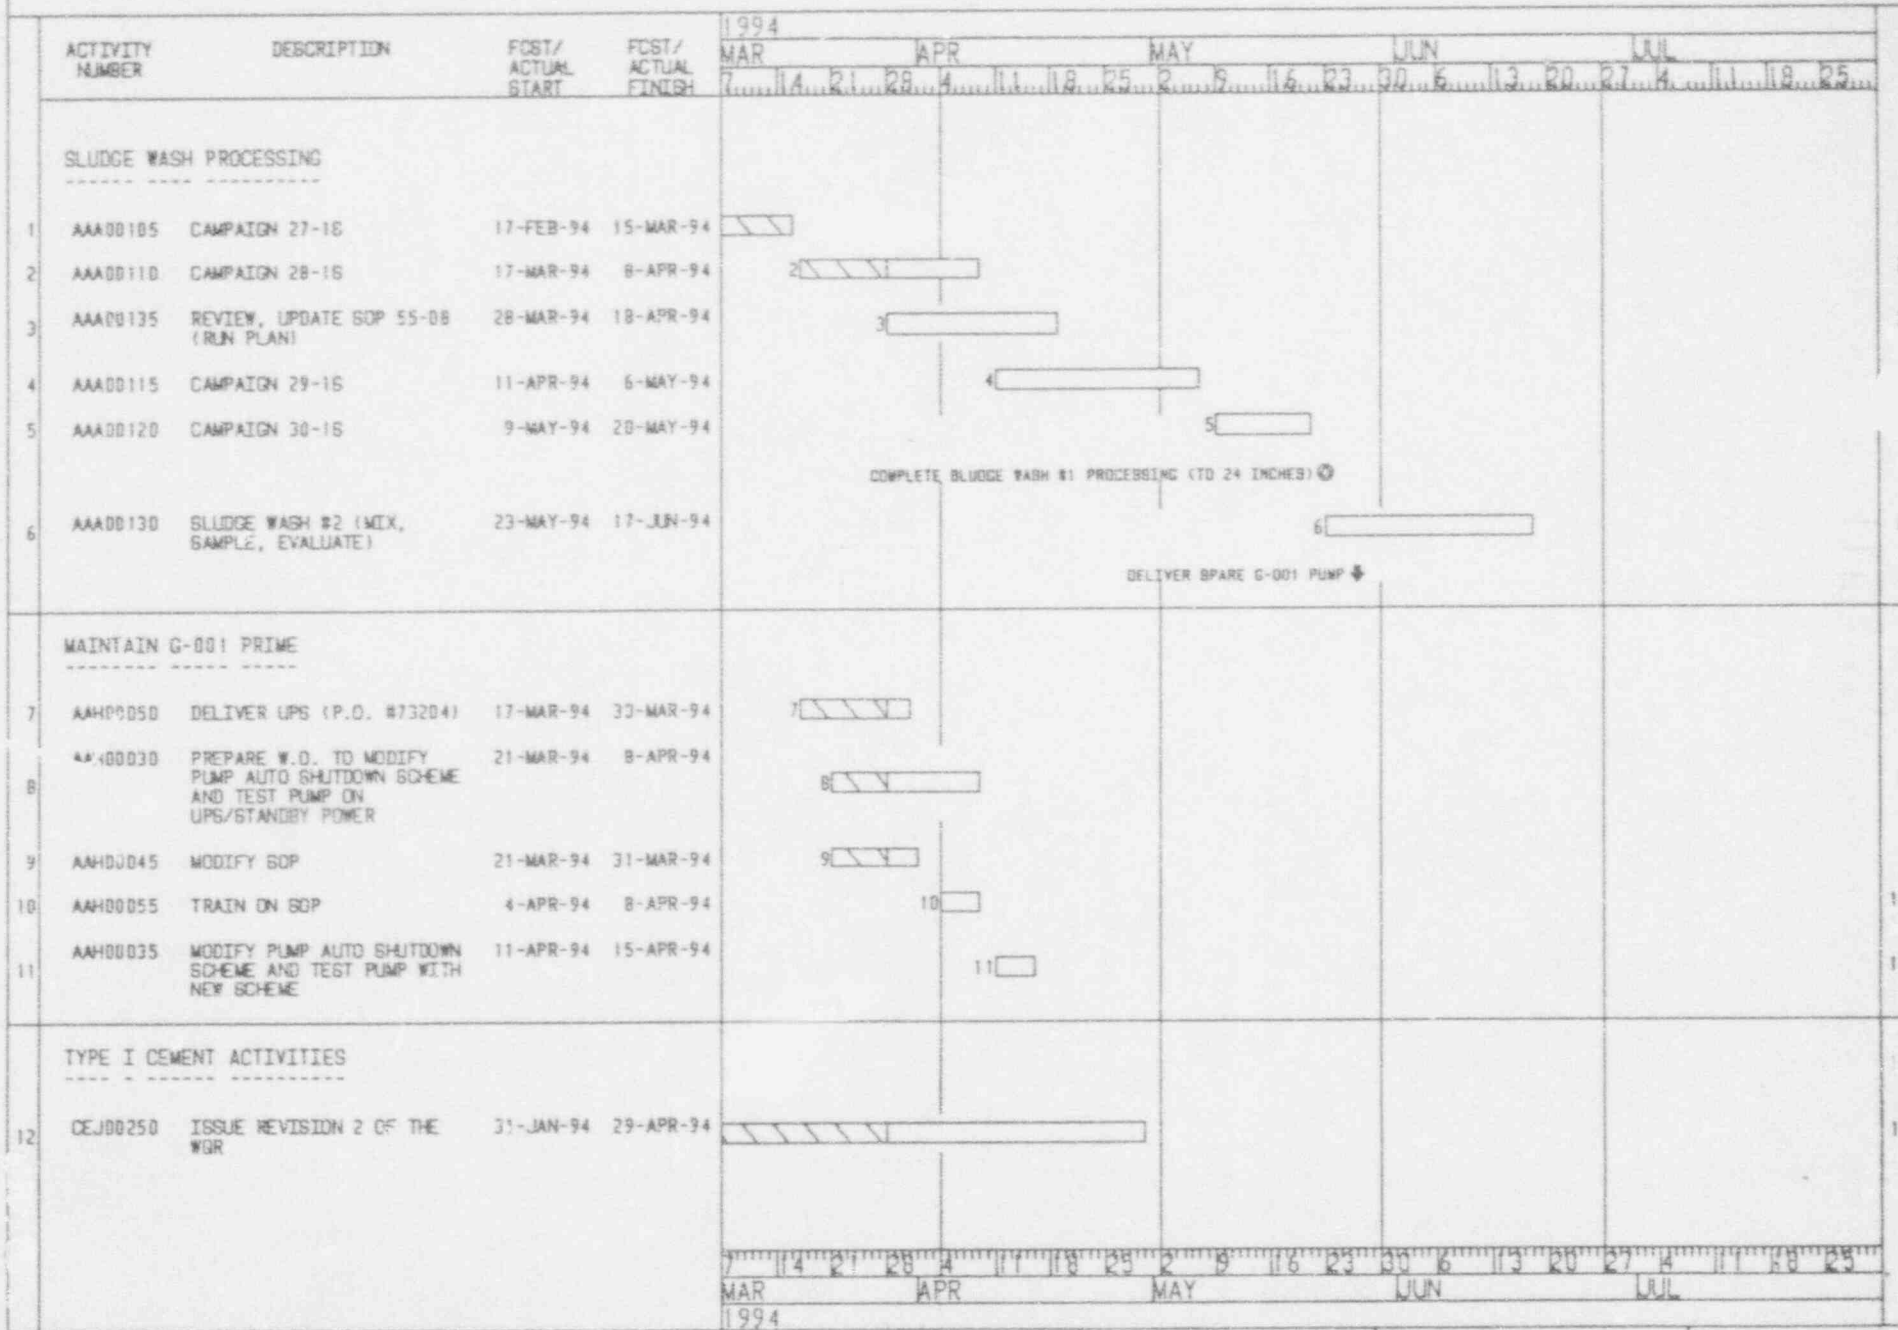


SCHEDULE OF MAJOR IRTS ACTIVITIES

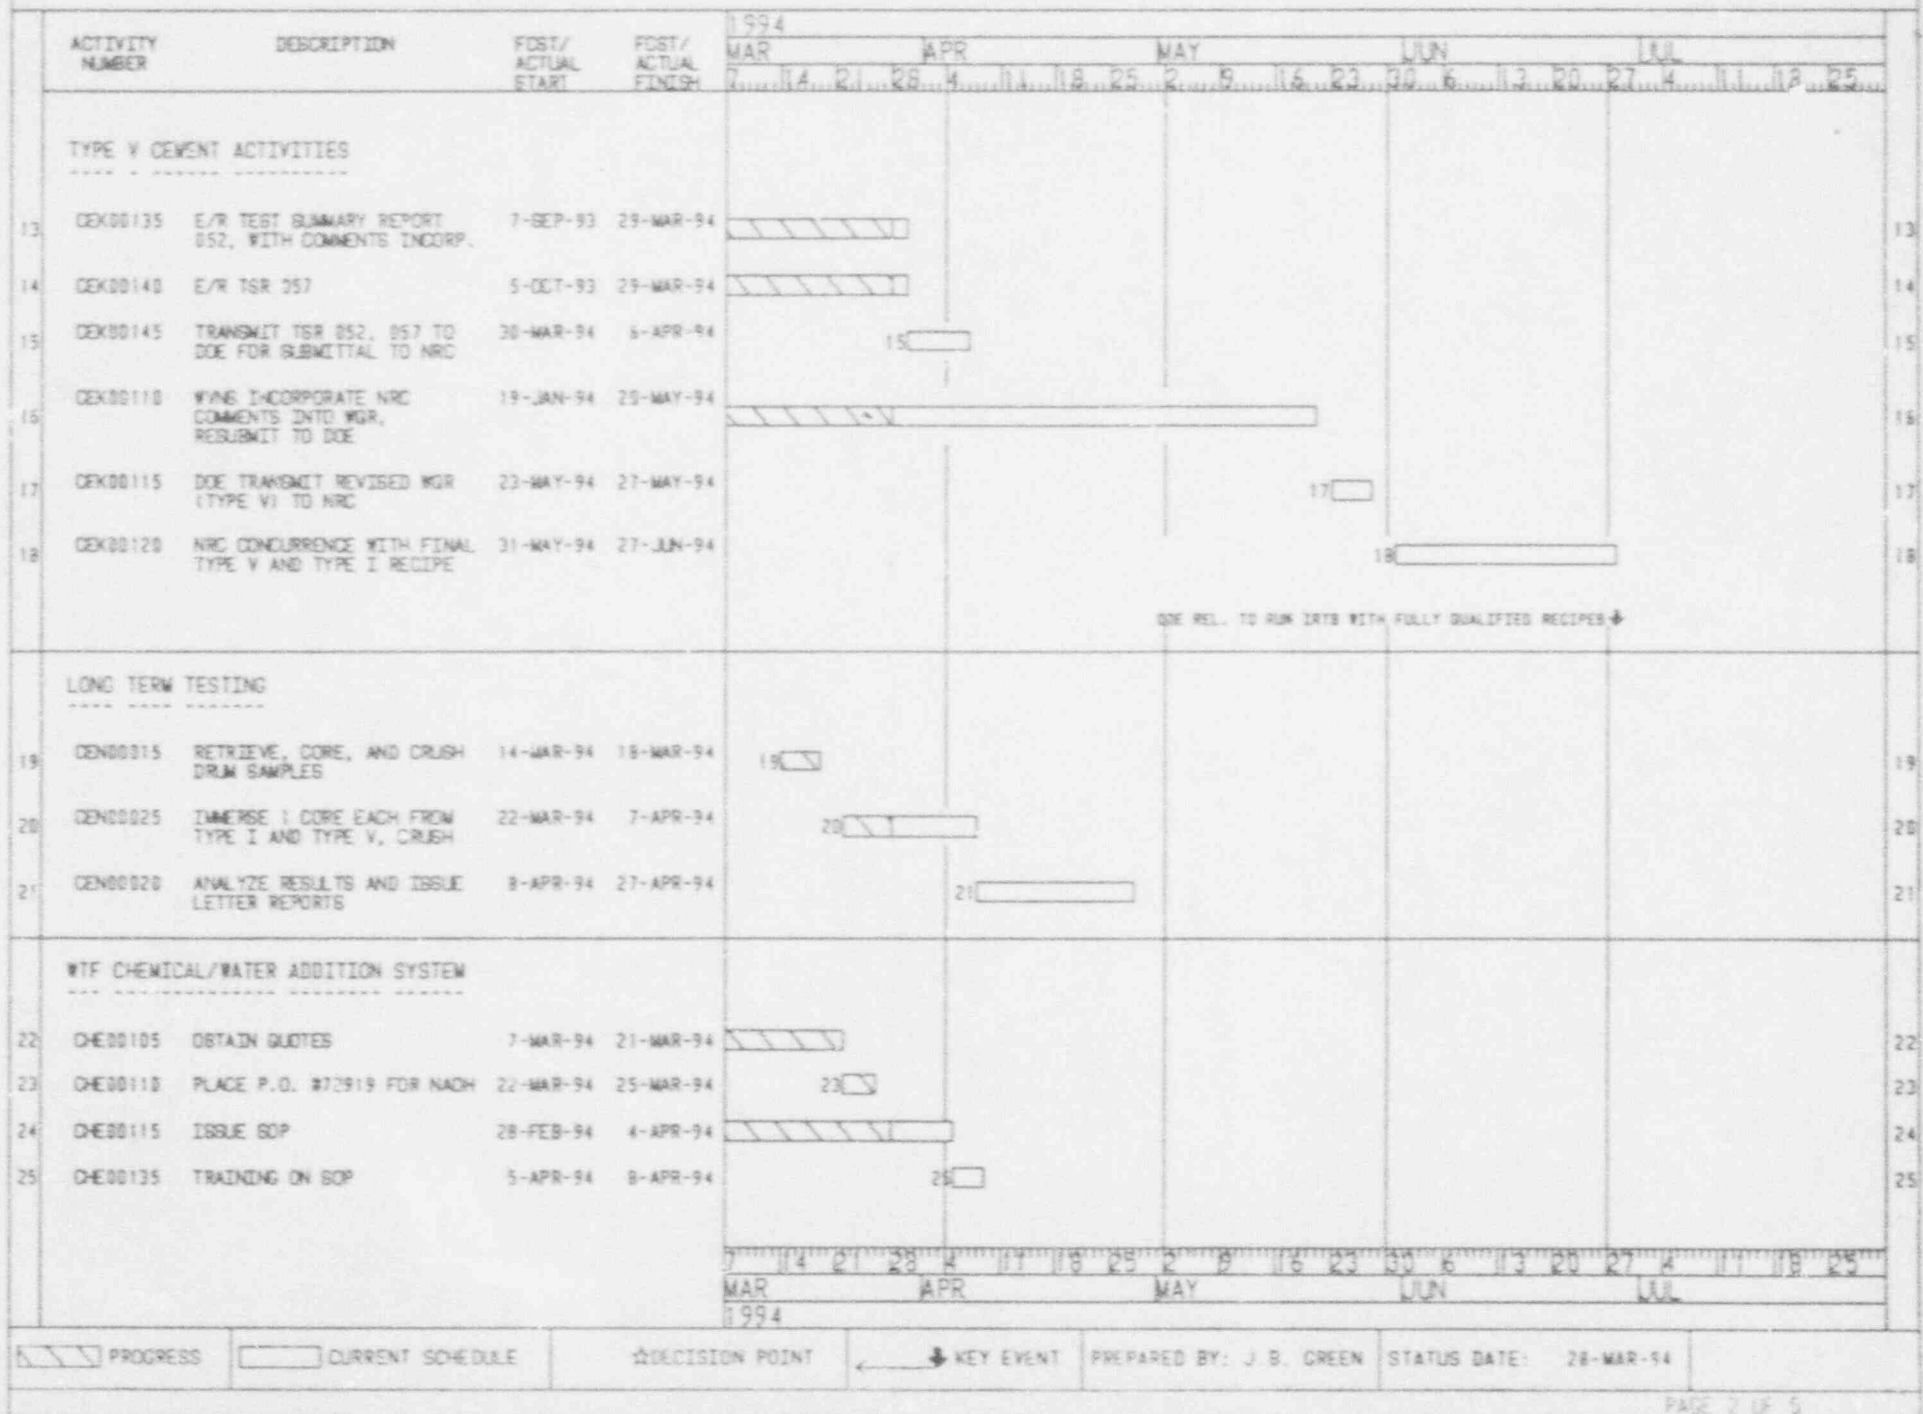

SCHEDULE OF MAJOR IRTS ACTIVITIES

| ACTIVITY NUMBER | DESCRIPTION | F0S1/ACTUAL START | FEST/ACTUAL FINISH | 1994 | | | | | | | |
|------------------------------------|--|-------------------|--------------------|------|-----|-----|-----|-----|--|--|--|
| | | | | MAR | APR | MAY | JUN | JUL | | | |
| RTF CHEMICAL/WATER ADDITION SYSTEM | | | | | | | | | | | |
| 26 | CH00125 MODIFY PUMP SUCTION LINE | 23-MAR-94 | 31-MAR-94 | | | | | | | | |
| 27 | CH00130 ISSUE TURN-OVER PACKAGE | 14-MAR-94 | 31-MAR-94 | | | | | | | | |
| COLUMN D DUMP VALVE DRILLING | | | | | | | | | | | |
| 28 | DMP00025 EVALUATE QUOTE/AWARD CONTRACT | 11-MAR-94 | 31-MAR-94 | | | | | | | | |
| 29 | DMP00105 MTD PROPOSE DEVELOPMENT AND TESTING PROGRAM | 4-APR-94 | 15-APR-94 | | | | | | | | |
| 30 | DMP00110 DEVELOP & TEST COMPLETE DRILLING PROCESS AT MTD | 18-APR-94 | 29-JUN-94 | | | | | | | | |
| 31 | DMP00115 SHIP ALL DRILLING EQUIPMENT TO WWS | 30-JUN-94 | 14-JUL-94 | | | | | | | | |
| 32 | DMP00120 SET UP EQUIPMENT IN TSB | 15-JUL-94 | 28-JUL-94 | | | | | | | | |
| 33 | DMP00990 WWS ISSUE LETTER TO DOE -- PROVIDE RECOMMENDATIONS FOR FUTURE DUMP VALVE ACTIVITIES | 17-FEB-94 | 31-MAR-94 | | | | | | | | |
| PIGGYBACK DUMP VALVE | | | | | | | | | | | |
| 34 | PGY00020 FABRICATE VALVES (P.O. #7111621 | 7-FEB-94 | 5-MAY-94 | | | | | | | | |
| 35 | PGY00025 TEST PROTOTYPE VALVE | 9-MAY-94 | 5-AUG-94 | | | | | | | | |
| PVS FILTER CHANGE | | | | | | | | | | | |
| 36 | PVS00110 PROCURE SHIELD BOXES | 7-MAR-94 | 20-MAY-94 | | | | | | | | |
| 37 | PVS00115 DESIGN AND PROCURE TENT | 28-MAR-94 | 29-APR-94 | | | | | | | | |

SCHEDULE OF MAJOR IRTS ACTIVITIES

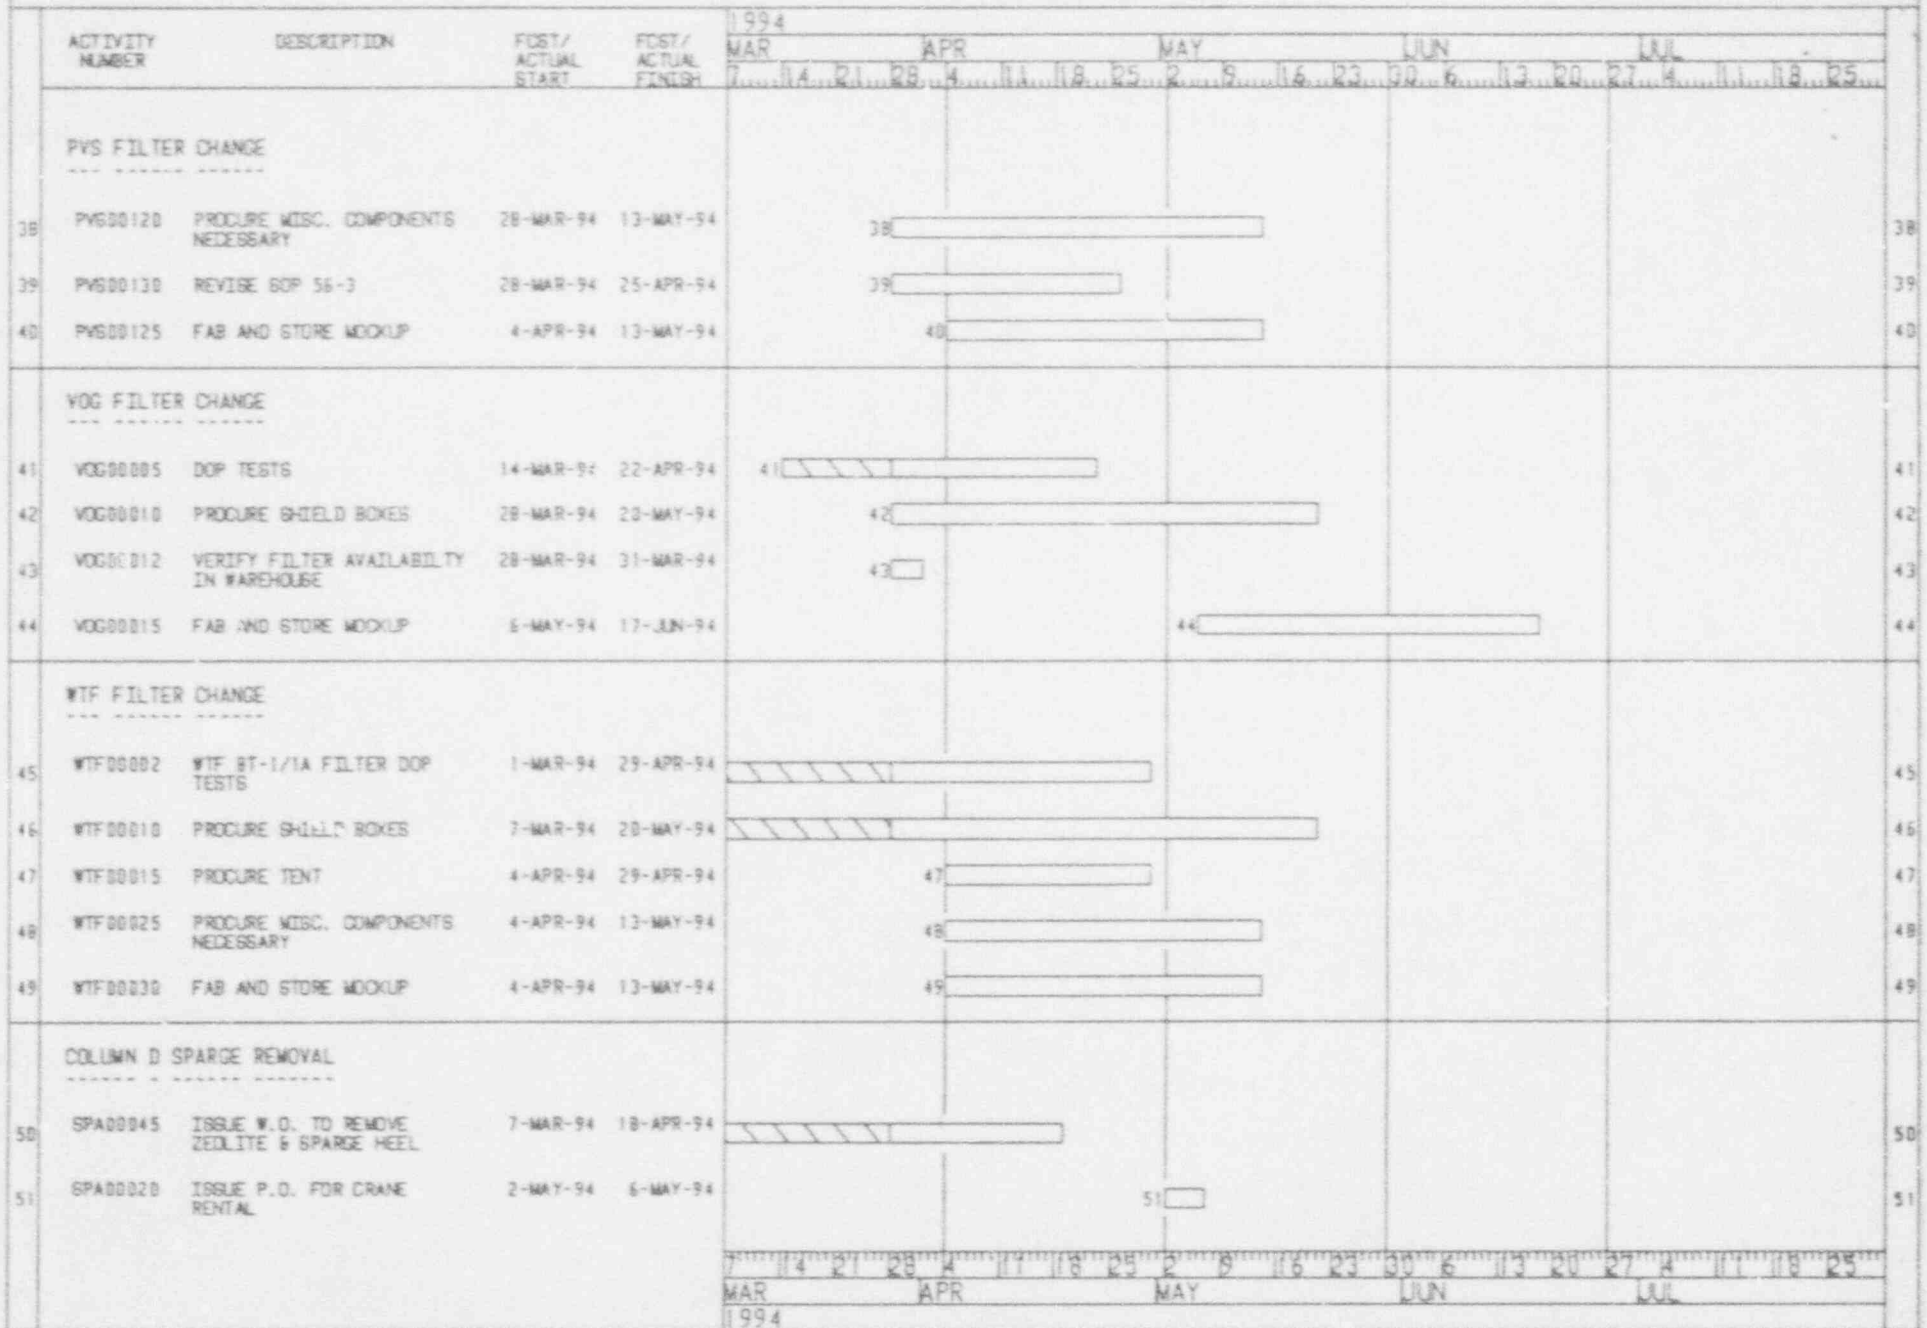

| | | | | | |
|----------|------------------|----------------|-----------|--------------------------|------------------------|
| PROGRESS | CURRENT SCHEDULE | DECISION POINT | KEY EVENT | PREPARED BY: J. B. GREEN | STATUS DATE: 28-MAR-94 |
|----------|------------------|----------------|-----------|--------------------------|------------------------|

SCHEDULE OF MAJOR IRTS ACTIVITIES

