


# Vogtle Unit 4 1Q/2022 Performance Summary

[Construction Action Matrix Column:](#)  
[Licensee Response](#)

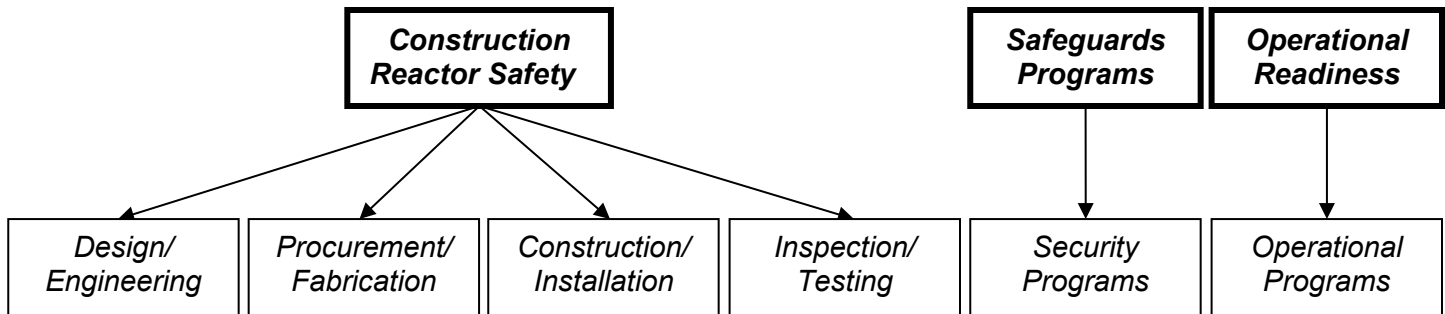

## Most Significant Inspection Findings

1Q/2022	No findings this quarter	No findings this quarter	No findings this quarter	No findings this quarter	No findings this quarter	No findings this quarter
4Q/2021	No findings this quarter	No findings this quarter	G	No findings this quarter	No findings this quarter	No findings this quarter
3Q/2021	No findings this quarter	No findings this quarter	No findings this quarter	No findings this quarter	No findings this quarter	No findings this quarter
2Q/2021	No findings this quarter	No findings this quarter	No findings this quarter	No findings this quarter	No findings this quarter	No findings this quarter

## Additional Inspection and Assessment Information

- ❖ [List of Construction Inspection Reports](#)
- ❖ [List of Construction Assessment Reports/Inspection Plans](#)
- ❖ [Vogtle Unit 4 Findings Archive](#)

## Design Engineering

---

[Back to Top](#)

## Procurement/Fabrication

---

[Back to Top](#)

## Construction/Installation

---

**Identified By:** NRC

**Identification Date:** 11/29/2021

**Significance:** Green

**Item Type:** Construction Finding

**Report:** Vogtle Electric Generating Plant, Units 3 And 4 - NRC Initial Test Program and Operational Programs Integrated Inspection Reports 05200025/2021008, 05200026/2021008

**Item Number:** 05200026/2021008-02

**Note:** Open in Report (NCV)

### Failure to Follow Procedure CNSITPP-502

NRC inspectors identified a construction finding of very low safety significance and an associated NCV of 10 CFR, Part 50, Appendix B, Criterion V, "Instructions, Procedures, and Drawings," for the licensee's failure to accomplish activities associated with local leak rate testing of electrical penetration 4-IDSC-EY-P29Y in accordance with procedure 4-CNS-ITPP-502, "Containment Penetration Leak Rate (Type B) Preoperational Test," Version 1.0. Specifically, the licensee failed to wait for flowmeter readings to stabilize prior to recording the leak rate data and inappropriately declaring the test acceptance criteria met. The licensee entered this issue into its CAP as CR 50116481.

The performance deficiency was determined to be of more than minor safety significance and thus a finding because it rendered the quality of a structure, system, or component (SSC) unacceptable or indeterminate and required substantial corrective action. The inspectors determined the finding was associated with the containment and was of very low safety significance (Green) because the issue did not affect a design function. The inspectors determined the finding had a cross-cutting aspect of training, in the area of Human Performance. Specifically, the organization failed to ensure that test personnel were trained to perform tests in a consistent manner.

[Back to Top](#)

## Inspection/Testing

---

[Back to Top](#)

## Security Programs

---

[Back to Top](#)

## Operational Programs

---

[Back to Top](#)
