


Vogtle Unit 4 4Q/2022 Performance Summary

[Construction Action Matrix Column:](#)
[Licensee Response](#)

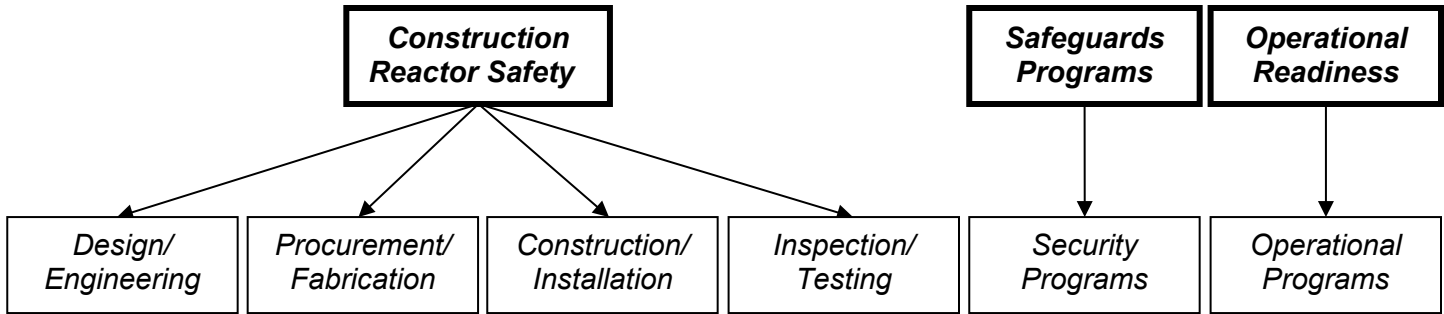

Most Significant Inspection Findings

| | | | | | | |
|---------|-----------------------------|-----------------------------|-----------------------------|-----------------------------|-----------------------------|-----------------------------|
| 4Q/2022 | No findings this quarter | No findings this quarter | G | No findings this quarter | No findings this quarter | No findings this quarter |
| 3Q/2022 | No findings this quarter | No findings this quarter | No findings this quarter | No findings this quarter | No findings this quarter | G |
| 2Q/2022 | No findings this quarter | No findings this quarter | No findings this quarter | No findings this quarter | No findings this quarter | No findings this quarter |
| 1Q/2022 | No findings this quarter | No findings this quarter | No findings this quarter | No findings this quarter | No findings this quarter | No findings this quarter |

Additional Inspection and Assessment Information

- ❖ [List of Construction Inspection Reports](#)
- ❖ [List of Construction Assessment Reports/Inspection Plans](#)
- ❖ [Vogtle Unit 4 Findings Archive](#)

Design Engineering

[Back to Top](#)

Procurement/Fabrication

[Back to Top](#)

Construction/Installation

Identified By: NRC

Identification Date: 10/25/2022

Significance: Green

Item Type: Construction Finding

Report: Vogtle Electric Generating Plant, Unit 4 - NRC Integrated Inspection Report 05200026/2022007

Item Number: 05200026/2022007-01

Note: Open/Closed in Report (NCV)

Failure to Include Certain Cables for Resistance Insulation (Megger) Testing

A construction finding of very low safety significance (Green) with an associated NCV of Title 10 of the Code of Federal Regulations (10 CFR), Part 50, Appendix B, Criterion V, "Instructions, Procedures, and Drawings," was identified for the licensee's failure to include the insulation resistance (megger) testing of certain "Y" service cables as required by specification APP-G1-V8-001 and procedure 26139-000-4MP-T81C-N3305, Appendix 1. The failure to include megger testing of certain "Y" service cables as required by the specification and the procedure was a violation of 10 CFR Part 50, Appendix B, Criterion V, and was a performance deficiency (PD). The licensee entered this issue into its corrective action program as condition reports 50159622 and 50164626. As immediate corrective actions, the licensee meggered the missed cable to restore compliance, commenced an extent of condition review, and initiated an evaluation of procedure revision.

The PD was of more than minor safety significance, and thus a finding, because it represented an adverse condition where the meggering requirements for the "Y" type service cables were not included in the testing procedure that rendered the quality of the safety function associated with the protection and safety monitoring system indeterminate and required substantive corrective action. Specifically, the failure to include the insulation resistance (megger) testing of certain "Y" service cables resulted in cable SV4-CVS-EWPLV045JYA not being megger tested and rendered the capability of letdown containment isolation valve CVS-PL-V045 indeterminate in the event of receiving a containment isolation signal. This violation was determined to be a construction finding because the finding is not material to the acceptance criteria of an ITAAC. The inspectors determined the finding was indicative of present licensee performance and was associated with the cross-cutting aspect of Documentation, in the area of Human Performance in accordance with IMC 0613, Appendix F, Construction "Cross-Cutting Areas and Aspects," dated November 4, 2020. The proximate cause of the PD was attributed the failure to create and maintain complete, accurate and up-to-date procedure documentation.

[Back to Top](#)

Inspection/Testing

[Back to Top](#)

Security Programs

[Back to Top](#)

Operational Programs

Identified By: NRC

Identification Date: 07/18/2022

Significance: Green

Item Type: Construction Finding

Report: Vogtle Electric Generating Plant, Unit 4 - NRC Initial Test Program and Operational Programs Integrated Inspection Report 05200026/2022006

Item Number: 05200026/2022006-01

Note: Open/Closed in Report (NCV)

NRC Annual Operating Test Scenarios Did Not Meet Qualitative Standards

NRC inspectors identified a construction finding of very low safety significance for the licensee's failure to identify the procedures required to be entered and expected operator actions to be performed in the simulator exam guides in accordance with NMP-TR-424-F05, "Annual Simulator Exam Development & Validation." Specifically, 9 out of 25 of the events in four sampled scenario guides used to evaluate licensed operators during the 2022 annual operating test lacked adequate crew/operator performance standards.

The performance deficiency was determined to be more than minor and a finding because it affected the training and qualification attribute of the Operational Readiness Cornerstone (Operational Programs). Specifically, the failure of the licensee to identify in simulator exam guides the required procedures to be entered and operator actions to be performed affected the quality of the 2022 annual operating test administered to all licensed operators and could have impacted the licensee's ability to evaluate the licensed operators. The performance deficiency did not impact an ITAAC, and therefore was determined to be a construction finding. The inspectors determined that the finding was associated with the Operational Readiness Cornerstone and assessed the finding in accordance with IMC 2519, "Construction Significance Determination Process," Appendix A, "AP-1000 Construction Significance Determination Process." Using the flowchart in Appendix A, since the finding was related to the licensed operator requalification (LOR) program, and the program was already required to be implemented, the finding was further assessed using the Reactor Oversight Process IMC 0609, "Significance Determination Process," (SDP) Appendix I, "Licensed Operator Requalification Significance Determination Process," Figure I.1, "Licensed Operator Requalification SDP Flowchart." The finding was related to the quality of the annual operating test but did not include greater than 40% of the reviewed simulator scenario events that were flawed; therefore, the inspectors determined that the finding was of very low safety significance (Green). The inspectors determined this finding was indicative of current licensee performance and was associated with the cross-cutting aspect of procedure adherence, in the area of human performance in accordance with IMC 0613, Appendix F, "Construction Cross-Cutting Areas and Aspects." The proximate cause was attributed to the failure to follow processes, procedures, and work instructions.

[Back to Top](#)
