

40-2377

KAISER ALUMINIUM
CORPORATE ENVIRONMENTAL

January 24, 2001

FEDERAL EXPRESS

Mr. John Buckley
Nuclear Regulatory Commission
TWFN, 7F27
Washington, DC 20555-0001


Re: Revised Kaiser Tulsa Adjacent Land Remediation Schedule

Dear Mr. Buckley:

Enclosed is the revised Kaiser Tulsa Adjacent Land Remediation Schedule. Unfavorable winter weather has caused delays in completing the field work. As a result, the schedule for completion is extended six weeks. Significant progress has been made in the last two weeks. If the weather cooperates, we expect to complete the field work by March 8, 2001.

If you have any questions concerning the enclosed, call me at 225/231-5116.

Very truly yours,




J. W. (Bill) Vinzant, P.E.
Project Manager

JWV/shh

- cc: Mr. Louis Carson II – United States Nuclear Regulatory Commission
- Ms. Pamela Bishop – Oklahoma Department of Environmental Quality
- Mr. Stephen L. Jantzen – State of Oklahoma
- Dr. Max Scott – ADA Consultants
- John Donnan – Houston
- Lamar Nichols – Tulsa
- Dave Tourdot – Earth Sciences
- Al Gutterman – Morgan, Lewis & Bockius
- Turgay Ertugrul – A&M
- Paul Handa – Tulsa
- U.S.N.R.C., Document Control Desk
- Scott Van Loo – City of Tulsa
- Mr. Harry Patterson – Union Pacific Railroad
- File – Tulsa – 3.12.07

NMSSOIPUBLIC

ADJACENT LAND AREA REMEDIATION KAISER ALUMINUM & CHEMICAL CORPORATION FACILITY

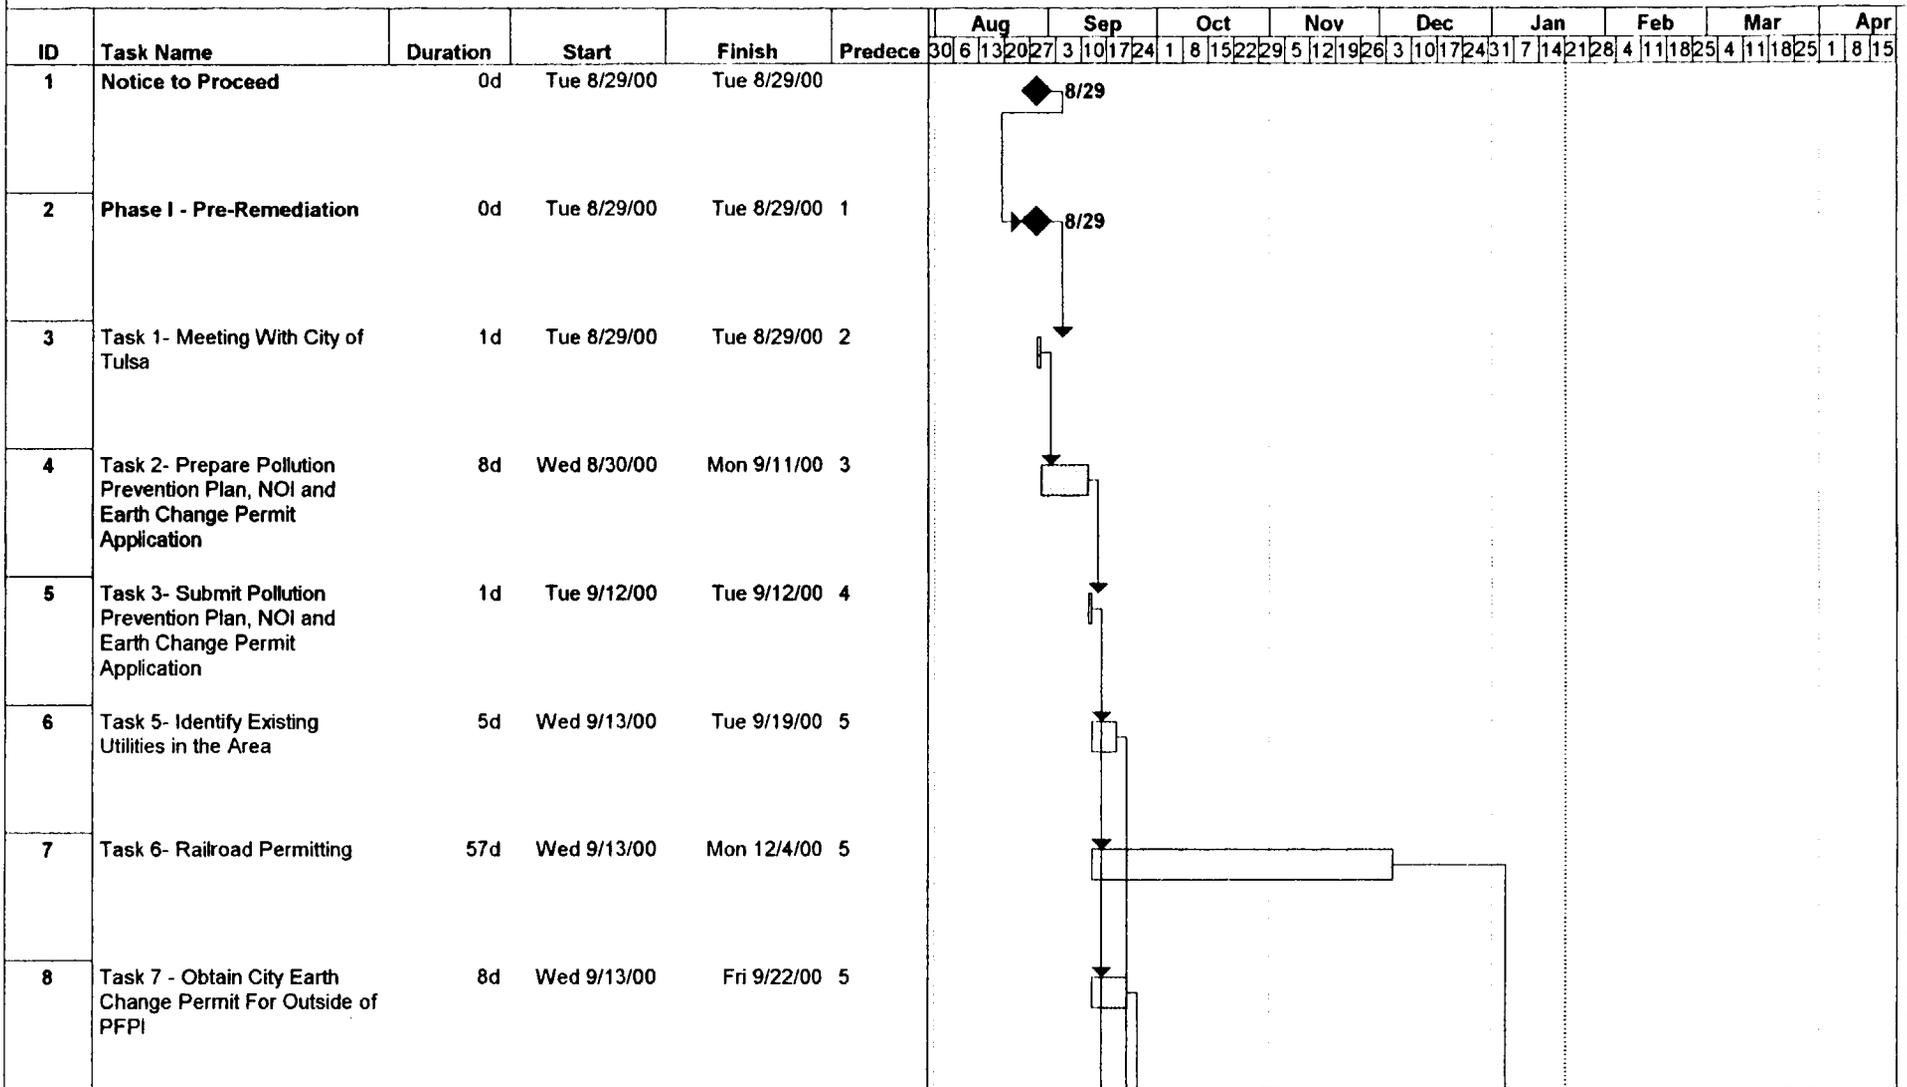

Project: KAISER ALUMINUM & CHEM Date: Sun 1/21/01	Task		Summary		Rolled Up Progress	
	Progress		Rolled Up Task			
	Milestone		Rolled Up Milestone			

ADJACENT LAND AREA REMEDIATION KAISER ALUMINUM & CHEMICAL CORPORATION FACILITY

ID	Task Name	Duration	Start	Finish	Predecessor	Aug		Sep		Oct		Nov		Dec		Jan		Feb		Mar		Apr											
						30	6	13	20	27	3	10	17	24	1	8	15	22	29	5	12	19	26	3	10	17	24	31	7	14	21	28	4
25	Task 9- Construct Decntamination Pad and Provide Water Supply	4d	Wed 9/27/00	Mon 10/2/00	21																												
26	Task 10- Survey and Grid the Contaminated Areas by Kaiser	4d	Wed 9/27/00	Mon 10/2/00	21																												
27	Phase III - Project Remediation	0d	Mon 10/2/00	Mon 10/2/00	22,23,24																												
28	Tasks 1- Beejay Inc. (Partial) and Red Man Properties- Soil Excavation, Segregation and Placement of Contaminated Soil in Stockpile	3d	Tue 10/3/00	Thu 10/5/00	27																												
29	Task 2- Screen and Final Survey the Excavation	3d	Fri 10/6/00	Tue 10/10/00	28																												
30	Task 3- Final Status Survey	3d	Wed 10/11/00	Fri 10/13/00	29																												
31	Task 4- Backfill Excavated Area with Clean Soil	1d	Mon 10/16/00	Mon 10/16/00	30																												
32	Task 5- Specific Systems Property- Soil Excavation, Segregation and Placement of Contaminated Soil in Stockpile Area	20d	Tue 10/17/00	Mon 11/13/00	31																												

Project: KAISER ALUMINUM & CHEN Date: Sun 1/21/01	Task		Summary		Rolled Up Progress	
	Progress		Rolled Up Task			
	Milestone		Rolled Up Milestone			

