




Survey Unit Release Record

Design #	EP-CRT-2	Revision #	Original	Page 1 of 3
Survey Unit #(s)	CRT-2			
Description	<p>1) Embedded Pipe (EP) Survey Unit CRT-2 meets the definition of embedded pipe for Plum Brook Reactor Facility (PBRF).</p> <p>2) EP CRT-2 is a Class 1, Group 1 survey unit as per the PBRF Final Status Survey Plan (FSSP) and Technical Basis Document (TBD)-06-004.</p> <p>3) Surveys in EP CRT-2 were performed using a scintillation detector optimized to measure gamma energies representative of Co-60. Sample #EP 3-9 from Survey Request (SR)-13 was referenced for this decision.</p> <p>4) Survey Instructions for this survey unit are incorporated into and performed in accordance with (IAW) the Babcock Services Incorporated (BSI)/LVS-002, Work Execution Package (WEP) 05-006. Survey instructions described in this document constitute "Special Methods" and the survey design used in the acquisition of survey measurements.</p> <p>5) Instrument efficiency determinations are developed in accordance with the BSI/LVS-002, WEP 05-006, these determinations are appropriate for the types of radiation involved and the media being surveyed.</p>			
Approval Signatures			Date:	
FSS/Characterization Engineer			11-12-07	
Technical Reviewer (FSS/Characterization Engineer)			11-14-07	
FSS/Characterization Manager	R. Case 		11/15/07	

Form CS-09/1 Rev 0

Survey Unit: CRT-2

1.0 History/Description

- 1.1 The subject pipe system is a 2.5" diameter penetration located on the CRT plate within the Sub Pile Room. The system access point is located on the -34' el. of the Rx building.
- 1.2 EP CRT-2 consists of 2.5" diameter piping that is approximately 3 feet in length.

2.0 Survey Design Information

- 2.1 EP CRT-2 was surveyed IAW Procedure #BSI/LVS-002.
- 2.2 100% of the piping was accessible for survey. The accessible pipe was surveyed by static measurement at one foot increments, for a total of 3 survey measurements.
- 2.3 The total surface area for the piping system is approximately 1,824 cm² (0.2 m²) for the entire length of (3') of piping.

3.0 Survey Unit Measurement Locations/Data

- 3.1 Pipe interior radiological survey forms are provided in Attachment 2 of this release record.

4.0 Survey Unit Investigations/Results

- 4.1 None

5.0 Data Assessment Results

- 5.1 Data assessment results are provided in the EP/Buried Pipe (BP) Survey Report provided in Attachment 1.
- 5.2 All measurement results are less than the Derived Concentration Guideline Level (DCGL) for radionuclide specific EP that corresponds to the 1 mrem/yr dose goal established in Table 3-3 of the FSSP.
- 5.3 When implementing the Unity Rule, provided in Section 3.6.3 of the FSSP, and applying the Nuclide Fraction (NF), provided in TBD-06-004, the survey unit that is constituted by EP CRT-2 passes FSS.
- 5.4 Background was not subtracted from the survey measurements and the Elevated Measurement Comparison (EMC) was not employed for this survey unit.

Survey Unit: CRT-2

5.5 Statistical Summary Table

Statistical Parameter	2.5" Pipe
Total Number of Survey Measurements	3
Number of Measurements >MDC	1
Number of Measurements Above 50% of DCGL	0
Number of Measurements Above DCGL	0
Mean	0.0545
Median	0.0178
Standard Deviation	0.0687
Maximum	0.1338
Minimum	0.0119

6.0 Documentation of evaluations pertaining to compliance with the unrestricted use limit of 25 mrem/yr and dose contributions from Embedded Pipe and radionuclides contributing 10% in aggregate of the total dose for both structural scenarios and soils.

6.1 A review of the survey results has shown that the dose contribution for EP CRT-2 to be less than 1 mrem/yr. The dose contribution is estimated to be 0.055 mrem/yr based on the average of the actual gross counts measured.

7.0 Attachments

Attachment 1 – BSI EP/BP Survey Report

Attachment 2 – Pipe Interior Radiological Survey Form

Attachment 3 – DQA Worksheet

Attachment 4 – Disc containing RR for EP CRT-2 & Spreadsheet

SECTION 7
ATTACHMENT 1
2 **PAGE(S)**



BSI EP/BP SURVEY REPORT

Pipe ID	EP CRT-2	Survey Location	Sub Pile Room Pen. -34 el.
Survey Date	24-Oct-07	2350-1 #	189094
Survey Time	16:30	Detector-Sled #	1MG1 LVS-1/ no sled
Pipe Size	2.5"	Detector Efficiency	0.00033
DCGL (dpm/100cm²)	2.41E+05	Pipe Area Incorporated by Detector Efficiency (in cm²)	608
Pipe Area Incorporated by Survey Data (m²)	0.2	Field BKG (cpm)	3.4
Routine Survey	X	Field MDCR (cpm)	10
QA Survey		Nominal MDC (dpm/100cm²)	3,927

Survey Measurement Results

Total Number of Survey Measurements	3
Number of Measurements >MDC	1
Number of Measurements Above 50% DCGL	0
Number of Measurements Above DCGL	0
Mean	0.0545
Median	0.0178
Standard Deviation	0.0687
Maximum	0.1338
Minimum	0.0119

Survey Technician(s)	FOWLER
-----------------------------	--------

Survey Unit Classification	1
TBD 06-004 Piping Group	1
SR-13 Radionuclide Distribution Sample	EP 3-9
Measured Nuclide	Co-60
Area Factor/EMC Used	No
Pass/Fail FSS	Pass
MREM/YR Contribution	<1

COMMENTS:
ACTIVITY VALUES NOT BACKGROUND CORRECTED

RP Engineer Date	<i>Dal Powell</i> 11-12-07
--------------------	----------------------------

EP CRT-2
2.5" Pipe
TBD 06-004 Group 1

Measurement #	gcpm	ncpm	Co-60 activity (total dpm)	Co-60 activity (dpm/100cm2)	Cs-137 activity (dpm/100cm2)	Eu-152 activity (dpm/100cm2)	Eu-154 activity (dpm/100cm2)	Nb-94 activity (dpm/100cm2)	Ag-108m activity (dpm/100cm2)	Unity
1	6	6	18,182	2,990	119	2,837	754	87	21	0.018
2	4	4	12,121	1,993	79	1,891	503	58	14	0.012
3	45	45	136,364	22,426	889	21,274	5,655	654	156	0.134
									MEAN	0.054
									MEDIAN	0.018
									STD DEV	0.069
									MAX	0.134
									MIN	0.012

SECTION 7
ATTACHMENT 2
2 **PAGE(S)**

Pipe Interior Radiological Survey Form

Date: 10-24-07 Time: 1630
 Pipe ID#: GRT-2 Pipe Diameter: 2.5" Access Point Area: Sub File Rm
 Building: CV Elevation: -34' System: Penetration
 Type of Survey Investigation Characterization Final Survey Other
 Gross Co60 Cs
 Detector ID# / Sled ID# 1MG1/LVS-1 / No Sled
 Detector Cal Date: 1-11-07 Detector Cal Due Date: 1-11-08
 Instrument: 2350-1 Instrument ID #: 189094
 Instrument Cal Date: 1-11-07 Instrument Cal Due Date: 1-11-08

From the Daily Pipe Survey Detector Control Form for the Selected Detector

Background Value 3.4 cpm
 MDCR_{static} 10 cpm
 Efficiency Factor for Pipe Diameter 0.00033 (from detector efficiency determination)

MDC_{static} 3927 dpm/ 100 cm²

Is the MDC_{static} acceptable? Yes No (if no, adjust sample count time and recalculate MDCR_{static})

Comments: Post Decon 100%, Complete

Technician Signature R. Ferrel

Pipe Interior Radiological Survey


Position #	Feet into Pipe from Opening	Count Time (min)	Gross Counts	Gross cpm	Net cpm	dpm/100cm ²
1	1	1	6	6	n/a	n/a
2	2	↓	4	4	↓	↓
3	3	↓	45	45	↓	↓
4						
5						
6						
7						
8						
9						
10						

Package Page 1 of 2

North
↓

IT-12

CRT Plate
↓

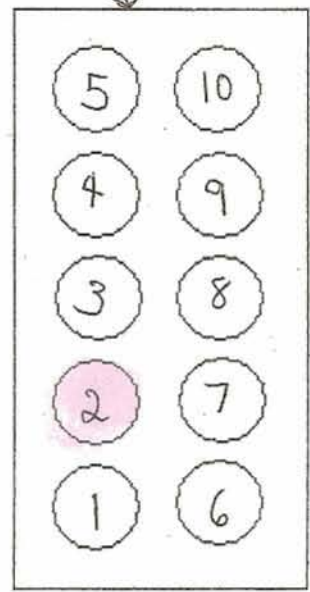

IT-14

IT-13

IT-11

REFERENCE COPY

PAGE 2 of 2

SECTION 7
ATTACHMENT 3
 1 **PAGE(S)**

DQA Check Sheet

Design #	EP CRT-2	Revision #	Original	
Survey Unit #	EP-CRT-2			

Preliminary Data Review

Answers to the following questions should be fully documented in the Survey Unit Release Record	Yes	No	N/A
1. Have surveys been performed in accordance with survey instructions in the Survey Design?	X		
2. Is the instrumentation MDC for structure static measurements below the DCGL _w for Class 1 and 2 survey units, or below 0.5 DCGL _w for Class 3 survey units?			X
3. Is the instrumentation MDC for embedded/buried piping static measurements below the DCGL _w ?	X		
4. Was the instrumentation MDC for structure scan measurements, soil scan measurements, and embedded/buried piping scan measurements below the DCGL _w , or, if not, was the need for additional static measurements or soil samples addressed in the survey design?			X
5. Was the instrumentation MDC for volumetric measurements and smear analysis < 10% DCGL _w ?			X
6. Were the MDCs and assumptions used to develop them appropriate for the instruments and techniques used to perform the survey?	X		
7. Were the survey methods used to collect data proper for the types of radiation involved and for the media being surveyed?	X		
8. Were "Special Methods" for data collection properly applied for the survey unit under review?	X		
9. Is the data set comprised of qualified measurement results collected in accordance with the survey design, which accurately reflects the radiological status of the facility?	X		

Graphical Data Review

1. Has a posting plot been created?			X
2. Has a histogram (or other frequency plot) been created?			X
3. Have other graphical data tools been created to assist in analyzing the data?			X

Data Analysis

1. Are all sample measurements below the DCGL _w (Class 1 & 2), or 0.5 DCGL _w (Class 3)?	X		
2. Is the mean of the sample data < DCGL _w ?	X		
3. If elevated areas have been identified by scans and/or sampling, is the average activity in each elevated area < DCGL _{EMC} (Class 1), < DCGL _w (Class 2), or < 0.5 DCGL _w (Class 3)?			X
4. Is the result of the Elevated Measurements Test < 1.0?			X
5. Is the result of the statistical test (S+ for Sign Test or W_r for WRS Test) ≥ the critical value?			X

Comments:

FSS/Characterization Engineer (print/sign)	<i>Dale Randall / Dale Randall</i>	Date	11-12-07
FSS/ Characterization Manager (print/sign)	R. Case <i>[Signature]</i>	Date	11/15/07

Form
 CS-09/2
 Rev 0

**SECTION 7
ATTACHMENT 4
1 DISC**
