



plant status daily archives enter daily plant status save

Oconee Information for 09/03/2009 (Modify/Update)

Outside of Scope

Outside of Scope

Significant TS / Issues:

ASW PIPING LEAK: Work continues on the excavation phase of the restoration of the ASW system to address the OBDN condition. Currently, approximately 4.5' of soil has been removed and support I-beams installed to allow shoring to be used in order to expose the old piping and the area where the new piping will come through the SSF building wall below-grade. Fabrication of the replacement piping is in progress. The current schedule shows installation of the new piping and exiting the OBDN status on or around 9/17/09.

9:15 mtg. Yes No

delete
Picture 006.jpg

delete
Picture 008.jpg


delete
I-Beams.jpg

Information in this record was deleted in accordance with the Freedom of Information Act Exemptions Outside of Scope FOIA/PA 201-0021

9/7

Outside of Scope

Outside of Scope

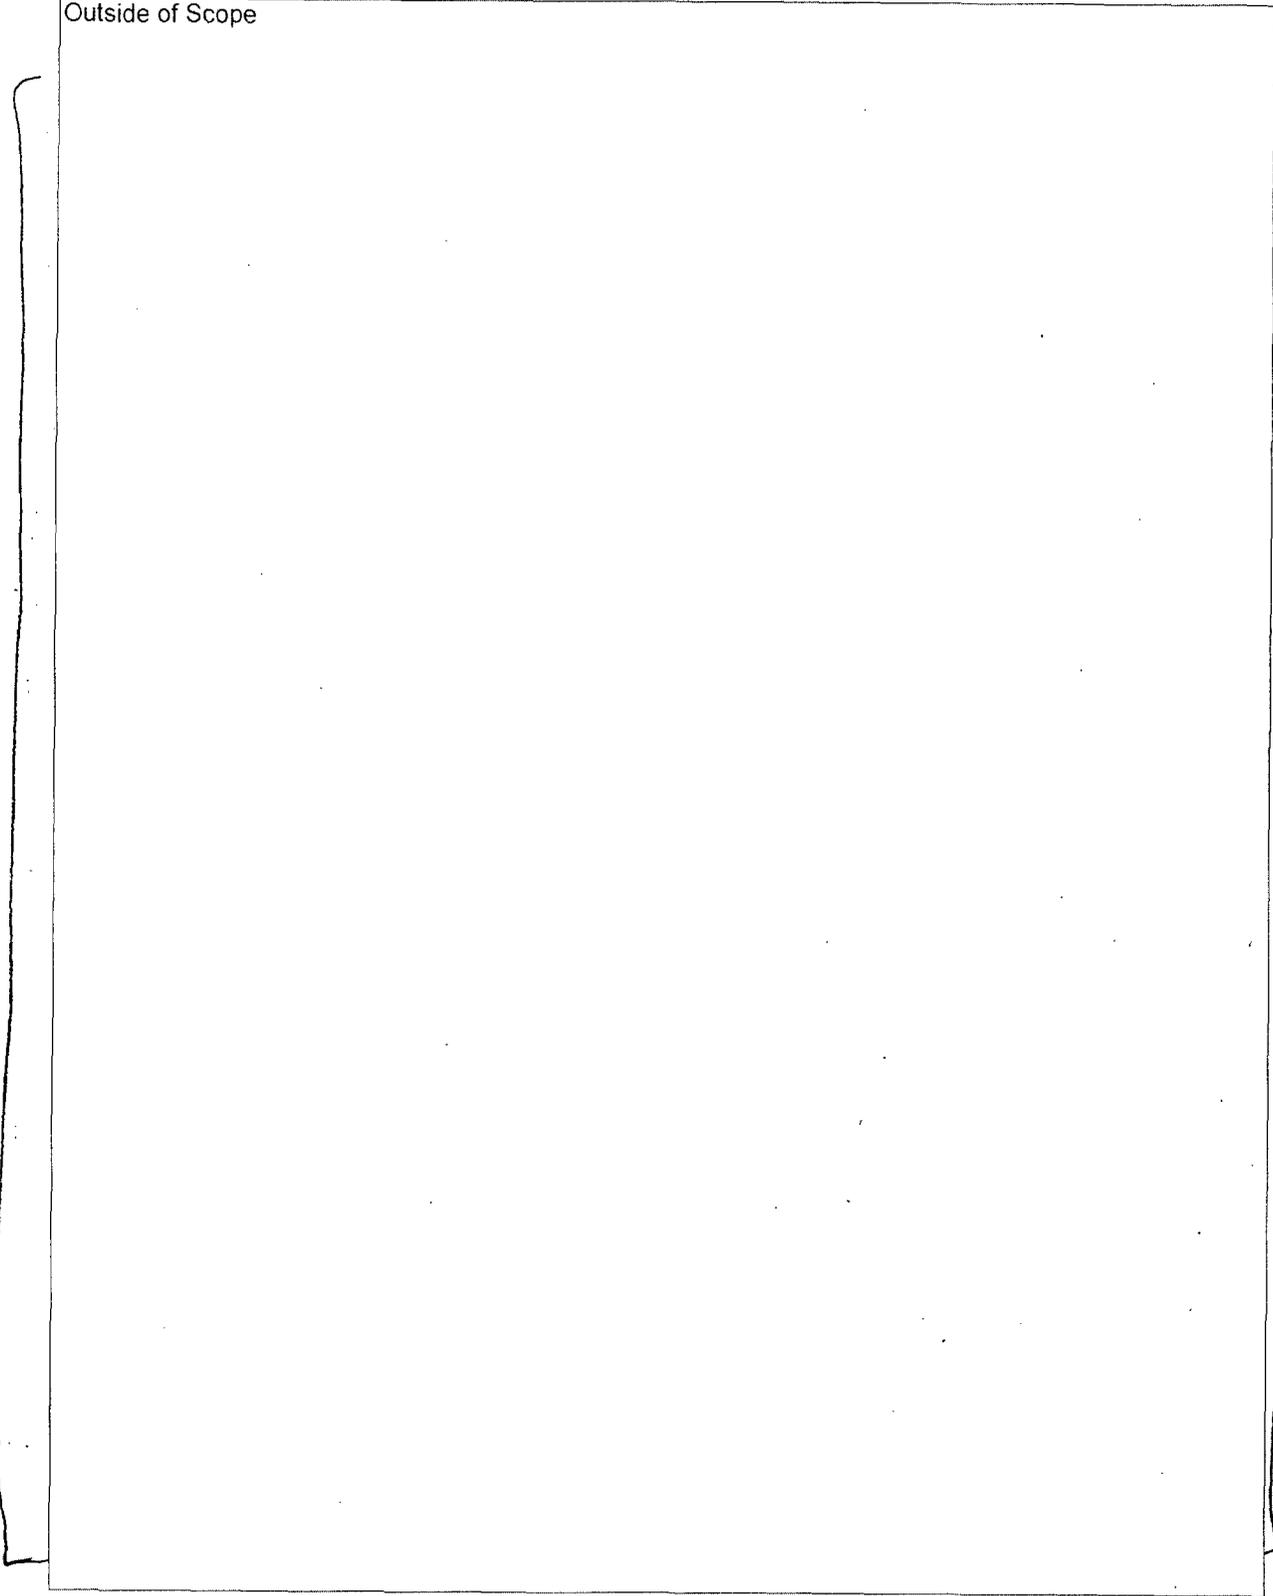

Outside
of
Scope

