

OP 359, Field Activity Documentation



CABRERA DAILY REPORT

1. PROJECT INFORMATION

PROJECT NAME/LOCATION: SUPPLEMENTAL RADIOLOGICAL SURVEY
Former UNC Manufacturing Facility, New Haven, CT

DATE: 05/24/17

REPORT NO. 066

CONTRACT #:

CABRERA PROJECT #: 10-1007.00

TASK #: 016

FIELD SITE MANAGER: Mike Plonski

PROJECT MANAGER: Rob Flowers

2. WEATHER

TEMPERATURE RANGE: 46-74 degrees F

WIND SPEED/DIRECTION: 5-25 mph E

PRECIPITATION LAST 24 HOURS: YES NO

TYPE: RAIN

AMOUNT: .27"

BAROMETRIC PRESSURE: 29.81"

HUMIDITY: 50-95%

HEAT INDEX RANGE: N/A

WEATHER DELAYS: YES NO

DELAY TIME (HOURS): N/A

3. SUMMARY OF WORK

- Conducted safety meeting prior to beginning field activities.
- Cabrera completed daily quality control checks on gamma spec and other radiological counting instrumentation.
- Cabrera continued to provide radiological support during ACM abatement activities, including air monitoring and general contamination control monitoring.
- AIG continued abatement of containment #8.
- Cabrera continued radiological surveys of drums and large debris.
- R. Powell from NRC on site for a tour of the building and update on progress.

4. MATERIALS & EQUIPMENT BROUGHT ON-SITE

Receipt inspection required & completed? Yes No

5. INSPECTIONS

TYPE	DESCRIPTION	ACTION
PREPARATORY		
INITIAL		
FOLLOW-UP		

ARE ANY DEFICIENCIES NOTED IN FOLLOW-UP INSPECTIONS? Yes No

6. DEFICIENCIES CORRECTED			
DEFICIENCY #	REPORT REFERENCE	DESCRIPTION	ACTION

7. TESTS PERFORMED		
SPECIFICATION REFERENCE	TYPE	TEST & RESULT

ARE TEST RESULTS ATTACHED? YES NO NA – IF NO, EXPLAIN:

8. CABRERA PERSONNEL ON-SITE		
EMPLOYEE NAME	TITLE	TASK(S) PERFORMED
Mike Plonski	Site Radiation Safety Lead (SRSL)	See Section 3 "Summary of Work" (8 Hrs)
Jon Cote	HP TECH	See Section 3 "Summary of Work" (8 Hrs)

9. SUBCONTRACTOR PERSONNEL ON-SITE				
SUBCONTRACTOR NAME	JOB DUTY	TASK(S) PERFORMED	# OF PERSONNEL	MAN-HOURS
AIG	Asbestos abatement	Asbestos abatement	7	56
TOTALS			7	56

10. EQUIPMENT & MATERIALS ON-SITE					
VENDOR	EQUIPMENT	SERIAL #.	ACTIVE OR IDLE	DATE RECEIVED	DATE RETURNED
ERG	1 Ludlum 2360 scaler/rate meter with 43-93 Zinc sulphide scintillation probe	184909/ PR298426	Active	02/21/2017	
ERG	1 Ludlum 2360 scaler/rate meter with 43-93 zinc sulphide scintillation probe	193638/ PR199836	Active	02/21/2017	
ERG	1 Ludlum 2360 scaler/rate meter	220242	Active	02/21/2017	
ERG	1 Ludlum 2221 scaler/ digital rate meter with FIDLER sodium iodide scintillation probe	190205/ PR01807D	Active	02/21/2017	
ERG	1 Ludlum 2929 scaler sample counter with 43-10-1 zinc sulphide scintillation probe	200051/ PR215948	Active	02/21/2017	
ERG	1 Ludlum model 12 meter with 44-9 Geiger-Mueller probe	276863/ PR147787	Active	02/21/2017	
ERG	Escort ELF Lapel Air sampler	A3-48588		02/21/2017	
ERG	1 MircoRem meter	2079		02/21/2017	
ERG	1 Low volume air sampler			02/21/2017	
ERG	1 Low volume air sampler			02/21/2017	
Cabrera	1 Th-230 check source	5648-06	Active	02/21/2017	
Cabrera	1 Tc-99 check source	5634-05	Active	02/21/2017	
Cabrera	1 Co-60 check source	267D21	Active	02/21/2017	
Cabrera	1 Ludlum model 2224-1 scaler/rate meter with 43-93 Zinc sulphide scintillation probe	227246/ PR244549	Active	02/21/2017	
Cabrera	1 Ludlum Model 3 rate meter with 44-9 Geiger-Mueller probe	219266/ PR	Active	02/21/2017	
Canberra	Gamma Spectroscopy Instrument (Canberra REGe)	SN 8381	Active	03/06/2017	
United Rentals	1 Bobcat T5 90 Skid Steer		Active	02/21/2017	
United Rentals	1 set of forks, and 1 grapple bucket for Skid Steer		Active	02/21/2017	
United Rentals	1 Magnum 130 tow behind generator			02/21/2017	
NEMF	Wheel Scale			02/21/2017	
Williams Scotsman	1 8' by 20' connex box		Active	06/22/2016	
United Rentals	Scaffold			03/23/2017	5/23/2017
United Rentals	1 heater			03/23/2017	

11. MATERIAL GENERATED/STORED ON-SITE

MATERIAL ID	SOLID, LIQUID, OR MIXED	DESCRIPTION OF MATERIAL	CONTAINER TYPE	DISPOSITION OR LOCATION OF MATERIAL	AMOUNT* (CY OR TONS)
BFLU000011	Solid	Soil/ Garbage/ Debris/ ACM	Intermodal	Building 6H	~12.35 Tons
GFLU001451	Solid	Soil/ Garbage/ Debris/ ACM	Intermodal	Building 6H	~10.05 Tons
GFLU002120	Solid	Soil/ Garbage/ Debris/ ACM	Intermodal	Building 6H	~ 12.4Tons
GFLU002008	Solid	Soil/ Garbage/ Debris/ ACM	Intermodal	Building 6H	~12.09 Tons
GFLU001483	Solid	Soil/ Garbage/ Debris/ ACM	Intermodal	Building 6H	~12.93 Tons
GFLU002198	solid	Soil/ Garbage/ Debris/ ACM	Intermodal	Building 6H	~7.83 Tons
BFLU000074	solid	Soil/ Garbage/ Debris/ ACM	Intermodal	Building 6H	~7.81 Tons
ERRU000226	solid	Soil/ Garbage/ Debris/ ACM	Intermodal	Building 6H	~7.34 Tons
ERRU000312	Solid	Soil/ Garbage/ Debris/ ACM	Intermodal	Building 3H	~8 Tons
MHFU-002362	Solid	Soil/ Garbage/ Debris/ ACM	Intermodal	Building 3H	~8 Tons
GFLU-002165	Solid	Soil/ Garbage/ Debris/ ACM	Intermodal	Building 3H	~8 Tons
GFLU-002002	Solid	Soil/ Garbage/ Debris/ ACM	Intermodal	Building 3H	~11.65 Tons
GFLU002079	Solid	Soil/ Garbage/ Debris/ ACM	Intermodal	Building 6H	~12.74 Tons
Totals					~131.19 Tons

ATTACH SEPARATE PAGES AS NEEDED. SEPARATE PAGES INCLUDED? YES NO

12. SAMPLE COLLECTION & ANALYSIS

Sample ID/Spectrum ID	Media (Soil Water, Other)	Sampler Initials	On-Site or Off-Site Lab	Analyses / Type	Count time (min) Does not include setup	Photo File #

ATTACH SEPARATE PAGES AS NEEDED. SEPARATE PAGES INCLUDED? YES NO

13. CHANGES/DELAYS/CONFLICTS

ANY CHANGES IN SITE CONDITIONS OCCUR TODAY? Yes No

IF YES, EXPLAIN:

DID A DELAY OR WORK STOPPAGE OCCUR TODAY? Yes No

IF YES, EXPLAIN:

HAS ANYTHING DEVELOPED IN THE WORK WHICH MAY LEAD TO A CHANGE? Yes No

IF YES, EXPLAIN:

14. VERBAL INSTRUCTIONS RECEIVED:

15. HEALTH & SAFETY SUMMARY	
SAFETY BRIEFINGS	
WAS A SAFETY MEETING HELD? <input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	TOPIC DISCUSSED: PPE, machine safety (skid steer, scissor lift), slips-trips-falls, slippery conditions
SAFETY INSPECTIONS	
WAS A SAFETY INSPECTION CONDUCTED? <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
DEFICIENCIES NOTED: <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	DESCRIBE:
CORRECTIVE ACTIONS TAKEN: <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	DESCRIBE:
SUMMARY OF WORK PERFORMED	
TYPE OF WORK:	Refer to description provided in Section 3
CHEMICALS USED:	None
PPE LEVEL:	Safety shoes, hard hats, and eye protection, safety vest
INCIDENT & NEAR MISS/OBSERVATION REPORTING	
ANY INCIDENTS ON-SITE TODAY? <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	DESCRIPTION:
CABRERA INCIDENT REPORTING FORM ATTACHED: <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
CLIENT SPECIFIC INCIDENT REPORTING FORM ATTACHED: <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	
ANY NEAR MISSES/OBSERVATIONS ON-SITE TODAY? <input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	DESCRIPTION:
H&S RECOMMENDATIONS	

16. REMARKS
<p>We are expecting more rain in the coming days and will continue survey of the floor when the areas can be dried.</p> <p>Ray Powell from NRC was onsite for about an hour and was very happy with the progress we have been making with all that challenges this project has faced, deterioration of the building and weather. We did a full site tour including a quick hello with Mr. Katz. He told us to keep up the good work and he can't wait to see the final survey report.</p>

17. VERIFICATION STATEMENT	
This report is complete and correct and all materials and equipment used and work performed during this reporting period are in compliance with the contract plans and specifications except as noted above.	
NAME/TITLE: Mike Plonski	SIGNATURE:
DATE: 05/25/17	

18. PROJECT MANAGER REVIEW & ACCEPTANCE

REMARKS AND/OR EXCEPTIONS TO REPORT:

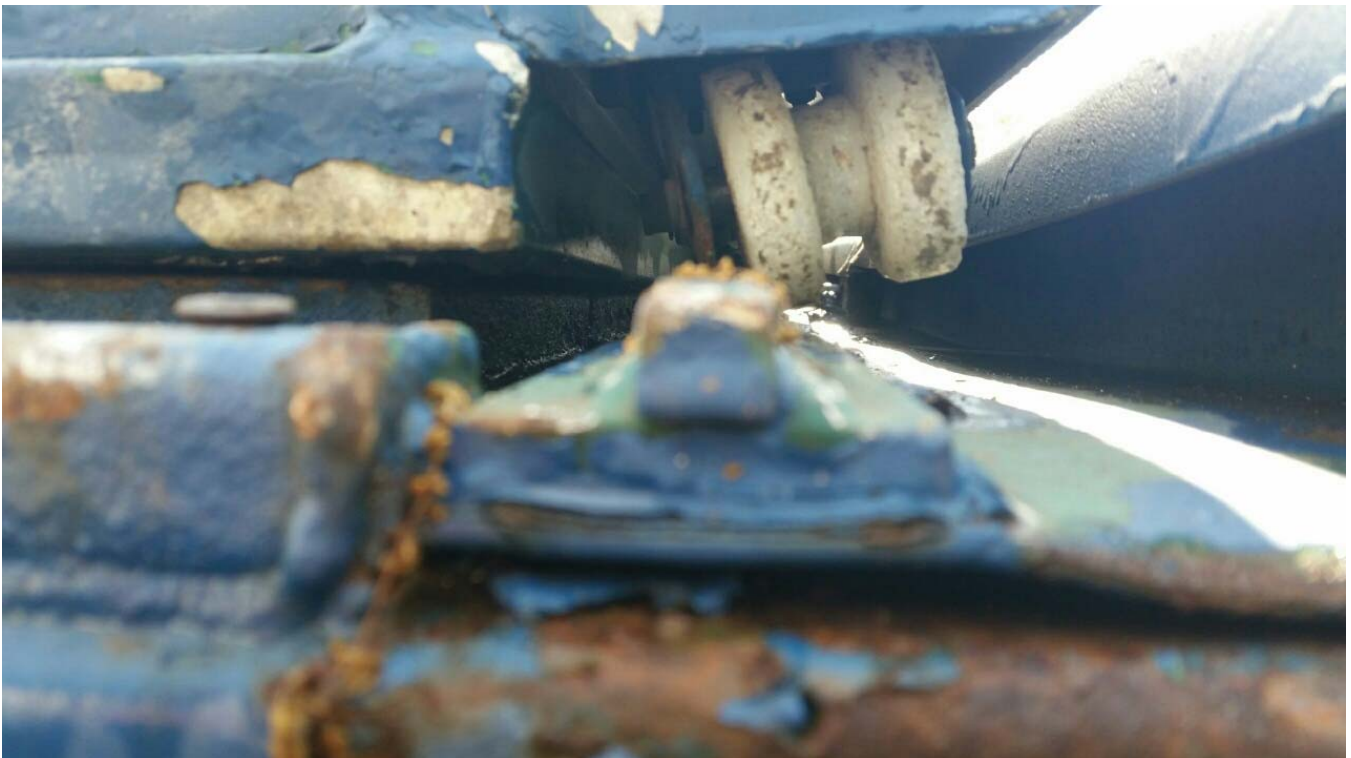
ACCEPTANCE

NAME/TITLE: Greg Bright, Deputy Project Manager

SIGNATURE:

DATE: 05/25/17

PHOTOS



Pictures of rejected IMC.
Broken roller pins were discovered on incoming inspection.

SIX QUESTIONS FOR SUCCESS – Take two minutes to think through and answer these questions:

1. What are we about to do?
2. What equipment are we going to use?
3. Have I/we been trained to use this equipment?
4. Have I/we been trained to do this job?
5. How can I/we be hurt?
6. How can I/we prevent this incident?

If you and your team aren't prepared to do the assigned work, STOP WORK, and take time to properly prepare.

This sign-in log documents the topics of the safety meeting and individual attendance. Personnel who perform work operations onsite are required to attend and acknowledge their ability to ask questions and receipt of such briefings daily. Please provide a brief narrative of the selected topics as applicable to the Project in the comment box (ex. Name of AHA reviewed).







PROJECT NAME & LOCATION UNC New Haven, New Haven, CT

PROJECT NO. 10-1007.00	DATE/TIME 5/24/17 0700	WEATHER CONDITIONS Rain 70's
----------------------------------	----------------------------------	--

Topic Discussion – check one			
Today's Scope of Work (All tasks)	<input checked="" type="checkbox"/> yes	<input type="checkbox"/> n/a	Access / Egress / Slips, Trips, & Falls
Schedule / New Work / Scope Changes	<input type="checkbox"/> yes	<input type="checkbox"/> n/a	Smoking, Eating, & Drinking
Reviewed Procedures, AHA, etc.	<input type="checkbox"/> yes	<input type="checkbox"/> n/a	Washroom / Facilities Location
Emergency Action Plan & Procedures	<input type="checkbox"/> yes	<input type="checkbox"/> n/a	Heat/Cold Stress
Communications Protocol	<input type="checkbox"/> yes	<input type="checkbox"/> n/a	Exclusion Areas Barricades / Cones
Required PPE	<input type="checkbox"/> yes	<input type="checkbox"/> n/a	Required Permits, Passes, Keys, etc.
Required Monitoring / Instruments	<input type="checkbox"/> yes	<input type="checkbox"/> n/a	Decon Procedures / IDW Mgmt.
Site Control / Work Zones / Security	<input type="checkbox"/> yes	<input type="checkbox"/> n/a	Eqpmt. Inspections/Safety Checklists

OTHER/COMMENTS:

Safety Meeting Attendees

Print Name	Signature
Andrew Baginski	
Fred Perches	
Chris Povera	
Guadalupe Gutierrez	
RICHARD FLORE	
Daniel Alvarri	

Safety Meeting Leader

<u>Mike Plonski</u>	
Name of Meeting Leader	Signature

Joselito R Flore

Trotter

OP 555 - Safety Meetings

~~Andrew B...~~
Jon Cotel
Ray Powell

~~John G...~~
John Powell
