

Kr 85 > 9.7 Ci (Less Than Background)

Particulate > 1.8⁺¹² LLD

6. Planned Release or Discharge Next Period

None

7. Radiological Waste Shipments

A. Special Limits on Shipments - none

B. Shipments Past Period (Last Working Day) - None

C. Planned Shipment Next Period (Next 2 Working Days)

Auxiliary Building Sludge Sample to SAI in Rockville, Md.,
on September 11, 1980

150 Milliliter RCS Sample to Idaho on September 12, 1980

DOE Archives Sample Drum to Idaho on September 12, 1980

8. Major Evaluations Next 24 Hours

A. Functional Testing in Mini Decay Heat Removal System Contin-
ues, Projected Startup September 22, 1980

B. Decon MU-F 5A & B, 2A & B Housing, Dry Run on September 10,
1980, Pull on September 11, 1980

C. Flush Sample Sink Line Connecting Unit I with Unit II

9. Problems

None


10. Progress vs. Schedule

Functional Testing on MDHR. Projected Oper. Date Sept. 22, 1980

11. N/A

12. Potential Public Interest Items - None

13. Non-routine NRC Audits - None

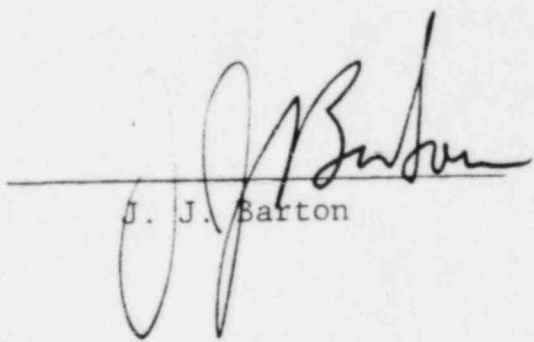

J. J. Barton

JJB/jw

cc: J. W. Brasher
J. T. Collins, U.S. NRC
J. C. Devine
B. D. Elam
S. Polon
File
