


THE  
B&W OWNERS GROUP

Arkansas Power & Light Company  
Duke Power Company  
Florida Power Corporation  
GPU Nuclear Corporation

ANO-1  
Oconee 1, 2, 3  
Crystal River 3  
TMI-1



Sacramento Municipal Utility District  
Toledo Edison Company  
San Valley Authority  
Wilcox Company

Rancho Seco  
Davis Besse  
Bellefonte 1,2

Working Together to Economically Provide Reliable and Safe Electrical Power

Suite 525 • 1700 Rockville Pike • Rockville, MD 20852 • (301) 230-2100

August 1, 1989  
OG-541

Mr. D. M. Crutchfield  
Associate Director for Projects  
Office of Nuclear Reactor Regulation  
U.S. Nuclear Regulatory Commission  
Washington, D. C. 20555

Subject: Transmittal of June 1989 Update of SPIP  
Recommendation Tracking System Report

Dear Mr. Crutchfield:

This letter transmits the June 1989 update of the portions of the B&W Owners Group (B&WOG) Recommendation Tracking System (RTS) Report applicable to the Safety and Performance Improvement Program (SPIP). This report updates the March 1989 report sent you by our letter of April 26, 1989.

As in the previous updates, the report provides the implementation status of the SPIP recommendations at each of the B&WOG utilities with operating plants. Also included is the estimated date for completion of the current implementation phase for each recommendation that has not yet been closed out. Changes in the implementation status information will be submitted to the NRC in future updates of the RTS report.

The implementation status of the recommendations at the Rancho Seco plant of Sacramento Municipal Utility District has been retained in this update although the plant has been shut down due the local voter mandate. The status information, however, has not been updated since the March 1989 report.

There were no revisions, additions or deletions of any of the recommendations since the last report.

Also included herewith are charts indicating the recent progress made by the B&WOG utilities on an aggregate basis in implementing the SPIP recommendations. One chart addresses all the recommendations, while the other addresses only the key recommendations. The progress shown on the charts covers the

8908070314 890801  
PDR TOPRP EMVBW  
B PDC

8/8/89  
Conversation  
with W.T. O'Connor  
& J.C. McKnight...  
Email can be reproduced & microfilmed  
G006  
1/1

period between September 1988 and June 1989, and projections are given of the status anticipated in September and December 1989. A comparison of the current (June 1989) status with the status for June that had been projected in March 1989 is also shown. The charts include the last reported status at Rancho Seco.

The charts show continued progress in implementing the SPIP recommendations. By December 1989 it is projected that over 99% of all the recommendations and virtually all of the key recommendations will be closed or in the process of being implemented.

If there are any questions concerning the above, please contact me at 419-321-8434.

Very truly yours,

*W. T. O'Connor*

W. T. O'Connor  
Chairman, B&W Owners Group  
Steering Committee

WTO/DM/kab

Enclosures


cc: B&WOG Steering Committee

D. H. Williams	- AP&L
N. A. Rutherford	- DPC
J. W. Langenbach	- GPUN
J. V. McColligan	- SMUD
R. C. Widell	- FPC

# AGGREGATE IMPLEMENTATION STATUS FOR ALL OPERATING PLANTS ALL SPIP RECOMMENDATIONS

CHART #1  
6/30/89


EVALUATING FOR  
APPLICABILITY



EVALUATING FOR  
IMPLEMENTATION



IMPLEMENTING



CLOSED




MARCH  
PROJECTION

PROJECTED

PROJECTED

AGGREGATE NO. OF RECOMMENDATIONS

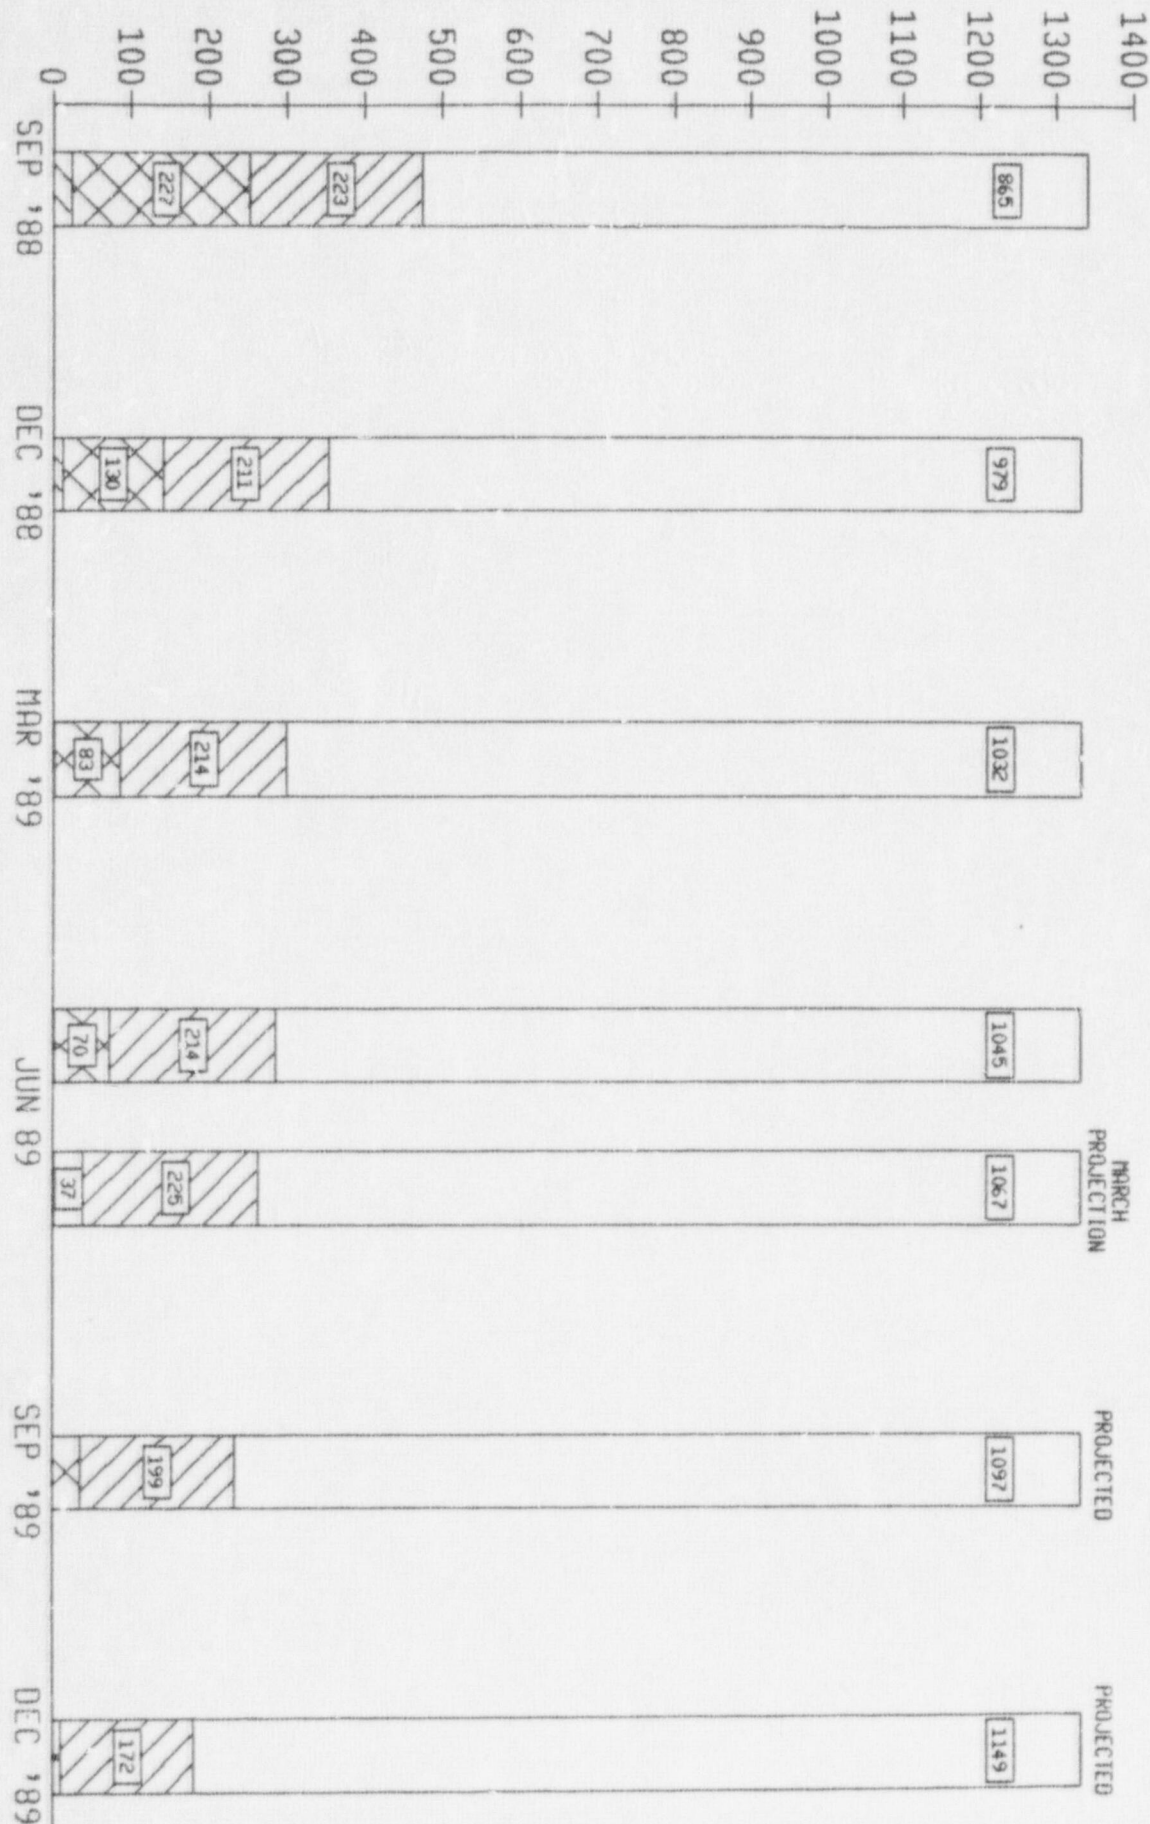



# AGGREGATE IMPLEMENTATION STATUS FOR ALL OPERATING PLANTS KEY SPIP RECOMMENDATIONS

CHART #2  
6/30/89

EVALUATING FOR APPLICABILITY  
EVALUATING FOR IMPLEMENTATION  
IMPLEMENTING  
CLOSED

