


**SAMPLE GANTT CHART:
KAISER ALUMINUM & CHEMICAL CORPORATION**

Kaiser Aluminum & Chemical Corporation

ID	Task Name	Start	Duration	1999		2000		2001		2002		2003		2004		2005		2006		2007		200
				H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
1	Review Phase 1 RAI	06/10/99	0 days	◆ 06/10																		
2	Kaiser prepares response to RAI	06/11/99	37 days	▣																		
3	NRC reviews response to RAI	08/03/99	1 day	▣																		
4	FRN - EA-FONSI	09/09/99	134 days	▣																		
5	PM - Draft FRN	09/09/99	90 days	▣																		
6	LA - Review of FRN	01/13/00	3 days	▣																		
7	Concurrence	01/18/00	25 days	▣																		
8	Publish FRN	03/08/00	5 days	◆ 03/08																		
9	Approve Phase 1 RP	04/04/00	0 days	◆ 04/04																		
10	Phase 1 Site Decommissioning	04/04/00	324 days	▣																		
11	Pre-cleanup staging activities	04/04/00	128 days	▣																		
12	Kaiser Performs Cleanup	09/29/00	136 days	▣																		
13	Region in process confirmatory survey	02/26/01	30 days	▣																		
14	Kaiser prepare FSSR	04/09/01	60 days	▣																		
15	Review Final Site Survey Report (FSSR)	07/02/01	90 days	▣																		
16	FSSR - Acceptance Review	07/02/01	46 days	▣																		
17	PM - Acceptance Review	07/02/01	30 days	▣																		
18	PM - Draft Letter	08/13/01	5 days	▣																		
19	Concurrence	08/20/01	10 days	▣																		
20	Issue letter to Kaiser	09/03/01	1 day	◆ 09/03																		
21	FSSR - Technical Review	08/13/01	60 days	▣																		
22	PM - Technical Review	08/13/01	60 days	▣																		

Kaiser Aluminum & Chemical Corporation

ID	Task Name	Start	Duration	1999		2000		2001		2002		2003		2004		2005		2006		2007		200	
				H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2
23	PM - Draft Letter	08/13/01	5 days																				
24	Concurrence	08/20/01	10 days																				
25	Issue letter to Kaiser	09/03/01	1 day																				
26	Off-site Acceptable for Release	09/04/01	1 day																				
27	Phase II DP - Review	06/01/01	396 days																				
28	DP - Acceptance Review	06/01/01	107 days																				
29	Receive DP	06/01/01	1 day																				
30	PM - Acceptance Review	06/04/01	90 days																				
31	PM - Draft Letter	10/08/01	5 days																				
32	Concurrence	10/15/01	10 days																				
33	Issue letter to Kaiser	10/29/01	1 day																				
34	Publish Federal Register Notice (FRN)	10/15/01	28 days																				
35	PM - Draft FRN	10/15/01	10 days																				
36	LA - Review of FRN	10/29/01	3 days																				
37	Concurrence	11/01/01	10 days																				
38	Publish FRN	11/15/01	5 days																				
39	Phase II DP - Technical Review	10/30/01	131 days																				
40	Develop Review Plan	10/30/01	21 days																				
41	PM - Prepare Task Plan	10/30/01	5 days																				
42	SL - Review Task Plan	11/06/01	5 days																				
43	PM - Prepare TAR	11/13/01	5 days																				
44	TAR concurrence	11/20/01	5 days																				




Kaiser Aluminum & Chemical Corporation


ID	Task Name	Start	Duration	1999		2000		2001		2002		2003		2004		2005		2006		2007		2008
				H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
45	Issue TAR	11/27/01	1 day							◆ 11/27												
46	Evaluate Decommissioning Plan	11/28/01	110 days							▶												
47	Review SRP 1 - Executive Summary	11/28/01	5 days							▶												
48	Review SRP 2 - Facility Operating Hist	12/05/01	5 days							▶												
49	Review SRP 3 - Facility Description	12/12/01	5 days							▶												
50	Review SRP 4 - Facility Radiological	12/19/01	5 days							▶												
51	Review SRP 5 - Dose Assessment	11/28/01	90 days							■												
52	Review SRP 6 - Alternatives Analysis	12/26/01	5 days							▶												
53	Review SRP 7 - ALARA	01/02/02	10 days							▶												
54	Review SRP 8 - Planned Decom Acti'	01/16/02	10 days							▶												
55	Review SRP 9 - Project Management	01/30/02	5 days							▶												
56	Review SRP 10 - Health & Safety Pla	02/06/02	10 days							▶												
57	Review SRP 11 - Envir. Monitoring PI	02/20/02	10 days							▶												
58	Review SRP 12 - Rad Waste Mgnt	03/06/02	5 days							▶												
59	Review SRP 13 - QA Program	03/13/02	5 days							▶												
60	Review SRP 14 - Radiation Surveys	03/20/02	10 days							▶												
61	Review SRP 15 - Financial Assuranc	04/03/02	15 days							▶												
62	Review SRP 16 - Restricted Use	04/24/02	5 days							▶												
63	Develop RAI / Resolve Comments	05/01/02	112 days							▶												
64	Develop TER	05/01/02	35 days							▶												
65	Review TER	06/19/02	5 days							◆ 06/19												
66	Meet with Kaiser to discuss concerns	06/26/02	1 day							▶												

Kaiser Aluminum & Chemical Corporation

ID	Task Name	Start	Duration	1999		2000		2001		2002		2003		2004		2005		2006		2007		200
				H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
67	Draft questions/comments	06/27/02	10 days																			
68	Review questions/comments	07/11/02	10 days																			
69	Issue comment letter	07/25/02	1 day																			
70	Kaiser review RAI	07/26/02	45 days																			
71	Review Kaiser response to RAI	09/27/02	5 days																			
72	Prepare EA - SER - FONSI	10/04/02	46 days																			
73	Prepare draft EA, SER, FONSI	10/04/02	30 days																			
74	Review draft EA, SER, FONSI	11/15/02	10 days																			
75	Revise draft EA, SER, FONSI	11/29/02	3 days																			
76	Finalize EA, SER, FONSI	12/04/02	1 day																			
77	Publish FRN	12/05/02	1 day																			
78	Approve Phase 2 DP	12/06/02	1 day																			
79	Site Decommissioning	12/09/02	936 days																			
80	Kaiser performs cleanup	12/09/02	700 days																			
81	Region in-process confirmatory survey	08/15/05	30 days																			
82	Kaiser prepares FSSR	09/26/05	30 days																			
83	Review FSSR	11/07/05	176 days																			
84	FSSR - Acceptance Review	11/07/05	19 days																			
85	PM - acceptance review	11/07/05	5 days																			
86	PM - draft letter	11/14/05	3 days																			
87	Concurrence	11/17/05	10 days																			
88	Issue letter to Kaiser	12/01/05	1 day																			

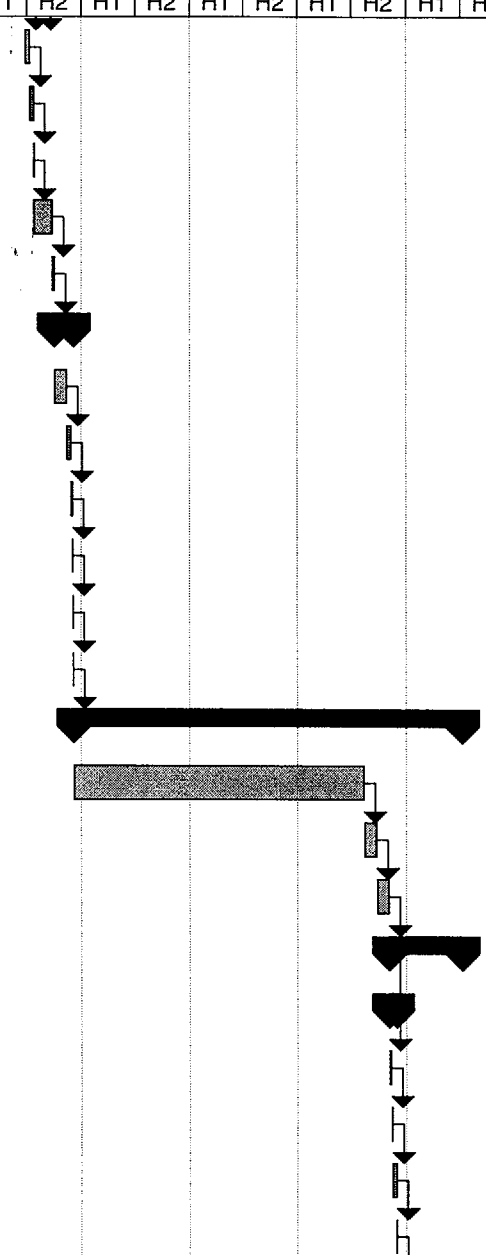

ID	Task Name	Start	Duration	1999		2000		2001		2002		2003		2004		2005		2006		2007		200
				H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
89	FSSR - Technicial review	12/02/05	156 days																			
90	PM - technial review	12/02/05	60 days																			
91	Complete FSSR review	02/23/06	0 days																			
92	Develop FSSR TER and FSSR RAI	02/24/06	30 days																			
93	Kaiser prepares response to RAI	04/07/06	30 days																			
94	NRC reviews response to RAI	05/19/06	20 days																			
95	PM - draft letter	06/16/06	5 days																			
96	Concurrence	06/23/06	10 days																			
97	Issue letter to Kaiser	07/07/06	1 day																			
98	Site acceptable for release	07/10/06	1 day																			
99	Remove Site From SDMP	07/11/06	88 days																			
100	Prepare Commission Paper	07/11/06	33 days																			
101	PM - prepare Commission Paper Outline	07/11/06	3 days																			
102	Management review	07/14/06	5 days																			
103	PM - draft Commission Paper	07/21/06	15 days																			
104	Concurrence	08/11/06	10 days																			
105	Prepare FRN to remove site from SDMP	08/25/06	18 days																			
106	PM - draft FRN	08/25/06	5 days																			
107	LA - review FRN	09/01/06	3 days																			
108	Concurrence	09/06/06	10 days																			
109	Prepare Letters to State & EPA	09/20/06	15 days																			
110	PM - draft letter to State/EPA	09/20/06	5 days																			



Kaiser Aluminum & Chemical Corporation

ID	Task Name	Start	Duration	1999		2000		2001		2002		2003		2004		2005		2006		2007		200
				H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1	H2	H1
111	Concurrence	09/27/06	10 days																			
112	Issue Commission Paper	10/11/06	1 day																			
113	Commission Review	10/12/06	15 days																			
114	Publish FRN & issue letters	11/02/06	5 days																			
115	Release site	11/09/06	1 day																			
