



# CR3 NPC Outage Containment Repair Project - Level 3 Schedule

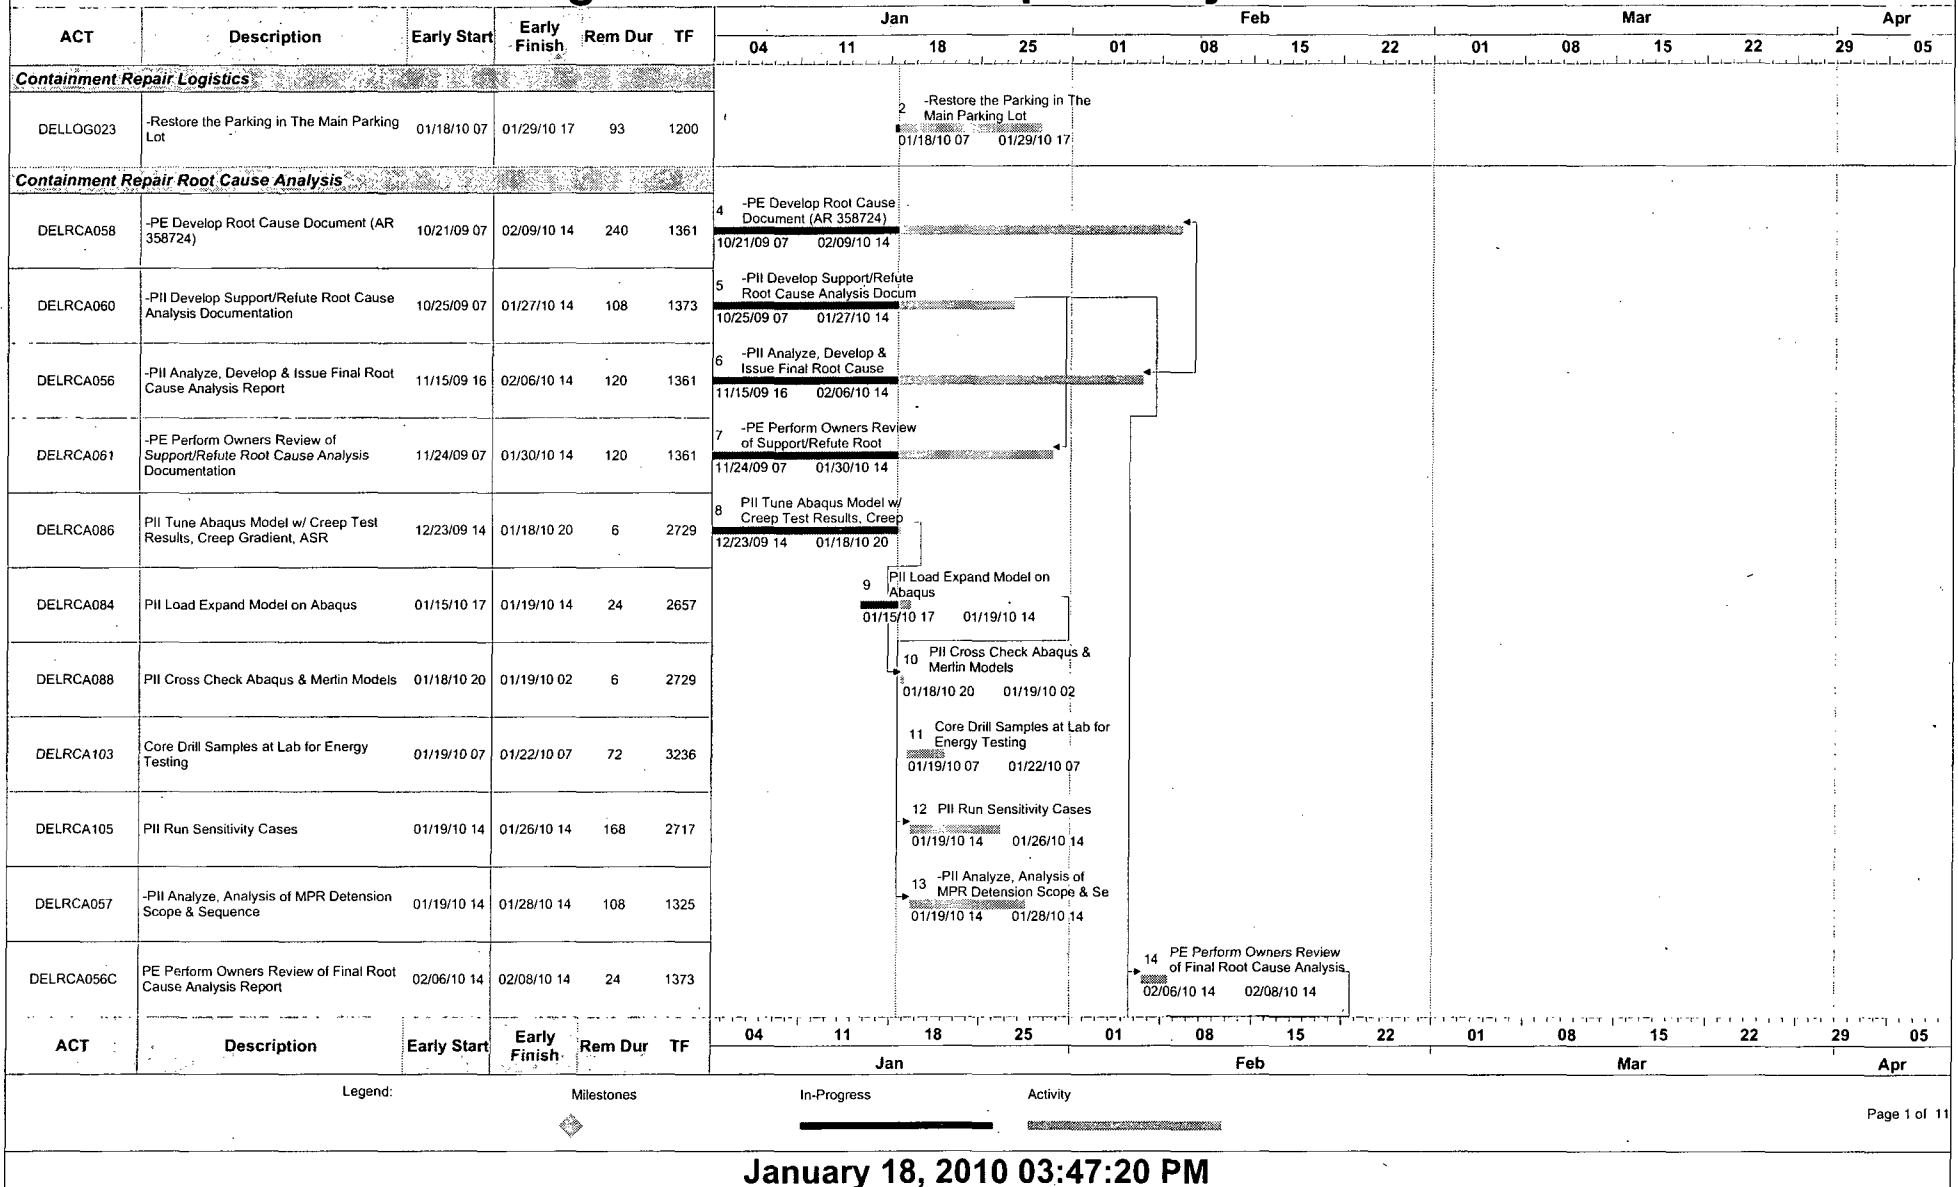

January 18, 2010 03:47:20 PM

2010/1/18

# CR3 NPC Outage Containment Repair Project - Level 3 Schedule

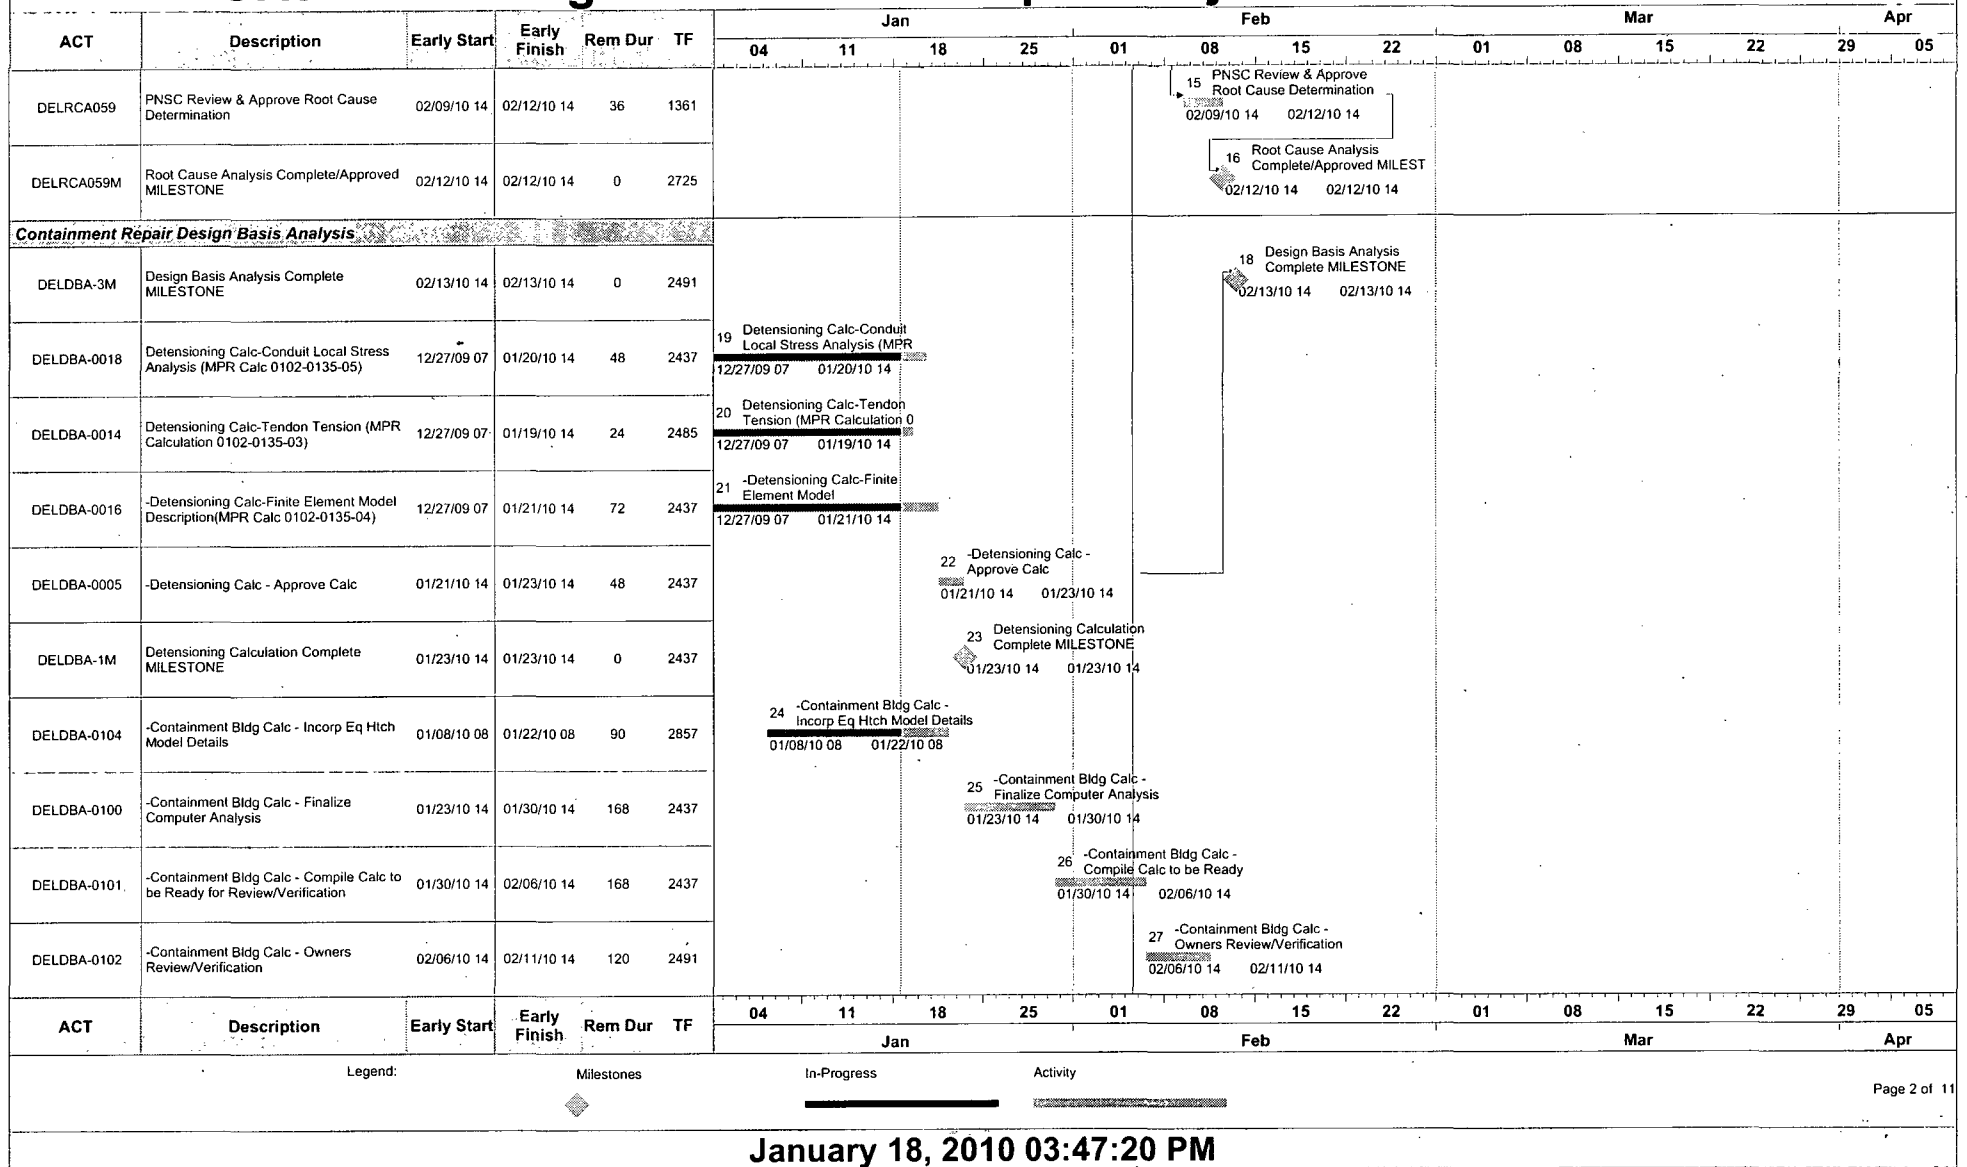

# CR3 NPC Outage Containment Repair Project - Level 3 Schedule

| ACT                                             | Description                                                    | Early Start | Early Finish | Rem Dur | TF   | Jan |    |             |                                                     | Feb |    |                                                        |             | Mar         |                                             |             |             | Apr |    |
|-------------------------------------------------|----------------------------------------------------------------|-------------|--------------|---------|------|-----|----|-------------|-----------------------------------------------------|-----|----|--------------------------------------------------------|-------------|-------------|---------------------------------------------|-------------|-------------|-----|----|
|                                                 |                                                                |             |              |         |      | 04  | 11 | 18          | 25                                                  | 01  | 08 | 15                                                     | 22          | 01          | 08                                          | 15          | 22          | 29  | 05 |
| DELDDBA-0103                                    | -Containment Bldg Calc - Incorporate Review Comments & Approve | 02/11/10 14 | 02/13/10 14  | 48      | 2491 |     |    |             |                                                     |     | 28 | -Containment Bldg Calc - Incorporate Review            | 02/11/10 14 | 02/13/10 14 |                                             |             |             |     |    |
| DELDDBA-2M                                      | Containment Bldg Calc Compl MILESTONE                          | 02/13/10 14 | 02/13/10 14  | 0       | 2491 |     |    |             |                                                     |     | 29 | Containment Bldg Calc Compl MILESTONE                  | 02/13/10 14 | 02/13/10 14 |                                             |             |             |     |    |
| <b>Containment Repair Implementation Design</b> |                                                                |             |              |         |      |     |    |             |                                                     |     |    |                                                        |             |             |                                             |             |             |     |    |
| DELDES1M                                        | EC Implementation Design Complete MILESTONE                    | 02/22/10 08 | 02/22/10 08  | 0       | 3033 |     |    |             |                                                     |     |    |                                                        |             | 31          | EC Implementation Design Complete MILESTONE | 02/22/10 08 | 02/22/10 08 |     |    |
| DELDES2111M                                     | -EC 75218 PH 2 Detension: Develop Final EC "Pkg for final DRB" | 01/13/10 07 | 01/20/10 14  | 48      | 2648 |     |    | 32          | -EC 75218 PH 2 Detension: Develop Final EC "Pkg for |     |    |                                                        |             |             |                                             |             |             |     |    |
|                                                 |                                                                |             |              |         |      |     |    | 01/13/10 07 | 01/20/10 14                                         |     |    |                                                        |             |             |                                             |             |             |     |    |
| DELDES2115M                                     | -EC 75218 PH 2 Detension: Mech / Struc - DV                    | 01/14/10 07 | 01/19/10 14  | 24      | 2648 |     |    |             |                                                     |     | 33 | -EC 75218 PH 2 Detension: Mech / Struc - DV            | 01/14/10 07 | 01/19/10 14 |                                             |             |             |     |    |
|                                                 |                                                                |             |              |         |      |     |    |             |                                                     |     |    |                                                        |             |             |                                             |             |             |     |    |
| DELDES2123                                      | -EC 75218 PH 2 Detension: Incorp Review Comments               | 01/18/10 13 | 01/19/10 13  | 23      | 2673 |     |    |             |                                                     |     | 34 | -EC 75218 PH 2 Detension: Incorp Review Comments       | 01/18/10 13 | 01/19/10 13 |                                             |             |             |     |    |
|                                                 |                                                                |             |              |         |      |     |    |             |                                                     |     |    |                                                        |             |             |                                             |             |             |     |    |
| DELDES2117                                      | -EC 75218 PH 2 Detension: Incorp Verification Comments         | 01/19/10 14 | 01/20/10 14  | 24      | 2648 |     |    |             |                                                     |     | 35 | -EC 75218 PH 2 Detension: Incorp Verification Comments | 01/19/10 14 | 01/20/10 14 |                                             |             |             |     |    |
|                                                 |                                                                |             |              |         |      |     |    |             |                                                     |     |    |                                                        |             |             |                                             |             |             |     |    |
| DELDES2125                                      | EC 75218 PH 2 Detension: Supv Review Prior to Final DRB        | 01/20/10 14 | 01/20/10 18  | 4       | 2648 |     |    |             |                                                     |     | 36 | EC 75218 PH 2 Detension: Supv Review Prior to Final D  | 01/20/10 14 | 01/20/10 18 |                                             |             |             |     |    |
|                                                 |                                                                |             |              |         |      |     |    |             |                                                     |     |    |                                                        |             |             |                                             |             |             |     |    |
| DELDES2125D                                     | EC 75218 PH 2 Detension: Distrib Final DRB Pkg for Review      | 01/20/10 18 | 01/20/10 19  | 1       | 2648 |     |    |             |                                                     |     | 37 | EC 75218 PH 2 Detension: Distrib Final DRB Pkg for Re  | 01/20/10 18 | 01/20/10 19 |                                             |             |             |     |    |
|                                                 |                                                                |             |              |         |      |     |    |             |                                                     |     |    |                                                        |             |             |                                             |             |             |     |    |
| DELDES2125R                                     | -EC 75218 PH 2 Detension: Review Final DRB Pkg                 | 01/20/10 19 | 01/24/10 19  | 96      | 2648 |     |    |             |                                                     |     | 38 | -EC 75218 PH 2 Detension: Review Final DRB Pkg         | 01/20/10 19 | 01/24/10 19 |                                             |             |             |     |    |
|                                                 |                                                                |             |              |         |      |     |    |             |                                                     |     |    |                                                        |             |             |                                             |             |             |     |    |
| DELDES21205                                     | EC 75218 PH 2 Detension: Final DRB Meeting                     | 01/24/10 19 | 01/24/10 21  | 2       | 2648 |     |    |             |                                                     |     | 39 | EC 75218 PH 2 Detension: Final DRB Meeting             | 01/24/10 19 | 01/24/10 21 |                                             |             |             |     |    |
|                                                 |                                                                |             |              |         |      |     |    |             |                                                     |     |    |                                                        |             |             |                                             |             |             |     |    |
| DELDES21215                                     | -EC 75218 PH 2 Detension: Incorporate Final DRB Comments       | 01/24/10 21 | 01/25/10 09  | 12      | 2648 |     |    |             |                                                     |     | 40 | -EC 75218 PH 2 Detension: Incorporate Final DRB Com    | 01/24/10 21 | 01/25/10 09 |                                             |             |             |     |    |
|                                                 |                                                                |             |              |         |      |     |    |             |                                                     |     |    |                                                        |             |             |                                             |             |             |     |    |
| ACT                                             | Description                                                    | Early Start | Early Finish | Rem Dur | TF   | 04  | 11 | 18          | 25                                                  | 01  | 08 | 15                                                     | 22          | 01          | 08                                          | 15          | 22          | 29  | 05 |

Legend:

Milestones

In-Progress

Activity

Page 3 of 11

January 18, 2010 03:47:20 PM

Rev D

# CR3 NPC Outage Containment Repair Project - Level 3 Schedule

| ACT         | Description                                         | Early Start | Early Finish | Rem Dur | TF   | Jan |    |    |                                                        |    |    |    | Feb |    |    |    |    |    |    | Mar |  |  |  |  |  |  | Apr |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
|-------------|-----------------------------------------------------|-------------|--------------|---------|------|-----|----|----|--------------------------------------------------------|----|----|----|-----|----|----|----|----|----|----|-----|--|--|--|--|--|--|-----|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|--|
|             |                                                     |             |              |         |      | 04  | 11 | 18 | 25                                                     | 01 | 08 | 15 | 22  | 01 | 08 | 15 | 22 | 29 | 05 |     |  |  |  |  |  |  |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |
| DELDES21220 | EC 75218 PH 2 Detension: Obtain Supervisor Approval | 01/25/10 09 | 01/25/10 11  | 2       | 2648 |     |    |    | 41 EC 75218 PH 2 Detension: Obtain Supervisor Approval |    |    |    |     |    |    |    |    |    |    |     |  |  |  |  |  |  |     |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |  |

Legend:

Milestones

In-Progress


Activity

Page 4 of 11


January 18, 2010 03:47:20 PM

Rev D

# CR3 NPC Outage Containment Repair Project - Level 3 Schedule

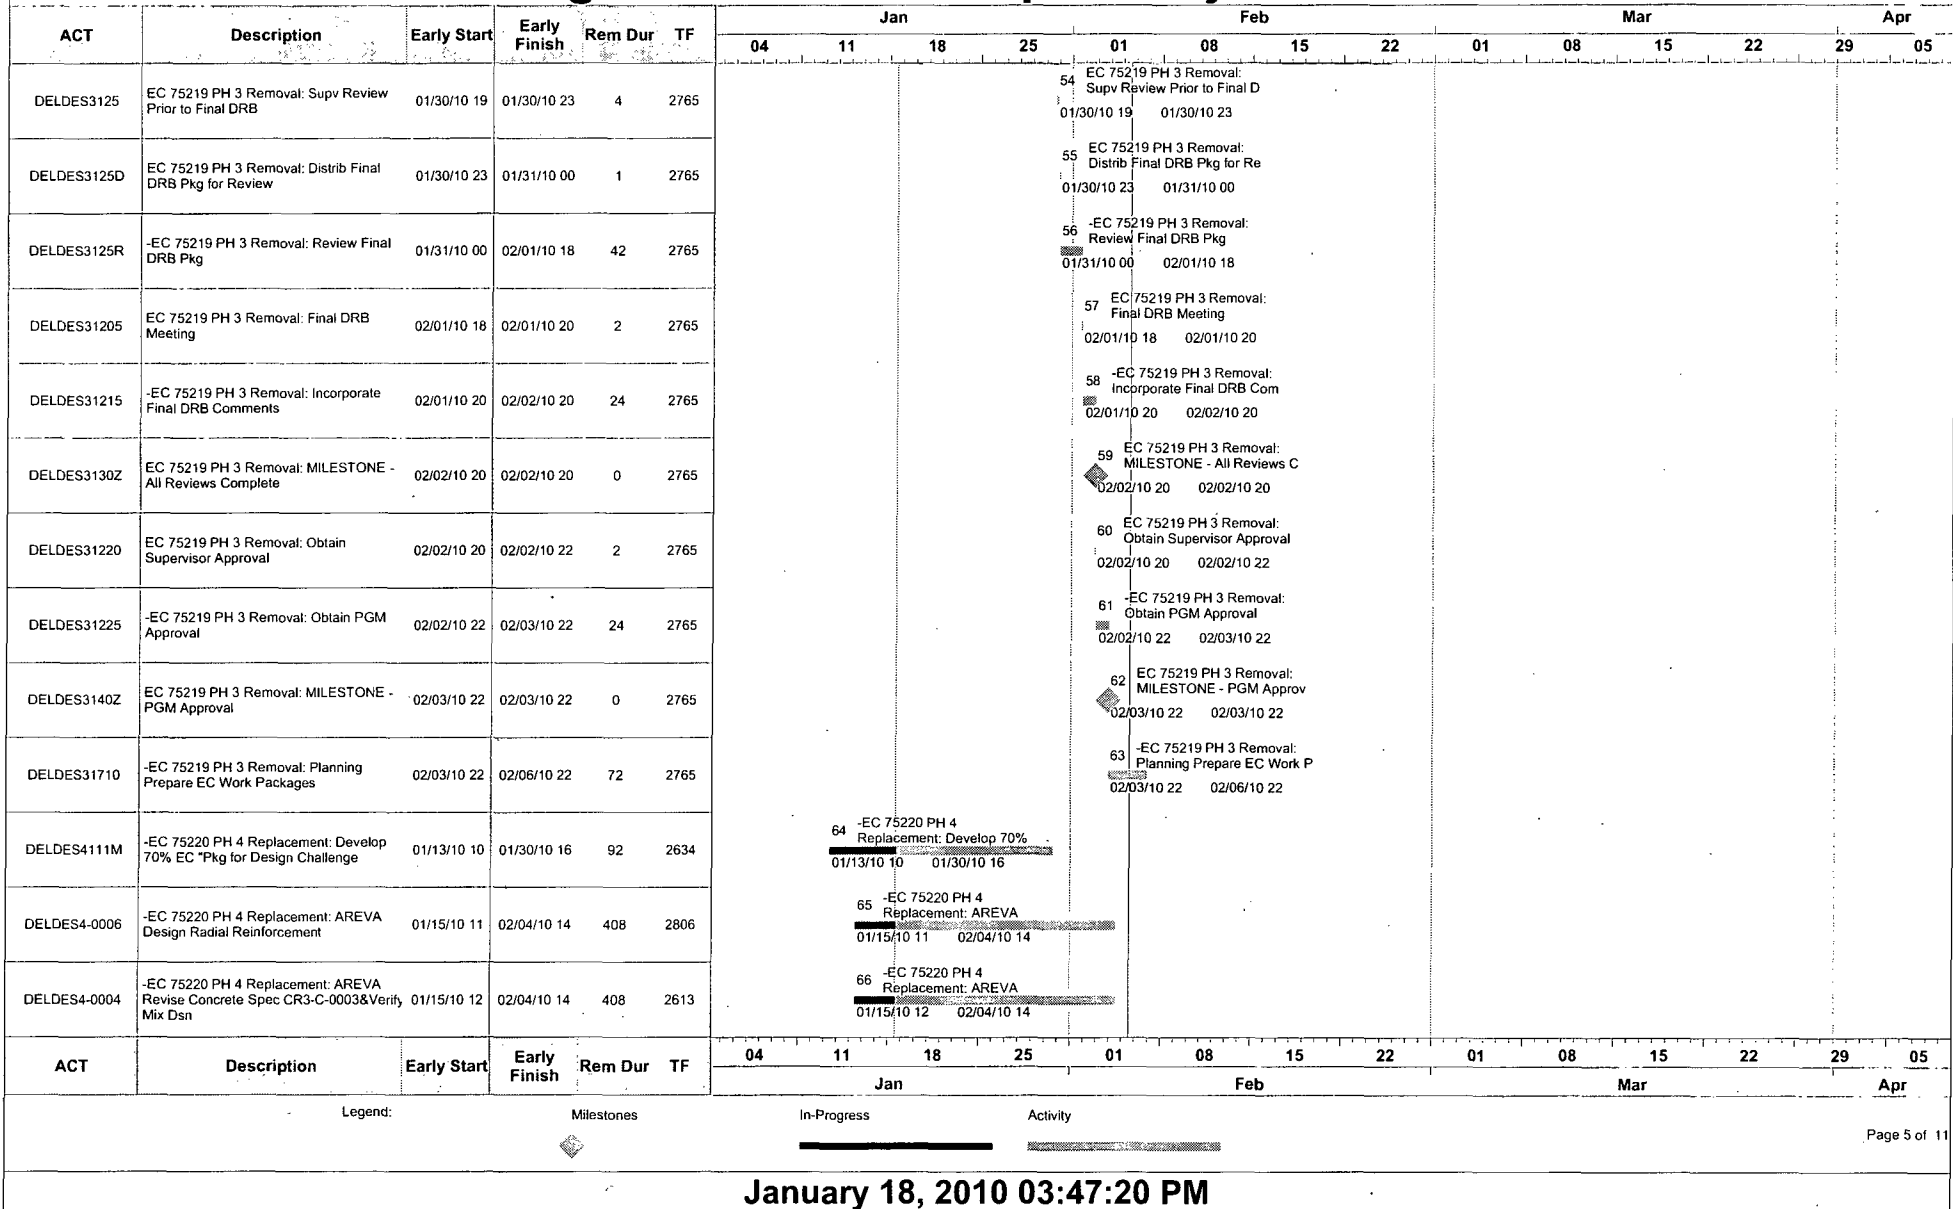

# CR3 NPC Outage Containment Repair Project - Level 3 Schedule

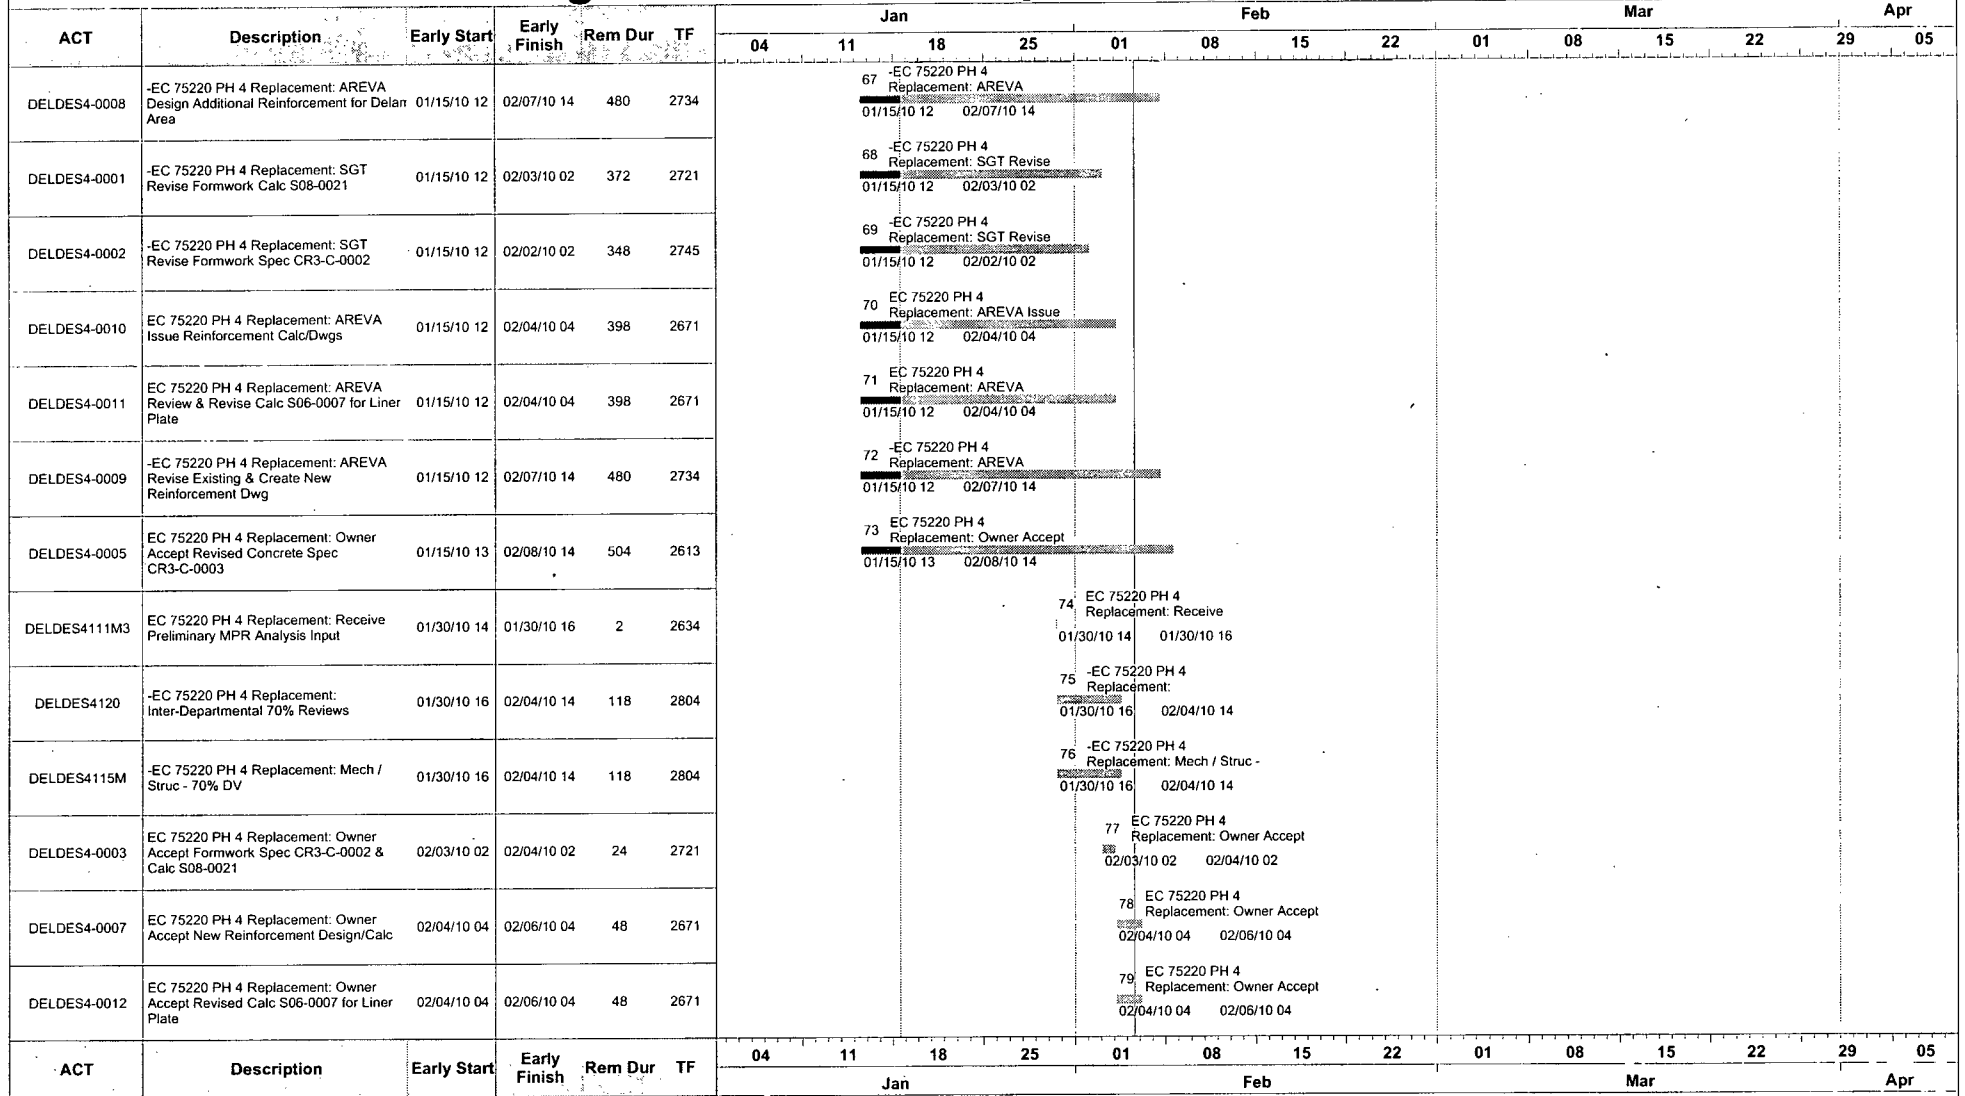

Legend:

Milestones

In-Progress

Activity

Page 6 of 11

January 18, 2010 03:47:20 PM

Rev D

# CR3 NPC Outage Containment Repair Project - Level 3 Schedule

| ACT          | Description                                                                  | Early Start | Early Finish | Rem Dur | TF   | Jan        |    |    |    | Feb         |                                           |    |    | Mar      |    |    |    | Apr |    |
|--------------|------------------------------------------------------------------------------|-------------|--------------|---------|------|------------|----|----|----|-------------|-------------------------------------------|----|----|----------|----|----|----|-----|----|
|              |                                                                              |             |              |         |      | 04         | 11 | 18 | 25 | 01          | 08                                        | 15 | 22 | 01       | 08 | 15 | 22 | 29  | 05 |
| DELDES41207  | EC 75220 PH 4 Replacement: 70% Design Challenge Meeting                      | 02/04/10 14 | 02/04/10 16  | 2       | 2804 |            |    |    |    | 80          | EC 75220 PH 4 Replacement: 70% Design     |    |    |          |    |    |    |     |    |
|              |                                                                              |             |              |         |      |            |    |    |    | 02/04/10 14 | 02/04/10 16                               |    |    |          |    |    |    |     |    |
| DELDES4117   | -EC 75220 PH 4 Replacement: Incorp 70% Verification Comments                 | 02/04/10 14 | 02/05/10 14  | 24      | 2806 |            |    |    |    | 81          | -EC 75220 PH 4 Replacement: Incorp 70%    |    |    |          |    |    |    |     |    |
|              |                                                                              |             |              |         |      |            |    |    |    | 02/04/10 14 | 02/05/10 14                               |    |    |          |    |    |    |     |    |
| DELDES4111M2 | -EC 75220 PH 4 Replacement: Develop Final EC "Pkg for final DRB"             | 02/05/10 15 | 02/13/10 16  | 193     | 2491 |            |    |    |    | 82          | -EC 75220 PH 4 Replacement: Develop Final |    |    |          |    |    |    |     |    |
|              |                                                                              |             |              |         |      |            |    |    |    | 02/05/10 15 | 02/13/10 16                               |    |    |          |    |    |    |     |    |
| DELDES4-0000 | EC 75220 PH 4 Replacement: Receive Design Input from PII Root Cause Analysis | 02/06/10 14 | 02/06/10 16  | 2       | 2843 |            |    |    |    | 83          | EC 75220 PH 4 Replacement: Receive        |    |    |          |    |    |    |     |    |
|              |                                                                              |             |              |         |      |            |    |    |    | 02/06/10 14 | 02/06/10 16                               |    |    |          |    |    |    |     |    |
| DELDES4123   | -EC 75220 PH 4 Replacement: Incorp 70% Review Comments                       | 02/07/10 14 | 02/08/10 14  | 24      | 2734 |            |    |    |    | 84          | -EC 75220 PH 4 Replacement: Incorp 70%    |    |    |          |    |    |    |     |    |
|              |                                                                              |             |              |         |      |            |    |    |    | 02/07/10 14 | 02/08/10 14                               |    |    |          |    |    |    |     |    |
| DELDES4190Z  | EC 75220 PH 4 Replacement: Milestone - Issued for 70% Review                 | 02/07/10 14 | 02/07/10 14  | 0       | 2734 |            |    |    |    | 85          | EC 75220 PH 4 Replacement: Milestone -    |    |    |          |    |    |    |     |    |
|              |                                                                              |             |              |         |      |            |    |    |    | 02/07/10 14 | 02/07/10 14                               |    |    |          |    |    |    |     |    |
| DELDES4111M1 | EC 75220 PH 4 Replacement: Receive Approved MPR Analysis Input               | 02/13/10 14 | 02/13/10 16  | 2       | 2491 |            |    |    |    | 86          | EC 75220 PH 4 Replacement: Receive        |    |    |          |    |    |    |     |    |
|              |                                                                              |             |              |         |      |            |    |    |    | 02/13/10 14 | 02/13/10 16                               |    |    |          |    |    |    |     |    |
| DELDES4120A  | -EC 75220 PH 4 Replacement: Final Inter-Departmental Reviews                 | 02/13/10 16 | 02/17/10 17  | 97      | 2495 |            |    |    |    | 87          | -EC 75220 PH 4 Replacement: Final         |    |    |          |    |    |    |     |    |
|              |                                                                              |             |              |         |      |            |    |    |    | 02/13/10 16 | 02/17/10 17                               |    |    |          |    |    |    |     |    |
| DELDES4115M1 | -EC 75220 PH 4 Replacement: Final Mech / Struc - DV                          | 02/13/10 16 | 02/17/10 17  | 97      | 2491 |            |    |    |    | 88          | -EC 75220 PH 4 Replacement: Final Mech /  |    |    |          |    |    |    |     |    |
|              |                                                                              |             |              |         |      |            |    |    |    | 02/13/10 16 | 02/17/10 17                               |    |    |          |    |    |    |     |    |
| DELDES4117F  | -EC 75220 PH 4 Replacement: Incorp Final Verification Comments               | 02/17/10 17 | 02/18/10 17  | 24      | 2491 |            |    |    |    | 89          | -EC 75220 PH 4 Replacement: Incorp Final  |    |    |          |    |    |    |     |    |
|              |                                                                              |             |              |         |      |            |    |    |    | 02/17/10 17 | 02/18/10 17                               |    |    |          |    |    |    |     |    |
| DELDES4123A  | -EC 75220 PH 4 Replacement: Incorp Final Review Comments                     | 02/17/10 17 | 02/18/10 17  | 24      | 2495 |            |    |    |    | 90          | -EC 75220 PH 4 Replacement: Incorp Final  |    |    |          |    |    |    |     |    |
|              |                                                                              |             |              |         |      |            |    |    |    | 02/17/10 17 | 02/18/10 17                               |    |    |          |    |    |    |     |    |
| DELDES4125   | EC 75220 PH 4 Replacement: Supv Review Prior to Final DRB                    | 02/18/10 17 | 02/18/10 21  | 4       | 2491 |            |    |    |    | 91          | EC 75220 PH 4 Replacement: Supv Review    |    |    |          |    |    |    |     |    |
|              |                                                                              |             |              |         |      |            |    |    |    | 02/18/10 17 | 02/18/10 21                               |    |    |          |    |    |    |     |    |
| DELDES4125D  | EC 75220 PH 4 Replacement: Distrib Final DRB Pkg for Review                  | 02/18/10 21 | 02/18/10 22  | 1       | 2491 |            |    |    |    | 92          | EC 75220 PH 4 Replacement: Distrib Final  |    |    |          |    |    |    |     |    |
|              |                                                                              |             |              |         |      |            |    |    |    | 02/18/10 21 | 02/18/10 22                               |    |    |          |    |    |    |     |    |
| ACT          | Description                                                                  | Early Start | Early Finish | Rem Dur | TF   | 04         | 11 | 18 | 25 | 01          | 08                                        | 15 | 22 | 01       | 08 | 15 | 22 | 29  | 05 |
|              |                                                                              |             |              |         |      | Jan        |    |    |    | Feb         |                                           |    |    | Mar      |    |    |    | Apr |    |
| Legend:      |                                                                              |             |              |         |      | Milestones |    |    |    | In-Progress |                                           |    |    | Activity |    |    |    |     |    |
|              |                                                                              |             |              |         |      |            |    |    |    |             |                                           |    |    |          |    |    |    |     |    |

# CR3 NPC Outage Containment Repair Project - Level 3 Schedule

| ACT          | Description                                                       | Early Start | Early Finish | Rem Dur | TF   | Jan |    |    |    | Feb |    |    |                                                                                        | Mar |    |    |    | Apr |    |
|--------------|-------------------------------------------------------------------|-------------|--------------|---------|------|-----|----|----|----|-----|----|----|----------------------------------------------------------------------------------------|-----|----|----|----|-----|----|
|              |                                                                   |             |              |         |      | 04  | 11 | 18 | 25 | 01  | 08 | 15 | 22                                                                                     | 01  | 08 | 15 | 22 | 29  | 05 |
| DELDES4125R  | -EC 75220 PH 4 Replacement: Review Final DRB Pkg                  | 02/18/10 22 | 02/19/10 22  | 24      | 2491 |     |    |    |    |     |    |    | 93 -EC 75220 PH 4 Replacement: Review Final<br>02/18/10 22 02/19/10 22                 |     |    |    |    |     |    |
| DELDES41205  | EC 75220 PH 4 Replacement: Final DRB Meeting                      | 02/19/10 22 | 02/20/10 00  | 2       | 2491 |     |    |    |    |     |    |    | 94 EC 75220 PH 4 Replacement: Final DRB Me<br>02/19/10 22 02/20/10 00                  |     |    |    |    |     |    |
| DELDES41215  | -EC 75220 PH 4 Replacement: Incorporate Final DRB Comments        | 02/20/10 00 | 02/21/10 00  | 24      | 2491 |     |    |    |    |     |    |    | 95 -EC 75220 PH 4 Replacement: Incorporate<br>02/20/10 00 02/21/10 00                  |     |    |    |    |     |    |
| DELDES4130Z  | EC 75220 PH 4 Replacement: MILESTONE - All Reviews Complete       | 02/21/10 00 | 02/21/10 00  | 0       | 2491 |     |    |    |    |     |    |    | 96 EC 75220 PH 4 Replacement: MILESTONE -<br>02/21/10 00 02/21/10 00                   |     |    |    |    |     |    |
| DELDES41220  | EC 75220 PH 4 Replacement: Obtain Supervisor Approval             | 02/21/10 00 | 02/21/10 08  | 8       | 2491 |     |    |    |    |     |    |    | 97 EC 75220 PH 4 Replacement: Obtain<br>02/21/10 00 02/21/10 08                        |     |    |    |    |     |    |
| DELDES41225  | -EC 75220 PH 4 Replacement: Obtain PGM Approval                   | 02/21/10 08 | 02/22/10 08  | 24      | 2491 |     |    |    |    |     |    |    | 98 -EC 75220 PH 4 Replacement: Obtain PGM A<br>02/21/10 08 02/22/10 08                 |     |    |    |    |     |    |
| DELDES41710  | EC 75220 PH 4 Replacement: Planning Prepare EC Work Packages      | 02/22/10 08 | 02/25/10 08  | 72      | 2491 |     |    |    |    |     |    |    | 99 EC 75220 PH 4 Replacement: Planning<br>02/22/10 08 02/25/10 08                      |     |    |    |    |     |    |
| DELDES4140Z  | EC 75220 Replacement MILESTONE - PGM Approval                     | 02/22/10 08 | 02/22/10 08  | 0       | 2491 |     |    |    |    |     |    |    | 100 EC 75220 Replacement MILESTONE - PGM Approv<br>02/22/10 08 02/22/10 08             |     |    |    |    |     |    |
| DELDES510Z   | EC 75221 PH 5 Retension: MILESTONE - "Start Project"              | 01/19/10 07 | 01/19/10 07  | 0       | 3234 |     |    |    |    |     |    |    | 101 EC 75221 PH 5 Retension: MILESTONE - "Start Project<br>01/19/10 07 01/19/10 07     |     |    |    |    |     |    |
| DELDES51005  | EC 75221 PH 5 Retension: Prep / Cplt Validation Plan w/Supv       | 01/19/10 07 | 01/19/10 09  | 2       | 3234 |     |    |    |    |     |    |    | 102 EC 75221 PH 5 Retension: Prep / Cplt Validation Plan w/<br>01/19/10 07 01/19/10 09 |     |    |    |    |     |    |
| DELDES51008  | EC 75221 PH 5 Retension: Develop Project Tm / Kick-Off Mtg        | 01/19/10 09 | 01/19/10 11  | 2       | 3234 |     |    |    |    |     |    |    | 103 EC 75221 PH 5 Retension: Develop Project Tm /<br>01/19/10 09 01/19/10 11           |     |    |    |    |     |    |
| DELDES51020M | -EC 75221 PH 5 Retension: Develop Draft Pkg for Conceptual DRB    | 01/19/10 11 | 01/23/10 17  | 102     | 3234 |     |    |    |    |     |    |    | 104 -EC 75221 PH 5 Retension: Develop Draft Pkg for<br>01/19/10 11 01/23/10 17         |     |    |    |    |     |    |
| DELDES51025  | EC 75221 PH 5 Retension: Distribute Conceptual 70% Pkg for Review | 01/23/10 17 | 01/23/10 18  | 1       | 3327 |     |    |    |    |     |    |    | 105 EC 75221 PH 5 Retension: Distribute Conceptual 70%<br>01/23/10 17 01/23/10 18      |     |    |    |    |     |    |
| ACT          | Description                                                       | Early Start | Early Finish | Rem Dur | TF   | 04  | 11 | 18 | 25 | 01  | 08 | 15 | 22                                                                                     | 01  | 08 | 15 | 22 | 29  | 05 |
|              |                                                                   |             |              |         |      | Jan |    |    |    | Feb |    |    |                                                                                        | Mar |    |    |    | Apr |    |

# CR3 NPC Outage Containment Repair Project - Level 3 Schedule

| ACT                          | Description                                                           | Early Start | Early Finish | Rem Dur | TF   | Jan                                                                                              |    |    |    |    |    |    | Feb         |    |    |    |    |    |    | Mar      |              |  |  |  |  |  | Apr |  |
|------------------------------|-----------------------------------------------------------------------|-------------|--------------|---------|------|--------------------------------------------------------------------------------------------------|----|----|----|----|----|----|-------------|----|----|----|----|----|----|----------|--------------|--|--|--|--|--|-----|--|
|                              |                                                                       |             |              |         |      | 04                                                                                               | 11 | 18 | 25 | 01 | 08 | 15 | 22          | 01 | 08 | 15 | 22 | 29 | 05 |          |              |  |  |  |  |  |     |  |
| DELDES5111M                  | -EC 75221 PH 5 Retension: Develop 70% EC "Pkg"                        | 01/23/10 17 | 01/26/10 17  | 72      | 3234 | <div>106 -EC 75221 PH 5 Retension: Develop 70% EC "Pkg"<br/>01/23/10 17 01/26/10 17</div>        |    |    |    |    |    |    |             |    |    |    |    |    |    |          |              |  |  |  |  |  |     |  |
| DELDES51027                  | -EC 75221 PH 5 Retension: Review Conceptual 70% Pkg                   | 01/23/10 18 | 01/26/10 18  | 72      | 3327 | <div>107 -EC 75221 PH 5 Retension: Review Conceptual 70% Pkg<br/>01/23/10 18 01/26/10 18</div>   |    |    |    |    |    |    |             |    |    |    |    |    |    |          |              |  |  |  |  |  |     |  |
| DELDES51030                  | EC 75221 PH 5 Retension: Conceptual DRB Meeting                       | 01/26/10 16 | 01/26/10 18  | 2       | 3329 | <div>108 EC 75221 PH 5 Retension: Conceptual DRB Meeting<br/>01/26/10 16 01/26/10 18</div>       |    |    |    |    |    |    |             |    |    |    |    |    |    |          |              |  |  |  |  |  |     |  |
| DELDES5115M                  | -EC 75221 PH 5 Retension: Mech / Struc - DV                           | 01/26/10 17 | 01/30/10 17  | 96      | 3234 | <div>109 -EC 75221 PH 5 Retension: Mech / Struc - DV<br/>01/26/10 17 01/30/10 17</div>           |    |    |    |    |    |    |             |    |    |    |    |    |    |          |              |  |  |  |  |  |     |  |
| DELDES5120                   | -EC 75221 PH 5 Retension: Inter-Departmental Reviews                  | 01/26/10 17 | 01/30/10 17  | 96      | 3234 | <div>110 -EC 75221 PH 5 Retension: Inter-Departmental Reviews<br/>01/26/10 17 01/30/10 17</div>  |    |    |    |    |    |    |             |    |    |    |    |    |    |          |              |  |  |  |  |  |     |  |
| DELDES5120Z                  | EC 75221 PH 5 Retension: MILESTONE - Conceptual DRB Mtg Cplt / Waived | 01/26/10 18 | 01/26/10 18  | 0       | 3329 | <div>111 EC 75221 PH 5 Retension: MILESTONE - Conceptual<br/>01/26/10 18 01/26/10 18</div>       |    |    |    |    |    |    |             |    |    |    |    |    |    |          |              |  |  |  |  |  |     |  |
| DELDES5190Z                  | EC 75221 PH 5 Retension: Milestone - Issued for 70% Review            | 01/26/10 18 | 01/26/10 18  | 0       | 3329 | <div>112 EC 75221 PH 5 Retension: Milestone - Issued for 70% R<br/>01/26/10 18 01/26/10 18</div> |    |    |    |    |    |    |             |    |    |    |    |    |    |          |              |  |  |  |  |  |     |  |
| DELDES5122                   | EC 75221 PH 5 Retension: 70% Design Challenge Mgt                     | 01/26/10 18 | 01/26/10 20  | 2       | 3327 | <div>113 EC 75221 PH 5 Retension: 70% Design Challenge Mgt<br/>01/26/10 18 01/26/10 20</div>     |    |    |    |    |    |    |             |    |    |    |    |    |    |          |              |  |  |  |  |  |     |  |
| DELDES5123                   | -EC 75221 PH 5 Retension: Incorp Review Comments                      | 01/30/10 17 | 02/02/10 18  | 73      | 3234 | <div>114 -EC 75221 PH 5 Retension: Incorp Review Comments<br/>01/30/10 17 02/02/10 18</div>      |    |    |    |    |    |    |             |    |    |    |    |    |    |          |              |  |  |  |  |  |     |  |
| DELDES5117                   | -EC 75221 PH 5 Retension: Incorp 70% Comments                         | 01/30/10 17 | 02/02/10 18  | 73      | 3234 | <div>115 -EC 75221 PH 5 Retension: Incorp 70% Comments<br/>01/30/10 17 02/02/10 18</div>         |    |    |    |    |    |    |             |    |    |    |    |    |    |          |              |  |  |  |  |  |     |  |
| DELDES5125                   | EC 75221 PH 5 Retension: Supv Review Prior to Final DRB               | 02/02/10 18 | 02/02/10 22  | 4       | 3234 | <div>116 EC 75221 PH 5 Retension: Supv Review Prior to Final D<br/>02/02/10 18 02/02/10 22</div> |    |    |    |    |    |    |             |    |    |    |    |    |    |          |              |  |  |  |  |  |     |  |
| DELDES5125D                  | EC 75221 PH 5 Retension: Distrib Final DRB Pkg for Review             | 02/02/10 22 | 02/02/10 23  | 1       | 3234 | <div>117 EC 75221 PH 5 Retension: Distrib Final DRB Pkg for Re<br/>02/02/10 22 02/02/10 23</div> |    |    |    |    |    |    |             |    |    |    |    |    |    |          |              |  |  |  |  |  |     |  |
| DELDES5125R                  | -EC 75221 PH 5 Retension: Review Final DRB Pkg                        | 02/02/10 23 | 02/08/10 13  | 134     | 3234 | <div>118 -EC 75221 PH 5 Retension: Review Final DRB Pkg<br/>02/02/10 23 02/08/10 13</div>        |    |    |    |    |    |    |             |    |    |    |    |    |    |          |              |  |  |  |  |  |     |  |
| ACT                          | Description                                                           | Early Start | Early Finish | Rem Dur | TF   | 04                                                                                               | 11 | 18 | 25 | 01 | 08 | 15 | 22          | 01 | 08 | 15 | 22 | 29 | 05 |          |              |  |  |  |  |  |     |  |
|                              |                                                                       |             |              |         |      | Jan                                                                                              |    |    |    |    |    |    | Feb         |    |    |    |    |    |    | Mar      |              |  |  |  |  |  | Apr |  |
| Legend:                      |                                                                       |             |              |         |      | Milestones                                                                                       |    |    |    |    |    |    | In-Progress |    |    |    |    |    |    | Activity |              |  |  |  |  |  |     |  |
|                              |                                                                       |             |              |         |      |                                                                                                  |    |    |    |    |    |    |             |    |    |    |    |    |    |          | Page 9 of 11 |  |  |  |  |  |     |  |
| January 18, 2010 03:47:20 PM |                                                                       |             |              |         |      |                                                                                                  |    |    |    |    |    |    |             |    |    |    |    |    |    |          |              |  |  |  |  |  |     |  |

# CR3 NPC Outage Containment Repair Project - Level 3 Schedule

| ACT                                                           | Description                                                | Early Start | Early Finish | Rem Dur | TF   | Jan                                                        |    |    |    | Feb |                                                                                      |    |    | Mar |    |    |    | Apr                                                           |    |  |  |
|---------------------------------------------------------------|------------------------------------------------------------|-------------|--------------|---------|------|------------------------------------------------------------|----|----|----|-----|--------------------------------------------------------------------------------------|----|----|-----|----|----|----|---------------------------------------------------------------|----|--|--|
|                                                               |                                                            |             |              |         |      | 04                                                         | 11 | 18 | 25 | 01  | 08                                                                                   | 15 | 22 | 01  | 08 | 15 | 22 | 29                                                            | 05 |  |  |
| DELDES51205                                                   | EC 75221 PH 5 Retension: Final DRB Meeting                 | 02/08/10 13 | 02/08/10 15  | 2       | 3234 |                                                            |    |    |    |     | 119 EC 75221 PH 5 Retension: Final DRB Meeting<br>02/08/10 13 02/08/10 15            |    |    |     |    |    |    |                                                               |    |  |  |
| DELDES51215                                                   | -EC 75221 PH 5 Retension: Incorporate Final DRB Comments   | 02/08/10 15 | 02/09/10 15  | 24      | 3234 |                                                            |    |    |    |     | 120 -EC 75221 PH 5 Retension: Incorporate Final DRB Com<br>02/08/10 15 02/09/10 15   |    |    |     |    |    |    |                                                               |    |  |  |
| DELDES51220                                                   | EC 75221 PH 5 Retension: Obtain Supervisor Approval        | 02/09/10 15 | 02/09/10 23  | 8       | 3234 |                                                            |    |    |    |     | 121 EC 75221 PH 5 Retension: Obtain Supervisor Approval<br>02/09/10 15 02/09/10 23   |    |    |     |    |    |    |                                                               |    |  |  |
| DELDES5130Z                                                   | EC 75221 PH 5 Retension: MILESTONE - All Reviews Complete  | 02/09/10 15 | 02/09/10 15  | 0       | 3234 |                                                            |    |    |    |     | 122 EC 75221 PH 5 Retension: MILESTONE - All Reviews C<br>02/09/10 15 02/09/10 15    |    |    |     |    |    |    |                                                               |    |  |  |
| DELDES51225                                                   | -EC 75221 PH 5 Retension: Obtain PGM Approval              | 02/09/10 23 | 02/10/10 23  | 24      | 3234 |                                                            |    |    |    |     | 123 -EC 75221 PH 5 Retension: Obtain PGM Approval<br>02/09/10 23 02/10/10 23         |    |    |     |    |    |    |                                                               |    |  |  |
| DELDES5140Z                                                   | EC 75221 PH 5 Retension: MILESTONE - PGM Approval          | 02/10/10 23 | 02/10/10 23  | 0       | 3234 |                                                            |    |    |    |     | 124 EC 75221 PH 5 Retension: MILESTONE - PGM Approv<br>02/10/10 23 02/10/10 23       |    |    |     |    |    |    |                                                               |    |  |  |
| DELDES51710                                                   | EC 75221 PH 5 Retension: Planning Prepare EC Work Packages | 02/10/10 23 | 02/13/10 23  | 72      | 3234 |                                                            |    |    |    |     | 125 EC 75221 PH 5 Retension: Planning Prepare EC Work P<br>02/10/10 23 02/13/10 23   |    |    |     |    |    |    |                                                               |    |  |  |
| Containment Repair Contracting / Subcontracting / Procurement |                                                            |             |              |         |      |                                                            |    |    |    |     |                                                                                      |    |    |     |    |    |    |                                                               |    |  |  |
| DELCON1M                                                      | Contracting/Subcontracting/Procurement Complete MILESTONE  | 02/08/10 17 | 02/08/10 17  | 0       | 3360 |                                                            |    |    |    |     | 127 Contracting/Subcontracting/ Procurement Complete MILE<br>02/08/10 17 02/08/10 17 |    |    |     |    |    |    |                                                               |    |  |  |
| Containment Repair Subcontracting                             |                                                            |             |              |         |      |                                                            |    |    |    |     |                                                                                      |    |    |     |    |    |    |                                                               |    |  |  |
| DELCON09M                                                     | Award Hydro-Demolition Contract Compl MILESTONE            | 01/18/10 14 | 01/18/10 14  | 0       | 3229 |                                                            |    |    |    |     | 129 Award Hydro-Demolition Contract Compl MILESTON<br>01/18/10 14 01/18/10 14        |    |    |     |    |    |    |                                                               |    |  |  |
| DELCON11                                                      | -Award Batch Plant Contract                                | 12/04/09 19 | 02/08/10 17  | 507     | 3082 | 130 -Award Batch Plant Contract<br>12/04/09 19 02/08/10 17 |    |    |    |     |                                                                                      |    |    |     |    |    |    |                                                               |    |  |  |
| DELCON11M                                                     | Award Batch Plant Contract Compl MILESTONE                 | 02/08/10 17 | 02/08/10 17  | 0       | 3082 |                                                            |    |    |    |     | 131 Award Batch Plant Contract Compl MILESTONE<br>02/08/10 17 02/08/10 17            |    |    |     |    |    |    |                                                               |    |  |  |
| Containment Repair Testing                                    |                                                            |             |              |         |      |                                                            |    |    |    |     |                                                                                      |    |    |     |    |    |    |                                                               |    |  |  |
| DELTST06                                                      | Perform Concrete Scan / Boring                             | 03/28/10 04 | 03/30/10 04  | 48      | 2437 |                                                            |    |    |    |     |                                                                                      |    |    |     |    |    |    | 133 Perform Concrete Scan / Boring<br>03/28/10 04 03/30/10 04 |    |  |  |
| ACT                                                           | Description                                                | Early Start | Early Finish | Rem Dur | TF   | 04                                                         | 11 | 18 | 25 | 01  | 08                                                                                   | 15 | 22 | 01  | 08 | 15 | 22 | 29                                                            | 05 |  |  |
|                                                               |                                                            |             |              |         |      | Jan                                                        |    |    |    | Feb |                                                                                      |    |    | Mar |    |    |    | Apr                                                           |    |  |  |

# CR3 NPC Outage Containment Repair Project - Level 3 Schedule

