

CONTRACTS - AWARD SUMMARY

LATA - SHARP REMEDIATION SERVICES, LLC

D&D of Building K-33 at the East Tennessee Technology Park (ETTP), Oak Ridge, Tennessee


[Clarification Of Codes](#)

Choose a quarter and click "Go."

October 1 - December 31, 2011

AWARD OVERVIEW

Award Number	DT0001408	Funding Agency	Department of Energy
Total Award Amount	\$71,037,996	Project Location - City	Oak Ridge
Award Date	04/06/2010	Project Location - State	TN
Project Status	More than 50% Completed	Project Location - Zip	378306898
Jobs Reported	72.92	Congressional District	03
Project Location - Country	US		

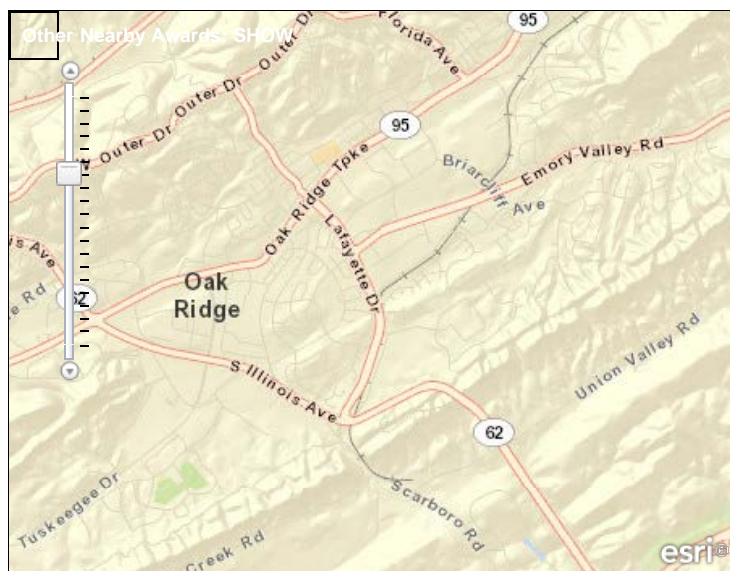

PROJECT LOCATION DETAIL

Latitude, Longitude	36° 0' 44", -84° 14' 23"
Congressional District	03
Address 1	185 Lafayette Drive
Address 2	
City	Oak Ridge
County	Anderson
State	TN
Zip	378306898

RECIPIENT INFORMATION (CONTRACTS)

Recipient Name	LATA - SHARP REMEDIATION SERVICES, LLC
Recipient DUNS Number	192272396
Recipient Address	999 CENTRAL AVE STE 300
Recipient City	LOS ALAMOS
Recipient State	New Mexico
Recipient Zip	875443328
Recipient Congressional District	03
Recipient Country	USA
Required to Report Top 5 Highly Compensated Officials	Yes
Top 5 Officer Compensations	91996.00, 261214.00, 188757.00, ,
Top 5 Officers	Ress Lattimer, Clyde Gaston, Ron Voorheis, ,

Feedback



Provide feedback or comments on the performance and progress of awards.

[» Submit Feedback/Comments](#)

PROJECTS AND JOBS INFORMATION

Project Title	Federal Contract
Project Status	More than 50% Completed
Final Project	

Report Submitted	No
Project Activities Description	Remediation Services
Quarterly Activities/Project Description	<p>Structural Demolition ? Structural demolition is 100% complete. ? 2,829,913 total square feet of floor area has been demolished. ? Waste loading / shipping is continuing at a pace well ahead of planned shipping schedules. Waste sizing is 100% complete. Project waste specialists monitor loading activities and occasionally require re-sizing of in individual item prior to shipment. Exterior Transite Removal ? This activity is 100% complete. Waste Transportation ? Building debris waste disposition is 100% complete. As of September 21, 2011, LSRS shipped 163,910.19 tons of building debris to EMWMF, representing 137.17% of the originally estimated debris tonnage. 14,742 truckloads were shipped over 150 days of hauling, providing a running average of 98.28 loads per day. ? Initiated shipment of slab debris on 9-26-11. ? For WE 12-30-11, LSRS shipped 30,458 tons of slab concrete representing 55.6% of total estimated tonnage. ? A total of 57.9 tons of above ground piping has been shipped to date. ? No loads rejected by EMWMF to date for WAC non-compliance. Slab Demolition ? Removal of the slab is continuing according to schedule ? A total of 678,436 square feet have been removed and processed to date, representing 48% of the total slab footprint. Above Ground Piping Above ground piping, pipe supports and base removal is 100% complete. Site restoration is 100% complete.</p>
Jobs Created	72.92
Description of Jobs Created	<p>Project Manager, Project Controls/EVMS Manager, ESH&Q Manager, Business Manager, Site Safety Officer, QA Specialist, Field Verification Officer, Document Controls Specialist, Purchasing Specialist, Contracts Manager, Project Administrator, Operator, Laborers, and Carpenters; Total Project FTEs - 72.92; LSRS FTEs - 45.3; Total Subcontractor FTEs - 27.62</p>

PURCHASER INFORMATION (CONTRACTS)

Contracting Office ID	00518
Contracting Office Name	Not Available
Contracting Office Region	Not Available
TAS Major Program	89-5657

AWARD INFORMATION

Award Date	04/06/2010
Award Number	DT0001408
Order Number	2002210
Award Type	Contracts
Funding Agency ID	89
Funding Agency Name	Department of Energy
Funding Office Name	Not Available
Awarding Agency ID	89
Awarding Agency Name	Department of Energy
Amount of Award	\$71,037,996

Funds Invoiced/Received	\$55,691,954
Expenditure Amount	\$0
Infrastructure Expenditure Amount	\$0
Infrastructure Purpose and Rationale	Not Reported
Infrastructure Point of Contact Name	Not Reported
Infrastructure Point of Contact Email	Not Reported
Infrastructure Point of Contact Phone	Not Reported
Infrastructure Point of Contact Address	Not Reported
Infrastructure Point of Contact City	Not Reported
Infrastructure Point of Contact State	Not Reported
Infrastructure Point of Contact Zip	Not Reported

PRODUCT OR SERVICE INFORMATION (CONTRACTS)

Primary Activity Code	562910
Activity Description	Remediation Services

SUB-AWARDS INFORMATION

Sub-awards to Organizations	18
Sub-award Amounts to Organizations	\$29,332,353
Sub-Awards to Individuals	0
Sub-Award Amounts to Individuals	\$0
Number of Sub-awards less than \$25,000/award	1069
Amount of Sub-awards less than \$25,000/award	\$1,552,002
Number of payments to vendors greater than \$25,000	0
Total Amount of payments to vendors greater than \$25,000/award	\$0
Number of payments to vendors less than \$25,000/award	0
Total Amount of payments to vendors less than \$25,000/award	\$0

SUB-AWARD TRANSACTIONS

- [+] Sub-Award TN-K33-10-117 - ALLIANT CORPORATION
- [+] Sub-Award TNO-K33-10-008 - ALLSTATE TRAILERS, INC
- [+] Sub-Award TN-K33-10-121 - AMARC LLC
- [+] Sub-Award TN-K33-10-153 - BIG TOP TRAMPOLINE, INC.
- [+] Sub-Award TN-K33-10-032 - BROADWAY ELECTRIC SERVICE CORPORATION
- [+] Sub-Award LSRS-10S0012 - CLAIBORNE HAULING, LLC
- [+] Sub-Award LSRS-10S0013 - COMPANY WRENCH, LTD.
- [+] Sub-Award TN-K33-11-532 - D & N ELECTRIC COMPANY
- [+] Sub-Award LSRS-10S0002 - ENERGYSOLUTIONS GOVERNMENT GROUP, INC.
- [+] Sub-Award LSRS-10S0003 - FLUOR FEDERAL SERVICES, INC.
- [+] Sub-Award LSRS10S0005 - FOCUS MANAGEMENT, INC.

[+] Sub-Award Inter-Company Agreement 70031-11073 - LOS ALAMOS TECHNICAL ASSOCIATES, INC.

[+] Sub-Award TN-K33-10-150 - RESTORATION SERVICES, INC.

[+] Sub-Award TN-K33-10-191 - S&ME, INC.

[+] Sub-Award LSRS-10S0004 - TETRA TECH, INC.

[+] Sub-Award TNO-K33-10-006 - TFE, INC

[+] Sub-Award LSRS-10S0015 - WACO INTERNATIONAL CORPORATION

[+] Sub-Award TN-K33-10-221 - WRAP IT UP CONSTRUCTION, L.L.C.
