



**Public Meeting on the Operating License
Application for Watts Bar Nuclear Plant
Unit 2**

April 9, 2014



Enclosure 4

Meeting Agenda

- Introductions
- TVA presentation on project status
- NRC presentation on project status and remaining activities
- Questions and comments

Topics

- Background
- Restart of Unit 2 Review
- Licensing Activities
- Oversight Activities
- Upcoming Milestones
- Public Involvement
- Questions

Background

- 1971 – Under Part 50, NRC receives construction permit (CP) application
- 1972 – Mandatory hearings held
- 1973 – CPs issued
- 1976 – Operating licenses (OLs) received
- 1985 – TVA suspends construction
- 1990 to 95 – TVA addresses construction quality issues for Unit 1 and defers work on Unit 2
- February 7, 1996 – NRC issues OL for Unit 1

Restart of Unit 2 Review


- 2007 – TVA informs NRC of its intent to restart construction activities and complete construction in 2012
- 2007 –2008 – NRC established Unit 2 resident inspector office (IMC2517 ADAMS ML13136A301)
- 2008 – NRC established the licensing review process (LIC-110 ADAMS ML092160833)
- 2009 – Notice in Federal Register to provide opportunity for hearing
- 2012 – TVA informs NRC of delays to construction of Unit 2
 - Operating License/Fuel load between January and June 2015
 - Commercial Operation by December 2015



United States Nuclear Regulatory Commission

Protecting People and the Environment

Operating License Review

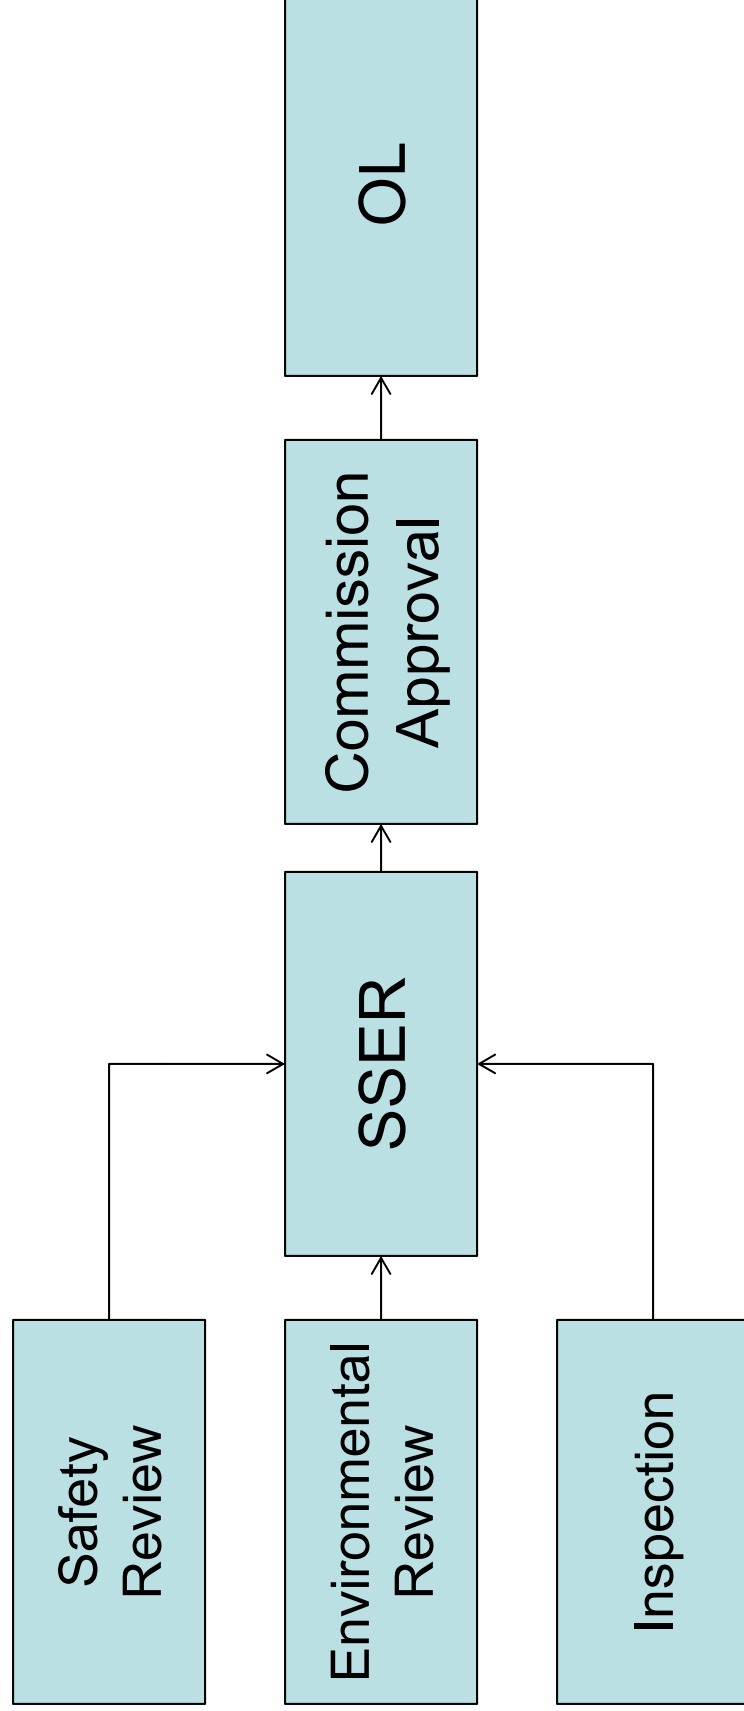


Licensing Activities

- Staff is working toward an operating license decision in January 2015
- Licensing activities completed
 - Issued 6 Supplemental Safety Evaluation Reports (SSERs) documenting the staff's safety review
 - Held 9 ACRS Subcommittee and one Full Committee meetings
 - Issued Supplement 2 to the Final Environmental Statement
- Licensing activities remaining
 - Closing out open items identified in previous 6 SSERs
 - Final ACRS Subcommittee and Full Committee meetings
 - Fukushima Orders review

Construction Inspection Program

Inspection Manual Chapter (IMC) 2517, Watts Bar
Unit 2 Construction Inspection Program

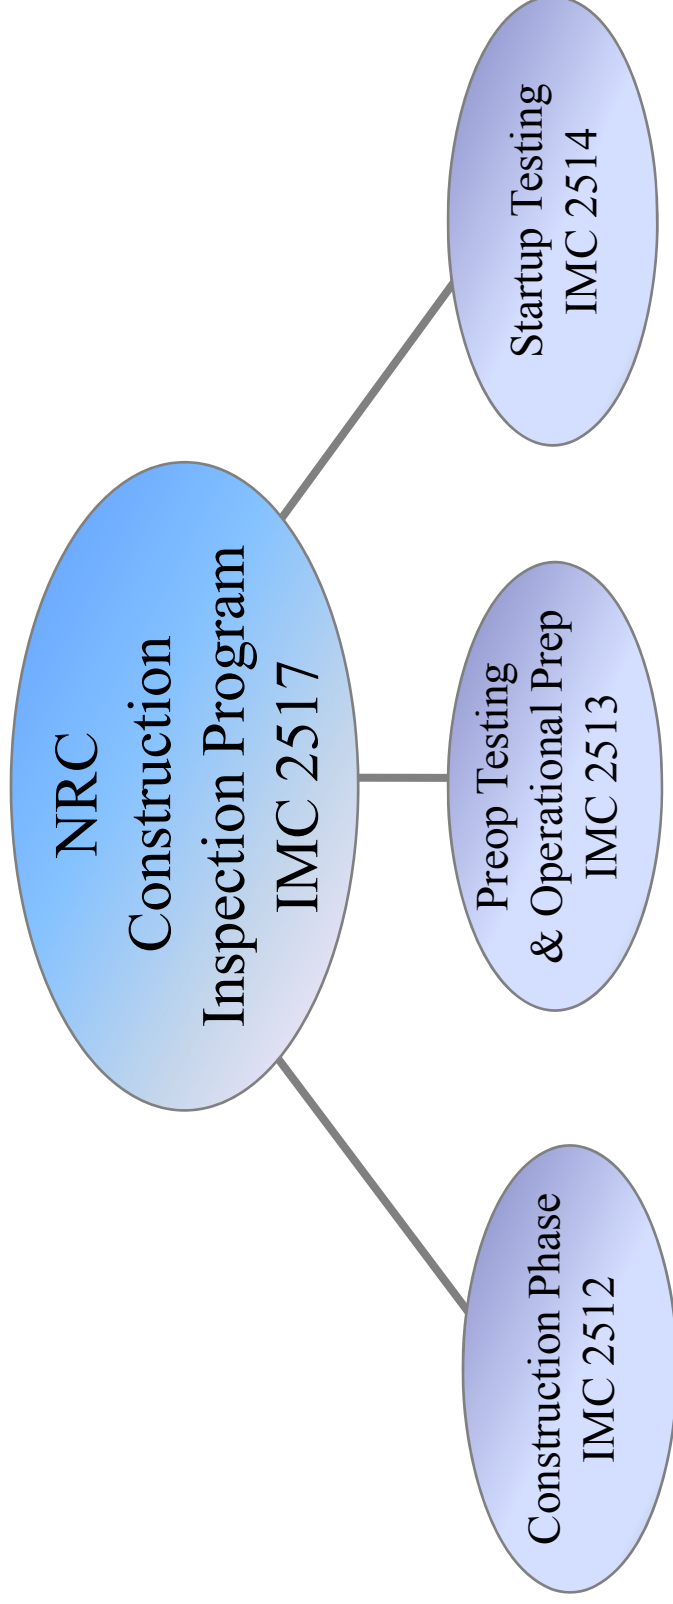

Status of Inspection Items

- 547 construction inspection items in the Inspection Planning and Scheduling (IP&S) database
- Inspections completed for 378 IP&S items
- Closed ten (10) Corrective Action Programs and Special Programs
- Pre-operational testing inspections started

Remaining Inspection Items

- Complete inspections for 169 open IP&S items
- Many remaining IP&S items have been inspected, but require additional effort to close
- Planning completed for preoperational testing inspections – Waiting on testing to be performed
- Operational readiness inspections started
- Majority of IMC 2514 start-up testing inspections performed after licensee issuance



United States Nuclear Regulatory Commission


Protecting People and the Environment

Oversight Activities

- Impact of Construction Schedule on Inspection Program
 - Increased number of residents to four
 - Increased resident support activities from the region
 - Focus is on scheduling and inspecting activities
 - Reviewing TVA’s Primavera construction schedule
 - Adjusting NRC schedule for remaining inspection items
 - Pace of regional inspections has increased
 - Scheduling of inspections
 - Scheduled inspections for 77% of the remaining open items
 - Scheduled 34 inspections to review pre-operational activities
 - Scheduled 6 operational readiness inspections
- Planning underway for transition to the Reactor Oversight Process

Milestones

<http://www.nrc.gov/info-finder/reactor/wb/watts-bar.html>

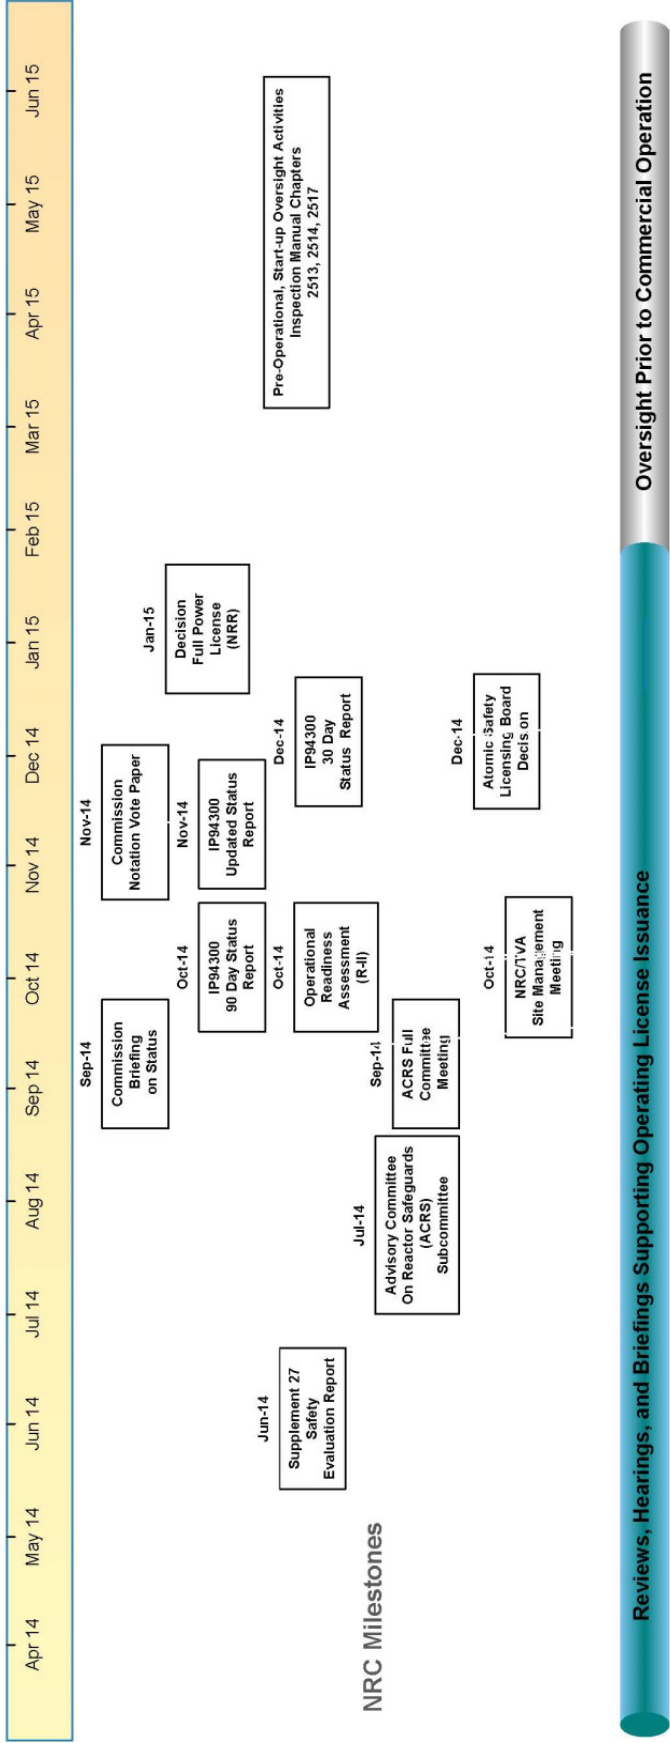

As of March 28, 2014
TVA to begin Watts Bar Nuclear Plant Unit 2 Commercial Operation approximately 6-8 months after issuance of Operating License and Initial Fuel Loading
Dates are subject to change

Watts Bar Nuclear Plant Licensing Schedule
U.S. Nuclear Regulatory Commission
Office of Nuclear Reactor Regulation



United States Nuclear Regulatory Commission

Protecting People and the Environment

Additional Information

- Website - <http://www.nrc.gov/info-finder/reactor/wb/watts-bar.html>
- NRR Office Instruction LIC-110
 - ADAMS (<http://www.nrc.gov/reading-rm/adams.html>) Accession No. ML092160833
- Inspection Manual Chapter 2517
 - Accession No. ML13136A301
- Points of contact
 - Justin Poole, Senior Project Manager
 - Phone: 301-415-2048
 - Email: justin.poole@nrc.gov
 - Jeanne Dion, Project Manager
 - Phone: 301-415-1349
 - Email: jeanne.dion@nrc.gov
 - Tomy Nazario, Senior Resident Inspector
 - Phone: 423-365-9112
 - Email: tomy.nazario@nrc.gov
