



Nuclear Decommissioning Citizens Advisory Panel (NDCAP)

May 25, 2017





Introductions

Joseph R. Lynch
Sr. Manager, Government Affairs
Decommissioning – EWC



Decommissioning Project Status


VY Decommissioning Update

- Dry Fuel Storage Project
 - ISFSI Pad Construction
 - Construction restarted on March 13th, 2017
 - Rebar placement for the second ISFSI pad is complete
 - Concrete placement is the next project milestone
- Dry Fuel Loading
 - 2017: Approximately 20 Dry Casks
 - 2018: Target loading remainder with 45 total loaded
 - All fuel transferred to the ISFSI: Target 3Q/4Q 2018, pending NRC approvals



VY Decommissioning Update (Cont'd)

Current ISFSI Pad Configuration

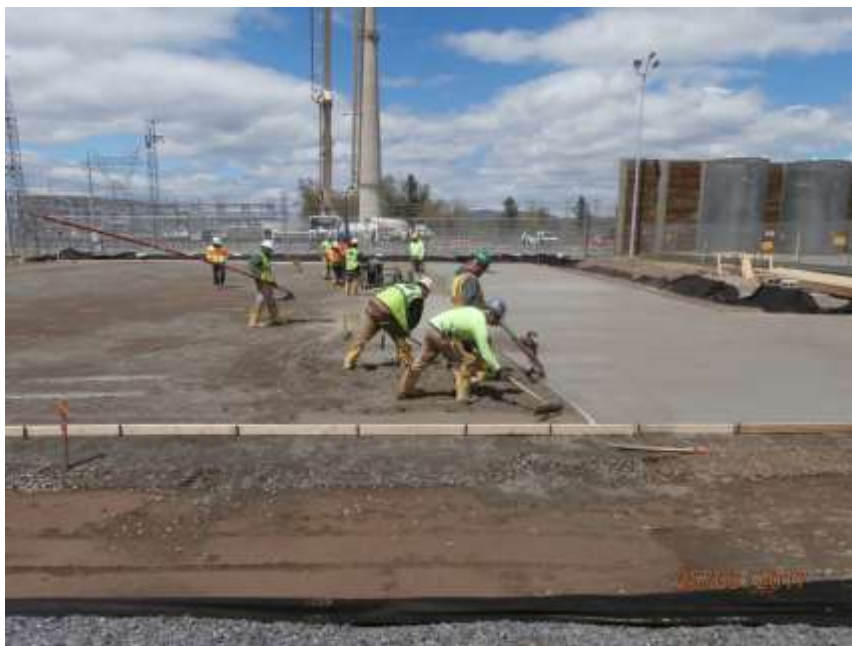

Pouring of Leveling Slab for ISFSI Pad 2



VY Decommissioning Update (Cont'd)

Rebar Placement for 2nd ISFSI Pad



VY Water Management Update

- Water Management Update

- Intrusion Water Disposition Plan

- Intrusion water retention, shipment and removal plan continues to be implemented.
 - In-leakage prevention projects seeking to further reduce the intrusion of groundwater continue.

- EnergySolutions is providing shipment and disposal services

- Groundwater is being shipped to EnergySolutions licensed disposal site in Tennessee.
 - Shipping approximately three shipments per month at the present intrusion rate to minimize on-site storage.
 - A total of 517,000 gallons have been shipped to date.





Proposed VY Sale and Accelerated Decommissioning

Public Service Board Proceeding Update

- First Round of Discovery Requests on Petitioners – March 17th
- Responses to First Round of Discovery Requests – April 26th
- DPS filed motion for protective order for confidential documents – May 2nd
- NorthStar filed Motion for Special Protocol for Access to Highly Confidential Documents – May 5th
- Second Round of Discovery Requests on Petitioners – May 10th*
- NEC filed a Motion for Partial Summary Judgment – May 5th
 - Petitioner response to NEC Motion due June 5th

* DPS filed Motion for Extension of Discovery Request Deadline





Nuclear Decommissioning Trust Update

Nuclear Decommissioning Trust Update

- The ENVY Nuclear Decommissioning Trust (NDT) balance was \$568.9 Million on March 31, 2017
- The NDT balance was \$570 Million on April 30, 2017
 - The increase was due to positive market performance, partially offset by reimbursements from the NDT. Fund expenses occur periodically throughout the year.
 - Summary of NDT Performance in 2017:
 - \$11.9M in Qualified Withdrawals
 - \$21.7M in Market Gains
 - \$1.4M in Fund Expenses
- The Site Restoration Trust balance was \$23.6 Million on April 30, 2017.
 - Entergy has funded \$20M to date; \$3.6M fund growth.
 - Final \$5M annual contribution to the Site Restoration Trust scheduled for December 2017.



Open Communication and Transparency

- Nuclear Decommissioning Citizens Advisory Panel (NDCAP)
- Stakeholder Outreach
 - Speaking Engagements
 - Media Interviews
 - Local Advertising
 - Continued Community Involvement
- Tours for Key Stakeholders
- Updated ENVY Decommissioning Website, www.vydecommissioning.com



Open Communication and Transparency



[History](#) [Get The Facts](#) [News](#) [Document Library](#) [Resources](#) [Contact](#) [Q](#)

WELCOME TO
ENERGY VERMONT YANKEE
DECOMMISSIONING

FAQS

View our answers to the most frequently asked questions we receive.

[More Details](#)

GET THE FACTS

Get accurate information about nuclear power station decommissioning.

[More Details](#)

DOCUMENT LIBRARY

Visit our Document Library for a full list of State and Federal filings.

[More Details](#)





QUESTIONS?

— WE POWER LIFE™

