



UNITED STATES
NUCLEAR REGULATORY COMMISSION
WASHINGTON, D. C. 20555

JUL 26 1984

Docket No.: STN 50-482

Mr. Glenn L. Koester
Vice President - Nuclear
Kansas Gas & Electric Company
201 North Market Street
Post Office Box 208
Wichita, Kansas 67201

Dear Mr. Koester:

Subject: Summary of May 24, 1984 Caseload Forecast Panel Visit

By letter dated May 9, 1984, the NRC staff informed Kansas Gas and Electric Company (KG&E) that we would conduct a Caseload Forecast Panel visit at the Wolf Creek site on May 24, 1984. To facilitate our assessment, we requested that KG&E respond to 17 questions relating to the detailed status of construction and preparation for fuel load at Wolf Creek. KG&E provided the requested information by letter dated May 18, 1984.

On May 24, 1984, the NRC Caseload Forecast Panel visited the Wolf Creek site for the purpose of reviewing construction progress and obtaining information for assessing KG&E's projected fuel load date.

At a brief meeting preceding the plant tour KG&E staff discussed the status of the construction completion and presented the panel with the then current Wolf Creek Project Milestone Schedule dated May 17, 1984 (Enclosure 1). That schedule identified a KG&E projected fuel load date of October 7, 1984.

The Caseload Forecast Panel toured the facility on May 24, 1984, with KG&E representatives and other interested parties (Enclosure 2) to observe the construction status and preparations for preoperational and hot functional testing. Following the tour the staff met briefly with KG&E staff and discussed the progress of the Wolf Creek preoperational testing program as compared with the schedule of actual completion of those tests at Callaway. KG&E provided a graph which compared the relative progress of the preoperational/acceptance tests at Callaway vs Wolf Creek (Enclosure 3).

In response to a request from the NRC staff, KG&E agreed to provide updated copies of the Wolf Creek Project Milestone Schedule every two weeks. By letters dated June 21 and July 9, 1984, KG&E has submitted these updated schedules dated June 18, 1984 and July 2, 1984 respectively. By letter dated June 19, 1984 (Enclosure 4) KG&E informed the NRC staff that they had revised their fuel load estimate from October 7, 1984 to November - December 1984.

8408070028 840726
PDR ADOCK 0500482
A PDR

JUL 26 1984

Based on our review of the material provided by KG&E and our observations during the May 24, 1984 site visit, the Caseload Forecast Panel has concluded that completion of the Wolf Creek Generating Station construction in the November - December time frame is achievable. While arriving at this conclusion, the panel recognizes that some contingency has been allowed in the preoperational and startup testing programs. However, a high degree of successful completion in a timely manner will be required by KG&E to conclude these programs within the projected range of dates.

The NRC staff will allocate its resources to assure that the NRC licensing review and inspection program are completed on a schedule compatible with the applicant's November - December projected fuel load date.

Sincerely,

ORIGINAL SIGNED BY:

B. J. Youngblood, Chief
Licensing Branch No. 1
Division of Licensing

Enclosures: As stated

cc: See next page

DISTRIBUTION:
See attached page

LB#1:DL *pwot*
PO'Connor:kab
07/23/84

[Signature]
LB#3:DL
JHolonich
07/23/84

[Signature]
LB#1:DL
BJYoungblood
07/23/84

RM *[Signature]*
RHartfield
07/23/84

AD:DL *[Signature]*
TNovak
07/26/84

D:DL *[Signature]*
DEisenhut
07/26/84

WOLF CREEK

JUL 26 1984

Mr. Glenn L. Koester
Vice President - Nuclear
Kansas Gas and Electric Company
201 North Market Street
Post Office Box 208
Wichita, Kansas 67201

cc: Mr. Nicholas A. Petrick
Executive Director, SNUPPS
5 Choke Cherry Road
Rockville, Maryland 20850

Jay Silberg, Esq.
Shaw, Pittman, Potts & Trowbridge
1800 M Street, N. W.
Washington, D. C. 20036

Mr. Donald T. McPhee
Vice President - Production
Kansas City Power & Light Company
1330 Baltimore Avenue
Kansas City, Missouri 64141

Ms. Mary Ellen Salava
Route 1, Box 56
Burlington, Kansas 66839

A. Scott Cauger
Assistant General Counsel
Public Service Commission
P. O. Box 360
Jefferson City, Missouri 65101

Mr. Howard Bundy
Resident Inspector/Wolf Creek NPS
c/o U.S.N.R.C.
Post Office Box 311
Burlington, Kansas 66839

Mr. Robert M. Fillmore
State Corporation Commission
State of Kansas
Fourth Floor, State Office Bldg.
Topeka, Kansas 66612

Terri Sculley, Director
Special Projects Division
Kansas Corporation Commission
State Office Building, Fourth Floor
Topeka, Kansas 66612

Ms. Wanda Christy
515 N. 1st Street
Burlington, Kansas

Eric A. Eisen, Esq.
Birch, Horton, Bittner & Moore
1140 Connecticut Avenue, N. W.
Washington, D. C. 20036

C. Edward Peterson, Esq.
Legal Division
Kansas Corporation Commission
State Office Building, Fourth Floor
Topeka, Kansas 66612

John M. Simpson, Esq.
Attorney for Intervenors
4350 Johnson Drive, Suite 120
Shawnee Mission, Kansas 66205

Mr. John T. Collins
U.S.N.R.C. - Region
611 Ryan Plaza
Suite 1000
Arlington, Texas 76011

Mr. Joe Mulholland
Manager of Power Supply & Engineering
Kansas Electric Power Cooperative, Inc.
Post Office Box 4877
Gage Center Station
Topeka, Kansas 66604

Mr. James G. Keppler
U.S.N.R.C. - Region III
799 Roosevelt Road
Glen Ellyn, Illinois 60137

Brian P. Cassidy, Regional Counsel
Federal Emergency Management Agency
Region I
J. W. McCormack POCH
Boston, Massachusetts 02109

WOLF CREEK PROJECT MILESTONE SCHEDULE

Milestones
 Construction Activities
 Engineering Activities
 Start-Up Activities
 Operations


Project Milestones
 Project Directives
 Bid Turnover
 Actual

X Complete
 007

DATE DATE

APPROVED BY: *[Signature]*
 REVISION: 6
 ISSUE DATE: 5/17/84

ENCLOSURE 1

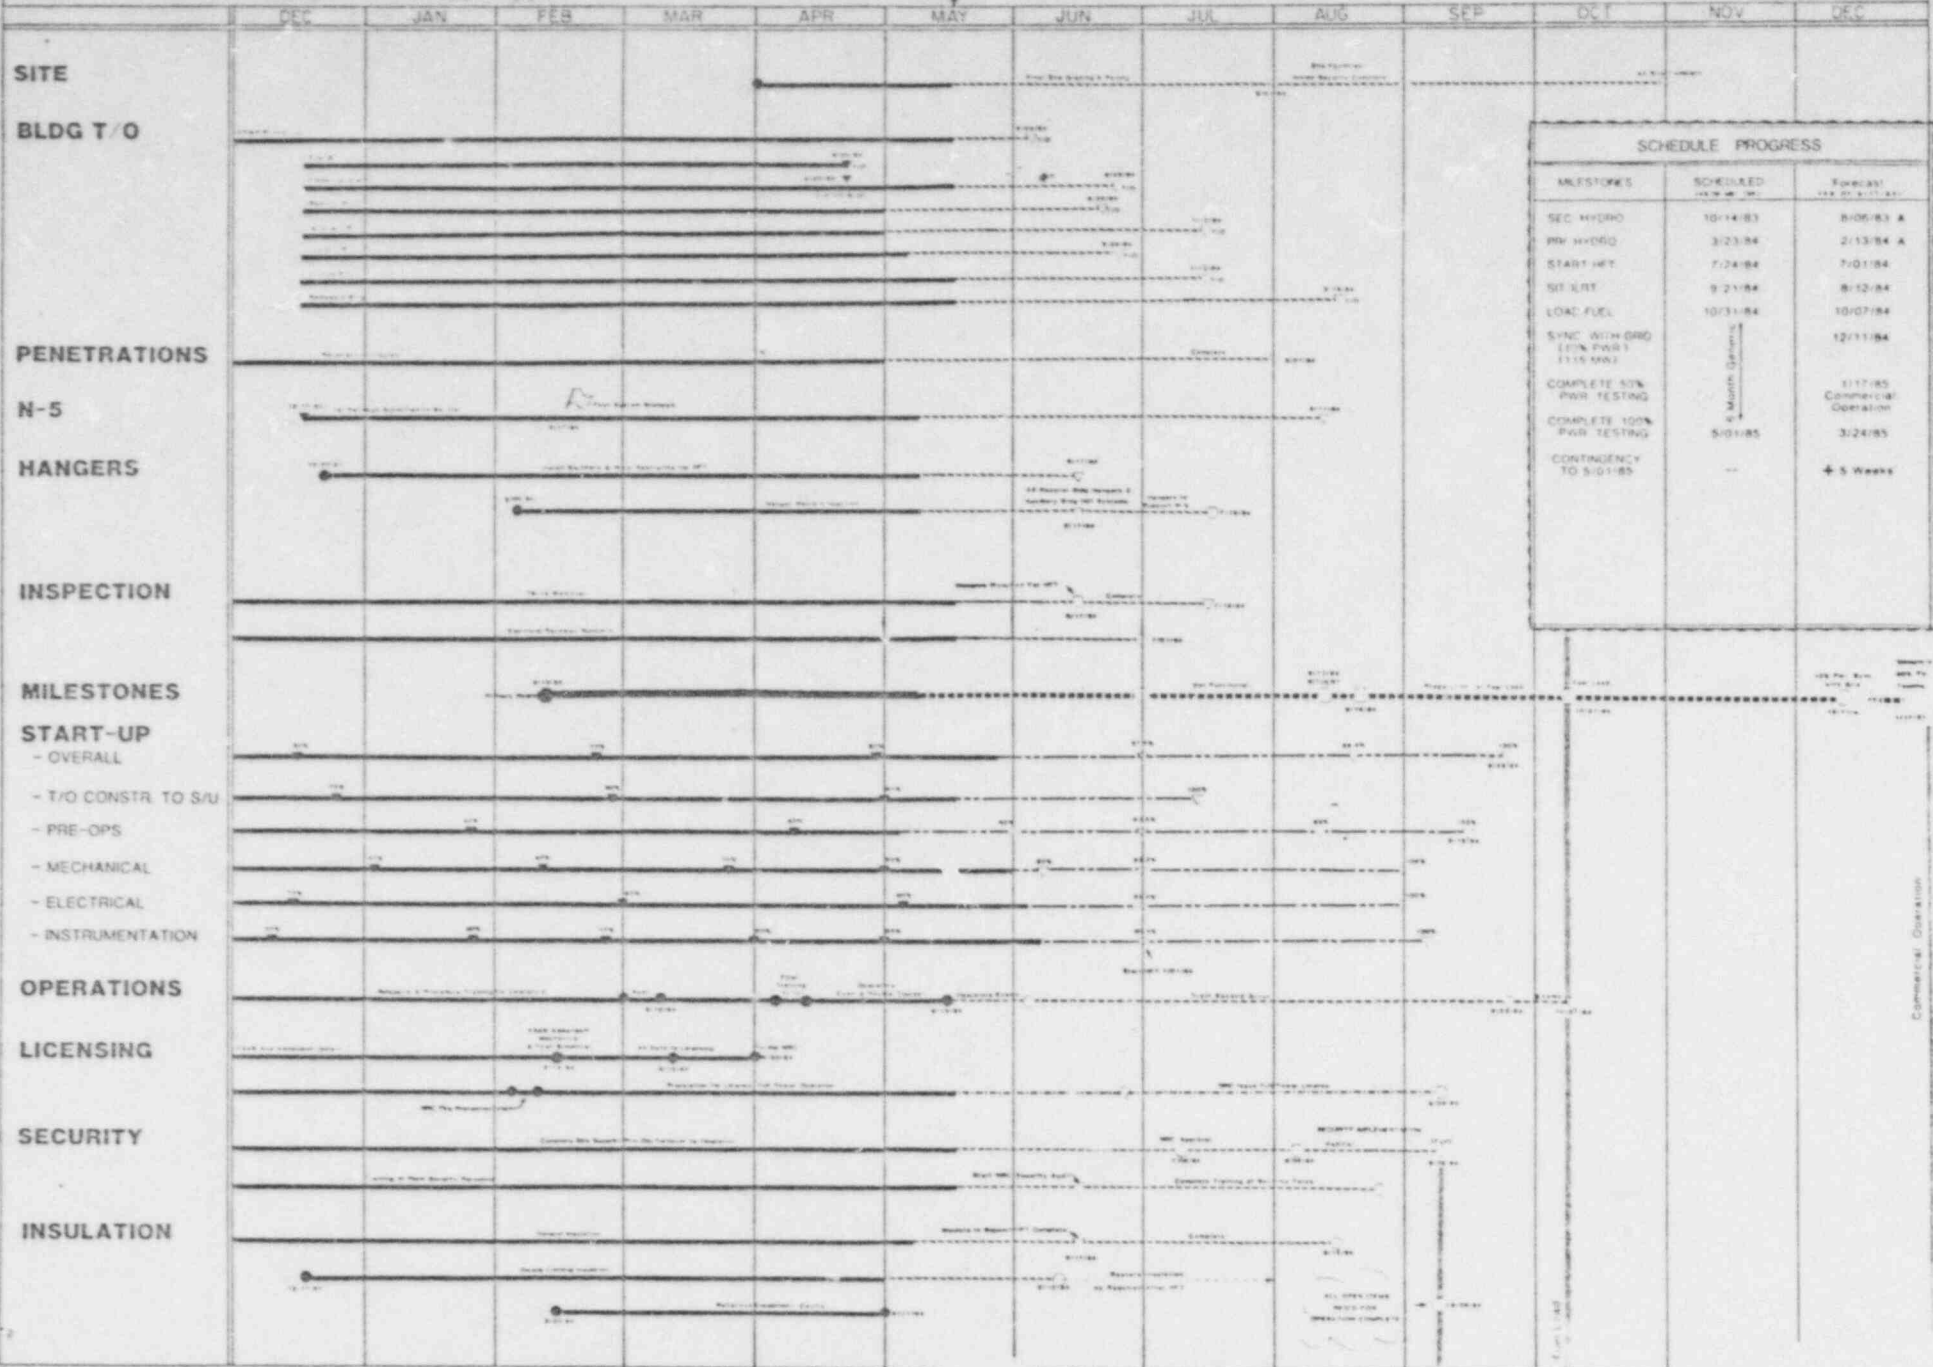

SCHEDULE PROGRESS		
MILESTONES	SCHEDULED	FORECAST
SEC HYDRO	10/14/83	8/06/84 A
PRY HYDRO	3/23/84	2/13/84 A
START-UP	7/24/84	7/01/84
50% CRT	9/21/84	8/12/84
LOAD FUEL	10/31/84	10/07/84
SYNC WITH GRID (10% PWR @ 11.55 MW)		12/11/84
COMPLETE 50% PWR TESTING		11/17/85
COMPLETE 100% PWR TESTING	5/01/85	3/24/85
CONTINGENCY TO 5/01/85		+ 5 Weeks

Commercial Operation

ENCLOSURE 2

MAY 24, 1984 SITE TOUR PARTICIPANTS

NRC Caseload Forecast Panel

B. J. Youngblood, Chairman
Paul W. O'Connor
Howard Bundy
John Neisler
James Konklin
Eric Johnson
R. Hartfield

Kansas Gas & Electric Company

Gary Fouts
Jim McKinstry
Ron Holloway
Otto Maynard
Lyle Koerper

KEPCO

Frank Garver

Kansas Corporation Commission

Emily Wellnar
Gary Hayden


Missouri Public Service Commission

Cary Featherston
Bill Nickel

Others

Bob Von Sternberg - Wichita Eagle - Beacon
Mitchel Benson - Kansas City Star
Roger Wilson - TV Channel 12 - Wichita

NUMBER OF PREOPERATIONAL TESTS

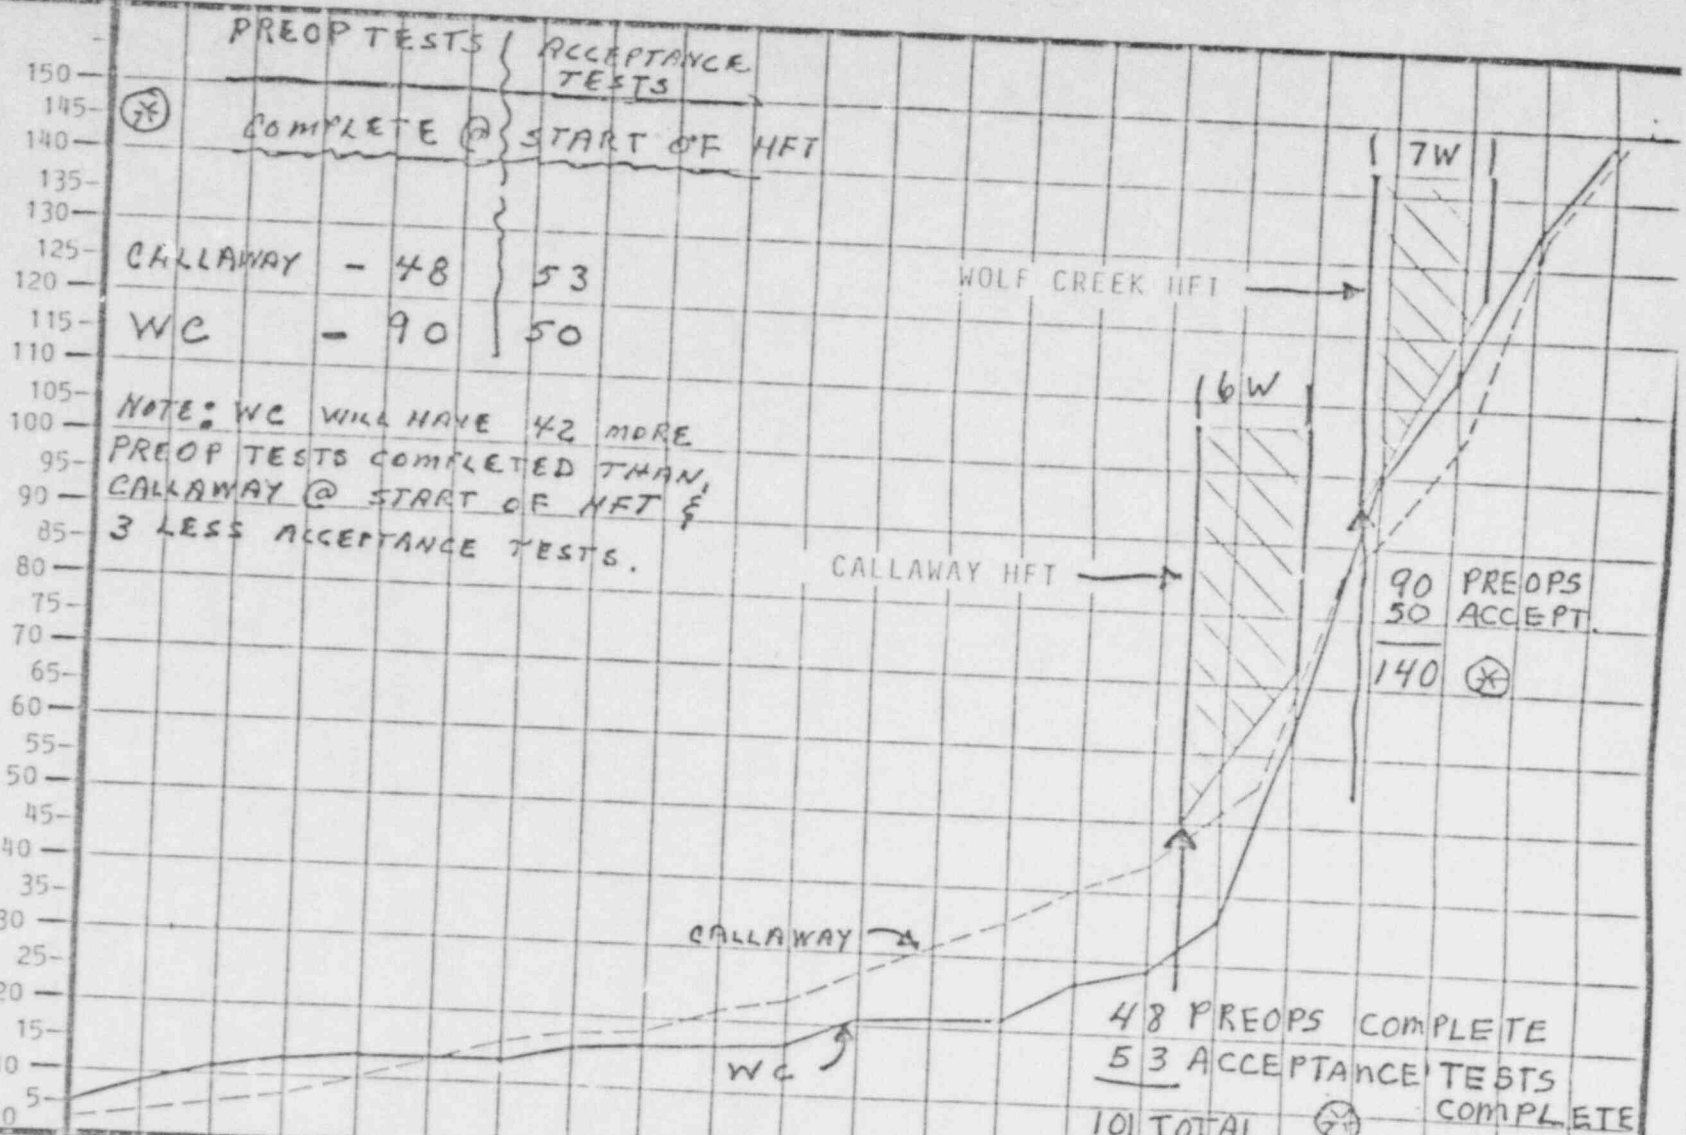

MONTHS TO FUEL LOAD	21	20	19	18	17	16	15	14	13	12	11	10	9	8	7	6	5	4	3	2	1	-
WOLF CREEK —	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT
CALLAWAY - - -	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY



KANSAS GAS AND ELECTRIC COMPANY

GLENN L. KOESTER
VICE PRESIDENT - NUCLEAR

June 19, 1984

Mr. Harold R. Denton, Director
Office of Nuclear Reactor Regulation
U.S. Nuclear Regulatory Commission
Washington, D.C. 20555

KMLNRC 84-093
Re: Docket No. STN 50-482
Subj: Wolf Creek Schedule

Dear Mr. Denton:

This letter is to inform the NRC of a revised construction completion/
fuel load schedule and a probable schedule range for Wolf Creek Generating
Station, Unit No. 1 (WCGS).

KG&E now projects fuel load for WCGS is probable in the November 1-
December 31, 1984 time frame. Current plant schedules indicate that
the plant could be ready for fuel load November 1, 1984. KG&E predicts
this probable range for WCGS fuel load of the November 1-December 31,
1984 time frame, when considering contingencies for presently unknown
factors.

The Wolf Creek Project Milestone Schedule is currently being updated
consistent with the November 1, 1984 schedule and will be forwarded
to the NRC within a week. This schedule will be updated twice monthly
and forwarded to the NRC as requested.

Yours very truly,

GLK:cks

cc: JTCollins, Region IV
PO'Connor
HBundy

~~8406250258 840619~~
PDR ADOCK 05000482
A PDR

Boo!
1/1

Meeting Summary Distribution

JUL 26 1984

Docket File

NRC PDR
Local PDR
PRC System
NSIC
LB #1 Reading File
OELD
Project Manager P. O'Connor
M. Rushbrook
R. Hartfield*
OPA*

NRC PARTICIPANTS:

B. J. Youngblood
P. O'Connor
H. Bundy
J. Neisler
J. Konklin
E. Johnson
R. Hartfield

OTHERS

bcc: Applicant & Service List

*Caseload Forecast Panel Visits
