

PHILADELPHIA ELECTRIC COMPANY

2301 MARKET STREET
P.O. BOX 8699
PHILADELPHIA, PA. 19101

C. A. McNEILL, JR.
EXECUTIVE VICE PRESIDENT - NUCLEAR

(215) 841-5352

May 5, 1988
Docket Nos. 50-277
50-278

Mr. William T. Russell
Administrator, Region I
U. S. Nuclear Regulatory Commission
Washington, DC 20555

Attention: Document Control Desk

Reference: Letter from J. F. Paquette, Jr., to W. T. Russell dated
April 8, 1988

Dear Mr. Russell:

On April 8, 1988 when we transmitted Sections I and II of the Plan for Restart of Peach Bottom Atomic Power Station, Revision I, as well as a schedule of the major activities in the revised Plan, we indicated that we would update our schedule monthly to enable PE and the NRC to monitor progress.

Enclosed are fifteen (15) copies of our first monthly schedule update. The solid line below each activity in the bar schedule is the original April 8, 1988 baseline schedule duration. The rectangular bar above the solid line represents the current forecast duration for each activity. The dark line within the rectangular bar represents current progress as of April 29, 1988.

As of April 29, 1988 we have actually completed 69 of the 138 total activities in Sections I and II of the Plan.

If you or your staff have any questions about our Restart Plan or schedule, please do not hesitate to contact me.

Sincerely,



cc: Addressee
R. E. Martin, Project Manager (5 copies)
T. P. Johnson, Resident Inspector

8805120179 880505
PDR ADOCK 05000277
R DCD

IE26
11

1987	OCT	NOV	DEC	JAN	FEB	MAR	APR	MAY	JUN	JUL	AUG	SEP	OCT	NOV	DEC	1988	JAN	FEB	MAR
------	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	-----	------	-----	-----	-----

PEACH BOTTOM RESTART PLAN EXECUTIVE SUMMARY

ISSUE SECTION I PEACH BOTTOM RESTART PLAN-CDMP

COMPLETE SECTION I CORRECTIVE ACTIONS

ISSUE SECTION II PEACH BOTTOM RESTART PLAN-SITE

COMPLETE SECTION II CORRECTIVE ACTIONS

QA SECTION I & II CLOSURE VERIFICATION

ISSUE SECTION I & II PBAPS RESTART PLAN REVISION

COMPLETE UNIT 2 CORRECTIVE MAINTENANCE

COMPLETE UNIT 2 PREVENTIVE MAINTENANCE

COMPLETE UNIT 2 MODIFICATIONS

COMPLETE SELF ASSESSMENT

PBAPS RESTART READINESS INSPECTION

PBAPS RESTART READINESS ASSESSMENT

UNIT 2 MODE SWITCH TO START-UP

UNIT 2 START-UP TO FULL POWER

REVISIONS BY DATE

INITIALS

DATE

PHILADELPHIA ELECTRIC CO.

PEACH BOTTOM RESTART PLAN - APR 89
EXECUTIVE SUMMARY SCHEDULE

Sheet 1 of 1

PEACH BOTTOM RESTART PLAN - SECTION II

Data Date: 2/28/89
Plot Date: 3/1/89


DATE	REVISION	DESCRIPTION

PEACH BOTTOM RESTART PLAN - APR 88

SECTION I

TASK COMPLETION CURVE

TASKS (EA)

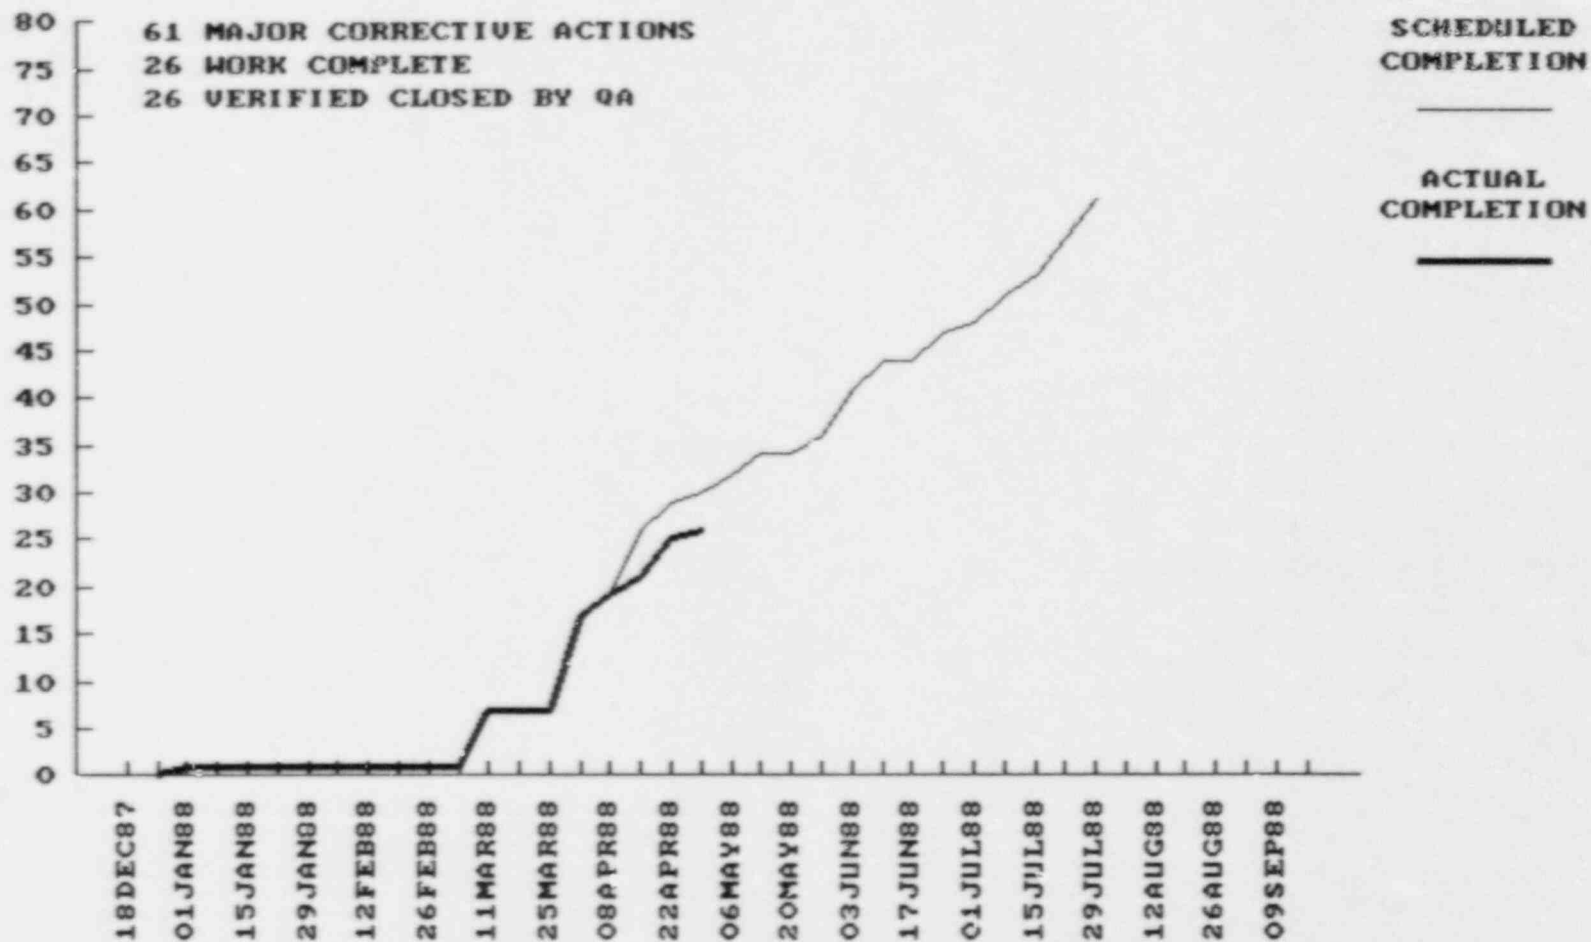


STATUS AS OF 29APR88
SECI

PEACH BOTTOM RESTART PLAN - APR 88


SECTION II

TASK COMPLETION CURVE

TASKS (EA)

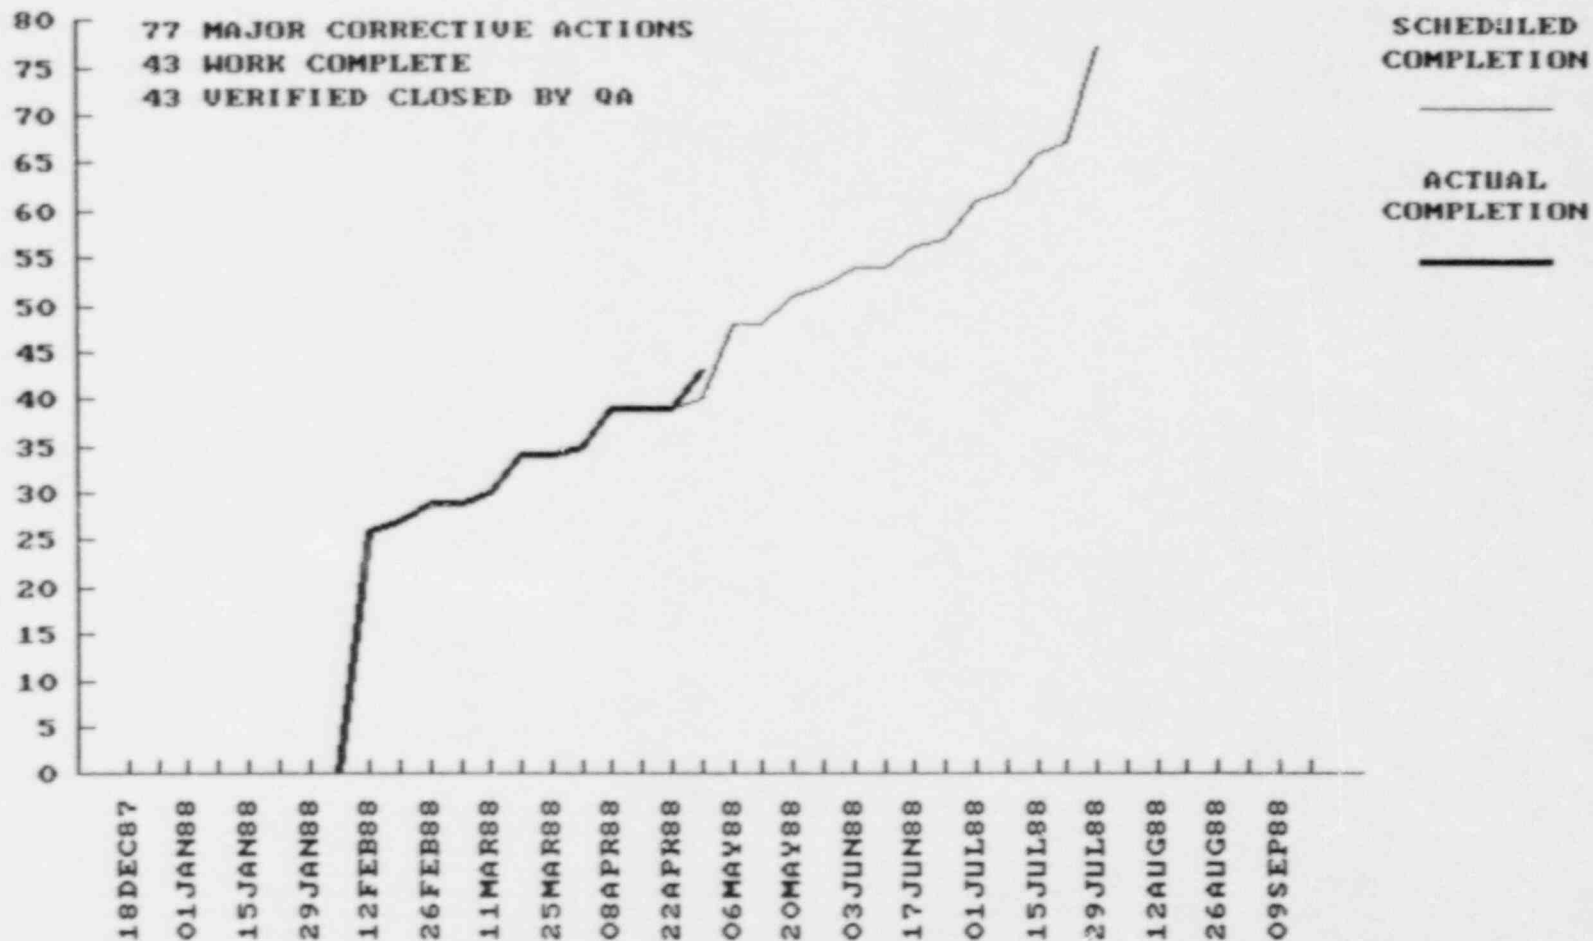

STATUS AS OF 29APR88
SECI I

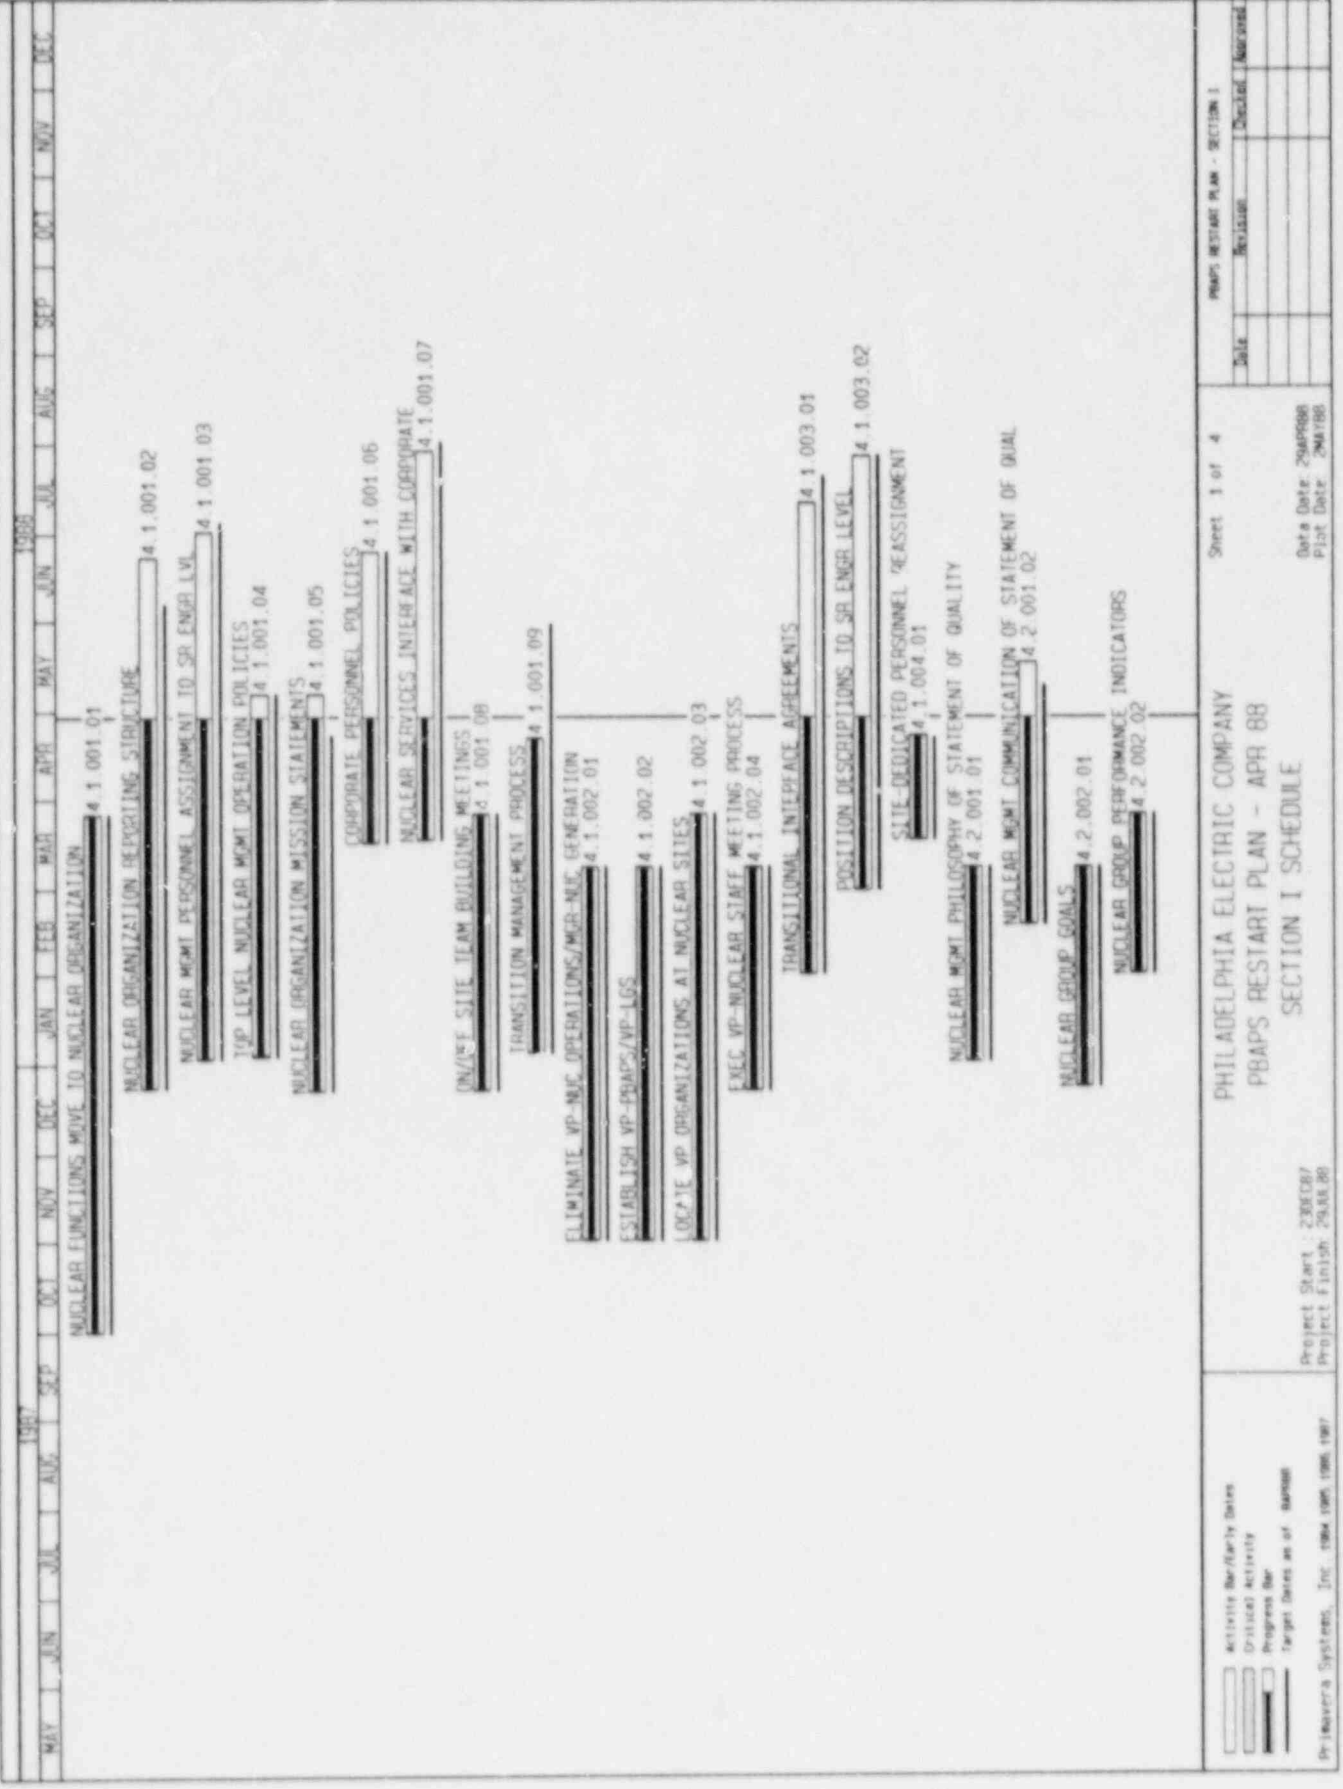

PHILADELPHIA ELECTRIC COMPANY
 PBAPS RESTART PLAN - APR 88
 SECTION I SCHEDULE

Project Start: 2/08/87
 Project Finish: 2/03/89

Sheet 1 of 4


Date: 2/04/88
 Revision: _____
 Checked: _____
 Approved: _____

Date: 2/04/88
 Plot Date: 2/04/88

Activity Bar (Early Date)
 Critical Activity
 Progress Bar
 Target Dates as of 2/04/88

Beaver Systems, Inc. (Rev. 08/1986)

MAY JUN JUL AUG SEP OCT NOV DEC JAN FEB MAR APR MAY JUN JUL AUG SEP OCT NOV DEC 1988

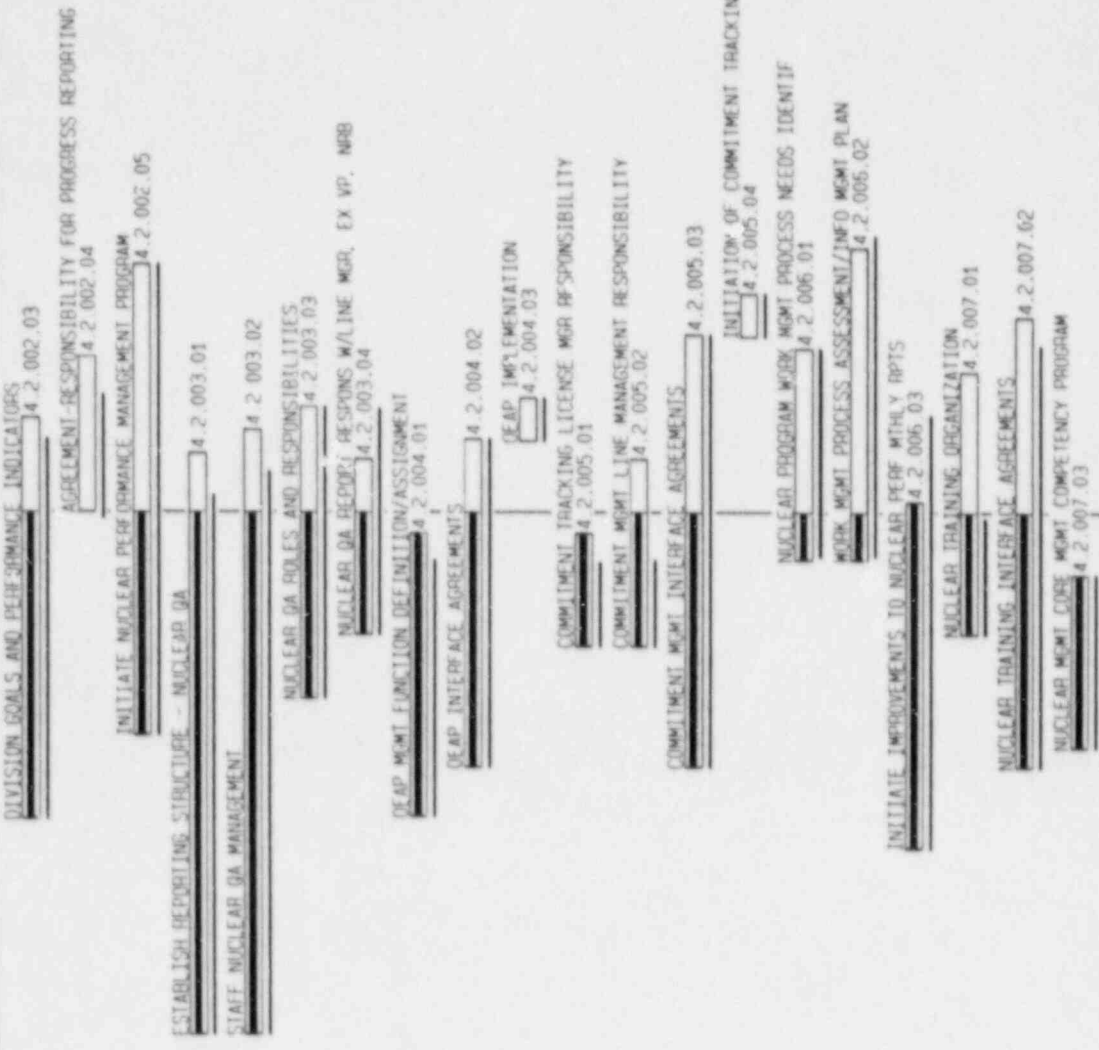

PHILADELPHIA ELECTRIC COMPANY
 PBAPS RESTART PLAN - APR 88
 SECTION I SCHEDULE

Project Start: 28FEB87
 Project Finish: 23DEC88

Sheet 2 of 4


PHAPS RESTART PLAN - SECTION 1

Date	Revision	Checked	Approved

Data Date: 29APR88
 Plot Date: 29APR88

Activity Bar/Bar/Bar Dates
 Critical Activity
 Progress Bar
 Target Dates as of baseline

Philadelphia Systems, Inc. 1984 1985 1986 1987

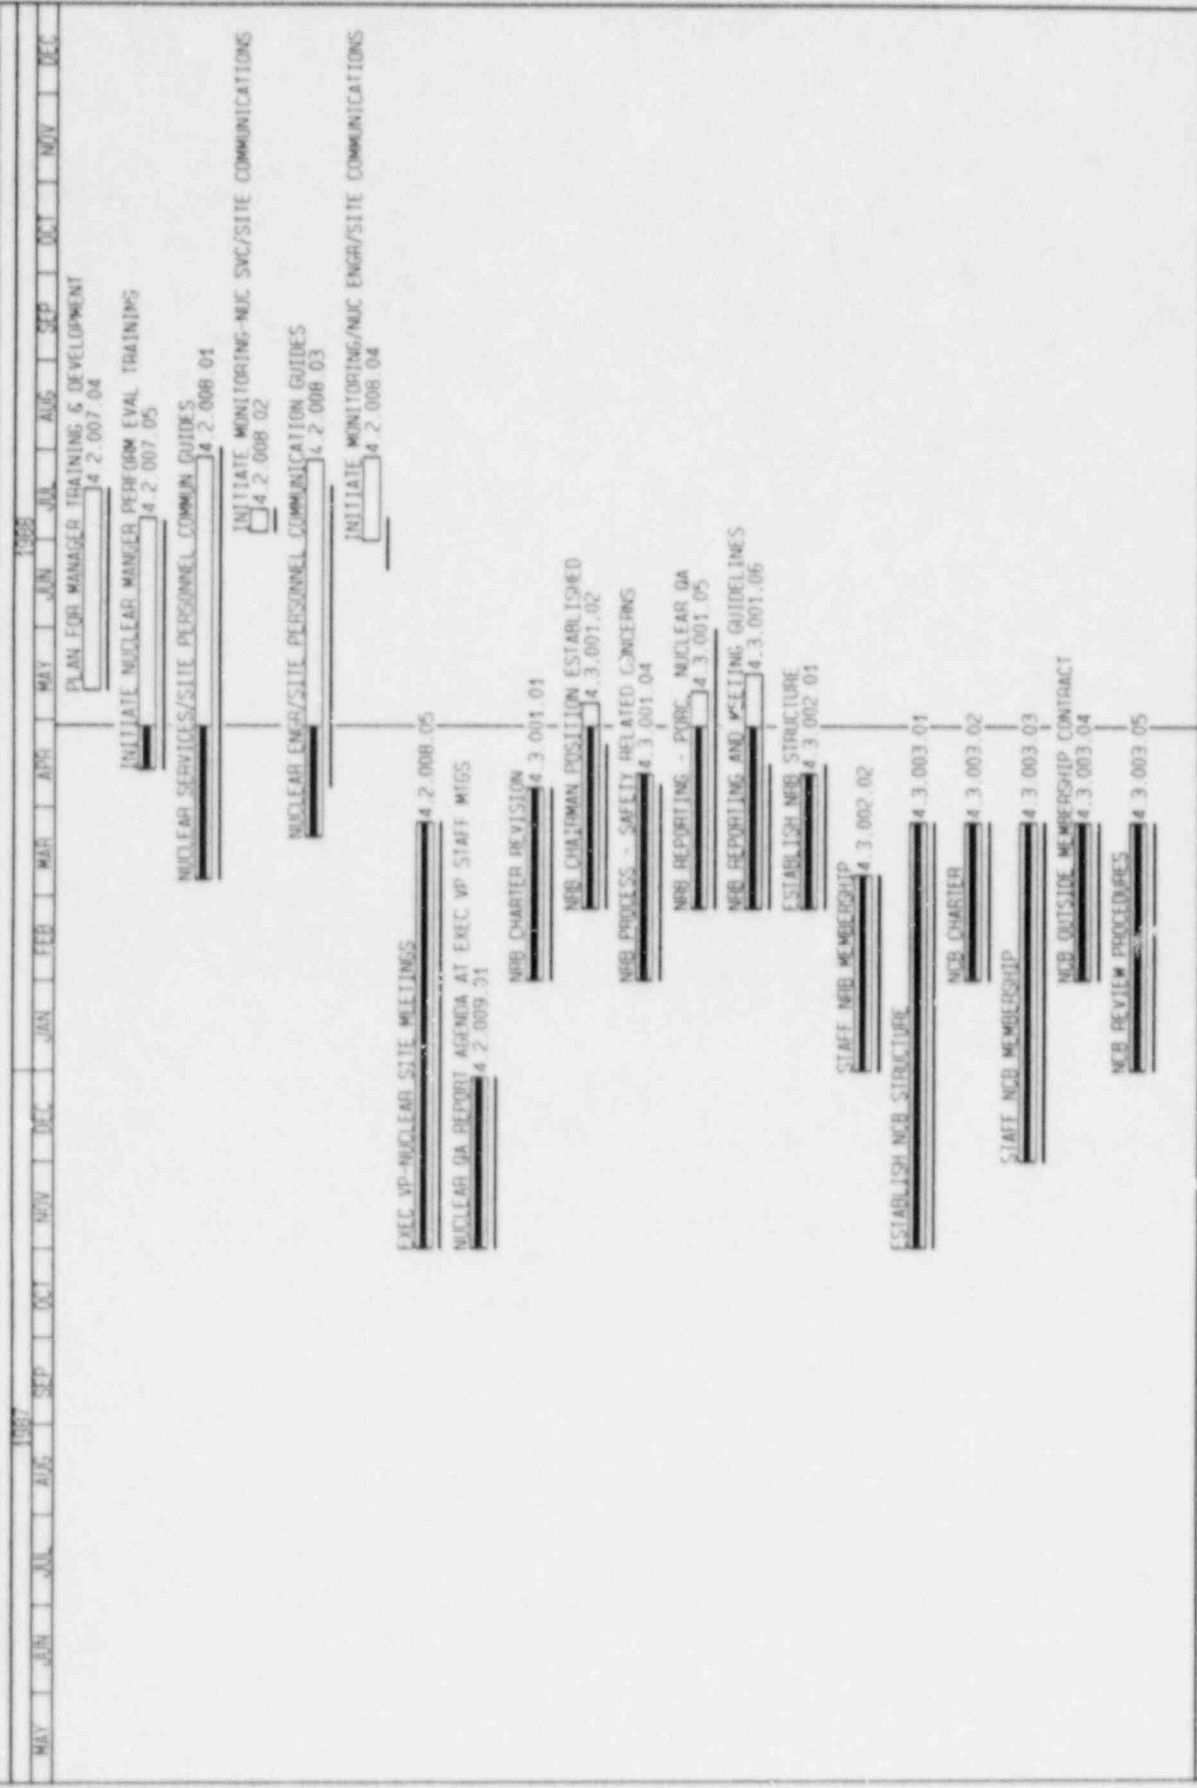

PHILADELPHIA ELECTRIC COMPANY
PBAPS RESTART PLAN - APR 88
SECTION I SCHEDULE

Project Start: 2/28/87
Project Finish: 2/28/88


Sheet 3 of 4

Data Date: 2/28/88
Plot Date: 2/28/88

PBAPS RESTART PLAN - SECTION I	
Date	Decision

Activity Bar/Bar's Dates
 Critical Activity
 Program Bar
 Target Dates as of status

Philadelphia Systems, Inc. 1984-1985, 1986, 1987

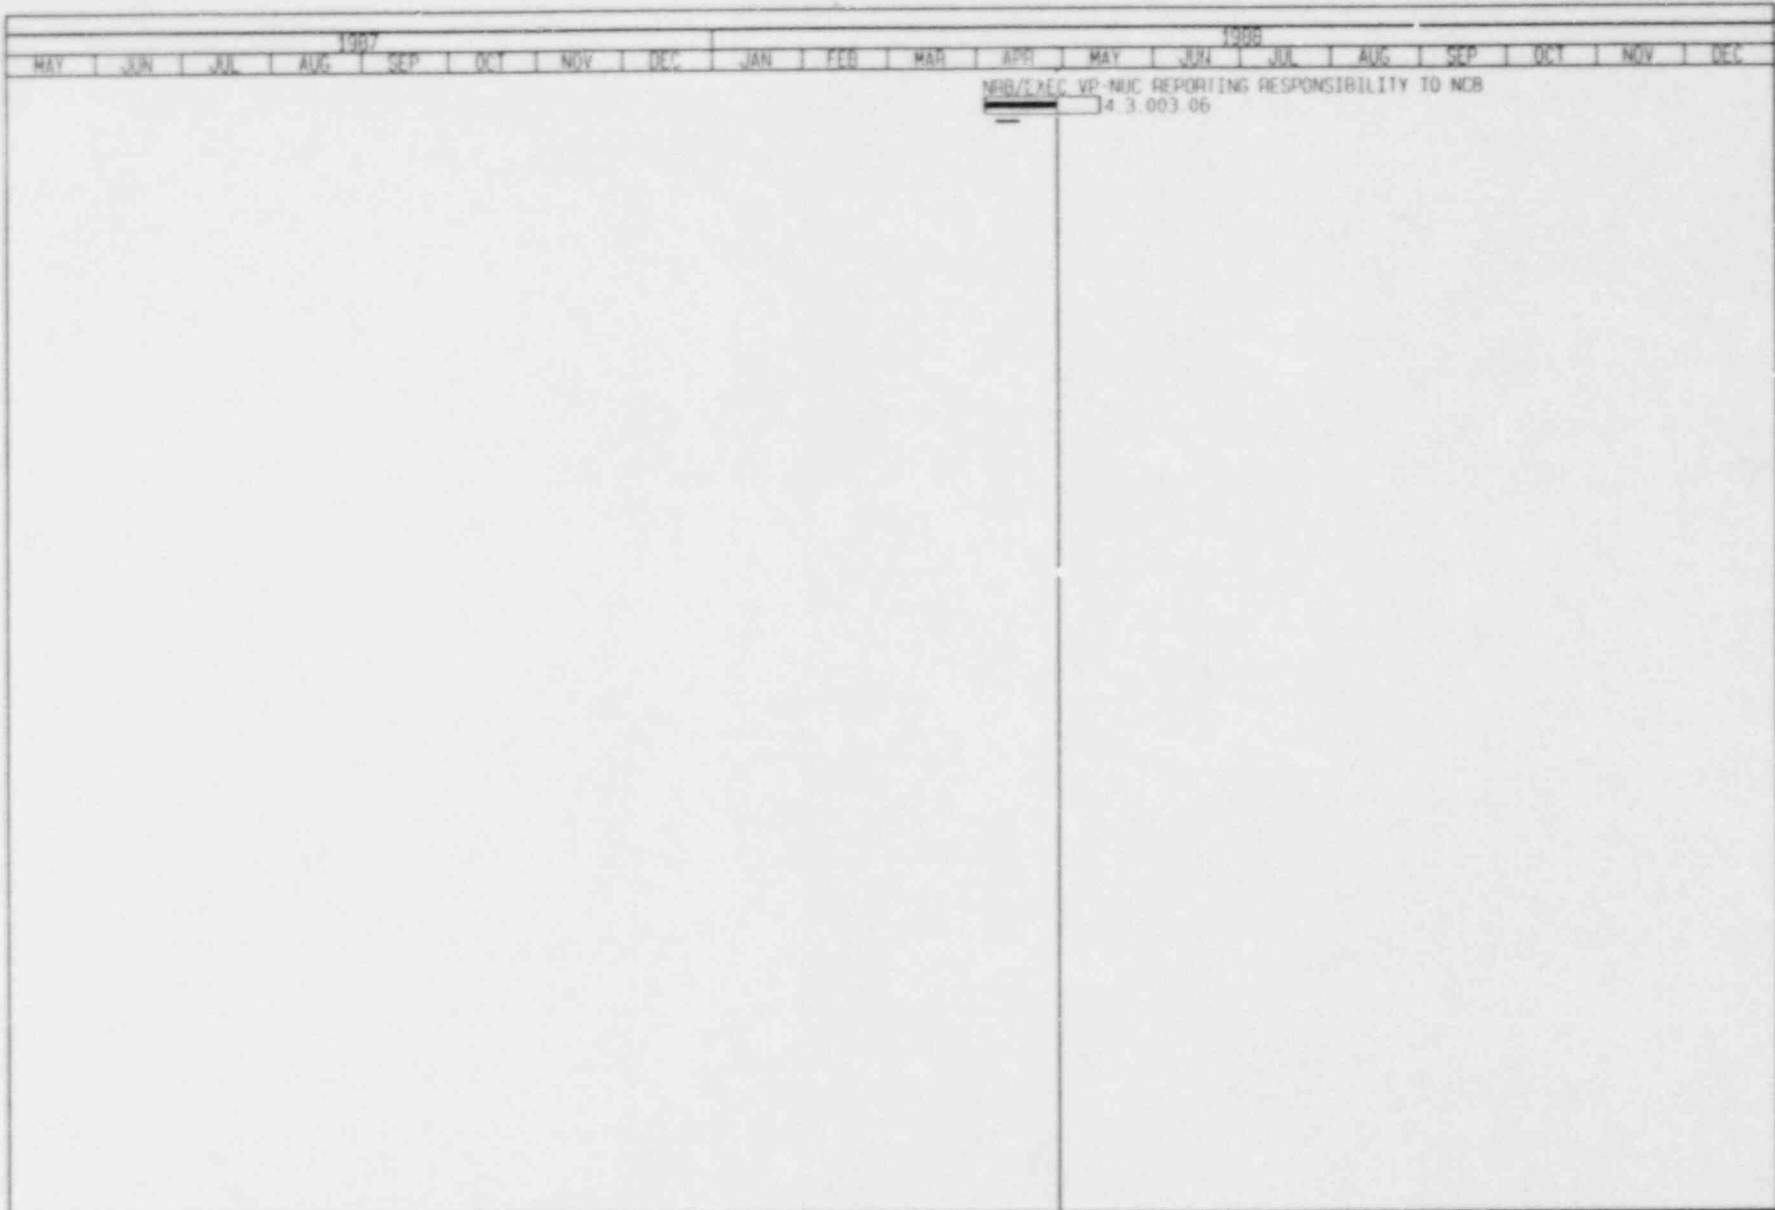


[] Activity Bar/Early Dates
 [] Critical Activity
 [] Progress Bar
 [] Target Dates as of 04/1988
 Primavera Systems, Inc. 1984, 1985, 1986, 1987

PHILADELPHIA ELECTRIC COMPANY
 PBAPS RESTART PLAN - APR 88
 SECTION I SCHEDULE

Project Start: 23DEC87
 Project Finish: 29AUG88

Sheet 4 of 4
 Date: 29APR88
 Plot Date: 2MAY88

PBAPS RESTART PLAN - SECTION I			
Date	Revision	Checked	Approved

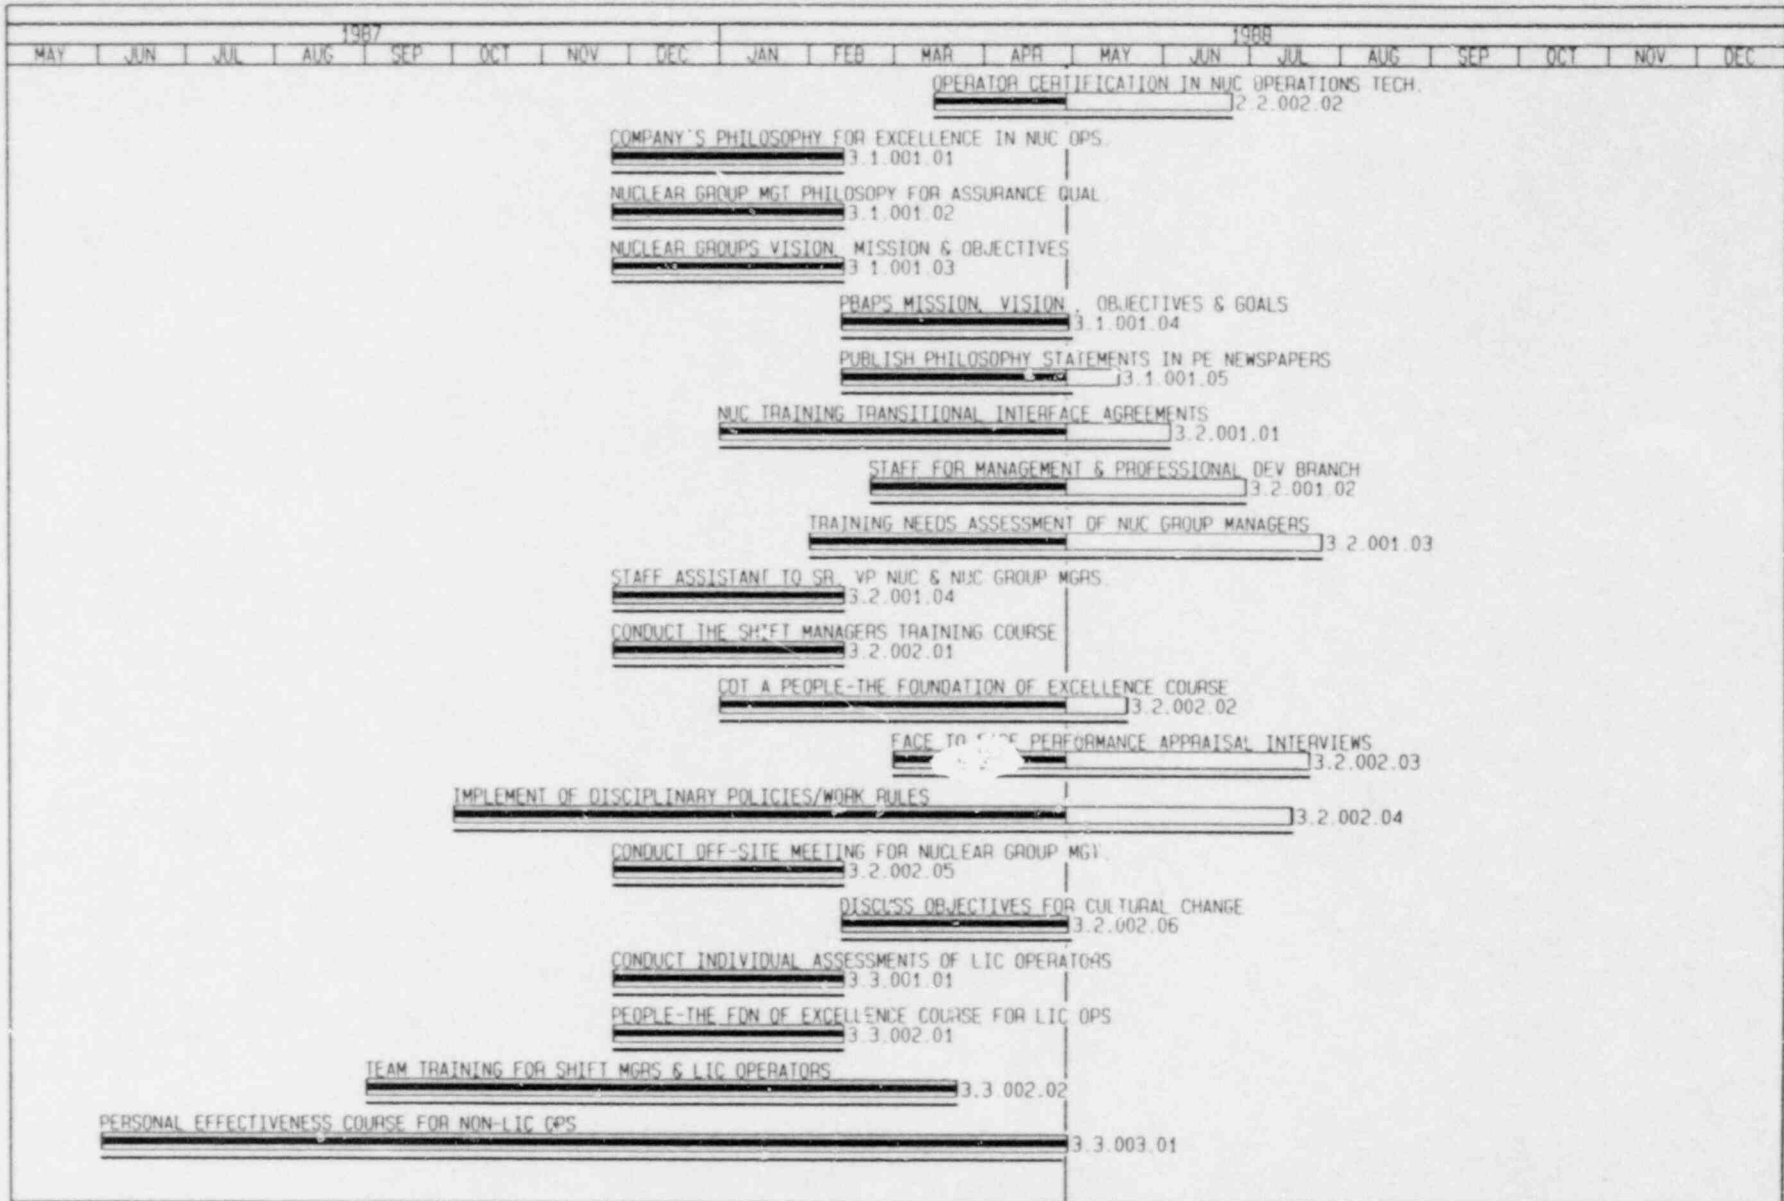


Activity Bar/Early Dates
 Critical Activity
 Progress Bar
 Target Dates as of 8APR88
 Primavera Systems, Inc. 1984 1985 1986 1987

PHILADELPHIA ELECTRIC CO.
 PEACH BOTTOM RESTART PLAN - APR 88
 SECTION II SCHEDULE

Project Start: 18MAY87
 Project Finish: 9DEC88*

Sheet 2 of 4
 Data Date: 29APR88
 Plot Date: 1MAY88

PEACH BOTTOM RESTART PLAN - SECTION II			
Date	Revision	Checked	Approved

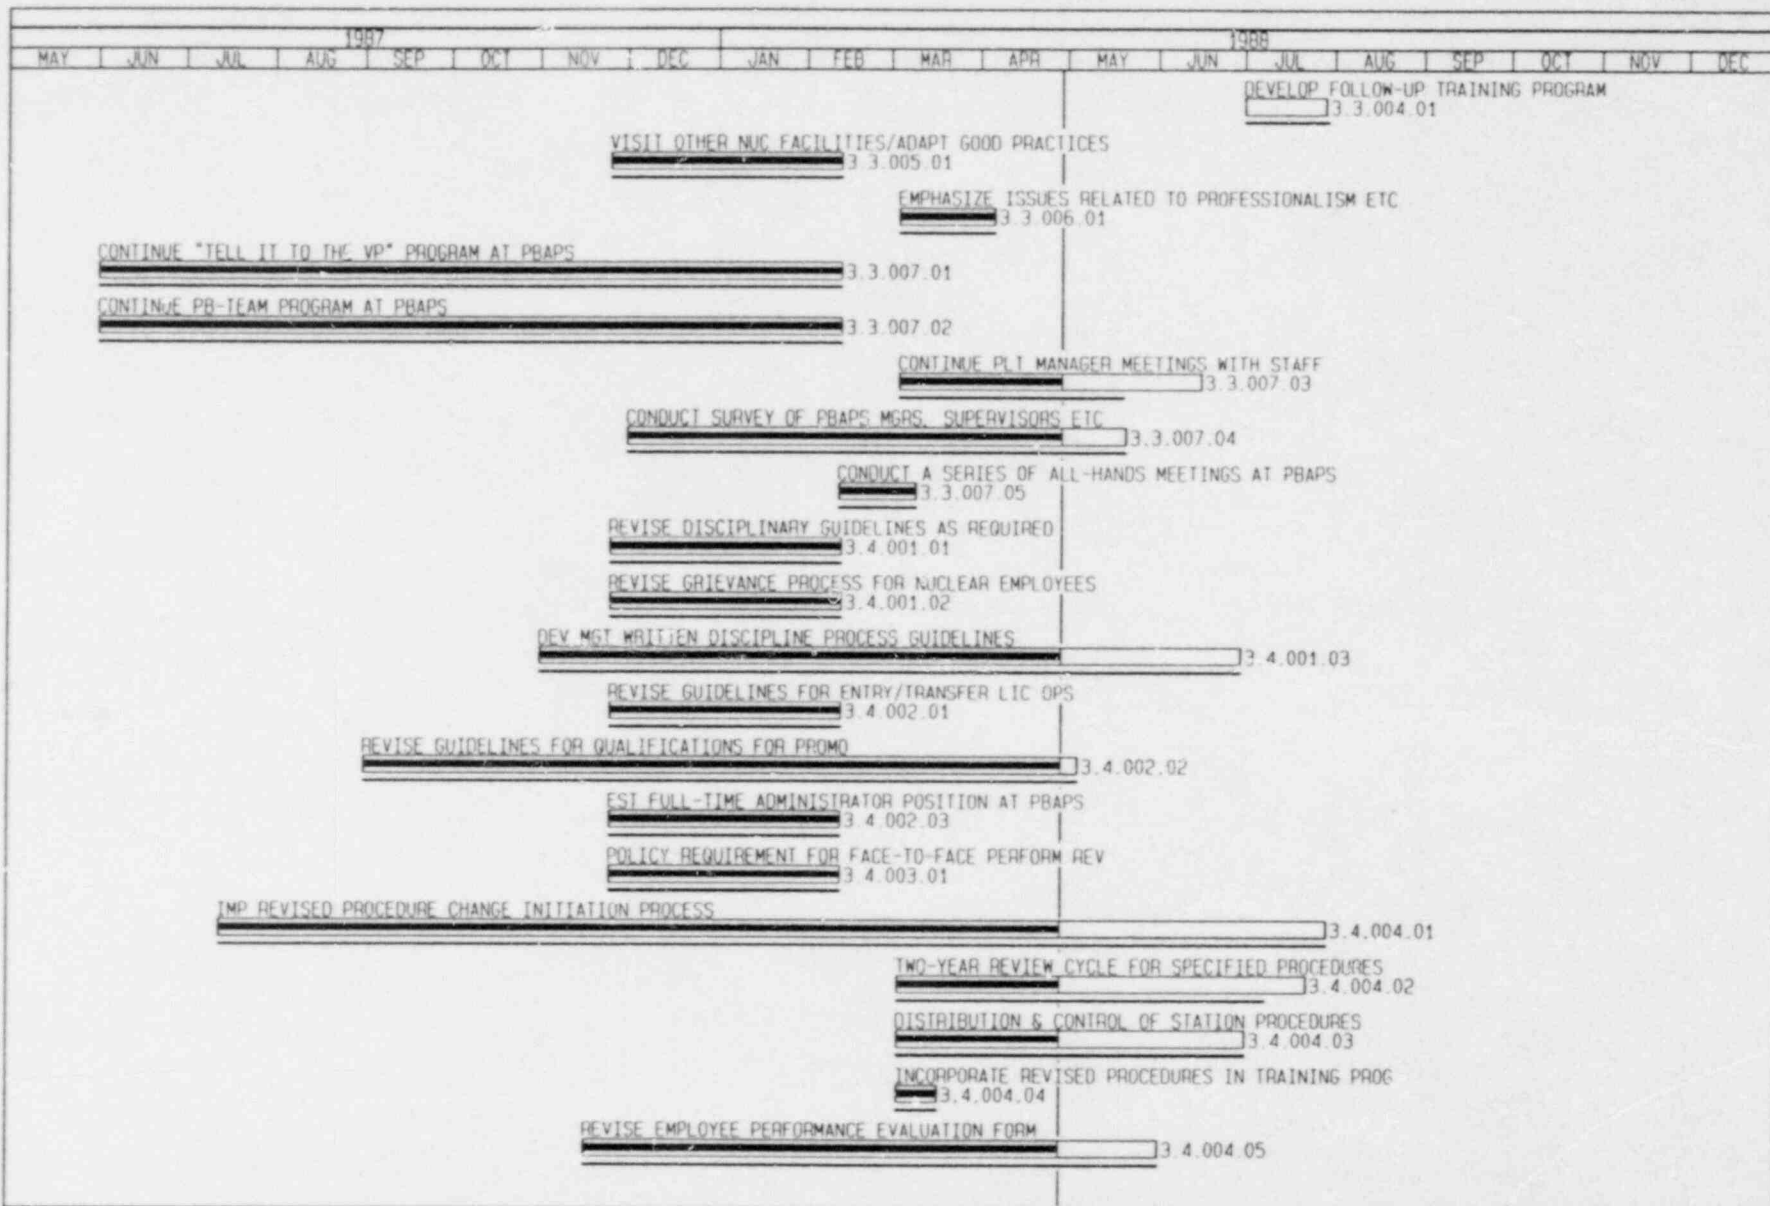

Activity Bar/Early Dates
 Critical Activity
 Progress Bar
 Target Dates as of 04P988


Primavera Systems, Inc. 1984 1985 1986 1987

PHILADELPHIA ELECTRIC CO.
 PEACH BOTTOM RESTART PLAN - APR 88
 SECTION II SCHEDULE

Project Start: 10MAY87
 Project Finish: 90EC88*

Sheet 3 of 4
 Date Date: 29APR88
 Plot Date: 1MAY88

PEACH BOTTOM RESTART PLAN - SECTION II			
Date	Revision	Checked	Approved

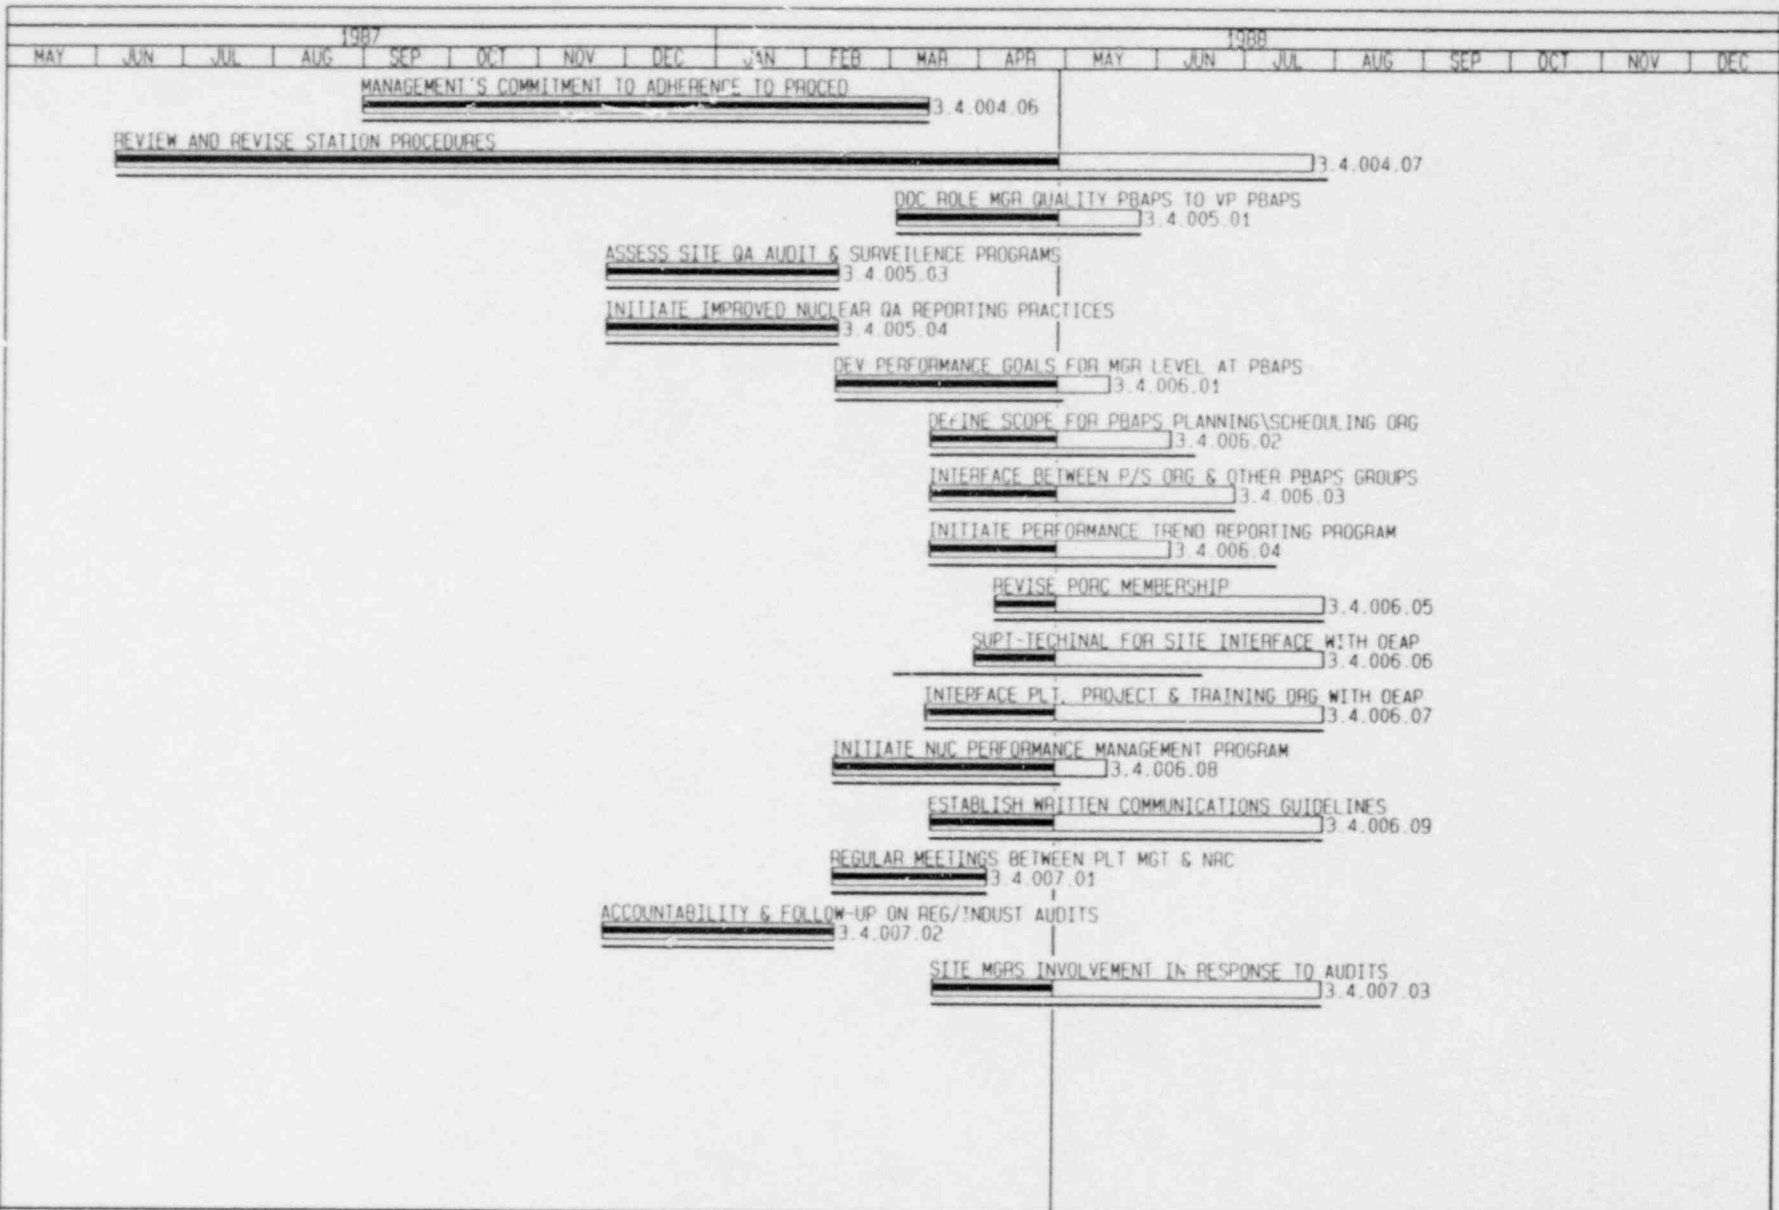

[] Activity Bar/Early Dates
 [] Critical Activity
 [] Progress Bar
 [] Target Dates as of 8/4/88
 Primavera Systems, Inc. 1984 1985 1986 1987

PHILADELPHIA ELECTRIC CO.
 PEACH BOTTOM RESTART PLAN - APR 88
 SECTION II SCHEDULE

Project Start: 18MAY87
 Project Finish: 90EC88*

Sheet 4 of 4
 Data Date: 29APR88
 Plot Date: 1MAY88

PEACH BOTTOM RESTART PLAN - SECTION II			
Date	Revision	Checked	Approved
