



Tennessee Valley Authority, Post Office Box 2000, Soddy-Daisy, Tennessee 37379

August 7, 1997

U.S. Nuclear Regulatory Commission
ATTN: Document Control Desk
Washington, D.C. 20555

Gentlemen:


In the Matter of) Docket Nos. 50-327
Tennessee Valley Authority)

SEQUOYAH NUCLEAR PLANT (SQN) - UNIT 1 - START-UP REPORT FOR
UNIT 1 CYCLE 9 OPERATION

In accordance with the requirements of SQN Technical Specifications 6.9.1.1, 6.9.1.2, and 6.9.1.3, the enclosure provides the Restart Physics Test Summary of plant start-up and power escalation testing following installation of Framatome Cogema Fuels Mark BW fuel assemblies. This summary report covers restart physics tests conducted during the first 16 effective full-power days between March 30, 1997, and May 31, 1997.

Please direct questions concerning this issue to me at (423) 843-7170 or J. D. Smith at (423) 843-6672. 1/1

Sincerely,


Pedro Salas
Site Licensing and Industry Affairs Manager

Ie 26

Enclosure
cc: See page 2

130073



9708140324 970807
PDR ADOCK 05000327
P PDR

U.S. Nuclear Regulatory Commission
Page 2
August 7, 1997

cc (Enclosure):

Mr. R. W. Hernan, Project Manager
Nuclear Regulatory Commission
One White Flint, North
11555 Rockville Pike
Rockville, Maryland 20852-2739


NRC Resident Inspector
Sequoyah Nuclear Plant
2600 Igou Ferry Road
Soddy-Daisy, Tennessee 37379-3624

Regional Administrator
U.S. Nuclear Regulatory Commission
Region II
61 Forsyth St., SW, Suite 23T85
Atlanta, Georgia 30303-3415

ENCLOSURE

SEQUOYAH NUCLEAR PLANT
UNIT 1 CYCLE 9
RESTART PHYSICS TEST SUMMARY

SEQUOYAH NUCLEAR PLANT

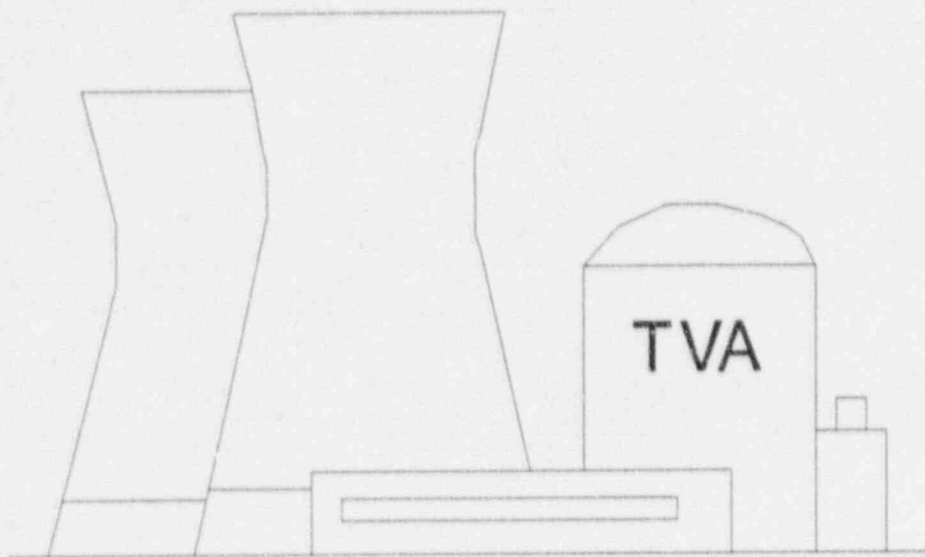

RESTART PHYSICS TEST SUMMARY

Unit 1 Cycle 9

