

Louisiana Energy Services Quarterly Management Meeting
Date: March 25, 2004

NAME	AFFILIATION	PHONE	EMAIL ADDRESS
TIM JOHNSON	NRC/FCSS	301-415-7244	TCJ@NRC.GOV
Brian Smith	NRC/FCSS	301-415-5331	BWS1@NRC.GOV
ROBERT PIERSON	NRC/NMSS/FCSS	301-415-7213	RCP@NRC.GOV
Bill Truskaski	NRC/NMSS/FCSS	301-415-8076	WMT@NRC.GOV
Melanie Wong	NRC/MSS/DWMEP	301-415-6262	MCW@NRC.GOV
MARK S. DELLIGATTI	NRC/NMSS/DWMEP	301-415-8518	MSD@NRC.GOV
Scott Flanders	NRC/NMSS/DWMEP	301-415-6717	SCF@NRC.GOV
Joseph Gritter	NRC/NMSS/FCSS	301-415-7485	JGG@NRC.GOV
Jim FERLAND	LES	505-944-0194	jferland@metnm.com
R M Krach	LES	630-657-2813	rod.krach@exeloncorp.com
MARWEST V FIDELITE	NRC/NMSS	301-415-7358	MVF@NRC.GOV
YAWAR FARAZ	NRC/NMSS/FCSS	301-415-8113	YHF@NRC.GOV
Abe Zeitoun	ATL	301-515-6770	zeitoun@atlintl.com
Robert Evans	NRC/NMSS	301-415-6084	
Don Palmrose	ATL	301-515-6769	dpalmrose@atlintl.com
Daniel Horner	McGraw-Hill	202-383-2164	daniel_horner@platts.com
Samuel Hernandez	NRC/NMSS/DWM	301-415-4049	SHQ@NRC.GOV

**Louisiana Energy Services Quarterly Management Meeting Agenda
March 25, 2004**

- I. Introduction
- II. Opening Remarks
- III. Project Status and NRC Issues
 - 1. Schedule
 - 2. Licensing Status
 - 3. Current Issues
 - 4. Resources
 - 5. Future Management Meetings
- IV. LES Issues
- V. Public Comments and Questions
- VI. Closing

LES REVIEW SCHEDULE


C = complete

DATE	ACTION
3/19/02 C	(NMSS) LES begins pre-application discussions
12/15/03 C	(NMSS) LES submits gas centrifuge facility application
12/15/03 C	(NMSS) LES submits Environmental Report
1/22/04 C	(NMSS) NRC completes acceptance review of application
2/4/04 C	(NMSS) NRC issues notice of intent (NOI) for EIS scoping meetings
2/6/04 C	(NMSS) NRC issues Notice of Opportunity for Public Hearing
3/4/04 C	(NMSS) Conduct EIS scoping meetings
4/30/04	(NMSS) Issue RAI for application (allow 30 days to respond)
4/30/04	(NMSS) Issue EIS scoping summary report
5/7/04	(NMSS) Complete technical review of Environmental Report/issue RAI
5/28/04	(NMSS) LES responds to application RAI
5/28/04	(NMSS) LES responds to Environmental Report RAI
9/30/04	(NMSS) Issue draft EIS for public comment
10/29/04	(NMSS) Conduct EIS public meetings
11/15/04	(NMSS) EIS public comment period ends
6/15/05	(NMSS) Issue final EIS
6/15/05	(NMSS) Issue final SER
7/15/05	(ASLB) Public hearing begins
2/11/06	(ASLB) ASLB issues initial decision
6/15/06	(COMM) Commission issues final decision
7/15/06	(NMSS) LES begins construction of facility
7/15/08	(NMSS) LES completes construction of facility
8/15/08	(REG II) Complete inspection of facility construction
10/15/08	(NMSS) Issue FR notice on construction inspection results
11/30/08	(NMSS) LES begins facility operation

Louisiana Energy Services Management Meeting With NRC

Rockville, MD
March 25, 2004

Organization Chart

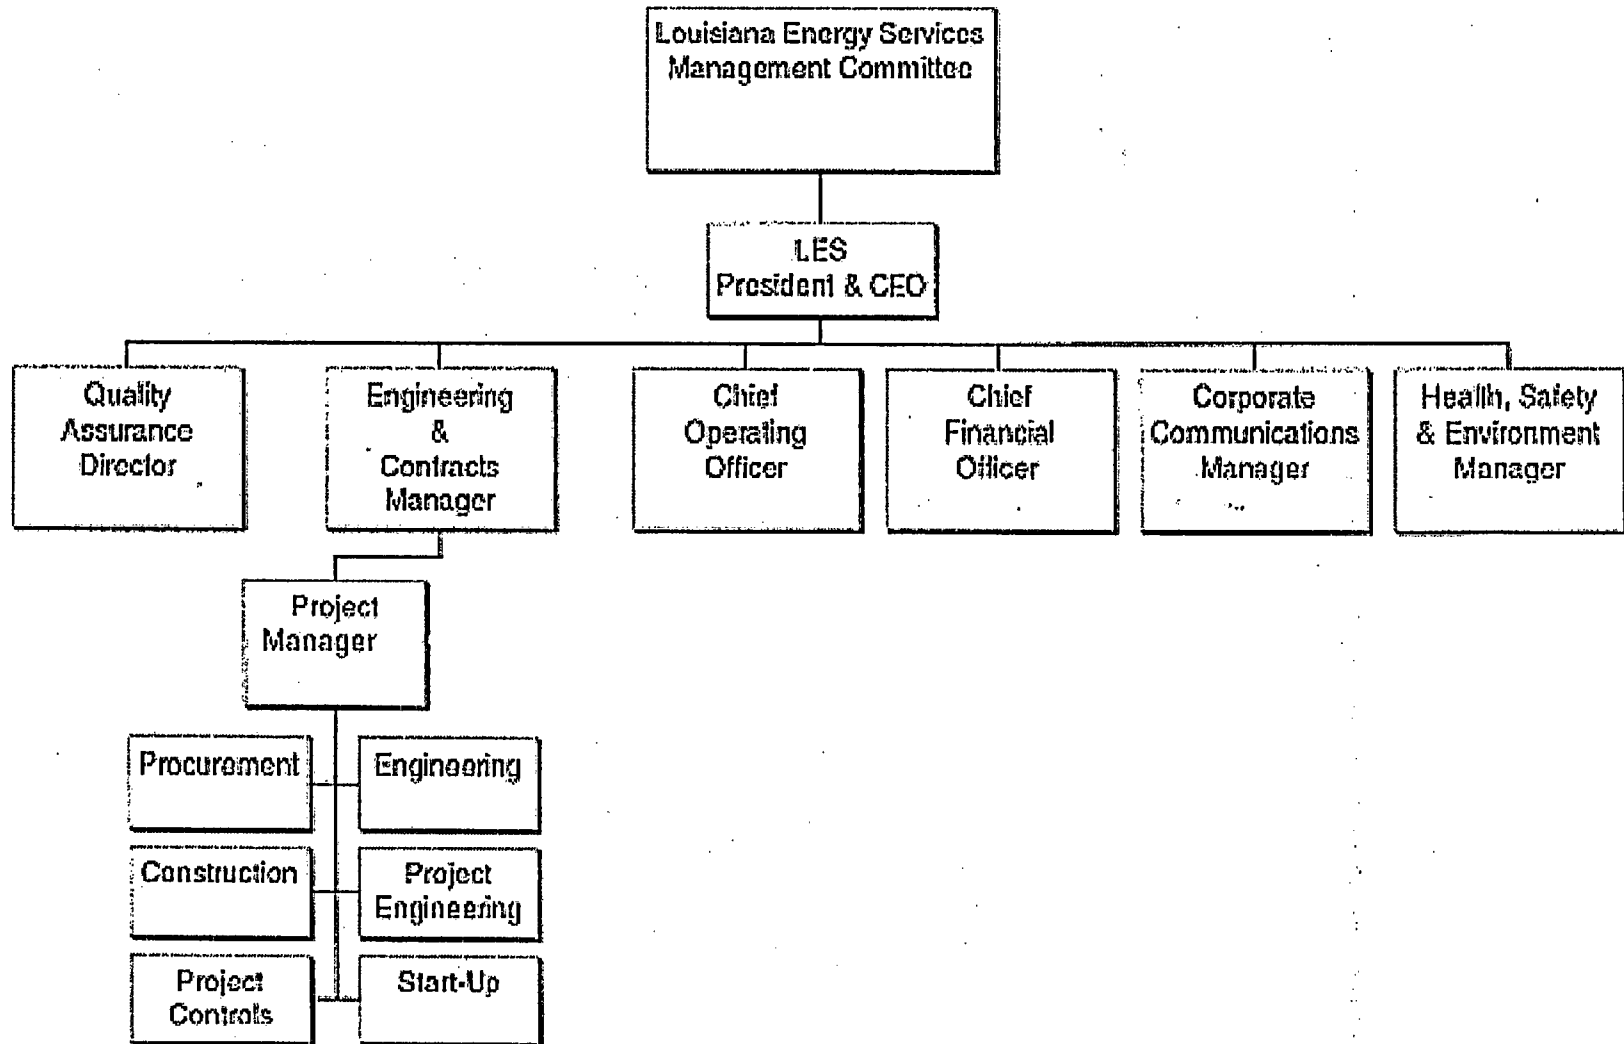

Organization

- Functional Responsibilities
 - President and Chief Executive Officer – Jim Ferland
 - Quality Assurance Director, Engineering and Contracts, and Health, Safety & Environment Managers – Rod Krich (VP – Licensing, Safety, and Nuclear Engineering)
 - Chief Financial Officer – Mat Lueras (Controller)
 - Corporate Communications Manager – Marshall Cohen (VP – Communications and Government Relations)
 - Project Manager – Mike Lynch (Urenco)

Capabilities

- Contracts with large consultant firms and specialty contractors
 - Areva (Formerly Framatome – ANP)
 - Energy Resources, Inc.
 - Local environmental firm
- Urenco's Enrichment Technology Company, Ltd. is interface to the entire Urenco organization
- Utility partners have made assistance available

Responses to Requests for Additional Information (RAI)



- Expected to start receiving safety RAI in April and environmental in May
- Will respond to safety RAI within 30 calendar days
- Will respond to environmental RAI within 15 business days
- Will notify the NRC promptly in writing if technical or other issues prevent us from meeting response commitments

Management Oversight

- Propose quarterly meetings or as necessary

- Purpose
 - Status of NRC review and LES responses
 - Identify and resolve obstacles to progress
 - Agree on focus areas

Feedback

- Good cooperation
- Good communications
- Excellent progress
 - Integrated Safety Analysis (ISA) meeting
 - On-site review of ISA documentation
 - Visit to the Almelo facility
 - Numerous teleconferences to obtain needed clarification
- Tracking responses to all verbal requests
