
Lesiocuf, Lemb, Leiby & MacRae Machington, D. C. (Same)	LTR. MEMO:		19 ₈ 1969	NO.: S4	<u> </u>
To:	ORIG.: CC:	C	THER:		
Dr. Peter A. Morris		CONCURRENCE		DATE ANSWERED:	
CLASSIF.: POST OFFICE REG. NO:	50-220 (Inp		prepared		
Ltr trans the following on behalf of the applicant:	referred to Tedesco	- ,755		EIVED BY	DAT
PETITION REQUESTING EXTENSION OF COMPLETION DATE specified in CPPR-16 be extended to Sept 1, 1969 due to certain const. delays making it impossible to meet prior schedule	H. Pr Morri Boyd Skovh		aff		
(3 Notarized & 19 conf'd cys)	Dube Kelly	orpson			-
DISTRIBUTION: 1-reg file 1-AEC PDR 2-Compliance [AGI]				542	

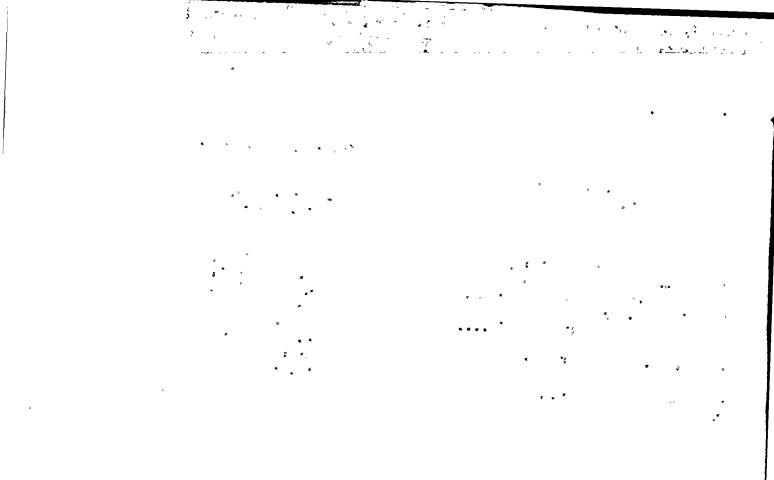

LAW OFFICES OF

LEBOEUF, LAMB, LEIBY & MACRAE 1821 JEFFERSON PLACE, N.W. WASHINGTON, D. C. 20036

ARVIN E. UPTON
EUGENE B. THOMAS, JR.
LEONARD M. TROSTEN
WASHINGTON PARTNERS

March 19, 1969

ONE CHASE MANHATTAN PLAZA NEW YORK, N.Y. 10005

WASHINGTON TELEPHONE: 202 FEDERAL 8-011

Dr. Peter A. Morris Director Division of Reactor Licensing U. S. Atomic Energy Commission Washington, D. C. 20545

Regulatory

File Cy.

Re: AEC Docket No. 50-220

Dear Dr. Morris:

With this letter we transmit three originals and nineteen copies of a petition requesting extension of the completion date for the Nine Mile Point facility.


Very truly yours,

LeBOEUF, LAMB, LEIBY & MacRAE

Counsel for Niagara Mohawk Power Corporation

Enclosures





4 •• 1.54 · *

BEFORE THE UNITED STATES ATOMIC ENERGY COMMISSION

/	الآلاية	TW)	. .
117	11/372°	DOK	
	MENT S	1965 CHERGY	目
1-1	U.S. 621. VI.S. 621. M	in Section	£5/
	(%) II	1110	•

In the Matter of) Regulator Cile Cy.

Docket No. 50-220

Niagara Mohawk Power Corporation)

PETITION REQUESTING EXTENSION

OF

COMPLETION DATE

Pursuant to Section 50.55(b) of the Commission's regulations, Niagara Mohawk Power Corporation, Applicant in the above-captioned proceeding, hereby requests that the latest completion date for its Nine Mile Point facility specified in Provisional Construction Permit No. CPPR-16 (as previously extended by an order of the Commission dated August 15, 1968) be extended to September 1, 1969. The reason for this request is that Licensee has experienced



Service Control of the Control of th

certain construction delays which make it impossible for it to meet its present completion date of May 1, 1969.

NIAGARA MOHAWK POWER CORPORATION

Dated: March /2 , 1969

____///////_____

Vice President & Executive Engineer

Subscribed and sworn to before me this 17th day of Warch, 1969.

Notary Public

Mx Commission Expires

1arch 30, 1969

JULIA SCHLOSSER
Notary Public In the State of New York
Qualified in Onen. Co. No. 34-3504850
My Commission Expires March 30, 19

v 09

.
