

**The Light
company**

Houston Lighting & Power P.O. Box 1700 Houston, Texas 77001 (713) 228-9211

January 15, 1981
ST-HL-AE-600
SFN: V-0110

Mr. Karl Seyfrit
Director, Region IV
Nuclear Regulatory Commission
611 Ryan Plaza Drive, Suite 1000
Arlington, Texas 76012


Dear Mr. Seyfrit:

South Texas Project
Units 1&2
Docket Nos. STN 50-498, STN 50-499
Update of Facility Status

Houston Lighting & Power Company has reviewed and updated the entries for the South Texas Project in NUREG-0030, "Construction Status Report." Submitted with this letter are those pages which require changes.

If you have any questions, please contact Mr. M. E. Powell at (713) 676-8592.

Very truly yours,


G. W. Oprea, Jr.
Executive Vice President

PLW/mmj

Attachments

8104230236

cc: Director, NRC Office of Inspection and Enforcement

Nuclear Regulatory Commission

M. D. Schwarz (Baker & Botts)

R. Gordon Gooch (Baker & Botts)

J. R. Newman (Lowenstein, Newman, Reis, Axelrad & Toll)

J. H. Goldberg

D. G. Barker

A. J. Granger

R. A. Frazar

G. B. Painter

R. L. Waldrop

H. R. Dean

Howard Pyle

POOR ORIGINAL


FACILITY STATUS SUMMARY

FACILITY NAME	UTILITY	LOCATION (COUNTY/STATE)	DOCKET NUMBER	REGION	DATE	APPLICANT'S COMMENTS	APPLICANT'S ESTIMATED FID	APPLICANT'S ESTIMATED FID	PERCENTAGE OF COMPLETION	FILE NUMBER DATE RELATE
13. DEL POWER 3	SOUTHERN CALIFORNIA ENERGY	BAR BEND/CA/92008	85000045	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
14. DELPOWER 3	PUBLIC SERVICE OF NEW HAMPSHIRE	NEW HAMPSHIRE/NEW HAMPSHIRE	85000042	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
15. DELPOWER 2	PHILIP MASTERS OF NEW HAMPSHIRE	NEW HAMPSHIRE/NEW HAMPSHIRE	85000044	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
16. DELPOWER 2	VERMONT VALLEY AUTHORITY	VERMONT/VERMONT	85000046	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
17. DELPOWER 2	SIEMENS ELECTRIC	SIEMENS/NEW YORK	85000048	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
18. DELPOWER 2	AMERICAN ELECTRIC POWER COMPANY	INDIANA/INDIANA	85000049	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
19. DELPOWER 2	AMERICAN ELECTRIC POWER COMPANY	INDIANA/INDIANA	85000048	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
20. DELPOWER 2	AMERICAN ELECTRIC POWER COMPANY	INDIANA/INDIANA	85000047	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
21. DELPOWER 2	AMERICAN ELECTRIC POWER COMPANY	INDIANA/INDIANA	85000046	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
22. DELPOWER 2	AMERICAN ELECTRIC POWER COMPANY	INDIANA/INDIANA	85000045	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
23. DELPOWER 2	AMERICAN ELECTRIC POWER COMPANY	INDIANA/INDIANA	85000044	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
24. DELPOWER 2	AMERICAN ELECTRIC POWER COMPANY	INDIANA/INDIANA	85000043	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
25. DELPOWER 2	AMERICAN ELECTRIC POWER COMPANY	INDIANA/INDIANA	85000042	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
26. DELPOWER 2	AMERICAN ELECTRIC POWER COMPANY	INDIANA/INDIANA	85000041	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
27. DELPOWER 2	AMERICAN ELECTRIC POWER COMPANY	INDIANA/INDIANA	85000040	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
28. DELPOWER 2	AMERICAN ELECTRIC POWER COMPANY	INDIANA/INDIANA	85000039	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
29. DELPOWER 2	AMERICAN ELECTRIC POWER COMPANY	INDIANA/INDIANA	85000038	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
30. DELPOWER 2	AMERICAN ELECTRIC POWER COMPANY	INDIANA/INDIANA	85000037	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
31. DELPOWER 2	AMERICAN ELECTRIC POWER COMPANY	INDIANA/INDIANA	85000036	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
32. DELPOWER 2	AMERICAN ELECTRIC POWER COMPANY	INDIANA/INDIANA	85000035	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
33. DELPOWER 2	AMERICAN ELECTRIC POWER COMPANY	INDIANA/INDIANA	85000034	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
34. DELPOWER 2	AMERICAN ELECTRIC POWER COMPANY	INDIANA/INDIANA	85000033	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
35. DELPOWER 2	AMERICAN ELECTRIC POWER COMPANY	INDIANA/INDIANA	85000032	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
36. DELPOWER 2	AMERICAN ELECTRIC POWER COMPANY	INDIANA/INDIANA	85000031	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
37. DELPOWER 2	AMERICAN ELECTRIC POWER COMPANY	INDIANA/INDIANA	85000030	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
38. DELPOWER 2	AMERICAN ELECTRIC POWER COMPANY	INDIANA/INDIANA	85000029	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
39. DELPOWER 2	AMERICAN ELECTRIC POWER COMPANY	INDIANA/INDIANA	85000028	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
40. DELPOWER 2	AMERICAN ELECTRIC POWER COMPANY	INDIANA/INDIANA	85000027	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
41. DELPOWER 2	AMERICAN ELECTRIC POWER COMPANY	INDIANA/INDIANA	85000026	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
42. DELPOWER 2	AMERICAN ELECTRIC POWER COMPANY	INDIANA/INDIANA	85000025	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
43. DELPOWER 2	AMERICAN ELECTRIC POWER COMPANY	INDIANA/INDIANA	85000024	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
44. DELPOWER 2	AMERICAN ELECTRIC POWER COMPANY	INDIANA/INDIANA	85000023	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
45. DELPOWER 2	AMERICAN ELECTRIC POWER COMPANY	INDIANA/INDIANA	85000022	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
46. DELPOWER 2	AMERICAN ELECTRIC POWER COMPANY	INDIANA/INDIANA	85000021	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
47. DELPOWER 2	AMERICAN ELECTRIC POWER COMPANY	INDIANA/INDIANA	85000020	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
48. DELPOWER 2	AMERICAN ELECTRIC POWER COMPANY	INDIANA/INDIANA	85000019	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81
49. DELPOWER 2	AMERICAN ELECTRIC POWER COMPANY	INDIANA/INDIANA	85000018	1100	05-11-81	05-11-81	05-11-81	05-11-81	0%	05-11-81

* INDICATES A CHANGE OF INFORMATION.
 * For the full text of a report, see the report.


POOR ORIGINAL

APPLICANT FUEL LOAD PROJECTIONS - PAGE 1

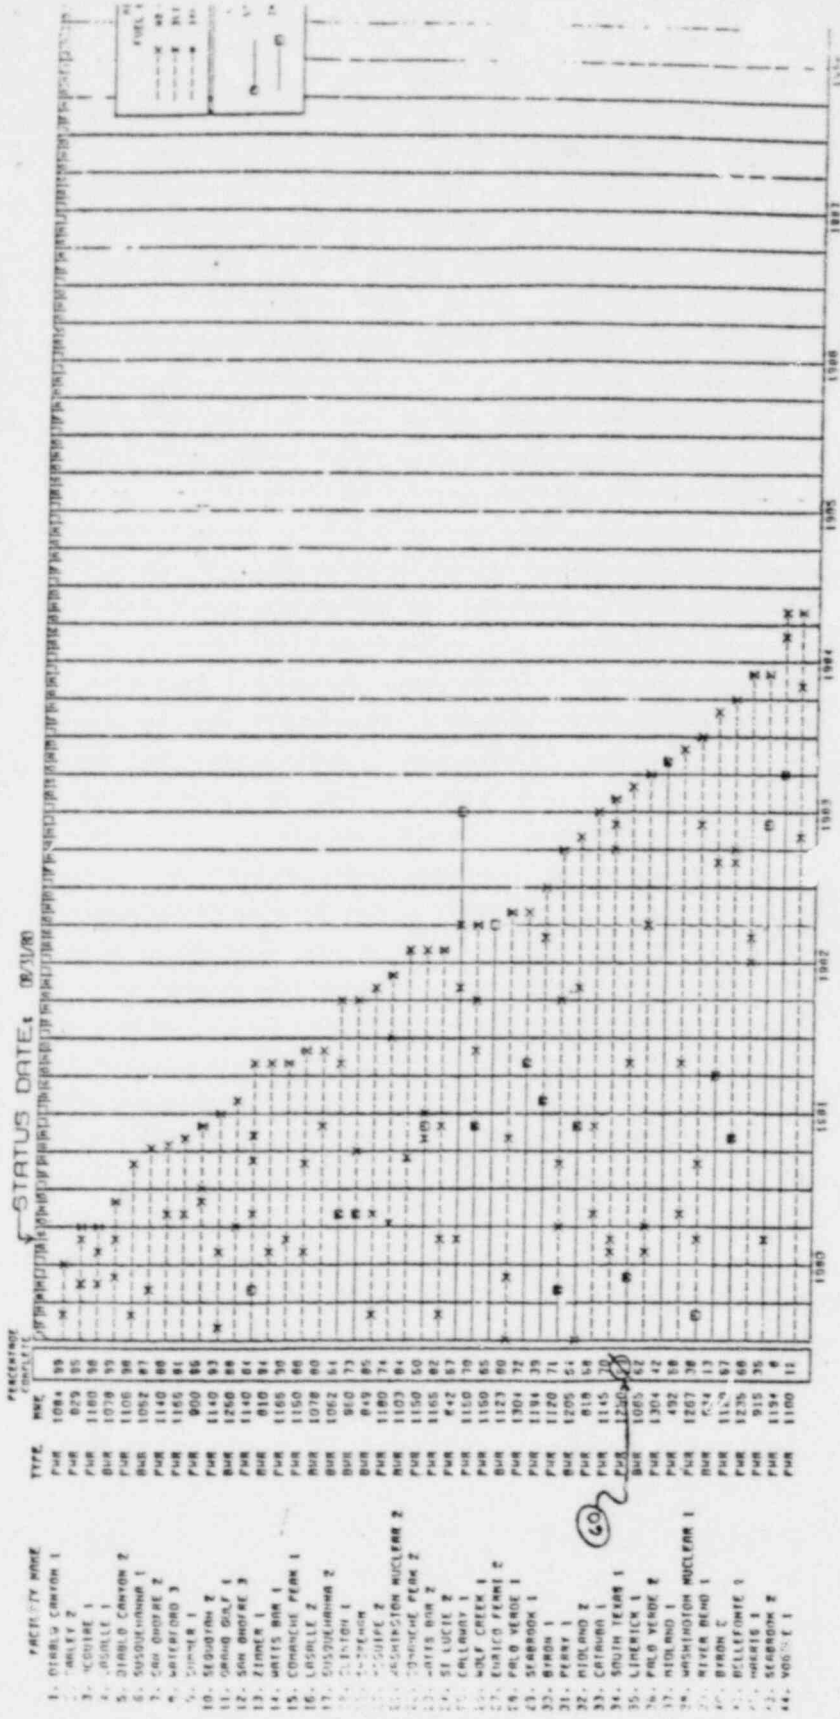


POOR ORIGINAL

APPLICANT FUEL LOAD PROJECTIONS - PAGE 2

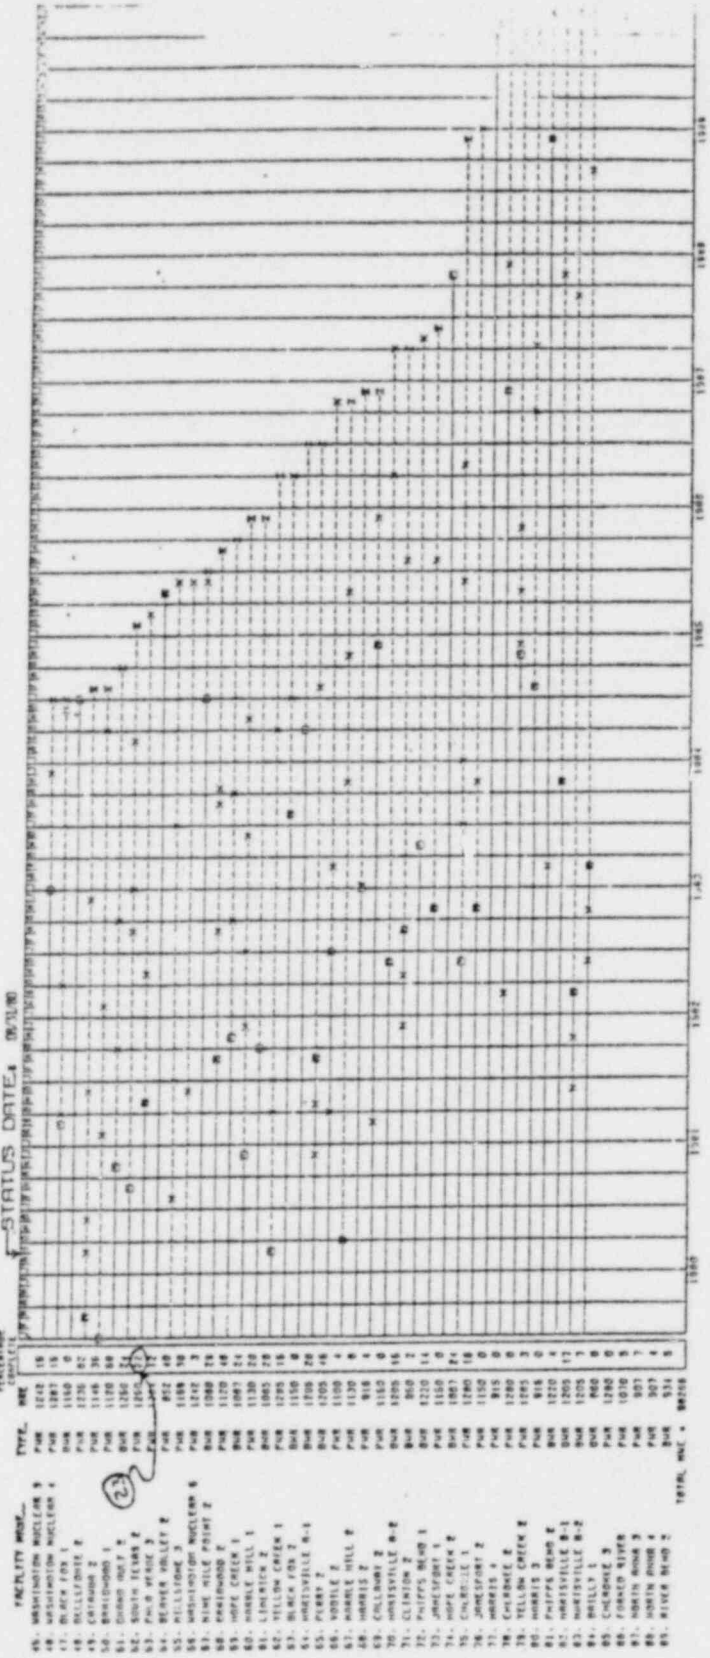

AVERAGE DURATION FOR NUCLEAR POWER PLANT CONSTRUCTION



187 - PROJECTED DURATIONS

DATE	PLANT	FIELD	PERCENT COMPLETE	PERCENT COMPLETE	PERCENT COMPLETE	PERCENT COMPLETE	PERCENT COMPLETE	PERCENT COMPLETE	PERCENT COMPLETE
05-88	02-27-86	0824	874	874	874	874	874	874	874
05-88	08-11-80	1004	874	874	874	874	874	874	874
05-88	07-00-80	1004	874	874	874	874	874	874	874
05-88	07-00-80	1004	874	874	874	874	874	874	874
05-88	07-00-80	1004	874	874	874	874	874	874	874

CALENDAR YEAR 1982 - PROJECTED DURATIONS

DATE	PLANT	FIELD	PERCENT COMPLETE	PERCENT COMPLETE	PERCENT COMPLETE	PERCENT COMPLETE	PERCENT COMPLETE	PERCENT COMPLETE	PERCENT COMPLETE
01-82	02-27-86	0824	874	874	874	874	874	874	874
01-82	08-11-80	1004	874	874	874	874	874	874	874
01-82	07-00-80	1004	874	874	874	874	874	874	874
01-82	07-00-80	1004	874	874	874	874	874	874	874

CALENDAR YEAR 1984 - PROJECTED DURATIONS

DATE	PLANT	FIELD	PERCENT COMPLETE	PERCENT COMPLETE	PERCENT COMPLETE	PERCENT COMPLETE	PERCENT COMPLETE	PERCENT COMPLETE	PERCENT COMPLETE
01-84	02-27-86	0824	874	874	874	874	874	874	874
01-84	08-11-80	1004	874	874	874	874	874	874	874
01-84	07-00-80	1004	874	874	874	874	874	874	874
01-84	07-00-80	1004	874	874	874	874	874	874	874

181 - PROJECTED DURATIONS

DATE	PLANT	FIELD	PERCENT COMPLETE	PERCENT COMPLETE	PERCENT COMPLETE	PERCENT COMPLETE	PERCENT COMPLETE	PERCENT COMPLETE	PERCENT COMPLETE
01-81	02-27-86	0824	874	874	874	874	874	874	874
01-81	08-11-80	1004	874	874	874	874	874	874	874
01-81	07-00-80	1004	874	874	874	874	874	874	874
01-81	07-00-80	1004	874	874	874	874	874	874	874

CALENDAR YEAR 1983 - PROJECTED DURATIONS

DATE	PLANT	FIELD	PERCENT COMPLETE	PERCENT COMPLETE	PERCENT COMPLETE	PERCENT COMPLETE	PERCENT COMPLETE	PERCENT COMPLETE	PERCENT COMPLETE
01-83	02-27-86	0824	874	874	874	874	874	874	874
01-83	08-11-80	1004	874	874	874	874	874	874	874
01-83	07-00-80	1004	874	874	874	874	874	874	874
01-83	07-00-80	1004	874	874	874	874	874	874	874

CALENDAR YEAR 1985 - PROJECTED DURATIONS

DATE	PLANT	FIELD	PERCENT COMPLETE	PERCENT COMPLETE	PERCENT COMPLETE	PERCENT COMPLETE	PERCENT COMPLETE	PERCENT COMPLETE	PERCENT COMPLETE
01-85	02-27-86	0824	874	874	874	874	874	874	874
01-85	08-11-80	1004	874	874	874	874	874	874	874
01-85	07-00-80	1004	874	874	874	874	874	874	874
01-85	07-00-80	1004	874	874	874	874	874	874	874

POOR ORIGINAL

STATUS

APPLICANT'S CURRENT FUEL LOADING DATE 08-83
 APPLICANT'S PREVIOUS FUEL LOADING DATE 11-81
 APPLICANT'S FLD # OF RESILIENCY 54-90

STATUS

NEW PERIOD
 08-1-1980 - 08-1-1980

REPORT NUMBER	REPORT DATE OF 1977	RD DATE OF 1978
05-08	05-10-80	05-22-80
05-09	05-11-80	05-23-80
05-10	05-12-80	05-24-80
05-11	05-13-80	05-25-80
05-12	05-14-80	05-26-80
05-13	05-15-80	05-27-80
05-14	05-16-80	05-28-80
05-15	05-17-80	05-29-80
05-16	05-18-80	05-30-80
05-17	05-19-80	05-31-80

Complete on Construction Facilities

Fuel Load Slip Dates: 5/82
 Change due to delay in completion of apparatus.

Impaction reports are available at local PDS's.

APPLICANT: LAMP LAMP Lighting Company
 ADDRESS: 170 East 8th Street
 CITY: Dallas, Tex 75201
 CONTACT: J. W. Wifford, Vice President
 PHONE: (214) 751-1000

NO REGION RESPONSIBLE: LAMP LAMP Lighting Company
 OPERATIONS DATE: 07-01-77

CONSTRUCTION DATE: 05-01-78

CONSTRUCTION PROJECT MANAGER: J. R. Wilson
 NO CONTACT PROJECT MANAGER: K. E. Gilliam
 FIELD PROJECT OFFICER: E. J. Berman

NO REGIONAL IN CHARGE: K. Wilson
 REGIONAL SUPERVISOR: J. C. Higgins (District Engineer)

LOCAL PUBLIC UTILITY BUREAU
 Municipal Public Utility Bureau
 Municipal, New York 10000

SOUTH TEXAS I

APPLICANT'S CURRENT FUEL LOADING DATE 08-83
 APPLICANT'S PREVIOUS FUEL LOADING DATE 11-81
 APPLICANT'S FLD # OF RESILIENCY 54-90

INSPECTION STATUS

NEW PERIOD
 08-1-1980 - 08-1-1980

REPORT NUMBER	REPORT DATE OF 1977	RD DATE OF 1978
05-08	05-10-80	05-22-80
05-09	05-11-80	05-23-80
05-10	05-12-80	05-24-80
05-11	05-13-80	05-25-80
05-12	05-14-80	05-26-80
05-13	05-15-80	05-27-80
05-14	05-16-80	05-28-80
05-15	05-17-80	05-29-80
05-16	05-18-80	05-30-80
05-17	05-19-80	05-31-80
05-18	05-20-80	06-01-80
05-19	05-21-80	06-02-80
05-20	05-22-80	06-03-80
05-21	05-23-80	06-04-80
05-22	05-24-80	06-05-80
05-23	05-25-80	06-06-80
05-24	05-26-80	06-07-80
05-25	05-27-80	06-08-80
05-26	05-28-80	06-09-80
05-27	05-29-80	06-10-80
05-28	05-30-80	06-11-80
05-29	05-31-80	06-12-80
05-30	06-01-80	06-13-80
05-31	06-02-80	06-14-80

Complete on Construction Facilities

Fuel Load Slip Dates: November 1981 to September 1982
 Impaction reports are available at local PDS's.

J. W. Coalberg, Vice President
 LAMP LAMP Lighting Company
 (713) 751-1000 - 3 R 2 B

APPLICANT: LAMP LAMP Lighting Company
 ADDRESS: 170 East 8th Street
 CITY: Dallas, Tex 75201
 CONTACT: J. W. Wifford, Vice President
 PHONE: (214) 751-1000

NO REGION RESPONSIBLE: LAMP LAMP Lighting Company
 OPERATIONS DATE: 07-01-77

CONSTRUCTION DATE: 05-01-78

CONSTRUCTION PROJECT MANAGER: J. R. Wilson
 NO CONTACT PROJECT MANAGER: K. E. Gilliam
 FIELD PROJECT OFFICER: E. J. Berman

NO REGIONAL IN CHARGE: K. Wilson
 REGIONAL SUPERVISOR: J. C. Higgins (District Engineer)

LOCAL PUBLIC UTILITY BUREAU
 Municipal Public Utility Bureau
 Municipal, New York 10000

FUEL LOAD DATE CHANGES AS REPORTED BY UTILITY

DATE	REPORT NUMBER	RD DATE	STATUS
10-30-80	05-80	11-81	Steadily reevaluation.
05-10-80	11-81	08-83	Steadily reevaluation.

Impaction reports are available at local PDS's.

DATE CHANGES AS REPORTED BY UTILITY

1. Results in REC indicate and area break criteria... (text continues)
2. Impaction reports are available at local PDS's.

POOR ORIGINAL

SOUTH TEXAS 2

APPLICANT'S CURRENT FUEL LOADING DATE 11-82
 APPLICANT'S PREVIOUS FUEL LOADING DATE 11-82
 APPLICANT'S FIB # OF ISSUANCE 191

J. H. Goldberg, Vice President
 Nuclear Engineering & Construction
 (713) 486-3826

APPLICANT: Electric Power & Lighting Company
 COMPANY: P. O. Box 100
 ADDRESS: 1000 West 10th Street, Fort Worth, Texas 76102
 CONTRACT: Power Plant Construction & Tech. Services
 TO BE INSPECTED: 11
 OF NO. & DATE ISSUED: 079-129(11-82)-11
 CONSTRUCTION STARTED: 11-81-25
 OF EXPIRATION DATE: 10-31-83
 LICENSE PROJECT NUMBER: 5, 14751
 NO. OF TESTS: 1
 TEST BRANCH: 1
 MUNICIPAL INSPECTOR: R. E. Johnson
 - TEST BRANCH: 1

LOCAL PUBLIC ROBERT BOER
 2000 County Line Library
 P. O. Box 488
 Fort Worth, Texas 76101

INSPECTION STATUS

YEAR PERIOD
 1982, 1983 - 1981, 1980

INSTRUMENT NUMBER	REQ. DATE OF TEST	TEST DATE
81500149	01-01-80	01-20-80
	01-01-80	01-20-80
	01-01-80	01-20-80
	01-01-80	01-20-80
	01-01-80	01-20-80
	01-01-80	01-20-80
	01-01-80	01-20-80
	01-01-80	01-20-80
	01-01-80	01-20-80
	01-01-80	01-20-80

Complete on Construction Project: (2) 2.3


Fuel Load Slip Dates: November 1982 to September 1983
 Inspection reports are available at local PPO's.

FUEL LOAD DATE CHANGES AS REPORTED BY UTILITY

REPORT DATE	PREVIOUS DATE	REASON FOR CHANGE
10-18-80	11-82	Schedule reevaluation.
01-18-80	11-82	Schedule reevaluation.


* 2.3 indicates a change of information

POOR ORIGINAL

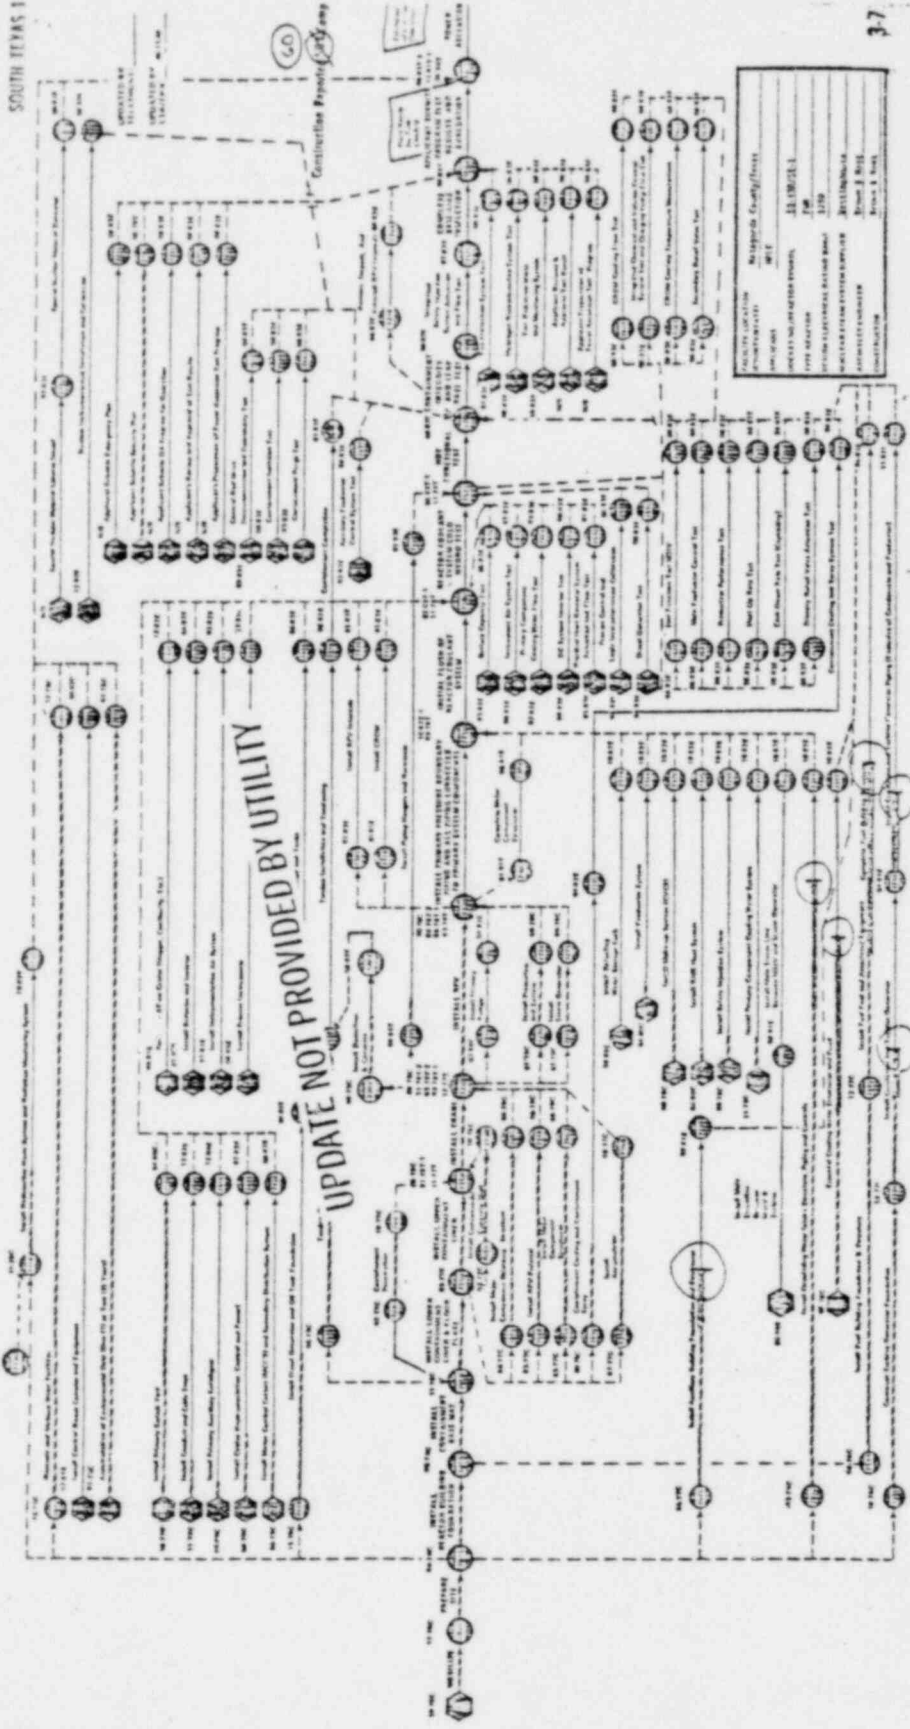

POOR ORIGINAL

SOUTH TEXAS 2

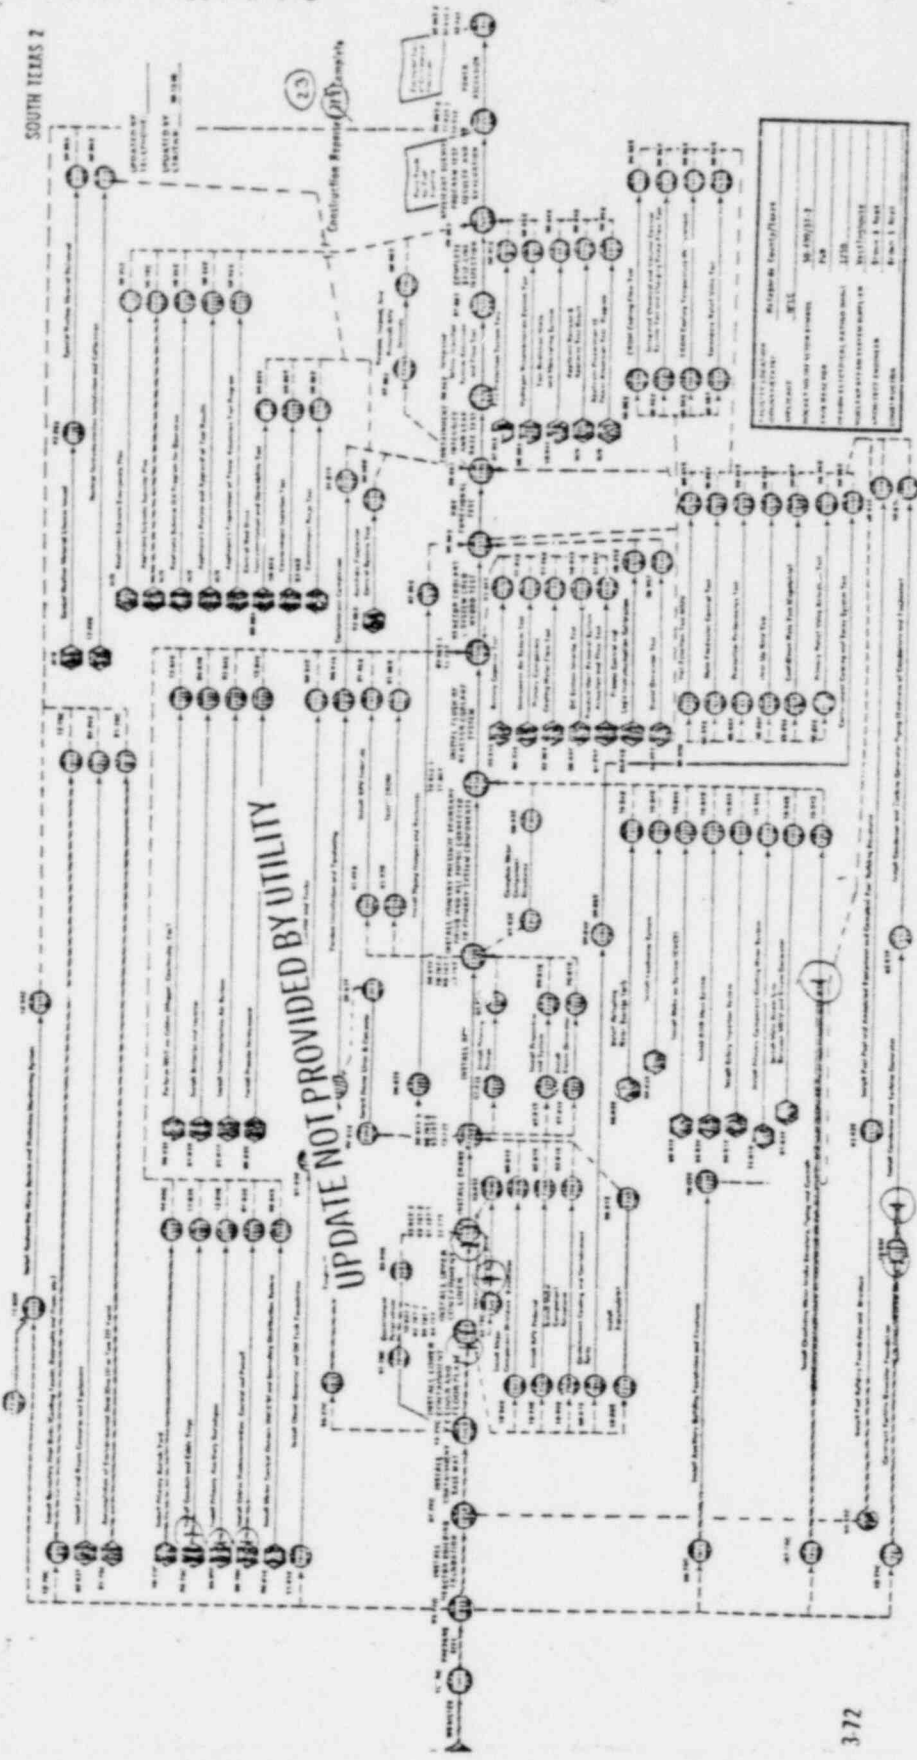

POOR ORIGINAL
