



A Subsidiary of RGS Energy Group, Inc.

ROCHESTER GAS AND ELECTRIC CORPORATION • 89 EAST AVENUE, ROCHESTER, N.Y. 14649-0001 • 716-771-3250

www.rge.com

JOSEPH A. WIDAY
VICE PRESIDENT & PLANT MANAGER
GINNA STATION

February 15, 2001


U.S. Nuclear Regulatory Commission
Document Control Desk
Attn: Guy S. Vissing
Project Directorate I
Washington, D.C. 20555

Subject: Emergency Operating Procedures
R.E. Ginna Nuclear Power Plant
Docket No. 50-244

Dear Mr. Vissing:

As requested, enclosed are Ginna Station Emergency Operating Procedures.

Very truly yours,


Joseph A. Widay

JAW/jdw

xc: U.S. Nuclear Regulatory Commission
Region I
475 Allendale Road
King of Prussia, PA 19406-1415

Ginna USNRC Senior Resident Inspector

Enclosure(s):

ATT Index
FIG Index
ATT-15.0, rev 7
FIG-9.0, rev 1

A002

PARAMETERS: DOC TYPES - PRAR PRATT PRFIG STATUS: EF QU 5 YEARS ONLY:

PROCEDURE NUMBER	PROCEDURE TITLE	REV	EFFECT DATE	LAST REVIEW	NEXT REVIEW	ST
ATT-1.0	ATTACHMENT AT POWER CCW ALIGNMENT	001	07/26/94	02/10/98	02/10/03	EF
ATT-1.1	ATTACHMENT NORMAL CCW FLOW	000	05/18/00	05/18/00	05/18/05	EF
ATT-2.1	ATTACHMENT MIN SW	005	02/01/01	02/10/98	02/10/03	EF
ATT-2.2	ATTACHMENT SW ISOLATION	006	03/25/99	08/11/98	08/11/03	EF
ATT-2.3	ATTACHMENT SW LOADS IN CNMT	003	01/25/95	12/31/99	12/31/04	EF
ATT-3.0	ATTACHMENT CI/CVI	005	01/25/99	01/06/99	01/06/04	EF
ATT-3.1	ATTACHMENT CNMT CLOSURE	003	01/25/99	01/25/99	01/25/04	EF
ATT-4.0	ATTACHMENT CNMT RECIRC FANS	003	07/26/94	05/13/98	05/13/03	EF
ATT-5.0	ATTACHMENT COND TO S/G	004	01/25/95	12/31/99	12/31/04	EF
ATT-5.1	ATTACHMENT SAFW	006	07/07/98	12/31/99	12/31/04	EF
ATT-5.2	ATTACHMENT FIRE WATER COOLING TO TDAFW PUMP	003	01/14/99	01/14/99	01/14/04	EF
ATT-6.0	ATTACHMENT COND VACUUM	003	12/18/96	02/10/98	02/10/03	EF
ATT-7.0	ATTACHMENT CR EVAC	005	02/11/00	02/10/98	02/10/03	EF
ATT-8.0	ATTACHMENT DC LOADS	006	03/22/99	01/14/99	01/14/04	EF
ATT-8.1	ATTACHMENT D/G STOP	004	11/03/95	02/10/98	02/10/03	EF
ATT-8.2	ATTACHMENT GEN DEGAS	006	08/17/99	08/17/99	08/17/04	EF
ATT-8.3	ATTACHMENT NONVITAL	003	07/26/94	02/10/98	02/10/03	EF
ATT-8.4	ATTACHMENT SI/UV	004	04/24/97	02/10/98	02/10/03	EF
ATT-9.0	ATTACHMENT LETDOWN	007	06/09/00	01/06/99	01/06/04	EF
ATT-9.1	ATTACHMENT EXCESS L/D	003	03/31/00	02/10/98	02/10/03	EF
ATT-10.0	ATTACHMENT FAULTED S/G	005	10/03/96	05/13/98	05/13/03	EF
ATT-11.0	ATTACHMENT IA CONCERNS	002	04/07/97	08/11/98	08/11/03	EF
ATT-11.1	ATTACHMENT IA SUPPLY	002	04/07/97	08/11/98	08/11/03	EF
ATT-11.2	ATTACHMENT DIESEL AIR COMPRESSOR	001	12/20/00	04/03/98	04/03/03	EF

PARAMETERS: DOC TYPES - PRAR PRATT PRFIG STATUS: EF QU 5 YEARS ONLY:

PROCEDURE NUMBER	PROCEDURE TITLE	REV	EFFECT DATE	LAST REVIEW	NEXT REVIEW	ST
ATT-12.0	ATTACHMENT N2 PORVS	003	03/24/97	02/10/98	02/10/03	EF
ATT-13.0	ATTACHMENT NC	002	07/26/94	02/10/98	02/10/03	EF
ATT-14.0	ATTACHMENT NORMAL RHR COOLING	002	04/07/97	09/23/99	09/23/04	EF
ATT-14.1	ATTACHMENT RHR COOL	004	05/01/98	05/01/98	05/01/03	EF
ATT-14.2	ATTACHMENT RHR ISOL	001	07/26/94	02/10/98	02/10/03	EF
ATT-14.3	ATTACHMENT RHR NPSH	002	08/01/97	01/06/99	01/06/04	EF
ATT-14.4	ATTACHMENT RHR SAMPLE	001	07/26/94	01/06/99	01/06/04	EF
ATT-14.5	ATTACHMENT RHR SYSTEM	002	07/26/94	02/10/98	02/10/03	EF
ATT-14.6	ATTACHMENT RHR PRESS REDUCTION	001	01/14/99	01/14/99	01/14/04	EF
ATT-15.0	ATTACHMENT RCP START	007	02/15/01	03/17/00	03/17/05	EF
ATT-15.1	ATTACHMENT RCP DIAGNOSTICS	003	04/24/97	02/10/98	02/10/03	EF
ATT-15.2	ATTACHMENT SEAL COOLING	003	05/22/97	02/10/98	02/10/03	EF
ATT-16.0	ATTACHMENT RUPTURED S/G	010	01/09/01	01/11/00	01/11/05	EF
ATT-16.1	ATTACHMENT SGTL	000	09/08/00	09/08/00	09/08/05	EF
ATT-16.2	ATTACHMENT RCS BORON FOR SGTL	001	10/13/00	09/08/00	09/08/05	EF
ATT-17.0	ATTACHMENT SD-1	011	01/09/01	02/29/00	02/28/05	EF
ATT-17.1	ATTACHMENT SD-2	005	09/26/96	01/30/01	01/30/06	EF
ATT-18.0	ATTACHMENT SFP - RWST	004	10/08/97	02/10/98	02/10/03	EF
ATT-20.0	ATTACHMENT VENT TIME	003	07/26/94	02/10/98	02/10/03	EF
ATT-21.0	ATTACHMENT RCS ISOLATION	001	07/26/94	02/10/98	02/10/03	EF
ATT-22.0	ATTACHMENT RESTORING FEED FLOW	001	02/12/99	03/24/97	03/24/02	EF
ATT-23.0	ATTACHMENT TRANSFER 4160V LOADS	000	02/26/99	02/26/99	02/26/04	EF
ATT-24.0	ATTACHMENT TRANSFER BATTERY TO TSC	000	09/08/00	09/08/00	09/08/05	EF

TOTAL FOR PRATT 47

PARAMETERS: DOC TYPES - PRAR PRATT PRFIG STATUS: EF QU 5 YEARS ONLY:

PROCEDURE NUMBER	PROCEDURE TITLE	REV	EFFECT DATE	LAST REVIEW	NEXT REVIEW	ST
FIG-1.0	FIGURE MIN SUBCOOLING	000	05/01/98	05/01/98	05/01/03	EF
FIG-2.0	FIGURE SDM	002	10/13/00	05/01/98	05/01/03	EF
FIG-3.0	FIGURE NAT CIRC C/D WITH SHROUD FANS	000	05/01/98	05/01/98	05/01/03	EF
FIG-3.1	FIGURE NAT CIRC C/D WITHOUT SHROUD FANS	001	02/08/01	05/01/98	05/01/03	EF
FIG-3.2	FIGURE NC C/D WITH VOID IN UPPER HEAD	000	05/01/98	05/01/98	05/01/03	EF
FIG-4.0	FIGURE RCP SEAL LEAKOFF	001	10/13/00	05/01/98	05/01/03	EF
FIG-5.0	FIGURE RHR INJECTION	000	05/01/98	05/01/98	05/01/03	EF
FIG-6.0	FIGURE MIN RCS INJECTION	000	05/01/98	05/01/98	05/01/03	EF
FIG-7.0	FIGURE INTACT S/G PRESSURE	001	05/18/98	05/01/98	05/01/03	EF
FIG-8.0	FIGURE TSAT	000	05/01/98	05/01/98	05/01/03	EF
FIG-9.0	FIGURE TECH SPEC C/D	001	02/15/01	05/01/98	05/01/03	EF
FIG-9.1	FIGURE C/D LIMITS	000	05/01/98	05/01/98	05/01/03	EF
FIG-10.0	FIGURE LIMIT A	000	05/01/98	05/01/98	05/01/03	EF
FIG-11.0	FIGURE SOAK LIMITS	000	05/01/98	05/01/98	05/01/03	EF
FIG-12.0	FIGURE CNMT HYDROGEN	000	05/01/98	05/01/98	05/01/03	EF
FIG-13.0	FIGURE BACK PRESSURE	000	05/01/98	05/01/98	05/01/03	EF
FIG-14.0	FIGURE IA ISOL	000	05/01/98	05/01/98	05/01/03	EF

TOTAL FOR PRFIG 17

EOP: ATT-15.0	TITLE: ATTACHMENT RCP START	REV: 7 PAGE 1 of 3
------------------	--------------------------------	-----------------------

Responsible Manager Reddington Date 2-15-2001

CAUTION: IF seal outlet temperature is greater than 235°F, THEN CCW thermal barrier cooling and seal injection should NOT be established to the affected RCP(s). Both of these methods of seal cooling could have unintended consequences that result in additional pump damage or failure of the CCW system. Seal cooling should instead be restored by cooling the RCS, which will reduce the temperature of the water flowing through the pump seals.

- A) The following are prerequisites for starting an RCP:
 - o RCP oil lift pump running (~2 minutes) (MCC E)
 - o RCP oil lift pressure white light - LIT

- B) In addition, the following conditions should be met prior to starting an RCP:
 - o Both PRZR spray valves closed - DEMAND AT 0%
 - o CCW in service to selected RCP(s) with flow and temperature alarms (A-7, A-15) extinguished.
 - o Selected RCP(s) seal inlet temperature - LESS THAN 135°F
 - o Selected RCP(s) motor bearing temperatures - LESS THAN 200°F (PPCS address is GD RCPS or use recorder, if selected)
 - o Selected RCP(s) seal injection in service
 - o Seal injection flow - GREATER THAN 6 GPM
 - o Labyrinth seal D/P - GREATER THAN 15 INCHES OF WATER
 - o Selected RCP(s) #1 seal D/P - GREATER THAN 220 PSID
 - o Selected RCP(s) oil levels:
 - o Level alarms (A-24, A-32) - EXTINGUISHED
 - o Level indicators - ON SCALE
 - o Selected RCP(s) seal return alignment:
 - a) RCP #1 seal outlet valve(s) open:
 - o AOV-270A for RCP A
 - o AOV-270B for RCP B
 - b) IF MOV-313, seal return isolation, open, THEN verify the following:
 - o VCT pressure - GREATER THAN 15 PSIG
 - o Selected RCP(s) #1 seal leakoff flow - WITHIN THE NORMAL OPERATING RANGE OF FIGURE RCP SEAL LEAKOFF
 - o Selected RCP(s) standpipe low level alarm (B-11, B-12) - EXTINGUISHED


EOP: ATT-15.0	TITLE: ATTACHMENT RCP START	REV: 7 PAGE 2 of 3
------------------	--------------------------------	-----------------------

- c) IF MOV-313 closed, THEN verify other RCP #1 seal parameters normal for selected RCP(s):
- o RCP #1 seal inlet temperature - LESS THAN 135°F
 - o RCP #1 seal D/P - GREATER THAN 220 PSID

NOTE: RCP oil lift pump should be stopped after RCP is running.

FIGURE RCP SEAL LEAKOFF

#1 SEAL LEAK RATE (GPM)

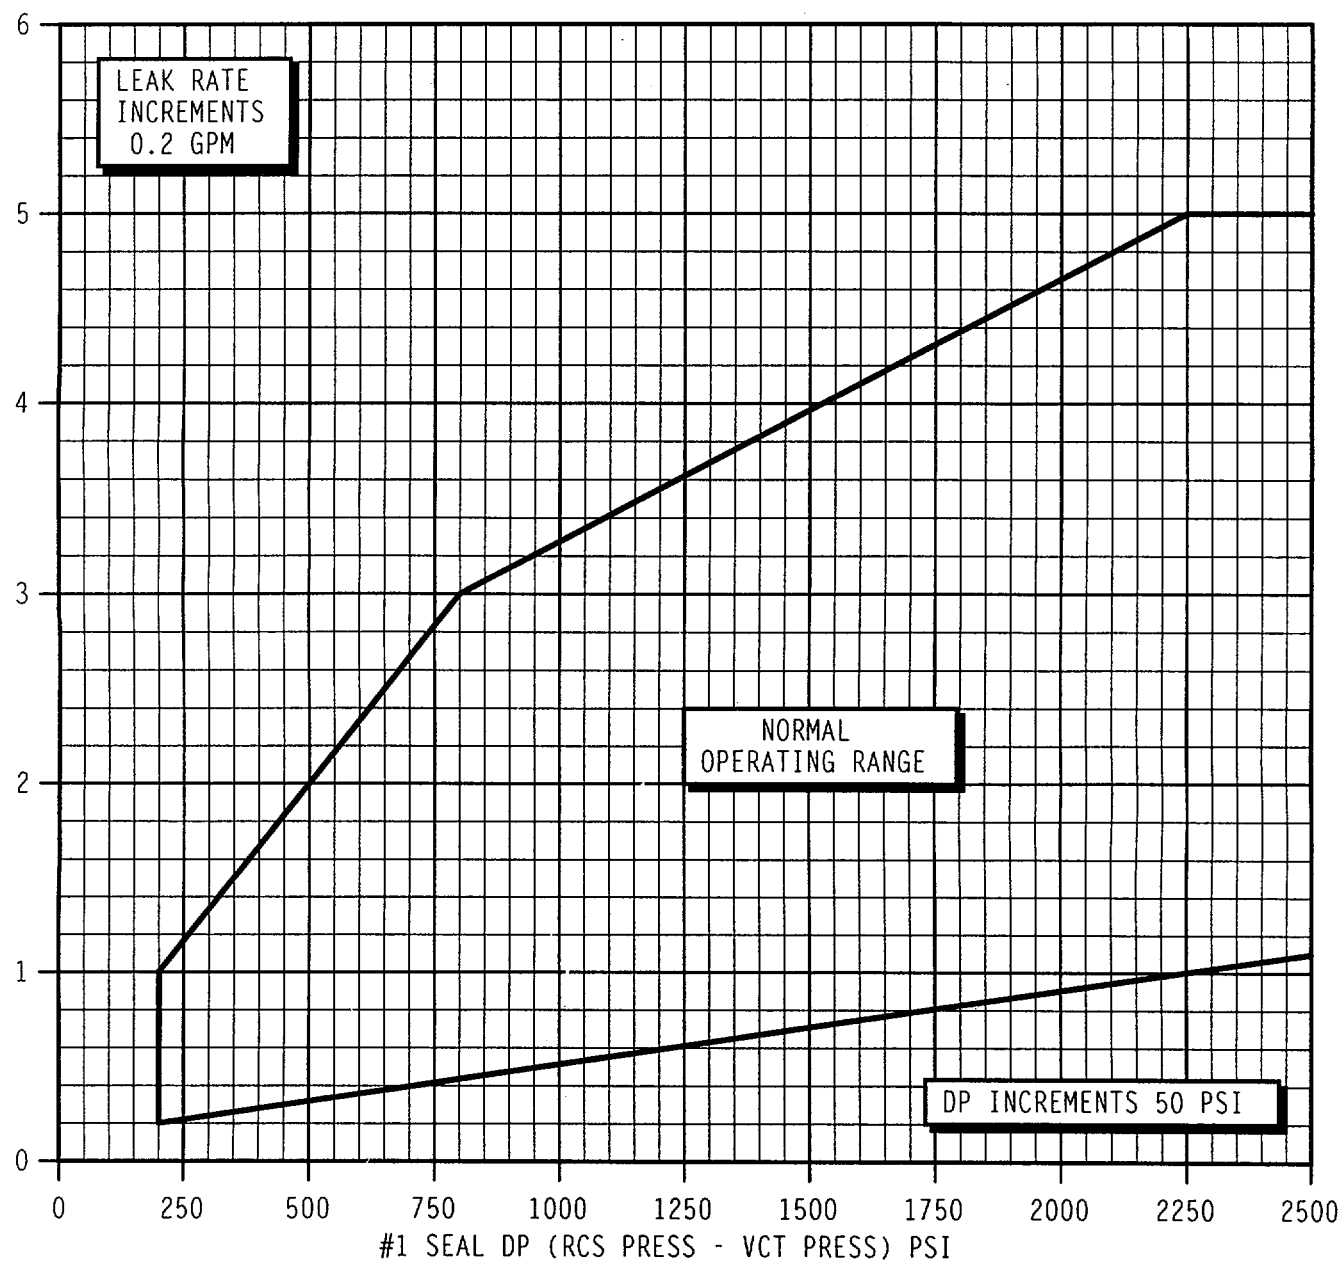

EOP: FIG-9.0	TITLE: FIGURE TECH SPEC C/D	REV: 1 PAGE 1 of 1
---------------------	------------------------------------	---------------------------

Responsible Manager *Neil Johnson* Date *2-15-2001*

FIGURE TECH SPEC C/D

