



Final Status Survey Final Report Phase IV

**Appendix A15
Survey Unit Release Record
9106-0015, Discharge Canal**

November 2006



CYAPCO
FINAL STATUS SURVEY RELEASE RECORD
DISCHARGE CANAL
SURVEY UNIT 9106-0015

Prepared By: *Paul Rouball* Date: 11-21-06
FSS Engineer

Reviewed By: *Robert J. M.* Date: 11-21-06
FSS Engineer

Approved By: *Clyde T. Jensen* Date: 11/26/06
Technical Support Manager

DISCHARGE CANAL
SURVEY UNIT 9106-0015
RELEASE RECORD

TABLE OF CONTENTS

1.	SURVEY UNIT DESCRIPTION	3
2.	CLASSIFICATION BASIS	3
3.	DATA QUALITY OBJECTIVES (DQO)	5
4.	SURVEY DESIGN	8
5.	SURVEY IMPLEMENTATION	12
6.	SURVEY RESULTS	13
7.	QUALITY CONTROL	15
8.	INVESTIGATIONS AND RESULTS	16
9.	REMEDICATION AND RESULTS	18
10.	CHANGES FROM THE FINAL STATUS SURVEY PLAN	18
11.	DATA QUALITY ASSESSMENT (DQA)	18
12.	ANOMALIES	19
13.	CONCLUSION	19
14.	ATTACHMENTS	20
14.1	Attachment 1 – Figures (9 pages including cover)	
14.2	Attachment 2 – Sample and Statistical Data (318 pages including covers)	

DISCHARGE CANAL
SURVEY UNIT 9106-0015

RELEASE RECORD

1. SURVEY UNIT DESCRIPTION

Survey Unit 9106-0015 (Discharge Canal) is designated as Final Status Survey (FSS) Class 1 and consists of approximately 1,170 m² (0.29 acres) of water covered sediment in an area located approximately 0.81 miles from the reference coordinate system benchmark used at the Haddam Neck Plant (HNP) (see Attachment 1, Figure 1). The Discharge Canal is a man-made mile long waterway that runs parallel to, and ultimately communicates with the Connecticut River. The Discharge Canal is subdivided into fifteen (15) survey units including two (2) permanent wetland areas for FSS purposes. The survey unit is completely surrounded by Discharge Canal Survey Unit 9106-0007. The survey unit comprises the canal sediments to the depth of three feet from the top of the sediment layer or the original construction depth. This survey unit is bounded by reference coordinates E022 through E029 and by S133 through S143 (refer to License Termination Plan Section 5.4.4). The reference coordinates provide the maximum dimensions of a rectangle containing this survey unit. Some areas contained in this rectangle may not be part of this survey unit. The boundary of the survey unit was defined using a Global Positioning System (GPS) based on the Connecticut State Plane System North American Datum (NAD) 1927.

2. CLASSIFICATION BASIS

The survey unit was classified in accordance with Procedure RPM 5.1-10, "Survey Unit Classification." The historical information, scoping analyses and characterization results provided sufficient data to designate Survey Unit 9106-0015 as Class 1 in June 2006.

The "Classification Basis Summary" conducted for this survey unit consisted of:

- a) A review of the 10CFR50.75 (g) (1) database,
- b) A review of the "Initial Characterization Report" and the "Historic Site Assessment (HSA) Supplement,"
- c) Historic and current survey records review,
- d) Visual inspections and a "walk-down."
- e) Formal or informal interviews with cognizant personnel.

A review of the 10CFR50.75(g)(1) database report identified a number of events that may have impacted this survey unit. Several events indicated the potential for plant related contamination in the survey unit. These included a number of primary side system to secondary side system leakage events, contamination found to be present in secondary side systems and components, and unmonitored spills that drained to the discharge canal. In 1986, samples were taken from the legacy dredge spoils removed in 1979 dredged spoils area and from recently dredged canal sediment. The sample analyses indicated that the concentrations of Cs-137, Co-60 and other radionuclides were a small

DISCHARGE CANAL
SURVEY UNIT 9106-0015

RELEASE RECORD

fraction of the DCGLs for those nuclides that could be identified by gamma spectroscopy. (refer to NE-86-RA-1142 dated 11-13-86). None of the available historical information reviewed would support a conclusion that any residual activity in this survey unit is likely to be present at concentrations greater than the respective DCGLs.

Additional information was provided by several historical documents, including the "Results of Scoping Survey", (completed 9/1/98), the "Historical Site Assessment", and the HSA Supplement (dated 6-30-00). These documents presented the results of several sediment samples taken in 1997. These sample results indicated concentrations of 0.5 pCi/g for Co-60, 0.024 pCi/g for Cs-134 and 0.722 pCi/g for Cs-137.

The survey area that constitutes Survey Unit 9106-0015 was initially a portion of Class 2 Survey Unit 9106-0007. However, upon reviewing the FSS data for Survey Unit 9106-0007, it was determined that one (1) sample exceeded the Operational DCGL for the area. This required that a portion of Survey Unit 9106-0007 be reclassified as a Class 1 survey unit. This was done and the newly created survey unit was designated 9106-0015.

The FSS data taken in association with the initial FSS design for Survey Unit 9106-0007, was deemed to be appropriate for characterization data for Survey Unit 9106-0015. This consisted of fifteen (15) sediment samples taken from fifteen (15) locations. All of the samples were analyzed by gamma spectroscopy and for Sr-90. In addition, two (2) of these samples were analyzed for all Hard-to-Detect (HTD) nuclides. The results indicated that the radionuclides of concern identified for FSS planning purposes were Cs-137, Co-60 and Sr-90 (refer to Table 1).

**Table 1 – Basic Statistical Quantities for Cs-137, Co-60 and Sr-90
from the Characterization Survey**

Parameter	Cs-137 (pCi/g)	Co-60 (pCi/g)	Sr-90 (pCi/g)
Minimum Value:	-1.62E-02	-1.46E-02	-9.81E-03
Maximum Value:	6.42E-01	3.09E+00	4.04E-02
Mean:	2.25E-01	4.90E-01	8.03E-03
Median:	2.21E-01	1.20E-01	7.30E-03
Standard Deviation:	2.22E-01	8.32E-01	1.08E-02
NOTE: The Operational DCGLs from Table 2 are 6.01 pCi/g for Cs-137, 2.90 pCi/g for Co-60 and 1.18 for Sr-90; these are used in conjunction with the unity rule to achieve nineteen (19) mrem/yr TEDE			

The FSS Engineer performed a visual inspection and walk-down during May 2006 to assess the physical condition of the survey unit, evaluate access points and travel paths and identify potentially hazardous conditions.

Based upon the historical information and the results of radiological surveys performed during characterization, it was concluded that there was significant probability for residual radioactivity to be present in this survey unit in

DISCHARGE CANAL
SURVEY UNIT 9106-0015

RELEASE RECORD

concentrations greater than the Operational DCGLs justifying a final survey unit classification of Class 1 (refer to Section 3).

3. DATA QUALITY OBJECTIVES (DQO)

FSS design and planning is based on the Data Quality Objective (DQO) process as described by the LTP, Procedure RPM 5.1-11, "*Preparation of Final Status Survey Plan*," and the "*Multi-Agency Radiation Survey and Site Investigation Manual*" (MARSSIM). A summary of the main features of the DQO process are provided herein.

The DQO process incorporates hypothesis testing and probabilistic sampling distributions to control decision errors during data analysis. Hypothesis testing is a process based on the scientific method that compares a baseline condition to an alternate condition. The baseline condition is technically known as the null hypothesis. Hypothesis testing rests on the premise that the null hypothesis is true and that sufficient evidence must be provided for rejection. In designing the survey plan, the underlying assumption, or null hypothesis was that residual activity in the survey unit exceeded the release criteria. Rejection of the null hypothesis would satisfy the release criteria objective of the FSS.

The primary objective of the Final Status Survey Plan (FSSP) was to demonstrate that the level of residual radioactivity in Survey Unit 9106-0015 did not exceed the release criteria specified in the LTP and that the potential dose from residual radioactivity is As Low As Reasonably Achievable (ALARA).

A fundamental precursor to survey design is to establish a relationship between the release criteria and some measurable quantity. This is done through the development of Derived Concentration Guideline Levels (DCGLs). The DCGLs represent the concentration of radioactivity above background, equivalent to a dose-based release criterion and is presented in terms of surface or mass activity concentrations. Chapter 6 of the LTP describes in detail the modeling used to develop the DCGLs for soil (called Base Case Soil DCGL), for existing groundwater radioactivity and for future groundwater radioactivity that will be contributed by building foundations and footings.

As described in detail in the LTP, the dose model applied to the discharge canal presumes that the canal sediments are dredged to a depth of three (3) feet below the top of the sediment layer and spread for the planting of crops per the Resident Farmer Scenario. Consequently, the soil DCGLs are directly applied to the canal sediment media

The DCGLs presented in Chapter 6 of the LTP were developed for exposures from three (3) components, that is, residual radioactivity in soil, existing groundwater radioactivity, and future groundwater radioactivity from the burial of concrete foundations or footings from site buildings containing residual radioactivity. Equation 1 shows the mathematical relationship between the three (3) components and the total dose.

DISCHARGE CANAL
SURVEY UNIT 9106-0015

RELEASE RECORD

Equation 1:

$$H_{\text{Total}} = H_{\text{Soil (sediment)}} + H_{\text{Existing GW}} + H_{\text{Future GW}}$$

The total dose under the LTP criteria is twenty-five (25) mrem/yr TEDE from all three components. The allowable total dose under the Connecticut Department of Environmental Protection (CTDEP) radiological remediation standard for Connecticut Yankee (CY) is nineteen (19) mrem/yr TEDE. To satisfy both the LTP and CY CTDEP criteria, the dose from soil must be reduced when using the groundwater dose values discussed above.

This survey unit is not affected by existing groundwater, (reference CY memo ISC 06-024). Therefore, dose contribution from existing groundwater is zero (0) mrem/yr TEDE.

This survey unit is not impacted by future groundwater radioactive contamination, as there are no concrete foundations or footings remaining within the groundwater saturated zone in the area (reference CY memo ISC 06-024). The dose contribution from future groundwater is zero (0) mrem/yr TEDE.

Equation 2:

$$19 \text{ mrem/yr}_{\text{Total}} = 19 \text{ mrem/yr}_{\text{Soil}} + 0 \text{ mrem/yr}_{\text{Existing GW}} + 0 \text{ mrem/yr}_{\text{Future GW}}$$

The allowable dose for soil in this survey unit is nineteen (19) mrem/yr TEDE as shown by Equation 2 above. The concentration of residual radioactivity resulting in nineteen (19) mrem/yr TEDE is designated as the Operational DCGL, and has been established for the radionuclides of concern as provided in Table 2.

Note: The survey design used a much smaller value for investigation than the Operational DCGL provided by Table 2 to conservatively account for the contribution to the total dose from existing and future groundwater which had not been established at the time of planning the FSS.

DISCHARGE CANAL
SURVEY UNIT 9106-0015
RELEASE RECORD

Table 2 – Radionuclide Specific Base Case Soil DCGL, Operational DCGLs and Required Minimum Detectable Concentrations

Radionuclide ⁽¹⁾	Base Case Soil DCGL (pCi/g) ⁽²⁾	Operational DCGL (pCi/g) ⁽³⁾	Required MDC (pCi/g) ⁽⁴⁾
H-3	4.12E+02	3.13E+02	1.65E+01
C-14	5.66E+00	4.30E+00	2.26E-01
Mn-54	1.74E+01	1.32E+01	6.96E-01
Fe-55	2.74E+04	2.08E+04	1.10E+03
Co-60	3.81E+00	2.90E+00	1.52E-01
Ni-63	7.23E+02	5.49E+02	2.89E+01
Sr-90	1.55E+00	1.18E+00	6.20E-02
Nb-94	7.12E+00	5.41E+00	2.85E-01
Tc-99	1.26E+01	9.58E+00	5.04E-01
Ag-108m	7.14E+00	5.43E+00	2.86E-01
Cs-134	4.67E+00	3.55E+00	1.87E-01
Cs-137	7.91E+00	6.01E+00	3.16E-01
Eu-152	1.01E+01	7.68E+00	4.04E-01
Eu-154	9.29E+00	7.06E+00	3.72E-01
Eu-155	3.92E+02	2.98E+02	1.57E+01
Pu-238	2.96E+01	2.25E+01	1.18E+00
Pu-239/240	2.67E+01	2.03E+01	1.07E+00
Pu-241	8.70E+02	6.61E+02	3.48E+01
Am-241 ⁽⁵⁾	2.58E+01	1.96E+01	1.03E+00
Cm-243/244	2.90E+01	2.20E+01	1.16E+00

- (1) **Bold** indicates those radionuclides considered to be Hard to Detect (HTD)
- (2) The Base Case Soil DCGLs for soil are specified by the LTP in Chapter 6 and are equivalent to twenty-five (25) mrem/yr TEDE
- (3) The Operational DCGL is equivalent to nineteen (19) mrem/yr TEDE
- (4) The required MDC is equivalent to one (1) mrem/yr TEDE
- (5) Americium-241 can be analyzed by gamma and alpha spectroscopy and is considered to be Easy to Detect (ETD). The preferred result is the alpha spectroscopy's when both analyses are performed.

Another important facet of the DQO process is to identify the radionuclides of concern and determine the concentration variability. Initial characterization was performed in April of 2004 as discussed in Section 2. Cs-137, Co-60 and Sr-90 were found to be the predominate radionuclides of concern. The basic statistical quantities (i.e., mean, standard deviation, median) for Cs-137, Co-60 and Sr-90 are provided in Table 1.

As part of the DQOs applied to laboratory processes, analysis results were reported as actual calculated results. Results reported as less than Minimum Detectable Concentration (<MDC) were not accepted for FSS. Sample report

DISCHARGE CANAL
SURVEY UNIT 9106-0015

RELEASE RECORD

summaries included unique sample identification, analytical method, radionuclide, result, and uncertainty to two (2) standard deviations, laboratory data qualifiers, units, and the required and observed MDC.

The Elevated Measurement Comparison (EMC) consists of comparing each measurement from the survey unit with the investigation levels discussed in Section 4 (and presented in Table 4). As stated in Section 5.8.3 of the LTP, any measurement from the survey unit that is greater than an investigation level indicates an area of relatively high concentrations that should be investigated, regardless of the outcome of the nonparametric statistical tests. Thus the use of the EMC against the investigation levels may be viewed as assurance that unusually large measurements will receive proper attention regardless of the outcome of those tests and that any area having the potential for significant dose contributions will be identified.

The LTP (by way of Equation 5-31) states that if residual radioactivity exists in an isolated area of elevated activity in addition to residual radioactivity distributed relatively uniformly across a survey unit, the unity rule will be used to ensure the total dose is within the release criterion. This is demonstrated in equation 3.

Equation 3:

$$\frac{\delta}{DCGL_w} + \frac{\bar{C}_{elevated} - \delta}{(AreaFactor) \times DCGL_w} < 1$$

Where:

δ = average concentration outside the elevated area,

$\bar{C}_{elevated}$ = average concentration in the elevated area.

A separate term will be used in Equation 3.0 for each elevated area in a survey unit.

4. SURVEY DESIGN

The level of effort associated with planning a survey is based on the complexity of the survey and nature of the hazards. Guidance for preparing FSS plans is provided in Procedure RPM 5.1-11, "Preparation of Final Status Survey Plans".

This survey was initially designed to ten (10) mrem/yr TEDE. At the time when the survey was designed, the dose contribution for existing and future groundwater had not yet been determined. Subsequently, a conservative value

DISCHARGE CANAL
SURVEY UNIT 9106-0015

RELEASE RECORD

was chosen for the design DCGL. This approach is no longer required as the total dose from existing and future groundwater has been established. The dose for soil used for this survey unit to demonstrate compliance with the LTP criteria is nineteen (19) mrem/yr TEDE, as discussed in Section 3 of this Release Record.

The DQO process determined that Cs-137, Co-60 and Sr-90 were the radionuclides of concern (refer to Section 2). The sum of fractions or unity rule was used with the individual Operational DCGLs because multiple radionuclides (Cs-137, Co-60 and Sr-90) were considered in the survey design.

Surrogate DCGLs were not required for this survey unit based on process knowledge from FSS of nearby adjacent areas and via screening process described in LTP Section 5.4.7.2, "Gross Activity DCGLs". Sr-90 concentrations in sediment and soil were ascertained by direct analysis.

Radionuclide screening or de-selection is a process where an individual radionuclide or aggregate may be considered insignificant and eliminated from the FSS. The criteria for de-selection are concentrations that are less than 5% for individual radionuclides and that are less than 10% for the aggregate of all radionuclides that are de-selected. This process was applied to analysis data for this survey unit.

The EMC applies to this survey unit since it is a Class 1 area.

The Sign Test was selected as the non-parametric statistical test to demonstrate that the null hypothesis was rejected. The use of the Sign Test did not require the selection or use of a background reference area, which simplified survey design and implementation. In addition, this approach is conservative since it includes background Cs-137 as part of the sample set.

The number of sediment samples for FSS was determined in accordance with Procedure RPM 5.1-12, "*Determination of the Number of Samples for Final Status Survey.*" The Lower Bound of the Gray Region (LBGR) was set in accordance with Procedure RPM 5.1-11 to 0.394 to maintain the relative shift (Δ/σ) in the range of 1 and 3. The resulting relative shift was 1.1. A Prospective Power Curve was generated using COMPASS, a software package developed under the sponsorship of the United States Nuclear Regulatory Commission (USNRC) for implementation of MARSSIM in support of the decommissioning license termination rule (10 CFR 20, Subpart E). The result of the COMPASS computer run showed adequate power for the survey design. This indicates that the survey unit has a high probability of rejecting the null hypothesis, assuming that the characterization data are representative of the FSS results. Survey design specified twenty-eight (28) sediment core samples for non-parametric statistical testing.

The grid pattern and locations of the sediment samples were determined using Visual Sample Plan (VSP) in accordance with Procedure RPM 5.1-14, "*Identifying, and Marking Surface Sample Locations for Final Status Survey.*"

DISCHARGE CANAL
SURVEY UNIT 9106-0015

RELEASE RECORD

Visual Sample Plan was created by Pacific Northwest National Laboratory (PNNL) for the United States Department of Energy. A systematic triangular grid pattern with a random starting point was selected for sample design, which is appropriate for a Class 1 area.

Sample locations were identified using AutoCAD-LT, a commercially available plotting software package with coordinates consistent with the Connecticut State Plane System. These coordinates were integrated with a GPS to locate sample locations in the field. Sample measurement locations for the design are listed with the GPS coordinates in Table 3.

Table 3 - Sample Measurement Locations with Associated GPS Coordinates

Designation	Northing	Easting
9106-0015-001F	235153.65	672480.81
9106-0015-002F	235133.21	672445.41
9106-0015-003F	235133.21	672469.01
9106-0015-004F	235133.21	672492.61
9106-0015-005F	235112.77	672410.01
9106-0015-006F	235112.77	672433.61
9106-0015-007F	235112.77	672457.21
9106-0015-008F	235112.77	672480.81
9106-0015-009F	235112.77	672504.40
9106-0015-010F	235092.34	672421.81
9106-0015-011F	235092.34	672445.41
9106-0015-012F	235092.34	672469.01
9106-0015-013F	235092.34	672492.61
9106-0015-014F	235092.34	672516.20
9106-0015-015F	235071.90	672433.61
9106-0015-016F	235071.90	672457.21
9106-0015-017F	235071.90	672480.81
9106-0015-018F	235071.90	672504.40
9106-0015-019F	235071.90	672528.00
9106-0015-020F	235051.46	672445.41
9106-0015-021F	235051.46	672469.01
9106-0015-022F	235051.46	672492.61
9106-0015-023F	235051.46	672516.20
9106-0015-024F	235051.46	672539.80
9106-0015-025F	235031.02	672457.21
9106-0015-026F	235031.02	672480.81
9106-0015-027F	235031.02	672504.40
9106-0015-028F	235010.58	672469.01

Five (5) sediment samples were analyzed for the full suite of radionuclides specified in Table 1, exceeding the requirement to analyze 5% of the sample population for HTD analysis specified in procedure RPM 5.1-11. Three (3) of the five (5) samples were randomly selected using the Microsoft Excel "RAND"

DISCHARGE CANAL
SURVEY UNIT 9106-0015

RELEASE RECORD

function. The two (2) samples exhibiting the highest observed radionuclide concentrations by gamma analyses were also selected.

The results of one (1) additional sample, number 9106-0007-017F, were included in this report as a result of the investigation that was conducted based on the results of the sample analyses.

The implementation of quality control measures as referenced by Procedure RPM 5.1-24, "*Split Sample Assessment for Final Status Survey*," required the collection of three (3) soil samples for "split sample" analysis by the off-site laboratory. These locations were selected randomly using the Microsoft Excel "RAND" function. The number of quality control samples exceeded the 5% requirement as specified by the LTP.

Section 5.7.3.2.6 of the LTP specifies that scanning is not required for the FSS of the Discharge Canal. Table 4 provides a synopsis of the survey design.

Feature	Design Criteria	Basis
Survey Unit Land Area	1,170 m ²	Based on AutoCAD-LT and Visual Sample Plan calculations
Number of Measurements ⁽³⁾	26	Type 1 and Type 2 errors were 0.05, sigma was 0.552 the LBGR was set to 0.394 to maintain Relative Shift in the range of 1 and 3, Relative Shift was 1.1
Grid Spacing	7.21 m	Based on triangular grid
Design DCGL	3.16 pCi/g Cs-137 1.52 pCi/g Co-60 0.62 pCi/g Sr-90	To achieve ten (10) mrem/yr TEDE
Operational DCGL	6.01 pCi/g Cs-137 2.90 pCi/g Co-60 1.18 pCi/g Sr-90	To achieve nineteen (19) mrem/yr TEDE ⁽²⁾ to demonstrate compliance with Equation 2 of this Release Record
Scan Coverage	N/A	The LTP exempts this area
Sediment Investigation Level	6.01 pCi/g Cs-137 2.90 pCi/g Co-60 1.18 pCi/g Sr-90	The Operational DCGL meets the LTP criteria for a Class 1 survey unit
Area between points	45 m ²	The survey unit area divided by the number of direct measurements used to calculate the grid size. (1,170 m ² /26 = 45 m ²)

(1) The survey design used a much smaller value for investigation than the Operational DCGL provided by Table 2 as the total dose from existing and future groundwater had not been established at the time of planning the FSS

(2) The allowable dose for soil in this survey unit is nineteen (19) mrem/yr TEDE as the bounding dose from existing and future groundwater has been established based on field data (reference CY memo ISC 06-024.)

(3) The grid size selected was based on twenty-six (26) samples. However, the VSP run generated twenty-eight (28) measurement locations, each of the twenty-eight (28) measurements taken were used in the Sign Test.

DISCHARGE CANAL
SURVEY UNIT 9106-0015

RELEASE RECORD

5. SURVEY IMPLEMENTATION

Final Status Survey field activities were conducted under Work Plan and Inspection Record (WP&IR) 2006-0021. The WP&IR package included a detailed FSSP, job safety analysis, job planning checklist and related procedures for reference. Daily briefings were conducted to discuss the expectations for job performance and the safety aspects of the survey. The "Daily Survey Journal" was used to document field activities and other information pertaining to the FSS.

Measurement locations were identified in North American Datum (NAD) 1927 coordinates that were supplied to the sampling vendor, Ocean Surveys, Inc. (OSI) of Old Saybrook, Connecticut. Discharge Canal sampling was accomplished using direct push technology to collect composite samples of bottom and mean high water mark sediments. Sediment cores from the Discharge Canal were obtained by OSI using a vibrating corer that is platform mounted on a sampling vessel. The core barrel was a three (3) inch diameter thin-walled aluminum tube which also served as a core liner (ten (10) feet or less). A core catcher was available to prevent the sample from sliding out of the bottom of the tube. Vessel positioning and the determination of sample locations were accomplished using a GPS interfaced with a navigation and data logging system.

After extraction, water was drained from above the sample by drilling holes above the sediment. The liner was cut, capped, sealed, labeled and turned over to site personnel who processed and controlled the samples under Chain of Custody (COC) protocols in accordance with procedure RPM 5.1-5, "*Chain of Custody for Final Status Survey Samples.*" Rinsing of the barrel and associated equipment was performed between sampling events. New aluminum tubes were used for each sample to prevent cross-contamination of subsequent samples.

The twenty-eight (28) sediment samples were collected and packaged in accordance with Haddam Neck Plant (HNP) Procedure RPM 5.1-3, "*Collection of Sample Media for Final Status Survey*" and FSS design. Samples were controlled, transported, stored, and transferred to the off-site laboratory using COC protocols.

Five (5) samples (9106-0015-002F, 9106-0015-004F, 9106-0015-015F, 9106-0015-018F and 9106-0015-021F) of the total number of samples identified for non-parametric testing were selected for HTD radionuclide analysis by the off-site laboratory. A sixth sample, 9106-0007-017F, was originally collected and analyzed as part of Survey Unit 9106-0007. However, since the sample results exceeded the limits for a Class 2 survey unit, Survey Unit 9106-0015, a Class 1 survey unit, was created. The results of sample number 9106-0007-017F were included in this survey unit as a investigative sample result that required

DISCHARGE CANAL
SURVEY UNIT 9106-0015

RELEASE RECORD

additional sampling and analysis and not for non-parametric testing purposes (refer to Section 8).

The implementation of quality control measures included the collection of three (3) split samples at locations (9106-0015-005F, 9106-0015-012F and 9106-0015-018F for comparative analysis by the off-site laboratory.

6. SURVEY RESULTS

The off-site laboratory employed for the radiological analyses of samples was General Engineering Laboratories (GEL) – Charleston, South Carolina. The laboratory analyzed the twenty-eight (28) samples taken for non-parametric statistical testing and the associated duplicates using gamma spectroscopy. Sr-90 was analyzed by liquid scintillation analyses. All analyses were performed to the required MDC.

Cs-137 was positively identified (i.e., a result greater than two (2) standard deviations uncertainty) in twenty-four (24), Co-60 was positively identified in twenty-one (21) and Sr-90 was positively identified in five (5) of the twenty-eight (28) samples.

Several other radionuclides, which were positively identified, could be de-selected or excluded using the 5% and 10% rule described in Section 5.4.7.2 of the LTP.

None of the sample results exceeded the Operational DCGL or required further investigation. A summary of the sample results is provided in Table 5.

DISCHARGE CANAL
SURVEY UNIT 9106-0015
RELEASE RECORD

Table 5- Summary of Sediment Sample Results

Sample Number	Cs-137 pCi/g	Co-60 pCi/g	Sr-90 pCi/g	Fraction of the Operational DCGL ⁽¹⁾	
				Nuclides of concern	Unity (Sign Test) ⁽²⁾
9106-0015-001F	2.560E-02	1.200E-02	2.480E-02	2.92E-02	8.33E-02
9106-0015-002F	5.220E-01	1.110E+00	-1.880E-02	4.54E-01	5.95E-01
9106-0015-003F	4.67E-02	1.42E-01	-3.33E-03	5.39E-02	1.08E-01
9106-0015-004F	-8.56E-03	9.74E-03	1.98E-02	1.86E-02	1.88E-02
9106-0015-005F	5.89E-02	9.29E-04	1.33E-02	2.13E-02	7.54E-02
9106-0015-006F	3.22E-01	3.50E-01	8.64E-03	1.82E-01	2.36E-01
9106-0015-007F	2.85E-01	3.55E-01	2.98E-03	1.72E-01	2.26E-01
9106-0015-008F	2.15E-01	3.49E-01	1.05E-02	1.65E-01	2.19E-01
9106-0015-009F	1.19E-02	3.23E-02	1.55E-02	2.61E-02	8.03E-02
9106-0015-010F	2.53E-01	0.00E+00	3.71E-03	4.52E-02	9.93E-02
9106-0015-011F	4.93E-01	3.96E-01	1.88E-02	2.34E-01	2.88E-01
9106-0015-012F	3.47E-01	6.55E-01	3.27E-03	2.86E-01	3.40E-01
9106-0015-013F	4.43E-01	7.05E-01	5.00E-03	3.21E-01	3.75E-01
9106-0015-014F	4.43E-02	4.32E-02	2.22E-02	4.09E-02	9.90E-02
9106-0015-015F	2.08E-01	7.07E-02	2.11E-02	7.67E-02	4.79E-02
9106-0015-016F	3.02E-01	1.01E-01	-2.59E-03	8.29E-02	1.37E-01
9106-0015-017F	4.74E-01	2.90E-01	4.49E-03	1.83E-01	2.37E-01
9106-0015-018F	3.54E-01	1.16E+00	-1.15E-02	4.49E-01	4.72E-01
9106-0015-019F	9.01E-02	2.38E-01	9.59E-03	1.05E-01	1.59E-01
9106-0015-020F	9.79E-02	2.03E-01	-8.28E-03	7.93E-02	1.33E-01
9106-0015-021F	3.98E-01	0.00E+00	-1.17E-02	5.64E-02	7.43E-02
9106-0015-022F	3.46E-01	6.97E-01	2.53E-03	3.00E-01	3.54E-01
9106-0015-023F	3.28E-01	1.06E+00	-1.20E-02	4.10E-01	4.64E-01
9106-0015-024F	6.71E-02	1.15E-01	2.52E-02	7.20E-02	1.03E-01
9106-0015-025F	1.17E-02	-3.63E-03	1.28E-02	1.15E-02	4.25E-02
9106-0015-026F	3.23E-01	5.75E-02	6.51E-03	7.90E-02	1.10E-01
9106-0015-027F	2.73E-01	1.39E-01	3.14E-03	9.60E-02	1.27E-01
9106-0015-028F	4.90E-03	-3.79E-03	-1.53E-02	-1.33E-02	1.77E-02

- (1) The Operational DCGLs from Table 2 are 6.01 pCi/g for Cs-137, 2.90 pCi/g for Co-60, 1.18 pCi/g for Sr-90; the Operational DCGL for C-14, a HTD radionuclide identified in one (1) or more FSS samples analyzed for HTD, is 4.30 pCi/g. These values were used in conjunction with the unity rule to achieve nineteen (19) mrem/yr TEDE.
- (2) This column is the sum of the DCGL unity fraction from identified radionuclides of concern and HTD isotope(s) exceeding the 5%/10% rule for one (1) or more FSS samples. For those samples not measured for HTD isotopes, an average calculated value of 3.1% of the DCGL was added to each sample.

The off-site laboratory also processed a total of five (5) samples, collected for non-parametric testing, for HTD analysis as required by the sample plan.

Sample number 9106-0007-017F was including in this report for the following reasons; because the sample result exceeded the Operational DCGL, the sample

DISCHARGE CANAL
SURVEY UNIT 9106-0015

RELEASE RECORD

result precipitated the creation of this survey unit, and as a part of the investigation relating to this sample to ensure that it complies the DCGL_{EMC} comparison Test of Section 5 of the LTP.

The analyses included alpha spectroscopy, gas proportional counting, and liquid scintillation depending on the radionuclide and the measurement method. All analyses met the required MDC.

Three (3) of the five (5) samples collected for non-parametric testing, and analyzed for HTD radionuclides, met the accepted criteria for detection (i.e., a result greater than two (2) standard deviations uncertainty. Each of the positive results for HTD radionuclides could be de-selected based on the 5% and 10% rules, with the exception of one (1) sample, 9106-0015-002F, which exceeded the 10% rule for a total of four (4) HTD radionuclides. Based on the HTD analyses, the maximum dose impact from these results was added to Table 5.

The HTD results are presented in Table 6.

Table 6 - Hard-to-Detect Sample Results					
Sample Number (9106-)	C-14 (pCi/g)	Tc-99 (pCi/g)	Am-241 (pCi/g)	Pu-241 (pCi/g)	Fraction of Operational DCGL ⁽¹⁾⁽²⁾
0015-002F	2.07E-01	3.90E-01	2.92E-01	2.46E+01	0.1409
0015-004F	8.18E-03	0.00E+00	0.00E+00	0.00E+00	0.0019
0015-015F	-1.24E-01	0.00E+00	0.00E+00	0.00E+00	-0.0288
0015-018F	5.72E-02	0.00E+00	1.93E-01	0.00E+00	0.0232
0015-021F	-4.90E-02	2.81E-01	0.00E+00	0.00E+00	0.0179
0007-017F ⁽³⁾	3.04E-02	1.20E-01	3.00E-03	-1.93E+00	0.0218

(1) The Operational DCGLs for C-14 is 4.30 pCi/g, Tc-99 is 9.58 pCi/g, Am-241 is 19.6 pCi/g, and Pu-241 is 661 pCi/g. These values were used in conjuncture with the unity rule to achieve nineteen (19) mrem/yr TEDE.

(2) This column is the sum of the DCGL unity fraction from identified HTD radionuclides identified in one (1) or more FSS samples.

(3) Sample number 9106-0007-017F was the initiating sample for the generation of this survey unit. This sample was analyzed for HTD radionuclides as part of the investigative process for an EMC. The results of the sample analyses of 9106-0007-017F were not included in the results of sample analyses conducted for non-parametric testing. (sample 9106-0007-017F was not taken as a part of the sample design for this survey unit).

7. QUALITY CONTROL

The three (3) split samples taken for QC were analyzed by the off-site laboratory. The data were evaluated using USNRC acceptance criteria specified in Inspection Procedure 84750 and as detailed in HNP Procedure RPM 5.1-24, "Split Sample Assessment for Final Status Survey."

DISCHARGE CANAL
SURVEY UNIT 9106-0015

RELEASE RECORD

One (1) split-sample (9106-0015-005F/S) did not meet the comparison criterion for Cs-137. A possible cause for this anomaly could be the presence of Cs-137 tightly bound to organic material in the sample aliquot. This distribution of material does not lend itself to homogenous mixing in a sediment matrix and, therefore, is not necessarily an indicator of inadequate sampling or sample preparation methodology. Additionally, since the resolution ratios for both Co-60 and Sr-90 were less than four (4), and the USNRC Inspection Procedure 84750 does not give guidance on resolution ratios below four (4), a determination on acceptability for such ratios can not be made. In this sample, K-40, a natural radioisotope, was found to be present at an acceptable level of agreement; therefore, the comparison was determined to be acceptable.

For the other two (2) QC split samples (9106-0015-012F/S & 9106-0015-018F/S), there was an acceptable level of agreement between the samples for Cs-137, Co-60 and K-40. However, the resolution ratio for Sr-90 was less than four (4), and the USNRC Inspection Procedure 84750 does not give guidance on resolution ratios below four (4), a determination on acceptability for such ratios can not be made.

The sample analysis vendor, GEL, maintained quality control and quality assurance plans as part of normal operation. Refer to Attachment 2 for data and data quality analysis results.

8. INVESTIGATIONS AND RESULTS

One (1) sample result, that led to the creation of this survey unit, was found to exceed the Operational DCGL of nineteen (19) mrem/yr, exceeding the investigation level from Table 4. Thus an investigation was required to determine compliance with Equation 3 of Section 3.

The first step in determining whether compliance with the EMC unity rule is to determine the area extent of the elevated measurement region. This was done by taking investigation samples at a distance of one (1) meter in each of the four (4) compass directions about the elevated sample point (9106-0007-017F). When these sample results were determined to be below the investigation levels specified in Table 4, the area was said to be bounded.

The area of the elevated measurement location (also the area used to determine area factors) was conservatively calculated by assuming the area was a circle with a radius equal to the most distant bounding measurement location. This was done using actual GPS log data. This was the most prudent approach since maneuvering the sampling vessel to obtain samples within such closely spaced locations imposes unusually high positioning precision. Table 7 provides sample measurement location information (in NAD 1927) and distances from sample location 9106-0007-017F.

DISCHARGE CANAL
SURVEY UNIT 9106-0015
RELEASE RECORD

Table 7 – Investigation Sample Measurement Locations with Associated GPS Coordinates			
Designation	Northing	Easting	Distance from 9106-0007-017F (m)
9106-0007-017F	235080.50	672486.69	-
9106-0015-017A	235083.20	672486.95	0.827309
9106-0015-017B	235080.67	672489.39	0.825131
9106-0015-017C	235076.99	672487.21	1.082234
9106-0015-017D	235081.57	672483.02	1.165954
Area (m ²)			4.3

Since the bounded area was determined to be 4.3 m², the Area Factor (AF) values from Table 5-5 of the LTP for six (6) m² were conservatively applied to determine the DCGL_{EMC} for each nuclide. With this information, it is possible to assess compliance with the EMC rule. This is demonstrated in Table 8. A map of the investigative sample locations is provided in Figure 6 of Attachment 1.

Table 8- Investigation Results				
Sample Number	Cs-137 pCi/g	Co-60 pCi/g	Sr-90 pCi/g	Fraction of the Operational DCGL
Area Factor (6 m ²)	7.01	3.29	211	Nuclides of concern ⁽¹⁾
DCGL _{EMC}	4.21E+01	9.53E+00	2.49E+02	
0007-017F	6.42E-01	3.09E+00	8.94E-03	
0015-017A	3.65E-01	1.02E+00	-1.08E-02	
0015-017B	1.92E-01	3.57E-01	3.32E-03	
0015-017C	1.95E-01	2.45E-01	4.84E-03	
0015-017D	3.13E-01	8.95E-01	-3.67E-03	
δ	2.26E-01	2.96E-01	5.37E-03	
Fraction of the DCGL _{EMC}				
$\bar{C}_{elevated}$	3.41E-01	1.12E+00	5.26E-04	Nuclides of concern ⁽¹⁾
$\bar{C}_{elevated} - \delta$	1.15E-01	8.26E-01	-4.84E-03	
$\frac{\bar{C}_{elevated} - \delta}{DCGL_{EMC}}$	2.74E-03	8.67E-02	-1.95E-05	
Hard-to-Detect (HTD) Results⁽²⁾				3.10E-02
Total				2.64E-01

(1) This represents the unity fraction of the DCGL from nuclides that are considered nuclides of concern (Cs-137, Co-60 and Sr-90) from the FSS plan.

(2) This represents the unity fraction of the DCGL from HTD nuclides that were not considered nuclides of concern from the FSS plan, and represents an increase of 3.1%. These values were not subtracted from the mean activity of the elevated area, which is conservative.

DISCHARGE CANAL
SURVEY UNIT 9106-0015

RELEASE RECORD

9. REMEDIATION AND RESULTS

Historically, no radiological remedial action as described by MARSSIM Section 5.4 was performed in this survey unit prior to or as a result of the FSS. Health Physics TSD BCY-HP-0078, "*ALARA Evaluation of Soil Remediation in Support of Final Status Survey*," determined that remediation beyond that required to meet the release criteria to be unnecessary and that the remaining residual radioactivity in soil was ALARA.

10. CHANGES FROM THE FINAL STATUS SURVEY PLAN

The survey was designed to ten (10) mrem/yr TEDE which was conservative and necessary at the time of FSS planning. It is no longer required as the total dose from existing and future groundwater has been established. The dose for soil used to demonstrate compliance with the LTP and CTDEP criteria is nineteen (19) mrem/yr TEDE as discussed in Section 2 of this Release Record.

11. DATA QUALITY ASSESSMENT (DQA)

The DQO sample design and data were reviewed in accordance with Procedure RPM 5.1-23, "*Data Quality Assessment*." The sample design had adequate power as indicated by the Retrospective Power Curve. The Sign Test was performed on the data and compared to the original assumptions of the DQOs. The evaluation of the Sign Test results indicates that the survey unit passes the unrestricted release criterion, thus, the null hypothesis is rejected.

Documentation was complete and legible. Surveys and sample collection were consistent with the DQOs and were sufficient to ensure that the survey unit was properly designated as Class 1.

The preliminary data review consisted of calculating basic statistical quantities (e.g., mean, median, standard deviation). The standard deviation was slightly more than the value used for the survey design. This is represented by the shift in the retrospective power curve as shown in Attachment 2f. This would indicate a need to change the original LBGR in order to maintain the number of samples at twenty-eight (28) to meet the Operational DCGL. However, the value of LBGR is not a critical issue as the survey unit has passed the statistical test, and the mean and median values are well below the Operational DCGL when used in conjunction with the unity rule. Also, the retrospective power curve shows that a sufficient number of samples were collected to achieve the desired power. Therefore, the survey unit meets the unrestricted release criterion with adequate power as required by the DQOs

The range of the data, about 3.47 standard deviations, was not unusually large. The difference between the mean and median was 42.2% of the standard deviation which indicates some skewness in the data. The data was represented graphically through posting plots, a frequency plot, and a quantile plot. The frequency plot shows some positive skewness as confirmed by the calculated skew of 1.09.

DISCHARGE CANAL
SURVEY UNIT 9106-0015

RELEASE RECORD

The survey area had one (1) elevated measurement location, which was evaluated using the unity EMC test. This resulted in a passing value of 0.264, which is significantly below unity.

All data, assessments, and graphical representations are provided in Attachment 2.

12. ANOMALIES

The anomalies associated with a disagreement on one (1) of the field splits has been discussed in Section 7. The source of the disagreement for Cs-137 is believed to be due to Cs-137 being tightly bound to organic materials in the sample media. Such a physical form does not lend itself to homogenous mixing in a sediment matrix.

13. CONCLUSION

Survey Unit 9106-0015 has demonstrated compliance with the dose based, unrestricted release criterion. The sample data passed the Sign Test and the null hypothesis was rejected. The ALARA criteria for soils as specified in Chapter 4 of the LTP were achieved. Reclassification and remediation of this survey unit was not required.

Graphical representation of data indicates some positive skewness that is probably due to localized differences in particulate deposition rates, hydraulic velocity and sedimentation rates. The Retrospective Power Curve generated using COMPASS shows adequate power was achieved. The survey unit was properly designated as a Class 1 survey unit.

The dose contribution from sediment in this survey unit is 3.1 mrem/yr TEDE based on the average concentration of the samples used for non-parametric statistical sampling.

This survey unit is not affected by existing groundwater (reference CY memo ISC 06-024). It has been determined that the dose contribution from groundwater sources is bounded by zero (0) mrem/yr TEDE.

This survey unit is not considered impacted by future groundwater radioactive contamination, as there are no concrete foundations or footings containing residual radioactive material within the groundwater saturated zone in the area (reference CY memo ISC 06-024). The dose contribution from future groundwater, the third dose component is, therefore, zero (0) mrem/yr TEDE.

The average total dose from residual radioactivity in this survey unit, including exposures from the three (3) components as described in Section 3, that is, residual radioactivity in soil, existing groundwater radioactivity, and future groundwater radioactivity from the burial of concrete foundations or footings from site buildings containing residual radioactivity, will not exceed 3.1 mrem/yr Total Effective Dose Equivalent (TEDE).

DISCHARGE CANAL
SURVEY UNIT 9106-0015
RELEASE RECORD


14. ATTACHMENTS

14.1 Attachment 1 – Figures

14.2 Attachment 2 – Sample and Statistical Data

DISCHARGE CANAL
SURVEY UNIT 9106-0015
RELEASE RECORD

Attachment 1
Figures
(9 pages)

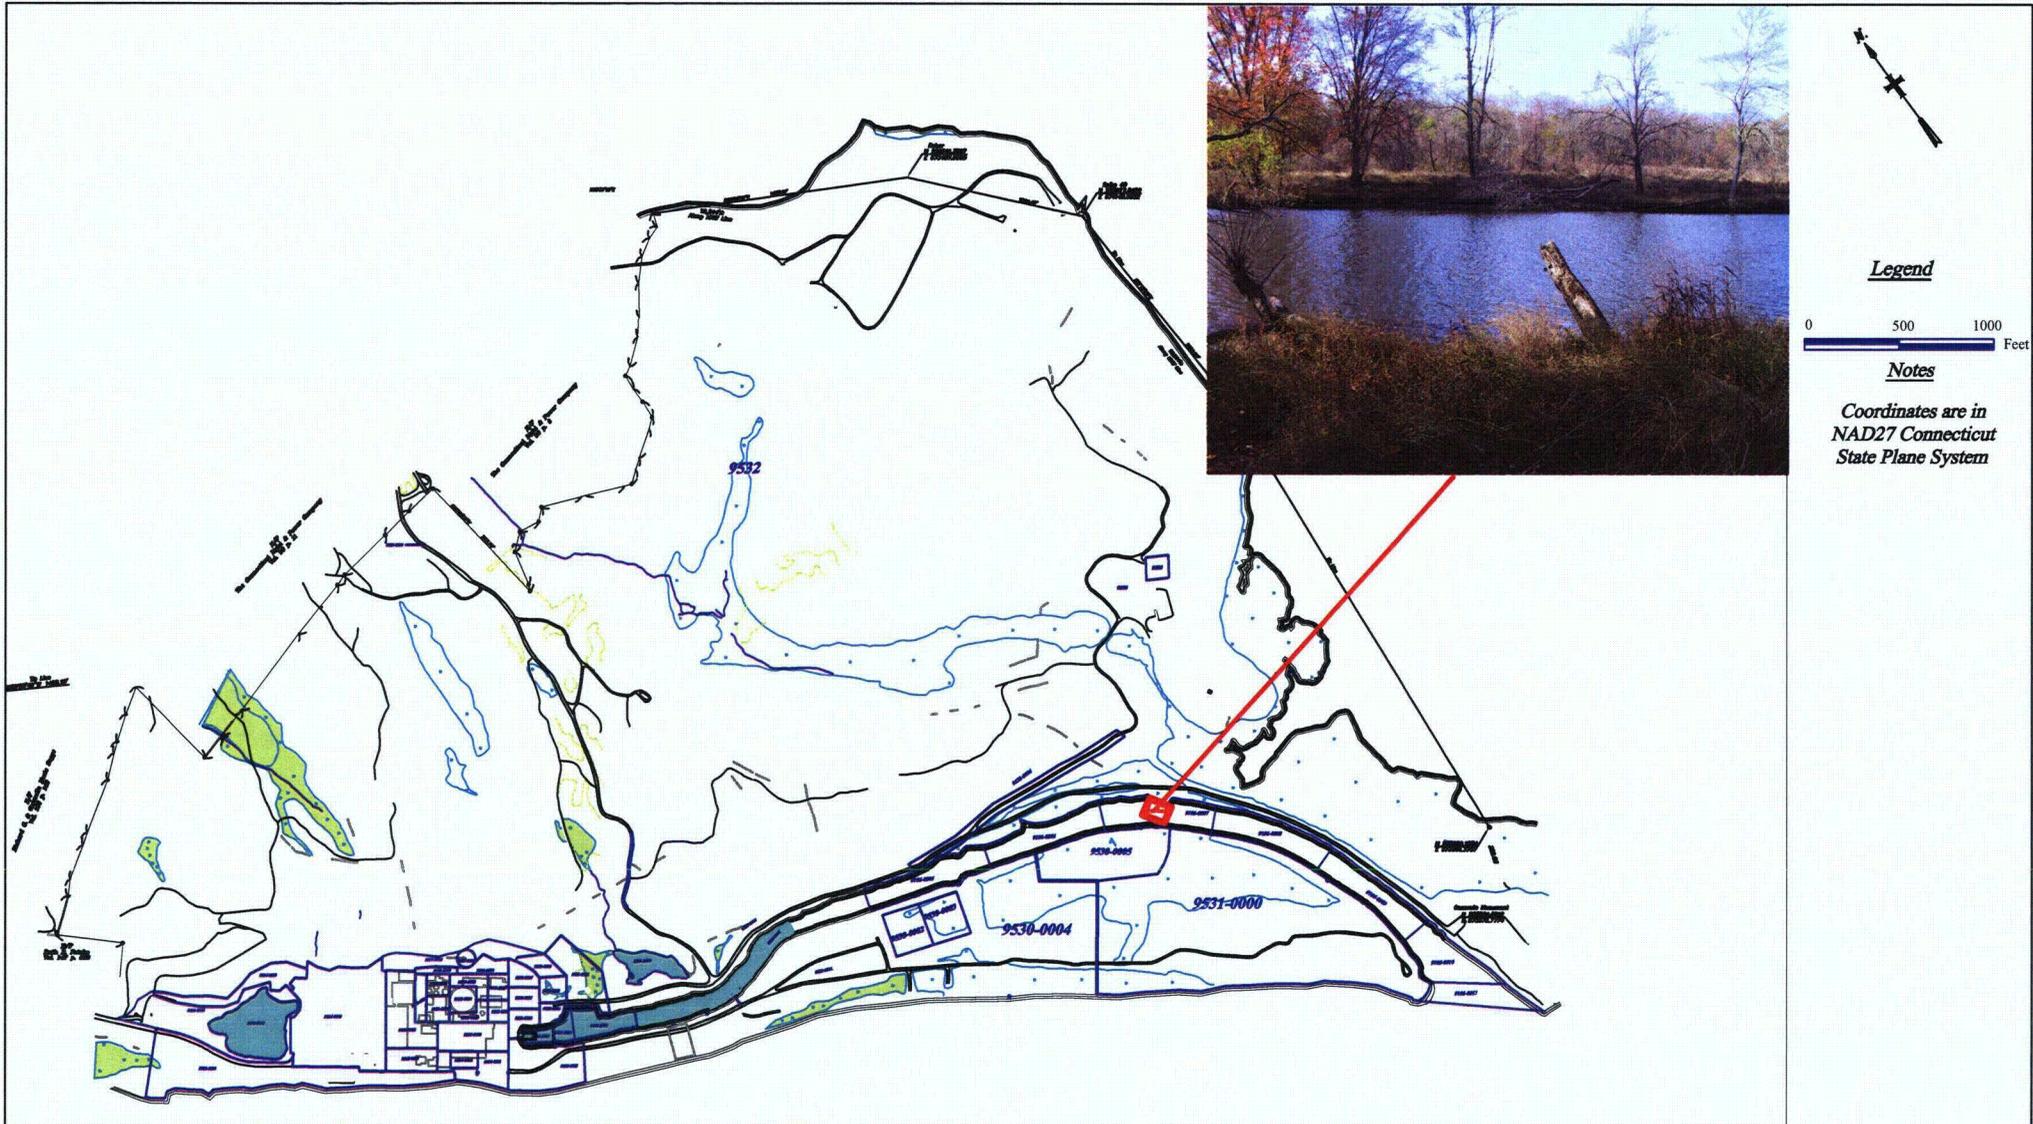

Legend

0 500 1000 Feet

Notes

Coordinates are in
NAD27 Connecticut
State Plane System

Date: November 2006

Revision: 0

Figure 1

Connecticut Yankee Atomic Power Company
9106-0015 Final Status Survey Design

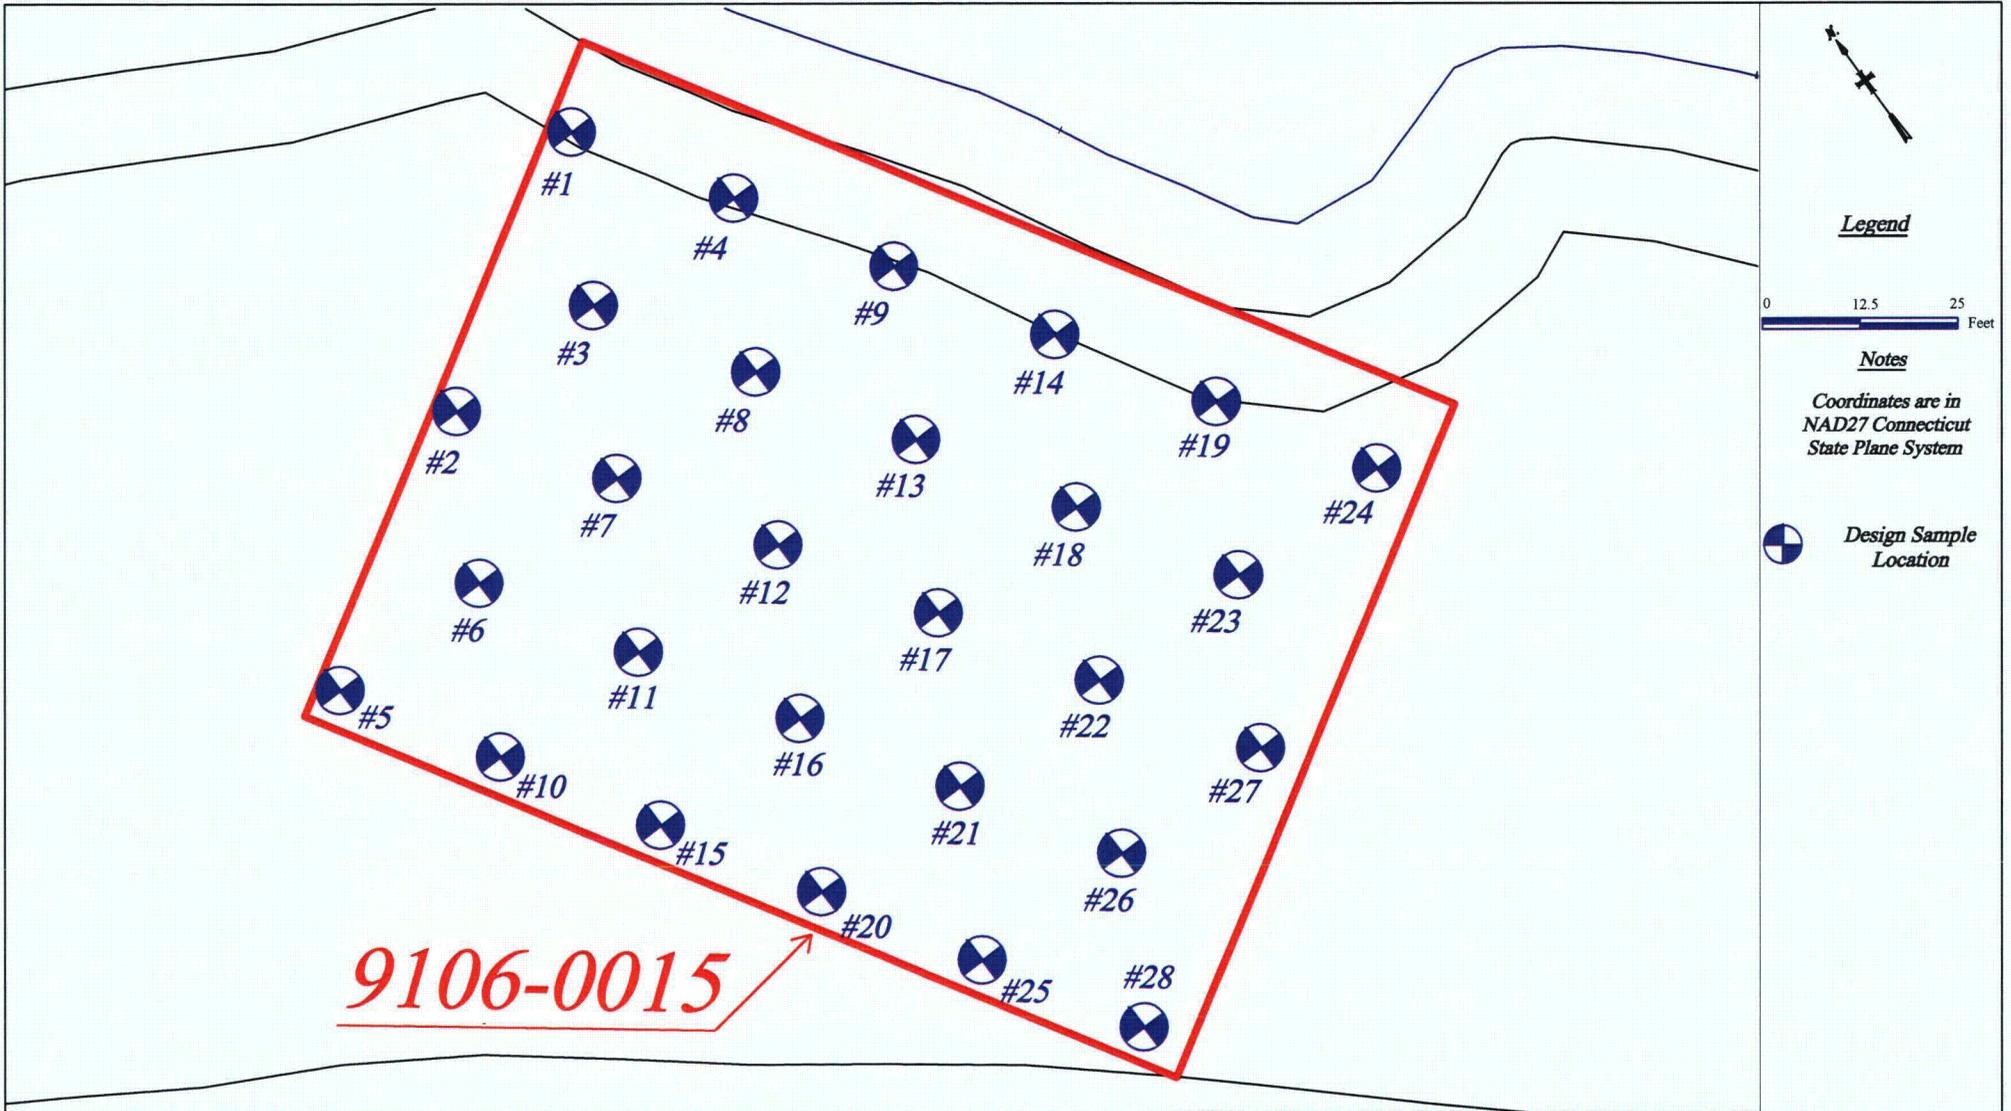


Figure 2

Connecticut Yankee Atomic Power Company
 9106-0015 Final Status Survey Design

Date: November 2006

Revision: 0


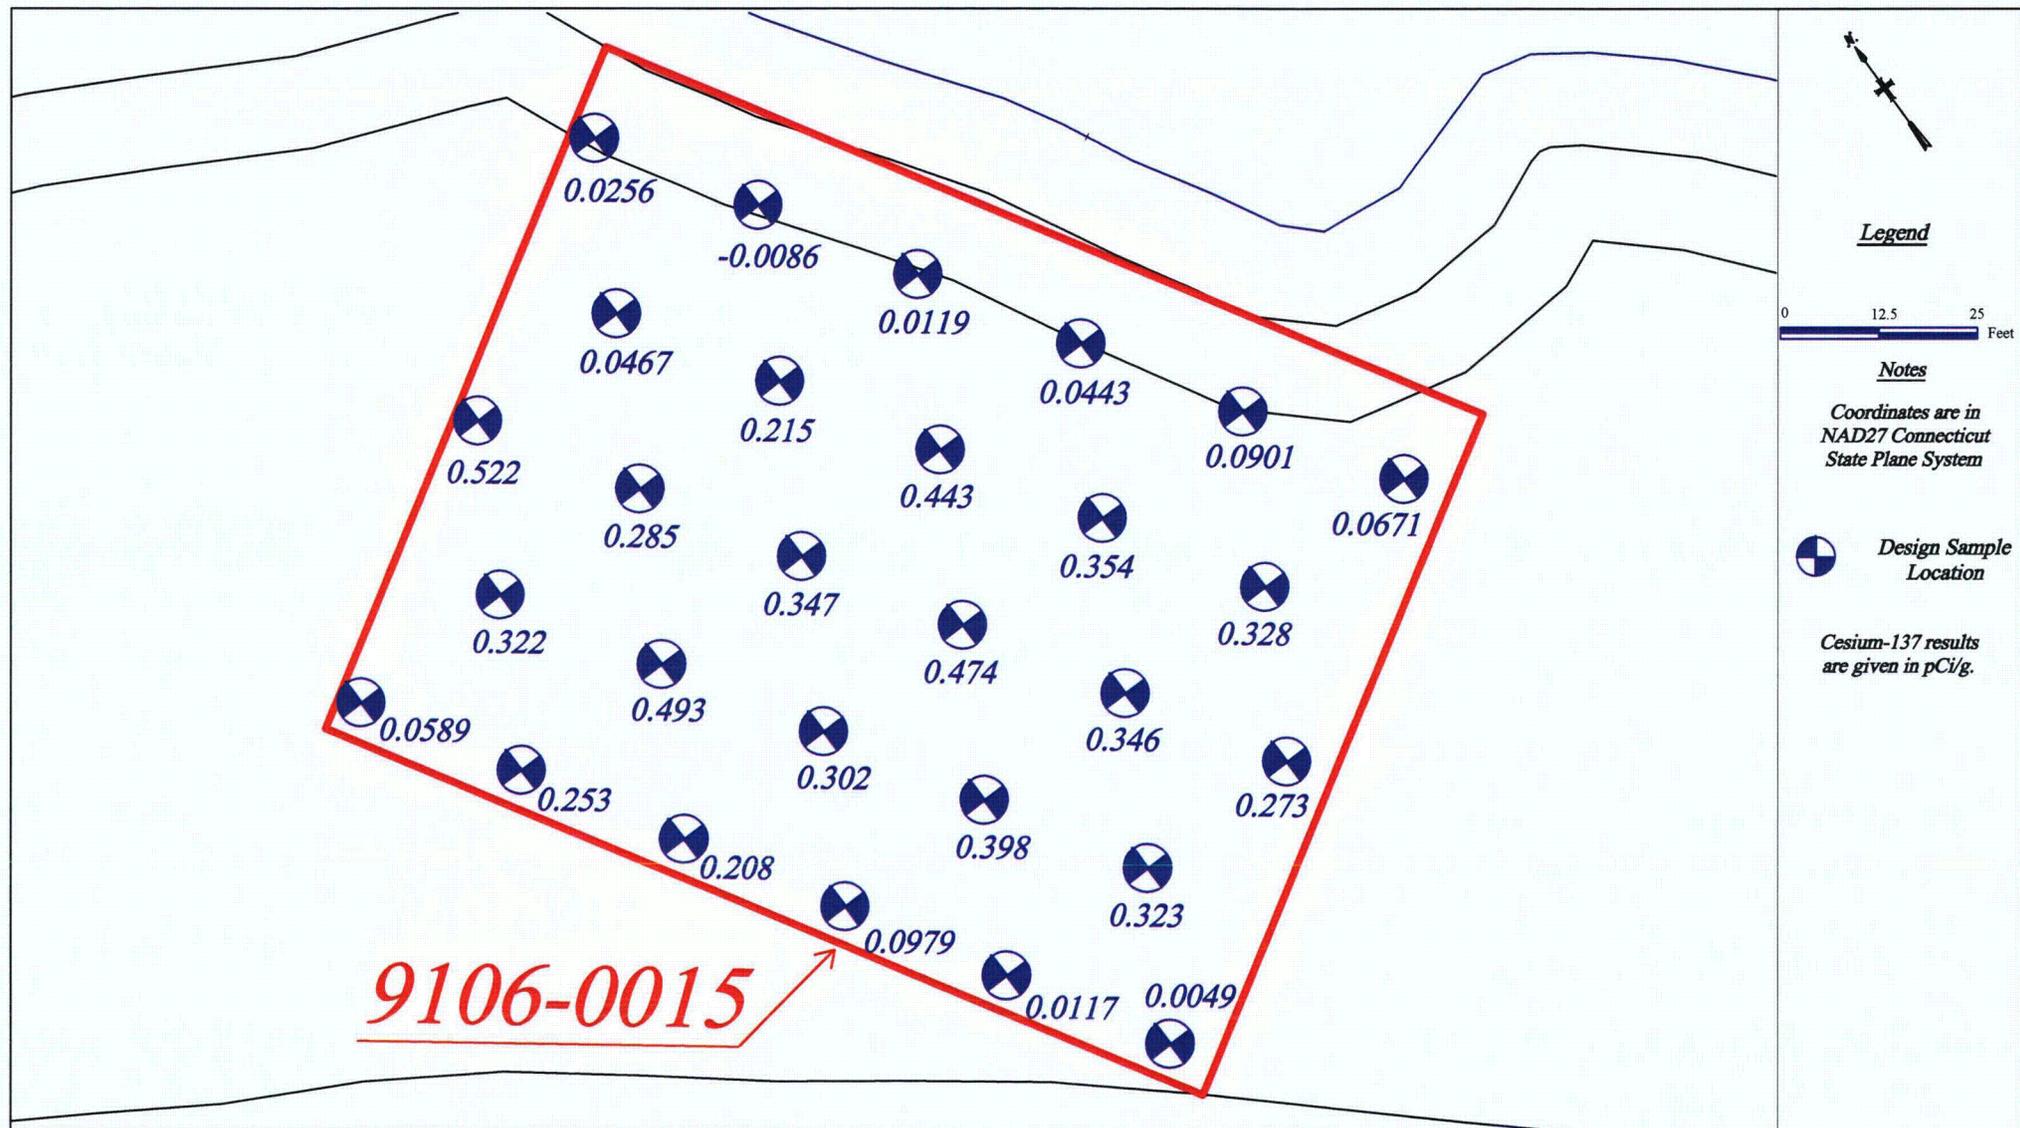


Figure 3

Connecticut Yankee Atomic Power Company
 9106-0015 Final Status Survey
 Cesium-137 Posting Plot

Date: November 2006

Revision: 0

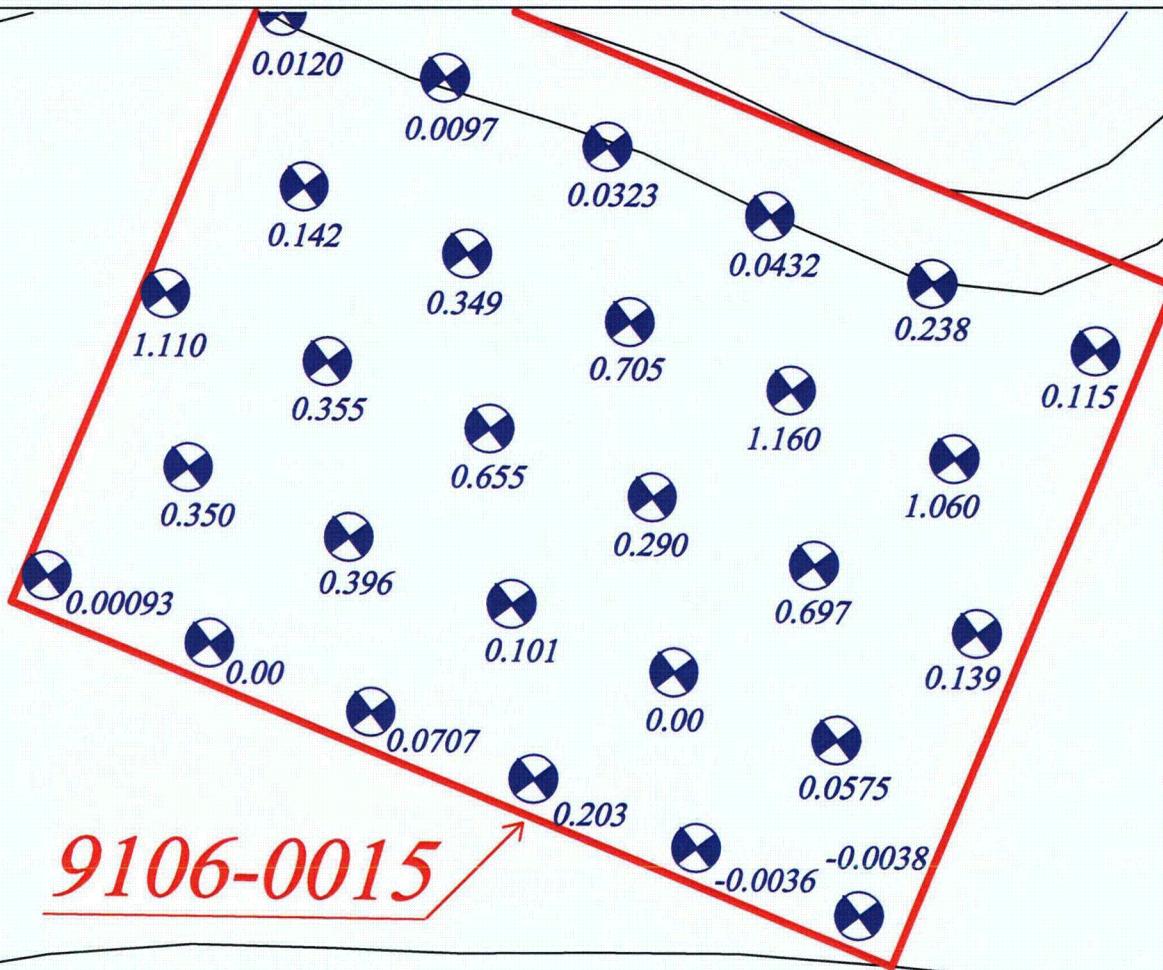

Legend



Notes

Coordinates are in NAD27 Connecticut State Plane System

Design Sample Location


Cobalt-60 results are given in pCi/g.

Figure 4


Connecticut Yankee Atomic Power Company
 9106-0015 Final Status Survey
 Cobalt-60 Posting Plot

Date: November 2006

Revision: 0

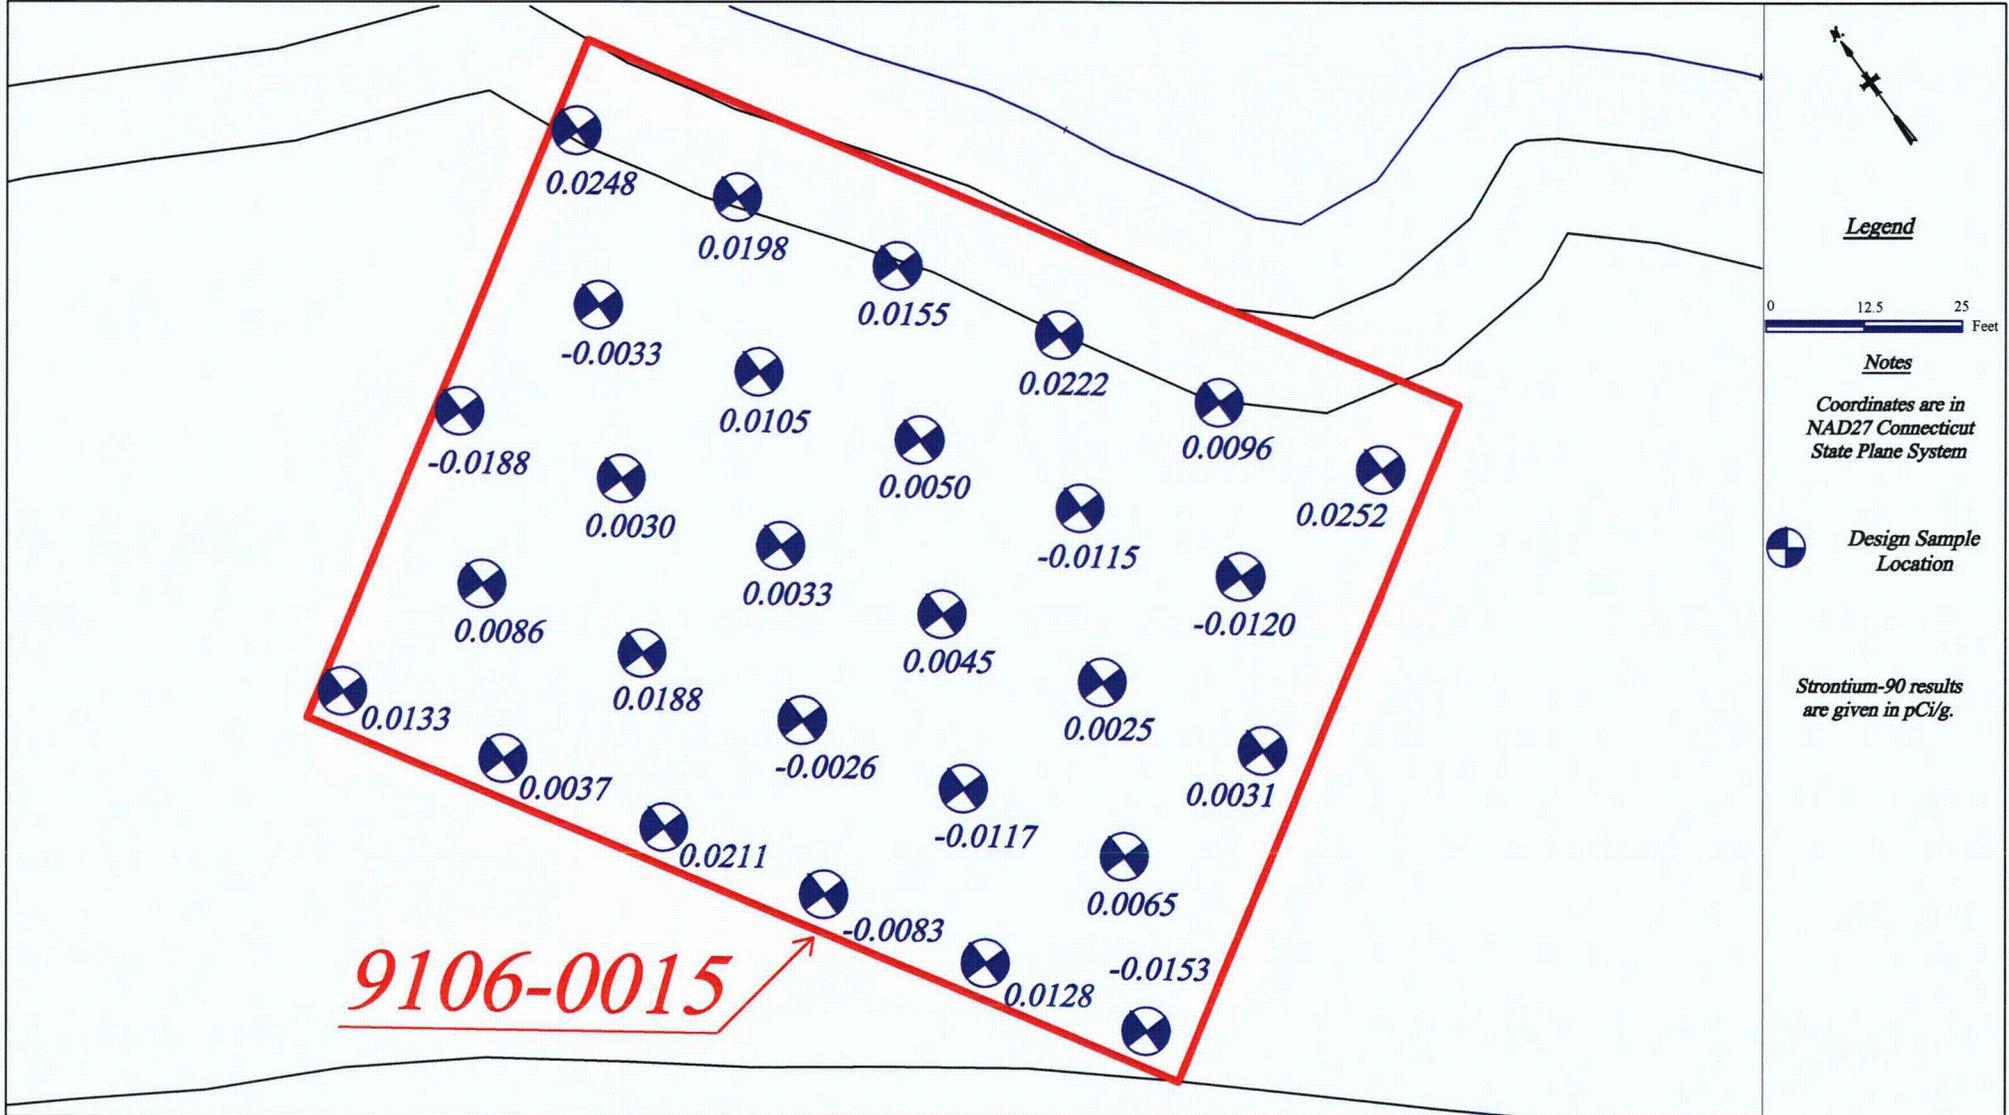

Legend



Notes

Coordinates are in NAD27 Connecticut State Plane System

Design Sample Location


Strontium-90 results are given in pCi/g.


Figure 5


Connecticut Yankee Atomic Power Company
 9106-0015 Final Status Survey
 Strontium-90 Posting Plot


Date: November 2006

Revision: 0

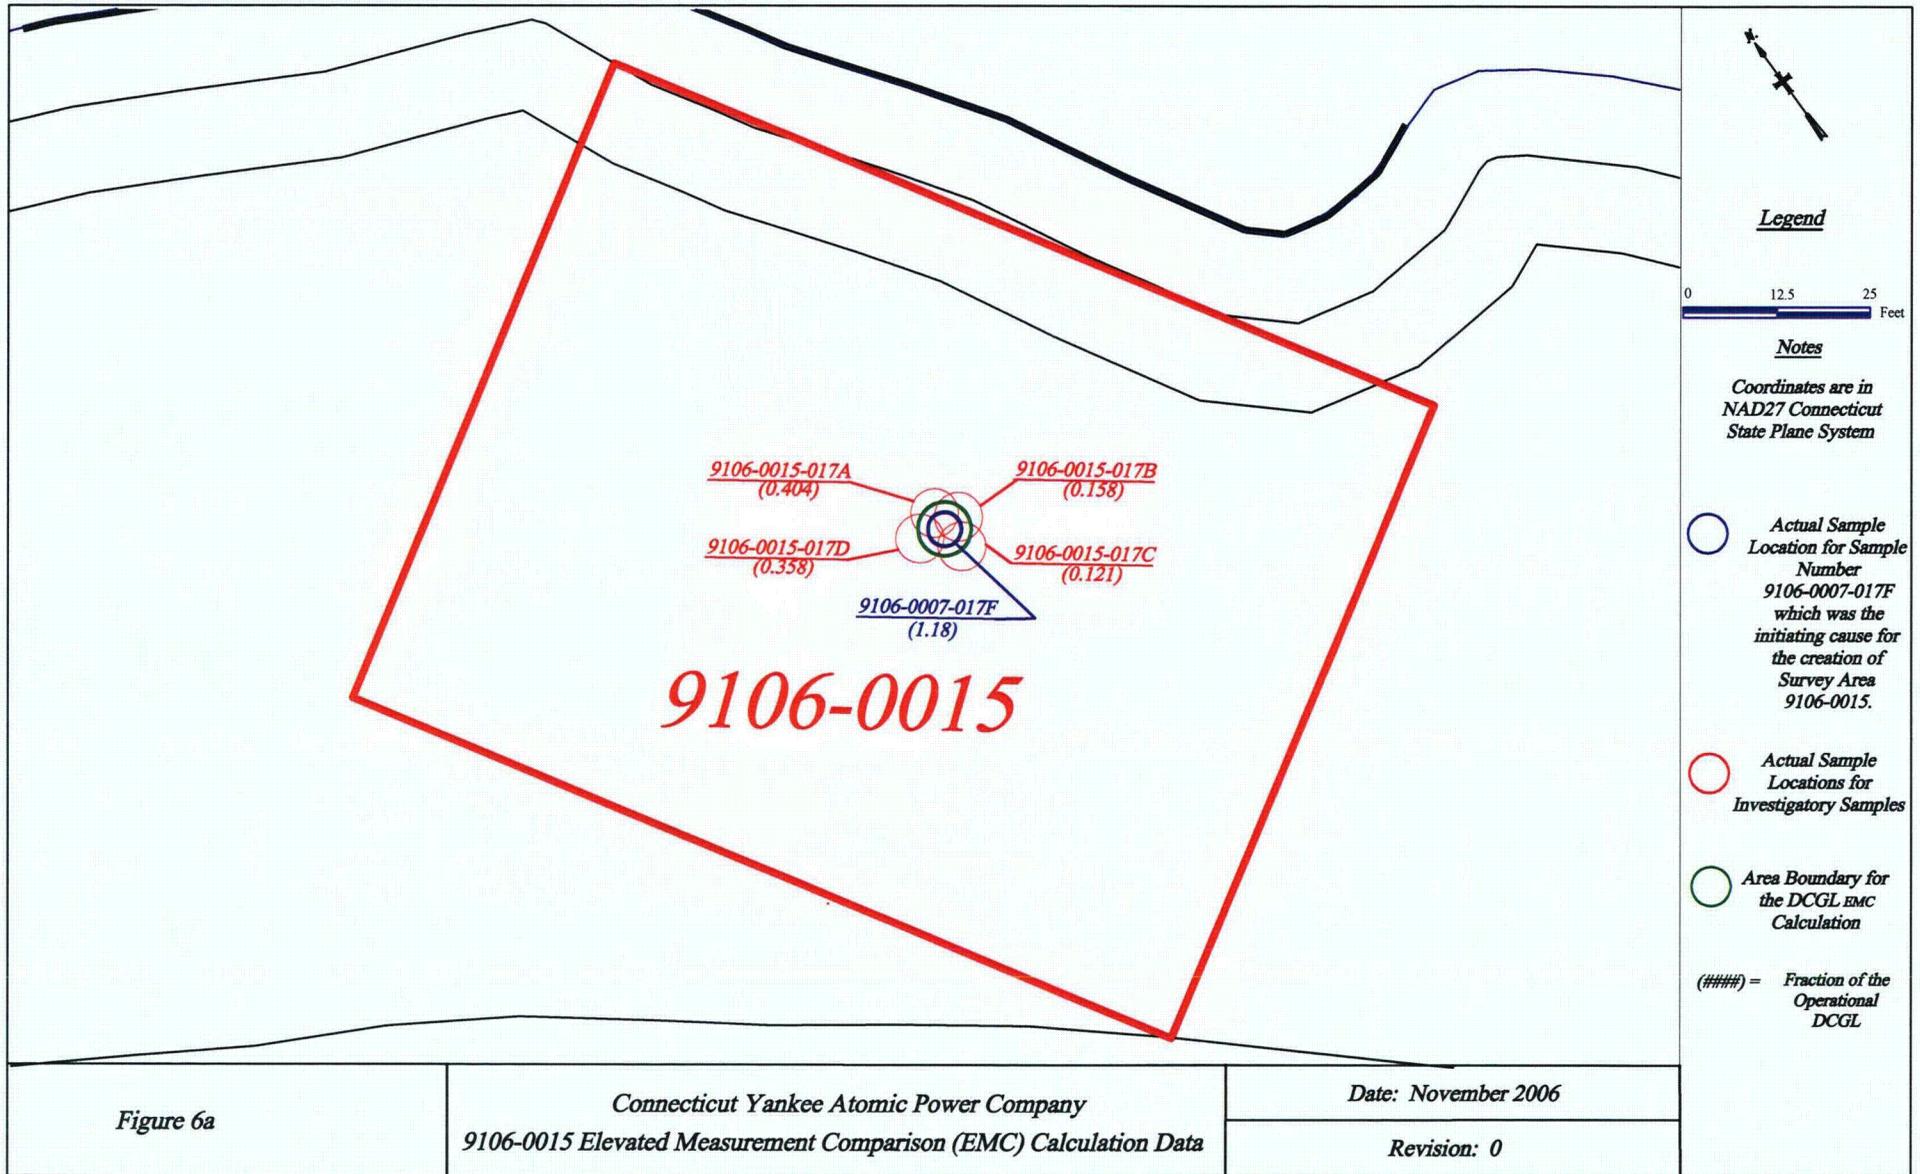

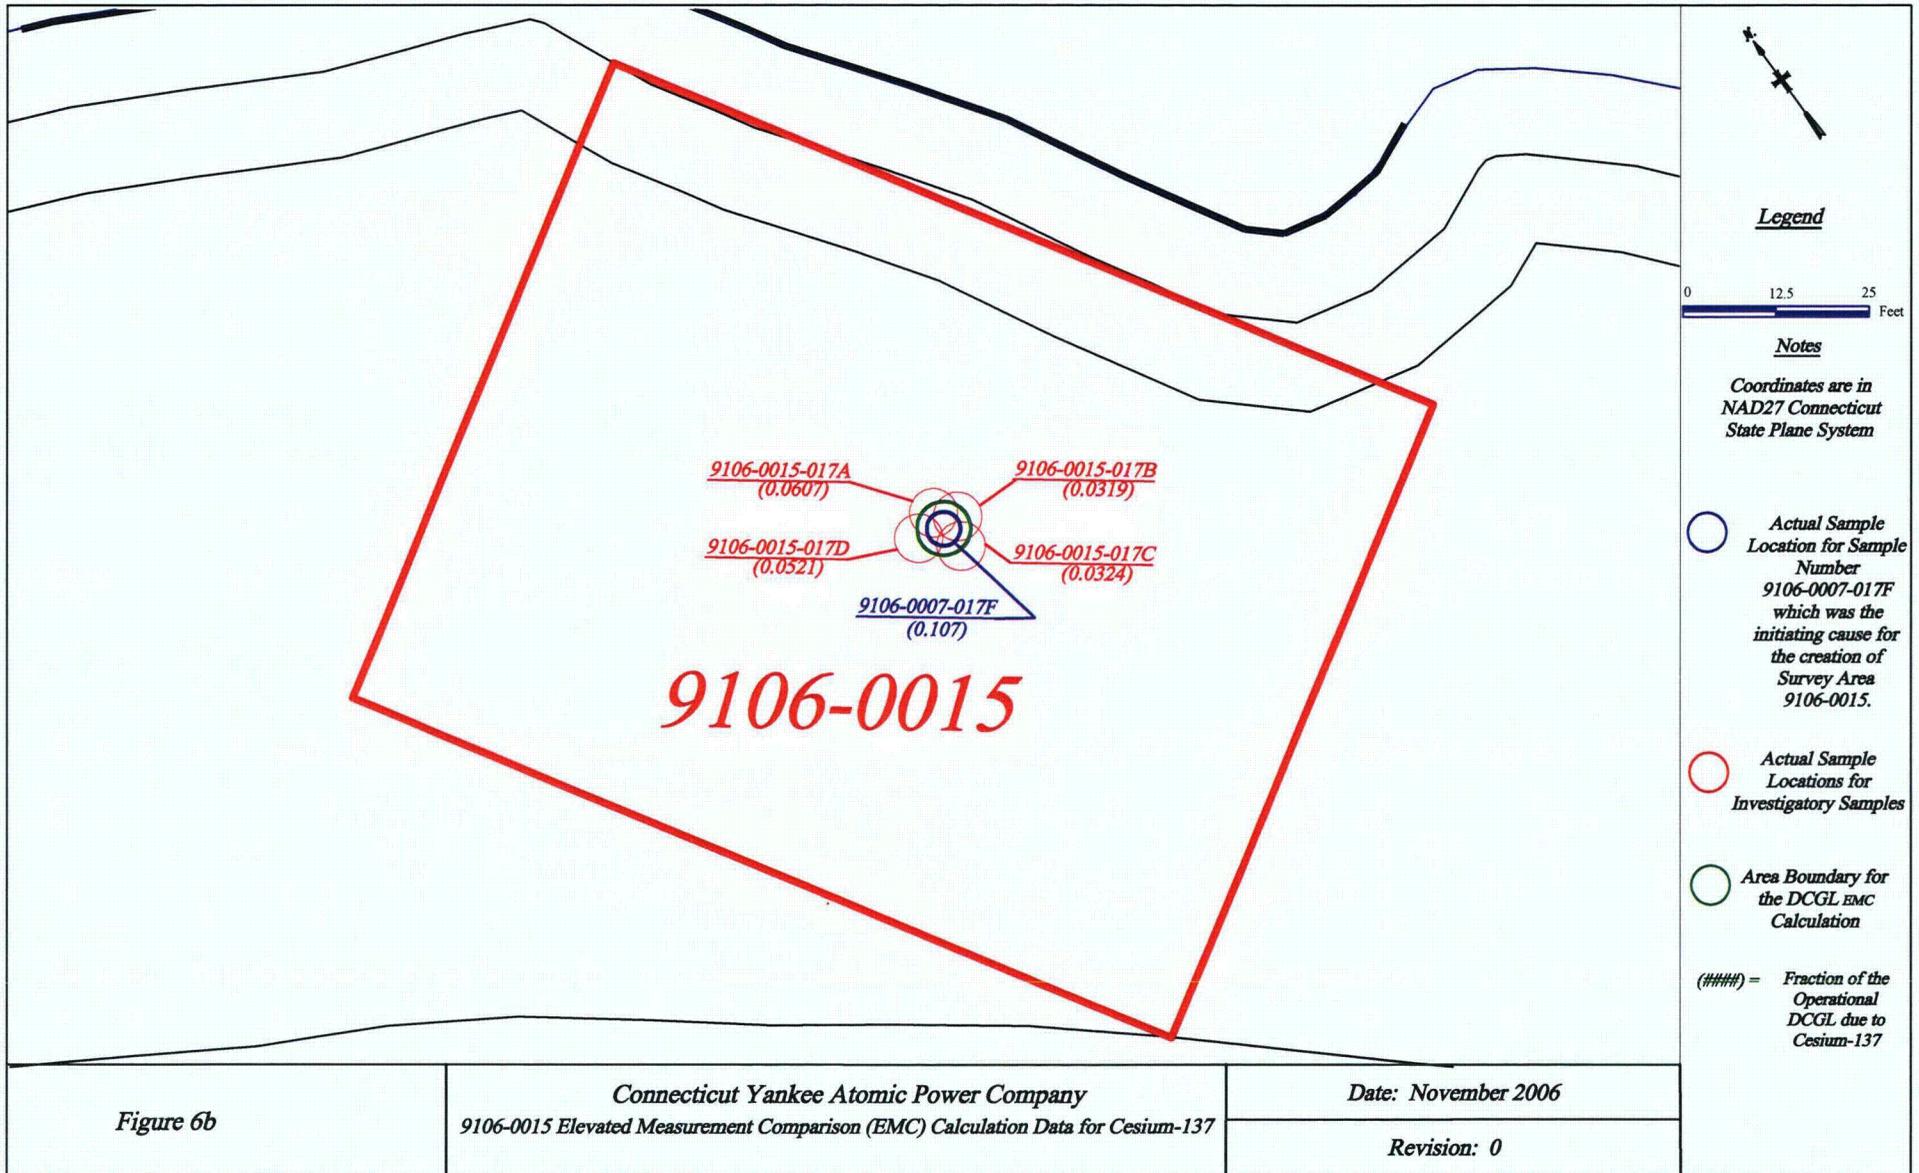

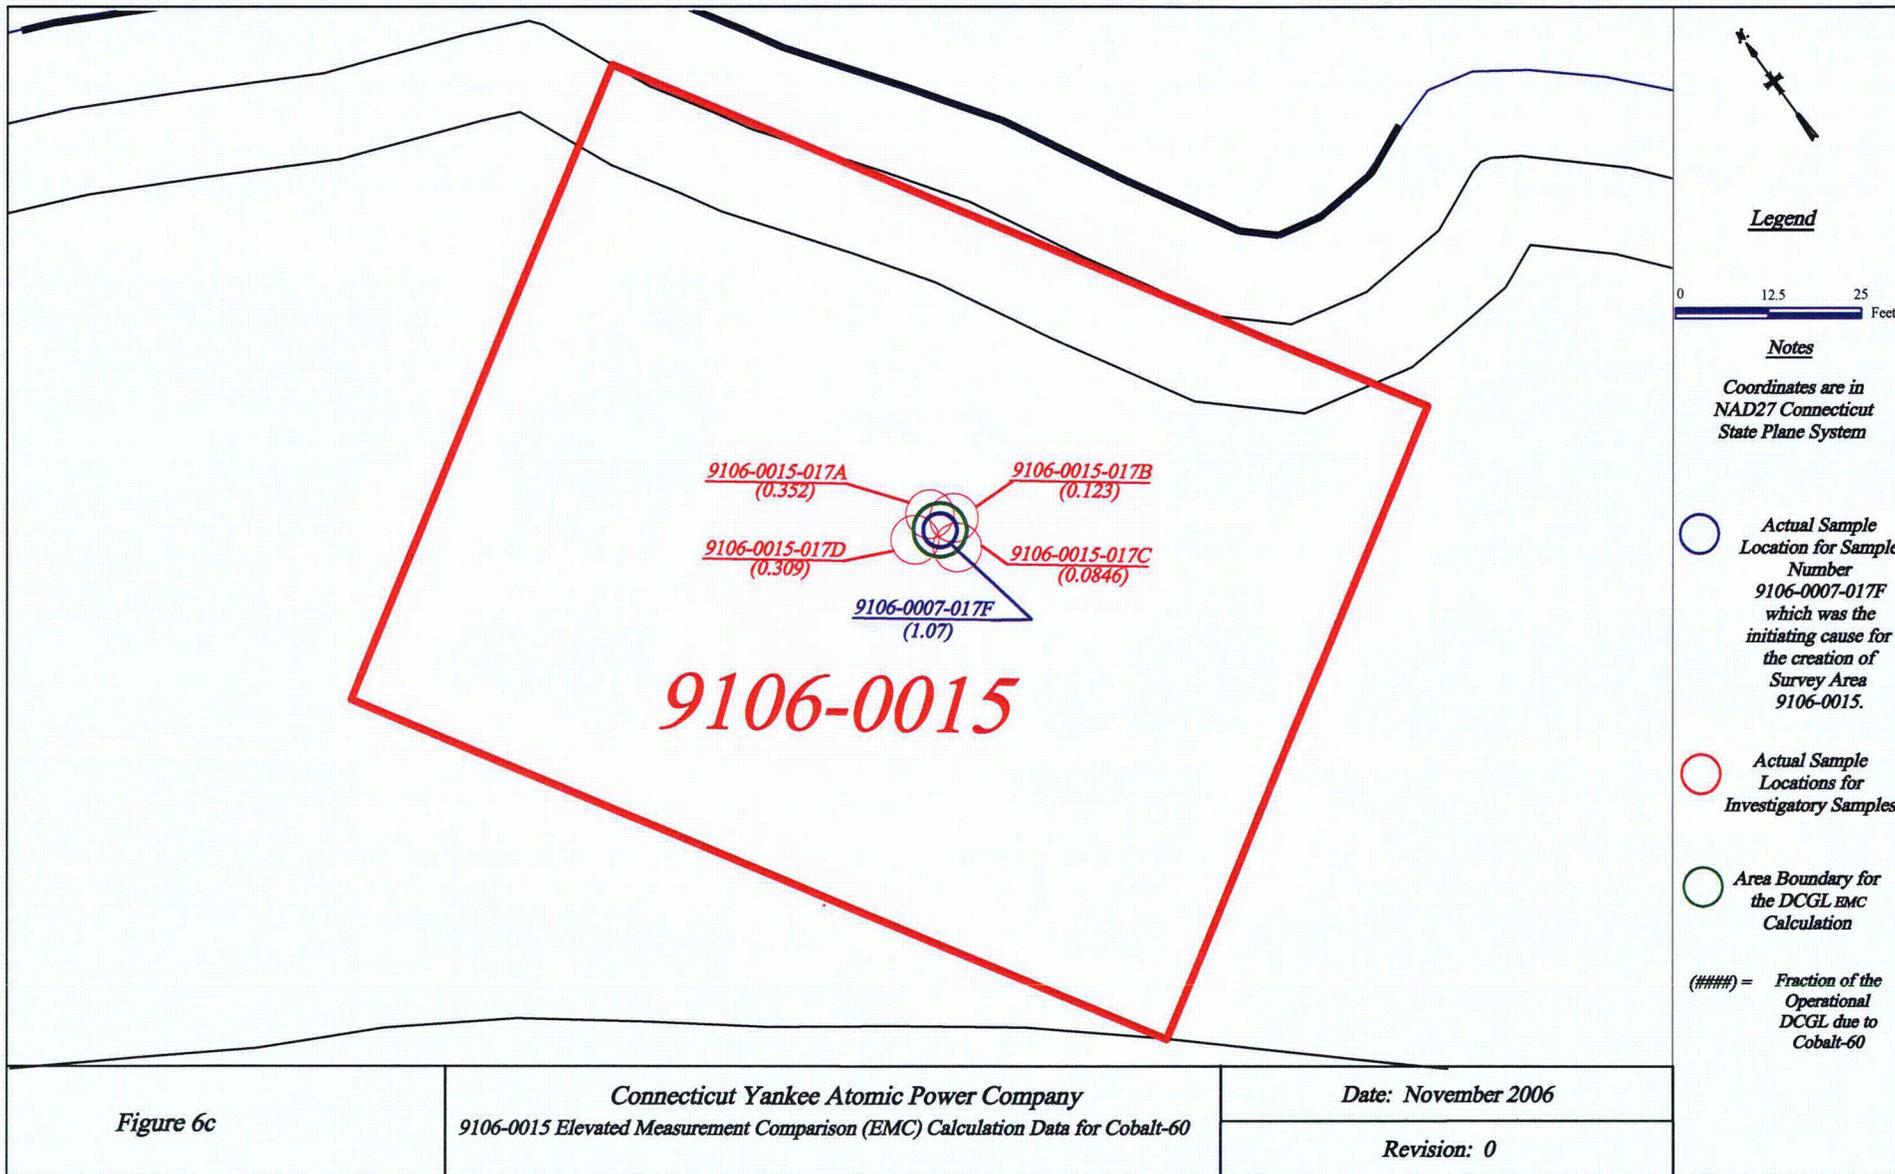

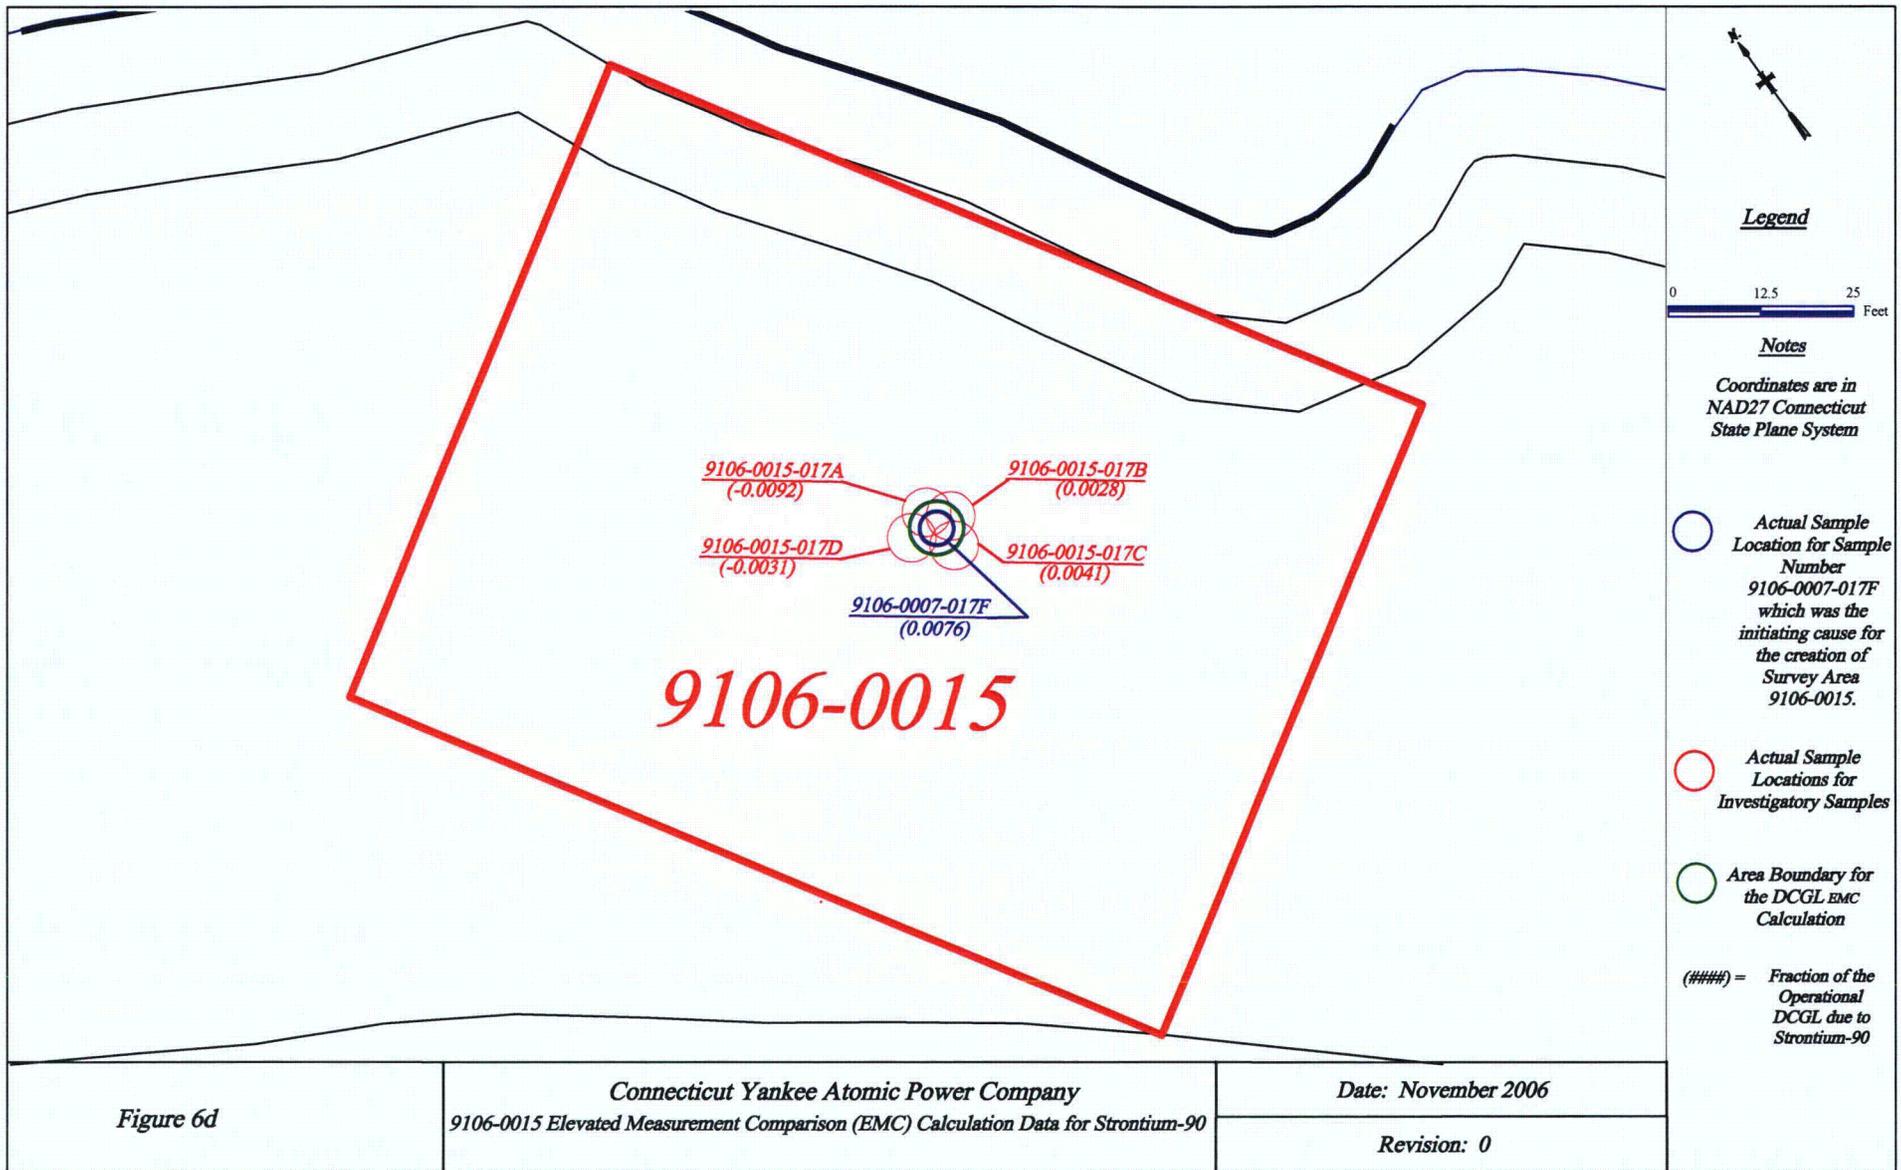

DISCHARGE CANAL
SURVEY UNIT 9106-0015
RELEASE RECORD

Attachment 2
Sample and Statistical Data

DISCHARGE CANAL
SURVEY UNIT 9106-0015
RELEASE RECORD

Attachment 2a
Sample Data
(294 Pages)

Table of Contents

General Narrative	1
Chain of Custody and Supporting Documentation	5
Radiological Analysis	13
Sample Data Summary	37
Quality Control Data	104

General Narrative

CASE NARRATIVE
For
CONNECTICUT YANKEE
RE: Soil
PO# 002332
Work Order: 167556
SDG: MSR #06-1037

August 2, 2006

Laboratory Identification:

General Engineering Laboratories, LLC

Mailing Address:

P.O. Box 30712
Charleston, South Carolina 29417

Express Mail Delivery and Shipping Address:

2040 Savage Road
Charleston, South Carolina 29407

Telephone Number:

(843) 556-8171

Summary:

Sample receipt

The sample(s) for this Project arrived at General Engineering Laboratories, LLC, (GEL) in Charleston, South Carolina on July 21, 2006. All sample containers arrived without any visible signs of tampering or breakage. The chain of custody contained the proper documentation and signatures.

The laboratory received the following sample(s):

<u>Sample ID</u>	<u>Client Sample ID</u>
167556001	9106-0015-022F
167556002	9106-0015-023F
167556003	9106-0015-024F
167556004	9106-0015-026F
167556005	9106-0015-027F
167556006	9106-0015-028F
167556007	9106-0015-018F
167556008	9106-0015-025F
167556009	9106-0015-001F

167556010	9106-0015-002F
167556011	9106-0015-003F
167556012	9106-0015-005F
167556013	9106-0015-006F
167556014	9106-0015-007F
167556015	9106-0015-008F
167556016	9106-0015-009F
167556017	9106-0015-010F
167556018	9106-0015-011F
167556019	9106-0015-012F
167556020	9106-0015-013F
167556021	9106-0015-014F
167556022	9106-0015-016F
167556023	9106-0015-017F
167556024	9106-0015-019F
167556025	9106-0015-020F
167556026	9106-0015-005FS
167556027	9106-0015-012FS
167556028	9106-0015-018FS
167556029	9106-0015-021F
167556030	9106-0015-004F
167556031	9106-0015-015F

Items of Note:

There are no items of note.

Case Narrative:

Sample analyses were conducted using methodology as outlined in General Engineering Laboratories (GEL) Standard Operating Procedures. Any technical or administrative problems during analysis, data review, and reduction are listed below by analytical parameter.

Analytical Request:

Twenty-eight soil samples were analyzed for FSSGAM and Sr-90.
Three soil samples were analyzed for FSSALL.

Internal Chain of Custody:

Custody was maintained for the sample(s).

Data Package:

The enclosed data package contains the following sections: Case Narrative, Chain of Custody and Supporting Documentation and all analytical fractions.

I certify that this data package is in compliance with the SOW, both technically and for completeness, for other than the conditions detailed above. Release of the data contained in this hard copy data package has been authorized by the Laboratory Manager or a designee, as verified by the following signature.



Cheryl Jones
Project Manager

**Chain of Custody
and
Supporting
Documentation**

167556/.

Connecticut Yankee Atomic Power Company 362 Injun Hollow Road, East Hampton, CT 06424 860-267-2556						Chain of Custody Form					No. 2006-00443		
Project Name: Haddam Neck Decommissioning			Media Code	Sample Type Code	Container Size- & Type Code	Analyses Requested					Lab Use Only		
Contact Name & Phone: Jack McCarthy 860-267-3924						FSSGAM	FSSALL	Sr-90	Ni-63				Comments:
Analytical Lab (Name, City, State) General Engineering Laboratories 2040 Savage Road, Charleston SC. 29407 843 556 8171. Attn. Cheryl Jones													
Priority: <input type="checkbox"/> 30 D. <input checked="" type="checkbox"/> 14 D. <input type="checkbox"/> 7 D.													
Sample Designation	Date	Time	Media Code	Sample Type Code	Container Size- & Type Code	FSSGAM	FSSALL	Sr-90	Ni-63			Comment, Preservation	Lab Sample ID
1) 9106-0015-022F	6-27-06	16:24	SE	C	BP	X		X					
2) 9106-0015-023F	6-27-06	16:03	SE	C	BP	X		X					
3) 9106-0015-024F	6-27-06	15:42	SE	C	BP	X		X					
4) 9106-0015-026F	6-27-06	14:58	SE	C	BP	X		X					
5) 9106-0015-027F	6-27-06	15:17	SE	C	BP	X		X					
6) 9106-0015-028F	6-27-06	14:31	SE	C	BP	X		X					
7) 9106-0015-018F	6-27-06	17:18	SE	C	BP	X		X					
8) 9106-0015-025F	6-27-06	16:43	SE	C	BP	X		X					
9) 9106-0015-021F	6-27-06	17:01	SE	C	BP		X						

NOTES: PO #: 002332 MSR #: 06-1037 SSWP#NA <input checked="" type="checkbox"/> LTP QA <input type="checkbox"/> Radwaste QA <input type="checkbox"/> Non QA				Samples Shipped Via: <input checked="" type="checkbox"/> Fed Ex <input type="checkbox"/> UPS <input type="checkbox"/> Hand <input type="checkbox"/> Other		Internal Container Temp.: <u>22</u> Deg. C Custody Sealed? Y <input type="checkbox"/> N <input checked="" type="checkbox"/> Custody Seal Intact? Y <input type="checkbox"/> N <input type="checkbox"/>	
1) Relinquished By <i>JAMIE RICHARDS</i>		Date/Time <i>7-20-06 / 1445</i>		2) Received By <i>K. Wright</i>		Date/Time <i>7/20/06 0930</i>	
3) Relinquished By		Date/Time		4) Received By		Date/Time	

Bill of Lading #
7910 57 11 1301

167556/.

Connecticut Yankee Atomic Power Company

362 Injun Hollow Road, East Hampton, CT 06424
860-267-2556

Chain of Custody Form

No. 2006-00448

Project Name: Haddam Neck Decommissioning						Analyses Requested			Lab Use Only	
Contact Name & Phone: Jack McCarthy 860-267-3924									Comments:	
Analytical Lab (Name, City, State) General Engineering Laboratories 2040 Savage Road, Charleston SC, 29407 843 556 8171. Attn. Cheryl Jones										
Priority: <input type="checkbox"/> 30 D. <input checked="" type="checkbox"/> 14 D. <input type="checkbox"/> 7 D.										
Sample Designation	Date	Time	Media Code	Sample Type Code	Container Size & Type Code	FSSGAM	FSSALL	Sr-90		
18 9106-0015-011F	6-28-06	14:39	SE	C	BP	X		X		
19 9106-0015-012F	6-28-06	10:58	SE	C	BP	X		X		
20 9106-0015-013F	6-28-06	10:04	SE	C	BP	X		X		
21 9106-0015-014F	6-28-06	09:05	SE	C	BP	X		X		
21 9106-0015-015F	6-28-06	08:25	SE	C	BP		X			
22 9106-0015-016F	6-28-06	08:46	SE	C	BP	X		X		
23 9106-0015-017F	6-28-06	09:47	SE	C	BP	X		X		
24 9106-0015-019F	6-28-06	09:25	SE	C	BP	X		X		
25 9106-0015-020F	6-28-06	07:59	SE	C	BP	X		X		

NOTES: PO #: 002332 MSR #: 06-1037 SSWP# NA LTP QA Radwaste QA Non QA

Samples Shipped Via:
 Fed Ex
 UPS
 Hand
 Other

Bill of Lading #
7910 5711 1286

Internal Container Temp: 21 Deg. C
 Custody Sealed? Y N
 Custody Seal Intact? Y N

1) Relinquished By *JAIME RICARTE* Date/Time *7-20-06/1445*

2) Received By *H. Light* Date/Time *7/21/06 0930*

3) Relinquished By

4) Received By

167556/1

Connecticut Yankee Atomic Power Company

362 Injun Hollow Road, East Hampton, CT 06424
860-267-2556

Chain of Custody Form

No. 2006-00447

Project Name: Haddam Neck Decommissioning			Media Code	Sample Type Code	Container Size- & Type Code	Analyses Requested				Lab Use Only				
Contact Name & Phone: Jack McCarthy 860-267-3924						FSSGAM	FSSALL	Sr-90					Comments:	
Analytical Lab (Name, City, State) General Engineering Laboratories 2040 Savage Road. Charleston SC. 29407 843 556 8171. Attn. Cheryl Jones														
Priority: <input type="checkbox"/> 30 D. <input checked="" type="checkbox"/> 14 D. <input type="checkbox"/> 7 D.														

Sample Designation	Date	Time	Media Code	Sample Type Code	Container Size- & Type Code	FSSGAM	FSSALL	Sr-90	Comment, Preservation	Lab Sample ID
9106-0015-001F	6-28-06	13:36	SE	C	BP	X		X		
9106-0015-002F	6-28-06	14:15	SE	C	BP	X		X		
9106-0015-003F	6-28-06	13:15	SE	C	BP	X		X		
9106-0015-004F	6-28-06	12:54	SE	C	BP		X			
9106-0015-005F	6-28-06	15:47	SE	C	BP	X		X		
9106-0015-006F	6-28-06	16:10	SE	C	BP	X		X		
9106-0015-007F	6-28-06	11:33	SE	C	BP	X		X		
9106-0015-008F	6-28-06	11:10	SE	C	BP	X		X		
9106-0015-009F	6-28-06	10:25	SE	C	BP	X		X		
9106-0015-010F	6-28-06	15:17	SE	C	BP	X		X		

NOTES: PO #: 002332 MSR #: 06-1037 SSWP# NA LTP QA Radwaste QA Non QA

Samples Shipped Via:
 Fed Ex
 UPS
 Hand
 Other

Internal Container Temp. 23 Deg. C
 Custody Sealed? Y N
 Custody Seal Intact? Y N

1) Relinquished By JAIME RICARTE	Date/Time 7-20-06 / 1445	2) Received By K. Wright	Date/Time 7/21/06 0930
3) Relinquished By	Date/Time	4) Received By	Date/Time

Bill of Lading #
79105711220

167556-1

Connecticut Yankee Atomic Power Company

362 Injun Hollow Road, East Hampton, CT 06424
860-267-2556

Chain of Custody Form

No. 2006-00468

Project Name: Haddam Neck Decommissioning						Analyses Requested				Lab Use Only		
Contact Name & Phone: Jack McCarthy 860-267-3924						FSSGAM	FSSALL	Sr-90	Comments:			
Analytical Lab (Name, City, State) General Engineering Laboratories 2040 Savage Road, Charleston SC, 29407 843 556 8171. Attn. Cheryl Jones												
Priority: <input type="checkbox"/> 30 D. <input checked="" type="checkbox"/> 14 D. <input type="checkbox"/> 7 D.												
Sample Designation	Date	Time	Media Code	Sample Type Code	Container Size & Type Code							
26 9106-0015-005FS	6-28-06	15:47	SE	C	BP	X		X				
27 9106-0015-012FS	6-28-06	10:58	SE	C	BP	X		X				
28 9106-0015-018FS	6-27-06	17:18	SE	C	BP	X		X				
NOTES: PO #: 002332 MSR #: 06-1037 SSWP# NA <input checked="" type="checkbox"/> LTP QA <input type="checkbox"/> Radwaste QA <input type="checkbox"/> Non QA												
1) Relinquished By JAIME RUARTE						2) Received By K. Wright						
Date/Time 7-20-06/1445						Date/Time 7/21/06 0930						
3) Relinquished By						4) Received By						
Date/Time						Date/Time						
Samples Shipped Via: <input checked="" type="checkbox"/> Fed Ex <input type="checkbox"/> UPS <input type="checkbox"/> Hand <input type="checkbox"/> Other												
Internal Container Temp: 21 Deg. C Custody Sealed? Y <input type="checkbox"/> N <input checked="" type="checkbox"/> Custody Seal Intact? Y <input type="checkbox"/> N <input checked="" type="checkbox"/>												
Bill of Lading # 7910 5711 1286												



SAMPLE RECEIPT & REVIEW FORM

PM use only

Client: <u>Conn. Bank.</u>	SDG/ARCO/Work Order: <u>167554, 167555, 167556</u>
Date Received: <u>7/21/06</u>	PM(A) Review (ensure non-conforming items are resolved prior to signing): <i>[Signature]</i>
Received By: <u>[Signature]</u>	

Sample Receipt Criteria	Yes	NA	No	Comments/Qualifiers (Required for Non-Conforming Items)
1 Shipping containers received intact and sealed?	/			Circle Applicable: seals broken damaged container leaking container other (describe)
2 Samples requiring cold preservation within (4 +/- 2 C)? Record preservation method.	/			Circle Coolant # ice bags blue ice dry ice <u>none</u> other (describe) <i>See Cont. Sheet.</i>
3 Chain of custody documents included with shipment?	/			
4 Sample containers intact and sealed?	/			Circle Applicable: seals broken damaged container leaking container other (describe)
5 Samples requiring chemical preservation at proper pH?		/		Sample ID's, containers affected and observed pH:
6 VOA vials free of headspace (defined as < 6mm bubble)?		/		Sample ID's and containers affected:
7 Are Encore containers present? (If yes, immediately deliver to VOA laboratory)			/	
8 Samples received within holding time?	/			Id's and tests affected:
9 Sample ID's on COC match ID's on bottles?			/	Sample ID's and containers affected: <i>See Cont. Sheet.</i>
10 Date & time on COC match date & time on bottles?	/			Sample ID's affected:
11 Number of containers received match number indicated on COC?	/			Sample ID's affected:
12 COC form is properly signed in relinquished/received sections?	/			
14 Air Bill, Tracking #'s, & Additional Comments				<i>See sheet</i>

Suspected Hazard Information	Non-Regulated	Regulated	High Level	RSO RAD Receipt # _____ *If > x2 area background is observed on samples identified as "non-regulated/non-radioactive", contact the Radiation Safety group for further investigation.
A Radiological Classification?	/			Maximum Counts Observed*: <u>cpm 40</u>
B PCB Regulated?	/			Comments:
C Shipped as DOT Hazardous Material? If yes, contact Waste Manager or ESH Manager.	/			Hazard Class Shipped: UN#:

PM (or PMA) review of Hazard classification: _____ Initials [Signature] Date: 7/21/06

Figure 1. Sample Check-in List

Date/Time Received: 7/21/06 0930

SDG#: MSR#06-1035, MSR#06-1036, MSR#06-1037

Work Order Number: 167556

Shipping Container ID: See Cont Sheet Chain of Custody # See Cont Sheet

1. Custody Seals on shipping container intact? Yes No
2. Custody Seals dated and signed? Yes No N/A
3. Chain-of-Custody record present? Yes No
4. Cooler temperature See Cont Sheet
5. Vermiculite/packing materials is: Wet Dry N/A
6. Number of samples in shipping container: See Cont Sheet
7. Sample holding times exceeded? Yes No

8. Samples have:	
<input checked="" type="checkbox"/> tape	<input type="checkbox"/> hazard labels
<input checked="" type="checkbox"/> custody seals	<input checked="" type="checkbox"/> appropriate sample labels
9. Samples are:	
<input checked="" type="checkbox"/> in good condition	<input type="checkbox"/> leaking
<input type="checkbox"/> broken	<input type="checkbox"/> have air bubbles

10. Were any anomalies identified in sample receipt? Yes No

11. Description of anomalies (include sample numbers): _____

Sample Custodian/Laboratory: K. Wright Date: 7/21/06

Telephoned to: _____ On _____ By _____

RADIOLOGICAL ANALYSIS

**Radiochemistry Case Narrative
Connecticut Yankee Atomic Power Co. (YANK)
Work Order 167556**

Method/Analysis Information

Product: Alphaspec Am241, Cm, Solid ALL FSS
Analytical Method: DOE EML HASL-300, Am-05-RC Modified
Prep Method: Ash Soil Prep
Dry Soil Prep GL-RAD-A-021 Method: Dry Soil Prep
Analytical Batch Number: 552678
Prep Batch Number: 550566
Dry Soil Prep GL-RAD-A-021 Batch Number: 550554

Sample ID	Client ID
167556029	9106-0015-021F
167556030	9106-0015-004F
167556031	9106-0015-015F
1201146077	Method Blank (MB)
1201146078	167555016(9106-0013-004F) Sample Duplicate (DUP)
1201146079	167555016(9106-0013-004F) Matrix Spike (MS)
1201146080	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-011 REV# 14.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 167555016 (9106-0013-004F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

None of the samples in this sample set required reprep or reanalysis.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Manual Integration

No manual integrations were performed on data in this batch.

Additional Comments

Additional comments were not required for this sample set.

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product: Alphaspec Pu, Solid-ALL FSS

Analytical Method: DOE EML HASL-300, Pu-11-RC Modified

Prep Method: Ash Soil Prep

Dry Soil Prep GL-RAD-A-021 Method: Dry Soil Prep

Analytical Batch Number: 550872

Prep Batch Number: 550566

Dry Soil Prep GL-RAD-A-021 Batch Number: 550554

Sample ID	Client ID
167556029	9106-0015-021F
167556030	9106-0015-004F
167556031	9106-0015-015F
1201141927	Method Blank (MB)
1201141928	167555016(9106-0013-004F) Sample Duplicate (DUP)
1201141929	167555016(9106-0013-004F) Matrix Spike (MS)
1201141930	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-011 REV# 14.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 167555016 (9106-0013-004F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

None of the samples in this sample set required reprep or reanalysis.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Manual Integration

No manual integrations were performed on data in this batch.

Additional Comments

Additional comments were not required for this sample set.

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product:	Liquid Scint Pu241, Solid-ALL FSS
Analytical Method:	DOE EML HASL-300, Pu-11-RC Modified
Prep Method:	Ash Soil Prep
Dry Soil Prep GL-RAD-A-021 Method:	Dry Soil Prep
Analytical Batch Number:	550873
Prep Batch Number:	550566
Dry Soil Prep GL-RAD-A-021 Batch Number:	550554

Sample ID	Client ID
167556029	9106-0015-021F
167556030	9106-0015-004F
167556031	9106-0015-015F
1201141931	Method Blank (MB)
1201141932	167555016(9106-0013-004F) Sample Duplicate (DUP)
1201141933	167555016(9106-0013-004F) Matrix Spike (MS)
1201141934	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-035 REV# 8.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 167555016 (9106-0013-004F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

None of the samples in this sample set required reprep or reanalysis.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Manual Integration

No manual integrations were performed on data in this batch.

Additional Comments

Additional comments were not required for this sample set.

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product:	Gamma,Solid-FSS GAM & ALL FSS 226 Ingrowth Waived
Analytical Method:	EML HASL 300, 4.5.2.3
Prep Method:	Dry Soil Prep
Analytical Batch Number:	551078
Prep Batch Number:	550552

Sample ID	Client ID
167556001	9106-0015-022F
167556002	9106-0015-023F
167556003	9106-0015-024F
167556004	9106-0015-026F
167556005	9106-0015-027F
167556006	9106-0015-028F
167556007	9106-0015-018F
167556008	9106-0015-025F
167556009	9106-0015-001F
167556010	9106-0015-002F
167556011	9106-0015-003F
167556012	9106-0015-005F
167556013	9106-0015-006F
167556014	9106-0015-007F
167556015	9106-0015-008F
167556016	9106-0015-009F
167556017	9106-0015-010F
167556018	9106-0015-011F
167556019	9106-0015-012F
167556020	9106-0015-013F
1201142453	Method Blank (MB)
1201142454	167556001(9106-0015-022F) Sample Duplicate (DUP)
1201142455	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-013 REV# 11.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 167556001 (9106-0015-022F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:**Holding Time**

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

None of the samples in this sample set required reprep or reanalysis.

Miscellaneous Information:**NCR Documentation**

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Additional Comments

The sample and the duplicate, 1201142454 (9106-0015-022F) and 167556001 (9106-0015-022F), did not meet the relative percent difference requirement for Ac-228 and Cs-137, however, they do meet the relative error ratio requirement with a value of 2.29 for Ac-228 and 2.54 for Cs-137.

Qualifier information

Qualifier	Reason	Analyte	Sample
UI	Data rejected due to interference.	Europium-155	167556002
			167556003
			167556010
		Manganese-54	167556003
UI	Data rejected due to low abundance.	Bismuth-212	167556017
		Cesium-134	167556003
			167556015
			167556017
			167556019
		Cobalt-60	167556017
			1201142453
		Europium-154	1201142454
		Europium-155	167556007
		Silver-108m	167556010
UI	Data rejected due to no valid peak.	Cesium-134	167556013

Method/Analysis Information

Product: Gamma,Solid-FSS GAM & ALL FSS 226 Ingrowth Waived
Analytical Method: EML HASL 300, 4.5.2.3
Prep Method: Dry Soil Prep
Analytical Batch Number: 551081
Prep Batch Number: 550554

Sample ID	Client ID
167556021	9106-0015-014F
167556022	9106-0015-016F
167556023	9106-0015-017F
167556024	9106-0015-019F
167556025	9106-0015-020F
167556026	9106-0015-005FS
167556027	9106-0015-012FS
167556028	9106-0015-018FS
167556029	9106-0015-021F
167556030	9106-0015-004F
167556031	9106-0015-015F
1201142459	Method Blank (MB)
1201142460	167556029(9106-0015-021F) Sample Duplicate (DUP)
1201142461	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-013 REV# 11.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 167556029 (9106-0015-021F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

None of the samples in this sample set required reprep or reanalysis.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Additional Comments

Additional comments were not required for this sample set.

Qualifier information

Qualifier	Reason	Analyte	Sample
UI	Data rejected due to high peak width.	Bismuth-212	167556022
		Cobalt-60	167556029
UI	Data rejected due to interference.	Manganese-54	167556024
			167556026
			167556031
UI	Data rejected due to low abundance.	Bismuth-214	167556027
			167556021
		Cesium-134	167556026
			167556031
		Lead-212	1201142460
			167556023
		1201142459	

Method/Analysis Information

Product:	GFPC, Sr90, solid-ALL FSS
Analytical Method:	EPA 905.0 Modified
Prep Method:	Ash Soil Prep
Dry Soil Prep GL-RAD-A-021 Method:	Dry Soil Prep
Analytical Batch Number:	550820
Prep Batch Number:	550564
Dry Soil Prep GL-RAD-A-021 Batch Number:	550552

Sample ID	Client ID
167556001	9106-0015-022F
167556002	9106-0015-023F
167556003	9106-0015-024F
167556004	9106-0015-026F
167556005	9106-0015-027F
167556006	9106-0015-028F
167556007	9106-0015-018F
167556008	9106-0015-025F
167556009	9106-0015-001F
167556010	9106-0015-002F
167556011	9106-0015-003F
167556012	9106-0015-005F
167556013	9106-0015-006F
167556014	9106-0015-007F
167556015	9106-0015-008F
167556016	9106-0015-009F
167556017	9106-0015-010F
167556018	9106-0015-011F
167556019	9106-0015-012F
167556020	9106-0015-013F
1201141746	Method Blank (MB)
1201141747	167556008(9106-0015-025F) Sample Duplicate (DUP)
1201141748	167556008(9106-0015-025F) Matrix Spike (MS)
1201141749	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-004 REV# 10.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 167556008 (9106-0015-025F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

None of the samples in this sample set required reprep or reanalysis.

Chemical Recoveries

All chemical recoveries meet the required acceptance limits for this sample set.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Additional Comments

Samples 1201141746 (MB), 1201141747 (9106-0015-025F), 1201141748 (9106-0015-025F), 1201141749 (LCS), 167556001 (9106-0015-022F), 167556002 (9106-0015-023F), 167556003 (9106-0015-024F), 167556004 (9106-0015-026F), 167556005 (9106-0015-027F), 167556006 (9106-0015-028F), 167556007 (9106-0015-018F), 167556008 (9106-0015-025F), 167556009 (9106-0015-001F), 167556010 (9106-0015-002F), 167556011 (9106-0015-003F), 167556012 (9106-0015-005F), 167556013 (9106-0015-006F), 167556014 (9106-0015-007F), 167556015 (9106-0015-008F), 167556016 (9106-0015-009F), 167556017 (9106-0015-010F), 167556018 (9106-0015-011F), 167556019 (9106-0015-012F) and 167556020 (9106-0015-013F) were dried and reweighed due to low matrix spike recovery.

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product:	GFPC, Sr90, solid-ALL FSS
Analytical Method:	EPA 905.0 Modified
Prep Method:	Ash Soil Prep
Dry Soil Prep GL-RAD-A-021 Method:	Dry Soil Prep
Analytical Batch Number:	550821
Prep Batch Number:	550566
Dry Soil Prep GL-RAD-A-021 Batch Number:	550554

Sample ID	Client ID
167556021	9106-0015-014F
167556022	9106-0015-016F
167556023	9106-0015-017F
167556024	9106-0015-019F
167556025	9106-0015-020F
167556026	9106-0015-005FS
167556027	9106-0015-012FS
167556028	9106-0015-018FS
167556029	9106-0015-021F
167556030	9106-0015-004F
167556031	9106-0015-015F
1201141750	Method Blank (MB)
1201141751	167554004(9106-0007-021F) Sample Duplicate (DUP)
1201141752	167554004(9106-0007-021F) Matrix Spike (MS)
1201141753	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-004 REV# 10.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 167554004 (9106-0007-021F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

None of the samples in this sample set required reprep or reanalysis.

Chemical Recoveries

All chemical recoveries meet the required acceptance limits for this sample set.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Additional Comments

Additional comments were not required for this sample set.

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product: Liquid Scint Tc99, Solid-ALL FSS
Analytical Method: DOE EML HASL-300, Tc-02-RC Modified
Analytical Batch Number: 550849

Sample ID	Client ID
167556029	9106-0015-021F
167556030	9106-0015-004F
167556031	9106-0015-015F
1201141843	Method Blank (MB)
1201141844	167556030(9106-0015-004F) Sample Duplicate (DUP)
1201141845	167556030(9106-0015-004F) Matrix Spike (MS)
1201141846	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-005 REV# 13.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 167556030 (9106-0015-004F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

None of the samples in this sample set required reprep or reanalysis.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Additional Comments

Additional comments were not required for this sample set.

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product:	Liquid Scint Fe55, Solid-ALL FSS
Analytical Method:	DOE RESL Fe-1, Modified
Prep Method:	Ash Soil Prep
Dry Soil Prep GL-RAD-A-021 Method:	Dry Soil Prep
Analytical Batch Number:	550847
Prep Batch Number:	550566
Dry Soil Prep GL-RAD-A-021 Batch Number:	550554

Sample ID	Client ID
167556029	9106-0015-021F
167556030	9106-0015-004F
167556031	9106-0015-015F
1201141835	Method Blank (MB)
1201141836	167555017(9106-0013-009F) Sample Duplicate (DUP)
1201141837	167555017(9106-0013-009F) Matrix Spike (MS)
1201141838	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-040 REV# 3.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 167555017 (9106-0013-009F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

None of the samples in this sample set required reprep or reanalysis.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Additional Comments

Additional comments were not required for this sample set.

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product: Liquid Scint Ni63, Solid-ALL FSS

Analytical Method: DOE RESL Ni-1, Modified

Prep Method: Ash Soil Prep

Dry Soil Prep GL-RAD-A-021 Method: Dry Soil Prep

Analytical Batch Number: 556697

Prep Batch Number: 550566

Dry Soil Prep GL-RAD-A-021 Batch Number: 550554

Sample ID	Client ID
167556029	9106-0015-021F
167556030	9106-0015-004F
167556031	9106-0015-015F
1201155543	Method Blank (MB)
1201155544	167555017(9106-0013-009F) Sample Duplicate (DUP)
1201155545	167555017(9106-0013-009F) Matrix Spike (MS)
1201155546	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-022 REV# 8.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 167555017 (9106-0013-009F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

Samples were reprepared due to low/high recovery.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Additional Comments

Additional comments were not required for this sample set.

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product: LSC, Tritium Dist, Solid-HTD2,ALL FSS
Analytical Method: EPA 906.0 Modified
Analytical Batch Number: 550850

Sample ID	Client ID
167556029	9106-0015-021F
167556030	9106-0015-004F
167556031	9106-0015-015F
1201141847	Method Blank (MB)
1201141848	167556031(9106-0015-015F) Sample Duplicate (DUP)
1201141849	167556031(9106-0015-015F) Matrix Spike (MS)
1201141850	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-002 REV# 12.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 167556031 (9106-0015-015F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

None of the samples in this sample set required reprep or reanalysis.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Additional Comments

Additional comments were not required for this sample set.

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product: Liquid Scint C14, Solid All,FSS
Analytical Method: EPA EERF C-01 Modified
Analytical Batch Number: 550851

Sample ID	Client ID
167556029	9106-0015-021F
167556030	9106-0015-004F
167556031	9106-0015-015F
1201141851	Method Blank (MB)
1201141852	167556029(9106-0015-021F) Sample Duplicate (DUP)
1201141853	167556029(9106-0015-021F) Matrix Spike (MS)
1201141854	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-003 REV# 8.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 167556029 (9106-0015-021F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

SAMPLE DATA SUMMARY

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

**Certificate of Analysis Report
for**

YANK001 Connecticut Yankee Atomic Power Co.

Client SDG: MSR#06-1037 GEL Work Order: 167556

The Qualifiers in this report are defined as follows:

- * A quality control analyte recovery is outside of specified acceptance criteria
- ** Analyte is a surrogate compound
- U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
- UI Gamma Spectroscopy--Uncertain identification
- ND The analyte concentration is not detected above the detection limit.

The above sample is reported on a dry weight basis except where prohibited by the analytical procedure.

Where the analytical method has been performed under NELAP certification, the analysis has met all of the requirements of the NELAC standard unless qualified on the Certificate of Analysis.

This data report has been prepared and reviewed in accordance with General Engineering Laboratories, LLC standard operating procedures. Please direct any questions to your Project Manager, Cheryl Jones.



Reviewed by _____

GENERAL ENGINEERING LABORATORIES, LLC
 2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
 Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
 Contact: Mr. Jack McCarthy
 Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID:	9106-0015-022F	Project:	YANK01204
Sample ID:	167556001	Client ID:	YANK001
Matrix:	SE	Vol. Recv.:	
Collect Date:	27-JUN-06		
Receive Date:	21-JUL-06		
Collector:	Client		
Moisture:	39.1%		

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
-----------	-----------	--------	-------------	----	-----	-----	-------	----	---------	------	------	-------	-----

Rad Gamma Spec Analysis

*Gamma, Solid-FSS GAM & ALL FSS 226 Ingrowth
 Waived*

Actinium-228		0.799	+/-0.156	0.0607	+/-0.156	0.128	pCi/g		MJH1	08/02/06	2157	551078	1
Americium-241	U	0.0246	+/-0.104	0.0853	+/-0.104	0.176	pCi/g						
Bismuth-212		0.457	+/-0.238	0.126	+/-0.238	0.266	pCi/g						
Bismuth-214		0.612	+/-0.0886	0.030	+/-0.0886	0.0628	pCi/g						
Cesium-134	U	0.0453	+/-0.0355	0.0231	+/-0.0355	0.0482	pCi/g						
Cesium-137		0.346	+/-0.0445	0.0178	+/-0.0445	0.0372	pCi/g						
Cobalt-60		0.697	+/-0.0732	0.0191	+/-0.0732	0.0409	pCi/g						
Europium-152	U	0.0354	+/-0.0503	0.0423	+/-0.0503	0.0878	pCi/g						
Europium-154	U	-0.00728	+/-0.0592	0.0487	+/-0.0592	0.105	pCi/g						
Europium-155	U	0.0128	+/-0.0649	0.0455	+/-0.0649	0.0935	pCi/g						
Lead-212		0.742	+/-0.0572	0.0235	+/-0.0572	0.0486	pCi/g						
Lead-214		0.625	+/-0.0879	0.0296	+/-0.0879	0.0615	pCi/g						
Manganese-54	U	0.022	+/-0.0235	0.017	+/-0.0235	0.0358	pCi/g						
Niobium-94	U	0.00715	+/-0.0183	0.0156	+/-0.0183	0.0326	pCi/g						
Potassium-40		12.5	+/-0.783	0.138	+/-0.783	0.302	pCi/g						
Radium-226		0.612	+/-0.0886	0.030	+/-0.0886	0.0628	pCi/g						
Silver-108m	U	0.00466	+/-0.0164	0.0143	+/-0.0164	0.0298	pCi/g						
Thallium-208		0.219	+/-0.0428	0.0167	+/-0.0428	0.0349	pCi/g						

Rad Gas Flow Proportional Counting

GFPC, Sr90, solid-ALL FSS

Strontium-90	U	0.00253	+/-0.0182	0.0196	+/-0.0182	0.0421	pCi/g		BXF1	07/28/06	2004	550820	2
--------------	---	---------	-----------	--------	-----------	--------	-------	--	------	----------	------	--------	---

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	AXP2	07/21/06	1531	550552

The following Analytical Methods were performed

Method	Description
1	EML HASL 300, 4.5.2.3
2	EPA 905.0 Modified

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-022F
Sample ID: 167556001

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Surrogate/Tracer recovery	Test				Recovery%		Acceptable Limits						
Carrier/Tracer Recovery		GFPC, Sr90, solid-ALL FSS			73		(25%-125%)						

Notes:

The Qualifiers in this report are defined as follows :

- * A quality control analyte recovery is outside of specified acceptance criteria
 - < Result is less than value reported
 - > Result is greater than value reported
 - A The TIC is a suspected aldol-condensation product
 - B Target analyte was detected in the associated blank
 - BD Results are either below the MDC or tracer recovery is low
 - C Analyte has been confirmed by GC/MS analysis
 - D Results are reported from a diluted aliquot of the sample
 - H Analytical holding time was exceeded
 - J Value is estimated
 - N/A Spike recovery limits do not apply. Sample concentration exceeds spike concentration by 4X or more
 - R Sample results are rejected
 - U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
 - UI Gamma Spectroscopy--Uncertain identification
 - X Consult Case Narrative, Data Summary package, or Project Manager concerning this qualifier
 - Y QC Samples were not spiked with this compound
 - ^ RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL
 - h Preparation or preservation holding time was exceeded
- The above sample is reported on a dry weight basis.

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-023F
Sample ID: 167556002
Matrix: SE
Collect Date: 27-JUN-06
Receive Date: 21-JUL-06
Collector: Client
Moisture: 50.3%

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Gamma Spec Analysis													
<i>Gamma, Solid-FSS GAM & ALL FSS 226 Ingrowth</i>													
<i>Waived</i>													
Actinium-228		0.918	+/-0.311	0.111	+/-0.311	0.236	pCi/g		MJH1	08/02/06	2157	551078	1
Americium-241		0.132	+/-0.0628	0.031	+/-0.0628	0.0639	pCi/g						
Bismuth-212		0.708	+/-0.479	0.232	+/-0.479	0.493	pCi/g						
Bismuth-214		0.655	+/-0.150	0.0538	+/-0.150	0.114	pCi/g						
Cesium-134	U	0.0612	+/-0.0474	0.0391	+/-0.0474	0.0825	pCi/g						
Cesium-137		0.328	+/-0.0695	0.0278	+/-0.0695	0.0592	pCi/g						
Cobalt-60		1.06	+/-0.130	0.0345	+/-0.130	0.0748	pCi/g						
Europium-152	U	0.0443	+/-0.0817	0.070	+/-0.0817	0.146	pCi/g						
Europium-154	U	-0.0323	+/-0.108	0.0858	+/-0.108	0.187	pCi/g						
Europium-155	UI	0.00	+/-0.100	0.0533	+/-0.100	0.110	pCi/g						
Lead-212		0.890	+/-0.134	0.0377	+/-0.134	0.0783	pCi/g						
Lead-214		0.652	+/-0.128	0.0484	+/-0.128	0.101	pCi/g						
Manganese-54	U	0.0531	+/-0.0448	0.0363	+/-0.0448	0.0767	pCi/g						
Niobium-94	U	-0.018	+/-0.0337	0.0259	+/-0.0337	0.055	pCi/g						
Potassium-40		13.5	+/-1.43	0.242	+/-1.43	0.541	pCi/g						
Radium-226		0.655	+/-0.150	0.0538	+/-0.150	0.114	pCi/g						
Silver-108m	U	0.00144	+/-0.0278	0.023	+/-0.0278	0.0486	pCi/g						
Thallium-208		0.264	+/-0.0861	0.0297	+/-0.0861	0.0628	pCi/g						
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid-ALL FSS</i>													
Strontium-90	U	-0.012	+/-0.0132	0.0172	+/-0.0132	0.0381	pCi/g		BXF1	07/31/06	1029	550820	2

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	AXP2	07/21/06	1531	550552

The following Analytical Methods were performed

Method	Description
1	EML HASL 300, 4.5.2.3
2	EPA 905.0 Modified

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
---------------------------	------	-----------	-------------------

GENERAL ENGINEERING LABORATORIES, LLC
 2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
 Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
 Contact: Mr. Jack McCarthy
 Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-024F
 Sample ID: 167556003
 Matrix: SE
 Collect Date: 27-JUN-06
 Receive Date: 21-JUL-06
 Collector: Client
 Moisture: 45.7%

Project: YANK01204
 Client ID: YANK001
 Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Gamma Spec Analysis													
<i>Gamma, Solid-FSS GAM & ALL FSS 226 Ingrowth</i>													
<i>Waived</i>													
Actinium-228		1.06	+/-0.175	0.0574	+/-0.175	0.120	pCi/g		MJH1	08/02/06	2158	551078	1
Americium-241	U	0.0554	+/-0.084	0.0647	+/-0.084	0.132	pCi/g						
Bismuth-212		0.705	+/-0.250	0.131	+/-0.250	0.272	pCi/g						
Bismuth-214		0.793	+/-0.103	0.0302	+/-0.103	0.0625	pCi/g						
Cesium-134	UI	0.00	+/-0.0438	0.0223	+/-0.0438	0.0461	pCi/g						
Cesium-137		0.0671	+/-0.0327	0.0165	+/-0.0327	0.0343	pCi/g						
Cobalt-60		0.115	+/-0.033	0.0194	+/-0.033	0.0408	pCi/g						
Europium-152	U	-0.0101	+/-0.0582	0.0458	+/-0.0582	0.0939	pCi/g						
Europium-154	U	0.00943	+/-0.0646	0.0545	+/-0.0646	0.114	pCi/g						
Europium-155	UI	0.00	+/-0.0595	0.0419	+/-0.0595	0.0853	pCi/g						
Lead-212		1.16	+/-0.0754	0.0248	+/-0.0754	0.0506	pCi/g						
Lead-214		0.903	+/-0.093	0.0319	+/-0.093	0.0654	pCi/g						
Manganese-54	UI	0.00	+/-0.0334	0.0169	+/-0.0334	0.0352	pCi/g						
Niobium-94	U	-0.00695	+/-0.0185	0.0149	+/-0.0185	0.031	pCi/g						
Potassium-40		17.0	+/-0.888	0.157	+/-0.888	0.335	pCi/g						
Radium-226		0.793	+/-0.103	0.0302	+/-0.103	0.0625	pCi/g						
Silver-108m	U	-7.690E-05	+/-0.0192	0.015	+/-0.0192	0.0309	pCi/g						
Thallium-208		0.358	+/-0.0516	0.0168	+/-0.0516	0.0348	pCi/g						

Rad Gas Flow Proportional Counting

GFPC, Sr90, solid-ALL FSS

Strontium-90	U	0.0252	+/-0.0167	0.0139	+/-0.0167	0.0312	pCi/g		BXF1	07/31/06	1029	550820	2
--------------	---	--------	-----------	--------	-----------	--------	-------	--	------	----------	------	--------	---

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	AXP2	07/21/06	1531	550552

The following Analytical Methods were performed

Method	Description
1	EML HASL 300, 4.5.2.3
2	EPA 905.0 Modified

GENERAL ENGINEERING LABORATORIES, LLC
2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-026F
Sample ID: 167556004
Matrix: SE
Collect Date: 27-JUN-06
Receive Date: 21-JUL-06
Collector: Client
Moisture: 36.3%

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Gamma Spec Analysis													
<i>Gamma, Solid-FSS GAM & ALL FSS 226 Ingrowth</i>													
<i>Waived</i>													
Actinium-228		0.690	+/-0.174	0.0631	+/-0.174	0.136	pCi/g		MJH1	08/02/06	2159	551078	1
Americium-241	U	0.0332	+/-0.091	0.0732	+/-0.091	0.151	pCi/g						
Bismuth-212		0.692	+/-0.285	0.134	+/-0.285	0.286	pCi/g						
Bismuth-214		0.655	+/-0.0893	0.0307	+/-0.0893	0.0652	pCi/g						
Cesium-134	U	0.0397	+/-0.0294	0.023	+/-0.0294	0.0487	pCi/g						
Cesium-137		0.323	+/-0.0534	0.0189	+/-0.0534	0.040	pCi/g						
Cobalt-60		0.0575	+/-0.0355	0.0178	+/-0.0355	0.0392	pCi/g						
Europium-152	U	-0.00373	+/-0.0526	0.0453	+/-0.0526	0.0949	pCi/g						
Europium-154	U	-0.0133	+/-0.0654	0.0531	+/-0.0654	0.116	pCi/g						
Europium-155	U	0.0257	+/-0.0565	0.0493	+/-0.0565	0.102	pCi/g						
Lead-212		0.752	+/-0.0638	0.0275	+/-0.0638	0.0569	pCi/g						
Lead-214		0.576	+/-0.0913	0.0335	+/-0.0913	0.070	pCi/g						
Manganese-54	U	-0.0123	+/-0.0224	0.0185	+/-0.0224	0.0395	pCi/g						
Niobium-94	U	0.00994	+/-0.0204	0.0174	+/-0.0204	0.0368	pCi/g						
Potassium-40		11.6	+/-0.899	0.162	+/-0.899	0.360	pCi/g						
Radium-226		0.655	+/-0.0893	0.0307	+/-0.0893	0.0652	pCi/g						
Silver-108m	U	0.00308	+/-0.0185	0.0159	+/-0.0185	0.0335	pCi/g						
Thallium-208		0.252	+/-0.0476	0.0171	+/-0.0476	0.0364	pCi/g						
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid-ALL FSS</i>													
Strontium-90	U	0.00651	+/-0.0133	0.0135	+/-0.0133	0.0304	pCi/g		BXF1	07/31/06	1029	550820	2

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	AXP2	07/21/06	1531	550552

The following Analytical Methods were performed

Method	Description
1	EML HASL 300, 4.5.2.3
2	EPA 905.0 Modified

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
---------------------------	------	-----------	-------------------

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-026F
Sample ID: 167556004

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Surrogate/Tracer recovery	Test				Recovery%		Acceptable Limits						
Carrier/Tracer Recovery		GFPC, Sr90, solid-ALL FSS			77		(25%-125%)						

Notes:

The Qualifiers in this report are defined as follows :

- * A quality control analyte recovery is outside of specified acceptance criteria
 - < Result is less than value reported
 - > Result is greater than value reported
 - A The TIC is a suspected aldol-condensation product
 - B Target analyte was detected in the associated blank
 - BD ¹ Results are either below the MDC or tracer recovery is low
 - C Analyte has been confirmed by GC/MS analysis
 - D Results are reported from a diluted aliquot of the sample
 - H Analytical holding time was exceeded
 - J Value is estimated
 - N/A Spike recovery limits do not apply. Sample concentration exceeds spike concentration by 4X or more
 - R Sample results are rejected
 - U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
 - UI Gamma Spectroscopy--Uncertain identification
 - X Consult Case Narrative, Data Summary package, or Project Manager concerning this qualifier
 - Y QC Samples were not spiked with this compound
 - ^ RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL
 - h Preparation or preservation holding time was exceeded
- The above sample is reported on a dry weight basis.

GENERAL ENGINEERING LABORATORIES, LLC
2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-027F
Sample ID: 167556005
Matrix: SE
Collect Date: 27-JUN-06
Receive Date: 21-JUL-06
Collector: Client
Moisture: 31.6%

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Gamma Spec Analysis													
<i>Gamma, Solid-FSS GAM & ALL FSS 226 Ingrowth</i>													
<i>Waived</i>													
Actinium-228		0.597	+/-0.226	0.0755	+/-0.226	0.162	pCi/g		MJH1	08/02/06	2159	551078	1
Americium-241	U	-0.0217	+/-0.0333	0.0295	+/-0.0333	0.0607	pCi/g						
Bismuth-212		0.505	+/-0.284	0.167	+/-0.284	0.356	pCi/g						
Bismuth-214		0.550	+/-0.102	0.0374	+/-0.102	0.0795	pCi/g						
Cesium-134	U	-0.00267	+/-0.0397	0.0285	+/-0.0397	0.0603	pCi/g						
Cesium-137		0.273	+/-0.0624	0.0235	+/-0.0624	0.0498	pCi/g						
Cobalt-60		0.139	+/-0.0451	0.0288	+/-0.0451	0.0621	pCi/g						
Europium-152	U	-0.0331	+/-0.0566	0.0484	+/-0.0566	0.102	pCi/g						
Europium-154	U	-0.0308	+/-0.0866	0.0704	+/-0.0866	0.153	pCi/g						
Europium-155	U	-0.00801	+/-0.0513	0.0449	+/-0.0513	0.0928	pCi/g						
Lead-212		0.645	+/-0.0718	0.0324	+/-0.0718	0.067	pCi/g						
Lead-214		0.522	+/-0.0805	0.0343	+/-0.0805	0.072	pCi/g						
Manganese-54	U	-0.0262	+/-0.0297	0.0227	+/-0.0297	0.0485	pCi/g						
Niobium-94	U	0.0158	+/-0.0251	0.022	+/-0.0251	0.0465	pCi/g						
Potassium-40		10.4	+/-0.947	0.198	+/-0.947	0.440	pCi/g						
Radium-226		0.550	+/-0.102	0.0374	+/-0.102	0.0795	pCi/g						
Silver-108m	U	0.00333	+/-0.0212	0.0186	+/-0.0212	0.0392	pCi/g						
Thallium-208		0.253	+/-0.0576	0.0206	+/-0.0576	0.0438	pCi/g						
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid-ALL FSS</i>													
Strontium-90	U	0.00314	+/-0.0156	0.0168	+/-0.0156	0.0378	pCi/g		BXF1	07/31/06	1029	550820	2

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	AXP2	07/21/06	1531	550552

The following Analytical Methods were performed

Method	Description
1	EML HASL 300, 4.5.2.3
2	EPA 905.0 Modified

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
---------------------------	------	-----------	-------------------

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-028F
Sample ID: 167556006
Matrix: SE
Collect Date: 27-JUN-06
Receive Date: 21-JUL-06
Collector: Client
Moisture: 24.7%

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Gamma Spec Analysis													
<i>Gamma, Solid-FSS GAM & ALL FSS 226 Ingrowth</i>													
<i>Waived</i>													
Actinium-228		0.367	+/-0.103	0.0378	+/-0.103	0.081	pCi/g		MJH1	08/02/06	2159	551078	1
Americium-241	U	-0.0354	+/-0.0729	0.0606	+/-0.0729	0.126	pCi/g						
Bismuth-212		0.352	+/-0.173	0.0996	+/-0.173	0.210	pCi/g						
Bismuth-214		0.202	+/-0.0692	0.0216	+/-0.0692	0.0455	pCi/g						
Cesium-134	U	0.0147	+/-0.0192	0.0135	+/-0.0192	0.0286	pCi/g						
Cesium-137	U	0.0049	+/-0.0152	0.013	+/-0.0152	0.0273	pCi/g						
Cobalt-60	U	-0.00379	+/-0.0141	0.0112	+/-0.0141	0.0245	pCi/g						
Europium-152	U	-0.0128	+/-0.033	0.0287	+/-0.033	0.0604	pCi/g						
Europium-154	U	0.0203	+/-0.0397	0.0346	+/-0.0397	0.0748	pCi/g						
Europium-155	U	0.052	+/-0.0407	0.039	+/-0.0407	0.0806	pCi/g						
Lead-212		0.444	+/-0.0425	0.0197	+/-0.0425	0.0408	pCi/g						
Lead-214		0.295	+/-0.0608	0.0201	+/-0.0608	0.0424	pCi/g						
Manganese-54	U	0.00289	+/-0.0136	0.0119	+/-0.0136	0.0253	pCi/g						
Niobium-94	U	0.00973	+/-0.013	0.0114	+/-0.013	0.0239	pCi/g						
Potassium-40		5.18	+/-0.461	0.0737	+/-0.461	0.168	pCi/g						
Radium-226		0.202	+/-0.0692	0.0216	+/-0.0692	0.0455	pCi/g						
Silver-108m	U	0.00217	+/-0.0111	0.00985	+/-0.0111	0.0208	pCi/g						
Thallium-208		0.101	+/-0.0274	0.012	+/-0.0274	0.0253	pCi/g						
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid-ALL FSS</i>													
Strontium-90	U	-0.0153	+/-0.016	0.0213	+/-0.016	0.0472	pCi/g		BXF1	07/31/06	1029	550820	2

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	AXP2	07/21/06	1531	550552

The following Analytical Methods were performed

Method	Description
1	EML HASL 300, 4.5.2.3
2	EPA 905.0 Modified

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
---------------------------	------	-----------	-------------------

GENERAL ENGINEERING LABORATORIES, LLC
 2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
 Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
 Contact: Mr. Jack McCarthy
 Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-028F Project: YANK01204
 Sample ID: 167556006 Client ID: YANK001
 Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Surrogate/Tracer recovery	Test				Recovery%		Acceptable Limits						
Carrier/Tracer Recovery	GFPC, Sr90, solid-ALL FSS				58		(25%-125%)						

Notes:

The Qualifiers in this report are defined as follows :

- * A quality control analyte recovery is outside of specified acceptance criteria
 - < Result is less than value reported
 - > Result is greater than value reported
 - A The TIC is a suspected aldol-condensation product
 - B Target analyte was detected in the associated blank
 - BD Results are either below the MDC or tracer recovery is low
 - C Analyte has been confirmed by GC/MS analysis
 - D Results are reported from a diluted aliquot of the sample
 - H Analytical holding time was exceeded
 - J Value is estimated
 - N/A Spike recovery limits do not apply. Sample concentration exceeds spike concentration by 4X or more.
 - R Sample results are rejected
 - U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
 - UI Gamma Spectroscopy--Uncertain identification
 - X Consult Case Narrative, Data Summary package, or Project Manager concerning this qualifier
 - Y QC Samples were not spiked with this compound
 - ^ RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL
 - h Preparation or preservation holding time was exceeded
- The above sample is reported on a dry weight basis.

GENERAL ENGINEERING LABORATORIES, LLC
2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-018F
Sample ID: 167556007
Matrix: SE
Collect Date: 27-JUN-06
Receive Date: 21-JUL-06
Collector: Client
Moisture: 30.5%

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Gamma Spec Analysis													
<i>Gamma, Solid-FSS GAM & ALL FSS 226 Ingrowth</i>													
<i>Waived</i>													
Actinium-228		0.704	+/-0.174	0.0798	+/-0.174	0.167	pCi/g		MJH1	08/02/06	2200	551078	1
Americium-241	U	0.0293	+/-0.0449	0.040	+/-0.0449	0.0822	pCi/g						
Bismuth-212		0.681	+/-0.263	0.152	+/-0.263	0.319	pCi/g						
Bismuth-214		0.517	+/-0.0941	0.0319	+/-0.0941	0.0669	pCi/g						
Cesium-134	U	0.0448	+/-0.047	0.0235	+/-0.047	0.0492	pCi/g						
Cesium-137		0.354	+/-0.0551	0.0169	+/-0.0551	0.0355	pCi/g						
Cobalt-60		1.16	+/-0.100	0.0146	+/-0.100	0.032	pCi/g						
Europium-152	U	0.019	+/-0.0509	0.0446	+/-0.0509	0.0926	pCi/g						
Europium-154	U	0.0126	+/-0.0546	0.046	+/-0.0546	0.0996	pCi/g						
Europium-155	UI	0.00	+/-0.0634	0.0432	+/-0.0634	0.0888	pCi/g						
Lead-212		0.690	+/-0.0918	0.0309	+/-0.0918	0.0634	pCi/g						
Lead-214		0.601	+/-0.0993	0.0288	+/-0.0993	0.0601	pCi/g						
Manganese-54	U	0.020	+/-0.0201	0.0185	+/-0.0201	0.039	pCi/g						
Niobium-94	U	0.0139	+/-0.0187	0.0169	+/-0.0187	0.0354	pCi/g						
Potassium-40		12.7	+/-1.09	0.127	+/-1.09	0.283	pCi/g						
Radium-226		0.517	+/-0.0941	0.0319	+/-0.0941	0.0669	pCi/g						
Silver-108m	U	0.0183	+/-0.0182	0.0162	+/-0.0182	0.0337	pCi/g						
Thallium-208		0.243	+/-0.0458	0.016	+/-0.0458	0.0337	pCi/g						

Rad Gas Flow Proportional Counting

GFPC, Sr90, solid-ALL FSS

Strontium-90	U	-0.0115	+/-0.0136	0.018	+/-0.0136	0.0403	pCi/g		BXF1	07/31/06	1029	550820	2
--------------	---	---------	-----------	-------	-----------	--------	-------	--	------	----------	------	--------	---

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	AXP2	07/21/06	1531	550552

The following Analytical Methods were performed

Method	Description
1	EML HASL 300, 4.5.2.3
2	EPA 905.0 Modified

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
---------------------------	------	-----------	-------------------

GENERAL ENGINEERING LABORATORIES, LLC
2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-025F
Sample ID: 167556008
Matrix: SE
Collect Date: 27-JUN-06
Receive Date: 21-JUL-06
Collector: Client
Moisture: 45.6%

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Gamma Spec Analysis													
<i>Gamma, Solid-FSS GAM & ALL FSS 226 Ingrowth</i>													
<i>Waived</i>													
Actinium-228		0.922	+/-0.242	0.087	+/-0.242	0.174	pCi/g		MJH1	08/02/06	2213	551078	1
Americium-241	U	0.0512	+/-0.0952	0.0694	+/-0.0952	0.139	pCi/g						
Bismuth-212		0.551	+/-0.420	0.179	+/-0.420	0.357	pCi/g						
Bismuth-214		0.755	+/-0.149	0.0416	+/-0.149	0.0831	pCi/g						
Cesium-134	U	0.0485	+/-0.058	0.0288	+/-0.058	0.0576	pCi/g						
Cesium-137	U	0.0117	+/-0.0299	0.0248	+/-0.0299	0.0495	pCi/g						
Cobalt-60	U	-0.00363	+/-0.0334	0.027	+/-0.0334	0.0539	pCi/g						
Europium-152	U	0.0385	+/-0.0988	0.0582	+/-0.0988	0.116	pCi/g						
Europium-154	U	-0.0447	+/-0.0909	0.0705	+/-0.0909	0.141	pCi/g						
Europium-155	U	0.0768	+/-0.0905	0.062	+/-0.0905	0.124	pCi/g						
Lead-212		1.12	+/-0.120	0.0344	+/-0.120	0.0688	pCi/g						
Lead-214		0.929	+/-0.136	0.0408	+/-0.136	0.0816	pCi/g						
Manganese-54	U	-0.0174	+/-0.0295	0.0235	+/-0.0295	0.047	pCi/g						
Niobium-94	U	0.0143	+/-0.0259	0.0226	+/-0.0259	0.0451	pCi/g						
Potassium-40		17.2	+/-1.53	0.199	+/-1.53	0.397	pCi/g						
Radium-226		0.755	+/-0.149	0.0416	+/-0.149	0.0831	pCi/g						
Silver-108m	U	-0.00906	+/-0.024	0.0192	+/-0.024	0.0384	pCi/g						
Thallium-208		0.308	+/-0.0692	0.023	+/-0.0692	0.0459	pCi/g						
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid-ALL FSS</i>													
Strontium-90	U	0.0128	+/-0.0169	0.0164	+/-0.0169	0.0368	pCi/g		BXF1	07/31/06	1029	550820	2

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	AXP2	07/21/06	1531	550552

The following Analytical Methods were performed

Method	Description
1	EML HASL 300, 4.5.2.3
2	EPA 905.0 Modified

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
---------------------------	------	-----------	-------------------

GENERAL ENGINEERING LABORATORIES, LLC
 2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
 Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
 Contact: Mr. Jack McCarthy
 Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-001F
 Sample ID: 167556009
 Matrix: SE
 Collect Date: 28-JUN-06
 Receive Date: 21-JUL-06
 Collector: Client
 Moisture: 15.2%

Project: YANK01204
 Client ID: YANK001
 Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Gamma Spec Analysis													
<i>Gamma, Solid--FSS GAM & ALL FSS 226 Ingrowth</i>													
<i>Waived</i>													
Actinium-228		0.592	+/-0.136	0.0625	+/-0.136	0.125	pCi/g		MJH1	08/02/06	2213	551078	1
Americium-241	U	-0.00472	+/-0.0757	0.0598	+/-0.0757	0.120	pCi/g						
Bismuth-212		0.646	+/-0.242	0.112	+/-0.242	0.223	pCi/g						
Bismuth-214		0.464	+/-0.0832	0.0304	+/-0.0832	0.0607	pCi/g						
Cesium-134	U	0.0344	+/-0.0232	0.0212	+/-0.0232	0.0425	pCi/g						
Cesium-137	U	0.0256	+/-0.020	0.0182	+/-0.020	0.0365	pCi/g						
Cobalt-60	U	0.012	+/-0.019	0.0171	+/-0.019	0.0341	pCi/g						
Europium-152	U	-0.00443	+/-0.0637	0.0423	+/-0.0637	0.0846	pCi/g						
Europium-154	U	-0.0276	+/-0.0606	0.0489	+/-0.0606	0.0977	pCi/g						
Europium-155	U	0.057	+/-0.0546	0.0464	+/-0.0546	0.0928	pCi/g						
Lead-212		0.634	+/-0.074	0.0235	+/-0.074	0.047	pCi/g						
Lead-214		0.550	+/-0.0878	0.0295	+/-0.0878	0.0589	pCi/g						
Manganese-54	U	-0.0143	+/-0.0195	0.0156	+/-0.0195	0.0311	pCi/g						
Niobium-94	U	0.00316	+/-0.021	0.0154	+/-0.021	0.0308	pCi/g						
Potassium-40		11.8	+/-1.02	0.116	+/-1.02	0.231	pCi/g						
Radium-226		0.464	+/-0.0832	0.0304	+/-0.0832	0.0607	pCi/g						
Silver-108m	U	-0.00452	+/-0.0168	0.0144	+/-0.0168	0.0287	pCi/g						
Thallium-208		0.221	+/-0.0445	0.0159	+/-0.0445	0.0317	pCi/g						
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid--ALL FSS</i>													
Strontium-90	U	0.0248	+/-0.0208	0.0185	+/-0.0208	0.0416	pCi/g		BXF1	07/31/06	1228	550820	2

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	AXP2	07/21/06	1531	550552

The following Analytical Methods were performed

Method	Description
1	EML HASL 300, 4.5.2.3
2	EPA 905.0 Modified

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
---------------------------	------	-----------	-------------------

GENERAL ENGINEERING LABORATORIES, LLC
 2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
 Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
 Contact: Mr. Jack McCarthy
 Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-001F Project: YANK01204
 Sample ID: 167556009 Client ID: YANK001
 Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Surrogate/Tracer recovery	Test				Recovery%		Acceptable Limits						
Carrier/Tracer Recovery		GFPC, Sr90, solid-ALL FSS			55		(25%-125%)						

Notes:

The Qualifiers in this report are defined as follows :

- * A quality control analyte recovery is outside of specified acceptance criteria
 - < Result is less than value reported
 - > Result is greater than value reported
 - A The TIC is a suspected aldol-condensation product
 - B Target analyte was detected in the associated blank
 - BD Results are either below the MDC or tracer recovery is low
 - C Analyte has been confirmed by GC/MS analysis
 - D Results are reported from a diluted aliquot of the sample
 - H Analytical holding time was exceeded
 - J Value is estimated
 - N/A Spike recovery limits do not apply. Sample concentration exceeds spike concentration by 4X or more
 - R Sample results are rejected
 - U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
 - UI Gamma Spectroscopy--Uncertain identification
 - X Consult Case Narrative, Data Summary package, or Project Manager concerning this qualifier
 - Y QC Samples were not spiked with this compound
 - ^ RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL
 - h Preparation or preservation holding time was exceeded
- The above sample is reported on a dry weight basis.

GENERAL ENGINEERING LABORATORIES, LLC
2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-002F
Sample ID: 167556010
Matrix: SE
Collect Date: 28-JUN-06
Receive Date: 21-JUL-06
Collector: Client
Moisture: 38.9%

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Gamma Spec Analysis													
<i>Gamma, Solid-FSS GAM & ALL FSS 226 Ingrowth</i>													
<i>Waived</i>													
Actinium-228		0.867	+/-0.261	0.108	+/-0.261	0.217	pCi/g		MJH1	08/02/06	2214	551078	1
Americium-241	U	0.0351	+/-0.0435	0.0289	+/-0.0435	0.0578	pCi/g						
Bismuth-212		0.817	+/-0.454	0.213	+/-0.454	0.426	pCi/g						
Bismuth-214		0.602	+/-0.128	0.0455	+/-0.128	0.0909	pCi/g						
Cesium-134	U	0.0334	+/-0.0399	0.0358	+/-0.0399	0.0716	pCi/g						
Cesium-137		0.522	+/-0.0825	0.0274	+/-0.0825	0.0548	pCi/g						
Cobalt-60		1.11	+/-0.109	0.0296	+/-0.109	0.0593	pCi/g						
Europium-152	U	-0.05	+/-0.0956	0.0591	+/-0.0956	0.118	pCi/g						
Europium-154	U	-0.00342	+/-0.0997	0.0824	+/-0.0997	0.165	pCi/g						
Europium-155	UI	0.00	+/-0.0735	0.0479	+/-0.0735	0.0958	pCi/g						
Lead-212		0.828	+/-0.0995	0.0315	+/-0.0995	0.063	pCi/g						
Lead-214		0.611	+/-0.118	0.0421	+/-0.118	0.0842	pCi/g						
Manganese-54	U	-0.00239	+/-0.0385	0.0327	+/-0.0385	0.0654	pCi/g						
Niobium-94	U	0.0158	+/-0.0294	0.0261	+/-0.0294	0.0522	pCi/g						
Potassium-40		13.2	+/-1.09	0.246	+/-1.09	0.492	pCi/g						
Radium-226		0.602	+/-0.128	0.0455	+/-0.128	0.0909	pCi/g						
Silver-108m	UI	0.00	+/-0.0604	0.0211	+/-0.0604	0.0421	pCi/g						
Thallium-208		0.248	+/-0.0665	0.025	+/-0.0665	0.050	pCi/g						
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid-ALL FSS</i>													
Strontium-90	U	-0.0188	+/-0.00973	0.0159	+/-0.00974	0.0359	pCi/g		BXF1	07/31/06	1228	550820	2

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	AXP2	07/21/06	1531	550552

The following Analytical Methods were performed

Method	Description
1	EML HASL 300, 4.5.2.3
2	EPA 905.0 Modified

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
---------------------------	------	-----------	-------------------

GENERAL ENGINEERING LABORATORIES, LLC
2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID:	9106-0015-003F	Project:	YANK01204
Sample ID:	167556011	Client ID:	YANK001
Matrix:	SE	Vol. Recv.:	
Collect Date:	28-JUN-06		
Receive Date:	21-JUL-06		
Collector:	Client		
Moisture:	51.9%		

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
-----------	-----------	--------	-------------	----	-----	-----	-------	----	---------	------	------	-------	-----

Rad Gamma Spec Analysis

*Gamma, Solid-FSS GAM & ALL FSS 226 Ingrowth
Waived*

Actinium-228		0.957	+/-0.187	0.0691	+/-0.187	0.146	pCi/g		MJH1	08/02/06	2319	551078	1
Americium-241	U	-0.019	+/-0.124	0.0838	+/-0.124	0.172	pCi/g						
Bismuth-212		0.724	+/-0.331	0.144	+/-0.331	0.302	pCi/g						
Bismuth-214		0.712	+/-0.114	0.0344	+/-0.114	0.0718	pCi/g						
Cesium-134	U	0.0123	+/-0.0552	0.0238	+/-0.0552	0.0499	pCi/g						
Cesium-137		0.0467	+/-0.0304	0.0208	+/-0.0304	0.0434	pCi/g						
Cobalt-60		0.142	+/-0.0629	0.0219	+/-0.0629	0.0468	pCi/g						
Europium-152	U	0.00241	+/-0.061	0.0472	+/-0.061	0.0979	pCi/g						
Europium-154	U	0.0408	+/-0.0795	0.0675	+/-0.0795	0.143	pCi/g						
Europium-155	U	0.0416	+/-0.0637	0.0521	+/-0.0637	0.107	pCi/g						
Lead-212		0.998	+/-0.076	0.0268	+/-0.076	0.0553	pCi/g						
Lead-214		0.706	+/-0.0995	0.0358	+/-0.0995	0.0741	pCi/g						
Manganese-54	U	0.0141	+/-0.0255	0.021	+/-0.0255	0.044	pCi/g						
Niobium-94	U	-0.00372	+/-0.0263	0.0183	+/-0.0263	0.0382	pCi/g						
Potassium-40		15.0	+/-0.976	0.184	+/-0.976	0.398	pCi/g						
Radium-226		0.712	+/-0.114	0.0344	+/-0.114	0.0718	pCi/g						
Silver-108m	U	-0.00288	+/-0.019	0.0155	+/-0.019	0.0324	pCi/g						
Thallium-208		0.282	+/-0.0552	0.0177	+/-0.0552	0.0371	pCi/g						

Rad Gas Flow Proportional Counting

GFPC, Sr90, solid-ALL FSS

Strontium-90	U	-0.00333	+/-0.0138	0.0162	+/-0.0138	0.0368	pCi/g		BXF1	07/31/06	1228	550820	2
--------------	---	----------	-----------	--------	-----------	--------	-------	--	------	----------	------	--------	---

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	AXP2	07/21/06	1531	550552

The following Analytical Methods were performed

Method	Description
1	EML HASL 300, 4.5.2.3
2	EPA 905.0 Modified

GENERAL ENGINEERING LABORATORIES, LLC
2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-005F
Sample ID: 167556012
Matrix: SE
Collect Date: 28-JUN-06
Receive Date: 21-JUL-06
Collector: Client
Moisture: 43.7%

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Gamma Spec Analysis													
<i>Gamma, Solid-FSS GAM & ALL FSS 226 Ingrowth</i>													
<i>Waived</i>													
Actinium-228		0.944	+/-0.231	0.0665	+/-0.231	0.143	pCi/g		MJH1	08/02/06	2320	551078	1
Americium-241	U	-0.0774	+/-0.104	0.0786	+/-0.104	0.162	pCi/g						
Bismuth-212		0.426	+/-0.330	0.165	+/-0.330	0.350	pCi/g						
Bismuth-214		0.548	+/-0.0998	0.0431	+/-0.0998	0.0904	pCi/g						
Cesium-134	U	0.0306	+/-0.0418	0.0272	+/-0.0418	0.0574	pCi/g						
Cesium-137		0.0589	+/-0.0336	0.0198	+/-0.0336	0.042	pCi/g						
Cobalt-60	U	0.000929	+/-0.0279	0.0233	+/-0.0279	0.0507	pCi/g						
Europium-152	U	-0.0167	+/-0.0582	0.0482	+/-0.0582	0.101	pCi/g						
Europium-154	U	-0.022	+/-0.0786	0.0638	+/-0.0786	0.139	pCi/g						
Europium-155	U	0.0444	+/-0.0641	0.052	+/-0.0641	0.108	pCi/g						
Lead-212		0.811	+/-0.101	0.0367	+/-0.101	0.0756	pCi/g						
Lead-214		0.711	+/-0.0995	0.0368	+/-0.0995	0.077	pCi/g						
Manganese-54	U	-0.00375	+/-0.0264	0.0217	+/-0.0264	0.0462	pCi/g						
Niobium-94	U	0.0166	+/-0.0243	0.0197	+/-0.0243	0.0417	pCi/g						
Potassium-40		14.2	+/-1.04	0.177	+/-1.04	0.396	pCi/g						
Radium-226		0.548	+/-0.0998	0.0431	+/-0.0998	0.0904	pCi/g						
Silver-108m	U	0.00534	+/-0.020	0.0169	+/-0.020	0.0356	pCi/g						
Thallium-208		0.301	+/-0.0503	0.0203	+/-0.0503	0.0429	pCi/g						
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid-ALL FSS</i>													
Strontium-90	U	0.0133	+/-0.018	0.0173	+/-0.018	0.0391	pCi/g		BXF1	07/31/06	1228	550820	2

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	AXP2	07/21/06	1531	550552

The following Analytical Methods were performed

Method	Description
1	EML HASL 300, 4.5.2.3
2	EPA 905.0 Modified

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
---------------------------	------	-----------	-------------------

GENERAL ENGINEERING LABORATORIES, LLC
 2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
 Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
 Contact: Mr. Jack McCarthy
 Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-005F Project: YANK01204
 Sample ID: 167556012 Client ID: YANK001
 Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Surrogate/Tracer recovery	Test				Recovery%		Acceptable Limits						
Carrier/Tracer Recovery		GFPC, Sr90, solid-ALL FSS			60		(25%-125%)						

Notes:

The Qualifiers in this report are defined as follows :

- * A quality control analyte recovery is outside of specified acceptance criteria
 - < Result is less than value reported
 - > Result is greater than value reported
 - A The TIC is a suspected aldol-condensation product
 - B Target analyte was detected in the associated blank
 - BD Results are either below the MDC or tracer recovery is low
 - C Analyte has been confirmed by GC/MS analysis
 - D Results are reported from a diluted aliquot of the sample
 - H Analytical holding time was exceeded
 - J Value is estimated
 - N/A Spike recovery limits do not apply. Sample concentration exceeds spike concentration by 4X or more
 - R Sample results are rejected
 - U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
 - UI Gamma Spectroscopy--Uncertain identification
 - X Consult Case Narrative, Data Summary package, or Project Manager concerning this qualifier
 - Y QC Samples were not spiked with this compound
 - ^ RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL
 - h Preparation or preservation holding time was exceeded
- The above sample is reported on a dry weight basis.

GENERAL ENGINEERING LABORATORIES, LLC
 2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
 Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
 Contact: Mr. Jack McCarthy
 Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-006F
 Sample ID: 167556013
 Matrix: SE
 Collect Date: 28-JUN-06
 Receive Date: 21-JUL-06
 Collector: Client
 Moisture: 31%

Project: YANK01204
 Client ID: YANK001
 Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Gamma Spec Analysis													
<i>Gamma, Solid-FSS GAM & ALL FSS 226 Ingrowth</i>													
<i>Waived</i>													
Actinium-228		0.630	+/-0.158	0.0716	+/-0.158	0.153	pCi/g		MJH1	08/02/06	2320	551078	1
Americium-241	U	-0.0436	+/-0.148	0.0812	+/-0.148	0.167	pCi/g						
Bismuth-212		0.700	+/-0.269	0.159	+/-0.269	0.337	pCi/g						
Bismuth-214		0.530	+/-0.091	0.0365	+/-0.091	0.0771	pCi/g						
Cesium-134	UI	0.00	+/-0.0371	0.0225	+/-0.0371	0.048	pCi/g						
Cesium-137		0.322	+/-0.0592	0.0193	+/-0.0592	0.0409	pCi/g						
Cobalt-60		0.350	+/-0.063	0.0198	+/-0.063	0.0434	pCi/g						
Europium-152	U	0.0139	+/-0.0652	0.0545	+/-0.0652	0.114	pCi/g						
Europium-154	U	-0.0671	+/-0.0782	0.058	+/-0.0782	0.126	pCi/g						
Europium-155	U	0.0798	+/-0.0796	0.0573	+/-0.0796	0.118	pCi/g						
Lead-212		0.728	+/-0.0655	0.0307	+/-0.0655	0.0636	pCi/g						
Lead-214		0.578	+/-0.0742	0.0402	+/-0.0742	0.0837	pCi/g						
Manganese-54	U	-0.0161	+/-0.031	0.0213	+/-0.031	0.0452	pCi/g						
Niobium-94	U	-0.00415	+/-0.021	0.0175	+/-0.021	0.0371	pCi/g						
Potassium-40		12.4	+/-0.882	0.157	+/-0.882	0.353	pCi/g						
Radium-226		0.530	+/-0.091	0.0365	+/-0.091	0.0771	pCi/g						
Silver-108m	U	-0.00876	+/-0.0226	0.018	+/-0.0226	0.0377	pCi/g						
Thallium-208		0.236	+/-0.0559	0.0184	+/-0.0559	0.0391	pCi/g						
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid-ALL FSS</i>													
Strontium-90	U	0.00864	+/-0.020	0.0207	+/-0.020	0.0462	pCi/g		BXF1	07/31/06	1228	550820	2

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	AXP2	07/21/06	1531	550552

The following Analytical Methods were performed

Method	Description
1	EML HASL 300, 4.5.2.3
2	EPA 905.0 Modified

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
---------------------------	------	-----------	-------------------

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 – (843) 556-8171 – www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-006F
Sample ID: 167556013

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Surrogate/Tracer recovery	Test				Recovery%		Acceptable Limits						
Carrier/Tracer Recovery		GFPC, Sr90, solid-ALL FSS			54		(25%-125%)						

Notes:

The Qualifiers in this report are defined as follows :

- * A quality control analyte recovery is outside of specified acceptance criteria
 - < Result is less than value reported
 - > Result is greater than value reported
 - A The TIC is a suspected aldol-condensation product
 - B Target analyte was detected in the associated blank
 - BD Results are either below the MDC or tracer recovery is low
 - C Analyte has been confirmed by GC/MS analysis
 - D Results are reported from a diluted aliquot of the sample
 - H Analytical holding time was exceeded
 - J Value is estimated
 - N/A Spike recovery limits do not apply. Sample concentration exceeds spike concentration by 4X or more
 - R Sample results are rejected
 - U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
 - UI Gamma Spectroscopy--Uncertain identification
 - X Consult Case Narrative, Data Summary package, or Project Manager concerning this qualifier
 - Y QC Samples were not spiked with this compound
 - ^ RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL
 - h Preparation or preservation holding time was exceeded
- The above sample is reported on a dry weight basis.

GENERAL ENGINEERING LABORATORIES, LLC
2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID:	9106-0015-007F	Project:	YANK01204
Sample ID:	167556014	Client ID:	YANK001
Matrix:	SE	Vol. Recv.:	
Collect Date:	28-JUN-06		
Receive Date:	21-JUL-06		
Collector:	Client		
Moisture:	36.2%		

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Gamma Spec Analysis													
<i>Gamma, Solid-FSS GAM & ALL FSS 226 Ingrowth</i>													
<i>Waived</i>													
Actinium-228		0.677	+/-0.304	0.109	+/-0.304	0.230	pCi/g		MJH1	08/02/06	2321	551078	1
Americium-241	U	-0.00383	+/-0.0411	0.0335	+/-0.0411	0.0689	pCi/g						
Bismuth-212		0.485	+/-0.523	0.218	+/-0.523	0.459	pCi/g						
Bismuth-214		0.546	+/-0.127	0.0561	+/-0.127	0.117	pCi/g						
Cesium-134	U	0.0351	+/-0.0412	0.0355	+/-0.0412	0.0746	pCi/g						
Cesium-137		0.285	+/-0.0741	0.0253	+/-0.0741	0.0535	pCi/g						
Cobalt-60		0.355	+/-0.0793	0.0294	+/-0.0793	0.0634	pCi/g						
Europium-152	U	-0.0141	+/-0.082	0.0661	+/-0.082	0.138	pCi/g						
Europium-154	U	-0.0392	+/-0.106	0.0846	+/-0.106	0.182	pCi/g						
Europium-155	U	0.0388	+/-0.0957	0.0571	+/-0.0957	0.118	pCi/g						
Lead-212		0.653	+/-0.0873	0.0421	+/-0.0873	0.0867	pCi/g						
Lead-214		0.650	+/-0.128	0.0461	+/-0.128	0.0961	pCi/g						
Manganese-54	U	0.0107	+/-0.0383	0.0317	+/-0.0383	0.0667	pCi/g						
Niobium-94	U	0.00394	+/-0.0314	0.0261	+/-0.0314	0.0548	pCi/g						
Potassium-40		12.4	+/-1.25	0.228	+/-1.25	0.501	pCi/g						
Radium-226		0.546	+/-0.127	0.0561	+/-0.127	0.117	pCi/g						
Silver-108m	U	0.00244	+/-0.0267	0.023	+/-0.0267	0.0481	pCi/g						
Thallium-208		0.229	+/-0.0738	0.027	+/-0.0738	0.0567	pCi/g						
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid-ALL FSS</i>													
Strontium-90	U	0.00298	+/-0.0178	0.0193	+/-0.0178	0.0437	pCi/g		BXF1	07/31/06	1228	550820	2

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	AXP2	07/21/06	1531	550552

The following Analytical Methods were performed

Method	Description
1	EML HASL 300, 4.5.2.3
2	EPA 905.0 Modified

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
---------------------------	------	-----------	-------------------

GENERAL ENGINEERING LABORATORIES, LLC
 2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
 Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
 Contact: Mr. Jack McCarthy
 Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-007F Project: YANK01204
 Sample ID: 167556014 Client ID: YANK001
 Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Surrogate/Tracer recovery	Test				Recovery%		Acceptable Limits						
Carrier/Tracer Recovery		GFPC, Sr90, solid-ALL FSS			50		(25%-125%)						

Notes:

The Qualifiers in this report are defined as follows :

- * A quality control analyte recovery is outside of specified acceptance criteria
 - < Result is less than value reported
 - > Result is greater than value reported
 - A The TIC is a suspected aldol-condensation product
 - B Target analyte was detected in the associated blank
 - BD Results are either below the MDC or tracer recovery is low
 - C Analyte has been confirmed by GC/MS analysis
 - D Results are reported from a diluted aliquot of the sample
 - H Analytical holding time was exceeded
 - J Value is estimated
 - N/A Spike recovery limits do not apply. Sample concentration exceeds spike concentration by 4X or more
 - R Sample results are rejected
 - U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
 - UI Gamma Spectroscopy--Uncertain identification
 - X Consult Case Narrative, Data Summary package, or Project Manager concerning this qualifier
 - Y QC Samples were not spiked with this compound
 - ^ RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL
 - h Preparation or preservation holding time was exceeded
- The above sample is reported on a dry weight basis.

GENERAL ENGINEERING LABORATORIES, LLC
 2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
 Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
 Contact: Mr. Jack McCarthy
 Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-008F
 Sample ID: 167556015
 Matrix: SE
 Collect Date: 28-JUN-06
 Receive Date: 21-JUL-06
 Collector: Client
 Moisture: 51.1%

Project: YANK01204
 Client ID: YANK001
 Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Gamma Spec Analysis													
<i>Gamma, Solid-FSS GAM & ALL FSS 226 Ingrowth</i>													
<i>Waived</i>													
Actinium-228		0.605	+/-0.173	0.048	+/-0.173	0.101	pCi/g		MJH1	08/02/06	2321	551078	1
Americium-241	U	-0.0586	+/-0.115	0.0867	+/-0.115	0.178	pCi/g						
Bismuth-212		0.410	+/-0.217	0.100	+/-0.217	0.211	pCi/g						
Bismuth-214		0.542	+/-0.0813	0.0245	+/-0.0813	0.051	pCi/g						
Cesium-134	UI	0.00	+/-0.0246	0.0164	+/-0.0246	0.0343	pCi/g						
Cesium-137		0.215	+/-0.0393	0.0146	+/-0.0393	0.0303	pCi/g						
Cobalt-60		0.349	+/-0.0513	0.0129	+/-0.0513	0.0277	pCi/g						
Europium-152	U	0.00521	+/-0.0451	0.0359	+/-0.0451	0.0743	pCi/g						
Europium-154	U	-0.00882	+/-0.054	0.0442	+/-0.054	0.0937	pCi/g						
Europium-155		0.0782	+/-0.0643	0.0369	+/-0.0643	0.0756	pCi/g						
Lead-212		0.742	+/-0.0872	0.0204	+/-0.0872	0.0419	pCi/g						
Lead-214		0.612	+/-0.0914	0.0262	+/-0.0914	0.0541	pCi/g						
Manganese-54	U	0.0307	+/-0.0243	0.0153	+/-0.0243	0.032	pCi/g						
Niobium-94	U	0.00405	+/-0.016	0.0132	+/-0.016	0.0276	pCi/g						
Potassium-40		11.8	+/-1.02	0.125	+/-1.02	0.270	pCi/g						
Radium-226		0.542	+/-0.0813	0.0245	+/-0.0813	0.051	pCi/g						
Silver-108m	U	0.00592	+/-0.0152	0.013	+/-0.0152	0.0269	pCi/g						
Thallium-208		0.244	+/-0.0493	0.0136	+/-0.0493	0.0284	pCi/g						
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid-ALL FSS</i>													
Strontium-90	U	0.0105	+/-0.0168	0.0163	+/-0.0168	0.0372	pCi/g		BXF1	07/31/06	1228	550820	2

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	AXP2	07/21/06	1531	550552

The following Analytical Methods were performed

Method	Description
1	EML HASL 300, 4.5.2.3
2	EPA 905.0 Modified

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
---------------------------	------	-----------	-------------------

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-008F
Sample ID: 167556015

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Surrogate/Tracer recovery	Test				Recovery%		Acceptable Limits						
Carrier/Tracer Recovery		GFPC, Sr90, solid-ALL FSS			56		(25%-125%)						

Notes:

The Qualifiers in this report are defined as follows :

- * A quality control analyte recovery is outside of specified acceptance criteria
 - < Result is less than value reported
 - > Result is greater than value reported
 - A The TIC is a suspected aldol-condensation product
 - B Target analyte was detected in the associated blank
 - BD Results are either below the MDC or tracer recovery is low
 - C Analyte has been confirmed by GC/MS analysis
 - D Results are reported from a diluted aliquot of the sample
 - H Analytical holding time was exceeded
 - J Value is estimated
 - N/A Spike recovery limits do not apply. Sample concentration exceeds spike concentration by 4X or more
 - R Sample results are rejected
 - U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
 - UI Gamma Spectroscopy--Uncertain identification
 - X Consult Case Narrative, Data Summary package, or Project Manager concerning this qualifier
 - Y QC Samples were not spiked with this compound
 - ^ RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL
 - h Preparation or preservation holding time was exceeded
- The above sample is reported on a dry weight basis.

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-009F
Sample ID: 167556016
Matrix: SE
Collect Date: 28-JUN-06
Receive Date: 21-JUL-06
Collector: Client
Moisture: 27.5%

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Gamma Spec Analysis													
<i>Gamma, Solid-FSS GAM & ALL FSS 226 Ingrowth</i>													
<i>Waived</i>													
Actinium-228		0.768	+/-0.163	0.0612	+/-0.163	0.122	pCi/g		MJH1	08/03/06	0645	551078	1
Americium-241	U	-0.0144	+/-0.0646	0.0497	+/-0.0646	0.0992	pCi/g						
Bismuth-212		0.362	+/-0.212	0.118	+/-0.212	0.236	pCi/g						
Bismuth-214		0.517	+/-0.0964	0.0292	+/-0.0964	0.0583	pCi/g						
Cesium-134	U	0.0282	+/-0.0267	0.0205	+/-0.0267	0.0409	pCi/g						
Cesium-137	U	0.0119	+/-0.0201	0.0174	+/-0.0201	0.0348	pCi/g						
Cobalt-60	U	0.0323	+/-0.0249	0.0194	+/-0.0249	0.0387	pCi/g						
Europium-152	U	0.00615	+/-0.061	0.042	+/-0.061	0.0839	pCi/g						
Europium-154	U	-0.0311	+/-0.0614	0.0486	+/-0.0614	0.0971	pCi/g						
Europium-155	U	0.0437	+/-0.0523	0.0465	+/-0.0523	0.093	pCi/g						
Lead-212		0.730	+/-0.0781	0.0244	+/-0.0781	0.0488	pCi/g						
Lead-214		0.591	+/-0.0853	0.0314	+/-0.0853	0.0628	pCi/g						
Manganese-54	U	0.0323	+/-0.0292	0.0172	+/-0.0292	0.0343	pCi/g						
Niobium-94	U	0.00976	+/-0.0172	0.0154	+/-0.0172	0.0308	pCi/g						
Potassium-40		13.3	+/-1.12	0.119	+/-1.12	0.239	pCi/g						
Radium-226		0.517	+/-0.0964	0.0292	+/-0.0964	0.0583	pCi/g						
Silver-108m	U	0.00821	+/-0.0166	0.0146	+/-0.0166	0.0292	pCi/g						
Thallium-208		0.235	+/-0.0438	0.0154	+/-0.0438	0.0309	pCi/g						
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid-ALL FSS</i>													
Strontium-90	U	0.0155	+/-0.0187	0.0182	+/-0.0187	0.0402	pCi/g		BXF1	07/31/06	1228	550820	2

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	AXP2	07/21/06	1531	550552

The following Analytical Methods were performed

Method	Description
1	EML HASL 300, 4.5.2.3
2	EPA 905.0 Modified

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
---------------------------	------	-----------	-------------------

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-009F
Sample ID: 167556016

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Surrogate/Tracer recovery	Test				Recovery%		Acceptable Limits						
Carrier/Tracer Recovery		GFPC, Sr90, solid-ALL FSS			68		(25%-125%)						

Notes:

The Qualifiers in this report are defined as follows :

- * A quality control analyte recovery is outside of specified acceptance criteria
 - < Result is less than value reported
 - > Result is greater than value reported
 - A The TIC is a suspected aldol-condensation product
 - B Target analyte was detected in the associated blank
 - BD Results are either below the MDC or tracer recovery is low
 - C Analyte has been confirmed by GC/MS analysis
 - D Results are reported from a diluted aliquot of the sample
 - H Analytical holding time was exceeded
 - J Value is estimated
 - N/A Spike recovery limits do not apply. Sample concentration exceeds spike concentration by 4X or more
 - R Sample results are rejected
 - U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
 - UI Gamma Spectroscopy--Uncertain identification
 - X Consult Case Narrative, Data Summary package, or Project Manager concerning this qualifier
 - Y QC Samples were not spiked with this compound
 - ^ RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL
 - h Preparation or preservation holding time was exceeded
- The above sample is reported on a dry weight basis.

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-010F
Sample ID: 167556017
Matrix: SE
Collect Date: 28-JUN-06
Receive Date: 21-JUL-06
Collector: Client
Moisture: 24.9%

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Gamma Spec Analysis													
<i>Gamma, Solid-FSS GAM & ALL FSS 226 Ingrowth</i>													
<i>Waived</i>													
Actinium-228		0.886	+/-0.192	0.0637	+/-0.192	0.127	pCi/g		MJH1	08/03/06	0646	551078	1
Americium-241	U	0.0804	+/-0.0885	0.0709	+/-0.0885	0.142	pCi/g						
Bismuth-212	UI	0.00	+/-0.213	0.200	+/-0.213	0.400	pCi/g						
Bismuth-214		0.490	+/-0.113	0.035	+/-0.113	0.070	pCi/g						
Cesium-134	UI	0.00	+/-0.0357	0.0236	+/-0.0357	0.0472	pCi/g						
Cesium-137		0.253	+/-0.0477	0.0181	+/-0.0477	0.0362	pCi/g						
Cobalt-60	UI	0.00	+/-0.0301	0.0277	+/-0.0301	0.0554	pCi/g						
Europium-152	U	0.00295	+/-0.0908	0.0461	+/-0.0908	0.0921	pCi/g						
Europium-154	U	0.0233	+/-0.066	0.0572	+/-0.066	0.114	pCi/g						
Europium-155	U	0.0607	+/-0.0751	0.0475	+/-0.0751	0.095	pCi/g						
Lead-212		0.830	+/-0.0917	0.0274	+/-0.0917	0.0548	pCi/g						
Lead-214		0.743	+/-0.110	0.0343	+/-0.110	0.0685	pCi/g						
Manganese-54	U	-0.014	+/-0.0226	0.0181	+/-0.0226	0.0362	pCi/g						
Niobium-94	U	0.00115	+/-0.0214	0.0179	+/-0.0214	0.0357	pCi/g						
Potassium-40		13.4	+/-1.20	0.178	+/-1.20	0.355	pCi/g						
Radium-226		0.490	+/-0.113	0.035	+/-0.113	0.070	pCi/g						
Silver-108m	U	-0.00373	+/-0.018	0.0152	+/-0.018	0.0304	pCi/g						
Thallium-208		0.279	+/-0.0557	0.0166	+/-0.0557	0.0332	pCi/g						
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid-ALL FSS</i>													
Strontium-90	U	0.00371	+/-0.014	0.0149	+/-0.014	0.0335	pCi/g		BXF1	07/31/06	1228	550820	2

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	AXP2	07/21/06	1531	550552

The following Analytical Methods were performed

Method	Description
1	EML HASL 300, 4.5.2.3
2	EPA 905.0 Modified

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
---------------------------	------	-----------	-------------------

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-010F
Sample ID: 167556017

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Surrogate/Tracer recovery	Test				Recovery%		Acceptable Limits						
Carrier/Tracer Recovery	GFPC, Sr90, solid-ALL FSS				72		(25%-125%)						

Notes:

The Qualifiers in this report are defined as follows :

- * A quality control analyte recovery is outside of specified acceptance criteria
 - < Result is less than value reported
 - > Result is greater than value reported
 - A The TIC is a suspected aldol-condensation product
 - B Target analyte was detected in the associated blank
 - BD Results are either below the MDC or tracer recovery is low
 - C Analyte has been confirmed by GC/MS analysis
 - D Results are reported from a diluted aliquot of the sample
 - H Analytical holding time was exceeded
 - J Value is estimated
 - N/A Spike recovery limits do not apply. Sample concentration exceeds spike concentration by 4X or more
 - R Sample results are rejected
 - U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
 - UI Gamma Spectroscopy--Uncertain identification
 - X Consult Case Narrative, Data Summary package, or Project Manager concerning this qualifier
 - Y QC Samples were not spiked with this compound
 - ^ RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL
 - h Preparation or preservation holding time was exceeded
- The above sample is reported on a dry weight basis.

GENERAL ENGINEERING LABORATORIES, LLC
2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-011F
Sample ID: 167556018
Matrix: SE
Collect Date: 28-JUN-06
Receive Date: 21-JUL-06
Collector: Client
Moisture: 26.9%

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Gamma Spec Analysis													
<i>Gamma, Solid-FSS GAM & ALL FSS 226 Ingrowth</i>													
<i>Waived</i>													
Actinium-228		0.811	+/-0.213	0.0921	+/-0.213	0.184	pCi/g		MJH1	08/03/06	0646	551078	1
Americium-241	U	0.0265	+/-0.0368	0.0293	+/-0.0368	0.0586	pCi/g						
Bismuth-212		0.541	+/-0.298	0.165	+/-0.298	0.330	pCi/g						
Bismuth-214		0.569	+/-0.124	0.0405	+/-0.124	0.0809	pCi/g						
Cesium-134	U	0.0423	+/-0.0528	0.0283	+/-0.0528	0.0566	pCi/g						
Cesium-137		0.493	+/-0.0759	0.0257	+/-0.0759	0.0513	pCi/g						
Cobalt-60		0.396	+/-0.0728	0.0235	+/-0.0728	0.047	pCi/g						
Europium-152	U	-0.054	+/-0.0716	0.0536	+/-0.0716	0.107	pCi/g						
Europium-154	U	0.00904	+/-0.0929	0.0781	+/-0.0929	0.156	pCi/g						
Europium-155	U	0.0563	+/-0.0579	0.0453	+/-0.0579	0.0905	pCi/g						
Lead-212		0.721	+/-0.086	0.0286	+/-0.086	0.0571	pCi/g						
Lead-214		0.553	+/-0.104	0.0404	+/-0.104	0.0807	pCi/g						
Manganese-54	U	0.0238	+/-0.0237	0.0246	+/-0.0237	0.0492	pCi/g						
Niobium-94	U	0.00116	+/-0.0261	0.0196	+/-0.0261	0.0392	pCi/g						
Potassium-40		11.2	+/-0.982	0.201	+/-0.982	0.402	pCi/g						
Radium-226		0.569	+/-0.124	0.0405	+/-0.124	0.0809	pCi/g						
Silver-108m	U	-0.0109	+/-0.0233	0.0194	+/-0.0233	0.0387	pCi/g						
Thallium-208		0.222	+/-0.0573	0.0235	+/-0.0573	0.047	pCi/g						
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid-ALL FSS</i>													
Strontium-90	U	0.0188	+/-0.0204	0.019	+/-0.0204	0.0428	pCi/g		BXF1	07/31/06	1228	550820	2

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	AXP2	07/21/06	1531	550552

The following Analytical Methods were performed

Method	Description
1	EML HASL 300, 4.5.2.3
2	EPA 905.0 Modified

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
---------------------------	------	-----------	-------------------

GENERAL ENGINEERING LABORATORIES, LLC
 2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
 Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
 Contact: Mr. Jack McCarthy
 Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-011F Project: YANK01204
 Sample ID: 167556018 Client ID: YANK001
 Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Surrogate/Tracer recovery	Test				Recovery%		Acceptable Limits						
Carrier/Tracer Recovery		GFPC, Sr90, solid-ALL FSS			55		(25%-125%)						

Notes:

The Qualifiers in this report are defined as follows :

- * A quality control analyte recovery is outside of specified acceptance criteria
 - < Result is less than value reported
 - > Result is greater than value reported
 - A The TIC is a suspected aldol-condensation product
 - B Target analyte was detected in the associated blank
 - BD Results are either below the MDC or tracer recovery is low
 - C Analyte has been confirmed by GC/MS analysis
 - D Results are reported from a diluted aliquot of the sample
 - H Analytical holding time was exceeded
 - J Value is estimated
 - N/A Spike recovery limits do not apply. Sample concentration exceeds spike concentration by 4X or more
 - R Sample results are rejected
 - U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
 - UI Gamma Spectroscopy--Uncertain identification
 - X Consult Case Narrative, Data Summary package, or Project Manager concerning this qualifier
 - Y QC Samples were not spiked with this compound
 - ^ RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL
 - h Preparation or preservation holding time was exceeded
- The above sample is reported on a dry weight basis.

GENERAL ENGINEERING LABORATORIES, LLC
2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-012F
Sample ID: 167556019
Matrix: SE
Collect Date: 28-JUN-06
Receive Date: 21-JUL-06
Collector: Client
Moisture: 37.4%

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Gamma Spec Analysis													
<i>Gamma, Solid-FSS GAM & ALL FSS 226 Ingrowth</i>													
<i>Waived</i>													
Actinium-228		0.545	+/-0.190	0.073	+/-0.190	0.155	pCi/g		MJH1	08/03/06	0749	551078	1
Americium-241	U	-0.000712	+/-0.135	0.0767	+/-0.135	0.158	pCi/g						
Bismuth-212		0.495	+/-0.270	0.156	+/-0.270	0.331	pCi/g						
Bismuth-214		0.538	+/-0.0906	0.0344	+/-0.0906	0.0727	pCi/g						
Cesium-134	UI	0.00	+/-0.0327	0.0243	+/-0.0327	0.0513	pCi/g						
Cesium-137		0.347	+/-0.0464	0.0191	+/-0.0464	0.0405	pCi/g						
Cobalt-60		0.655	+/-0.0758	0.0183	+/-0.0758	0.0402	pCi/g						
Europium-152	U	-0.0264	+/-0.0656	0.0534	+/-0.0656	0.111	pCi/g						
Europium-154	U	0.0739	+/-0.0791	0.0704	+/-0.0791	0.151	pCi/g						
Europium-155	U	0.0911	+/-0.0754	0.0532	+/-0.0754	0.110	pCi/g						
Lead-212		0.704	+/-0.0622	0.0298	+/-0.0622	0.0617	pCi/g						
Lead-214		0.608	+/-0.0947	0.0394	+/-0.0947	0.082	pCi/g						
Manganese-54	U	-0.00361	+/-0.0246	0.0205	+/-0.0246	0.0435	pCi/g						
Niobium-94	U	0.000366	+/-0.0209	0.0178	+/-0.0209	0.0375	pCi/g						
Potassium-40		11.8	+/-0.881	0.173	+/-0.881	0.383	pCi/g						
Radium-226		0.538	+/-0.0906	0.0344	+/-0.0906	0.0727	pCi/g						
Silver-108m	U	-0.00627	+/-0.0213	0.0172	+/-0.0213	0.036	pCi/g						
Thallium-208		0.255	+/-0.0488	0.019	+/-0.0488	0.0402	pCi/g						
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid-ALL FSS</i>													
Strontium-90	U	0.00327	+/-0.016	0.0172	+/-0.016	0.0388	pCi/g		BXF1	07/31/06	1228	550820	2

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	AXP2	07/21/06	1531	550552

The following Analytical Methods were performed

Method	Description
1	EML HASL 300, 4.5.2.3
2	EPA 905.0 Modified

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
---------------------------	------	-----------	-------------------

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-012F
Sample ID: 167556019

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Surrogate/Tracer recovery	Test				Recovery%		Acceptable Limits						
Carrier/Tracer Recovery		GFPC, Sr90, solid-ALL FSS			60		(25%-125%)						

Notes:

The Qualifiers in this report are defined as follows :

- * A quality control analyte recovery is outside of specified acceptance criteria
- < Result is less than value reported
- > Result is greater than value reported
- A The TIC is a suspected aldol-condensation product
- B Target analyte was detected in the associated blank
- BD Results are either below the MDC or tracer recovery is low
- C Analyte has been confirmed by GC/MS analysis
- D Results are reported from a diluted aliquot of the sample
- H Analytical holding time was exceeded
- J Value is estimated
- N/A Spike recovery limits do not apply. Sample concentration exceeds spike concentration by 4X or more
- R Sample results are rejected
- U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
- UI Gamma Spectroscopy--Uncertain identification
- X Consult Case Narrative, Data Summary package, or Project Manager concerning this qualifier
- Y QC Samples were not spiked with this compound
- ^ RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL
- h Preparation or preservation holding time was exceeded

The above sample is reported on a dry weight basis.

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-013F
Sample ID: 167556020
Matrix: SE
Collect Date: 28-JUN-06
Receive Date: 21-JUL-06
Collector: Client
Moisture: 41.1%

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Gamma Spec Analysis													
<i>Gamma, Solid-FSS GAM & ALL FSS 226 Ingrowth</i>													
<i>Waived</i>													
Actinium-228		0.891	+/-0.296	0.109	+/-0.296	0.229	pCi/g		MJH1	08/03/06	0749	551078	1
Americium-241	U	0.0308	+/-0.0435	0.0365	+/-0.0435	0.075	pCi/g						
Bismuth-212		0.554	+/-0.355	0.234	+/-0.355	0.491	pCi/g						
Bismuth-214		0.659	+/-0.156	0.051	+/-0.156	0.107	pCi/g						
Cesium-134	U	0.0764	+/-0.0633	0.037	+/-0.0633	0.0775	pCi/g						
Cesium-137		0.443	+/-0.0825	0.0307	+/-0.0825	0.0644	pCi/g						
Cobalt-60		0.705	+/-0.111	0.0289	+/-0.111	0.0624	pCi/g						
Europium-152	U	0.0411	+/-0.0808	0.0675	+/-0.0808	0.140	pCi/g						
Europium-154	U	-0.0205	+/-0.112	0.0911	+/-0.112	0.194	pCi/g						
Europium-155	U	0.0149	+/-0.0911	0.0565	+/-0.0911	0.116	pCi/g						
Lead-212		0.709	+/-0.0944	0.0452	+/-0.0944	0.0928	pCi/g						
Lead-214		0.683	+/-0.115	0.0491	+/-0.115	0.102	pCi/g						
Manganese-54	U	-0.0037	+/-0.0425	0.0344	+/-0.0425	0.072	pCi/g						
Niobium-94	U	0.0225	+/-0.0323	0.0278	+/-0.0323	0.0582	pCi/g						
Potassium-40		12.2	+/-1.24	0.295	+/-1.24	0.635	pCi/g						
Radium-226		0.659	+/-0.156	0.051	+/-0.156	0.107	pCi/g						
Silver-108m	U	0.00193	+/-0.0268	0.0231	+/-0.0268	0.0482	pCi/g						
Thallium-208		0.222	+/-0.080	0.0294	+/-0.080	0.0616	pCi/g						
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid-ALL FSS</i>													
Strontium-90	U	0.005	+/-0.0179	0.0191	+/-0.0179	0.0425	pCi/g		BXF1	07/31/06	1228	550820	2

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	AXP2	07/21/06	1531	550552

The following Analytical Methods were performed

Method	Description
1	EML HASL 300, 4.5.2.3
2	EPA 905.0 Modified

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
---------------------------	------	-----------	-------------------

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-013F
Sample ID: 167556020

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Surrogate/Tracer recovery	Test				Recovery%		Acceptable Limits						
Carrier/Tracer Recovery		GFPC, Sr90, solid-ALL FSS			64		(25%-125%)						

Notes:

The Qualifiers in this report are defined as follows :

- * A quality control analyte recovery is outside of specified acceptance criteria
- < Result is less than value reported
- > Result is greater than value reported
- A The TIC is a suspected aldol-condensation product
- B Target analyte was detected in the associated blank
- BD Results are either below the MDC or tracer recovery is low
- C Analyte has been confirmed by GC/MS analysis
- D Results are reported from a diluted aliquot of the sample
- H Analytical holding time was exceeded
- J Value is estimated
- N/A Spike recovery limits do not apply. Sample concentration exceeds spike concentration by 4X or more
- R Sample results are rejected
- U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
- UI Gamma Spectroscopy--Uncertain identification
- X Consult Case Narrative, Data Summary package, or Project Manager concerning this qualifier
- Y QC Samples were not spiked with this compound
- ^ RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL
- h Preparation or preservation holding time was exceeded

The above sample is reported on a dry weight basis.

GENERAL ENGINEERING LABORATORIES, LLC
2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID:	9106-0015-014F	Project:	YANK01204
Sample ID:	167556021	Client ID:	YANK001
Matrix:	SE	Vol. Recv.:	
Collect Date:	28-JUN-06		
Receive Date:	21-JUL-06		
Collector:	Client		
Moisture:	64.3%		

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
-----------	-----------	--------	-------------	----	-----	-----	-------	----	---------	------	------	-------	-----

Rad Gamma Spec Analysis

*Gamma, Solid-FSS GAM & ALL FSS 226 Ingrowth
Waived*

Actinium-228		0.857	+/-0.320	0.114	+/-0.320	0.236	pCi/g		MJH1	08/03/06	2120	551081	1
Americium-241	U	-0.014	+/-0.0435	0.0317	+/-0.0435	0.0646	pCi/g						
Bismuth-212		0.585	+/-0.605	0.244	+/-0.605	0.504	pCi/g						
Bismuth-214		0.756	+/-0.167	0.0568	+/-0.167	0.117	pCi/g						
Cesium-134	UI	0.00	+/-0.0662	0.039	+/-0.0662	0.0804	pCi/g						
Cesium-137	U	0.0443	+/-0.0394	0.0328	+/-0.0394	0.0676	pCi/g						
Cobalt-60	U	0.0432	+/-0.0428	0.0365	+/-0.0428	0.0762	pCi/g						
Europium-152	U	-0.0422	+/-0.0867	0.0654	+/-0.0867	0.134	pCi/g						
Europium-154	U	-0.103	+/-0.118	0.0905	+/-0.118	0.190	pCi/g						
Europium-155	U	0.066	+/-0.0764	0.0567	+/-0.0764	0.116	pCi/g						
Lead-212		1.01	+/-0.0961	0.0357	+/-0.0961	0.073	pCi/g						
Lead-214		0.850	+/-0.139	0.0505	+/-0.139	0.104	pCi/g						
Manganese-54	U	-0.025	+/-0.040	0.0305	+/-0.040	0.0634	pCi/g						
Niobium-94	U	-0.00255	+/-0.0365	0.0289	+/-0.0365	0.0597	pCi/g						
Potassium-40		13.2	+/-1.43	0.284	+/-1.43	0.601	pCi/g						
Radium-226		0.756	+/-0.167	0.0568	+/-0.167	0.117	pCi/g						
Silver-108m	U	0.0181	+/-0.0311	0.0258	+/-0.0311	0.053	pCi/g						
Thallium-208		0.273	+/-0.095	0.0298	+/-0.095	0.0615	pCi/g						

Rad Gas Flow Proportional Counting

GFPC, Sr90, solid-ALL FSS

Strontium-90	U	0.0222	+/-0.0208	0.0191	+/-0.0208	0.0428	pCi/g		BXF1	07/30/06	1114	550821	2
--------------	---	--------	-----------	--------	-----------	--------	-------	--	------	----------	------	--------	---

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	BSW1	07/21/06	1518	550554

The following Analytical Methods were performed

Method	Description
1	EML HASL 300, 4.5.2.3
2	EPA 905.0 Modified

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-014F
Sample ID: 167556021

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Surrogate/Tracer recovery	Test				Recovery%		Acceptable Limits						
Carrier/Tracer Recovery	GFPC, Sr90, solid-ALL FSS				64		(25%-125%)						

Notes:

The Qualifiers in this report are defined as follows :

- * A quality control analyte recovery is outside of specified acceptance criteria
 - < Result is less than value reported
 - > Result is greater than value reported
 - A The TIC is a suspected aldol-condensation product
 - B Target analyte was detected in the associated blank
 - BD Results are either below the MDC or tracer recovery is low
 - C Analyte has been confirmed by GC/MS analysis
 - D Results are reported from a diluted aliquot of the sample
 - H Analytical holding time was exceeded
 - J Value is estimated
 - N/A Spike recovery limits do not apply. Sample concentration exceeds spike concentration by 4X or more
 - R Sample results are rejected
 - U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
 - UI Gamma Spectroscopy--Uncertain identification
 - X Consult Case Narrative, Data Summary package, or Project Manager concerning this qualifier
 - Y QC Samples were not spiked with this compound
 - ^ RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL
 - h Preparation or preservation holding time was exceeded
- The above sample is reported on a dry weight basis.

GENERAL ENGINEERING LABORATORIES, LLC
 2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
 Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
 Contact: Mr. Jack McCarthy
 Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-016F
 Sample ID: 167556022
 Matrix: SE
 Collect Date: 28-JUN-06
 Receive Date: 21-JUL-06
 Collector: Client
 Moisture: 32.4%

Project: YANK01204
 Client ID: YANK001
 Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Gamma Spec Analysis													
<i>Gamma, Solid-FSS GAM & ALL FSS 226 Ingrowth</i>													
<i>Waived</i>													
Actinium-228		0.817	+/-0.201	0.0536	+/-0.201	0.115	pCi/g		MJH1	08/03/06	1539	551081	1
Americium-241	U	-0.0173	+/-0.0759	0.0648	+/-0.0759	0.134	pCi/g						
Bismuth-212	UI	0.00	+/-0.345	0.123	+/-0.345	0.263	pCi/g						
Bismuth-214		0.697	+/-0.118	0.0324	+/-0.118	0.0682	pCi/g						
Cesium-134	U	0.0299	+/-0.023	0.0212	+/-0.023	0.0448	pCi/g						
Cesium-137		0.302	+/-0.0569	0.0174	+/-0.0569	0.0369	pCi/g						
Cobalt-60		0.101	+/-0.0393	0.0204	+/-0.0393	0.0439	pCi/g						
Europium-152	U	0.00133	+/-0.0618	0.0463	+/-0.0618	0.0967	pCi/g						
Europium-154	U	0.0226	+/-0.0617	0.0523	+/-0.0617	0.113	pCi/g						
Europium-155	U	0.00768	+/-0.064	0.0541	+/-0.064	0.112	pCi/g						
Lead-212		0.833	+/-0.0921	0.0266	+/-0.0921	0.0552	pCi/g						
Lead-214		0.647	+/-0.110	0.0328	+/-0.110	0.0685	pCi/g						
Manganese-54	U	-0.00512	+/-0.0208	0.0172	+/-0.0208	0.0367	pCi/g						
Niobium-94	U	0.00927	+/-0.0184	0.0162	+/-0.0184	0.0343	pCi/g						
Potassium-40		12.4	+/-1.11	0.126	+/-1.11	0.282	pCi/g						
Radium-226		0.697	+/-0.118	0.0324	+/-0.118	0.0682	pCi/g						
Silver-108m	U	0.00762	+/-0.0178	0.0153	+/-0.0178	0.0322	pCi/g						
Thallium-208		0.252	+/-0.0502	0.0177	+/-0.0502	0.0374	pCi/g						
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid-ALL FSS</i>													
Strontium-90	U	-0.00259	+/-0.0179	0.0207	+/-0.0179	0.0464	pCi/g		BXF1	07/30/06	1225	550821	2

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	BSW1	07/21/06	1518	550554

The following Analytical Methods were performed

Method	Description
1	EML HASL 300, 4.5.2.3
2	EPA 905.0 Modified

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
---------------------------	------	-----------	-------------------

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-016F
Sample ID: 167556022

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Surrogate/Tracer recovery	Test				Recovery%		Acceptable Limits						
Carrier/Tracer Recovery	GFPC, Sr90, solid-ALL FSS				56		(25%-125%)						

Notes:

The Qualifiers in this report are defined as follows :

- * A quality control analyte recovery is outside of specified acceptance criteria
- < Result is less than value reported
- > Result is greater than value reported
- A The TIC is a suspected aldol-condensation product
- B Target analyte was detected in the associated blank
- BD Results are either below the MDC or tracer recovery is low
- C Analyte has been confirmed by GC/MS analysis
- D Results are reported from a diluted aliquot of the sample
- H Analytical holding time was exceeded
- J Value is estimated
- N/A Spike recovery limits do not apply. Sample concentration exceeds spike concentration by 4X or more.
- R Sample results are rejected
- U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
- UI Gamma Spectroscopy—Uncertain identification
- X Consult Case Narrative, Data Summary package, or Project Manager concerning this qualifier
- Y QC Samples were not spiked with this compound
- ^ RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL
- h Preparation or preservation holding time was exceeded

The above sample is reported on a dry weight basis.

GENERAL ENGINEERING LABORATORIES, LLC
2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-017F
Sample ID: 167556023
Matrix: SE
Collect Date: 28-JUN-06
Receive Date: 21-JUL-06
Collector: Client
Moisture: 32.5%

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Gamma Spec Analysis													
<i>Gamma, Solid-FSS GAM & ALL FSS 226 Ingrowth</i>													
<i>Waived</i>													
Actinium-228		0.849	+/-0.216	0.0965	+/-0.216	0.193	pCi/g		MJH1	08/03/06	1549	551081	1
Americium-241	U	-0.0909	+/-0.107	0.0747	+/-0.107	0.149	pCi/g						
Bismuth-212		0.493	+/-0.275	0.192	+/-0.275	0.383	pCi/g						
Bismuth-214		0.503	+/-0.103	0.043	+/-0.103	0.0859	pCi/g						
Cesium-134	U	0.0541	+/-0.0346	0.0323	+/-0.0346	0.0645	pCi/g						
Cesium-137		0.474	+/-0.0715	0.0241	+/-0.0715	0.0482	pCi/g						
Cobalt-60		0.290	+/-0.0732	0.0295	+/-0.0732	0.0589	pCi/g						
Europium-152	U	0.0207	+/-0.0897	0.0626	+/-0.0897	0.125	pCi/g						
Europium-154	U	0.0229	+/-0.0979	0.0808	+/-0.0979	0.162	pCi/g						
Europium-155	U	0.0412	+/-0.075	0.063	+/-0.075	0.126	pCi/g						
Lead-212	UI	0.00	+/-0.101	0.0367	+/-0.101	0.0734	pCi/g						
Lead-214		0.663	+/-0.129	0.0442	+/-0.129	0.0884	pCi/g						
Manganese-54	U	-0.00553	+/-0.0317	0.0263	+/-0.0317	0.0526	pCi/g						
Niobium-94	U	0.016	+/-0.0283	0.0216	+/-0.0283	0.0431	pCi/g						
Potassium-40		13.0	+/-1.28	0.217	+/-1.28	0.433	pCi/g						
Radium-226		0.503	+/-0.103	0.043	+/-0.103	0.0859	pCi/g						
Silver-108m	U	-0.0122	+/-0.0283	0.0228	+/-0.0283	0.0457	pCi/g						
Thallium-208		0.278	+/-0.0618	0.0209	+/-0.0618	0.0417	pCi/g						
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid-ALL FSS</i>													
Strontium-90	U	0.00449	+/-0.0181	0.0193	+/-0.0181	0.0436	pCi/g		BXF1	07/30/06	1225	550821	2

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	BSW1	07/21/06	1518	550554

The following Analytical Methods were performed

Method	Description
1	EML HASL 300, 4.5.2.3
2	EPA 905.0 Modified

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
---------------------------	------	-----------	-------------------

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-017F
Sample ID: 167556023

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Surrogate/Tracer recovery	Test				Recovery%		Acceptable Limits						
Carrier/Tracer Recovery		GFPC, Sr90, solid-ALL FSS			59		(25%-125%)						

Notes:

The Qualifiers in this report are defined as follows :

- * A quality control analyte recovery is outside of specified acceptance criteria
 - < Result is less than value reported
 - > Result is greater than value reported
 - A The TIC is a suspected aldol-condensation product
 - B Target analyte was detected in the associated blank
 - BD Results are either below the MDC or tracer recovery is low
 - C Analyte has been confirmed by GC/MS analysis
 - D Results are reported from a diluted aliquot of the sample
 - H Analytical holding time was exceeded
 - J Value is estimated
 - N/A Spike recovery limits do not apply. Sample concentration exceeds spike concentration by 4X or more
 - R Sample results are rejected
 - U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
 - UI Gamma Spectroscopy--Uncertain identification
 - X Consult Case Narrative, Data Summary package, or Project Manager concerning this qualifier
 - Y QC Samples were not spiked with this compound
 - ^ RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL
 - h Preparation or preservation holding time was exceeded
- The above sample is reported on a dry weight basis.

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-019F
Sample ID: 167556024
Matrix: SE
Collect Date: 28-JUN-06
Receive Date: 21-JUL-06
Collector: Client
Moisture: 61%

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Gamma Spec Analysis													
<i>Gamma, Solid-FSS GAM & ALL FSS 226 Ingrowth</i>													
<i>Waived</i>													
Actinium-228		1.02	+/-0.176	0.0562	+/-0.176	0.117	pCi/g		MJH1	08/03/06	2120	551081	1
Americium-241	U	0.00165	+/-0.133	0.0887	+/-0.133	0.181	pCi/g						
Bismuth-212		0.713	+/-0.308	0.131	+/-0.308	0.271	pCi/g						
Bismuth-214		0.745	+/-0.126	0.0324	+/-0.126	0.0668	pCi/g						
Cesium-134	U	0.0417	+/-0.0377	0.0205	+/-0.0377	0.0423	pCi/g						
Cesium-137		0.0901	+/-0.0369	0.0172	+/-0.0369	0.0356	pCi/g						
Cobalt-60		0.238	+/-0.0442	0.0163	+/-0.0442	0.0345	pCi/g						
Europium-152	U	-0.0236	+/-0.0532	0.0428	+/-0.0532	0.088	pCi/g						
Europium-154	U	0.0354	+/-0.0642	0.0531	+/-0.0642	0.111	pCi/g						
Europium-155	U	0.0656	+/-0.103	0.0483	+/-0.103	0.0987	pCi/g						
Lead-212		1.14	+/-0.072	0.0248	+/-0.072	0.0508	pCi/g						
Lead-214		0.884	+/-0.0967	0.0303	+/-0.0967	0.0623	pCi/g						
Manganese-54	UI	0.00	+/-0.0255	0.0166	+/-0.0255	0.0344	pCi/g						
Niobium-94	U	-0.0232	+/-0.0205	0.0153	+/-0.0205	0.0317	pCi/g						
Potassium-40		16.7	+/-0.832	0.141	+/-0.832	0.299	pCi/g						
Radium-226		0.745	+/-0.126	0.0324	+/-0.126	0.0668	pCi/g						
Silver-108m	U	0.00571	+/-0.0182	0.0148	+/-0.0182	0.0306	pCi/g						
Thallium-208		0.273	+/-0.0515	0.0165	+/-0.0515	0.0341	pCi/g						
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid-ALL FSS</i>													
Strontium-90	U	0.00959	+/-0.0191	0.0192	+/-0.0191	0.0437	pCi/g		BXF1	07/30/06	1225	550821	2

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	BSW1	07/21/06	1518	550554

The following Analytical Methods were performed

Method	Description
1	EML HASL 300, 4.5.2.3
2	EPA 905.0 Modified

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
---------------------------	------	-----------	-------------------

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-020F
Sample ID: 167556025
Matrix: SE
Collect Date: 28-JUN-06
Receive Date: 21-JUL-06
Collector: Client
Moisture: 53%

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Gamma Spec Analysis													
<i>Gamma, Solid-FSS GAM & ALL FSS 226 Ingrowth</i>													
<i>Waived</i>													
Actinium-228		1.06	+/-0.220	0.0646	+/-0.220	0.135	pCi/g		MJH1	08/03/06	2314	551081	1
Americium-241	U	0.0148	+/-0.0265	0.0213	+/-0.0265	0.0434	pCi/g						
Bismuth-212		0.646	+/-0.287	0.139	+/-0.287	0.291	pCi/g						
Bismuth-214		0.728	+/-0.122	0.0344	+/-0.122	0.0714	pCi/g						
Cesium-134	U	0.0341	+/-0.0405	0.0236	+/-0.0405	0.0489	pCi/g						
Cesium-137		0.0979	+/-0.0494	0.0192	+/-0.0494	0.040	pCi/g						
Cobalt-60		0.203	+/-0.0509	0.0191	+/-0.0509	0.0406	pCi/g						
Europium-152	U	0.0475	+/-0.0527	0.0444	+/-0.0527	0.0915	pCi/g						
Europium-154	U	0.0684	+/-0.0693	0.060	+/-0.0693	0.127	pCi/g						
Europium-155	U	0.0653	+/-0.0648	0.0373	+/-0.0648	0.0761	pCi/g						
Lead-212		1.09	+/-0.137	0.0234	+/-0.137	0.048	pCi/g						
Lead-214		0.920	+/-0.130	0.031	+/-0.130	0.0638	pCi/g						
Manganese-54	U	0.0291	+/-0.0221	0.0191	+/-0.0221	0.0399	pCi/g						
Niobium-94	U	-0.00245	+/-0.0226	0.0179	+/-0.0226	0.0371	pCi/g						
Potassium-40		14.7	+/-1.23	0.170	+/-1.23	0.364	pCi/g						
Radium-226		0.728	+/-0.122	0.0344	+/-0.122	0.0714	pCi/g						
Silver-108m	U	0.00757	+/-0.026	0.0162	+/-0.026	0.0334	pCi/g						
Thallium-208		0.306	+/-0.0675	0.0174	+/-0.0675	0.0362	pCi/g						
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid-ALL FSS</i>													
Strontium-90	U	-0.00828	+/-0.0139	0.0175	+/-0.0139	0.0396	pCi/g		BXF1	07/30/06	1226	550821	2

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	BSW1	07/21/06	1518	550554

The following Analytical Methods were performed

Method	Description
1	EML HASL 300, 4.5.2.3
2	EPA 905.0 Modified

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-020F
Sample ID: 167556025

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Surrogate/Tracer recovery	Test				Recovery%		Acceptable Limits						
Carrier/Tracer Recovery		GFPC, Sr90, solid-ALL FSS			64		(25%-125%)						

Notes:

The Qualifiers in this report are defined as follows :

- * A quality control analyte recovery is outside of specified acceptance criteria
 - < Result is less than value reported
 - > Result is greater than value reported
 - A The TIC is a suspected aldol-condensation product
 - B Target analyte was detected in the associated blank
 - BD Results are either below the MDC or tracer recovery is low
 - C Analyte has been confirmed by GC/MS analysis
 - D Results are reported from a diluted aliquot of the sample
 - H Analytical holding time was exceeded
 - J Value is estimated
 - N/A Spike recovery limits do not apply. Sample concentration exceeds spike concentration by 4X or more
 - R Sample results are rejected
 - U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
 - UI Gamma Spectroscopy--Uncertain identification
 - X Consult Case Narrative, Data Summary package, or Project Manager concerning this qualifier
 - Y QC Samples were not spiked with this compound
 - ^ RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL
 - h Preparation or preservation holding time was exceeded
- The above sample is reported on a dry weight basis.

GENERAL ENGINEERING LABORATORIES, LLC
 2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
 Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
 Contact: Mr. Jack McCarthy
 Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-005FS
 Sample ID: 167556026
 Matrix: SE
 Collect Date: 28-JUN-06
 Receive Date: 21-JUL-06
 Collector: Client
 Moisture: 40.6%

Project: YANK01204
 Client ID: YANK001
 Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Gamma Spec Analysis													
<i>Gamma, Solid-FSS GAM & ALL FSS 226 Ingrowth</i>													
<i>Waived</i>													
Actinium-228		0.841	+/-0.177	0.0452	+/-0.177	0.0951	pCi/g		MJH1	08/03/06	2033	551081	1
Americium-241	U	0.000696	+/-0.103	0.0865	+/-0.103	0.177	pCi/g						
Bismuth-212		0.288	+/-0.248	0.104	+/-0.248	0.216	pCi/g						
Bismuth-214		0.526	+/-0.0834	0.0251	+/-0.0834	0.052	pCi/g						
Cesium-134	UI	0.00	+/-0.0198	0.0173	+/-0.0198	0.036	pCi/g						
Cesium-137		0.222	+/-0.0438	0.0156	+/-0.0438	0.0322	pCi/g						
Cobalt-60		0.0632	+/-0.0366	0.0159	+/-0.0366	0.0337	pCi/g						
Europium-152	U	0.0128	+/-0.0469	0.0373	+/-0.0469	0.0768	pCi/g						
Europium-154	U	-0.0345	+/-0.055	0.0434	+/-0.055	0.0917	pCi/g						
Europium-155	U	0.0594	+/-0.0588	0.0374	+/-0.0588	0.0765	pCi/g						
Lead-212		0.974	+/-0.106	0.0201	+/-0.106	0.0412	pCi/g						
Lead-214		0.689	+/-0.0946	0.0264	+/-0.0946	0.0544	pCi/g						
Manganese-54	UI	0.00	+/-0.0229	0.015	+/-0.0229	0.0312	pCi/g						
Niobium-94	U	0.00363	+/-0.0156	0.0128	+/-0.0156	0.0266	pCi/g						
Potassium-40		14.9	+/-1.20	0.126	+/-1.20	0.270	pCi/g						
Radium-226		0.526	+/-0.0834	0.0251	+/-0.0834	0.052	pCi/g						
Silver-108m	U	0.00987	+/-0.0144	0.0123	+/-0.0144	0.0254	pCi/g						
Thallium-208		0.291	+/-0.0447	0.0128	+/-0.0447	0.0267	pCi/g						
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid-ALL FSS</i>													
Strontium-90	U	0.0149	+/-0.0199	0.0194	+/-0.0199	0.0434	pCi/g		BXF1	07/30/06	1226	550821	2

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	BSW1	07/21/06	1518	550554

The following Analytical Methods were performed

Method	Description
1	EML HASL 300, 4.5.2.3
2	EPA 905.0 Modified

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
---------------------------	------	-----------	-------------------

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-005FS
Sample ID: 167556026

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Surrogate/Tracer recovery	Test				Recovery%		Acceptable Limits						
Carrier/Tracer Recovery		GFPC, Sr90, solid-ALL FSS			63		(25%-125%)						

Notes:

The Qualifiers in this report are defined as follows :

- * A quality control analyte recovery is outside of specified acceptance criteria
- < Result is less than value reported
- > Result is greater than value reported
- A The TIC is a suspected aldol-condensation product
- B Target analyte was detected in the associated blank
- BD Results are either below the MDC or tracer recovery is low
- C Analyte has been confirmed by GC/MS analysis
- D Results are reported from a diluted aliquot of the sample
- H Analytical holding time was exceeded
- J Value is estimated
- N/A Spike recovery limits do not apply. Sample concentration exceeds spike concentration by 4X or more
- R Sample results are rejected
- U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
- UI Gamma Spectroscopy--Uncertain identification
- X Consult Case Narrative, Data Summary package, or Project Manager concerning this qualifier
- Y QC Samples were not spiked with this compound
- ^ RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL
- h Preparation or preservation holding time was exceeded

The above sample is reported on a dry weight basis.

GENERAL ENGINEERING LABORATORIES, LLC
2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-012FS
Sample ID: 167556027
Matrix: SE
Collect Date: 28-JUN-06
Receive Date: 21-JUL-06
Collector: Client
Moisture: 35.6%

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Gamma Spec Analysis													
<i>Gamma, Solid-FSS GAM & ALL FSS 226 Ingrowth</i>													
<i>Waived</i>													
Actinium-228		0.760	+/-0.213	0.0971	+/-0.213	0.194	pCi/g		MJH1	08/03/06	1550	551081	1
Americium-241	U	-0.0898	+/-0.0992	0.082	+/-0.0992	0.164	pCi/g						
Bismuth-212		0.493	+/-0.353	0.168	+/-0.353	0.336	pCi/g						
Bismuth-214	UI	0.00	+/-0.114	0.0877	+/-0.114	0.175	pCi/g						
Cesium-134	U	0.055	+/-0.0454	0.0277	+/-0.0454	0.0553	pCi/g						
Cesium-137		0.328	+/-0.0634	0.0236	+/-0.0634	0.0472	pCi/g						
Cobalt-60		0.626	+/-0.0821	0.0189	+/-0.0821	0.0379	pCi/g						
Europium-152	U	-0.0189	+/-0.0795	0.0579	+/-0.0795	0.116	pCi/g						
Europium-154	U	0.0718	+/-0.0877	0.0791	+/-0.0877	0.158	pCi/g						
Europium-155	U	0.0413	+/-0.0707	0.0612	+/-0.0707	0.122	pCi/g						
Lead-212		0.719	+/-0.0934	0.0327	+/-0.0934	0.0654	pCi/g						
Lead-214		0.567	+/-0.110	0.043	+/-0.110	0.086	pCi/g						
Manganese-54	U	0.00108	+/-0.0317	0.0268	+/-0.0317	0.0536	pCi/g						
Niobium-94	U	-0.00351	+/-0.023	0.0187	+/-0.023	0.0375	pCi/g						
Potassium-40		12.4	+/-1.26	0.163	+/-1.26	0.326	pCi/g						
Radium-226		0.503	+/-0.114	0.0461	+/-0.114	0.0922	pCi/g						
Silver-108m	U	0.0149	+/-0.0244	0.0214	+/-0.0244	0.0428	pCi/g						
Thallium-208		0.203	+/-0.0574	0.0236	+/-0.0574	0.0473	pCi/g						

Rad Gas Flow Proportional Counting

GFPC, Sr90, solid-ALL FSS

Strontium-90	U	0.00815	+/-0.0147	0.0147	+/-0.0147	0.0332	pCi/g		BXF1	07/30/06	1226	550821	2
--------------	---	---------	-----------	--------	-----------	--------	-------	--	------	----------	------	--------	---

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	BSW1	07/21/06	1519	550554

The following Analytical Methods were performed

Method	Description
1	EML HASL 300, 4.5.2.3
2	EPA 905.0 Modified

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
---------------------------	------	-----------	-------------------

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-012FS
Sample ID: 167556027

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Surrogate/Tracer recovery	Test				Recovery%		Acceptable Limits						
Carrier/Tracer Recovery	GFPC, Sr90, solid-ALL FSS				73		(25%-125%)						

Notes:

The Qualifiers in this report are defined as follows :

- * A quality control analyte recovery is outside of specified acceptance criteria
 - < Result is less than value reported
 - > Result is greater than value reported
 - A The TIC is a suspected aldol-condensation product
 - B Target analyte was detected in the associated blank
 - BD Results are either below the MDC or tracer recovery is low
 - C Analyte has been confirmed by GC/MS analysis
 - D Results are reported from a diluted aliquot of the sample
 - H Analytical holding time was exceeded
 - J Value is estimated
 - N/A Spike recovery limits do not apply. Sample concentration exceeds spike concentration by 4X or more
 - R Sample results are rejected
 - U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
 - UI Gamma Spectroscopy--Uncertain identification
 - X Consult Case Narrative, Data Summary package, or Project Manager concerning this qualifier
 - Y QC Samples were not spiked with this compound
 - ^ RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL
 - h Preparation or preservation holding time was exceeded
- The above sample is reported on a dry weight basis.

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-018FS
Sample ID: 167556028
Matrix: SE
Collect Date: 27-JUN-06
Receive Date: 21-JUL-06
Collector: Client
Moisture: 52.8%

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Gamma Spec Analysis													
<i>Gamma, Solid-FSS GAM & ALL FSS 226 Ingrowth</i>													
<i>Waived</i>													
Actinium-228		0.727	+/-0.341	0.142	+/-0.341	0.283	pCi/g		MJH1	08/03/06	1551	551081	1
Americium-241	U	0.0233	+/-0.0517	0.0364	+/-0.0517	0.0727	pCi/g						
Bismuth-212	U	0.576	+/-0.466	0.289	+/-0.466	0.577	pCi/g						
Bismuth-214		0.570	+/-0.156	0.0628	+/-0.156	0.126	pCi/g						
Cesium-134	U	0.0389	+/-0.054	0.0427	+/-0.054	0.0854	pCi/g						
Cesium-137		0.398	+/-0.0986	0.0407	+/-0.0986	0.0813	pCi/g						
Cobalt-60		1.09	+/-0.120	0.0241	+/-0.120	0.0482	pCi/g						
Europium-152	U	0.0152	+/-0.131	0.0839	+/-0.131	0.168	pCi/g						
Europium-154	U	0.0517	+/-0.129	0.112	+/-0.129	0.223	pCi/g						
Europium-155	U	0.00474	+/-0.0783	0.0646	+/-0.0783	0.129	pCi/g						
Lead-212		0.948	+/-0.122	0.0394	+/-0.122	0.0788	pCi/g						
Lead-214		0.672	+/-0.155	0.059	+/-0.155	0.118	pCi/g						
Manganese-54	U	-0.022	+/-0.0519	0.0422	+/-0.0519	0.0843	pCi/g						
Niobium-94	U	0.0292	+/-0.0385	0.0344	+/-0.0385	0.0688	pCi/g						
Potassium-40		13.2	+/-1.54	0.306	+/-1.54	0.612	pCi/g						
Radium-226		0.570	+/-0.156	0.0628	+/-0.156	0.126	pCi/g						
Silver-108m	U	-0.0123	+/-0.0354	0.0287	+/-0.0354	0.0573	pCi/g						
Thallium-208		0.334	+/-0.0879	0.0337	+/-0.0879	0.0673	pCi/g						
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid-ALL FSS</i>													
Strontium-90	U	0.0146	+/-0.0182	0.017	+/-0.0183	0.039	pCi/g		BXF1	07/30/06	1226	550821	2

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	BSW1	07/21/06	1519	550554

The following Analytical Methods were performed

Method	Description
1	EML HASL 300, 4.5.2.3
2	EPA 905.0 Modified

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
---------------------------	------	-----------	-------------------

GENERAL ENGINEERING LABORATORIES, LLC
 2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
 Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
 Contact: Mr. Jack McCarthy
 Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-018FS Project: YANK01204
 Sample ID: 167556028 Client ID: YANK001
 Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Surrogate/Tracer recovery	Test				Recovery%		Acceptable Limits						
Carrier/Tracer Recovery	GFPC, Sr90, solid-ALL FSS				58		(25%-125%)						

Notes:

The Qualifiers in this report are defined as follows :

- * A quality control analyte recovery is outside of specified acceptance criteria
 - < Result is less than value reported
 - > Result is greater than value reported
 - A The TIC is a suspected aldol-condensation product
 - B Target analyte was detected in the associated blank
 - BD Results are either below the MDC or tracer recovery is low
 - C Analyte has been confirmed by GC/MS analysis
 - D Results are reported from a diluted aliquot of the sample
 - H Analytical holding time was exceeded
 - J Value is estimated
 - N/A Spike recovery limits do not apply. Sample concentration exceeds spike concentration by 4X or more
 - R Sample results are rejected
 - U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
 - UI Gamma Spectroscopy--Uncertain identification
 - X Consult Case Narrative, Data Summary package, or Project Manager concerning this qualifier
 - Y QC Samples were not spiked with this compound
 - ^ RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL
 - h Preparation or preservation holding time was exceeded
- The above sample is reported on a dry weight basis.

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-021F
Sample ID: 167556029
Matrix: SE
Collect Date: 27-JUN-06
Receive Date: 21-JUL-06
Collector: Client
Moisture: 1.03%

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Alpha Spec Analysis													
<i>Alphaspec Am241, Cm, Solid ALL FSS</i>													
Americium-241	U	-0.162	+/-0.221	0.311	+/-0.222	0.778	pCi/g		MXA	08/01/06	0823	552678	1
Curium-242	U	0.0918	+/-0.285	0.255	+/-0.285	0.693	pCi/g						
Curium-243/244	U	0.287	+/-0.361	0.274	+/-0.364	0.705	pCi/g						
<i>Alphaspec Pu, Solid-ALL FSS</i>													
Plutonium-238	U	0.00298	+/-0.114	0.120	+/-0.114	0.341	pCi/g		JXG1	07/27/06	1535	550872	2
Plutonium-239/240	U	0.00	+/-0.0729	0.00	+/-0.0729	0.101	pCi/g						
<i>Liquid Scint Pu241, Solid-ALL FSS</i>													
Plutonium-241	U	-4.29	+/-8.51	7.32	+/-8.52	15.3	pCi/g		JXG1	08/03/06	0118	550873	3
Rad Gamma Spec Analysis													
<i>Gamma, Solid-FSS GAM & ALL FSS 226 Ingrowth</i>													
<i>Waived</i>													
Actinium-228		0.790	+/-0.172	0.0624	+/-0.172	0.136	pCi/g		MJH1	08/03/06	1646	551081	4
Americium-241	U	0.0198	+/-0.114	0.0743	+/-0.114	0.154	pCi/g						
Bismuth-212		0.359	+/-0.298	0.143	+/-0.298	0.307	pCi/g						
Bismuth-214		0.508	+/-0.0957	0.0358	+/-0.0957	0.0762	pCi/g						
Cesium-134	U	0.0251	+/-0.0294	0.0208	+/-0.0294	0.0447	pCi/g						
Cesium-137		0.398	+/-0.0607	0.0188	+/-0.0607	0.0402	pCi/g						
Cobalt-60	UI	0.00	+/-0.0661	0.0192	+/-0.0661	0.0427	pCi/g						
Europium-152	U	0.0597	+/-0.0735	0.0515	+/-0.0735	0.108	pCi/g						
Europium-154	U	-0.0284	+/-0.0714	0.0577	+/-0.0714	0.127	pCi/g						
Europium-155	U	0.0771	+/-0.0795	0.0563	+/-0.0795	0.116	pCi/g						
Lead-212		0.668	+/-0.0704	0.0297	+/-0.0704	0.0617	pCi/g						
Lead-214		0.682	+/-0.0987	0.0351	+/-0.0987	0.0739	pCi/g						
Manganese-54	U	-0.00723	+/-0.0238	0.0195	+/-0.0238	0.0419	pCi/g						
Niobium-94	U	-0.0046	+/-0.0252	0.0183	+/-0.0252	0.039	pCi/g						
Potassium-40		10.7	+/-0.959	0.144	+/-0.959	0.330	pCi/g						
Radium-226		0.508	+/-0.0957	0.0358	+/-0.0957	0.0762	pCi/g						
Silver-108m	U	-0.0179	+/-0.0211	0.0167	+/-0.0211	0.0354	pCi/g						
Thallium-208		0.259	+/-0.0511	0.0181	+/-0.0511	0.0386	pCi/g						
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid-ALL FSS</i>													
Strontium-90	U	-0.0117	+/-0.0147	0.0189	+/-0.0147	0.0418	pCi/g		BXF1	07/30/06	1226	550821	5
Rad Liquid Scintillation Analysis													
<i>LSC, Tritium Dist, Solid-HTD2, ALL FSS</i>													

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

Contact: East Hampton, Connecticut 06424
Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-021F
Sample ID: 167556029

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Liquid Scintillation Analysis													
<i>LSC, Tritium Dist, Solid-HTD2, ALL FSS</i>													
Tritium	U	1.36	+/-6.20	5.10	+/-6.20	11.0	pCi/g		NXP1	08/02/06	1942	550850	6
<i>Liquid Scint C14, Solid ALL FSS</i>													
Carbon-14	U	-0.049	+/-0.124	0.105	+/-0.124	0.213	pCi/g		ATH2	07/29/06	0827	550851	7
<i>Liquid Scint Fe55, Solid-ALL FSS</i>													
Iron-55	U	-0.0337	+/-19.0	15.0	+/-19.0	31.7	pCi/g		MXP1	08/03/06	1159	550847	8
<i>Liquid Scint Ni63, Solid-ALL FSS</i>													
Nickel-63	U	-5.71	+/-6.73	5.83	+/-6.73	12.0	pCi/g		MXP1	08/14/06	0806	556697	9
<i>Liquid Scint Tc99, Solid-ALL FSS</i>													
Technetium-99	U	0.281	+/-0.191	0.150	+/-0.191	0.311	pCi/g		EGD1	08/03/06	1847	550849	11

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	BSW1	07/21/06	1519	550554

The following Analytical Methods were performed

Method	Description
1	DOE EML HASL-300, Am-05-RC Modified
2	DOE EML HASL-300, Pu-11-RC Modified
3	DOE EML HASL-300, Pu-11-RC Modified
4	EML HASL 300, 4.5.2.3
5	EPA 905.0 Modified
6	EPA 906.0 Modified
7	EPA EERF C-01 Modified
8	DOE RESL Fe-1, Modified
9	DOE RESL Ni-1, Modified
10	DOE RESL Ni-1, Modified
11	DOE EML HASL-300, Tc-02-RC Modified

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
Americium-243	Alphaspec Am241, Cm, Solid ALL	53	(15%-125%)
Plutonium-242	Alphaspec Pu, Solid-ALL FSS	76	(15%-125%)
Carrier/Tracer Recovery	Liquid Scint Pu241, Solid-ALL FS	79	(25%-125%)
Carrier/Tracer Recovery	GFPC, Sr90, solid-ALL FSS	69	(25%-125%)

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-021F
Sample ID: 167556029

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time Batch	Mtd
Carrier/Tracer Recovery		Liquid Scint Fe55, Solid-ALL FS			95		(15%-125%)					
Carrier/Tracer Recovery		Liquid Scint Ni63, Solid-ALL FS			82		(25%-125%)					
Carrier/Tracer Recovery		Liquid Scint Tc99, Solid-ALL FS			87		(15%-125%)					

Notes:

The Qualifiers in this report are defined as follows :

- * A quality control analyte recovery is outside of specified acceptance criteria
 - < Result is less than value reported
 - > Result is greater than value reported
 - A The TIC is a suspected aldo1-condensation product
 - B Target analyte was detected in the associated blank
 - BD Results are either below the MDC or tracer recovery is low
 - C Analyte has been confirmed by GC/MS analysis
 - D Results are reported from a diluted aliquot of the sample
 - H Analytical holding time was exceeded
 - J Value is estimated
 - N/A Spike recovery limits do not apply. Sample concentration exceeds spike concentration by 4X or more
 - R Sample results are rejected
 - U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
 - UI Gamma Spectroscopy--Uncertain identification
 - X Consult Case Narrative, Data Summary package, or Project Manager concerning this qualifier
 - Y QC Samples were not spiked with this compound
 - ^ RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL
 - h Preparation or preservation holding time was exceeded
- The above sample is reported on a dry weight basis.

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-004F
Sample ID: 167556030
Matrix: SE
Collect Date: 28-JUN-06
Receive Date: 21-JUL-06
Collector: Client
Moisture: 26.3%

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Alpha Spec Analysis													
<i>Alphaspec Am241, Cm, Solid ALL FSS</i>													
Americium-241	U	-0.0595	+/-0.0921	0.136	+/-0.0924	0.366	pCi/g		MXA	08/01/06	0823	552678	1
Curium-242	U	-0.0864	+/-0.0564	0.137	+/-0.0574	0.382	pCi/g						
Curium-243/244	U	0.0859	+/-0.207	0.189	+/-0.208	0.472	pCi/g						
<i>Alphaspec Pu, Solid- ALL FSS</i>													
Plutonium-238	U	0.0291	+/-0.0571	0.00	+/-0.0572	0.079	pCi/g		JXG1	07/27/06	1535	550872	2
Plutonium-239/240	U	0.0373	+/-0.0841	0.0575	+/-0.0842	0.194	pCi/g						
<i>Liquid Scint Pu241, Solid-ALL FSS</i>													
Plutonium-241	U	-2.82	+/-8.21	7.01	+/-8.22	14.6	pCi/g		JXG1	08/03/06	0134	550873	3
Rad Gamma Spec Analysis													
<i>Gamma, Solid-FSS GAM & ALL FSS 226 Ingrowth</i>													
<i>Waived</i>													
Actinium-228		0.767	+/-0.182	0.0447	+/-0.182	0.0973	pCi/g		MJH1	08/03/06	1646	551081	4
Americium-241	U	-0.0267	+/-0.103	0.0846	+/-0.103	0.175	pCi/g						
Bismuth-212		0.408	+/-0.269	0.120	+/-0.269	0.256	pCi/g						
Bismuth-214		0.550	+/-0.101	0.0271	+/-0.101	0.0574	pCi/g						
Cesium-134	U	0.0201	+/-0.0204	0.0189	+/-0.0204	0.0402	pCi/g						
Cesium-137	U	-0.00856	+/-0.0183	0.0147	+/-0.0183	0.0313	pCi/g						
Cobalt-60	U	0.00974	+/-0.0202	0.0177	+/-0.0202	0.0384	pCi/g						
Europium-152	U	0.0233	+/-0.0435	0.0395	+/-0.0435	0.0826	pCi/g						
Europium-154	U	-0.0107	+/-0.0585	0.0477	+/-0.0585	0.104	pCi/g						
Europium-155	U	0.0755	+/-0.0498	0.0468	+/-0.0498	0.0964	pCi/g						
Lead-212		0.734	+/-0.083	0.0227	+/-0.083	0.0471	pCi/g						
Lead-214		0.653	+/-0.0961	0.026	+/-0.0961	0.0545	pCi/g						
Manganese-54	U	0.0198	+/-0.0254	0.0151	+/-0.0254	0.0324	pCi/g						
Niobium-94	U	0.0179	+/-0.0169	0.0152	+/-0.0169	0.032	pCi/g						
Potassium-40		13.2	+/-1.21	0.144	+/-1.21	0.319	pCi/g						
Radium-226		0.550	+/-0.101	0.0271	+/-0.101	0.0574	pCi/g						
Silver-108m	U	0.00388	+/-0.014	0.0124	+/-0.014	0.0261	pCi/g						
Thallium-208		0.282	+/-0.0555	0.0163	+/-0.0555	0.0345	pCi/g						
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid-ALL FSS</i>													
Strontium-90	U	0.0198	+/-0.0185	0.0167	+/-0.0185	0.0377	pCi/g		BXF1	07/30/06	1226	550821	5
Rad Liquid Scintillation Analysis													
<i>LSC, Tritium Dist, Solid-HTD2, ALL FSS</i>													

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-004F
Sample ID: 167556030

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Liquid Scintillation Analysis													
<i>LSC, Tritium Dist, Solid-HTD2, ALL FSS</i>													
Tritium	U	-2.23	+/-5.76	5.02	+/-5.76	10.8	pCi/g		NXP1	08/02/06	1957	550850	6
<i>Liquid Scint C14, Solid ALL FSS</i>													
Carbon-14	U	0.00818	+/-0.125	0.105	+/-0.125	0.214	pCi/g		ATH2	07/29/06	1003	550851	7
<i>Liquid Scint Fe55, Solid-ALL FSS</i>													
Iron-55	U	14.1	+/-21.5	16.4	+/-21.7	34.7	pCi/g		MXP1	08/03/06	1216	550847	8
<i>Liquid Scint Ni63, Solid-ALL FSS</i>													
Nickel-63	U	-5.42	+/-5.34	4.65	+/-5.34	9.59	pCi/g		MXP1	08/14/06	0838	556697	9
<i>Liquid Scint Tc99, Solid-ALL FSS</i>													
Technetium-99	U	0.178	+/-0.190	0.153	+/-0.190	0.317	pCi/g		EGD1	08/03/06	1946	550849	11

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	BSW1	07/21/06	1519	550554

The following Analytical Methods were performed

Method	Description
1	DOE EML HASL-300, Am-05-RC Modified
2	DOE EML HASL-300, Pu-11-RC Modified
3	DOE EML HASL-300, Pu-11-RC Modified
4	EML HASL 300, 4.5.2.3
5	EPA 905.0 Modified
6	EPA 906.0 Modified
7	EPA EERF C-01 Modified
8	DOE RESL Fe-1, Modified
9	DOE RESL Ni-1, Modified
10	DOE RESL Ni-1, Modified
11	DOE EML HASL-300, Tc-02-RC Modified

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
Americium-243	Alphaspec Am241, Cm, Solid ALL	78	(15%-125%)
Plutonium-242	Alphaspec Pu, Solid-ALL FSS	89	(15%-125%)
Carrier/Tracer Recovery	Liquid Scint Pu241, Solid-ALL FS	84	(25%-125%)
Carrier/Tracer Recovery	GFPC, Sr90, solid-ALL FSS	66	(25%-125%)

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-004F
Sample ID: 167556030

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Carrier/Tracer Recovery		Liquid Scint Fe55, Solid-ALL FS			91		(15%-125%)						
Carrier/Tracer Recovery		Liquid Scint Ni63, Solid-ALL FS			95		(25%-125%)						
Carrier/Tracer Recovery		Liquid Scint Tc99, Solid-ALL FS			85		(15%-125%)						

Notes:

The Qualifiers in this report are defined as follows :

- * A quality control analyte recovery is outside of specified acceptance criteria
- < Result is less than value reported
- > Result is greater than value reported
- A The TIC is a suspected aldol-condensation product
- B Target analyte was detected in the associated blank
- BD Results are either below the MDC or tracer recovery is low
- C Analyte has been confirmed by GC/MS analysis
- D Results are reported from a diluted aliquot of the sample
- H Analytical holding time was exceeded
- J Value is estimated
- N/A Spike recovery limits do not apply. Sample concentration exceeds spike concentration by 4X or more
- R Sample results are rejected
- U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
- UI Gamma Spectroscopy--Uncertain identification
- X Consult Case Narrative, Data Summary package, or Project Manager concerning this qualifier
- Y QC Samples were not spiked with this compound
- ^ RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL
- h Preparation or preservation holding time was exceeded

The above sample is reported on a dry weight basis.

GENERAL ENGINEERING LABORATORIES, LLC
2040 Savage Road Charleston SC 29407 – (843) 556-8171 – www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

Contact: East Hampton, Connecticut 06424
Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID:	9106-0015-015F	Project:	YANK01204
Sample ID:	167556031	Client ID:	YANK001
Matrix:	SE	Vol. Recv.:	
Collect Date:	28-JUN-06		
Receive Date:	21-JUL-06		
Collector:	Client		
Moisture:	29.9%		

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Alpha Spec Analysis													
<i>Alphaspec Am241, Cm, Solid ALL FSS</i>													
Americium-241	U	0.00402	+/-0.0974	0.101	+/-0.0974	0.287	pCi/g		MXA	08/01/06	0823	552678	1
Curium-242	U	-0.0145	+/-0.114	0.131	+/-0.114	0.360	pCi/g						
Curium-243/244	U	-0.0227	+/-0.170	0.190	+/-0.170	0.465	pCi/g						
<i>Alphaspec Pu, Solid-ALL FSS</i>													
Plutonium-238	U	-0.00829	+/-0.0163	0.0394	+/-0.0163	0.172	pCi/g		JXG1	07/27/06	1535	550872	2
Plutonium-239/240	U	-0.0497	+/-0.0398	0.0964	+/-0.0401	0.286	pCi/g						
<i>Liquid Scint Pu241, Solid-ALL FSS</i>													
Plutonium-241	U	-4.09	+/-8.10	6.97	+/-8.11	14.5	pCi/g		JXG1	08/03/06	0150	550873	3
Rad Gamma Spec Analysis													
<i>Gamma, Solid-FSS GAM & ALL FSS 226 Ingrowth</i>													
<i>Waived</i>													
Actinium-228		0.747	+/-0.157	0.0482	+/-0.157	0.103	pCi/g		MJH1	08/03/06	1646	551081	4
Americium-241	U	0.021	+/-0.108	0.0836	+/-0.108	0.173	pCi/g						
Bismuth-212		0.427	+/-0.259	0.108	+/-0.259	0.229	pCi/g						
Bismuth-214		0.531	+/-0.0855	0.0268	+/-0.0855	0.0563	pCi/g						
Cesium-134	UI	0.00	+/-0.0359	0.0195	+/-0.0359	0.0408	pCi/g						
Cesium-137		0.208	+/-0.0325	0.0153	+/-0.0325	0.0321	pCi/g						
Cobalt-60		0.0707	+/-0.0298	0.0144	+/-0.0298	0.0311	pCi/g						
Europium-152	U	-0.0367	+/-0.0423	0.0355	+/-0.0423	0.0742	pCi/g						
Europium-154	U	-0.011	+/-0.0561	0.0453	+/-0.0561	0.0969	pCi/g						
Europium-155	U	0.0566	+/-0.0709	0.0483	+/-0.0709	0.0997	pCi/g						
Lead-212		0.804	+/-0.0557	0.0237	+/-0.0557	0.049	pCi/g						
Lead-214		0.637	+/-0.0847	0.0267	+/-0.0847	0.0558	pCi/g						
Manganese-54	UI	0.00	+/-0.0203	0.0129	+/-0.0203	0.0276	pCi/g						
Niobium-94	U	0.0205	+/-0.0372	0.0134	+/-0.0372	0.0281	pCi/g						
Potassium-40		13.8	+/-0.775	0.120	+/-0.775	0.263	pCi/g						
Radium-226		0.531	+/-0.0855	0.0268	+/-0.0855	0.0563	pCi/g						
Silver-108m	U	0.00734	+/-0.0147	0.013	+/-0.0147	0.0272	pCi/g						
Thallium-208		0.242	+/-0.0419	0.0146	+/-0.0419	0.0306	pCi/g						
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid-ALL FSS</i>													
Strontium-90	U	0.0211	+/-0.0182	0.0161	+/-0.0182	0.0363	pCi/g		BXF1	07/30/06	1226	550821	5
Rad Liquid Scintillation Analysis													
<i>LSC, Tritium Dist, Solid-HTD2, ALL FSS</i>													

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-015F
Sample ID: 167556031

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Liquid Scintillation Analysis													
<i>LSC, Tritium Dist, Solid-HTD2, ALL FSS</i>													
Tritium	U	2.73	+/-7.57	6.14	+/-7.57	13.3	pCi/g		NXP1	08/02/06	2013	550850	6
<i>Liquid Scint C14, Solid All, FSS</i>													
Carbon-14	U	-0.124	+/-0.124	0.106	+/-0.124	0.216	pCi/g		ATH2	07/29/06	1104	550851	7
<i>Liquid Scint Fe55, Solid-ALL FSS</i>													
Iron-55	U	3.86	+/-16.9	13.2	+/-16.9	27.8	pCi/g		MXP1	08/03/06	1232	550847	8
<i>Liquid Scint Ni63, Solid-ALL FSS</i>													
Nickel-63	U	-1.76	+/-7.03	5.96	+/-7.03	12.3	pCi/g		MXPI	08/14/06	0909	556697	9
<i>Liquid Scint Tc99, Solid-ALL FSS</i>													
Technetium-99	U	0.175	+/-0.186	0.150	+/-0.186	0.311	pCi/g		EGD1	08/03/06	2002	550849	11

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	BSW1	07/21/06	1519	550554

The following Analytical Methods were performed

Method	Description
1	DOE EML HASL-300, Am-05-RC Modified
2	DOE EML HASL-300, Pu-11-RC Modified
3	DOE EML HASL-300, Pu-11-RC Modified
4	EML HASL 300, 4.5.2.3
5	EPA 905.0 Modified
6	EPA 906.0 Modified
7	EPA EERF C-01 Modified
8	DOE RESL Fe-1, Modified
9	DOE RESL Ni-1, Modified
10	DOE RESL Ni-1, Modified
11	DOE EML HASL-300, Tc-02-RC Modified

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
Americium-243	Alphaspec Am241, Cm, Solid ALL	102	(15%-125%)
Plutonium-242	Alphaspec Pu, Solid-ALL FSS	78	(15%-125%)
Carrier/Tracer Recovery	Liquid Scint Pu241, Solid-ALL FS	83	(25%-125%)
Carrier/Tracer Recovery	GFPC, Sr90, solid-ALL FSS	68	(25%-125%)

GENERAL ENGINEERING LABORATORIES, LLC
 2040 Savage Road Charleston SC 29407 – (843) 556-8171 – www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
 Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
 Contact: Mr. Jack McCarthy
 Project: Soils PO# 002332

Report Date: August 14, 2006

Client Sample ID: 9106-0015-015F
 Sample ID: 167556031

Project: YANK01204
 Client ID: YANK001
 Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time Batch	Mtd
Carrier/Tracer Recovery		Liquid Scint Fe55, Solid-ALL FS			97		(15%-125%)					
Carrier/Tracer Recovery		Liquid Scint Ni63, Solid-ALL FS			86		(25%-125%)					
Carrier/Tracer Recovery		Liquid Scint Tc99, Solid-ALL FS			87		(15%-125%)					

Notes:

The Qualifiers in this report are defined as follows :

- * A quality control analyte recovery is outside of specified acceptance criteria
 - < Result is less than value reported
 - > Result is greater than value reported
 - A The TIC is a suspected aldol-condensation product
 - B Target analyte was detected in the associated blank
 - BD Results are either below the MDC or tracer recovery is low
 - C Analyte has been confirmed by GC/MS analysis
 - D Results are reported from a diluted aliquot of the sample
 - H Analytical holding time was exceeded
 - J Value is estimated
 - N/A Spike recovery limits do not apply. Sample concentration exceeds spike concentration by 4X or more
 - R Sample results are rejected
 - U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
 - UI Gamma Spectroscopy—Uncertain identification
 - X Consult Case Narrative, Data Summary package, or Project Manager concerning this qualifier
 - Y QC Samples were not spiked with this compound
 - ^ RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL
 - h Preparation or preservation holding time was exceeded
- The above sample is reported on a dry weight basis.

QUALITY CONTROL DATA

GENERAL ENGINEERING LABORATORIES, LLC
 2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

QC Summary

Report Date: August 14, 2006
 Page 1 of 13

Client : Connecticut Yankee Atomic Power
 362 Injun Hollow Rd

 East Hampton, Connecticut
 Contact: Mr. Jack McCarthy
 Workorder: 167556

Parname	NOM	Sample	Qual	QC	Units	RPD%	REC%	Range	Anlst	Date	Time
Rad Alpha Spec											
Batch 550872											
QC1201141928	167555016	DUP									
Plutonium-238	U	0.00	U	0.00115	pCi/g	200		(0% - 100%)	JXG1	07/27/06	15:35
	Uncert:	+/-0.0636		+/-0.0623							
	TPU:	+/-0.0636		+/-0.0623							
Plutonium-239/240	U	-0.00648	U	-0.0195	pCi/g	100		(0% - 100%)			
	Uncert:	+/-0.0721		+/-0.0665							
	TPU:	+/-0.0721		+/-0.0665							
QC1201141930	LCS										
Plutonium-238			U	-0.095	pCi/g			(75%-125%)		07/27/06	15:34
	Uncert:			+/-0.103							
	TPU:			+/-0.103							
Plutonium-239/240	12.0			9.17	pCi/g		76	(75%-125%)			
	Uncert:			+/-1.01							
	TPU:			+/-1.37							
QC1201141927	MB										
Plutonium-238			U	0.017	pCi/g					07/27/06	15:35
	Uncert:			+/-0.0678							
	TPU:			+/-0.0678							
Plutonium-239/240			U	0.0249	pCi/g						
	Uncert:			+/-0.066							
	TPU:			+/-0.0661							
QC1201141929	167555016	MS									
Plutonium-238	U	0.00	U	0.0791	pCi/g			(75%-125%)			
	Uncert:	+/-0.0636		+/-0.121							
	TPU:	+/-0.0636		+/-0.121							
Plutonium-239/240	12.3	U	-0.00648	11.9	pCi/g		97	(75%-125%)			
	Uncert:	+/-0.0721		+/-1.26							
	TPU:	+/-0.0721		+/-1.79							
Batch 550873											
QC1201141932	167555016	DUP									
Plutonium-241	U	-3.28	U	-3.69	pCi/g	0		(0% - 100%)	JXG1	08/03/06	02:22
	Uncert:	+/-7.74		+/-7.74							
	TPU:	+/-7.74		+/-7.75							
QC1201141934	LCS										
Plutonium-241	139			124	pCi/g		90	(75%-125%)		08/03/06	02:54
	Uncert:			+/-12.3							
	TPU:			+/-17.2							
QC1201141931	MB										
Plutonium-241			U	-3.62	pCi/g					08/03/06	02:06
	Uncert:			+/-8.07							
	TPU:			+/-8.08							
QC1201141933	167555016	MS									
Plutonium-241	140	U	-3.28	133	pCi/g		95	(75%-125%)		08/03/06	02:38
	Uncert:	+/-7.74		+/-13.0							

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

QC Summary

Workorder: 167556

Page 2 of 13

Parmname	NOM	Sample	Qual	QC	Units	RPD%	REC%	Range	Anlst	Date	Time
Rad Alpha Spec											
Batch	550873										
		TPU:	+/-7.74								
Batch	552678										
		TPU:	+/-7.74								
QC1201146078	167555016	DUP									
Americium-241		U	0.166	U	0.0987	pCi/g	51	(0% - 100%)	JXA1	08/01/06	12:11
		Uncert:	+/-0.236		+/-0.149						
		TPU:	+/-0.237		+/-0.149						
Curium-242		U	0.0107	U	0.0613	pCi/g	141	(0% - 100%)			
		Uncert:	+/-0.0813		+/-0.0979						
		TPU:	+/-0.0814		+/-0.0982						
Curium-243/244		U	0.0872	U	0.0225	pCi/g	118	(0% - 100%)			
		Uncert:	+/-0.181		+/-0.169						
		TPU:	+/-0.181		+/-0.169						
QC1201146080	LCS										
Americium-241			13.3		16.6	pCi/g		125 (75%-125%)			
		Uncert:			+/-1.61						
		TPU:			+/-2.68						
Curium-242				U	0.00	pCi/g					
		Uncert:			+/-0.0807						
		TPU:			+/-0.0807						
Curium-243/244			16.2		16.8	pCi/g		104 (75%-125%)			
		Uncert:			+/-1.63						
		TPU:			+/-2.71						
QC1201146077	MB										
Americium-241				U	-0.0657	pCi/g				08/01/06	08:23
		Uncert:			+/-0.0872						
		TPU:			+/-0.0876						
Curium-242				U	-0.0159	pCi/g					
		Uncert:			+/-0.022						
		TPU:			+/-0.0221						
Curium-243/244				U	0.0313	pCi/g					
		Uncert:			+/-0.172						
		TPU:			+/-0.172						
QC1201146079	167555016	MS									
Americium-241		U	0.166		13.0	pCi/g		96 (75%-125%)		08/01/06	12:11
		Uncert:	+/-0.236		+/-1.30						
		TPU:	+/-0.237		+/-2.05						
Curium-242		U	0.0107	U	-0.00953	pCi/g					
		Uncert:	+/-0.0813		+/-0.0187						
		TPU:	+/-0.0814		+/-0.0187						
Curium-243/244		U	0.0872		17.7	pCi/g		107 (75%-125%)			
		Uncert:	+/-0.181		+/-1.52						
		TPU:	+/-0.181		+/-2.65						
Rad Gamma Spec											
Batch	551078										
QC1201142454	167556001	DUP									
Actinium-228			0.799		0.934	pCi/g	38	(0% - 100%)	MJH1	08/03/06	07:50
		Uncert:	+/-0.156		+/-0.173						
		TPU:	+/-0.156		+/-0.173						

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

QC Summary

Workorder: 167556

Page 3 of 13

Parmname	NOM	Sample	Qual	QC	Units	RPD%	REC%	Range	Anlst	Date	Time
Rad Gamma Spec											
Batch	551078										
Americium-241	U	0.0246	U	0.016	pCi/g	122		(0% - 100%)			
	Uncert:	+/-0.104		+/-0.113							
	TPU:	+/-0.104		+/-0.113							
Bismuth-212		0.457		0.333	pCi/g	32		(0% - 100%)			
	Uncert:	+/-0.238		+/-0.245							
	TPU:	+/-0.238		+/-0.245							
Bismuth-214		0.612		0.623	pCi/g	1		(0% - 100%)			
	Uncert:	+/-0.0886		+/-0.0891							
	TPU:	+/-0.0886		+/-0.0891							
Cesium-134	U	0.0453	U	0.0442	pCi/g	5		(0% - 100%)			
	Uncert:	+/-0.0355		+/-0.0223							
	TPU:	+/-0.0355		+/-0.0223							
Cesium-137		0.346		0.426	pCi/g	23		(0% - 100%)			
	Uncert:	+/-0.0445		+/-0.0418							
	TPU:	+/-0.0445		+/-0.0418							
Cobalt-60		0.697		0.882	pCi/g	20*		(0%-20%)			
	Uncert:	+/-0.0732		+/-0.0656							
	TPU:	+/-0.0732		+/-0.0656							
Europium-152	U	0.0354	U	-0.00721	pCi/g	2650		(0% - 100%)			
	Uncert:	+/-0.0503		+/-0.051							
	TPU:	+/-0.0503		+/-0.051							
Europium-154	U	-0.00728	UI	0.00	pCi/g	151		(0% - 100%)			
	Uncert:	+/-0.0592		+/-0.0709							
	TPU:	+/-0.0592		+/-0.0709							
Europium-155	U	0.0128	U	0.0488	pCi/g	42		(0% - 100%)			
	Uncert:	+/-0.0649		+/-0.0617							
	TPU:	+/-0.0649		+/-0.0617							
Lead-212		0.742		0.848	pCi/g	12		(0% - 20%)			
	Uncert:	+/-0.0572		+/-0.0639							
	TPU:	+/-0.0572		+/-0.0639							
Lead-214		0.625		0.666	pCi/g	5		(0% - 20%)			
	Uncert:	+/-0.0879		+/-0.0868							
	TPU:	+/-0.0879		+/-0.0868							
Manganese-54	U	0.022	U	0.00611	pCi/g	156		(0% - 100%)			
	Uncert:	+/-0.0235		+/-0.0227							
	TPU:	+/-0.0235		+/-0.0227							
Niobium-94	U	0.00715	U	0.0114	pCi/g	46		(0% - 100%)			
	Uncert:	+/-0.0183		+/-0.0172							
	TPU:	+/-0.0183		+/-0.0172							
Potassium-40		12.5		14.1	pCi/g	12		(0% - 20%)			
	Uncert:	+/-0.783		+/-0.877							
	TPU:	+/-0.783		+/-0.877							
Radium-226		0.612		0.623	pCi/g	1		(0% - 100%)			
	Uncert:	+/-0.0886		+/-0.0891							
	TPU:	+/-0.0886		+/-0.0891							
Silver-108m	U	0.00466	U	-0.00177	pCi/g	424		(0% - 100%)			
	Uncert:	+/-0.0164		+/-0.0177							
	TPU:	+/-0.0164		+/-0.0177							

GENERAL ENGINEERING LABORATORIES, LLC
 2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

QC Summary

Workorder: 167556

Page 4 of 13

Parmname	NOM	Sample	Qual	QC	Units	RPD%	REC%	Range	Anlst	Date	Time
Rad Gamma Spec											
Batch	551078										
Thallium-208		0.219		0.243	pCi/g	18		(0% - 100%)			
		Uncert:		+/-0.0419							
		TPU:		+/-0.0419							
QC1201142455	LCS										
Actinium-228			U	0.0932	pCi/g					08/03/06	07:51
		Uncert:		+/-0.385							
		TPU:		+/-0.385							
Americium-241	23.4			25.5	pCi/g		109	(75%-125%)			
		Uncert:		+/-2.06							
		TPU:		+/-2.06							
Bismuth-212			U	-0.0457	pCi/g						
		Uncert:		+/-0.703							
		TPU:		+/-0.703							
Bismuth-214			U	-0.0521	pCi/g						
		Uncert:		+/-0.173							
		TPU:		+/-0.173							
Cesium-134			U	0.0241	pCi/g						
		Uncert:		+/-0.0978							
		TPU:		+/-0.0978							
Cesium-137	9.60			10.7	pCi/g		111	(75%-125%)			
		Uncert:		+/-0.956							
		TPU:		+/-0.956							
Cobalt-60	14.7			15.2	pCi/g		103	(75%-125%)			
		Uncert:		+/-0.948							
		TPU:		+/-0.948							
Europium-152			U	-0.0199	pCi/g						
		Uncert:		+/-0.228							
		TPU:		+/-0.228							
Europium-154			U	-0.00469	pCi/g						
		Uncert:		+/-0.229							
		TPU:		+/-0.229							
Europium-155			U	-0.0534	pCi/g						
		Uncert:		+/-0.275							
		TPU:		+/-0.275							
Lead-212			U	0.131	pCi/g						
		Uncert:		+/-0.129							
		TPU:		+/-0.129							
Lead-214			U	-0.0264	pCi/g						
		Uncert:		+/-0.155							
		TPU:		+/-0.155							
Manganese-54			U	-0.0301	pCi/g						
		Uncert:		+/-0.0923							
		TPU:		+/-0.0923							
Niobium-94			U	0.0336	pCi/g						
		Uncert:		+/-0.0841							
		TPU:		+/-0.0841							
Potassium-40			U	0.279	pCi/g						
		Uncert:		+/-0.767							

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

QC Summary

Workorder: 167556

Page 5 of 13

Parmname	NOM	Sample Qual	QC	Units	RPD%	REC%	Range	Anlst	Date	Time
Rad Gamma Spec										
Batch 551078										
Radium-226			TPU: +/-0.767							
		U	-0.0521	pCi/g						
			Uncert: +/-0.173							
Silver-108m			TPU: +/-0.173							
		U	0.0643	pCi/g						
			Uncert: +/-0.0799							
Thallium-208			TPU: +/-0.0799							
		U	0.0241	pCi/g						
			Uncert: +/-0.0853							
			TPU: +/-0.0853							
QC1201142453 MB										
Actinium-228									08/03/06	07:50
		U	0.0428	pCi/g						
			Uncert: +/-0.100							
			TPU: +/-0.100							
Americium-241										
		U	-0.0272	pCi/g						
			Uncert: +/-0.0189							
			TPU: +/-0.0189							
Bismuth-212										
		U	0.0764	pCi/g						
			Uncert: +/-0.150							
			TPU: +/-0.150							
Bismuth-214										
		U	0.0338	pCi/g						
			Uncert: +/-0.0366							
			TPU: +/-0.0366							
Cesium-134										
		U	0.00494	pCi/g						
			Uncert: +/-0.0199							
			TPU: +/-0.0199							
Cesium-137										
		U	0.00159	pCi/g						
			Uncert: +/-0.0169							
			TPU: +/-0.0169							
Cobalt-60										
		UI	0.00	pCi/g						
			Uncert: +/-0.0635							
			TPU: +/-0.0635							
Europium-152										
		U	0.0138	pCi/g						
			Uncert: +/-0.0386							
			TPU: +/-0.0386							
Europium-154										
		U	0.0793	pCi/g						
			Uncert: +/-0.059							
			TPU: +/-0.059							
Europium-155										
		U	-0.0205	pCi/g						
			Uncert: +/-0.0333							
			TPU: +/-0.0333							
Lead-212										
		U	0.0209	pCi/g						
			Uncert: +/-0.0501							
			TPU: +/-0.0501							
Lead-214										
		U	0.0167	pCi/g						
			Uncert: +/-0.0313							
			TPU: +/-0.0313							
Manganese-54										
		U	-0.00145	pCi/g						

GENERAL ENGINEERING LABORATORIES, LLC
 2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

QC Summary

Workorder: 167556

Page 6 of 13

Parmname	NOM	Sample	Qual	QC	Units	RPD%	REC%	Range	Anlst	Date	Time
Rad Gamma Spec											
Batch	551078										
		Uncert:		+/-0.0166							
		TPU:		+/-0.0166							
Niobium-94			U	-0.00102	pCi/g						
		Uncert:		+/-0.0166							
		TPU:		+/-0.0166							
Potassium-40			U	0.127	pCi/g						
		Uncert:		+/-0.219							
		TPU:		+/-0.219							
Radium-226			U	0.0338	pCi/g						
		Uncert:		+/-0.0366							
		TPU:		+/-0.0366							
Silver-108m			U	-0.00435	pCi/g						
		Uncert:		+/-0.0144							
		TPU:		+/-0.0144							
Thallium-208			U	0.0137	pCi/g						
		Uncert:		+/-0.0191							
		TPU:		+/-0.0191							
Batch	551081										
	QC1201142460 167556029 DUP										
Actinium-228				0.790	pCi/g	47		(0% - 100%)	MJH1	08/03/06	20:35
		Uncert:		+/-0.172							
		TPU:		+/-0.172							
Americium-241			U	0.0198	pCi/g	127		(0% - 100%)			
		Uncert:		+/-0.114							
		TPU:		+/-0.114							
Bismuth-212				0.359	pCi/g	71		(0% - 100%)			
		Uncert:		+/-0.298							
		TPU:		+/-0.298							
Bismuth-214				0.508	pCi/g	1		(0% - 100%)			
		Uncert:		+/-0.0957							
		TPU:		+/-0.0957							
Cesium-134			U	0.0251	pCi/g	108		(0% - 100%)			
		Uncert:		+/-0.0294							
		TPU:		+/-0.0294							
Cesium-137				0.398	pCi/g	8		(0% - 100%)			
		Uncert:		+/-0.0607							
		TPU:		+/-0.0607							
Cobalt-60			UI	0.00	pCi/g	14		(0% - 100%)			
		Uncert:		+/-0.0661							
		TPU:		+/-0.0661							
Europium-152			U	0.0597	pCi/g	40		(0% - 100%)			
		Uncert:		+/-0.0735							
		TPU:		+/-0.0735							
Europium-154			U	-0.0284	pCi/g	81		(0% - 100%)			
		Uncert:		+/-0.0714							
		TPU:		+/-0.0714							
Europium-155			U	0.0771	pCi/g	16		(0% - 100%)			
		Uncert:		+/-0.0795							

GENERAL ENGINEERING LABORATORIES, LLC
 2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

QC Summary

Workorder: 167556

Page 7 of 13

Parmname	NOM	Sample Qual	QC	Units	RPD%	REC%	Range	Anlst	Date	Time
Rad Gamma Spec										
Batch	551081									
Lead-212		TPU: +/-0.0795 0.668	+/-0.0667 0.725	pCi/g	8		(0% - 20%)			
		Uncert: +/-0.0704	+/-0.115							
Lead-214		TPU: +/-0.0704 0.682	+/-0.115 0.682	pCi/g	0		(0% - 20%)			
		Uncert: +/-0.0987	+/-0.145							
Manganese-54		TPU: +/-0.0987 U -0.00723	+/-0.145 U -0.00539	pCi/g	29		(0% - 100%)			
		Uncert: +/-0.0238	+/-0.0291							
Niobium-94		TPU: +/-0.0238 U -0.0046	+/-0.0291 U 0.00917	pCi/g	604		(0% - 100%)			
		Uncert: +/-0.0252	+/-0.0277							
Potassium-40		TPU: +/-0.0252 10.7	+/-0.0277 10.8	pCi/g	1		(0% - 20%)			
		Uncert: +/-0.959	+/-1.39							
Radium-226		TPU: +/-0.959 0.508	+/-1.39 0.502	pCi/g	1		(0% - 100%)			
		Uncert: +/-0.0957	+/-0.135							
Silver-108m		TPU: +/-0.0957 U -0.0179	+/-0.135 U -0.00479	pCi/g	116		(0% - 100%)			
		Uncert: +/-0.0211	+/-0.0252							
Thallium-208		TPU: +/-0.0211 0.259	+/-0.0252 0.201	pCi/g	25		(0% - 100%)			
		Uncert: +/-0.0511	+/-0.0618							
		TPU: +/-0.0511	+/-0.0618							
QC1201142461	LCS									
Actinium-228			U 0.679	pCi/g					08/04/06	05:20
		Uncert: +/-0.533								
Americium-241	23.4	TPU: +/-0.533 23.9	+/-0.533 23.9	pCi/g		102	(75%-125%)			
		Uncert: +/-0.486	+/-0.486							
Bismuth-212		TPU: +/-0.486 U -0.492	+/-0.486 U -0.492	pCi/g						
		Uncert: +/-0.975	+/-0.975							
Bismuth-214		TPU: +/-0.975 U 0.0917	+/-0.975 U 0.0917	pCi/g						
		Uncert: +/-0.224	+/-0.224							
Cesium-134		TPU: +/-0.224 U 0.112	+/-0.224 U 0.112	pCi/g						
		Uncert: +/-0.141	+/-0.141							
Cesium-137	9.60	TPU: +/-0.141 9.60	+/-0.141 10.4	pCi/g		108	(75%-125%)			
		Uncert: +/-0.482	+/-0.482							
Cobalt-60	14.7	TPU: +/-0.482 14.7	+/-0.482 15.1	pCi/g		103	(75%-125%)			
		Uncert: +/-0.658	+/-0.658							
Europium-152		TPU: +/-0.658 U 0.251	+/-0.658 U 0.251	pCi/g						

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

QC Summary

Workorder: 167556

Page 8 of 13

Parmname	NOM	Sample Qual	QC	Units	RPD%	REC%	Range	Anlst	Date	Time
Rad Gamma Spec										
Batch	551081									
			Uncert:							
			TPU:							
Europium-154		U	-0.0933	pCi/g						
			Uncert:							
			TPU:							
Europium-155		U	0.0511	pCi/g						
			Uncert:							
			TPU:							
Lead-212		U	0.0671	pCi/g						
			Uncert:							
			TPU:							
Lead-214		U	0.0144	pCi/g						
			Uncert:							
			TPU:							
Manganese-54		U	0.0924	pCi/g						
			Uncert:							
			TPU:							
Niobium-94		U	0.0204	pCi/g						
			Uncert:							
			TPU:							
Potassium-40		U	-0.16	pCi/g						
			Uncert:							
			TPU:							
Radium-226		U	0.0917	pCi/g						
			Uncert:							
			TPU:							
Silver-108m		U	0.0594	pCi/g						
			Uncert:							
			TPU:							
Thallium-208		U	0.00785	pCi/g						
			Uncert:							
			TPU:							
QC1201142459	MB									
Actinium-228		U	0.0349	pCi/g					08/03/06	16:47
			Uncert:							
			TPU:							
Americium-241		U	-0.0155	pCi/g						
			Uncert:							
			TPU:							
Bismuth-212		U	-0.00927	pCi/g						
			Uncert:							
			TPU:							
Bismuth-214		U	0.000364	pCi/g						
			Uncert:							
			TPU:							
Cesium-134		U	-0.0203	pCi/g						
			Uncert:							
			TPU:							

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

QC Summary

Workorder: 167556

Page 9 of 13

Parmname	NOM	Sample Qual	QC	Units	RPD%	REC%	Range	Anlst	Date	Time
Rad Gamma Spec										
Batch	551081									
Cesium-137		U	0.00632	pCi/g						
	Uncert:		+/-0.0155							
	TPU:		+/-0.0155							
Cobalt-60		U	0.00791	pCi/g						
	Uncert:		+/-0.0133							
	TPU:		+/-0.0133							
Europium-152		U	0.0226	pCi/g						
	Uncert:		+/-0.0397							
	TPU:		+/-0.0397							
Europium-154		U	-0.0169	pCi/g						
	Uncert:		+/-0.0349							
	TPU:		+/-0.0349							
Europium-155		U	0.00825	pCi/g						
	Uncert:		+/-0.0314							
	TPU:		+/-0.0314							
Lead-212		UI	0.00	pCi/g						
	Uncert:		+/-0.0486							
	TPU:		+/-0.0486							
Lead-214		U	0.00294	pCi/g						
	Uncert:		+/-0.0376							
	TPU:		+/-0.0376							
Manganese-54		U	-0.005	pCi/g						
	Uncert:		+/-0.0155							
	TPU:		+/-0.0155							
Niobium-94		U	-0.00181	pCi/g						
	Uncert:		+/-0.0139							
	TPU:		+/-0.0139							
Potassium-40		U	0.133	pCi/g						
	Uncert:		+/-0.157							
	TPU:		+/-0.157							
Radium-226		U	0.000364	pCi/g						
	Uncert:		+/-0.0284							
	TPU:		+/-0.0284							
Silver-108m		U	0.0148	pCi/g						
	Uncert:		+/-0.0137							
	TPU:		+/-0.0137							
Thallium-208		U	0.0242	pCi/g						
	Uncert:		+/-0.0173							
	TPU:		+/-0.0173							
Rad Gas Flow										
Batch	550820									
QC1201141747	167556008 DUP									
Strontium-90		U	0.0128	U	-0.00326	pCi/g	0	(0% - 100%)	BXF1	07/31/06 12:27
	Uncert:		+/-0.0169		+/-0.0135					
	TPU:		+/-0.0169		+/-0.0135					
QC1201141749	LCS									
Strontium-90	1.48				1.27	pCi/g	86	(75%-125%)		07/31/06 14:58
	Uncert:				+/-0.0879					

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

QC Summary

Workorder: 167556

Page 10 of 13

Parmname	NOM	Sample	Qual	QC	Units	RPD%	REC%	Range	Anlst	Date	Time
Rad Gas Flow											
Batch	550820										
QC1201141746	MB	TPU:		+/-0.0956							
Strontium-90			U	-0.0183	pCi/g					07/31/06	12:27
		Uncert:		+/-0.00866							
		TPU:		+/-0.00868							
QC1201141748	167556008	MS									
Strontium-90		1.56	U	0.0128	1.27	pCi/g	82	(75%-125%)		07/31/06	14:58
		Uncert:		+/-0.0169							
		TPU:		+/-0.0169							
Batch	550821										
QC1201141751	167554004	DUP									
Strontium-90			U	-0.00221	U	-0.00355	pCi/g	0	(0% - 100%)	BXF1	07/30/06 12:41
		Uncert:		+/-0.0165							
		TPU:		+/-0.0165							
QC1201141753	LCS										
Strontium-90		1.53			1.55	pCi/g	102	(75%-125%)		07/30/06	17:23
		Uncert:		+/-0.101							
		TPU:		+/-0.111							
QC1201141750	MB										
Strontium-90			U	-0.00113	U	-0.00113	pCi/g			07/30/06	12:26
		Uncert:		+/-0.014							
		TPU:		+/-0.014							
QC1201141752	167554004	MS									
Strontium-90		1.54	U	-0.00221	1.43	pCi/g	93	(75%-125%)		07/30/06	12:41
		Uncert:		+/-0.0165							
		TPU:		+/-0.0165							
Rad Liquid Scintillation											
Batch	550847										
QC1201141836	167555017	DUP									
Iron-55			U	8.69	U	0.0266	pCi/g	0	(0% - 100%)	MXP1	08/03/06 13:05
		Uncert:		+/-22.8							
		TPU:		+/-22.9							
QC1201141838	LCS										
Iron-55		580			449	pCi/g	78	(75%-125%)		08/03/06	13:37
		Uncert:		+/-34.1							
		TPU:		+/-88.0							
QC1201141835	MB										
Iron-55			U	5.19	U	5.19	pCi/g			08/03/06	12:48
		Uncert:		+/-20.9							
		TPU:		+/-20.9							
QC1201141837	167555017	MS									
Iron-55		663	U	8.69	553	pCi/g	83	(75%-125%)		08/03/06	13:21
		Uncert:		+/-22.8							
		TPU:		+/-22.9							
Batch	550849										
QC1201141844	167556030	DUP									
Technetium-99			U	0.178	U	0.247	pCi/g	0	(0% - 100%)	EGD1	08/03/06 20:34
		Uncert:		+/-0.190							
		TPU:		+/-0.190							

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

QC Summary

Workorder: 167556

Page 11 of 13

Parname	NOM	Sample	Qual	QC	Units	RPD%	REC%	Range	Anlst	Date	Time
Rad Liquid Scintillation											
Batch 550849											
QC1201141846	LCS										
Technetium-99		13.1		12.2	pCi/g		93	(75%-125%)		08/03/06	21:06
		Uncert:		+/-0.459							
		TPU:		+/-0.536							
QC1201141843	MB										
Technetium-99			U	0.155	pCi/g					08/03/06	20:18
		Uncert:		+/-0.172							
		TPU:		+/-0.172							
QC1201141845	167556030	MS									
Technetium-99		12.8	U	0.178	pCi/g		92	(75%-125%)		08/03/06	20:50
		Uncert:		+/-0.190							
		TPU:		+/-0.190							
Batch 550850											
QC1201141848	167556031	DUP									
Tritium			U	2.73	pCi/g	0		(0% - 100%)	NXP1	08/02/06	20:45
		Uncert:		+/-7.57							
		TPU:		+/-7.57							
QC1201141850	LCS										
Tritium		68.4		56.4	pCi/g		83	(75%-125%)		08/02/06	21:17
		Uncert:		+/-12.5							
		TPU:		+/-12.5							
QC1201141847	MB										
Tritium			U	3.69	pCi/g					08/02/06	20:29
		Uncert:		+/-8.58							
		TPU:		+/-8.58							
QC1201141849	167556031	MS									
Tritium		63.9	U	2.73	pCi/g		86	(75%-125%)		08/02/06	21:01
		Uncert:		+/-7.57							
		TPU:		+/-7.57							
Batch 550851											
QC1201141852	167556029	DUP									
Carbon-14			U	-0.049	pCi/g	0		(0% - 100%)	ATH2	08/03/06	00:16
		Uncert:		+/-0.124							
		TPU:		+/-0.124							
QC1201141854	LCS										
Carbon-14		7.10		6.83	pCi/g		96	(75%-125%)		07/29/06	16:11
		Uncert:		+/-0.238							
		TPU:		+/-0.261							
QC1201141851	MB										
Carbon-14			U	-0.157	pCi/g					07/29/06	13:08
		Uncert:		+/-0.123							
		TPU:		+/-0.123							
QC1201141853	167556029	MS									
Carbon-14		15.6	U	-0.049	pCi/g		95	(75%-125%)		07/29/06	15:10
		Uncert:		+/-0.124							
		TPU:		+/-0.124							
Batch 556697											
QC1201155544	167555017	DUP									
Nickel-63			U	-2.07	pCi/g	0		(0% - 100%)	MXP1	08/14/06	10:13

GENERAL ENGINEERING LABORATORIES, LLC
2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

QC Summary

Workorder: 167556

Page 13 of 13

Parmname	NOM	Sample Qual	QC	Units	RPD%	REC%	Range	Anlst	Date	Time
-----------------	------------	--------------------	-----------	--------------	-------------	-------------	--------------	--------------	-------------	-------------

N/A indicates that spike recovery limits do not apply when sample concentration exceeds spike conc. by a factor of 4 or more.

** Indicates analyte is a surrogate compound.

^ The Relative Percent Difference (RPD) obtained from the sample duplicate (DUP) is evaluated against the acceptance criteria when the sample is greater than five times (5X) the contract required detection limit (RL). In cases where either the sample or duplicate value is less than 5X the RL, a control limit of +/- the RL is used to evaluate the DUP result.

For PS, PSD, and SDILT results, the values listed are the measured amounts, not final concentrations.

Where the analytical method has been performed under NELAP certification, the analysis has met all of the requirements of the NELAC standard unless qualified on the QC Summary.

Table of Contents

General Narrative	1
Chain of Custody and Supporting Documentation	4
Radiological Analysis	8
Sample Data Summary	13
Quality Control Data	23

General Narrative

CASE NARRATIVE
For
CONNECTICUT YANKEE
RE: Soil
PO# 002332
Work Order: 166655
SDG: MSR #06-0968

July 21, 2006

Laboratory Identification:

General Engineering Laboratories, LLC

Mailing Address:

P.O. Box 30712
Charleston, South Carolina 29417

Express Mail Delivery and Shipping Address:

2040 Savage Road
Charleston, South Carolina 29407

Telephone Number:

(843) 556-8171

Summary:

Sample receipt

The sample(s) for this Project arrived at General Engineering Laboratories, LLC, (GEL) in Charleston, South Carolina on July 7, 2006. All sample containers arrived without any visible signs of tampering or breakage. The chain of custody contained the proper documentation and signatures.

The laboratory received the following sample(s):

<u>Sample ID</u>	<u>Client Sample ID</u>
166655001	9106-0015-017A
166655002	9106-0015-017B
166655003	9106-0015-017C
166655004	9106-0015-017D

Items of Note:

There are no items of note.

Case Narrative:

Sample analyses were conducted using methodology as outlined in General Engineering Laboratories (GEL) Standard Operating Procedures. Any technical or administrative problems during analysis, data review, and reduction are listed below by analytical parameter.

Analytical Request:

Four soil samples were analyzed for FSSGAM and Sr-90.

Internal Chain of Custody:

Custody was maintained for the sample(s).

Data Package:

The enclosed data package contains the following sections: Case Narrative, Chain of Custody and Supporting Documentation and all analytical fractions.

I certify that this data package is in compliance with the SOW, both technically and for completeness, for other than the conditions detailed above. Release of the data contained in this hard copy data package has been authorized by the Laboratory Manager or a designee, as verified by the following signature.



Cheryl Jones
Project Manager

**Chain of Custody
And
Supporting
Documentation**

Connecticut Yankee Atomic Power Company

362 Injun Hollow Road, East Hampton, CT 06424
860-267-2556

166655/-

Chain of Custody Form

No. 2006-00449

Project Name: Haddam Neck Decommissioning							Analyses Requested				Lab Use Only	
Contact Name & Phone: Jack McCarthy 860-267-3924							FSSGAM	FSSALL	Sr-90	Ni-63	Comments:	
Analytical Lab (Name, City, State) General Engineering Laboratories 2040 Savage Road. Charleston SC. 29407 843 556 8171. Attn. Cheryl Jones												
Priority: <input checked="" type="checkbox"/> 30 D. <input checked="" type="checkbox"/> 14 D. <input type="checkbox"/> 7 D.												
Sample Designation	Date	Time	Media Code	Sample Type Code	Container Size- & Type Code					Comment, Preservation		
9106-0015-017A	6-28-06	16:55	SE	C	BP	X		X			001	
9106-0015-017B	6-28-06	17:09	SE	C	BP	X		X			002	
9106-0015-017C	6-28-06	17:21	SE	C	BP	X		X			003	
9106-0015-017D	6-28-06	16:41	SE	C	BP	X		X			004	
NOTES: PO #: 002332 MSR #: 06-0968 SSWP# NA <input checked="" type="checkbox"/> LTP QA <input type="checkbox"/> Radwaste QA <input type="checkbox"/> Non QA												
1) Relinquished By <i>[Signature]</i> Date/Time 6/28/06 17:50						2) Received By JAIME RICARTE Date/Time 6-28-06/17:50						
3) Relinquished By JAIME RICARTE Date/Time 7-6-06/1400						4) Received By <i>[Signature]</i> Date/Time 7/7/06 900						
Samples Shipped Via: <input checked="" type="checkbox"/> Fed Ex <input type="checkbox"/> UPS <input type="checkbox"/> Hand <input type="checkbox"/> Other										Internal Container Temp: _____ Deg. C Custody Sealed? Y <input type="checkbox"/> N <input type="checkbox"/> Custody Seal Intact? Y <input type="checkbox"/> N <input type="checkbox"/>		
Bill of Lading # 7919 8876 4783												

5

Figure 1. Sample Check-in List

Date/Time Received: 7/7/06

SDG#: _____

Work Order Number: 166653/166655/166656

Shipping Container ID: 7919 8876 4783 - 23°C Chain of Custody # 2006 - 00449
7910 4024 2952 - 22°C 2006 - 00440
7917 8782 3139 - 23°C 2006 - 00451
2006 - 00452

1. Custody Seals on shipping container intact? Yes No
2. Custody Seals dated and signed? Yes No
3. Chain-of-Custody record present? Yes No
4. Cooler temperature 23°C - 22°C - 23°C
5. Vermiculite/packing materials is: Wet Dry
6. Number of samples in shipping container: (1) 3 (2) 12 (3) 9
7. Sample holding times exceeded? Yes No

8. Samples have:	
<input checked="" type="checkbox"/> tape	<input type="checkbox"/> hazard labels
<input type="checkbox"/> custody seals	<input type="checkbox"/> appropriate sample labels
9. Samples are:	
<input checked="" type="checkbox"/> in good condition	<input type="checkbox"/> leaking
<input type="checkbox"/> broken	<input type="checkbox"/> have air bubbles

10. Were any anomalies identified in sample receipt? Yes No
11. Description of anomalies (include sample numbers): _____

Sample Custodian/Laboratory: Devin [Signature] Date: 7/7/06 0900
Telephoned to: _____ On _____ By _____



SAMPLE RECEIPT & REVIEW FORM

PM use only

Client: <u>Connecticut Yankee</u>	SDG/ARCO/Work Order: <u>166653, 166655, 166656</u>
Date Received: <u>7/7/06</u>	PM(A) Review (ensure non-conforming items are resolved prior to signing):
Received By: <u>[Signature]</u>	<u>[Signature]</u>

Sample Receipt Criteria	Yes	NA	No	Comments/Qualifiers (Required for Non-Conforming Items)
1 Shipping containers received intact and sealed?				Circle Applicable: seals broken damaged container leaking container other (describe)
2 Samples requiring cold preservation within (4 +/- 2 C)? Record preservation method.				Circle Coolant # ice bags blue ice dry ice none other describe)
3 Chain of custody documents included with shipment?				
4 Sample containers intact and sealed?				Circle Applicable: seals broken damaged container leaking container other (describe)
5 Samples requiring chemical preservation at proper pH?				Sample ID's, containers affected and observed pH:
6 VOA vials free of headspace (defined as < 6mm bubble)?				Sample ID's and containers affected:
7 Are Encore containers present? (If yes, immediately deliver to VOA laboratory)				
8 Samples received within holding time?				Id's and tests affected:
9 Sample ID's on COC match ID's on bottles?				Sample ID's and containers affected:
10 Date & time on COC match date & time on bottles?				Sample ID's affected:
11 Number of containers received match number indicated on COC?				Sample ID's affected:
12 COC form is properly signed in relinquished/received sections?				
14 Air Bill ,Tracking #'s, & Additional Comments				

Suspected Hazard Information	Non-Regulated	Regulated	High Level	RSO RAD Receipt # _____ *If > x2 area background is observed on samples identified as "non-regulated/non-radioactive", contact the Radiation Safety group for further investigation.
A Radiological Classification?				Maximum Counts Observed*: <u>2 PM 40</u>
B PCB Regulated?				Comments:
C Shipped as DOT Hazardous Material? If yes, contact Waste Manager or ESH Manager.				Hazard Class Shipped: UN#:

PM (or PMA) review of Hazard classification: _____ Initials [Signature] Date: 7/7/06

RADIOLOGICAL ANALYSIS

Designated QC

The following sample was used for QC: 166655001 (9106-0015-017A).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

None of the samples in this sample set required reprep or reanalysis.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Additional Comments

The sample and the duplicate, 1201131808 (9106-0015-017A) and 166655001 (9106-0015-017A), did not meet the relative percent difference requirement for Ra-226, however they do meet the relative error ratio requirement with value of 1.94.

Qualifier information

Qualifier	Reason	Analyte	Sample
UI	Data rejected due to high peak width	Bismuth-212	166655002
UI	Data rejected due to low abundance	Cesium-134	166655003

Method/Analysis Information

Product: GFPC, Sr90, solid-ALL FSS

Analytical Method: EPA 905.0 Modified

Prep Method: Ash Soil Prep

Dry Soil Prep GL-RAD-A-021 Method: Dry Soil Prep

Analytical Batch Number: 547395

Prep Batch Number: 546301

Dry Soil Prep GL-RAD-A-021 Batch Number: 546300

Sample ID	Client ID
166655001	9106-0015-017A
166655002	9106-0015-017B
166655003	9106-0015-017C
166655004	9106-0015-017D
1201133604	Method Blank (MB)
1201133605	166653016(9106-0012-004F) Sample Duplicate (DUP)
1201133606	166653016(9106-0012-004F) Matrix Spike (MS)
1201133607	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-004 REV# 10.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 166653016 (9106-0012-004F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

None of the samples in this sample set required reprep or reanalysis.

Chemical Recoveries

All chemical recoveries meet the required acceptance limits for this sample set.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Additional Comments

Additional comments were not required for this sample set.

Qualifier information

Manual qualifiers were not required.

Certification Statement

Where the analytical method has been performed under NELAP certification, the analysis has met all of the requirements of the NELAC standard unless otherwise noted in the analytical case narrative.

Review Validation:

GEL requires all analytical data to be verified by a qualified data validator. In addition, all data designated for CLP or CLP-like packaging will receive a third level validation upon completion of the data package.

The following data validator verified the information presented in this case narrative:

Reviewer/Date: _____

 7/21/16

SAMPLE DATA SUMMARY

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

**Certificate of Analysis Report
for**

YANK001 Connecticut Yankee Atomic Power Co.

Client SDG: MSR#06-0968 GEL Work Order: 166655

The Qualifiers in this report are defined as follows:

- * A quality control analyte recovery is outside of specified acceptance criteria
- ** Analyte is a surrogate compound
- U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
- UI Gamma Spectroscopy--Uncertain identification
- ND The analyte concentration is not detected above the detection limit.

The above sample is reported on a dry weight basis except where prohibited by the analytical procedure.

Where the analytical method has been performed under NELAP certification, the analysis has met all of the requirements of the NELAC standard unless qualified on the Certificate of Analysis.

This data report has been prepared and reviewed in accordance with General Engineering Laboratories, LLC standard operating procedures. Please direct any questions to your Project Manager, Cheryl Jones.



Reviewed by _____

GENERAL ENGINEERING LABORATORIES, LLC
2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: July 21, 2006

Client Sample ID:	9106-0015-017A	Project:	YANK01204
Sample ID:	166655001	Client ID:	YANK001
Matrix:	SE	Vol. Recv.:	
Collect Date:	28-JUN-06		
Receive Date:	07-JUL-06		
Collector:	Client		
Moisture:	21.8%		

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Gamma Spec Analysis													
<i>Gamma, Solid-FSS GAM & ALL FSS 226 Ingrowth</i>													
<i>Waived</i>													
Actinium-228		0.880	+/-0.190	0.0701	+/-0.190	0.148	pCi/g		MJH1	07/17/06	1826	546530	1
Americium-241	U	0.0144	+/-0.0976	0.0798	+/-0.0976	0.164	pCi/g						
Bismuth-212		0.586	+/-0.272	0.126	+/-0.272	0.266	pCi/g						
Bismuth-214		0.599	+/-0.0901	0.0315	+/-0.0901	0.066	pCi/g						
Cesium-134	U	0.0267	+/-0.0293	0.0214	+/-0.0293	0.0449	pCi/g						
Cesium-137		0.365	+/-0.050	0.0181	+/-0.050	0.038	pCi/g						
Cobalt-60		1.02	+/-0.0748	0.0175	+/-0.0748	0.038	pCi/g						
Europium-152	U	0.0287	+/-0.0546	0.0456	+/-0.0546	0.0946	pCi/g						
Europium-154	U	0.0179	+/-0.0614	0.0526	+/-0.0614	0.113	pCi/g						
Europium-155	U	0.0449	+/-0.0829	0.0441	+/-0.0829	0.0908	pCi/g						
Lead-212		0.818	+/-0.0599	0.0252	+/-0.0599	0.052	pCi/g						
Lead-214		0.731	+/-0.087	0.0298	+/-0.087	0.062	pCi/g						
Manganese-54	U	0.0186	+/-0.0224	0.0194	+/-0.0224	0.0406	pCi/g						
Niobium-94	U	0.0138	+/-0.0188	0.0163	+/-0.0188	0.0342	pCi/g						
Potassium-40		13.7	+/-0.845	0.155	+/-0.845	0.339	pCi/g						
Radium-226		0.599	+/-0.0901	0.0315	+/-0.0901	0.066	pCi/g						
Silver-108m	U	0.00949	+/-0.0173	0.0153	+/-0.0173	0.0318	pCi/g						
Thallium-208		0.265	+/-0.0477	0.017	+/-0.0477	0.0356	pCi/g						
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid-ALL FSS</i>													
Strontium-90	U	-0.0108	+/-0.00917	0.00818	+/-0.00918	0.0171	pCi/g		BXF1	07/14/06	2255	547395	2

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	LXM2	07/09/06	1715	546300

The following Analytical Methods were performed

Method	Description
1	EML HASL 300, 4.5.2.3
2	EPA 905.0 Modified

GENERAL ENGINEERING LABORATORIES, LLC
 2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
 Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
 Contact: Mr. Jack McCarthy
 Project: Soils PO# 002332

Report Date: July 21, 2006

Client Sample ID: 9106-0015-017B
 Sample ID: 166655002
 Matrix: SE
 Collect Date: 28-JUN-06
 Receive Date: 07-JUL-06
 Collector: Client
 Moisture: 27.1%

Project: YANK01204
 Client ID: YANK001
 Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Gamma Spec Analysis													
<i>Gamma, Solid-FSS GAM & ALL FSS 226 Ingrowth</i>													
<i>Waived</i>													
Actinium-228		0.747	+/-0.273	0.096	+/-0.273	0.192	pCi/g		MJH1	07/17/06	1847	546530	1
Americium-241	U	0.0467	+/-0.101	0.0738	+/-0.101	0.148	pCi/g						
Bismuth-212	UI	0.00	+/-0.458	0.194	+/-0.458	0.388	pCi/g						
Bismuth-214		0.726	+/-0.124	0.042	+/-0.124	0.084	pCi/g						
Cesium-134	U	0.0606	+/-0.0415	0.0319	+/-0.0415	0.0637	pCi/g						
Cesium-137		0.192	+/-0.057	0.0269	+/-0.057	0.0537	pCi/g						
Cobalt-60		0.357	+/-0.0806	0.0313	+/-0.0806	0.0626	pCi/g						
Europium-152	U	0.0185	+/-0.107	0.0685	+/-0.107	0.137	pCi/g						
Europium-154	U	0.00443	+/-0.102	0.0838	+/-0.102	0.168	pCi/g						
Europium-155	U	-0.00816	+/-0.0781	0.0634	+/-0.0781	0.127	pCi/g						
Lead-212		0.818	+/-0.102	0.0367	+/-0.102	0.0734	pCi/g						
Lead-214		0.756	+/-0.121	0.046	+/-0.121	0.0919	pCi/g						
Manganese-54	U	0.0425	+/-0.0386	0.0252	+/-0.0386	0.0504	pCi/g						
Niobium-94	U	-0.0111	+/-0.0275	0.0226	+/-0.0275	0.0451	pCi/g						
Potassium-40		12.8	+/-1.41	0.216	+/-1.41	0.431	pCi/g						
Radium-226		0.726	+/-0.124	0.042	+/-0.124	0.084	pCi/g						
Silver-108m	U	0.0101	+/-0.0278	0.0235	+/-0.0278	0.0469	pCi/g						
Thallium-208		0.309	+/-0.067	0.0212	+/-0.067	0.0424	pCi/g						
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid-ALL FSS</i>													
Strontium-90	U	0.00332	+/-0.0102	0.00839	+/-0.0102	0.0175	pCi/g		BXF1	07/14/06	2255	547395	2

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	LXM2	07/09/06	1715	546300

The following Analytical Methods were performed

Method	Description
1	EML HASL 300, 4.5.2.3
2	EPA 905.0 Modified

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
---------------------------	------	-----------	-------------------

GENERAL ENGINEERING LABORATORIES, LLC
2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: July 21, 2006

Client Sample ID: 9106-0015-017C
Sample ID: 166655003
Matrix: SE
Collect Date: 28-JUN-06
Receive Date: 07-JUL-06
Collector: Client
Moisture: 28.2%

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Gamma Spec Analysis													
<i>Gamma, Solid-FSS GAM & ALL FSS 226 Ingrowth</i>													
<i>Waived</i>													
Actinium-228		0.651	+/-0.218	0.101	+/-0.218	0.201	pCi/g		MJH1	07/17/06	1849	546530	1
Americium-241	U	0.0671	+/-0.122	0.0913	+/-0.122	0.182	pCi/g						
Bismuth-212		0.903	+/-0.350	0.205	+/-0.350	0.409	pCi/g						
Bismuth-214		0.567	+/-0.142	0.0456	+/-0.142	0.0911	pCi/g						
Cesium-134	UI	0.00	+/-0.0758	0.0328	+/-0.0758	0.0656	pCi/g						
Cesium-137		0.195	+/-0.0465	0.0248	+/-0.0465	0.0496	pCi/g						
Cobalt-60		0.245	+/-0.0599	0.0122	+/-0.0599	0.0243	pCi/g						
Europium-152	U	-0.0437	+/-0.0885	0.0616	+/-0.0885	0.123	pCi/g						
Europium-154	U	-0.0373	+/-0.0952	0.075	+/-0.0952	0.150	pCi/g						
Europium-155	U	0.0405	+/-0.0812	0.0682	+/-0.0812	0.136	pCi/g						
Lead-212		0.627	+/-0.0977	0.0356	+/-0.0977	0.0712	pCi/g						
Lead-214		0.653	+/-0.142	0.0467	+/-0.142	0.0932	pCi/g						
Manganese-54	U	-0.00607	+/-0.0318	0.0265	+/-0.0318	0.0529	pCi/g						
Niobium-94	U	0.012	+/-0.0311	0.0261	+/-0.0311	0.0522	pCi/g						
Potassium-40		11.1	+/-1.28	0.279	+/-1.28	0.559	pCi/g						
Radium-226		0.567	+/-0.142	0.0456	+/-0.142	0.0911	pCi/g						
Silver-108m	U	0.0232	+/-0.0269	0.0236	+/-0.0269	0.0473	pCi/g						
Thallium-208		0.240	+/-0.0661	0.0237	+/-0.0661	0.0473	pCi/g						
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid-ALL FSS</i>													
Strontium-90	U	0.00484	+/-0.00887	0.00724	+/-0.00887	0.0151	pCi/g		BXF1	07/14/06	2256	547395	2

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	LXM2	07/09/06	1715	546300

The following Analytical Methods were performed

Method	Description
1	EML HASL 300, 4.5.2.3
2	EPA 905.0 Modified

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
---------------------------	------	-----------	-------------------

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: July 21, 2006

Client Sample ID: 9106-0015-017C
Sample ID: 166655003

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Surrogate/Tracer recovery	Test				Recovery%		Acceptable Limits						
Carrier/Tracer Recovery		GFPC, Sr90, solid-ALL FSS			80		(25%-125%)						

Notes:

The Qualifiers in this report are defined as follows :

- * A quality control analyte recovery is outside of specified acceptance criteria
 - < Result is less than value reported
 - > Result is greater than value reported
 - A The TIC is a suspected aldol-condensation product
 - B Target analyte was detected in the associated blank
 - BD Results are either below the MDC or tracer recovery is low
 - C Analyte has been confirmed by GC/MS analysis
 - D Results are reported from a diluted aliquot of the sample
 - H Analytical holding time was exceeded
 - J Value is estimated
 - N/A Spike recovery limits do not apply. Sample concentration exceeds spike concentration by 4X or more
 - R Sample results are rejected
 - U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
 - UI Gamma Spectroscopy--Uncertain identification
 - X Consult Case Narrative, Data Summary package, or Project Manager concerning this qualifier
 - Y QC Samples were not spiked with this compound
 - ^ RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL
 - h Preparation or preservation holding time was exceeded
- The above sample is reported on a dry weight basis.

GENERAL ENGINEERING LABORATORIES, LLC
 2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
 Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
 Contact: Mr. Jack McCarthy
 Project: Soils PO# 002332

Report Date: July 21, 2006

Client Sample ID: 9106-0015-017D
 Sample ID: 166655004
 Matrix: SE
 Collect Date: 28-JUN-06
 Receive Date: 07-JUL-06
 Collector: Client
 Moisture: 19.5%

Project: YANK01204
 Client ID: YANK001
 Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Gamma Spec Analysis													
<i>Gamma, Solid-FSS GAM & ALL FSS 226 Ingrowth</i>													
<i>Waived</i>													
Actinium-228		0.566	+/-0.242	0.103	+/-0.242	0.220	pCi/g		MJH1	07/17/06	1854	546530	1
Americium-241	U	0.0677	+/-0.107	0.0878	+/-0.107	0.182	pCi/g						
Bismuth-212		0.686	+/-0.349	0.195	+/-0.349	0.417	pCi/g						
Bismuth-214		0.582	+/-0.125	0.0395	+/-0.125	0.0849	pCi/g						
Cesium-134	U	0.0273	+/-0.0482	0.030	+/-0.0482	0.064	pCi/g						
Cesium-137		0.313	+/-0.064	0.0255	+/-0.064	0.0544	pCi/g						
Cobalt-60		0.895	+/-0.107	0.0205	+/-0.107	0.0466	pCi/g						
Europium-152	U	0.0387	+/-0.0717	0.0607	+/-0.0717	0.128	pCi/g						
Europium-154	U	0.0601	+/-0.0784	0.0729	+/-0.0784	0.161	pCi/g						
Europium-155	U	0.0863	+/-0.0665	0.0608	+/-0.0665	0.126	pCi/g						
Lead-212		0.804	+/-0.0801	0.0309	+/-0.0801	0.0648	pCi/g						
Lead-214		0.709	+/-0.124	0.0385	+/-0.124	0.0817	pCi/g						
Manganese-54	U	0.00366	+/-0.0295	0.0247	+/-0.0295	0.0533	pCi/g						
Niobium-94	U	-0.01	+/-0.0236	0.019	+/-0.0236	0.0411	pCi/g						
Potassium-40		12.2	+/-1.12	0.185	+/-1.12	0.427	pCi/g						
Radium-226		0.582	+/-0.125	0.0395	+/-0.125	0.0849	pCi/g						
Silver-108m	U	0.00728	+/-0.0225	0.0199	+/-0.0225	0.0423	pCi/g						
Thallium-208		0.228	+/-0.0512	0.0214	+/-0.0512	0.0459	pCi/g						
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid-ALL FSS</i>													
Strontium-90	U	-0.00367	+/-0.00821	0.00707	+/-0.00821	0.0148	pCi/g		BXF1	07/14/06	2256	547395	2

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	LXM2	07/09/06	1715	546300

The following Analytical Methods were performed

Method	Description
1	EML HASL 300, 4.5.2.3
2	EPA 905.0 Modified

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
---------------------------	------	-----------	-------------------

GENERAL ENGINEERING LABORATORIES, LLC
 2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
 Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
 Contact: Mr. Jack McCarthy
 Project: Soils PO# 002332

Report Date: July 21, 2006

Client Sample ID: 9106-0015-017D Project: YANK01204
 Sample ID: 166655004 Client ID: YANK001
 Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Surrogate/Tracer recovery	Test				Recovery%		Acceptable Limits						
Carrier/Tracer Recovery		GFPC, Sr90, solid-ALL FSS			68		(25%-125%)						

Notes:

The Qualifiers in this report are defined as follows :

- * A quality control analyte recovery is outside of specified acceptance criteria
 - < Result is less than value reported
 - > Result is greater than value reported
 - A The TIC is a suspected aldol-condensation product
 - B Target analyte was detected in the associated blank
 - BD Results are either below the MDC or tracer recovery is low
 - C Analyte has been confirmed by GC/MS analysis
 - D Results are reported from a diluted aliquot of the sample
 - H Analytical holding time was exceeded
 - J Value is estimated
 - N/A Spike recovery limits do not apply. Sample concentration exceeds spike concentration by 4X or more
 - R Sample results are rejected
 - U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
 - UI Gamma Spectroscopy--Uncertain identification
 - X Consult Case Narrative, Data Summary package, or Project Manager concerning this qualifier
 - Y QC Samples were not spiked with this compound
 - ^ RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL
 - h Preparation or preservation holding time was exceeded
- The above sample is reported on a dry weight basis.

QUALITY CONTROL DATA

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

QC Summary

Client : Connecticut Yankee Atomic Power
362 Injun Hollow Rd

Report Date: July 21, 2006
Page 1 of 5

Contact: East Hampton, Connecticut
Mr. Jack McCarthy

Workorder: 166655

Parname	NOM	Sample	Qual	QC	Units	RPD%	REC%	Range	Anlst	Date	Time
Rad Gamma Spec											
Batch	546530										
QC1201131808 166655001 DUP											
Actinium-228		0.880		0.785	pCi/g	7		(0% - 100%)	MJH1	07/17/06	19:00
	Uncert:	+/-0.190		+/-0.261							
	TPU:	+/-0.190		+/-0.261							
Americium-241	U	0.0144	U	0.0531	pCi/g	44		(0% - 100%)			
	Uncert:	+/-0.0976		+/-0.0519							
	TPU:	+/-0.0976		+/-0.0519							
Bismuth-212		0.586		1.42	pCi/g	67*		(0% - 100%)			
	Uncert:	+/-0.272		+/-0.597							
	TPU:	+/-0.272		+/-0.597							
Bismuth-214		0.599		0.695	pCi/g	32		(0% - 100%)			
	Uncert:	+/-0.0901		+/-0.165							
	TPU:	+/-0.0901		+/-0.165							
Cesium-134	U	0.0267	U	0.035	pCi/g	24		(0% - 100%)			
	Uncert:	+/-0.0293		+/-0.0628							
	TPU:	+/-0.0293		+/-0.0628							
Cesium-137		0.365		0.359	pCi/g	1		(0% - 100%)			
	Uncert:	+/-0.050		+/-0.0764							
	TPU:	+/-0.050		+/-0.0764							
Cobalt-60		1.02		0.828	pCi/g	20		(0% - 20%)			
	Uncert:	+/-0.0748		+/-0.132							
	TPU:	+/-0.0748		+/-0.132							
Europium-152	U	0.0287	U	0.0537	pCi/g	56		(0% - 100%)			
	Uncert:	+/-0.0546		+/-0.0862							
	TPU:	+/-0.0546		+/-0.0862							
Europium-154	U	0.0179	U	0.127	pCi/g	361		(0% - 100%)			
	Uncert:	+/-0.0614		+/-0.129							
	TPU:	+/-0.0614		+/-0.129							
Europium-155	U	0.0449	U	0.055	pCi/g	24		(0% - 100%)			
	Uncert:	+/-0.0829		+/-0.109							
	TPU:	+/-0.0829		+/-0.109							
Lead-212		0.818		0.756	pCi/g	6		(0% - 20%)			
	Uncert:	+/-0.0599		+/-0.0927							
	TPU:	+/-0.0599		+/-0.0927							
Lead-214		0.731		0.694	pCi/g	4		(0% - 20%)			
	Uncert:	+/-0.087		+/-0.121							
	TPU:	+/-0.087		+/-0.121							
Manganese-54	U	0.0186	U	0.0308	pCi/g	49		(0% - 100%)			
	Uncert:	+/-0.0224		+/-0.0506							
	TPU:	+/-0.0224		+/-0.0506							
Niobium-94	U	0.0138	U	0.00511	pCi/g	15		(0% - 100%)			
	Uncert:	+/-0.0188		+/-0.0378							
	TPU:	+/-0.0188		+/-0.0378							

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

QC Summary

Workorder: 166655

Page 2 of 5

Parmname	NOM	Sample	Qual	QC	Units	RPD%	REC%	Range	Anlst	Date	Time
Rad Gamma Spec											
Batch	546530										
Potassium-40		13.7		12.6	pCi/g	5		(0% - 20%)			
		Uncert:	+/-0.845	+/-1.23							
		TPU:	+/-0.845	+/-1.23							
Radium-226		0.599		0.695	pCi/g	32		(0% - 100%)			
		Uncert:	+/-0.0901	+/-0.165							
		TPU:	+/-0.0901	+/-0.165							
Silver-108m	U	0.00949	U	0.00566	pCi/g	71		(0% - 100%)			
		Uncert:	+/-0.0173	+/-0.0494							
		TPU:	+/-0.0173	+/-0.0494							
Thallium-208		0.265		0.271	pCi/g	6		(0% - 100%)			
		Uncert:	+/-0.0477	+/-0.0726							
		TPU:	+/-0.0477	+/-0.0726							
QC1201131809	LCS										
Actinium-228			U	0.160	pCi/g					07/17/06	19:01
		Uncert:		+/-0.545							
		TPU:		+/-0.545							
Americium-241	23.4			24.4	pCi/g		104	(75%-125%)			
		Uncert:		+/-0.599							
		TPU:		+/-0.599							
Bismuth-212			U	-0.135	pCi/g						
		Uncert:		+/-1.00							
		TPU:		+/-1.00							
Bismuth-214			U	-0.106	pCi/g						
		Uncert:		+/-0.219							
		TPU:		+/-0.219							
Cesium-134			U	-0.0105	pCi/g						
		Uncert:		+/-0.149							
		TPU:		+/-0.149							
Cesium-137	9.61			10.8	pCi/g		112	(75%-125%)			
		Uncert:		+/-0.468							
		TPU:		+/-0.468							
Cobalt-60	14.8			15.5	pCi/g		105	(75%-125%)			
		Uncert:		+/-0.660							
		TPU:		+/-0.660							
Europium-152			U	0.0894	pCi/g						
		Uncert:		+/-0.281							
		TPU:		+/-0.281							
Europium-154			U	0.0901	pCi/g						
		Uncert:		+/-0.291							
		TPU:		+/-0.291							
Europium-155			U	0.0661	pCi/g						
		Uncert:		+/-0.236							
		TPU:		+/-0.236							
Lead-212			U	0.00863	pCi/g						
		Uncert:		+/-0.144							
		TPU:		+/-0.144							
Lead-214			U	-0.0928	pCi/g						
		Uncert:		+/-0.197							

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

QC Summary

Workorder: 166655

Page 3 of 5

Parmname	NOM	Sample Qual	QC	Units	RPD%	REC%	Range	Anlst	Date	Time
Rad Gamma Spec										
Batch	546530									
Manganese-54	TPU:	U	+/-0.197	pCi/g						
	Uncert:		-0.0301							
	TPU:		+/-0.142							
Niobium-94	TPU:	U	+/-0.142	pCi/g						
	Uncert:		-0.105							
	TPU:		+/-0.119							
Potassium-40	TPU:	U	+/-0.119	pCi/g						
	Uncert:		0.577							
	TPU:		+/-1.17							
Radium-226	TPU:	U	+/-1.17	pCi/g			(75%-125%)			
	Uncert:		-0.106							
	TPU:		+/-0.219							
Silver-108m	TPU:	U	+/-0.219	pCi/g						
	Uncert:		-0.0449							
	TPU:		+/-0.101							
Thallium-208	TPU:	U	+/-0.101	pCi/g						
	Uncert:		-0.0572							
	TPU:		+/-0.118							
	Uncert:		+/-0.118							
QC1201131807 MB										
Actinium-228	TPU:	U	0.0538	pCi/g					07/17/06	18:57
	Uncert:		+/-0.0733							
	TPU:		+/-0.0733							
Americium-241	TPU:	U	0.0126	pCi/g						
	Uncert:		+/-0.0946							
	TPU:		+/-0.0946							
Bismuth-212	TPU:	U	-0.0364	pCi/g						
	Uncert:		+/-0.125							
	TPU:		+/-0.125							
Bismuth-214	TPU:	U	0.00552	pCi/g						
	Uncert:		+/-0.0416							
	TPU:		+/-0.0416							
Cesium-134	TPU:	U	0.00875	pCi/g						
	Uncert:		+/-0.0182							
	TPU:		+/-0.0182							
Cesium-137	TPU:	U	-0.000566	pCi/g						
	Uncert:		+/-0.0173							
	TPU:		+/-0.0173							
Cobalt-60	TPU:	U	-0.015	pCi/g						
	Uncert:		+/-0.0194							
	TPU:		+/-0.0194							
Europium-152	TPU:	U	0.0584	pCi/g						
	Uncert:		+/-0.053							
	TPU:		+/-0.053							
Europium-154	TPU:	U	0.0222	pCi/g						
	Uncert:		+/-0.0583							
	TPU:		+/-0.0583							
Europium-155	TPU:	U	-0.0079	pCi/g						

GENERAL ENGINEERING LABORATORIES, LLC
 2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

QC Summary

Workorder: 166655

Page 4 of 5

Parmname	NOM	Sample	Qual	QC	Units	RPD%	REC%	Range	Anlst	Date	Time
Rad Gamma Spec											
Batch	546530										
		Uncert:		+/-0.0403							
		TPU:		+/-0.0403							
Lead-212			U	0.0336	pCi/g						
		Uncert:		+/-0.0283							
		TPU:		+/-0.0283							
Lead-214			U	0.0301	pCi/g						
		Uncert:		+/-0.0341							
		TPU:		+/-0.0341							
Manganese-54			U	0.0139	pCi/g						
		Uncert:		+/-0.0175							
		TPU:		+/-0.0175							
Niobium-94			U	-0.0065	pCi/g						
		Uncert:		+/-0.0171							
		TPU:		+/-0.0171							
Potassium-40			U	0.122	pCi/g						
		Uncert:		+/-0.188							
		TPU:		+/-0.188							
Radium-226			U	0.00552	pCi/g						
		Uncert:		+/-0.0416							
		TPU:		+/-0.0416							
Silver-108m			U	-0.00533	pCi/g						
		Uncert:		+/-0.0176							
		TPU:		+/-0.0176							
Thallium-208			U	0.000666	pCi/g						
		Uncert:		+/-0.0172							
		TPU:		+/-0.0172							
Rad Gas Flow											
Batch	547395										
QC1201133605	166653016	DUP									
Strontium-90			U	-0.00399	pCi/g	0		(0% - 100%)	BXF1	07/14/06	22:56
		Uncert:		+/-0.0104							
		TPU:		+/-0.0104							
QC1201133607	LCS										
Strontium-90				1.50	pCi/g		97	(75%-125%)		07/14/06	22:56
		Uncert:									
		TPU:									
QC1201133604	MB										
Strontium-90			U	-0.00607	pCi/g					07/14/06	22:56
		Uncert:		+/-0.0062							
		TPU:		+/-0.0062							
QC1201133606	166653016	MS									
Strontium-90			1.52	U	-0.00399	pCi/g		81	(75%-125%)	07/14/06	22:55
		Uncert:									
		TPU:									

Notes:

The Qualifiers in this report are defined as follows:

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

QC Summary

Workorder: 166655

Page 5 of 5

Parmname	NOM	Sample Qual	QC	Units	RPD%	REC%	Range	Anlst	Date	Time
*										
<										
>										
A										
B										
BD										
C										
D										
H										
J										
N/A										
R										
U										
UI										
X										
Y										
^										
h										


N/A indicates that spike recovery limits do not apply when sample concentration exceeds spike conc. by a factor of 4 or more.

** Indicates analyte is a surrogate compound.

^ The Relative Percent Difference (RPD) obtained from the sample duplicate (DUP) is evaluated against the acceptance criteria when the sample is greater than five times (5X) the contract required detection limit (RL). In cases where either the sample or duplicate value is less than 5X the RL, a control limit of +/- the RL is used to evaluate the DUP result.

For PS, PSD, and SDILT results, the values listed are the measured amounts, not final concentrations.

Where the analytical method has been performed under NELAP certification, the analysis has met all of the requirements of the NELAC standard unless qualified on the QC Summary.



GENERAL ENGINEERING LABORATORIES, LLC
a Member of THE GEL GROUP, INC.
Meeting Today's Needs with a Vision for Tomorrow

October 31, 2006

Mr. Jack McCarthy
Connecticut Yankee Atomic Power
362 Injun Hollow Rd
East Hampton, Connecticut 06424

Re: Soils PO# 002332
Work Order: 174791
SDG: MSR#06-0730

Dear Mr. McCarthy:

General Engineering Laboratories, LLC (GEL) appreciates the opportunity to provide the following analytical results for the sample(s) we received on May 24, 2006. This data report has been prepared and reviewed in accordance with GEL's standard operating procedures.

Our policy is to provide high quality, personalized analytical services to enable you to meet your analytical needs on time every time. We trust that you will find everything in order and to your satisfaction. If you have any questions, please do not hesitate to call me at (843) 556-8171, ext. 4243.

Sincerely,

Cheryl Jones
Project Manager

Purchase Order: 002332
Chain of Custody: 2006-00362
Enclosures

Connecticut Yankee Atomic Power Co.
Soils PO# 002332
Work Order: 174791
SDG: MSR#06-0730

<u>Laboratory ID</u>	<u>Client ID</u>
174791001	9106-0007-017F

Table of Contents

General Narrative	1
Chain of Custody and Supporting Documentation	5
Data Review Qualifier Definitions	11
Radiological Analysis.....	13
Sample Data Summary	27
Quality Control Data	32

General Narrative

**General Narrative
for
Connecticut Yankee Atomic Power Co.
Work Order: 174791
SDG: MSR#06-0730**

October 31, 2006

Laboratory Identification:

General Engineering Laboratories, LLC
2040 Savage Road
Charleston, South Carolina 29407
(843) 556-8171

Summary

Sample receipt

The sample arrived at General Engineering Laboratories, LLC, Charleston, South Carolina on May 24, 2006 for analysis. Shipping container temperature was checked, documented, and within specifications. The sample was delivered with proper chain of custody documentation and signatures. All sample containers arrived without any visible signs of tampering or breakage.

Sample Identification The laboratory received the following sample:

Laboratory Identification	Sample Description
174791001	9106-0007-017F

Items of Note

Dale Roberts requested via email on 10/24/06, to analyze this sample for FSSALL minus gamma and Sr-90.

Case Narrative

Sample analyses were conducted using methodology as outlined in General Engineering Laboratories (GEL) Standard Operating Procedures. Any technical or administrative problems during analysis, data review, and reduction are contained in the analytical case narratives in the enclosed data package.


Analytical Request

One soil sample was reanalyzed for FSSALL, minus gamma and Sr-90. See attached email.

Data Package

The enclosed data package contains the following sections: General Narrative, Chain of Custody and Supporting Documentation, Data Review Qualifier Definitions, and data from the following fractions: Radiochemistry.

I certify that this data package is in compliance with the SOW, both technically and for completeness, for other than the conditions detailed above. Release of the data contained in this hard copy data package has been authorized by the Laboratory Manager or a designee, as verified by the following signature.



Cheryl Jones
Project Manager

List of current GEL Certifications as of 31 October 2006

State	Certification
Alaska	UST-062
Arizona	AZ0668
Arkansas	88-0651
CLIA	42D0904046
California	01151CA
Colorado	GenEngLabs
Connecticut	PH-0169
Dept. of Navy	NFESC 413
EPA	WG-15J
Florida/NELAP	E87156
Georgia	E87156 (FL/NELAP)
Hawaii	N/A
Idaho	N/A
Illinois	200029
Indiana	C-SC-01
Kansas	E-10332
Kentucky	90129
Louisiana	03046
Maryland	270
Massachusetts	M-SC012
Michigan	9903
Nevada	SC12
New Jersey	SC002
New Mexico	FL NELAP E87156
New York	11501
North Carolina	233
North Carolina Drinking W	45709
North Dakota	R-158
Oklahoma	9904
Pennsylvania	68-00485
South Carolina	10120001/10585001/10120002
Tennessee	02934
Texas	TX213-2006A
Texas NELAP	T104704235-06-TX
U.S. Dept. of Agriculture	S-52597
US Army Corps of Engineer	N/A
Utah	8037697376 GEL
Vermont	VT87156
Virginia	00151
Washington	C1641

**Chain of Custody
and
Supporting
Documentation**

Connecticut Yankee Atomic Power Company

362 Injun Hollow Road, East Hampton, CT 06424
860-267-2556

Chain of Custody Form

No. 2006-00362

163626%

174791% Relog

Project Name: Haddam Neck Decommissioning							Analyses Requested			Lab Use Only		
Contact Name & Phone: Jack McCarthy 860-267-2556 Ext. 3024							FSSGAM	FSSALL	Sr-90	Comments		
Analytical Lab (Name, City, State) General Engineering Laboratories 2040 Savage Road, Charleston SC. 29407 843 556 8171. Attn. Cheryl Jones												
Priority: <input checked="" type="checkbox"/> 30 D. <input type="checkbox"/> 14 D. <input type="checkbox"/> 7 D.												
Sample Designation	Date	Time	Media Code	Sample Type Code	Container Size- & Type Code					Comment, Preservation	Lab Sample ID	
9106-0007-016F	5/10/06	14:54	SE	C	BP	X		X		Transferred from COC 2006-00343	163626/001	
9106-0007-017F	5/11/06	10:39	SE	C	BP	X		X		Transferred from COC 2006-00345	163626/002	
9106-0007-001F	5/11/06	09:43	SE	C	BP		X			Transferred from COC 2006-00345	163626/016	
9106-0007-002F	5/08/06	13:27	SE	C	BP		X			Transferred from COC 2006-00329	163626/017	
9106-0007-003F	5/08/06	13:53	SE	C	BP	X		X		Transferred from COC 2006-00329	163626/003	
9106-0007-004F	5/08/06	14:13	SE	C	BP	X		X		Transferred from COC 2006-00329	163626/004	
9106-0007-004FS	5/08/06	14:13	SE	C	BP	X		X		Transferred from COC 2006-00329	163626/005	
9106-0007-005F	5/08/06	14:32	SE	C	BP	X		X		Transferred from COC 2006-00329	163626/006	
9106-0007-006F	5/08/06	14:52	SE	C	BP	X		X		Transferred from COC 2006-00329	163626/007	
NOTES: PO #: 002332 MSR #: 06-0736 SSWP# NA <input checked="" type="checkbox"/> LTP QA <input type="checkbox"/> Radwaste QA <input type="checkbox"/> Non QA										Samples Shipped Via: <input checked="" type="checkbox"/> Fed Ex <input type="checkbox"/> UPS <input type="checkbox"/> Hand <input type="checkbox"/> Other		
1) Relinquished By <i>[Signature]</i>			Date/Time 5/23/06 085			2) Received By <i>[Signature]</i>			Date/Time 5/24/06 0930			
3) Relinquished By			Date/Time			4) Received By			Date/Time			
										Internal Container Temp: _____ Deg. C Custody Sealed? <input type="checkbox"/> Y <input type="checkbox"/> N Custody Seal Intact? <input type="checkbox"/> Y <input type="checkbox"/> N		
										Bill of Lading # 19210573 5432		

9

Connecticut Yankee Atomic Power Company

362 Injun Hollow Road, East Hampton, CT 06424
860-267-2556

Chain of Custody Form

No. 2006-00363

163626/

Project Name: Haddam Neck Decommissioning			Media Code	Sample Type Code	Container Size & Type Code	Analyses Requested				Lab Use Only				
Contact Name & Phone: Jack McCarthy 860-267-2556 Ext. 3024						FSSGAM	FSSALL	Sr-90	Comments					
Analytical Lab (Name, City, State) General Engineering Laboratories 2040 Savage Road, Charleston SC. 29407 843 556 8171. Attn. Cheryl Jones														
Priority: <input checked="" type="checkbox"/> 30 D. <input type="checkbox"/> 14 D. <input type="checkbox"/> 7 D.														
Sample Designation	Date	Time	Comment, Preservation		Lab Sample ID									
9106-0007-007F	5/08/06	15:11	SE	C	BP	X		X			Transferred from COC 2006-00329	163626/008		
9106-0007-008F	5/09/06	10:39	SE	C	BP	X		X			Transferred from COC 2006-00334	163626/009		
9106-0007-011F	5/09/06	09:43	SE	C	BP	X		X			Transferred from COC 2006-00334	163626/010		
9106-0007-012F	5/09/06	13:27	SE	C	BP	X		X			Transferred from COC 2006-00334	163626/011		
9106-0007-013F	5/09/06	13:53	SE	C	BP	X		X			Transferred from COC 2006-00334	163626/012		
9106-0007-013FS	5/09/06	14:13	SE	C	BP	X		X			Transferred from COC 2006-00334	163626/013		
9106-0007-014F	5/09/06	14:13	SE	C	BP	X		X			Transferred from COC 2006-00334	163626/014		
9106-0007-015F	5/16/06	07:56	SE	C	BP	X		X			Transferred from COC 2006-00353	163626/015		
NOTES: PO #: 002332 MSR #: 06-0730 SSWP# NA <input checked="" type="checkbox"/> LTP QA <input type="checkbox"/> Radwaste QA <input type="checkbox"/> Non QA 5/21/06											Samples Shipped Via: <input checked="" type="checkbox"/> Fed Ex <input type="checkbox"/> UPS <input type="checkbox"/> Hand <input type="checkbox"/> Other		Internal Container Temp: _____ Deg C Custody Sealed? <input checked="" type="checkbox"/> Y <input type="checkbox"/> N Custody Seal Intact? <input checked="" type="checkbox"/> Y <input type="checkbox"/> N	
1) Relinquished By <i>Ken Puller</i>			Date/Time 5-23-06 0815			2) Received By <i>K. Light</i>			Date/Time 5/24/06 0930					
3) Relinquished By			Date/Time			4) Received By			Date/Time					
Bill of Lading # 792105735443														

7

Subject: 9106-0007-017F, FSSALL request
From: "Dale Randall" <randall@cyapco.com>
Date: Tue, 24 Oct 2006 14:02:27 -0400
To: "Cheryl Jones" <cj@gel.com>
CC: "Arthur L. Hammond" <Hammond@CYAPCO.com>, "John McCarthy"
<McCarthy@CYAPCO.com>


Cheryl:

We need sample 9106-0007-017F, initially sent as part of MSR#06-0730, to be analysed to the FSSALL protocol. It has already been measured for FSSGAM and Sr-90. Once you have had an opportunity to verify that you have enough sample aliquot and can estimate the turn around time (TAT) please call or e-mail me at your earliest convenience.

Thank You,

Dale

(860) 267-3133



SAMPLE RECEIPT & REVIEW FORM

PM use only

Client: <u>Conn Yankee</u>	SDG/ARCO/Work Order: <u>110310210</u>
Date Received: <u>5/24/06</u>	PM(A) Review (ensure non-conforming items are resolved prior to signing):
Received By: <u>(Signature)</u>	

Sample Receipt Criteria	Yes	NA	No	Comments/Qualifiers (Required for Non-Conforming Items)
1 Shipping containers received intact and sealed?	/			Circle Applicable: seals broken damaged container leaking container other (describe)
2 Samples requiring cold preservation within (4 +/- 2 C)? Record preservation method.		/		Circle Coolant # ice bags blue ice dry ice <u>none</u> other (describe) <u>19°C</u>
3 Chain of custody documents included with shipment?	/			
4 Sample containers intact and sealed?	/			Circle Applicable: seals broken damaged container leaking container other (describe)
5 Samples requiring chemical preservation at proper pH?		/		Sample ID's, containers affected and observed pH:
6 VOA vials free of headspace (defined as < 6mm bubble)?		/		Sample ID's and containers affected:
7 Are Encore containers present? (If yes, immediately deliver to VOA laboratory)			/	
8 Samples received within holding time?	/			Id's and tests affected:
9 Sample ID's on COC match ID's on bottles?	/			Sample ID's and containers affected:
10 Date & time on COC match date & time on bottles?	/			Sample ID's affected:
11 Number of containers received match number indicated on COC?	/			Sample ID's affected:
12 COC form is properly signed in relinquished/received sections?	/			

14 Air Bill ,Tracking #'s, & Additional Comments	<u>7921 0673 5432</u>		
--	-----------------------	--	--

Suspected Hazard Information		Non-Regulated	Regulated	High Level	RSO RAD Receipt # _____ *If > x2 area background is observed on samples identified as "non-regulated/non-radioactive", contact the Radiation Safety group for further investigation.
A	Radiological Classification?	<input checked="" type="checkbox"/>	<input checked="" type="checkbox"/>		Maximum Counts Observed*: <u>cpm 60</u>
B	PCB Regulated?	<input checked="" type="checkbox"/>			Comments:
C	Shipped as DOT Hazardous Material? If yes, contact Waste Manager or ESH Manager.	<input checked="" type="checkbox"/>			Hazard Class Shipped: UN#:
PM (or PMA) review of Hazard classification:		Initials <u>CS</u>		Date: <u>5/24/06</u>	

Figure 1. Sample Check-in List

Date/Time Received: 5/24/06 0930

SDG#: MSB# 06-0730

Work Order Number: 163626

Shipping Container ID: 792109735432 Chain of Custody #: 2006-003002

1. Custody Seals on shipping container intact? Yes No
2. Custody Seals dated and signed? Yes No
3. Chain-of-Custody record present? Yes No
4. Cooler temperature 19°C
5. Vermiculite/packing materials is: Wet Dry NA
6. Number of samples in shipping container: 9
7. Sample holding times exceeded? Yes No

8. Samples have:	
<input checked="" type="checkbox"/> tape	<input type="checkbox"/> hazard labels
<input checked="" type="checkbox"/> custody seals	<input checked="" type="checkbox"/> appropriate sample labels
9. Samples are:	
<input checked="" type="checkbox"/> in good condition	<input type="checkbox"/> leaking
<input type="checkbox"/> broken	<input type="checkbox"/> have air bubbles

10. Were any anomalies identified in sample receipt? Yes No

11. Description of anomalies (include sample numbers): _____

Sample Custodian/Laboratory: [Signature] Date: 5/24/06

Telephoned to: _____ On _____ By _____

Data Review Qualifier Definitions

Data Review Qualifier Definitions

Qualifier	Explanation
*	A quality control analyte recovery is outside of specified acceptance criteria
**	Analyte is a surrogate compound
<	Result is less than value reported
>	Result is greater than value reported
^	RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL
A	The TIC is a suspected aldol-condensation product
B	Target analyte was detected in the associated blank
B	Metals-Either presence of analyte detected in the associated blank, or MDL/IDL < sample value < PQL
BD	Results are either below the MDC or tracer recovery is low
C	Analyte has been confirmed by GC/MS analysis
D	Results are reported from a diluted aliquot of the sample
d	5-day BOD-The 2:1 depletion requirement was not met for this sample
E	Organics-Concentration of the target analyte exceeds the instrument calibration range
E	Metals-%difference of sample and SD is >10%. Sample concentration must meet flagging criteria
H	Analytical holding time was exceeded
h	Preparation or preservation holding time was exceeded
J	Value is estimated
N	Metals-The Matrix spike sample recovery is not within specified control limits
N	Organics-Presumptive evidence based on mass spectral library search to make a tentative identification of the analyte (TIC). Quantitation is based on nearest internal standard response factor
N/A	Spike recovery limits do not apply. Sample concentration exceeds spike concentration by 4X or more
ND	Analyte concentration is not detected above the reporting limit
UI	Gamma Spectroscopy-Uncertain identification
X	Consult Case Narrative, Data Summary package, or Project Manager concerning this qualifier
Y	QC Samples were not spiked with this compound
Z	Paint Filter Test-Particulates passed through the filter, however no free liquids were observed.

RADIOLOGICAL ANALYSIS

**Radiochemistry Case Narrative
Connecticut Yankee Atomic Power Co. (YANK)
Work Order 174791**

Method/Analysis Information

Product:	Alphaspec Am241, Cm, Solid ALL FSS
Analytical Method:	DOE EML HASL-300, Am-05-RC Modified
Prep Method:	Ash Soil Prep
Dry Soil Prep GL-RAD-A-021 Method:	Dry Soil Prep
Analytical Batch Number:	582798
Prep Batch Number:	582531
Dry Soil Prep GL-RAD-A-021 Batch Number:	582530

Sample ID	Client ID
174791001	9106-0007-017F
1201215730	Method Blank (MB)
1201215731	174791001(9106-0007-017F) Sample Duplicate (DUP)
1201215732	174791001(9106-0007-017F) Matrix Spike (MS)
1201215733	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-011 REV# 14.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 174791001 (9106-0007-017F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

None of the samples in this sample set required reprep or reanalysis.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Manual Integration

No manual integrations were performed on data in this batch.

Additional Comments

Additional comments were not required for this sample set.

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product: Alphaspec Pu, Solid-ALL FSS

Analytical Method: DOE EML HASL-300, Pu-11-RC Modified

Prep Method: Ash Soil Prep

Dry Soil Prep GL-RAD-A-021 Method: Dry Soil Prep

Analytical Batch Number: 582799

Prep Batch Number: 582531

Dry Soil Prep GL-RAD-A-021 Batch Number: 582530

Sample ID	Client ID
174791001	9106-0007-017F
1201215734	Method Blank (MB)
1201215735	174791001(9106-0007-017F) Sample Duplicate (DUP)
1201215736	174791001(9106-0007-017F) Matrix Spike (MS)
1201215737	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-011 REV# 14.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 174791001 (9106-0007-017F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

Samples 1201215734 (MB) and 174791001 (9106-0007-017F) were recounted due to detector error.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Manual Integration

No manual integrations were performed on data in this batch.

Additional Comments

Additional comments were not required for this sample set.

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product:	Liquid Scint Pu241, Solid-ALL FSS
Analytical Method:	DOE EML HASL-300, Pu-11-RC Modified
Prep Method:	Ash Soil Prep
Dry Soil Prep GL-RAD-A-021 Method:	Dry Soil Prep
Analytical Batch Number:	582800
Prep Batch Number:	582531
Dry Soil Prep GL-RAD-A-021 Batch Number:	582530

Sample ID	Client ID
174791001	9106-0007-017F
1201215738	Method Blank (MB)
1201215739	174791001(9106-0007-017F) Sample Duplicate (DUP)
1201215740	174791001(9106-0007-017F) Matrix Spike (MS)
1201215741	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-035 REV# 8.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 174791001 (9106-0007-017F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

None of the samples in this sample set required reprep or reanalysis.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this

SDG.

Manual Integration

No manual integrations were performed on data in this batch.

Additional Comments

Additional comments were not required for this sample set.

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product: Liquid Scint Tc99, Solid-ALL FSS
Analytical Method: DOE EML HASL-300, Tc-02-RC Modified
Analytical Batch Number: 582788

Sample ID	Client ID
174791001	9106-0007-017F
1201215687	Method Blank (MB)
1201215688	174791001(9106-0007-017F) Sample Duplicate (DUP)
1201215689	174791001(9106-0007-017F) Matrix Spike (MS)
1201215690	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-005 REV# 13.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volumes in this batch.

Designated QC

The following sample was used for QC: 174791001 (9106-0007-017F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:**Holding Time**

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

Samples were recounted due to a suspected blank false positive.

Miscellaneous Information:**NCR Documentation**

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Additional Comments

Additional comments were not required for this sample set.

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product:	Liquid Scint Fe55, Solid-ALL FSS
Analytical Method:	DOE RESL Fe-1, Modified
Prep Method:	Ash Soil Prep
Dry Soil Prep GL-RAD-A-021 Method:	Dry Soil Prep
Analytical Batch Number:	582786
Prep Batch Number:	582531
Dry Soil Prep GL-RAD-A-021 Batch Number:	582530

Sample ID	Client ID
174791001	9106-0007-017F
1201215679	Method Blank (MB)
1201215680	174791001(9106-0007-017F) Sample Duplicate (DUP)
1201215681	174791001(9106-0007-017F) Matrix Spike (MS)
1201215682	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-040 REV# 3.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 174791001 (9106-0007-017F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

None of the samples in this sample set required reprep or reanalysis.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this

SDG.

Additional Comments

Additional comments were not required for this sample set.

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product:	Liquid Scint Ni63, Solid-ALL FSS
Analytical Method:	DOE RESL Ni-1, Modified
Prep Method:	Ash Soil Prep
Dry Soil Prep GL-RAD-A-021 Method:	Dry Soil Prep
Analytical Batch Number:	582787
Prep Batch Number:	582531
Dry Soil Prep GL-RAD-A-021 Batch Number:	582530

Sample ID	Client ID
174791001	9106-0007-017F
1201215683	Method Blank (MB)
1201215684	174791001(9106-0007-017F) Sample Duplicate (DUP)
1201215685	174791001(9106-0007-017F) Matrix Spike (MS)
1201215686	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-022 REV# 8.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 174791001 (9106-0007-017F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

None of the samples in this sample set required reprep or reanalysis.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Additional Comments

Additional comments were not required for this sample set.

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product: LSC, Tritium Dist, Solid-HTD2,ALL FSS
Analytical Method: EPA 906.0 Modified
Analytical Batch Number: 582789

Sample ID	Client ID
174791001	9106-0007-017F
1201215691	Method Blank (MB)
1201215692	174791001(9106-0007-017F) Sample Duplicate (DUP)
1201215693	174791001(9106-0007-017F) Matrix Spike (MS)
1201215694	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-002 REV# 13.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 174791001 (9106-0007-017F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

None of the samples in this sample set required reprep or reanalysis.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this

SDG.

Additional Comments

Additional comments were not required for this sample set.

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product: Liquid Scint C14, Solid All,FSS

Analytical Method: EPA EERF C-01 Modified

Analytical Batch Number: 582790

Sample ID	Client ID
174791001	9106-0007-017F
1201215695	Method Blank (MB)
1201215696	174791001(9106-0007-017F) Sample Duplicate (DUP)
1201215697	174791001(9106-0007-017F) Matrix Spike (MS)
1201215698	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-003 REV# 8.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 174791001 (9106-0007-017F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

None of the samples in this sample set required reprep or reanalysis.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Additional Comments

Additional comments were not required for this sample set.

Qualifier information

Manual qualifiers were not required.

Certification Statement

Where the analytical method has been performed under NELAP certification, the analysis has met all of the requirements of the NELAC standard unless otherwise noted in the analytical case narrative.

Review Validation:

GEL requires all analytical data to be verified by a qualified data validator. In addition, all data designated for CLP or CLP-like packaging will receive a third level validation upon completion of the data package.

The following data validator verified the information presented in this case narrative:

Reviewer/Date: *Ramona Welton* 11/6/07

SAMPLE DATA SUMMARY

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

**Certificate of Analysis Report
for**

YANK001 Connecticut Yankee Atomic Power Co.

Client SDG: MSR#06-0730 GEL Work Order: 174791

The Qualifiers in this report are defined as follows:

- * A quality control analyte recovery is outside of specified acceptance criteria
- ** Analyte is a surrogate compound
- U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
- ND The analyte concentration is not detected above the detection limit.

The above sample is reported on a dry weight basis except where prohibited by the analytical procedure.

Where the analytical method has been performed under NELAP certification, the analysis has met all of the requirements of the NELAC standard unless qualified on the Certificate of Analysis.

This data report has been prepared and reviewed in accordance with General Engineering Laboratories, LLC standard operating procedures. Please direct any questions to your Project Manager, Cheryl Jones.



Reviewed by _____

GENERAL ENGINEERING LABORATORIES, LLC
2040 Savage Road Charleston SC 29407 – (843) 556-8171 – www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

Contact: East Hampton, Connecticut 06424
Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: November 3, 2006

Client Sample ID:	9106-0007-017F	Project:	YANK01204
Sample ID:	174791001	Client ID:	YANK001
Matrix:	TS	Vol. Recv.:	
Collect Date:	11-MAY-06		
Receive Date:	24-MAY-06		
Collector:	Client		
Moisture:	38.1%		

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Alpha Spec Analysis													
<i>Alphaspec Am241, Cm, Solid ALL FSS</i>													
Americium-241	U	0.00318	+/-0.0201	0.00	+/-0.0201	0.0896	pCi/g		MXA	10/27/06	0938	582798	1
Curium-242	U	-0.0163	+/-0.137	0.061	+/-0.137	0.306	pCi/g						
Curium-243/244	U	0.0591	+/-0.0945	0.0302	+/-0.0947	0.151	pCi/g						
<i>Alphaspec Pu, Solid-ALL FSS</i>													
Plutonium-238	U	0.0128	+/-0.133	0.106	+/-0.133	0.309	pCi/g		MXA	10/28/06	1032	582799	2
Plutonium-239/240	U	0.0469	+/-0.129	0.0844	+/-0.129	0.265	pCi/g						
<i>Liquid Scint Pu241, Solid-ALL FSS</i>													
Plutonium-241	U	-1.93	+/-6.47	5.51	+/-6.47	11.6	pCi/g		MXA	10/31/06	0217	582800	3
Rad Liquid Scintillation Analysis													
<i>LSC, Tritium Dist, Solid-HTD2, ALL FSS</i>													
Tritium	U	2.94	+/-7.03	5.68	+/-7.03	12.3	pCi/g		MXP1	10/26/06	2118	582789	4
<i>Liquid Scint C14, Solid All, FSS</i>													
Carbon-14	U	0.0304	+/-0.120	0.0999	+/-0.120	0.205	pCi/g		AXD2	10/28/06	0831	582790	5
<i>Liquid Scint Fe55, Solid-ALL FSS</i>													
Iron-55	U	-7.05	+/-34.5	26.2	+/-34.5	55.0	pCi/g		MXP1	10/31/06	1634	582786	6
<i>Liquid Scint Ni63, Solid-ALL FSS</i>													
Nickel-63	U	2.73	+/-9.43	7.78	+/-9.43	16.4	pCi/g		MXP1	11/02/06	0756	582787	7
<i>Liquid Scint Tc99, Solid-ALL FSS</i>													
Technetium-99	U	0.120	+/-0.236	0.194	+/-0.236	0.404	pCi/g		KXR1	11/02/06	1009	582788	8

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	MXP2	10/24/06	1704	582530

The following Analytical Methods were performed

Method	Description
1	DOE EML HASL-300, Am-05-RC Modified
2	DOE EML HASL-300, Pu-11-RC Modified

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 – (843) 556-8171 – www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

Contact: East Hampton, Connecticut 06424
Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: November 3, 2006

Client Sample ID: 9106-0007-017F
Sample ID: 174791001

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
3		DOE EML HASL-300, Pu-11-RC Modified											
4		EPA 906.0 Modified											
5		EPA EERF C-01 Modified											
6		DOE RESL Fe-1, Modified											
7		DOE RESL Ni-1, Modified											
8		DOE EML HASL-300, Tc-02-RC Modified											
9		DOE EML HASL-300, Tc-02-RC Modified											

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
Americium-243	Alphaspec Am241, Cm, Solid ALL	85	(15%-125%)
Plutonium-242	Alphaspec Pu, Solid-ALL FSS	91	(15%-125%)
Plutonium-241	Liquid Scint Pu241, Solid-ALL FS	100	(25%-125%)
Iron-55	Liquid Scint Fe55, Solid-ALL FS	54	(15%-125%)
Nickel-63	Liquid Scint Ni63, Solid-ALL FS	84	(25%-125%)
Carrier/Tracer Recovery	Liquid Scint Ni63, Solid-ALL FS	84	(25%-125%)
Technetium-99	Liquid Scint Tc99, Solid-ALL FS	75	(15%-125%)
Carrier/Tracer Recovery	Liquid Scint Tc99, Solid-ALL FS	75	(15%-125%)

Notes:

The Qualifiers in this report are defined as follows :

- * A quality control analyte recovery is outside of specified acceptance criteria
- < Result is less than value reported
- > Result is greater than value reported
- A The TIC is a suspected aldol-condensation product
- B Target analyte was detected in the associated blank
- BD Results are either below the MDC or tracer recovery is low
- C Analyte has been confirmed by GC/MS analysis
- D Results are reported from a diluted aliquot of the sample
- H Analytical holding time was exceeded
- J Value is estimated
- N/A Spike recovery limits do not apply. Sample concentration exceeds spike concentration by 4X or more
- R Sample results are rejected
- U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
- UI Gamma Spectroscopy--Uncertain identification
- X Consult Case Narrative, Data Summary package, or Project Manager concerning this qualifier
- Y QC Samples were not spiked with this compound
- ^ RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL

GENERAL ENGINEERING LABORATORIES, LLC
2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: November 3, 2006

Client Sample ID: 9106-0007-017F
Sample ID: 174791001

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
-----------	-----------	--------	-------------	----	-----	-----	-------	----	---------	------	------	-------	-----

h Preparation or preservation holding time was exceeded
The above sample is reported on a dry weight basis.

**QUALITY
CONTROL
DATA**

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

QC Summary

Report Date: November 3, 2006

Page 1 of 5

Client : Connecticut Yankee Atomic Power
362 Injun Hollow Rd

Contact: East Hampton, Connecticut
Mr. Jack McCarthy

Workorder: 174791

Parmname	NOM	Sample	Qual	QC	Units	RPD%	REC%	Range	Anlst	Date	Time
Rad Alpha Spec											
Batch	582798										
QC1201215731	174791001 DUP										
Americium-241	U	0.00318	U	0.0674	pCi/g	182		(0% - 100%)	AXA1	10/27/06	09:38
	Uncert:	+/-0.0201		+/-0.103							
	TPU:	+/-0.0201		+/-0.103							
Curium-242	U	-0.0163	U	0.0722	pCi/g	317		(0% - 100%)			
	Uncert:	+/-0.137		+/-0.142							
	TPU:	+/-0.137		+/-0.142							
Curium-243/244	U	0.0591	U	0.090	pCi/g	41		(0% - 100%)			
	Uncert:	+/-0.0945		+/-0.124							
	TPU:	+/-0.0947		+/-0.124							
QC1201215733	LCS										
Americium-241		13.5		11.7	pCi/g		87	(75%-125%)			
	Uncert:			+/-1.32							
	TPU:			+/-1.99							
Curium-242			U	0.00	pCi/g						
	Uncert:			+/-0.0764							
	TPU:			+/-0.0764							
Curium-243/244		16.3		15.5	pCi/g		95	(75%-125%)			
	Uncert:			+/-1.52							
	TPU:			+/-2.49							
QC1201215730	MB										
Americium-241			U	0.0124	pCi/g						
	Uncert:			+/-0.0448							
	TPU:			+/-0.0448							
Curium-242			U	0.00	pCi/g						
	Uncert:			+/-0.0827							
	TPU:			+/-0.0827							
Curium-243/244			U	-0.0201	pCi/g						
	Uncert:			+/-0.0868							
	TPU:			+/-0.0869							
QC1201215732	174791001 MS										
Americium-241	U	0.00318		13.2	pCi/g		98	(75%-125%)			
	Uncert:	+/-0.0201		+/-1.30							
	TPU:	+/-0.0201		+/-2.06							
Curium-242	U	-0.0163	U	-0.0163	pCi/g						
	Uncert:	+/-0.137		+/-0.137							
	TPU:	+/-0.137		+/-0.137							
Curium-243/244	U	0.0591		15.2	pCi/g		92	(75%-125%)			
	Uncert:	+/-0.0945		+/-1.40							
	TPU:	+/-0.0947		+/-2.32							
Batch	582799										
QC1201215735	174791001 DUP										
Plutonium-238	U	0.0128	U	-0.0132	pCi/g	13000		(0% - 100%)	AXA1	10/27/06	09:37

GENERAL ENGINEERING LABORATORIES, LLC
 2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

QC Summary

Workorder: 174791

Page 2 of 5

Parmname	NOM	Sample	Qual	QC	Units	RPD%	REC%	Range	Anlst	Date	Time
Rad Alpha Spec											
Batch	582799										
Plutonium-239/240		Uncert:		+/-0.133							
		TPU:		+/-0.133							
	U		0.0469	U	0.0208						
		Uncert:		+/-0.129		+/-0.0553					
		TPU:		+/-0.129		+/-0.0553					
QC1201215737	LCS										
Plutonium-238			U	0.0489	pCi/g			(75%-125%)		10/27/06	09:37
		Uncert:		+/-0.0966							
		TPU:		+/-0.0967							
Plutonium-239/240	12.5			10.1	pCi/g		81	(75%-125%)			
		Uncert:		+/-1.03							
		TPU:		+/-1.53							
QC1201215734	MB										
Plutonium-238			U	-0.0402	pCi/g					10/28/06	10:32
		Uncert:		+/-0.117							
		TPU:		+/-0.117							
Plutonium-239/240			U	-0.00717	pCi/g						
		Uncert:		+/-0.0798							
		TPU:		+/-0.0798							
QC1201215736	174791001	MS									
Plutonium-238		U	0.0128	0.0824	pCi/g			(75%-125%)		10/27/06	09:37
		Uncert:		+/-0.133							
		TPU:		+/-0.133							
Plutonium-239/240	12.5	U	0.0469	12.7	pCi/g		102	(75%-125%)			
		Uncert:		+/-0.129							
		TPU:		+/-0.129							
Batch	582800										
QC1201215739	174791001	DUP									
Plutonium-241		U	-1.93	U	-2.07	pCi/g	0	(0% - 100%)	4XA1	10/31/06	02:49
		Uncert:		+/-6.47							
		TPU:		+/-6.47							
QC1201215741	LCS										
Plutonium-241	144			134	pCi/g		93	(75%-125%)		10/31/06	03:21
		Uncert:		+/-12.2							
		TPU:		+/-17.8							
QC1201215738	MB										
Plutonium-241			U	-2.88	pCi/g					10/31/06	02:33
		Uncert:		+/-6.98							
		TPU:		+/-6.98							
QC1201215740	174791001	MS									
Plutonium-241	147	U	-1.93	131	pCi/g		90	(75%-125%)		10/31/06	03:05
		Uncert:		+/-6.47							
		TPU:		+/-6.47							
Rad Liquid Scintillation											
Batch	582786										
QC1201215680	174791001	DUP									
Iron-55		U	-7.05	U	-26.2	pCi/g	0	(0% - 100%)	4XP1	10/31/06	17:07
		Uncert:		+/-34.5							

GENERAL ENGINEERING LABORATORIES, LLC
 2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

QC Summary

Workorder: 174791

Page 3 of 5

Parmname	NOM	Sample	Qual	QC	Units	RPD%	REC%	Range	Anlst	Date	Time
Rad Liquid Scintillation											
Batch	582786										
QC1201215682	LCS										
Iron-55		679		624	pCi/g		92	(75%-125%)		10/31/06	17:40
		TPU:	+/-34.5								
		Uncert:		+/-48.6							
		TPU:		+/-72.2							
QC1201215679	MB										
Iron-55			U	7.04	pCi/g					10/31/06	16:50
		Uncert:		+/-28.0							
		TPU:		+/-28.0							
QC1201215681	174791001	MS									
Iron-55		763	U	-7.05	pCi/g		89	(75%-125%)		10/31/06	17:23
		Uncert:		+/-34.5							
		TPU:		+/-34.5							
Batch	582787										
QC1201215684	174791001	DUP									
Nickel-63			U	2.73	pCi/g	0		(0% - 100%)	MXP1	11/02/06	08:28
		Uncert:		+/-9.43							
		TPU:		+/-9.43							
QC1201215686	LCS										
Nickel-63		573		479	pCi/g		84	(75%-125%)		11/02/06	09:01
		Uncert:		+/-24.2							
		TPU:		+/-29.7							
QC1201215683	MB										
Nickel-63			U	-0.527	pCi/g					11/02/06	08:12
		Uncert:		+/-9.21							
		TPU:		+/-9.21							
QC1201215685	174791001	MS									
Nickel-63		581	U	2.73	pCi/g		78	(75%-125%)		11/02/06	08:45
		Uncert:		+/-9.43							
		TPU:		+/-9.43							
Batch	582788										
QC1201215688	174791001	DUP									
Technetium-99			U	0.120	pCi/g	0		(0% - 100%)	KXR1	11/02/06	10:42
		Uncert:		+/-0.236							
		TPU:		+/-0.236							
QC1201215690	LCS										
Technetium-99		12.8		11.6	pCi/g		91	(75%-125%)		11/02/06	11:14
		Uncert:		+/-0.496							
		TPU:		+/-0.559							
QC1201215687	MB										
Technetium-99			U	0.0646	pCi/g					11/02/06	10:26
		Uncert:		+/-0.215							
		TPU:		+/-0.215							
QC1201215689	174791001	MS									
Technetium-99		12.8	U	0.120	pCi/g		88	(75%-125%)		11/02/06	10:58
		Uncert:		+/-0.236							
		TPU:		+/-0.236							
Batch	582789										
QC1201215692	174791001	DUP									

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

QC Summary

Workorder: 174791

Page 4 of 5

Parmname	NOM	Sample Qual	QC	Units	RPD%	REC%	Range	Anlst	Date Time
Rad Liquid Scintillation									
Batch	582789								
Tritium	U	2.94	U	2.89	pCi/g	0	(0% - 100%)	MXP1	10/26/06 21:50
	Uncert:	+/-7.03		+/-6.93					
	TPU:	+/-7.03		+/-6.93					
QC1201215694	LCS								
Tritium	57.1			56.6	pCi/g	99	(75%-125%)		10/26/06 22:22
	Uncert:			+/-10.2					
	TPU:			+/-10.3					
QC1201215691	MB								
Tritium			U	3.92	pCi/g				10/26/06 21:34
	Uncert:			+/-6.59					
	TPU:			+/-6.59					
QC1201215693	174791001	MS							
Tritium	66.9	U	2.94	62.5	pCi/g	94	(75%-125%)		10/26/06 22:06
	Uncert:			+/-11.9					
	TPU:			+/-11.9					
Batch	582790								
QC1201215696	174791001	DUP							
Carbon-14	U	0.0304	U	0.0477	pCi/g	0	(0% - 100%)	AXD2	10/28/06 10:05
	Uncert:	+/-0.120		+/-0.113					
	TPU:	+/-0.120		+/-0.113					
QC1201215698	LCS								
Carbon-14	6.70			6.44	pCi/g	96	(75%-125%)		10/28/06 11:40
	Uncert:			+/-0.228					
	TPU:			+/-0.249					
QC1201215695	MB								
Carbon-14			U	-0.0883	pCi/g				10/28/06 09:18
	Uncert:			+/-0.109					
	TPU:			+/-0.109					
QC1201215697	174791001	MS							
Carbon-14	12.8	U	0.0304	12.2	pCi/g	95	(75%-125%)		10/28/06 10:53
	Uncert:			+/-0.433					
	TPU:			+/-0.473					

Notes:

The Qualifiers in this report are defined as follows:

- * A quality control analyte recovery is outside of specified acceptance criteria
 - < Result is less than value reported
 - > Result is greater than value reported
 - A The TIC is a suspected aldol-condensation product
 - B Target analyte was detected in the associated blank
 - BD Results are either below the MDC or tracer recovery is low
 - C Analyte has been confirmed by GC/MS analysis
 - D Results are reported from a diluted aliquot of the sample
 - H Analytical holding time was exceeded
 - J Value is estimated
- Spike recovery limits do not apply. Sample concentration exceeds spike concentration by 4X or more

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

QC Summary

Workorder: 174791

Page 5 of 5

Parmname	NOM	Sample Qual	QC	Units	RPD%	REC%	Range	Anlst	Date	Time
N/A										
R		Sample results are rejected								
U		Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.								
UI		Gamma Spectroscopy--Uncertain identification								
X		Consult Case Narrative, Data Summary package, or Project Manager concerning this qualifier								
Y		QC Samples were not spiked with this compound								
^		RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL								
h		Preparation or preservation holding time was exceeded								

N/A indicates that spike recovery limits do not apply when sample concentration exceeds spike conc. by a factor of 4 or more.

** Indicates analyte is a surrogate compound.

^ The Relative Percent Difference (RPD) obtained from the sample duplicate (DUP) is evaluated against the acceptance criteria when the sample is greater than five times (5X) the contract required detection limit (RL). In cases where either the sample or duplicate value is less than 5X the RL, a control limit of +/- the RL is used to evaluate the DUP result.

For PS, PSD, and SDILT results, the values listed are the measured amounts, not final concentrations.

Where the analytical method has been performed under NELAP certification, the analysis has met all of the requirements of the NELAC standard unless qualified on the QC Summary.

CASE NARRATIVE
For
CONNECTICUT YANKEE
RE: Soil
PO# 002332
Work Order: 170683
SDG: 170683

September 6, 2006

Laboratory Identification:

General Engineering Laboratories, LLC

Mailing Address:

P.O. Box 30712
Charleston, South Carolina 29417

Express Mail Delivery and Shipping Address:

2040 Savage Road
Charleston, South Carolina 29407

Telephone Number:

(843) 556-8171

Summary:

Sample receipt

The sample(s) for this Project arrived at General Engineering Laboratories, LLC, (GEL) in Charleston, South Carolina on August 17, 2006, July 07, 2006, July 13, 2006, July 21, 2006 and June 21, 2006. All sample containers arrived without any visible signs of tampering or breakage. The chain of custody contained the proper documentation and signatures.

The laboratory received the following sample(s):

<u>Sample ID</u>	<u>Client Sample ID</u>
170683001	9106-0011-018F
170683002	9106-0012-005F
170683003	9106-0012-014F
170683004	9106-0013-006F
170683005	9106-0013-005F
170683006	9106-0014-012F
170683007	9106-0014-033F
170683008	9106-0015-018F

GENERAL ENGINEERING LABORATORIES, LLC
a Member of THE GEL GROUP, INC.

P.O. Box 30712 • Charleston, SC 29417 • 2040 Savage Road (29407)
Phone (843) 556-8171 • Fax (843) 766-1178 • www.gel.com

170683009 9106-0015-002F
170683010 9106-0001-132F

Items of Note:

At the request of Dale Randall on August 31, 2006, the samples listed above were relogged for various analyses. A list of Sample ID's and requested tests follows.

Case Narrative:

Sample analyses were conducted using methodology as outlined in General Engineering Laboratories (GEL) Standard Operating Procedures. Any technical or administrative problems during analysis, data review, and reduction are listed below by analytical parameter.

Analytical Request:

Ten soil samples were analyzed for various analyses included in the FSSALL suite.

Internal Chain of Custody:

Custody was maintained for the sample(s).

Data Package:

The enclosed data package contains the following sections: Case Narrative, Chain of Custody and Supporting Documentation and all analytical fractions.

I certify that this data package is in compliance with the SOW, both technically and for completeness, for other than the conditions detailed above. Release of the data contained in this hard copy data package has been authorized by the Laboratory Manager or a designee, as verified by the following signature.



Cheryl Jones
Project Manager

Analysis request - 8/31/06

Done

To be done


Previous GEL ID	CY sample location IDs	FSS Gam	Sr-90	Ni-63	Am	Pu	Sr90	Pu241	Fe55	Ni63	Tc99	H3	C14
165614006	9106-0011-018F	x		x	X	X	X	X	X		X	X	X
166653003	9106-0012-005F	x			X	X	X	X	X	X	X	X	X
166653010	9106-0012-014F	x			X	X	X	X	X	X	X	X	X
167555007	9106-0013-005F	x			X	X	X	X	X	X	X	X	X
167555001	9106-0013-006F	x			X	X	X	X	X	X	X	X	X
167014026	9106-0014-012F	x			X	X	X	X	X	X	X	X	X
167014042	9106-0014-033F	x			X	X	X	X	X	X	X	X	X
167556010	9106-0015-002F	x	x		X	X		X	X	X	X	X	X
167556007	9106-0015-018F	x	x		X	X		X	X	X	X	X	X
169489001	9106-0001-132F	x			X	X	X	X	X	X	X	X	X

RELOGGED AS 170683

List of current GEL Certifications as of 06 September 2006

State	Certification
Alaska	UST-062
Arizona	AZ0668
Arkansas	88-0651
CLIA	42D0904046
California	01151CA
Colorado	GenEngLabs
Connecticut	PH-0169
Dept. of Navy	NFESC 413
EPA	WG-15J
Florida/NELAP	E87156
Georgia	E87156 (FL/NELAP)
Idaho	N/A
Illinois	200029
Indiana	C-SC-01
Kansas	E-10332
Kentucky	90129
Maryland	270
Massachusetts	M-SC012
Michigan	9903
Nevada	SC12
New Jersey	SC002
New York	11501
North Carolina	233
North Carolina Drinking W	45709
North Dakota	R-158
Oklahoma	9904
Pennsylvania	68-485
South Carolina	10120001/10585001/10120002
Tennessee	02934
Texas	TX213-2006A
U.S. Dept. of Agriculture	S-52597
US Army Corps of Engineer	N/A
Utah	8037697376 GEL
Vermont	N/A
Virginia	00151
Washington	C223

Chain of Custody And Supporting Documentation



SAMPLE RECEIPT & REVIEW FORM

PM use only

Client: CONN ATOMIC XANKEE	SDG/ARCO/Work Order: 165614
Date Received: 6-21-06	PM(A) Review (ensure non-conforming items are resolved prior to signing): <i>[Signature]</i>
Received By: ACM	

Sample Receipt Criteria	Yes	NA	No	Comments/Qualifiers (Required for Non-Conforming Items)
1 Shipping containers received intact and sealed?	/			Circle Applicable: seals broken damaged container leaking container other (describe)
2 Samples requiring cold preservation within (4 +/- 2 C)? Record preservation method.		/		Circle Coolant # ice bags blue ice dry ice none other (describe) 21°C
3 Chain of custody documents included with shipment?	/			
4 Sample containers intact and sealed?	/			Circle Applicable: seals broken damaged container leaking container other (describe)
5 Samples requiring chemical preservation at proper pH?		/		Sample ID's, containers affected and observed pH:
6 VOA vials free of headspace (defined as < 6mm bubble)?		/		Sample ID's and containers affected:
7 Are Encore containers present? (If yes, immediately deliver to VOA laboratory)			/	
8 Samples received within holding time?	/			Id's and tests affected:
9 Sample ID's on COC match ID's on bottles?	/			Sample ID's and containers affected:
10 Date & time on COC match date & time on bottles?			/	Sample ID's affected: TIME & DATES WERE WIPED OFF
11 Number of containers received match number indicated on COC?	/			Sample ID's affected:
12 COC form is properly signed in relinquished/received sections?	/			

14 Air Bill ,Tracking #'s, & Additional Comments	7910 2328 754D
--	-----------------------

Suspected Hazard Information	Non-Regulated	Regulated	High Level	RSO RAD Receipt # _____ *If > x2 area background is observed on samples identified as "non-regulated/non-radioactive", contact the Radiation Safety group for further investigation.
A Radiological Classification?		X		Maximum Counts Observed*: CAM 60
B PCB Regulated?	X			Comments:
C Shipped as DOT Hazardous Material? If yes, contact Waste Manager or ESH Manager.	X			Hazard Class Shipped: UN#:
PM (or PMA) review of Hazard classification:		Initials		Date: 6/21/06

Figure 1. Sample Check-in List

Date/Time Received: 6-21-06 0930

SDG#: MSR# 06-0877

Work Order Number: 1656141

Shipping Container ID: 7910 2328 2540 Chain of Custody #: 2006-00913

1. Custody Seals on shipping container intact? Yes No
2. Custody Seals dated and signed? Yes No
3. Chain-of-Custody record present? Yes No
4. Cooler temperature 24°C
5. Vermiculite/packing materials is: Wet Dry
6. Number of samples in shipping container: 8
7. Sample holding times exceeded? Yes No

8. Samples have:	
<input checked="" type="checkbox"/> tape	<input checked="" type="checkbox"/> hazard labels
<input checked="" type="checkbox"/> custody seals	<input checked="" type="checkbox"/> appropriate sample labels
9. Samples are:	
<input checked="" type="checkbox"/> in good condition	<input type="checkbox"/> leaking
<input type="checkbox"/> broken	<input type="checkbox"/> have air bubbles

10. Were any anomalies identified in sample receipt? Yes No

11. Description of anomalies (include sample numbers): _____

Sample Custodian/Laboratory: AMaly Date: 6/21/06 0930


Telephoned to: _____ On _____ By _____

Page 10 of 108

Connecticut Yankee Atomic Power Company						Chain of Custody Form						No. 2006-00451			
362 Injun Hollow Road, East Hampton, CT 06424 860-267-2556						166653-1									
Project Name: Haddam Neck Decommissioning			Media Code	Sample Type Code	Container Size & Type Code	Analyses Requested						Lab Use Only			
Contact Name & Phone: Jack McCarthy 860-267-2556 Ext. 3924						FSSGAM	FSSALL							Comments:	
Analytical Lab (Name, City, State) General Engineering Laboratories 2040 Savage Road. Charleston SC. 29407 843 556 8171. Attn. Cheryl Jones															
Priority: <input type="checkbox"/> 30 D. <input checked="" type="checkbox"/> 14 D. <input type="checkbox"/> 7 D.															
Sample Designation	Date	Time	Media Code	Sample Type Code	Container Size & Type Code	FSSGAM	FSSALL						Comment, Preservation	Lab Sample ID	
9106-0012-002F	6/23/06	08:56	SE	C	BP	X							Transferred from COC 2006-00436	001	
9106-0012-003F	6/23/06	08:39	SE	C	BP	X							Transferred from COC 2006-00436	002	
9106-0012-004F	6/23/06	09:32	SE	C	BP		X						Transferred from COC 2006-00436	016	
9106-0012-005F	6/23/06	09:56	SE	C	BP	X							Transferred from COC 2006-00436	003	
9106-0012-006F	6/23/06	13:07	SE	C	BP	X							Transferred from COC 2006-00436	004	
9106-0012-010F	6/23/06	11:08	SE	C	BP		X						Transferred from COC 2006-00436	017	
9106-0012-013F	6/23/06	10:56	SE	C	BP	X							Transferred from COC 2006-00436	005	
9106-0012-013FS	6/23/06	10:56	SE	C	BP	X							Transferred from COC 2006-00436	006	
NOTES: PO #: 002332 MSR #: 06-0960 SSWP# NA <input checked="" type="checkbox"/> LTP QA <input type="checkbox"/> Radwaste QA <input type="checkbox"/> Non QA												Samples Shipped Via: <input checked="" type="checkbox"/> Fed Ex <input type="checkbox"/> UPS <input type="checkbox"/> Hand <input type="checkbox"/> Other		Internal Container Temp.: ___ Deg. C Custody Sealed? Y <input type="checkbox"/> N <input type="checkbox"/> Custody Seal Intact? Y <input type="checkbox"/> N <input type="checkbox"/>	
1) Relinquished By JAME RICARTE			Date/Time 7-6-06 / 1400			2) Received By <i>[Signature]</i>			Date/Time 7/7/06 900			Bill of Lading # 7919 8876 4783			
3) Relinquished By			Date/Time			4) Received By			Date/Time						
5) Relinquished By			Date/Time			6) Received By			Date/Time						

Connecticut Yankee Atomic Power Company 362 Injun Hollow Road, East Hampton, CT 06424 860-267-2556						Chain of Custody Form				No. 2006-00452				
Project Name: Haddam Neck Decommissioning						Analyses Requested						Lab Use Only		
														Contact Name & Phone: Jack McCarthy 860-267-2556 Ext. 3924
Analytical Lab (Name, City, State) General Engineering Laboratories 2040 Savage Road. Charleston SC. 29407 843 556 8171. Attn. Cheryl Jones						FSSGAM FSSALL						Priority: <input type="checkbox"/> 30 D. <input checked="" type="checkbox"/> 14 D. <input type="checkbox"/> 7 D.		
														Sample Designation
9106-0012-007F			6/21/06	09:32	SE	C	BP	X					Transferred from COC # 2006-00433	007
9106-0012-008F			6/21/06	09:00	SE	C	BP	X					Transferred from COC # 2006-00433	008
9106-0012-012F			6/21/06	09:19	SE	C	BP	X					Transferred from COC # 2006-00433	009
9106-0012-014F			6/21/06	10:05	SE	C	BP	X					Transferred from COC # 2006-00433	010
9106-0012-011F			6/21/06	09:51	SE	C	BP	X					Transferred from COC # 2006-00433	011
9106-0012-015F			6/21/06	14:24	SE	C	BP	X					Transferred from COC # 2006-00433	012
9106-0012-009F			6/23/06	10:33	SE	C	BP	X					Transferred from COC # 2006-00436	013
9106-0012-009FS			6/23/06	10:33	SE	C	BP	X					Transferred from COC # 2006-00436	014
9106-0012-001F			6/23/06	09:18	SE	C	BP	X					Transferred from COC # 2006-00436	015
NOTES: PO #: 002332 MSR #: 06-0967 SSWP# NA <input checked="" type="checkbox"/> LTP QA <input type="checkbox"/> Radwaste QA <input type="checkbox"/> Non QA										Samples Shipped Via: <input checked="" type="checkbox"/> Fed Ex <input type="checkbox"/> UPS <input type="checkbox"/> Hand <input type="checkbox"/> Other		Internal Container Temp.: _____ Deg. C Custody Sealed? Y <input type="checkbox"/> N <input type="checkbox"/> Custody Seal Intact? Y <input type="checkbox"/> N <input type="checkbox"/>		
1) Relinquished By JAMIE RUADE			Date/Time 7-6-06/1400			2) Received By <i>Maria Santos</i>			Date/Time 7/7/06 900			Bill of Lading # 7927 8782 3129		
3) Relinquished By			Date/Time			4) Received By			Date/Time					
5) Relinquished By			Date/Time			6) Received By			Date/Time					

1666531



SAMPLE RECEIPT & REVIEW FORM

PM use only

Client: <u>Connecticut Yankee</u>	SDG/ARCOC/Work Order: <u>166653, 166655, 166656</u>
Date Received: <u>7/7/06</u>	PM(A) Review (ensure non-conforming items are resolved prior to signing):
Received By: <u>[Signature]</u>	<u>[Signature]</u>

	Sample Receipt Criteria	Yes	NA	No	Comments/Qualifiers (Required for Non-Conforming Items)
1	Shipping containers received intact and sealed?				Circle Applicable: seals broken damaged container leaking container other (describe)
2	Samples requiring cold preservation within (4 +/- 2 C)? Record preservation method.				Circle Coolant # ice bags blue ice dry ice none other describe)
3	Chain of custody documents included with shipment?				
4	Sample containers intact and sealed?				Circle Applicable: seals broken damaged container leaking container other (describe)
5	Samples requiring chemical preservation at proper pH?				Sample ID's, containers affected and observed pH:
6	VOA vials free of headspace (defined as < 6mm bubble)?				Sample ID's and containers affected:
7	Are Encore containers present? (If yes, immediately deliver to VOA laboratory)				
8	Samples received within holding time?				Id's and tests affected:
9	Sample ID's on COC match ID's on bottles?				Sample ID's and containers affected:
10	Date & time on COC match date & time on bottles?				Sample ID's affected:
11	Number of containers received match number indicated on COC?				Sample ID's affected:
12	COC form is properly signed in relinquished/received sections?				
14	Air Bill ,Tracking #'s, & Additional Comments				

Suspected Hazard Information	Non-Regulated	Regulated	High Level	RSO RAD Receipt # _____ *If > x2 area background is observed on samples identified as "non-regulated/non-radioactive", contact the Radiation Safety group for further investigation.
A Radiological Classification?				Maximum Counts Observed*: <u>14m 40</u>
B PCB Regulated?				Comments:
C Shipped as DOT Hazardous Material? If yes, contact Waste Manager or ESH Manager.				Hazard Class Shipped: UN#:

PM (or PMA) review of Hazard classification: _____ Initials [Signature] Date: 7/7/06

Figure 1. Sample Check-in List

Date/Time Received: 7/7/06

SDG#: _____

Work Order Number: 166653/166655/166656

Shipping Container ID: 7919 8876 4783 - 23°C Chain of Custody # 2006-00449
7910 4024 2957 - 22°C 2006-00445
7957 8782 3129 - 23°C 2006-00451
2006-00452

1. Custody Seals on shipping container intact? Yes No
2. Custody Seals dated and signed? Yes No
3. Chain-of-Custody record present? Yes No
4. Cooler temperature 23°C - 22°C - 23°C
5. Vermiculite/packing materials is: Wet Dry
6. Number of samples in shipping container: (1) 3 : (2) 12 (3) 9
7. Sample holding times exceeded? Yes No

8. Samples have:	
<input checked="" type="checkbox"/> tape	<input type="checkbox"/> hazard labels
<input type="checkbox"/> custody seals	<input type="checkbox"/> appropriate sample labels
9. Samples are:	
<input checked="" type="checkbox"/> in good condition	<input type="checkbox"/> leaking
<input type="checkbox"/> broken	<input type="checkbox"/> have air bubbles

10. Were any anomalies identified in sample receipt? Yes No
11. Description of anomalies (include sample numbers): _____

Sample Custodian/Laboratory: David Lathrop Date: 7/7/06 0900
Telephoned to: _____ On _____ By _____

1107555/.

Page 14 of 108

Connecticut Yankee Atomic Power Company

362 Injun Hollow Road, East Hampton, CT 06424
860-267-2556

Chain of Custody Form

No. 2006-00434

Project Name: Haddam Neck Decommissioning			Media Code	Sample Type Code	Container Size- & Type Code	Analyses Requested					Lab Use Only										
Contact Name & Phone: Jack McCarthy 860-267-2556 Ext. 3924						FSSGAM	FSSALL						Comments:								
Analytical Lab (Name, City, State) General Engineering Laboratories 2040 Savage Road, Charleston SC. 29407 843 556 8171. Attn. Cheryl Jones													FSSGAM	FSSALL							
Priority: <input type="checkbox"/> 30 D. <input checked="" type="checkbox"/> 14 D. <input type="checkbox"/> 7 D.																					
Sample Designation	Date	Time	Media Code	Sample Type Code	Container Size- & Type Code	FSSGAM	FSSALL					Comment, Preservation	Lab Sample ID								
9106-0013-006F	6/21/06	10:33	SE	C	BP	X															
9106-0013-003F	6/21/06	10:51	SE	C	BP	X															
9106-0013-002F	6/21/06	10:19	SE	C	BP	X															
9106-0013-002FS	6/21/06	10:19	SE	C	BP	X															
9106-0013-010F	6/21/06	13:56	SE	C	BP	X															
9106-0013-010FS	6/21/06	13:56	SE	C	BP	X															
9106-0013-005F	6/21/06	14:40	SE	C	BP	X															
9106-0013-011F	6/21/06	13:35	SE	C	BP	X															
NOTES: PO #: 002332 MSR #: 06-1036 SSWP# NA <input checked="" type="checkbox"/> LTP QA <input type="checkbox"/> Radwaste QA <input type="checkbox"/> Non QA											Samples Shipped Via: <input checked="" type="checkbox"/> Fed Ex <input type="checkbox"/> UPS <input type="checkbox"/> Hand <input type="checkbox"/> Other		Internal Container Temp.: 21 Deg. C Custody Sealed? Y <input type="checkbox"/> N <input checked="" type="checkbox"/> Custody Seal Intact? Y <input type="checkbox"/> N <input type="checkbox"/>								
1) Relinquished By SAIME RUIART			Date/Time 7-20-06 / 1445			2) Received By K. Light			Date/Time 7/20/06 0930			Bill of Lading # 7910-5711-1264									
3) Relinquished By			Date/Time			4) Received By			Date/Time												
5) Relinquished By			Date/Time			6) Received By			Date/Time												

167555/

Page 15 of 108

Connecticut Yankee Atomic Power Company

362 Injun Hollow Road, East Hampton, CT 06424
860-267-2556


Chain of Custody Form

No. 2006-00444

Project Name: Haddam Neck Decommissioning			Analyses Requested				Lab Use Only		
Contact Name & Phone: Jack McCarthy 860-267-3924			Media Code	Sample Type Code	Container Size & Type Code	FSSGAM	FSSALL	Comments:	
Analytical Lab (Name, City, State) General Engineering Laboratories 2040 Savage Road, Charleston SC. 29407 843 556 8171. Attn. Cheryl Jones									
Priority: <input type="checkbox"/> 30 D. <input checked="" type="checkbox"/> 14 D. <input type="checkbox"/> 7 D.									
Sample Designation	Date	Time	Media Code	Sample Type Code	Container Size & Type Code	FSSGAM	FSSALL	Comment, Preservation	Lab Sample ID
9106-0013-007F	6-27-06	10:58	SE	C	BP	X			
9106-0013-014F	6-27-06	09:22	SE	C	BP	X			
9106-0013-015F	6-26-06	15:06	SE	C	BP	X		Transferred from COC 2006-00438	
9106-0013-001F	6-23-06	13:32	SE	C	BP	X		Transferred from COC 2006-00437	
9106-0013-004F	6-23-06	13:51	SE	C	BP		X	Transferred from COC 2006-00437	
9106-0013-009F	6-23-06	14:08	SE	C	BP		X	Transferred from COC 2006-00437	
9106-0013-013F	6-23-06	14:38	SE	C	BP	X		Transferred from COC 2006-00437	
9106-0013-008F	6-26-06	11:11	SE	C	BP	X		Transferred from COC 2006-00438	
9106-0013-012F	6-26-06	12:35	SE	C	BP	X		Transferred from COC 2006-00438	

NOTES: PO #: 002332 MSR #: 06-5036 SSWP# NA <input checked="" type="checkbox"/> LTP QA <input type="checkbox"/> Radwaste QA <input type="checkbox"/> Non QA			Samples Shipped Via: <input checked="" type="checkbox"/> Fed Ex <input type="checkbox"/> UPS <input type="checkbox"/> Hand <input type="checkbox"/> Other		Internal Container Temp.: 21 Deg. C Custody Sealed? Y <input type="checkbox"/> N <input checked="" type="checkbox"/> Custody Seal Intact? Y <input type="checkbox"/> N <input type="checkbox"/>	
1) Relinquished By JAIME RICARTE		Date/Time 7-20-06/1445	2) Received By K. Wright		Date/Time 7/20/06 0930	
3) Relinquished By		Date/Time	4) Received By		Date/Time	

Bill of Lading #
7910 5711 1209



SAMPLE RECEIPT & REVIEW FORM

PM use only

Client: <u>Conn. Vank.</u>	SDG/ARCO/Work Order: <u>167554, 167555, 167556</u>
Date Received: <u>7/21/06</u>	PM(A) Review (ensure non-conforming items are resolved prior to signing): <u>[Signature]</u>
Received By: <u>[Signature]</u>	

Sample Receipt Criteria	Yes	NA	No	Comments/Qualifiers (Required for Non-Conforming Items)
1 Shipping containers received intact and sealed?	/			Circle Applicable: seals broken damaged container leaking container other (describe)
2 Samples requiring cold preservation within (4 +/- 2 C)? Record preservation method.	/			Circle Coolant # ice bags blue ice dry ice <u>none</u> other (describe) <u>See Cont. Sheet.</u>
3 Chain of custody documents included with shipment?	/			
4 Sample containers intact and sealed?	/			Circle Applicable: seals broken damaged container leaking container other (describe)
5 Samples requiring chemical preservation at proper pH?		/		Sample ID's, containers affected and observed pH:
6 VOA vials free of headspace (defined as < 6mm bubble)?		/		Sample ID's and containers affected:
7 Are Encore containers present? (If yes, immediately deliver to VOA laboratory)			/	
8 Samples received within holding time?	/			Id's and tests affected:
9 Sample ID's on COC match ID's on bottles?			/	Sample ID's and containers affected: <u>See Cont. Sheet</u>
10 Date & time on COC match date & time on bottles?	/			Sample ID's affected:
11 Number of containers received match number indicated on COC?	/			Sample ID's affected:
12 COC form is properly signed in relinquished/received sections?	/			

14 Air Bill, Tracking #'s, & Additional Comments
See sheet

Suspected Hazard Information	Non-Regulated	Regulated	High Level	RSO RAD Receipt #
A Radiological Classification?	/			*If > x2 area background is observed on samples identified as "non-regulated/non-radioactive", contact the Radiation Safety group for further investigation.
B PCB Regulated?	/			Maximum Counts Observed*: <u>cpm 40</u>
C Shipped as DOT Hazardous Material? If yes, contact Waste Manager or ESH Manager.	/			Comments: Hazard Class Shipped: UN#:

PM (or PMA) review of Hazard classification: _____ Initials [Signature] Date: 7/21/06

Figure 1. Sample Check-in List

Date/Time Received: 7/21/06 0930

SDG#: MSR#06-1035, MSR#06-1036, MSR#06-1037

Work Order Number: 167555/

Shipping Container ID: See cont. sheet Chain of Custody #: See cont. sheet

1. Custody Seals on shipping container intact? Yes No
2. Custody Seals dated and signed? Yes No N/A
3. Chain-of-Custody record present? Yes No
4. Cooler temperature See cont. sheet
5. Vermiculite/packing materials is: Wet Dry N/A
6. Number of samples in shipping container: See cont. sheet
7. Sample holding times exceeded? Yes No

8. Samples have:	
<input checked="" type="checkbox"/> tape	<input type="checkbox"/> hazard labels
<input checked="" type="checkbox"/> custody seals	<input checked="" type="checkbox"/> appropriate sample labels
9. Samples are:	
<input checked="" type="checkbox"/> in good condition	<input type="checkbox"/> leaking
<input type="checkbox"/> broken	<input type="checkbox"/> have air bubbles

10. Were any anomalies identified in sample receipt? Yes No

11. Description of anomalies (include sample numbers):

Sample Custodian/Laboratory: K. W. Flight Date: 7/21/06

Telephoned to: _____ On _____ By _____

167014-1

Page 19 of 108

Connecticut Yankee Atomic Power Company

362 Injun Hollow Road, East Hampton, CT 06424
860-267-2556

Chain of Custody Form

No. 2006-00456

Project Name: Haddam Neck Decommissioning			Media Code	Sample Type Code	Container Size & Type Code	Analyses Requested				Lab Use Only										
Contact Name & Phone: Jack McCarthy 860-267-2556 Ext. 3924						FSSGAM	FSSALL						Comments:							
Analytical Lab (Name, City, State) General Engineering Laboratories 2040 Savage Road, Charleston SC. 29407 843 556 8171. Attn. Cheryl Jones																				
Priority: <input type="checkbox"/> 30 D. <input checked="" type="checkbox"/> 14 D. <input type="checkbox"/> 7 D.																				
Sample Designation	Date	Time								Comment, Preservation	Lab Sample ID									
9106-0014-021F	6/15/06	10:50	SE	C	BP	X				Transferred from COC 2006-00407										
9106-0014-030F	6/15/06	11:20	SE	C	BP	X				Transferred from COC 2006-00407										
9106-0014-032F	6/15/06	09:31	SE	C	BP	X				Transferred from COC 2006-00407										
9106-0014-043F	6/16/06	08:45	SE	C	BP	X				Transferred from COC 2006-00409										
9106-0014-010F	6/12/06	14:23	SE	C	BP	X				Transferred from COC 2006-00391										
9106-0014-016F	6/12/06	14:51	SE	C	BP	X				Transferred from COC 2006-00391										
9106-0014-022F	6/12/06	15:12	SE	C	BP	X				Transferred from COC 2006-00391										
9106-0014-013F	6/13/06	15:06	SE	C	BP	X				Transferred from COC 2006-00394										
9106-0014-024F	6/07/06	09:58	SE	C	BP	X				Transferred from COC 2006-00385										
NOTES: PO #: 002332 MSR #: 06- 0958 SSWP# NA <input checked="" type="checkbox"/> LTP QA <input type="checkbox"/> Radwaste QA <input type="checkbox"/> Non QA										Samples Shipped Via: <input checked="" type="checkbox"/> Fed Ex <input type="checkbox"/> UPS <input type="checkbox"/> Hand <input type="checkbox"/> Other		Internal Container Temp.: _____ Deg. C Custody Sealed? Y <input type="checkbox"/> N <input type="checkbox"/> Custody Seal Intact? Y <input type="checkbox"/> N <input type="checkbox"/>								
1) Relinquished By JAIME RICARTE			Date/Time 7-12-06 / 1200			2) Received By <i>Marion [Signature]</i>			Date/Time 7/13/06 945			Bill of Lading # 7921 4950 3967								
3) Relinquished By			Date/Time			4) Received By			Date/Time											
5) Relinquished By			Date/Time			6) Received By			Date/Time											

021
052
083
084
085
086
087
088
089

167014/.

Page 20 of 108

Connecticut Yankee Atomic Power Company

362 Injun Hollow Road, East Hampton, CT 06424
860-267-2556

Chain of Custody Form

No. 2006-00457

Project Name: Haddam Neck Decommissioning							Analyses Requested				Lab Use Only			
Contact Name & Phone: Jack McCarthy 860-267-2556 Ext. 3924											Comments:			
Analytical Lab (Name, City, State) General Engineering Laboratories 2040 Savage Road, Charleston SC. 29407 843 556 8171. Attn. Cheryl Jones														
Priority: <input type="checkbox"/> 30 D. <input checked="" type="checkbox"/> 14 D. <input type="checkbox"/> 7 D.														
Sample Designation	Date	Time	Media Code	Sample Type Code	Container Size- & Type Code	FSSGAM	FSSALL					Comment, Preservation	Lab Sample ID	
010 9106-0014-025F	6/7/06	10:18	SE	C	BP	X						Transferred from COC 2006-00387		
011 9106-0014-031F	6/7/06	10:44	SE	C	BP	X						Transferred from COC 2006-00387		
012 9106-0014-017F	6/9/06	07:39	SE	C	BP	X						Transferred from COC 2006-00387		
013 9106-0014-023F	6/9/06	08:23	SE	C	BP	X						Transferred from COC 2006-00387		
014 9106-0014-035F	6/9/06	09:03	SE	C	BP	X						Transferred from COC 2006-00387		
043 9106-0014-038F	6/9/06	10:59	SE	C	BP		X					Transferred from COC 2006-00387		
015 9106-0014-039F	6/9/06	09:28	SE	C	BP	X						Transferred from COC 2006-00387		
016 9106-0014-042F	6/9/06	09:53	SE	C	BP	X						Transferred from COC 2006-00387		
017 9106-0014-034F	6/9/06	10:11	SE	C	BP	X						Transferred from COC 2006-00387		
NOTES: PO #: 002332 MSR #: 06- SSWP# NA <input checked="" type="checkbox"/> LTP QA <input type="checkbox"/> Radwaste QA <input type="checkbox"/> Non QA 0083											Samples Shipped Via: <input checked="" type="checkbox"/> Fed Ex <input type="checkbox"/> UPS <input type="checkbox"/> Hand <input type="checkbox"/> Other		Internal Container Temp.: ___ Deg. C Custody Sealed? Y <input type="checkbox"/> N <input type="checkbox"/> Custody Seal Intact? Y <input type="checkbox"/> N <input type="checkbox"/>	
1) Relinquished By JAIME RICARTE			Date/Time 7-12-06/1200			2) Received By <i>Maria Sotomayor</i>			Date/Time 7/13/06 945			Bill of Lading # 7921 4950 3989		
3) Relinquished By			Date/Time			4) Received By			Date/Time					
5) Relinquished By			Date/Time			6) Received By			Date/Time					

167014/.

Page 21 of 108

Connecticut Yankee Atomic Power Company

362 Injun Hollow Road, East Hampton, CT 06424
860-267-2556

Chain of Custody Form

No. 2006-00458

Project Name: Haddam Neck Decommissioning							Analyses Requested				Lab Use Only			
Contact Name & Phone: Jack McCarthy 860-267-2556 Ext. 3924											Comments:			
Analytical Lab (Name, City, State) General Engineering Laboratories 2040 Savage Road. Charleston SC. 29407 843 556 8171. Attn. Cheryl Jones														
Priority: <input type="checkbox"/> 30 D. <input checked="" type="checkbox"/> 14 D. <input type="checkbox"/> 7 D.														
Sample Designation	Date	Time	Media Code	Sample Type Code	Container Size- & Type Code	FSSGAM	FSSALL					Comment, Preservation	Lab Sample ID	
9106-0014-029F	6/09/06	08:42	SE	C	BP	X						Transferred from COC 2006-00387		
9106-0014-009F	6/13/06	08:44	SE	C	BP	X						Transferred from COC 2006-00392		
9106-0014-028F	6/13/06	08:08	SE	C	BP	X						Transferred from COC 2006-00392		
9106-0014-028FS	6/13/06	08:08	SE	C	BP	X						Transferred from COC 2006-00392		
9106-0014-036F	6/13/06	09:38	SE	C	BP	X						Transferred from COC 2006-00392		
9106-0014-037F	6/13/06	09:12	SE	C	BP		X					Transferred from COC 2006-00392		
9106-0014-040F	6/13/06	10:42	SE	C	BP	X						Transferred from COC 2006-00392		
9106-0014-041F	6/13/06	10:13	SE	C	BP	X						Transferred from COC 2006-00392		
9106-0014-041FS	6/13/06	10:13	SE	C	BP	X						Transferred from COC 2006-00392		
NOTES: PO #: 002332 MSR #: 06- 0984 SSWP# NA <input checked="" type="checkbox"/> LTP QA <input type="checkbox"/> Radwaste QA <input type="checkbox"/> Non QA											Samples Shipped Via: <input checked="" type="checkbox"/> Fed Ex <input type="checkbox"/> UPS <input type="checkbox"/> Hand <input type="checkbox"/> Other		Internal Container Temp.: ___ Deg. C Custody Sealed? Y <input type="checkbox"/> N <input type="checkbox"/> Custody Seal Intact? Y <input type="checkbox"/> N <input type="checkbox"/>	
1) Relinquished By JAIME RICARTE			Date/Time 7-12-06/1200			2) Received By <i>Marian Sathorn</i>			Date/Time 7/13/06 945			Bill of Lading # 7921 4950 401A		
3) Relinquished By			Date/Time			4) Received By			Date/Time					
5) Relinquished By			Date/Time			6) Received By			Date/Time					

88
99
100
101
102
103
104
105
106
107
108

167014/.

Page 22 of 108

Connecticut Yankee Atomic Power Company

362 Injun Hollow Road, East Hampton, CT 06424
860-267-2556

Chain of Custody Form

No. 2006-00459

Project Name: Haddam Neck Decommissioning			Media Code	Sample Type Code	Container Size- & Type Code	Analyses Requested					Lab Use Only				
Contact Name & Phone: Jack McCarthy 860-267-2556 Ext. 3924						FSSGAM	FSSALL						Comments		
Analytical Lab (Name, City, State) General Engineering Laboratories 2040 Savage Road, Charleston SC. 29407 843 556 8171. Attn. Cheryl Jones													Comment, Preservation		Lab Sample ID
Priority: <input type="checkbox"/> 30 D. <input checked="" type="checkbox"/> 14 D. <input type="checkbox"/> 7 D.															
Sample Designation	Date	Time													
026 45 127 128 029 330 031 032 46 9106-0014-012F	6/06/06	12:47	SE	C	BP	X					Transferred from COC 2006-00384				
9106-0014-018F	6/06/06	14:45	SE	C	BP		X				Transferred from COC 2006-00384				
9106-0014-019F	6/06/06	14:25	SE	C	BP	X					Transferred from COC 2006-00384				
9106-0014-001F	6/09/06	13:37	SE	C	BP	X					Transferred from COC 2006-00392				
9106-0014-002F	6/09/06	14:40	SE	C	BP	X					Transferred from COC 2006-00392				
9106-0014-002FS	6/09/06	14:40	SE	C	BP	X					Transferred from COC 2006-00392				
9106-0014-005F	6/09/06	14:12	SE	C	BP	X					Transferred from COC 2006-00392				
9106-0014-006F	6/09/06	13:07	SE	C	BP	X					Transferred from COC 2006-00392				
9106-0014-011F	6/09/06	12:44	SE	C	BP		X				Transferred from COC 2006-00392				
NOTES: PO #: 002332 MSR #: 06- 09 88 SSWP# NA <input checked="" type="checkbox"/> LTP QA <input type="checkbox"/> Radwaste QA <input type="checkbox"/> Non QA										Samples Shipped Via: <input checked="" type="checkbox"/> Fed Ex <input type="checkbox"/> UPS <input type="checkbox"/> Hand <input type="checkbox"/> Other		Internal Container Temp: _____ Temp: _____ Custody Sealed: _____ Custody Seal Intact: _____ Y E N C			
1) Relinquished By JAIME RICARTE			Date/Time 7-12-06/1200		2) Received By <i>[Signature]</i>			Date/Time 7/13/06 0945		Bill of Lading #					
3) Relinquished By			Date/Time		4) Received By			Date/Time		7921 4950 3990					
5) Relinquished By			Date/Time		6) Received By			Date/Time							

11670141

Page 23 of 108

Connecticut Yankee Atomic Power Company

362 Injun Hollow Road, East Hampton, CT 06424
860-267-2556

Chain of Custody Form

No. 2006-00460

Project Name: Haddam Neck Decommissioning							Analyses Requested				Lab Use Only				
Contact Name & Phone: Jack McCarthy 860-267-2556 Ext. 3924											Comments:				
Analytical Lab (Name, City, State) General Engineering Laboratories 2040 Savage Road, Charleston SC. 29407 843 556 8171. Attn. Cheryl Jones															
Priority: <input type="checkbox"/> 30 D. <input checked="" type="checkbox"/> 14 D. <input type="checkbox"/> 7 D.															
Sample Designation	Date	Time	Media Code	Sample Type Code	Container Size & Type Code	FSSGAM	FSSALL					Comment, Preservation	Lab Sample ID		
047 9106-0014-003F	6/14/06	08:46	SE	C	BP		X					Transferred from COC 2006-00396			
083 9106-0014-007F	6/14/06	09:13	SE	C	BP	X						Transferred from COC 2006-00396			
024 9106-0014-008F	6/14/06	07:34	SE	C	BP	X						Transferred from COC 2006-00396			
035 9106-0014-008FS	6/14/06	07:34	SE	C	BP	X						Transferred from COC 2006-00396			
026 9106-0014-014F	6/14/06	10:23	SE	C	BP	X						Transferred from COC 2006-00396			
NOTES: PO #: 002332 MSR #: 06- 0988 SSWP# NA <input checked="" type="checkbox"/> LTP QA <input type="checkbox"/> Radwaste QA <input type="checkbox"/> Non QA												Samples Shipped Via: <input checked="" type="checkbox"/> Fed Ex <input type="checkbox"/> UPS <input type="checkbox"/> Hand <input type="checkbox"/> Other		Internal Container Temp: _____ Deg C Custody Sealed? Y/N Custody Seal Intact? Y/N	
1) Relinquished By JAIME RICARTE			Date/Time 7-12-06/1200			2) Received By <i>Maureen Gath...</i>			Date/Time 7/13/06 0945						
3) Relinquished By			Date/Time			4) Received By			Date/Time			Bill of Lading # 7921 A950 3978			
5) Relinquished By			Date/Time			6) Received By			Date/Time						

167014/

Page 24 of 108

Connecticut Yankee Atomic Power Company

362 Injun Hollow Road, East Hampton, CT 06424
860-267-2556

Chain of Custody Form

No. 2006-00461

Project Name: Haddam Neck Decommissioning			Media Code	Sample Type Code	Container Size- & Type Code	Analyses Requested				Lab Use Only					
Contact Name & Phone: Jack McCarthy 860-267-2556 Ext. 3924						FSSGAM	FSSALL						Comments		
Analytical Lab (Name, City, State) General Engineering Laboratories 2040 Savage Road, Charleston SC. 29407 843 556 8171. Attn. Cheryl Jones													Comment, Preservation		Lab Sample ID
Priority: <input type="checkbox"/> 30 D. <input checked="" type="checkbox"/> 14 D. <input type="checkbox"/> 7 D.															
Sample Designation	Date	Time													
087 9106-0014-015F	6/14/06	11:39	SE	C	BP	X					Transferred from COC 2006-00396				
088 9106-0014-020F	6/14/06	13:10	SE	C	BP	X					Transferred from COC 2006-00396				
089 9106-0014-026F	6/14/06	13:53	SE	C	BP	X					Transferred from COC 2006-00396				
046 9106-0014-027F	6/14/06	14:26	SE	C	BP	X					Transferred from COC 2006-00396				
049 9106-0014-027FS	6/14/06	14:26	SE	C	BP	X					Transferred from COC 2006-00396				
042 9106-0014-033F	6/14/06	15:04	SE	C	BP	X									
NOTES: PO #: 002332 MSR #: 06- 0988 SSWP# NA <input checked="" type="checkbox"/> LTP QA <input type="checkbox"/> Radwaste QA <input type="checkbox"/> Non QA										Samples Shipped Via: <input checked="" type="checkbox"/> Fed Ex <input type="checkbox"/> UPS <input type="checkbox"/> Hand <input type="checkbox"/> Other					
1) Relinquished By JAIME RUARTE			Date/Time 7-12-06/1200			2) Received By <i>Mariano Lathen</i>			Date/Time 7/13/06 0945						
3) Relinquished By			Date/Time			4) Received By			Date/Time						
5) Relinquished By			Date/Time			6) Received By			Date/Time						
Bill of Lading #										7921 4950 3978					
Internal Container Temp: _____ Deg. C										Custody Sealed? Y <input type="checkbox"/> N <input type="checkbox"/>					
Custody Seal Intact? Y <input type="checkbox"/> N <input type="checkbox"/>															



SAMPLE RECEIPT & REVIEW FORM

PM use only

Client: <u>YANK</u>	SDG/ARCOC/Work Order: <u>16704</u>
Date Received: <u>7/13/06</u>	PM(A) Review (ensure non-conforming items are resolved prior to signing): <u>[Signature]</u>
Received By: <u>[Signature]</u>	

Sample Receipt Criteria	Yes	NA	No	Comments/Qualifiers (Required for Non-Conforming Items)
1 Shipping containers received intact and sealed?				Circle Applicable: seals broken damaged container leaking container other (describe)
2 Samples requiring cold preservation within (4 +/- 2 C)? Record preservation method.				Circle Coolant # ice bags blue ice dry ice none other describe
3 Chain of custody documents included with shipment?				
4 Sample containers intact and sealed?				Circle Applicable: seals broken damaged container leaking container other (describe)
5 Samples requiring chemical preservation at proper pH?				Sample ID's, containers affected and observed pH:
6 VOA vials free of headspace (defined as < 6mm bubble)?				Sample ID's and containers affected:
7 Are Encore containers present? (If yes, immediately deliver to VOA laboratory)				
8 Samples received within holding time?				ID's and tests affected:
9 Sample ID's on COC match ID's on bottles?				Sample ID's and containers affected:
10 Date & time on COC match date & time on bottles?				Sample ID's affected:
11 Number of containers received match number indicated on COC?				Sample ID's affected:
12 COC form is properly signed in relinquished/received sections?				
14 Air Bill, Tracking #'s, & Additional Comments				
Suspected Hazard Information				RSO RAD Receipt # _____ *If > x2 area background is observed on samples identified as "non-regulated/non-radioactive", contact the Radiation Safety group for further investigation.
A Radiological Classification?				Maximum Counts Observed*: <u>CPM 40</u>
B PCB Regulated?				Comments:
C Shipped as DOT Hazardous Material? If yes, contact Waste Manager or ESH Manager.				Hazard Class Shipped: UN#:

PM (or PMA) review of Hazard classification:

Initials [Signature]

Date: 7/13/06

Figure 1. Sample Check-in List

Date/Time Received: 7/13/06 0945

SDG#: MSR# 06-0988

Work Order Number: 167014

Shipping Container ID: 792149503789 Chain of Custody #: 2006-00456

1. Custody Seals on shipping container intact? Yes No
2. Custody Seals dated and signed? Yes No
3. Chain-of-Custody record present? Yes No
4. Cooler temperature 24°C
5. Vermiculite/packing materials is: Wet Dry
6. Number of samples in shipping container: 9
7. Sample holding times exceeded? Yes No

8. Samples have:	
<input checked="" type="checkbox"/> tape	<input type="checkbox"/> hazard labels
<input checked="" type="checkbox"/> custody seals	<input type="checkbox"/> appropriate sample labels
9. Samples are:	
<input checked="" type="checkbox"/> in good condition	<input type="checkbox"/> leaking
<input type="checkbox"/> broken	<input type="checkbox"/> have air bubbles

10. Were any anomalies identified in sample receipt? Yes No

11. Description of anomalies (include sample numbers): _____

Sample Custodian/Laboratory: Marisa [Signature] Date: 7/13/06 0945

Telephoned to: _____ On _____ By _____

Figure 1. Sample Check-in List

Date/Time Received: 7/13/06 0945

SDG#: MSR#06-0988

Work Order Number: 167014

Shipping Container ID: 7921 4950 3978
2006-0045 Chain of Custody #: 2006-0045

1. Custody Seals on shipping container intact? Yes No
2. Custody Seals dated and signed? Yes No
3. Chain-of-Custody record present? Yes No
4. Cooler temperature 24°C
5. Vermiculite/packing materials is: Wet Dry
6. Number of samples in shipping container: 9
7. Sample holding times exceeded? Yes No

8. Samples have:	
<input checked="" type="checkbox"/> tape	<input type="checkbox"/> hazard labels
<input checked="" type="checkbox"/> custody seals	<input type="checkbox"/> appropriate sample labels
9. Samples are:	
<input checked="" type="checkbox"/> in good condition	<input type="checkbox"/> leaking
<input type="checkbox"/> broken	<input type="checkbox"/> have air bubbles

10. Were any anomalies identified in sample receipt? Yes No

11. Description of anomalies (include sample numbers): _____

Sample Custodian/Laboratory: Marian Batters Date: 7/13/06 0945

Telephoned to: _____ On _____ By _____

Figure 1. Sample Check-in List

Date/Time Received: 7/13/06 0945

SDG#: MSR#06-0988

Work Order Number: 167014

Shipping Container ID: 7921 4950 3967 Chain of Custody #: 2006-00458

1. Custody Seals on shipping container intact? Yes No
2. Custody Seals dated and signed? Yes No
3. Chain-of-Custody record present? Yes No
4. Cooler temperature 24°C
5. Vermiculite/packing materials is: Wet Dry
6. Number of samples in shipping container: 9
7. Sample holding times exceeded? Yes No

8. Samples have:	
<input checked="" type="checkbox"/> tape	<input type="checkbox"/> hazard labels
<input checked="" type="checkbox"/> custody seals	<input type="checkbox"/> appropriate sample labels
9. Samples are:	
<input checked="" type="checkbox"/> in good condition	<input type="checkbox"/> leaking
<input type="checkbox"/> broken	<input type="checkbox"/> have air bubbles

10. Were any anomalies identified in sample receipt? Yes No

11. Description of anomalies (include sample numbers): _____

Sample Custodian/Laboratory: Marion Gathier Date: 7/13/06 0945

Telephoned to: _____ On _____ By _____

Figure 1. Sample Check-in List

Date/Time Received: 7/13/06 0945

SDG#: MSR#06-0988

Work Order Number: 167014

Shipping Container ID: 7921 4950 3990 Chain of Custody # 2006-00459

1. Custody Seals on shipping container intact? Yes No
2. Custody Seals dated and signed? Yes No
3. Chain-of-Custody record present? Yes No
4. Cooler temperature _____
5. Vermiculite/packing materials is: Wet Dry
6. Number of samples in shipping container: _____
7. Sample holding times exceeded? Yes No

8. Samples have:	
<input checked="" type="checkbox"/> tape	_____ hazard labels
<input checked="" type="checkbox"/> custody seals	_____ appropriate sample labels
9. Samples are:	
<input checked="" type="checkbox"/> in good condition	_____ leaking
_____ broken	_____ have air bubbles

10. Were any anomalies identified in sample receipt? Yes No

11. Description of anomalies (include sample numbers): _____

Sample Custodian/Laboratory: *Maria C. ...* Date: 7/13/06 0945

Telephoned to: _____ On _____ By _____

Figure 1. Sample Check-in List

Date/Time Received: 7/13/06 0945

SDG#: USR#06-0988

Work Order Number: 16704

Shipping Container ID: 7921 4950 3998 WJ 3978 Chain of Custody # 2006-00460 -00461

- 1. Custody Seals on shipping container intact? Yes No
- 2. Custody Seals dated and signed? Yes No
- 3. Chain-of-Custody record present? Yes No
- 4. Cooler temperature 23⁰⁰
- 5. Vermiculite/packing materials is: Wet Dry
- 6. Number of samples in shipping container: 11
- 7. Sample holding times exceeded? Yes No

8. Samples have:	
<input checked="" type="checkbox"/> tape	<input type="checkbox"/> hazard labels
<input checked="" type="checkbox"/> custody seals	<input type="checkbox"/> appropriate sample labels
9. Samples are:	
<input checked="" type="checkbox"/> in good condition	<input type="checkbox"/> leaking
<input type="checkbox"/> broken	<input type="checkbox"/> have air bubbles

10. Were any anomalies identified in sample receipt? Yes No

11. Description of anomalies (include sample numbers): _____

Sample Custodian/Laboratory: Maria Sathre Date: 7/13/06 0945
Telephoned to: _____ On _____ By _____

167556/.

Page 31 of 108

Connecticut Yankee Atomic Power Company

362 Injun Hollow Road, East Hampton, CT 06424
860-267-2556

Chain of Custody Form

No. 2006-00443

Project Name: Haddam Neck Decommissioning							Analyses Requested				Lab Use Only		
Contact Name & Phone: Jack McCarthy 860-267-3924							FSSGAM	FSSALL	Sr-90	Ni-63	Comments:		
Analytical Lab (Name, City, State) General Engineering Laboratories 2040 Savage Road, Charleston SC, 29407 843 556 8171. Attn. Cheryl Jones													
Priority: <input type="checkbox"/> 30 D. <input checked="" type="checkbox"/> 14 D. <input type="checkbox"/> 7 D.													
Sample Designation	Date	Time	Media Code	Sample Type Code	Container Size & Type Code						Comment, Preservation	Lab Sample ID	
1) 9106-0015-022F	6-27-06	16:24	SE	C	BP	X		X					
2) 9106-0015-023F	6-27-06	16:03	SE	C	BP	X		X					
3) 9106-0015-024F	6-27-06	15:42	SE	C	BP	X		X					
4) 9106-0015-026F	6-27-06	14:58	SE	C	BP	X		X					
5) 9106-0015-027F	6-27-06	15:17	SE	C	BP	X		X					
6) 9106-0015-028F	6-27-06	14:31	SE	C	BP	X		X					
7) 9106-0015-018F	6-27-06	17:18	SE	C	BP	X		X					
8) 9106-0015-025F	6-27-06	16:43	SE	C	BP	X		X					
9) 9106-0015-021F	6-27-06	17:01	SE	C	BP		X						
NOTES: PO #: 002332 MSR #: 06-1037 SSWP# NA <input checked="" type="checkbox"/> LTP QA <input type="checkbox"/> Radwaste QA <input type="checkbox"/> Non QA										Samples Shipped Via: <input checked="" type="checkbox"/> Fed Ex <input type="checkbox"/> UPS <input type="checkbox"/> Hand <input type="checkbox"/> Other		Internal Container Temp.: <u>22</u> Deg. C Custody Sealed? Y <input type="checkbox"/> N <input checked="" type="checkbox"/> Custody Seal Intact? Y <input type="checkbox"/> N <input type="checkbox"/>	
1) Relinquished By JAMES RICARTE			Date/Time 7-20-06/1445			2) Received By K. WRIGHT			Date/Time 7/21/06 0930			Bill of Lading # 7910 57 11 1301	
3) Relinquished By			Date/Time			4) Received By			Date/Time				

167556/.

Page 32 of 108

Connecticut Yankee Atomic Power Company

362 Injun Hollow Road, East Hampton, CT 06424
860-267-2556

Chain of Custody Form

No. 2006-00448

Project Name: Haddam Neck Decommissioning						Analyses Requested			Lab Use Only		
Contact Name & Phone: Jack McCarthy 860-267-3924						FSSGAM	FSSALL	Sr-90	Comments		
Analytical Lab (Name, City, State) General Engineering Laboratories 2040 Savage Road, Charleston SC, 29407 843 556 8171. Attn. Cheryl Jones											
Priority: <input type="checkbox"/> 30 D. <input checked="" type="checkbox"/> 14 D. <input type="checkbox"/> 7 D.											
Sample Designation	Date	Time	Media Code	Sample Type Code	Container Size & Type Code					Comment, Preservation	Lab Sample ID
18 9106-0015-011F	6-28-06	14:39	SE	C	BP	X		X			
19 9106-0015-012F	6-28-06	10:58	SE	C	BP	X		X			
20 9106-0015-013F	6-28-06	10:04	SE	C	BP	X		X			
21 9106-0015-014F	6-28-06	09:05	SE	C	BP	X		X			
31 9106-0015-015F	6-28-06	08:25	SE	C	BP		X				
22 9106-0015-016F	6-28-06	08:46	SE	C	BP	X		X			
23 9106-0015-017F	6-28-06	09:47	SE	C	BP	X		X			
24 9106-0015-019F	6-28-06	09:25	SE	C	BP	X		X			
25 9106-0015-020F	6-28-06	07:59	SE	C	BP	X		X			

NOTES: PO #: 002332 MSR #: 06-1037 SSWP# NA LTP QA Radwaste QA Non QA

Samples Shipped Via:
 Fed Ex
 UPS
 Hand
 Other

Internal Container Temp: 21 Deg. C
 Custody Sealed? Y N
 Custody Seal Intact? Y N

Bill of Lading #
7910 5711 1286

1) Relinquished By: JAMIE RICHIE Date/Time: 7-20-06/1445
 2) Received By: A. Leight Date/Time: 7/21/06 0930
 3) Relinquished By: _____ Date/Time: _____
 4) Received By: _____ Date/Time: _____

167556/.

Page 33 of 108

Connecticut Yankee Atomic Power Company

362 Injun Hollow Road, East Hampton, CT 06424
860-267-2556

Chain of Custody Form

No. 2006-00447

Project Name: Haddam Neck Decommissioning			Media Code	Sample Type Code	Container Size & Type Code	Analyses Requested				Lab Use Only				
Contact Name & Phone: Jack McCarthy 860-267-3924						FSSGAM	FSSALL	Sr-90					Comments:	
Analytical Lab (Name, City, State) General Engineering Laboratories 2040 Savage Road, Charleston SC. 29407 843 556 8171. Attn. Cheryl Jones														
Priority: <input type="checkbox"/> 30 D. <input checked="" type="checkbox"/> 14 D. <input type="checkbox"/> 7 D.														
Sample Designation	Date	Time								Comment, Preservation	Lab Sample ID			
9106-0015-001F	6-28-06	13:36	SE	C	BP	X		X						
9106-0015-002F	6-28-06	14:15	SE	C	BP	X		X						
9106-0015-003F	6-28-06	13:15	SE	C	BP	X		X						
9106-0015-004F	6-28-06	12:54	SE	C	BP		X							
9106-0015-005F	6-28-06	15:47	SE	C	BP	X		X						
9106-0015-006F	6-28-06	16:10	SE	C	BP	X		X						
9106-0015-007F	6-28-06	11:33	SE	C	BP	X		X						
9106-0015-008F	6-28-06	11:10	SE	C	BP	X		X						
9106-0015-009F	6-28-06	10:25	SE	C	BP	X		X						
9106-0015-010F	6-28-06	15:17	SE	C	BP	X		X						

NOTES: PO #: 002332 MSR #: 06-1037 SSWP# NA LTP QA Radwaste QA Non QA

Samples Shipped Via:
 Fed Ex
 UPS
 Hand
 Other

Internal Container Temp: 23 Deg. C
 Custody Sealed? Y N
 Custody Seal Intact? Y N

Bill of Lading #
79105711220

1) Relinquished By <i>SARME RICARTE</i>	Date/Time <i>7-20-06/1445</i>	2) Received By <i>B. Wright</i>	Date/Time <i>7/21/06 0930</i>
3) Relinquished By	Date/Time	4) Received By	Date/Time



SAMPLE RECEIPT & REVIEW FORM

PM use only

Client: <u>Conn. Yank.</u>	SDG/ARCOC/Work Order: <u>167554, 167555, 167556</u>
Date Received: <u>7/21/06</u>	PM(A) Review (ensure non-conforming items are resolved prior to signing): <i>[Signature]</i>
Received By: <u>[Signature]</u>	

Sample Receipt Criteria	Yes	NA	No	Comments/Qualifiers (Required for Non-Conforming Items)
1 Shipping containers received intact and sealed?	/			Circle Applicable: seals broken damaged container leaking container other (describe)
2 Samples requiring cold preservation within (4 +/- 2 C)? Record preservation method.	/			Circle Coolant / ice bags blue ice dry ice <u>none</u> other (describe) <u>see cont. sheet</u>
3 Chain of custody documents included with shipment?	/			
4 Sample containers intact and sealed?	/			Circle Applicable: seals broken damaged container leaking container other (describe)
5 Samples requiring chemical preservation at proper pH?		/		Sample ID's, containers affected and observed pH:
6 VOA vials free of headspace (defined as < 6mm bubble)?		/		Sample ID's and containers affected:
7 Are Encore containers present? (If yes, immediately deliver to VOA laboratory)			/	
8 Samples received within holding time?	/			Id's and tests affected:
9 Sample ID's on COC match ID's on bottles?			/	Sample ID's and containers affected: <u>see cont. sheet</u>
10 Date & time on COC match date & time on bottles?	/			Sample ID's affected:
11 Number of containers received match number indicated on COC?	/			Sample ID's affected:
12 COC form is properly signed in relinquished/received sections?	/			

14	Air Bill ,Tracking #'s, & Additional Comments	<u>see sheet</u>
----	---	------------------

Suspected Hazard Information	Non-Regulated	Regulated	High Level	RSO RAD Receipt # _____ *If > x2 area background is observed on samples identified as "non-regulated/non-radioactive", contact the Radiation Safety group for further investigation.
A Radiological Classification?	/			Maximum Counts Observed*: <u>cpm 40</u>
B PCB Regulated?	/			Comments:
C Shipped as DOT Hazardous Material? If yes, contact Waste Manager or ESH Manager.	/			Hazard Class Shipped: UN#:

PM (or PMA) review of Hazard classification:	Initials <u>[Signature]</u>	Date: <u>7/21/06</u>
--	-----------------------------	----------------------

Figure 1. Sample Check-in List

Date/Time Received: 7/21/06 0930

SDG#: MSR#06-1035, MSR#06-1036, MSR#06-1037

Work Order Number: 167556

Shipping Container ID: See Cont Sheet Chain of Custody #: See Cont Sheet

1. Custody Seals on shipping container intact? Yes No
2. Custody Seals dated and signed? Yes No N/A
3. Chain-of-Custody record present? Yes No
4. Cooler temperature See Cont Sheet
5. Vermiculite/packing materials is: Wet Dry N/A
6. Number of samples in shipping container: See Cont Sheet
7. Sample holding times exceeded? Yes No

8. Samples have:	
<input checked="" type="checkbox"/> tape	<input type="checkbox"/> hazard labels
<input checked="" type="checkbox"/> custody seals	<input checked="" type="checkbox"/> appropriate sample labels
9. Samples are:	
<input checked="" type="checkbox"/> in good condition	<input type="checkbox"/> leaking
<input type="checkbox"/> broken	<input type="checkbox"/> have air bubbles

10. Were any anomalies identified in sample receipt? Yes No

11. Description of anomalies (include sample numbers): _____

Sample Custodian/Laboratory: K. Wright Date: 7/21/06

Telephoned to: _____ On _____ By _____

Connecticut Yankee Atomic Power Company 362 Injun Hollow Road, East Hampton, CT 06424 860-267-2556						Chain of Custody Form					No. 2006-00497			
Project Name: Haddam Neck Decommissioning						Analyses Requested					Lab Use Only			
Contact Name & Phone: Jack McCarthy 860-267-2556 Ext. 3924						FSSGAM	FSSALL						Comments:	
Analytical Lab (Name, City, State) General Engineering Laboratories 2040 Savage Road, Charleston SC. 29407 843 556 8171. Attn. Cheryl Jones														
Priority: <input type="checkbox"/> 30 D. <input type="checkbox"/> 14 D. <input type="checkbox"/> 7 D. <input checked="" type="checkbox"/> 3 D.														
Sample Designation	Date	Time	Media Code	Sample Type Code	Container Size & Type Code						Comment, Preservation	Lab Sample ID		
9106-0001-112D			SE	C	BP	X								
NOTES: PO #: 002332 MSR #: 06-1130 SSWP# NA <input checked="" type="checkbox"/> LTP QA <input type="checkbox"/> Radwaste QA <input type="checkbox"/> Non QA											Samples Shipped Via: <input checked="" type="checkbox"/> Fed Ex <input type="checkbox"/> UPS <input type="checkbox"/> Hand <input type="checkbox"/> Other		Internal Container Temp: Deg Custody Sealed? Y <input checked="" type="checkbox"/> N <input type="checkbox"/> Custody Seal Intact? Y <input type="checkbox"/> N <input type="checkbox"/>	
1) Relinquished By JAME RICARTE			Date/Time 8-16-06/1155			2) Received By C. Dini cuta			Date/Time 8/17/06 @ 915a			Bill of Lading # 7921 8130 3482		
3) Relinquished By			Date/Time			4) Received By			Date/Time					
5) Relinquished By			Date/Time			6) Received By			Date/Time					

Figure 1. Sample Check-in List

Date/Time Received: 8/17/06 @ 9:54
SDG#: MSR#06-1130
Work Order Number: 1694897
Shipping Container ID: 792181303482 Chain of Custody #: 2606-PB496

1. Custody Seals on shipping container intact? Yes [] No []
2. Custody Seals dated and signed? Yes [] No []
3. Chain-of-Custody record present? Yes [] No []
4. Cooler temperature 26°C
5. Vermiculite/packing materials is: Wet [] Dry []
6. Number of samples in shipping container: 10 - samples
7. Sample holding times exceeded? Yes [] No []

8. Samples have:	
<input checked="" type="checkbox"/> tape	<input type="checkbox"/> hazard labels
<input checked="" type="checkbox"/> custody seals	<input type="checkbox"/> appropriate sample labels
9. Samples are:	
<input checked="" type="checkbox"/> in good condition	<input type="checkbox"/> leaking
<input type="checkbox"/> broken	<input type="checkbox"/> have air bubbles

10. Were any anomalies identified in sample receipt? Yes [] No []
11. Description of anomalies (include sample numbers): none

Sample Custodian/Laboratory: C. Duric Date: 8/17/06
Telephoned to: _____ On _____ By _____

RADIOLOGICAL ANALYSIS

**Radiochemistry Case Narrative
Connecticut Yankee Atomic Power Co. (YANK)
Work Order 170683**

Method/Analysis Information

Product: Alphaspec Am241, Cm, Solid ALL FSS
Analytical Method: DOE EML HASL-300, Am-05-RC Modified
Prep Method: Ash Soil Prep
Dry Soil Prep GL-RAD-A-021 Method: Dry Soil Prep
Analytical Batch Number: 565213
Prep Batch Number: 564526
Dry Soil Prep GL-RAD-A-021 Batch Number: 564525

Sample ID	Client ID
170683004	9106-0013-006F
170683005	9106-0013-005F
170683008	9106-0015-018F
170683009	9106-0015-002F
170683010	9106-0001-132F
1201175602	Method Blank (MB)
1201175603	170683004(9106-0013-006F) Sample Duplicate (DUP)
1201175604	170683004(9106-0013-006F) Matrix Spike (MS)
1201175605	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-011 REV# 14.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 170683004 (9106-0013-006F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

None of the samples in this sample set required reprep or reanalysis.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Manual Integration

No manual integrations were performed on data in this batch.

Additional Comments

The sample and the duplicate, 1201175603 (9106-0013-006F) and 170683004 (9106-0013-006F), did not meet the relative percent difference requirement, however they do meet the relative error ratio requirement with value of 2.11.

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product:	Alphaspec Am241, Cm, Solid ALL FSS
Analytical Method:	DOE EML HASL-300, Am-05-RC Modified
Prep Method:	Ash Soil Prep
Dry Soil Prep GL-RAD-A-021 Method:	Dry Soil Prep
Analytical Batch Number:	567705
Prep Batch Number:	564526
Dry Soil Prep GL-RAD-A-021 Batch Number:	564525

Sample ID	Client ID
170683001	9106-0011-018F
170683002	9106-0012-005F
170683003	9106-0012-014F
170683006	9106-0014-012F
170683007	9106-0014-033F
1201181287	Method Blank (MB)
1201181288	170683003(9106-0012-014F) Sample Duplicate (DUP)
1201181289	170683003(9106-0012-014F) Matrix Spike (MS)
1201181290	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering

Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-011 REV# 14.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 170683003 (9106-0012-014F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

Batch reprep'd due to Thorium interference.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Manual Integration

No manual integrations were performed on data in this batch.

Additional Comments

The sample and the duplicate, 1201181288 (9106-0012-014F) and 170683003 (9106-0012-014F), did not meet the Am-241 relative percent difference requirement, however they do meet the relative error ratio requirement with a value of 0.512.

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product:

Alphaspec Pu, Solid-ALL FSS

Analytical Method: DOE EML HASL-300, Pu-11-RC Modified
Prep Method: Ash Soil Prep
Dry Soil Prep GL-RAD-A-021 Method: Dry Soil Prep
Analytical Batch Number: 565210
Prep Batch Number: 564526
Dry Soil Prep GL-RAD-A-021 Batch Number: 564525

Sample ID	Client ID
170683001	9106-0011-018F
170683002	9106-0012-005F
170683003	9106-0012-014F
170683006	9106-0014-012F
170683007	9106-0014-033F
1201175591	Method Blank (MB)
1201175592	170683001(9106-0011-018F) Sample Duplicate (DUP)
1201175593	170683001(9106-0011-018F) Matrix Spike (MS)
1201175594	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-011 REV# 14.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 170683001 (9106-0011-018F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

None of the samples in this sample set required reprep or reanalysis.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Manual Integration

No manual integrations were performed on data in this batch.

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product:	Alphaspec Pu, Solid-ALL FSS
Analytical Method:	DOE EML HASL-300, Pu-11-RC Modified
Prep Method:	Ash Soil Prep
Dry Soil Prep GL-RAD-A-021 Method:	Dry Soil Prep
Analytical Batch Number:	565214
Prep Batch Number:	564526
Dry Soil Prep GL-RAD-A-021 Batch Number:	564525

Sample ID	Client ID
170683004	9106-0013-006F
170683005	9106-0013-005F
170683008	9106-0015-018F
170683009	9106-0015-002F
170683010	9106-0001-132F
1201175606	Method Blank (MB)
1201175607	170683004(9106-0013-006F) Sample Duplicate (DUP)
1201175608	170683004(9106-0013-006F) Matrix Spike (MS)
1201175609	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-011 REV# 14.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 170683004 (9106-0013-006F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

None of the samples in this sample set required reprep or reanalysis.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Manual Integration

No manual integrations were performed on data in this batch.

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product:	Liquid Scint Pu241, Solid-ALL FSS
Analytical Method:	DOE EML HASL-300, Pu-11-RC Modified
Prep Method:	Ash Soil Prep
Dry Soil Prep GL-RAD-A-021 Method:	Dry Soil Prep
Analytical Batch Number:	565216
Prep Batch Number:	564526
Dry Soil Prep GL-RAD-A-021 Batch Number:	564525

Sample ID	Client ID
170683004	9106-0013-006F
170683005	9106-0013-005F
170683008	9106-0015-018F
170683009	9106-0015-002F
170683010	9106-0001-132F
1201175614	Method Blank (MB)
1201175615	170683004(9106-0013-006F) Sample Duplicate (DUP)

1201175616 170683004(9106-0013-006F) Matrix Spike (MS)
1201175617 Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-035 REV# 8.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 170683004 (9106-0013-006F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

Samples 1201175614 (MB), 1201175615 (9106-0013-006F), 170683004 (9106-0013-006F), 170683005 (9106-0013-005F), 170683008 (9106-0015-018F), 170683009 (9106-0015-002F) and 170683010 (9106-0001-132F) were recounted due to high MDAs.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Manual Integration

No manual integrations were performed on data in this batch.

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product: Liquid Scint Pu241, Solid-ALL FSS
Analytical Method: DOE EML HASL-300, Pu-11-RC Modified
Prep Method: Ash Soil Prep
Dry Soil Prep GL-RAD-A-021 Method: Dry Soil Prep
Analytical Batch Number: 567883
Prep Batch Number: 564526
Dry Soil Prep GL-RAD-A-021 Batch Number: 564525

Sample ID	Client ID
170683001	9106-0011-018F
170683002	9106-0012-005F
170683003	9106-0012-014F
170683006	9106-0014-012F
170683007	9106-0014-033F
1201181751	Method Blank (MB)
1201181752	170683001(9106-0011-018F) Sample Duplicate (DUP)
1201181753	170683001(9106-0011-018F) Matrix Spike (MS)
1201181754	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-035 REV# 8.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 170683001 (9106-0011-018F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

The batch was reprepared due to high MDAs.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Manual Integration

No manual integrations were performed on data in this batch.

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product:	GFPC, Sr90, solid-ALL FSS
Analytical Method:	EPA 905.0 Modified
Prep Method:	Ash Soil Prep
Dry Soil Prep GL-RAD-A-021 Method:	Dry Soil Prep
Analytical Batch Number:	565250
Prep Batch Number:	564526
Dry Soil Prep GL-RAD-A-021 Batch Number:	564525

Sample ID	Client ID
170683001	9106-0011-018F
170683002	9106-0012-005F
170683003	9106-0012-014F
170683006	9106-0014-012F
170683007	9106-0014-033F
1201175679	Method Blank (MB)
1201175680	170683002(9106-0012-005F) Sample Duplicate (DUP)
1201175681	170683002(9106-0012-005F) Matrix Spike (MS)
1201175682	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-004 REV# 10.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:**Blank Information**

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 170683002 (9106-0012-005F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:**Holding Time**

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

Samples 170683001 (9106-0011-018F) and 170683006 (9106-0014-012F) were recounted due to high MDAs.

Chemical Recoveries

All chemical recoveries meet the required acceptance limits for this sample set.

Miscellaneous Information:**NCR Documentation**

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Additional Comments

Samples were dried and reweighed due to low matrix spike recovery.

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product:	GFPC, Sr90, solid-ALL FSS
Analytical Method:	EPA 905.0 Modified
Prep Method:	Ash Soil Prep
Dry Soil Prep GL-RAD-A-021 Method:	Dry Soil Prep
Analytical Batch Number:	565253
Prep Batch Number:	564526
Dry Soil Prep GL-RAD-A-021 Batch Number:	564525

Sample ID	Client ID
170683004	9106-0013-006F
170683005	9106-0013-005F
170683010	9106-0001-132F

1201175686 Method Blank (MB)
1201175687 170683005(9106-0013-005F) Sample Duplicate (DUP)
1201175688 170683005(9106-0013-005F) Matrix Spike (MS)
1201175689 Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-004 REV# 10.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 170683005 (9106-0013-005F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

None of the samples in this sample set required reprep or reanalysis.

Chemical Recoveries

All chemical recoveries meet the required acceptance limits for this sample set.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product: Liquid Scint Tc99, Solid-ALL FSS
Analytical Method: DOE EML HASL-300, Tc-02-RC Modified
Analytical Batch Number: 564445

Sample ID	Client ID
170683004	9106-0013-006F
170683005	9106-0013-005F
170683008	9106-0015-018F
170683009	9106-0015-002F
1201173840	Method Blank (MB)
1201173841	170544018(9304-0002-005F) Sample Duplicate (DUP)
1201173842	170544018(9304-0002-005F) Matrix Spike (MS)
1201173843	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-005 REV# 13.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 170544018 (9304-0002-005F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

None of the samples in this sample set required reprep or reanalysis.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product: Liquid Scint Tc99, Solid-ALL FSS
Analytical Method: DOE EML HASL-300, Tc-02-RC Modified
Analytical Batch Number: 564623

Sample ID	Client ID
170683001	9106-0011-018F
170683002	9106-0012-005F
170683003	9106-0012-014F
170683006	9106-0014-012F
170683007	9106-0014-033F
1201174253	Method Blank (MB)
1201174254	170683001(9106-0011-018F) Sample Duplicate (DUP)
1201174255	170683001(9106-0011-018F) Matrix Spike (MS)
1201174256	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-005 REV# 13.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 170683001 (9106-0011-018F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

Sample 1201174254 (9106-0011-018F) was recounted due to high MDA.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product: Liquid Scint Tc99, Solid-ALL FSS
Analytical Method: DOE EML HASL-300, Tc-02-RC Modified
Analytical Batch Number: 565648

Sample ID	Client ID
170683010	9106-0001-132F
1201176786	Method Blank (MB)
1201176787	170683010(9106-0001-132F) Sample Duplicate (DUP)
1201176788	170683010(9106-0001-132F) Matrix Spike (MS)
1201176789	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-005 REV# 13.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 170683010 (9106-0001-132F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

None of the samples in this sample set required reprep or reanalysis.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product:	Liquid Scint Fe55, Solid-ALL FSS
Analytical Method:	DOE RESL Fe-1, Modified
Prep Method:	Ash Soil Prep
Dry Soil Prep GL-RAD-A-021 Method:	Dry Soil Prep
Analytical Batch Number:	565287
Prep Batch Number:	564526
Dry Soil Prep GL-RAD-A-021 Batch Number:	564525

Sample ID	Client ID
170683001	9106-0011-018F
170683002	9106-0012-005F
170683003	9106-0012-014F
170683006	9106-0014-012F
170683007	9106-0014-033F
1201175808	Method Blank (MB)
1201175809	170683006(9106-0014-012F) Sample Duplicate (DUP)
1201175810	170683006(9106-0014-012F) Matrix Spike (MS)
1201175811	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-040 REV# 3.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 170683006 (9106-0014-012F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

Samples 1201175810 (9106-0014-012F), 170683001 (9106-0011-018F), 170683002 (9106-0012-005F) and 170683006 (9106-0014-012F) were recounted due to the quench number being outside the calibration range.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. The following NCR was generated for this SDG:

NCR 356906 was generated due to Container scanning event for custody missed. 1. The analyst did not scan the sample 170683001 into the batch prior to analysis, however the samples did remain in their custody at all times. 1. The error has been corrected and the analyst has been instructed on the proper scanning procedures. Reporting results.

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product:	Liquid Scint Fe55, Solid-ALL FSS
Analytical Method:	DOE RESL Fe-1, Modified
Prep Method:	Ash Soil Prep
Dry Soil Prep GL-RAD-A-021 Method:	Dry Soil Prep
Analytical Batch Number:	565291
Prep Batch Number:	564526

Dry Soil Prep GL-RAD-A-021 Batch Number: 564525

Sample ID	Client ID
170683004	9106-0013-006F
170683005	9106-0013-005F
170683008	9106-0015-018F
170683009	9106-0015-002F
170683010	9106-0001-132F
1201175818	Method Blank (MB)
1201175819	170683004(9106-0013-006F) Sample Duplicate (DUP)
1201175820	170683004(9106-0013-006F) Matrix Spike (MS)
1201175821	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-040 REV# 3.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 170683004 (9106-0013-006F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

Samples 170683004 (9106-0013-006F) and 170683009 (9106-0015-002F) were recounted due to the quench number being outside the calibration range.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product:	Liquid Scint Ni63, Solid-ALL FSS
Analytical Method:	DOE RESL Ni-1, Modified
Prep Method:	Ash Soil Prep
Dry Soil Prep GL-RAD-A-021 Method:	Dry Soil Prep
Analytical Batch Number:	565289
Prep Batch Number:	564526
Dry Soil Prep GL-RAD-A-021 Batch Number:	564525

Sample ID	Client ID
170683002	9106-0012-005F
170683003	9106-0012-014F
170683006	9106-0014-012F
170683007	9106-0014-033F
1201175814	Method Blank (MB)
1201175815	170683006(9106-0014-012F) Sample Duplicate (DUP)
1201175816	170683006(9106-0014-012F) Matrix Spike (MS)
1201175817	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-022 REV# 8.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 170683006 (9106-0014-012F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

None of the samples in this sample set required reprep or reanalysis.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product:	Liquid Scint Ni63, Solid-ALL FSS
Analytical Method:	DOE RESL Ni-1, Modified
Prep Method:	Ash Soil Prep
Dry Soil Prep GL-RAD-A-021 Method:	Dry Soil Prep
Analytical Batch Number:	565293
Prep Batch Number:	564526
Dry Soil Prep GL-RAD-A-021 Batch Number:	564525

Sample ID	Client ID
170683004	9106-0013-006F
170683005	9106-0013-005F
170683008	9106-0015-018F
170683009	9106-0015-002F
170683010	9106-0001-132F
1201175822	Method Blank (MB)
1201175823	170683004(9106-0013-006F) Sample Duplicate (DUP)
1201175824	170683004(9106-0013-006F) Matrix Spike (MS)
1201175825	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-022 REV# 8.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 170683004 (9106-0013-006F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

None of the samples in this sample set required reprep or reanalysis.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product: LSC, Tritium Dist, Solid-HTD2,ALL FSS

Analytical Method: EPA 906.0 Modified

Analytical Batch Number: 564447

Sample ID	Client ID
170683004	9106-0013-006F
170683005	9106-0013-005F
170683008	9106-0015-018F
170683009	9106-0015-002F
1201173844	Method Blank (MB)
1201173845	170544018(9304-0002-005F) Sample Duplicate (DUP)
1201173846	170544018(9304-0002-005F) Matrix Spike (MS)
1201173847	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-002 REV# 13.

Calibration Information:**Calibration Information**

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:**Blank Information**

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 170544018 (9304-0002-005F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:**Holding Time**

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

Samples 1201173846 (9304-0002-005F) and 1201173847 (LCS) were recounted due to low/high recovery.

Miscellaneous Information:**NCR Documentation**

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. The following NCR was generated for this SDG:

NCR 356177 was generated due to Container scanning event for custody missed. 1. Container scanning event for custody missed: The analyst did not scan the samples into the batch prior to analysis, however the samples did remain in their custody at all times. 1. The error has been corrected and the analyst has been instructed on proper scanning procedures. Reporting results

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product: LSC, Tritium Dist, Solid-HTD2,ALL FSS

Analytical Method: EPA 906.0 Modified

Analytical Batch Number: 564514

Sample ID	Client ID
170683001	9106-0011-018F
170683002	9106-0012-005F
170683003	9106-0012-014F
170683006	9106-0014-012F
170683007	9106-0014-033F
1201174038	Method Blank (MB)
1201174039	170683006(9106-0014-012F) Sample Duplicate (DUP)
1201174040	170683006(9106-0014-012F) Matrix Spike (MS)
1201174041	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-002 REV# 13.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 170683006 (9106-0014-012F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

None of the samples in this sample set required reprep or reanalysis.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product: LSC, Tritium Dist, Solid-HTD2,ALL FSS
Analytical Method: EPA 906.0 Modified
Analytical Batch Number: 565650

Sample ID	Client ID
170683010	9106-0001-132F
1201176794	Method Blank (MB)
1201176795	170683010(9106-0001-132F) Sample Duplicate (DUP)
1201176796	170683010(9106-0001-132F) Matrix Spike (MS)
1201176797	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-002 REV# 13.

Calibration Information:**Calibration Information**

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:**Blank Information**

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 170683010 (9106-0001-132F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:**Holding Time**

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

None of the samples in this sample set required reprep or reanalysis.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product: Liquid Scint C14, Solid All,FSS

Analytical Method: EPA EERF C-01 Modified

Analytical Batch Number: 564449

Sample ID	Client ID
170683004	9106-0013-006F
170683005	9106-0013-005F
170683008	9106-0015-018F
170683009	9106-0015-002F
1201173848	Method Blank (MB)
1201173849	170544019(9304-0002-008F) Sample Duplicate (DUP)
1201173850	170544019(9304-0002-008F) Matrix Spike (MS)
1201173851	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-003 REV# 8.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 170544019 (9304-0002-008F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:**Holding Time**

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

Sample 1201173849 (9304-0002-008F) was recounted due to a negative result greater than three times the error. Samples 170683008 (9106-0015-018F) and 170683009 (9106-0015-002F) were recounted to verify results. Second counts being reported.

Miscellaneous Information:**NCR Documentation**

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product: Liquid Scint C14, Solid All,FSS

Analytical Method: EPA EERF C-01 Modified

Analytical Batch Number: 564520

Sample ID	Client ID
170683001	9106-0011-018F
170683002	9106-0012-005F
170683003	9106-0012-014F
170683006	9106-0014-012F
170683007	9106-0014-033F
1201174056	Method Blank (MB)
1201174057	170683007(9106-0014-033F) Sample Duplicate (DUP)
1201174058	170683007(9106-0014-033F) Matrix Spike (MS)
1201174059	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-003 REV# 8.

Calibration Information:**Calibration Information**

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 170683007 (9106-0014-033F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

None of the samples in this sample set required reprep or reanalysis.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Qualifier information

Manual qualifiers were not required.

Method/Analysis Information

Product: Liquid Scint C14, Solid All,FSS
Analytical Method: EPA EERF C-01 Modified
Analytical Batch Number: 565649

Sample ID	Client ID
170683010	9106-0001-132F
1201176790	Method Blank (MB)
1201176791	170683010(9106-0001-132F) Sample Duplicate (DUP)
1201176792	170683010(9106-0001-132F) Matrix Spike (MS)
1201176793	Laboratory Control Sample (LCS)

SOP Reference

Procedure for preparation, analysis and reporting of analytical data are controlled by General Engineering Laboratories, LLC as Standard Operating Procedure (SOP). The data discussed in this narrative has been analyzed in accordance with GL-RAD-A-003 REV# 8.

Calibration Information:

Calibration Information

All initial and continuing calibration requirements have been met.

Standards Information

Standard solution(s) for these analyses are NIST traceable and used before the expiration date(s).

Sample Geometry

All counting sources were prepared in the same geometry as the calibration standards.

Quality Control (QC) Information:

Blank Information

The blank volume is representative of the sample volume in this batch.

Designated QC

The following sample was used for QC: 170683010 (9106-0001-132F).

QC Information

All of the QC samples met the required acceptance limits.

Technical Information:

Holding Time

All sample procedures for this sample set were performed within the required holding time.

Preparation Information

All preparation criteria have been met for these analyses.

Sample Re-prep/Re-analysis

None of the samples in this sample set required reprep or reanalysis.

Miscellaneous Information:

NCR Documentation

Nonconformance reports are generated to document any procedural anomalies that may deviate from referenced SOP or contractual documents. A nonconformance report (NCR) was not generated for this SDG.

Qualifier information

Manual qualifiers were not required.

Certification Statement


Where the analytical method has been performed under NELAP certification, the analysis has met all of the requirements of the NELAC standard unless otherwise noted in the analytical case narrative.

Review Validation:

GEL requires all analytical data to be verified by a qualified data validator. In addition, all data designated for CLP or CLP-like packaging will receive a third level validation upon completion of the data package.

The following data validator verified the information presented in this case narrative:

Reviewer/Date: _____



COMPANY - WIDE NONCONFORMANCE REPORT			
Mo. Day Yr. 11-SEP-06	Division: Radiochemistry	Quality Criteria: Specifications	Type: Process
Instrument Type: LSC	Test / Method: DOE RESL Fe-1, Modified	Matrix Type: Solid	Client Code: YANK
Batch ID: 565287	Sample Numbers: See Below		
Potentially affected work order(s)(SDG): 170683			
Application Issues: Container scanning event for custody missed			
Specification and Requirements		NRG Disposition:	
Nonconformance Description:			
1. The analyst did not scan the sample 170683001 into the batch prior to analysis, however the samples did remain in their custody at all times.		1. The error has been corrected and the analyst has been instructed on the proper scanning procedures. Reporting results.	

Originator's Name:
 Melanie Aycock 11-SEP-06

Data Validator/Group Leader:
 Heather Anderson 11-SEP-06

Quality Review:

Director:

COMPANY - WIDE NONCONFORMANCE REPORT			
Mo. Day Yr. 08-SEP-06	Division: Radiochemistry	Quality Criteria: Specifications	Type: Process
Instrument Type: LSC	Test / Method: EPA 906.0 Modified	Matrix Type: Solid	Client Code: YANK
Batch ID: 564447	Sample Numbers: See Below		
Potentially affected work order(s)(SDG): 170543(MSR#06-1172),170544(MSR#06-1174),170683			
Application Issues: Container scanning event for custody missed			
Specification and Requirements		NRG Disposition:	
Nonconformance Description:			
1. Container scanning event for custody missed: The analyst did not scan the samples into the batch prior to analysis, however the samples did remain in their custody at all times.		1. The error has been corrected and the analyst has been instructed on proper scanning procedures. Reporting results	

Originator's Name:
 Kenshalla Oston 08-SEP-06

Data Validator/Group Leader:
 Melanie Aycock 08-SEP-06

Quality Review:

Director:

SAMPLE DATA SUMMARY

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

**Certificate of Analysis Report
for**

YANK001 Connecticut Yankee Atomic Power Co.

Client SDG: 170683 GEL Work Order: 170683

The Qualifiers in this report are defined as follows:

- * A quality control analyte recovery is outside of specified acceptance criteria
- ** Analyte is a surrogate compound
- U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
- ND The analyte concentration is not detected above the detection limit.

The above sample is reported on a dry weight basis except where prohibited by the analytical procedure.

Where the analytical method has been performed under NELAP certification, the analysis has met all of the requirements of the NELAC standard unless qualified on the Certificate of Analysis.

This data report has been prepared and reviewed in accordance with General Engineering Laboratories, LLC standard operating procedures. Please direct any questions to your Project Manager, Cheryl Jones.



Reviewed by _____

GENERAL ENGINEERING LABORATORIES, LLC
2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: September 18, 2006

Client Sample ID:	9106-0011-018F	Project:	YANK01204
Sample ID:	170683001	Client ID:	YANK001
Matrix:	SE	Vol. Recv.:	
Collect Date:	17-MAY-06		
Receive Date:	21-JUN-06		
Collector:	Client		
Moisture:	36.3%		

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Alpha Spec Analysis													
<i>Alphaspec Am241, Cm, Solid ALL FSS</i>													
Americium-241	U	0.0277	+/-0.0418	0.0128	+/-0.042	0.0643	pCi/g	TC1	09/14/06	0931	567705		1
Curium-242	U	0.00666	+/-0.0505	0.037	+/-0.0505	0.138	pCi/g						
Curium-243/244	U	-0.0167	+/-0.0348	0.0388	+/-0.0349	0.117	pCi/g						
<i>Alphaspec Pu, Solid-ALL FSS</i>													
Plutonium-238	U	-0.148	+/-0.269	0.289	+/-0.270	0.795	pCi/g	MXA	09/11/06	0919	565210		3
Plutonium-239/240	U	0.00321	+/-0.174	0.144	+/-0.174	0.505	pCi/g	1					
<i>Liquid Scint Pu241, Solid-ALL FSS</i>													
Plutonium-241	U	9.87	+/-11.1	8.90	+/-11.1	18.6	pCi/g	TC1	09/17/06	0214	567883		4
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid-ALL FSS</i>													
Strontium-90	U	0.00422	+/-0.0151	0.0123	+/-0.0151	0.0271	pCi/g	KSD1	09/11/06	1917	565250		6
Rad Liquid Scintillation Analysis													
<i>LSC, Tritium Dist, Solid-HTD2, ALL FSS</i>													
Tritium	U	3.33	+/-6.35	5.16	+/-6.35	10.9	pCi/g	DFA1	09/05/06	1123	564514		7
<i>Liquid Scint C14, Solid All, FSS</i>													
Carbon-14	U	0.00	+/-0.0818	0.0686	+/-0.0818	0.140	pCi/g	AXD2	09/06/06	0035	564520		8
<i>Liquid Scint Fe55, Solid-ALL FSS</i>													
Iron-55	U	0.852	+/-61.3	41.7	+/-61.3	86.4	pCi/g	MXP1	09/10/06	1419	565287		9
<i>Liquid Scint Tc99, Solid-ALL FSS</i>													
Technetium-99	U	0.341	+/-0.291	0.235	+/-0.291	0.485	pCi/g	KXR1	09/06/06	1232	564623		10

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	AXP2	09/01/06	1328	564525

The following Analytical Methods were performed

Method	Description
1	DOE EML HASL-300, Am-05-RC Modified
2	DOE EML HASL-300, Am-05-RC Modified

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: September 18, 2006

Client Sample ID: 9106-0011-018F Project: YANK01204
Sample ID: 170683001 Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
3		DOE EML HASL-300, Pu-11-RC Modified											
4		DOE EML HASL-300, Pu-11-RC Modified											
5		DOE EML HASL-300, Pu-11-RC Modified											
6		EPA 905.0 Modified											
7		EPA 906.0 Modified											
8		EPA EERF C-01 Modified											
9		DOE RESL Fe-1, Modified											
10		DOE EML HASL-300, Tc-02-RC Modified											

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
Americium-243	Alphaspec Am241, Cm, Solid ALL	89	(15%-125%)
Plutonium-242	Alphaspec Pu, Solid-ALL FSS	38	(15%-125%)
Carrier/Tracer Recovery	Liquid Scint Pu241, Solid-ALL FS	89	(25%-125%)
Carrier/Tracer Recovery	GFPC, Sr90, solid-ALL FSS	51	(25%-125%)
Carrier/Tracer Recovery	Liquid Scint Fe55, Solid-ALL FS	75	(15%-125%)
Carrier/Tracer Recovery	Liquid Scint Tc99, Solid-ALL FS	78	(15%-125%)

Notes:

The Qualifiers in this report are defined as follows :

- * A quality control analyte recovery is outside of specified acceptance criteria
- < Result is less than value reported
- > Result is greater than value reported
- A The TIC is a suspected aldol-condensation product
- B Target analyte was detected in the associated blank
- BD Results are either below the MDC or tracer recovery is low
- C Analyte has been confirmed by GC/MS analysis
- D Results are reported from a diluted aliquot of the sample
- H Analytical holding time was exceeded
- J Value is estimated
- N/A Spike recovery limits do not apply. Sample concentration exceeds spike concentration by 4X or more
- R Sample results are rejected
- U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
- UI Gamma Spectroscopy--Uncertain identification
- X Consult Case Narrative, Data Summary package, or Project Manager concerning this qualifier
- Y QC Samples were not spiked with this compound
- ^ RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL
- h Preparation or preservation holding time was exceeded

GENERAL ENGINEERING LABORATORIES, LLC
 2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
 Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
 Contact: Mr. Jack McCarthy
 Project: Soils PO# 002332

Report Date: September 18, 2006

Client Sample ID: 9106-0011-018F
 Sample ID: 170683001

Project: YANK01204
 Client ID: YANK001
 Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
-----------	-----------	--------	-------------	----	-----	-----	-------	----	---------	------	------	-------	-----

The above sample is reported on a dry weight basis.

GENERAL ENGINEERING LABORATORIES, LLC
2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: September 18, 2006

Client Sample ID: 9106-0012-005F
Sample ID: 170683002
Matrix: SE
Collect Date: 23-JUN-06
Receive Date: 07-JUL-06
Collector: Client
Moisture: 23.4%

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Alpha Spec Analysis													
<i>Alphaspec Am241, Cm, Solid ALL FSS</i>													
Americium-241	U	0.00725	+/-0.0262	0.0156	+/-0.0262	0.0644	pCi/g	TC1	09/14/06	0931	567705		1
Curium-242	U	0.00	+/-0.0343	0.00	+/-0.0343	0.0474	pCi/g						
Curium-243/244	U	-0.00297	+/-0.0249	0.0111	+/-0.025	0.0557	pCi/g						
<i>Alphaspec Pu, Solid-ALL FSS</i>													
Plutonium-238	U	0.0214	+/-0.203	0.159	+/-0.203	0.498	pCi/g	MXA	09/11/06	0919	565210		3
Plutonium-239/240	U	0.120	+/-0.237	0.134	+/-0.238	0.449	pCi/g	1					
<i>Liquid Scint Pu241, Solid-ALL FSS</i>													
Plutonium-241	U	-10	+/-8.47	7.55	+/-8.47	15.8	pCi/g	TC1	09/17/06	0230	567883		4
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid-ALL FSS</i>													
Strontium-90	U	-0.00415	+/-0.016	0.0141	+/-0.016	0.0332	pCi/g	KSD1	09/08/06	1803	565250		6
Rad Liquid Scintillation Analysis													
<i>LSC, Tritium Dist, Solid-HTD2,ALL FSS</i>													
Tritium	U	4.39	+/-5.57	4.46	+/-5.57	9.42	pCi/g	DFA1	09/05/06	1155	564514		7
<i>Liquid Scint C14, Solid All,FSS</i>													
Carbon-14	U	-0.0271	+/-0.0822	0.0694	+/-0.0822	0.141	pCi/g	AXD2	09/06/06	0253	564520		8
<i>Liquid Scint Fe55, Solid-ALL FSS</i>													
Iron-55	U	3.71	+/-50.4	34.5	+/-50.4	71.6	pCi/g	MXP1	09/10/06	1435	565287		9
<i>Liquid Scint Ni63, Solid-ALL FSS</i>													
Nickel-63	U	5.04	+/-7.63	6.28	+/-7.63	12.9	pCi/g	MXP1	09/08/06	0035	565289		10
<i>Liquid Scint Tc99, Solid-ALL FSS</i>													
Technetium-99	U	0.057	+/-0.270	0.225	+/-0.270	0.464	pCi/g	KXR1	09/06/06	1249	564623		11

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	AXP2	09/01/06	1328	564525

The following Analytical Methods were performed

Method	Description
1	DOE EML HASL-300, Am-05-RC Modified

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: September 18, 2006

Client Sample ID: 9106-0012-005F
Sample ID: 170683002

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
-----------	-----------	--------	-------------	----	-----	-----	-------	----	---------	------	------	-------	-----

Y QC Samples were not spiked with this compound
^ RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL
h Preparation or preservation holding time was exceeded
The above sample is reported on a dry weight basis.

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: September 18, 2006

Client Sample ID: 9106-0012-014F
Sample ID: 170683003
Matrix: SE
Collect Date: 21-JUN-06
Receive Date: 07-JUL-06
Collector: Client
Moisture: 24.1%

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Alpha Spec Analysis													
<i>Alphaspec Am241, Cm, Solid ALL FSS</i>													
Americium-241	U	0.012	+/-0.0233	0.00	+/-0.0234	0.032	pCi/g	TC1	09/14/06	0931	567705		1
Curium-242	U	-0.00814	+/-0.0351	0.0215	+/-0.0351	0.089	pCi/g						
Curium-243/244	U	-0.00571	+/-0.0246	0.0151	+/-0.0246	0.0624	pCi/g						
<i>Alphaspec Pu, Solid-ALL FSS</i>													
Plutonium-238	U	-0.00589	+/-0.322	0.272	+/-0.322	0.744	pCi/g	MXA	09/11/06	0919	565210		3
Plutonium-239/240	U	0.0588	+/-0.218	0.147	+/-0.218	0.494	pCi/g	1					
<i>Liquid Scint Pu241, Solid-ALL FSS</i>													
Plutonium-241	U	4.22	+/-11.5	9.47	+/-11.5	19.8	pCi/g	TC1	09/17/06	0246	567883		4
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid-ALL FSS</i>													
Strontium-90	U	0.0176	+/-0.0191	0.0133	+/-0.0191	0.0316	pCi/g	KSD1	09/08/06	1803	565250		6
Rad Liquid Scintillation Analysis													
<i>LSC, Tritium Dist, Solid-HTD2, ALL FSS</i>													
Tritium	U	1.38	+/-6.13	5.08	+/-6.13	10.7	pCi/g	DFA1	09/05/06	1226	564514		7
<i>Liquid Scint C14, Solid All, FSS</i>													
Carbon-14	U	0.00209	+/-0.0745	0.0625	+/-0.0745	0.127	pCi/g	AXD2	09/06/06	0501	564520		8
<i>Liquid Scint Fe55, Solid-ALL FSS</i>													
Iron-55	U	13.9	+/-36.7	24.3	+/-36.7	50.7	pCi/g	MXP1	09/07/06	2253	565287		9
<i>Liquid Scint Ni63, Solid-ALL FSS</i>													
Nickel-63	U	4.26	+/-8.20	6.78	+/-8.20	13.9	pCi/g	MXP1	09/08/06	0106	565289		10
<i>Liquid Scint Tc99, Solid-ALL FSS</i>													
Technetium-99	U	0.269	+/-0.281	0.228	+/-0.281	0.470	pCi/g	KXR1	09/06/06	1305	564623		11

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	AXP2	09/01/06	1328	564525

The following Analytical Methods were performed

Method	Description
1	DOE EML HASL-300, Am-05-RC Modified

GENERAL ENGINEERING LABORATORIES, LLC
 2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
 Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
 Contact: Mr. Jack McCarthy
 Project: Soils PO# 002332

Report Date: September 18, 2006

Client Sample ID: 9106-0012-014F
 Sample ID: 170683003

Project: YANK01204
 Client ID: YANK001
 Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
-----------	-----------	--------	-------------	----	-----	-----	-------	----	---------	------	------	-------	-----

Y QC Samples were not spiked with this compound
 ^ RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL
 h Preparation or preservation holding time was exceeded
 The above sample is reported on a dry weight basis.

GENERAL ENGINEERING LABORATORIES, LLC
2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: September 18, 2006

Client Sample ID: 9106-0013-006F
Sample ID: 170683004
Matrix: SE
Collect Date: 21-JUN-06
Receive Date: 21-JUL-06
Collector: Client

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Alpha Spec Analysis													
<i>Alphaspec Am241, Cm, Solid ALL FSS</i>													
Americium-241		0.187	+/-0.170	0.0339	+/-0.172	0.170	pCi/g		MXA	09/12/06	0844	565213	1
Curium-242	U	-0.0387	+/-0.0438	0.0836	+/-0.0442	0.313	pCi/g						
Curium-243/244	U	-0.00608	+/-0.118	0.102	+/-0.118	0.308	pCi/g						
<i>Alphaspec Pu, Solid- ALL FSS</i>													
Plutonium-238	U	-0.012	+/-0.0236	0.045	+/-0.0236	0.226	pCi/g		MXA	09/11/06	0919	565214	2
Plutonium-239/240	U	-0.0601	+/-0.0526	0.100	+/-0.0531	0.337	pCi/g						
<i>Liquid Scint Pu241, Solid- ALL FSS</i>													
Plutonium-241	U	16.2	+/-13.4	10.8	+/-13.5	22.3	pCi/g		MXA	09/12/06	2245	565216	3
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid- ALL FSS</i>													
Strontium-90	U	0.000813	+/-0.0187	0.0156	+/-0.0187	0.036	pCi/g		KSD1	09/08/06	1932	565253	4
Rad Liquid Scintillation Analysis													
<i>LSC, Tritium Dist, Solid-HTD2, ALL FSS</i>													
Tritium	U	0.997	+/-4.80	3.98	+/-4.80	8.39	pCi/g		DFA1	09/05/06	1847	564447	5
<i>Liquid Scint C14, Solid All, FSS</i>													
Carbon-14	U	-0.0199	+/-0.109	0.0921	+/-0.109	0.192	pCi/g		AXD2	09/06/06	0955	564449	6
<i>Liquid Scint Fe55, Solid- ALL FSS</i>													
Iron-55	U	33.7	+/-51.9	34.2	+/-52.0	71.2	pCi/g		MXP1	09/11/06	1150	565291	7
<i>Liquid Scint Ni63, Solid- ALL FSS</i>													
Nickel-63	U	0.395	+/-9.40	7.88	+/-9.40	16.2	pCi/g		MXP1	09/08/06	2220	565293	8
<i>Liquid Scint Tc99, Solid- ALL FSS</i>													
Technetium-99	U	-0.0409	+/-0.273	0.231	+/-0.273	0.475	pCi/g		KXR1	09/06/06	1637	564445	9

The following Analytical Methods were performed

Method	Description
1	DOE EML HASL-300, Am-05-RC Modified
2	DOE EML HASL-300, Pu-11-RC Modified
3	DOE EML HASL-300, Pu-11-RC Modified
4	EPA 905.0 Modified

GENERAL ENGINEERING LABORATORIES, LLC
 2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
 Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
 Contact: Mr. Jack McCarthy
 Project: Soils PO# 002332

Report Date: September 18, 2006

Client Sample ID: 9106-0013-006F Project: YANK01204
 Sample ID: 170683004 Client ID: YANK001
 Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
5	EPA 906.0 Modified												
6	EPA EERF C-01 Modified												
7	DOE RESL Fe-1, Modified												
8	DOE RESL Ni-1, Modified												
9	DOE EML HASL-300, Tc-02-RC Modified												

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
Americium-243	Alphaspec Am241, Cm, Solid ALL	86	(15%-125%)
Plutonium-242	Alphaspec Pu, Solid-ALL FSS	60	(15%-125%)
Carrier/Tracer Recovery	Liquid Scint Pu241, Solid-ALL FS	72	(25%-125%)
Carrier/Tracer Recovery	GFPC, Sr90, solid-ALL FSS	100	(25%-125%)
Carrier/Tracer Recovery	Liquid Scint Fe55, Solid-ALL FS	70	(15%-125%)
Carrier/Tracer Recovery	Liquid Scint Ni63, Solid-ALL FS	43	(25%-125%)
Carrier/Tracer Recovery	Liquid Scint Tc99, Solid-ALL FS	79	(15%-125%)

Notes:

The Qualifiers in this report are defined as follows :

- * A quality control analyte recovery is outside of specified acceptance criteria
 - < Result is less than value reported
 - > Result is greater than value reported
 - A The TIC is a suspected aldol-condensation product
 - B Target analyte was detected in the associated blank
 - BD Results are either below the MDC or tracer recovery is low
 - C Analyte has been confirmed by GC/MS analysis
 - D Results are reported from a diluted aliquot of the sample
 - H Analytical holding time was exceeded
 - J Value is estimated
 - N/A Spike recovery limits do not apply. Sample concentration exceeds spike concentration by 4X or more
 - R Sample results are rejected
 - U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
 - UI Gamma Spectroscopy--Uncertain identification
 - X Consult Case Narrative, Data Summary package, or Project Manager concerning this qualifier
 - Y QC Samples were not spiked with this compound
 - ^ RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL
 - h Preparation or preservation holding time was exceeded
- The above sample is reported on an "as received" basis.

GENERAL ENGINEERING LABORATORIES, LLC
2040 Savage Road Charleston SC 29407 – (843) 556-8171 – www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: September 18, 2006

Client Sample ID: 9106-0013-005F
Sample ID: 170683005
Matrix: SE
Collect Date: 21-JUN-06
Receive Date: 21-JUL-06
Collector: Client

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Alpha Spec Analysis													
<i>Alphaspec Am241, Cm, Solid ALL FSS</i>													
Americium-241		0.505	+/-0.295	0.0542	+/-0.304	0.224	pCi/g		MXA	09/12/06	0844	565213	1
Curium-242	U	0.00	+/-0.119	0.00	+/-0.119	0.165	pCi/g						
Curium-243/244	U	0.0327	+/-0.0868	0.0387	+/-0.0869	0.194	pCi/g						
<i>Alphaspec Pu, Solid-ALL FSS</i>													
Plutonium-238	U	-0.008	+/-0.0157	0.0299	+/-0.0157	0.150	pCi/g		MXA	09/11/06	0919	565214	2
Plutonium-239/240	U	-0.0399	+/-0.035	0.0668	+/-0.0352	0.224	pCi/g						
<i>Liquid Scint Pu241, Solid-ALL FSS</i>													
Plutonium-241	U	7.84	+/-13.5	11.1	+/-13.5	22.8	pCi/g		MXA	09/12/06	2332	565216	3
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid-ALL FSS</i>													
Strontium-90	U	-0.000759	+/-0.0157	0.0133	+/-0.0157	0.0313	pCi/g		KSD1	09/08/06	1932	565253	4
Rad Liquid Scintillation Analysis													
<i>LSC, Tritium Dist, Solid-HTD2, ALL FSS</i>													
Tritium	U	-0.175	+/-4.77	4.01	+/-4.77	8.45	pCi/g		DFA1	09/05/06	1919	564447	5
<i>Liquid Scint C14, Solid All, FSS</i>													
Carbon-14	U	-0.0246	+/-0.107	0.0905	+/-0.107	0.188	pCi/g		AXD2	09/06/06	1027	564449	6
<i>Liquid Scint Fe55, Solid-ALL FSS</i>													
Iron-55	U	8.33	+/-39.2	26.6	+/-39.2	55.3	pCi/g		MXP1	09/08/06	0121	565291	7
<i>Liquid Scint Ni63, Solid-ALL FSS</i>													
Nickel-63	U	-1.92	+/-5.36	4.55	+/-5.36	9.32	pCi/g		MXP1	09/08/06	2323	565293	8
<i>Liquid Scint Tc99, Solid-ALL FSS</i>													
Technetium-99	U	0.0807	+/-0.273	0.227	+/-0.273	0.468	pCi/g		KXR1	09/06/06	1654	564445	9

The following Analytical Methods were performed

Method	Description
1	DOE EML HASL-300, Am-05-RC Modified
2	DOE EML HASL-300, Pu-11-RC Modified
3	DOE EML HASL-300, Pu-11-RC Modified
4	EPA 905.0 Modified

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: September 18, 2006

Client Sample ID: 9106-0013-005F
Sample ID: 170683005

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time Batch	Mtd
5	EPA 906.0 Modified											
6	EPA EERF C-01 Modified											
7	DOE RESL Fe-1, Modified											
8	DOE RESL Ni-1, Modified											
9	DOE EML HASL-300, Tc-02-RC Modified											

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
Americium-243	Alphaspec Am241, Cm, Solid ALL	68	(15%-125%)
Plutonium-242	Alphaspec Pu, Solid-ALL FSS	86	(15%-125%)
Carrier/Tracer Recovery	Liquid Scint Pu241, Solid-ALL FS	71	(25%-125%)
Carrier/Tracer Recovery	GFPC, Sr90, solid-ALL FSS	101	(25%-125%)
Carrier/Tracer Recovery	Liquid Scint Fe55, Solid-ALL FS	71	(15%-125%)
Carrier/Tracer Recovery	Liquid Scint Ni63, Solid-ALL FS	72	(25%-125%)
Carrier/Tracer Recovery	Liquid Scint Tc99, Solid-ALL FS	80	(15%-125%)

Notes:

The Qualifiers in this report are defined as follows :

- * A quality control analyte recovery is outside of specified acceptance criteria
 - < Result is less than value reported
 - > Result is greater than value reported
 - A The TIC is a suspected aldol-condensation product
 - B Target analyte was detected in the associated blank
 - BD Results are either below the MDC or tracer recovery is low
 - C Analyte has been confirmed by GC/MS analysis
 - D Results are reported from a diluted aliquot of the sample
 - H Analytical holding time was exceeded
 - J Value is estimated
 - N/A Spike recovery limits do not apply. Sample concentration exceeds spike concentration by 4X or more
 - R Sample results are rejected
 - U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
 - UI Gamma Spectroscopy—Uncertain identification
 - X Consult Case Narrative, Data Summary package, or Project Manager concerning this qualifier
 - Y QC Samples were not spiked with this compound
 - ^ RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL
 - h Preparation or preservation holding time was exceeded
- The above sample is reported on an "as received" basis.

GENERAL ENGINEERING LABORATORIES, LLC
2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: September 18, 2006

Client Sample ID: 9106-0014-012F
Sample ID: 170683006
Matrix: SE
Collect Date: 06-JUN-06
Receive Date: 13-JUL-06
Collector: Client

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Alpha Spec Analysis													
<i>Alphaspec Am241, Cm, Solid ALL FSS</i>													
Americium-241		0.0945	+/-0.0698	0.0158	+/-0.0709	0.0654	pCi/g	TC1	09/14/06	0931	567705		1
Curium-242	U	0.0191	+/-0.0374	0.00	+/-0.0375	0.0517	pCi/g						
Curium-243/244	U	0.0473	+/-0.0497	0.0113	+/-0.050	0.0567	pCi/g						
<i>Alphaspec Pu, Solid-ALL FSS</i>													
Plutonium-238	U	-0.113	+/-0.329	0.328	+/-0.330	0.930	pCi/g	MXA	09/11/06	0919	565210		3
Plutonium-239/240	U	-0.097	+/-0.0951	0.181	+/-0.0963	0.637	pCi/g	1					
<i>Liquid Scint Pu241, Solid-ALL FSS</i>													
Plutonium-241	U	4.84	+/-11.6	9.54	+/-11.6	20.0	pCi/g	TC1	09/17/06	0302	567883		4
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid-ALL FSS</i>													
Strontium-90	U	-0.00246	+/-0.00901	0.00776	+/-0.00901	0.0169	pCi/g	KSD1	09/11/06	1917	565250		6
Rad Liquid Scintillation Analysis													
<i>LSC, Tritium Dist, Solid-HTD2, ALL FSS</i>													
Tritium	U	3.44	+/-6.25	5.07	+/-6.25	10.7	pCi/g	DFA1	09/05/06	1258	564514		7
<i>Liquid Scint C14, Solid All, FSS</i>													
Carbon-14	U	0.0486	+/-0.0773	0.064	+/-0.0773	0.130	pCi/g	AXD2	09/06/06	0635	564520		8
<i>Liquid Scint Fe55, Solid-ALL FSS</i>													
Iron-55	U	-12.6	+/-44.5	30.6	+/-44.5	63.6	pCi/g	MXP1	09/10/06	1451	565287		9
<i>Liquid Scint Ni63, Solid-ALL FSS</i>													
Nickel-63	U	4.82	+/-7.80	6.44	+/-7.80	13.2	pCi/g	MXP1	09/08/06	0138	565289		10
<i>Liquid Scint Tc99, Solid-ALL FSS</i>													
Technetium-99	U	0.0865	+/-0.281	0.234	+/-0.281	0.481	pCi/g	KXR1	09/06/06	1321	564623		11

The following Analytical Methods were performed

Method	Description
1	DOE EML HASL-300, Am-05-RC Modified
2	DOE EML HASL-300, Am-05-RC Modified
3	DOE EML HASL-300, Pu-11-RC Modified
4	DOE EML HASL-300, Pu-11-RC Modified
5	DOE EML HASL-300, Pu-11-RC Modified
6	EPA 905.0 Modified

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

Contact: East Hampton, Connecticut 06424
Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: September 18, 2006

Client Sample ID: 9106-0014-012F
Sample ID: 170683006

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time Batch	Mtd
7	EPA 906.0 Modified											
8	EPA EERF C-01 Modified											
9	DOE RESL Fe-1, Modified											
10	DOE RESL Ni-1, Modified											
11	DOE EML HASL-300, Tc-02-RC Modified											

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
Americium-243	Alphaspec Am241, Cm, Solid ALL	93	(15%-125%)
Plutonium-242	Alphaspec Pu, Solid-ALL FSS	33	(15%-125%)
Carrier/Tracer Recovery	Liquid Scint Pu241, Solid-ALL FS	84	(25%-125%)
Carrier/Tracer Recovery	GFPC, Sr90, solid-ALL FSS	91	(25%-125%)
Carrier/Tracer Recovery	Liquid Scint Fe55, Solid-ALL FS	74	(15%-125%)
Carrier/Tracer Recovery	Liquid Scint Ni63, Solid-ALL FS	80	(25%-125%)
Carrier/Tracer Recovery	Liquid Scint Tc99, Solid-ALL FS	79	(15%-125%)

Notes:

The Qualifiers in this report are defined as follows :

- * A quality control analyte recovery is outside of specified acceptance criteria
 - < Result is less than value reported
 - > Result is greater than value reported
 - A The TIC is a suspected aldol-condensation product
 - B Target analyte was detected in the associated blank
 - BD Results are either below the MDC or tracer recovery is low
 - C Analyte has been confirmed by GC/MS analysis
 - D Results are reported from a diluted aliquot of the sample
 - H Analytical holding time was exceeded
 - J Value is estimated
 - N/A Spike recovery limits do not apply. Sample concentration exceeds spike concentration by 4X or more
 - R Sample results are rejected
 - U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
 - UI Gamma Spectroscopy—Uncertain identification
 - X Consult Case Narrative, Data Summary package, or Project Manager concerning this qualifier
 - Y QC Samples were not spiked with this compound
 - ^ RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL
 - h Preparation or preservation holding time was exceeded
- The above sample is reported on an "as received" basis.

GENERAL ENGINEERING LABORATORIES, LLC
2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

Contact: East Hampton, Connecticut 06424
Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: September 18, 2006

Client Sample ID: 9106-0014-033F
Sample ID: 170683007
Matrix: SE
Collect Date: 14-JUN-06
Receive Date: 13-JUL-06
Collector: Client

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Alpha Spec Analysis													
<i>Alphaspec Am241, Cm, Solid ALL FSS</i>													
Americium-241		0.0906	+/-0.0692	0.0118	+/-0.0703	0.0594	pCi/g	TC1	09/14/06	0931	567705		1
Curium-242	U	0.0195	+/-0.0383	0.00	+/-0.0384	0.053	pCi/g						
Curium-243/244		0.0799	+/-0.0639	0.00	+/-0.0648	0.0361	pCi/g						
<i>Alphaspec Pu, Solid-ALL FSS</i>													
Plutonium-238	U	-0.0396	+/-0.254	0.229	+/-0.254	0.638	pCi/g	MXA	09/11/06	0919	565210		3
Plutonium-239/240	U	-0.203	+/-0.182	0.244	+/-0.184	0.666	pCi/g	1					
<i>Liquid Scint Pu241, Solid-ALL FSS</i>													
Plutonium-241	U	4.34	+/-11.1	9.14	+/-11.1	19.2	pCi/g	TC1	09/17/06	0319	567883		4
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid-ALL FSS</i>													
Strontium-90	U	0.00411	+/-0.0167	0.0133	+/-0.0167	0.0316	pCi/g	KSD1	09/08/06	1803	565250		6
Rad Liquid Scintillation Analysis													
<i>LSC, Tritium Dist, Solid-HTD2, ALL FSS</i>													
Tritium	U	3.13	+/-5.10	4.12	+/-5.10	8.71	pCi/g	DFA1	09/05/06	1330	564514		7
<i>Liquid Scint C14, Solid All, FSS</i>													
Carbon-14	U	0.0995	+/-0.0918	0.075	+/-0.0918	0.153	pCi/g	AXD2	09/06/06	0807	564520		8
<i>Liquid Scint Fe55, Solid-ALL FSS</i>													
Iron-55	U	19.3	+/-37.9	24.9	+/-37.9	51.8	pCi/g	MXP1	09/07/06	2326	565287		9
<i>Liquid Scint Ni63, Solid-ALL FSS</i>													
Nickel-63	U	4.62	+/-7.14	5.88	+/-7.14	12.1	pCi/g	MXP1	09/08/06	0209	565289		10
<i>Liquid Scint Tc99, Solid-ALL FSS</i>													
Technetium-99	U	0.00	+/-0.282	0.236	+/-0.282	0.487	pCi/g	KXR1	09/06/06	1338	564623		11

The following Analytical Methods were performed

Method	Description
1	DOE EML HASL-300, Am-05-RC Modified
2	DOE EML HASL-300, Am-05-RC Modified
3	DOE EML HASL-300, Pu-11-RC Modified
4	DOE EML HASL-300, Pu-11-RC Modified
5	DOE EML HASL-300, Pu-11-RC Modified
6	EPA 905.0 Modified

GENERAL ENGINEERING LABORATORIES, LLC
2040 Savage Road Charleston SC 29407 – (843) 556-8171 – www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: September 18, 2006

Client Sample ID: 9106-0015-018F
Sample ID: 170683008
Matrix: SE
Collect Date: 27-JUN-06
Receive Date: 21-JUL-06
Collector: Client

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Alpha Spec Analysis													
<i>Alphaspec Am241, Cm, Solid ALL FSS</i>													
Americium-241		0.193	+/-0.166	0.00	+/-0.168	0.101	pCi/g		MXA	09/12/06	0844	565213	1
Curium-242	U	0.0784	+/-0.147	0.0655	+/-0.147	0.271	pCi/g						
Curium-243/244	U	0.0942	+/-0.129	0.0474	+/-0.130	0.196	pCi/g						
<i>Alphaspec Pu, Solid- ALL FSS</i>													
Plutonium-238	U	0.0325	+/-0.0637	0.00	+/-0.0638	0.0881	pCi/g		MXA	09/11/06	0919	565214	2
Plutonium-239/240	U	0.0013	+/-0.0705	0.0582	+/-0.0705	0.204	pCi/g						
<i>Liquid Scint Pu241, Solid- ALL FSS</i>													
Plutonium-241	U	7.19	+/-12.0	9.91	+/-12.1	20.4	pCi/g		MXA	09/13/06	0019	565216	3
Rad Liquid Scintillation Analysis													
<i>LSC, Tritium Dist, Solid-HTD2, ALL FSS</i>													
Tritium	U	-0.686	+/-5.32	4.50	+/-5.32	9.48	pCi/g		DFA1	09/05/06	1950	564447	4
<i>Liquid Scint C14, Solid All, FSS</i>													
Carbon-14	U	0.0572	+/-0.114	0.0942	+/-0.114	0.193	pCi/g		AXD2	09/09/06	0331	564449	5
<i>Liquid Scint Fe55, Solid- ALL FSS</i>													
Iron-55	U	7.27	+/-37.9	25.6	+/-37.9	53.2	pCi/g		MXP1	09/08/06	0137	565291	6
<i>Liquid Scint Ni63, Solid- ALL FSS</i>													
Nickel-63	U	-2.39	+/-7.60	6.43	+/-7.60	13.2	pCi/g		MXP1	09/09/06	0025	565293	7
<i>Liquid Scint Tc99, Solid- ALL FSS</i>													
Technetium-99	U	0.132	+/-0.270	0.223	+/-0.270	0.460	pCi/g		KXR1	09/06/06	1710	564445	8

The following Analytical Methods were performed

Method	Description
1	DOE EML HASL-300, Am-05-RC Modified
2	DOE EML HASL-300, Pu-11-RC Modified
3	DOE EML HASL-300, Pu-11-RC Modified
4	EPA 906.0 Modified
5	EPA EERF C-01 Modified
6	DOE RESL Fe-1, Modified
7	DOE RESL Ni-1, Modified

GENERAL ENGINEERING LABORATORIES, LLC
2040 Savage Road Charleston SC 29407 – (843) 556-8171 – www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: September 18, 2006

Client Sample ID: 9106-0015-018F Project: YANK01204
Sample ID: 170683008 Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time Batch	Mtd
8		DOE EML HASL-300, Tc-02-RC Modified										

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
Americium-243	Alphaspec Am241, Cm, Solid ALL	78	(15%-125%)
Plutonium-242	Alphaspec Pu, Solid-ALL FSS	86	(15%-125%)
Carrier/Tracer Recovery	Liquid Scint Pu241, Solid-ALL FS	79	(25%-125%)
Carrier/Tracer Recovery	Liquid Scint Fe55, Solid-ALL FS	79	(15%-125%)
Carrier/Tracer Recovery	Liquid Scint Ni63, Solid-ALL FS	47	(25%-125%)
Carrier/Tracer Recovery	Liquid Scint Tc99, Solid-ALL FS	82	(15%-125%)

Notes:

The Qualifiers in this report are defined as follows :

- * A quality control analyte recovery is outside of specified acceptance criteria
 - < Result is less than value reported
 - > Result is greater than value reported
 - A The TIC is a suspected aldol-condensation product
 - B Target analyte was detected in the associated blank
 - BD Results are either below the MDC or tracer recovery is low
 - C Analyte has been confirmed by GC/MS analysis
 - D Results are reported from a diluted aliquot of the sample
 - H Analytical holding time was exceeded
 - J Value is estimated
 - N/A Spike recovery limits do not apply. Sample concentration exceeds spike concentration by 4X or more
 - R Sample results are rejected
 - U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
 - UI Gamma Spectroscopy--Uncertain identification
 - X Consult Case Narrative, Data Summary package, or Project Manager concerning this qualifier
 - Y QC Samples were not spiked with this compound
 - ^ RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL
 - h Preparation or preservation holding time was exceeded
- The above sample is reported on an "as received" basis.

GENERAL ENGINEERING LABORATORIES, LLC
2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: September 18, 2006

Client Sample ID: 9106-0015-002F
Sample ID: 170683009
Matrix: SE
Collect Date: 28-JUN-06
Receive Date: 21-JUL-06
Collector: Client

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Alpha Spec Analysis													
<i>Alphaspec Am241, Cm, Solid ALL FSS</i>													
Americium-241		0.292	+/-0.213	0.0479	+/-0.217	0.198	pCi/g		MXA	09/12/06	0844	565213	1
Curium-242	U	0.0522	+/-0.102	0.00	+/-0.103	0.141	pCi/g						
Curium-243/244	U	0.0289	+/-0.0766	0.0341	+/-0.0767	0.171	pCi/g						
<i>Alphaspec Pu, Solid-ALL FSS</i>													
Plutonium-238	U	-0.0352	+/-0.0798	0.0658	+/-0.0798	0.231	pCi/g		MXA	09/11/06	0919	565214	2
Plutonium-239/240	U	0.019	+/-0.0758	0.0465	+/-0.0758	0.192	pCi/g						
<i>Liquid Scint Pu241, Solid-ALL FSS</i>													
Plutonium-241	U	24.6	+/-16.2	13.0	+/-16.5	26.7	pCi/g		MXA	09/13/06	0106	565216	3
Rad Liquid Scintillation Analysis													
<i>LSC, Tritium Dist, Solid-HTD2, ALL FSS</i>													
Tritium	U	-1.6	+/-7.22	6.13	+/-7.22	12.9	pCi/g		DFA1	09/05/06	2022	564447	4
<i>Liquid Scint C14, Solid All, FSS</i>													
Carbon-14		0.207	+/-0.113	0.0898	+/-0.113	0.185	pCi/g		AXD2	09/09/06	0418	564449	5
<i>Liquid Scint Fe55, Solid-ALL FSS</i>													
Iron-55	U	10.8	+/-47.1	31.3	+/-47.1	65.2	pCi/g		MXP1	09/11/06	1206	565291	6
<i>Liquid Scint Ni63, Solid-ALL FSS</i>													
Nickel-63	U	-3.07	+/-6.78	5.76	+/-6.78	11.8	pCi/g		MXP1	09/09/06	0127	565293	7
<i>Liquid Scint Tc99, Solid-ALL FSS</i>													
Technetium-99	U	0.390	+/-0.283	0.227	+/-0.283	0.468	pCi/g		KXR1	09/06/06	1726	564445	8

The following Analytical Methods were performed

Method	Description
1	DOE EML HASL-300, Am-05-RC Modified
2	DOE EML HASL-300, Pu-11-RC Modified
3	DOE EML HASL-300, Pu-11-RC Modified
4	EPA 906.0 Modified
5	EPA EERF C-01 Modified
6	DOE RESL Fe-1, Modified
7	DOE RESL Ni-1, Modified

GENERAL ENGINEERING LABORATORIES, LLC
2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
Contact: Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: September 18, 2006

Client Sample ID: 9106-0001-132F
Sample ID: 170683010
Matrix: SE
Collect Date: 07-AUG-06
Receive Date: 17-AUG-06
Collector: Client
Moisture: 23.8%

Project: YANK01204
Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
Rad Alpha Spec Analysis													
<i>Alphaspec Am241, Cm, Solid ALL FSS</i>													
Americium-241		0.160	+/-0.147	0.0296	+/-0.148	0.148	pCi/g		MXA	09/12/06	0844	565213	1
Curium-242	U	0.00	+/-0.0754	0.00	+/-0.0754	0.104	pCi/g						
Curium-243/244		0.132	+/-0.130	0.00	+/-0.131	0.0896	pCi/g						
<i>Alphaspec Pu, Solid- ALL FSS</i>													
Plutonium-238	U	-0.0279	+/-0.0954	0.0976	+/-0.0955	0.306	pCi/g		MXA	09/11/06	0919	565214	2
Plutonium-239/240	U	-0.0591	+/-0.0934	0.0903	+/-0.0934	0.292	pCi/g						
<i>Liquid Scint Pu241, Solid-ALL FSS</i>													
Plutonium-241	U	14.0	+/-14.7	12.0	+/-14.8	24.6	pCi/g		MXA	09/13/06	0153	565216	3
Rad Gas Flow Proportional Counting													
<i>GFPC, Sr90, solid-ALL FSS</i>													
Strontium-90	U	0.00619	+/-0.0168	0.0131	+/-0.0168	0.0311	pCi/g		KSD1	09/08/06	1932	565253	4
Rad Liquid Scintillation Analysis													
<i>LSC, Tritium Dist, Solid-HTD2, ALL FSS</i>													
Tritium	U	4.94	+/-7.02	5.55	+/-7.02	12.0	pCi/g		ATH2	09/07/06	0102	565650	5
<i>Liquid Scint C14, Solid All, FSS</i>													
Carbon-14		0.324	+/-0.115	0.0889	+/-0.115	0.183	pCi/g		AXD2	09/08/06	0456	565649	6
<i>Liquid Scint Fe55, Solid-ALL FSS</i>													
Iron-55	U	-1.92	+/-38.0	25.9	+/-38.0	53.9	pCi/g		MXP1	09/08/06	0210	565291	7
<i>Liquid Scint Ni63, Solid-ALL FSS</i>													
Nickel-63	U	0.735	+/-5.83	4.88	+/-5.83	10.0	pCi/g		MXP1	09/09/06	0229	565293	8
<i>Liquid Scint Tc99, Solid-ALL FSS</i>													
Technetium-99	U	0.0126	+/-0.193	0.161	+/-0.193	0.330	pCi/g		KXR1	09/12/06	1349	565648	9

The following Prep Methods were performed

Method	Description	Analyst	Date	Time	Prep Batch
Dry Soil Prep	Dry Soil Prep GL-RAD-A-021	JMB1	09/05/06	1736	565454

The following Analytical Methods were performed

Method	Description
--------	-------------

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
Address : 362 Injun Hollow Rd

Contact: East Hampton, Connecticut 06424
Mr. Jack McCarthy
Project: Soils PO# 002332

Report Date: September 18, 2006

Client Sample ID: 9106-0001-132F Project: YANK01204
Sample ID: 170683010 Client ID: YANK001
Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
1		DOE EML HASL-300, Am-05-RC Modified											
2		DOE EML HASL-300, Pu-11-RC Modified											
3		DOE EML HASL-300, Pu-11-RC Modified											
4		EPA 905.0 Modified											
5		EPA 906.0 Modified											
6		EPA EERF C-01 Modified											
7		DOE RESL Fe-1, Modified											
8		DOE RESL Ni-1, Modified											
9		DOE EML HASL-300, Tc-02-RC Modified											

Surrogate/Tracer recovery	Test	Recovery%	Acceptable Limits
Americium-243	Alphaspec Am241, Cm, Solid ALL	87	(15%-125%)
Plutonium-242	Alphaspec Pu, Solid-ALL FSS	66	(15%-125%)
Carrier/Tracer Recovery	Liquid Scint Pu241, Solid-ALL FS	66	(25%-125%)
Carrier/Tracer Recovery	GFPC, Sr90, solid-ALL FSS	100	(25%-125%)
Carrier/Tracer Recovery	Liquid Scint Fe55, Solid-ALL FS	76	(15%-125%)
Carrier/Tracer Recovery	Liquid Scint Ni63, Solid-ALL FS	72	(25%-125%)
Carrier/Tracer Recovery	Liquid Scint Tc99, Solid-ALL FS	72	(15%-125%)

Notes:

The Qualifiers in this report are defined as follows :

- * A quality control analyte recovery is outside of specified acceptance criteria
- < Result is less than value reported
- > Result is greater than value reported
- A The TIC is a suspected aldol-condensation product
- B Target analyte was detected in the associated blank
- BD Results are either below the MDC or tracer recovery is low
- C Analyte has been confirmed by GC/MS analysis
- D Results are reported from a diluted aliquot of the sample
- H Analytical holding time was exceeded
- J Value is estimated
- N/A Spike recovery limits do not apply. Sample concentration exceeds spike concentration by 4X or more
- R Sample results are rejected
- U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
- UI Gamma Spectroscopy--Uncertain identification
- X Consult Case Narrative, Data Summary package, or Project Manager concerning this qualifier
- Y QC Samples were not spiked with this compound

GENERAL ENGINEERING LABORATORIES, LLC
 2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

Certificate of Analysis

Company : Connecticut Yankee Atomic Power
 Address : 362 Injun Hollow Rd

East Hampton, Connecticut 06424
 Contact: Mr. Jack McCarthy
 Project: Soils PO# 002332

Report Date: September 18, 2006

Client Sample ID: 9106-0001-132F
 Sample ID: 170683010

Project: YANK01204
 Client ID: YANK001
 Vol. Recv.:

Parameter	Qualifier	Result	Uncertainty	LC	TPU	MDA	Units	DF	Analyst	Date	Time	Batch	Mtd
-----------	-----------	--------	-------------	----	-----	-----	-------	----	---------	------	------	-------	-----

^ RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL
 h Preparation or preservation holding time was exceeded
 The above sample is reported on a dry weight basis.

QUALITY CONTROL DATA

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

QC Summary

Report Date: September 18, 2006

Page 1 of 10

Client : Connecticut Yankee Atomic Power
362 Injun Hollow Rd

Contact: East Hampton, Connecticut
Mr. Jack McCarthy

Workorder: 170683

Parname	NOM	Sample	Qual	QC	Units	RPD%	REC%	Range	Anlst	Date	Time
Rad Alpha Spec											
Batch	565210										
QC1201175592	170683001	DUP									
Plutonium-238	U	-0.148	U	0.137	pCi/g	5180		(0% - 100%)	AXA1	09/11/06	09:19
	Uncert:	+/-0.269		+/-0.303							
	TPU:	+/-0.270		+/-0.304							
Plutonium-239/240	U	0.00321	U	-0.215	pCi/g	206		(0% - 100%)			
	Uncert:	+/-0.174		+/-0.181							
	TPU:	+/-0.174		+/-0.183							
QC1201175594	LCS										
Plutonium-238			U	-0.0564	pCi/g			(75%-125%)			
	Uncert:			+/-0.446							
	TPU:			+/-0.446							
Plutonium-239/240	12.3			9.42	pCi/g		77	(75%-125%)			
	Uncert:			+/-1.98							
	TPU:			+/-2.49							
QC1201175591	MB										
Plutonium-238			U	0.117	pCi/g						
	Uncert:			+/-0.220							
	TPU:			+/-0.221							
Plutonium-239/240			U	0.0802	pCi/g						
	Uncert:			+/-0.226							
	TPU:			+/-0.226							
QC1201175593	170683001	MS									
Plutonium-238	U	-0.148	U	0.110	pCi/g			(75%-125%)			
	Uncert:	+/-0.269		+/-0.175							
	TPU:	+/-0.270		+/-0.176							
Plutonium-239/240	12.5	U	0.00321	11.8	pCi/g		94	(75%-125%)			
	Uncert:	+/-0.174		+/-1.70							
	TPU:	+/-0.174		+/-2.29							
Batch	565213										
QC1201175603	170683004	DUP									
Americium-241		0.187		0.163	pCi/g	14		(0% - 100%)	AXA1	09/12/06	08:44
	Uncert:	+/-0.170		+/-0.149							
	TPU:	+/-0.172		+/-0.151							
Curium-242	U	-0.0387		0.143	pCi/g	348		(0% - 100%)			
	Uncert:	+/-0.0438		+/-0.162							
	TPU:	+/-0.0442		+/-0.163							
Curium-243/244	U	-0.00608	U	-0.0487	pCi/g	156		(0% - 100%)			
	Uncert:	+/-0.118		+/-0.0768							
	TPU:	+/-0.118		+/-0.0769							
QC1201175605	LCS										
Americium-241	13.5			12.8	pCi/g		95	(75%-125%)			
	Uncert:			+/-1.24							
	TPU:			+/-2.12							

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

QC Summary

Workorder: 170683

Page 2 of 10

Parmname	NOM	Sample	Qual	QC	Units	RPD%	REC%	Range	Anlst	Date	Time
Rad Alpha Spec											
Batch	565213										
Curium-242			U	0.00	pCi/g						
				Uncert: +/-0.0625							
				TPU: +/-0.0625							
Curium-243/244	16.4			15.1	pCi/g		92	(75%-125%)			
				Uncert: +/-1.35							
				TPU: +/-2.44							
QC1201175602 MB											
Americium-241			U	0.0812	pCi/g					09/12/06	08:44
				Uncert: +/-0.107							
				TPU: +/-0.108							
Curium-242			U	0.0664	pCi/g						
				Uncert: +/-0.106							
				TPU: +/-0.107							
Curium-243/244			U	-0.00886	pCi/g						
				Uncert: +/-0.0744							
				TPU: +/-0.0745							
QC1201175604 170683004 MS											
Americium-241	13.7	0.187		14.1	pCi/g		102	(75%-125%)		09/12/06	08:44
				Uncert: +/-0.170							
				TPU: +/-0.172							
Curium-242			U	-0.0387	pCi/g						
				Uncert: +/-0.0438							
				TPU: +/-0.0442							
Curium-243/244	16.7		U	-0.00608	pCi/g		97	(75%-125%)			
				Uncert: +/-0.118							
				TPU: +/-0.118							
Batch	565214										
QC1201175607 170683004 DUP											
Plutonium-238			U	-0.012	pCi/g	110		(0% - 100%)	4XA1	09/11/06	09:19
				Uncert: +/-0.0236							
				TPU: +/-0.0236							
Plutonium-239/240			U	-0.0601	pCi/g	64		(0% - 100%)			
				Uncert: +/-0.0526							
				TPU: +/-0.0531							
QC1201175609 LCS											
Plutonium-238			U	0.00142	pCi/g			(75%-125%)			
				Uncert: +/-0.0772							
				TPU: +/-0.0772							
Plutonium-239/240	12.5			10.7	pCi/g		86	(75%-125%)			
				Uncert: +/-1.21							
				TPU: +/-1.66							
QC1201175606 MB											
Plutonium-238			U	-0.0382	pCi/g						
				Uncert: +/-0.113							
				TPU: +/-0.113							
Plutonium-239/240			U	-0.0891	pCi/g						
				Uncert: +/-0.066							
				TPU: +/-0.0669							
QC1201175608 170683004 MS											

GENERAL ENGINEERING LABORATORIES, LLC
 2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

QC Summary

Workorder: 170683

Page 3 of 10

Parmname	NOM	Sample	Qual	QC	Units	RPD%	REC%	Range	Anlst	Date	Time
Rad Alpha Spec											
Batch	565214										
Plutonium-238	U	-0.012	U	0.0632	pCi/g			(75%-125%)			
		Uncert: +/-0.0236		+/-0.143							
		TPU: +/-0.0236		+/-0.143							
Plutonium-239/240	12.6 U	-0.0601		10.9	pCi/g		87	(75%-125%)			
		Uncert: +/-0.0526		+/-1.20							
		TPU: +/-0.0531		+/-1.66							
Batch	565216										
QC1201175615	170683004 DUP										
Plutonium-241	U	16.2	U	5.89	pCi/g	0		(0% - 100%)	AXA1	09/13/06	03:26
		Uncert: +/-13.4		+/-12.7							
		TPU: +/-13.5		+/-12.7							
QC1201175617	LCS										
Plutonium-241	341			310	pCi/g		91	(75%-125%)		09/12/06	11:26
		Uncert: +/-32.9		+/-45.2							
		TPU: +/-45.2									
QC1201175614	MB										
Plutonium-241			U	5.70	pCi/g					09/13/06	02:39
		Uncert: +/-12.7		+/-12.7							
		TPU: +/-12.7									
QC1201175616	170683004 MS										
Plutonium-241	344 U	16.2		341	pCi/g		99	(75%-125%)		09/12/06	11:10
		Uncert: +/-13.4		+/-51.8							
		TPU: +/-13.5		+/-66.7							
Batch	567705										
QC1201181288	170683003 DUP										
Americium-241	U	0.012		0.120	pCi/g	164		(0% - 100%)	TC1	09/14/06	09:31
		Uncert: +/-0.0233		+/-0.0804							
		TPU: +/-0.0234		+/-0.082							
Curium-242	U	-0.00814	U	0.00	pCi/g	200		(0% - 100%)			
		Uncert: +/-0.0351		+/-0.0381							
		TPU: +/-0.0351		+/-0.0381							
Curium-243/244	U	-0.00571	U	-0.0196	pCi/g	110		(0% - 100%)			
		Uncert: +/-0.0246		+/-0.031							
		TPU: +/-0.0246		+/-0.031							
QC1201181290	LCS										
Americium-241	5.23			5.41	pCi/g		103	(75%-125%)			
		Uncert: +/-0.508		+/-0.878							
		TPU: +/-0.878									
Curium-242			U	0.00	pCi/g						
		Uncert: +/-0.0244		+/-0.0244							
		TPU: +/-0.0244									
Curium-243/244	6.31			6.40	pCi/g		101	(75%-125%)			
		Uncert: +/-0.553		+/-1.01							
		TPU: +/-1.01									
QC1201181287	MB										
Americium-241			U	0.00039	pCi/g					09/14/06	09:31
		Uncert: +/-0.00421		+/-0.00421							
		TPU: +/-0.00421		+/-0.00421							

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

QC Summary

Workorder: 170683

Page 4 of 10

Parmname	NOM	Sample Qual	QC	Units	RPD%	REC%	Range	Anlst	Date Time
Rad Alpha Spec									
Batch	567705								
Curium-242		U	0.00902	pCi/g					
	Uncert:		+/-0.0239						
	TPU:		+/-0.0239						
Curium-243/244		U	-0.00283	pCi/g					
	Uncert:		+/-0.0238						
	TPU:		+/-0.0238						
QC1201181289 170683003 MS									
Americium-241	5.27	U	0.012	5.58	pCi/g	106	(75%-125%)		09/14/06 09:31
	Uncert:		+/-0.0233	+/-0.524					
	TPU:		+/-0.0234	+/-0.908					
Curium-242		U	-0.00814	0.0183	pCi/g				
	Uncert:		+/-0.0351	+/-0.0359					
	TPU:		+/-0.0351	+/-0.036					
Curium-243/244	6.41	U	-0.00571	7.36	pCi/g	115	(75%-125%)		
	Uncert:		+/-0.0246	+/-0.603					
	TPU:		+/-0.0246	+/-1.15					
Batch	567883								
QC1201181752 170683001 DUP									
Plutonium-241		U	9.87	-3.06	pCi/g	0	(0% - 100%)	TC1	09/17/06 03:51
	Uncert:		+/-11.1	+/-10.4					
	TPU:		+/-11.1	+/-10.4					
QC1201181754 LCS									
Plutonium-241	135			120	pCi/g	89	(75%-125%)		09/17/06 04:24
	Uncert:			+/-16.2					
	TPU:			+/-19.8					
QC1201181751 MB									
Plutonium-241				1.78	pCi/g				09/17/06 03:35
	Uncert:			+/-9.61					
	TPU:			+/-9.61					
QC1201181753 170683001 MS									
Plutonium-241	142	U	9.87	113	pCi/g	80	(75%-125%)		09/17/06 04:08
	Uncert:		+/-11.1	+/-15.8					
	TPU:		+/-11.1	+/-19.1					
Rad Gas Flow									
Batch	565250								
QC1201175680 170683002 DUP									
Strontium-90		U	-0.00415	0.000131	pCi/g	0	(0% - 100%)	KSD1	09/08/06 18:03
	Uncert:		+/-0.016	+/-0.0253					
	TPU:		+/-0.016	+/-0.0253					
QC1201175682 LCS									
Strontium-90	1.56			1.63	pCi/g	105	(75%-125%)		09/08/06 18:05
	Uncert:			+/-0.151					
	TPU:			+/-0.155					
QC1201175679 MB									
Strontium-90				-0.00458	pCi/g				09/08/06 18:03
	Uncert:			+/-0.018					
	TPU:			+/-0.018					
QC1201175681 170683002 MS									
Strontium-90	3.13	U	-0.00415	2.38	pCi/g	76	(75%-125%)		09/08/06 18:03

GENERAL ENGINEERING LABORATORIES, LLC
 2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

QC Summary

Workorder: 170683

Page 5 of 10

Parmname	NOM	Sample	Qual	QC	Units	RPD%	REC%	Range	Anlst	Date	Time
Rad Gas Flow											
Batch	565250										
		Uncert:	+/-0.016	+/-0.249							
		TPU:	+/-0.016	+/-0.253							
Batch	565253										
QC1201175687	170683005	DUP									
Strontium-90		U	-0.000759	U	-0.000963	pCi/g	0	(0% - 100%)	KSD1	09/08/06	19:32
		Uncert:	+/-0.0157	+/-0.0166							
		TPU:	+/-0.0157	+/-0.0166							
QC1201175689	LCS										
Strontium-90			1.57		1.20	pCi/g		77 (75%-125%)		09/09/06	12:26
		Uncert:			+/-0.113						
		TPU:			+/-0.118						
QC1201175686	MB										
Strontium-90				U	-0.0216	pCi/g				09/08/06	19:32
		Uncert:			+/-0.00992						
		TPU:			+/-0.00992						
QC1201175688	170683005	MS									
Strontium-90			3.14	U	-0.000759	pCi/g		88 (75%-125%)		09/08/06	19:31
		Uncert:			+/-0.0157						
		TPU:			+/-0.0157						
Rad Liquid Scintillation											
Batch	564445										
QC1201173841	170544018	DUP									
Technetium-99		U	0.128	U	0.0496	pCi/g	0	(0% - 100%)	KXR1	09/06/06	17:59
		Uncert:	+/-0.272	+/-0.251							
		TPU:	+/-0.272	+/-0.251							
QC1201173843	LCS										
Technetium-99			12.7		13.0	pCi/g		103 (75%-125%)		09/06/06	18:32
		Uncert:			+/-0.501						
		TPU:			+/-0.582						
QC1201173840	MB										
Technetium-99				U	0.0991	pCi/g				09/06/06	17:43
		Uncert:			+/-0.243						
		TPU:			+/-0.243						
QC1201173842	170544018	MS									
Technetium-99			13.1	U	0.128	pCi/g		102 (75%-125%)		09/06/06	18:15
		Uncert:			+/-0.272						
		TPU:			+/-0.272						
Batch	564447										
QC1201173845	170544018	DUP									
Tritium		U	1.53	U	0.760	pCi/g	0	(0% - 100%)	DFA1	09/05/06	21:25
		Uncert:	+/-6.54	+/-5.24							
		TPU:	+/-6.54	+/-5.24							
QC1201173847	LCS										
Tritium			46.9		44.3	pCi/g		95 (75%-125%)		09/07/06	11:21
		Uncert:			+/-8.94						
		TPU:			+/-8.98						
QC1201173844	MB										
Tritium				U	-0.43	pCi/g				09/05/06	20:54

GENERAL ENGINEERING LABORATORIES, LLC
 2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

QC Summary

Workorder: 170683

Page 6 of 10

Parname	NOM	Sample	Qual	QC	Units	RPD%	REC%	Range	Anlst	Date	Time
Rad Liquid Scintillation											
Batch	564447										
QC1201173846	170544018	MS									
Tritium	54.5	U	1.53	57.4	pCi/g		105	(75%-125%)		09/07/06	11:05
	Uncert:			+/-4.67							
	TPU:			+/-4.67							
Batch	564449										
QC1201173849	170544019	DUP									
Carbon-14		U	-0.0997	U -0.0804	pCi/g	0		(0% - 100%)	AXD2	09/09/06	05:04
	Uncert:		+/-0.0966	+/-0.108							
	TPU:		+/-0.0966	+/-0.108							
QC1201173851	LCS										
Carbon-14	6.66			6.26	pCi/g		94	(75%-125%)		09/06/06	13:38
	Uncert:			+/-0.258							
	TPU:			+/-0.276							
QC1201173848	MB										
Carbon-14				U -0.0326	pCi/g					09/06/06	12:02
	Uncert:			+/-0.102							
	TPU:			+/-0.102							
QC1201173850	170544019	MS									
Carbon-14	6.86	U	-0.0997	6.85	pCi/g		100	(75%-125%)		09/06/06	13:07
	Uncert:		+/-0.0966	+/-0.273							
	TPU:		+/-0.0966	+/-0.293							
Batch	564514										
QC1201174039	170683006	DUP									
Tritium		U	3.44	U 1.46	pCi/g	0		(0% - 100%)	DFA1	09/05/06	14:33
	Uncert:		+/-6.25	+/-5.79							
	TPU:		+/-6.25	+/-5.79							
QC1201174041	LCS										
Tritium	48.4			53.7	pCi/g		111	(75%-125%)		09/05/06	15:36
	Uncert:			+/-7.25							
	TPU:			+/-7.31							
QC1201174038	MB										
Tritium				U 0.308	pCi/g					09/05/06	14:01
	Uncert:			+/-4.66							
	TPU:			+/-4.66							
QC1201174040	170683006	MS									
Tritium	49.1	U	3.44	61.1	pCi/g		124	(75%-125%)		09/05/06	15:05
	Uncert:		+/-6.25	+/-7.58							
	TPU:		+/-6.25	+/-7.65							
Batch	564520										
QC1201174057	170683007	DUP									
Carbon-14		U	0.0995	U 0.0741	pCi/g	0		(0% - 100%)	AXD2	09/06/06	10:24
	Uncert:		+/-0.0918	+/-0.118							
	TPU:		+/-0.0918	+/-0.118							
QC1201174059	LCS										
Carbon-14	6.58			6.51	pCi/g		99	(75%-125%)		09/06/06	11:28
	Uncert:			+/-0.263							
	TPU:			+/-0.282							

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

QC Summary

Workorder: 170683

Page 7 of 10

Parmname	NOM	Sample	Qual	QC	Units	RPD%	REC%	Range	Anlst	Date	Time
Rad Liquid Scintillation											
Batch	564520										
QC1201174056	MB										
Carbon-14			U	-0.0231	pCi/g					09/06/06	09:53
				Uncert: +/-0.105							
				TPU: +/-0.105							
QC1201174058	170683007	MS									
Carbon-14		7.19	U	0.0995	6.42	pCi/g	89	(75%-125%)		09/06/06	10:56
				Uncert: +/-0.0918	+/-0.276						
				TPU: +/-0.0918	+/-0.293						
Batch	564623										
QC1201174254	170683001	DUP									
Technetium-99			U	0.341	U	0.187	pCi/g	0	(0% - 100%)	KXR1	09/08/06 19:42
				Uncert: +/-0.291	+/-0.211						
				TPU: +/-0.291	+/-0.211						
QC1201174256	LCS										
Technetium-99		13.0			12.2	pCi/g	94	(75%-125%)		09/06/06	14:43
				Uncert: +/-0.490							
				TPU: +/-0.566							
QC1201174253	MB										
Technetium-99			U	0.151	pCi/g					09/06/06	13:54
				Uncert: +/-0.247							
				TPU: +/-0.247							
QC1201174255	170683001	MS									
Technetium-99		13.0	U	0.341	12.9	pCi/g	99	(75%-125%)		09/06/06	14:27
				Uncert: +/-0.291	+/-0.547						
				TPU: +/-0.291	+/-0.623						
Batch	565287										
QC1201175809	170683006	DUP									
Iron-55			U	-12.6	U	38.3	pCi/g	0	(0% - 100%)	MXP1	09/07/06 23:59
				Uncert: +/-44.5	+/-41.2						
				TPU: +/-44.5	+/-41.2						
QC1201175811	LCS										
Iron-55		628			613	pCi/g	98	(75%-125%)		09/08/06	00:31
				Uncert: +/-56.2							
				TPU: +/-67.5							
QC1201175808	MB										
Iron-55			U	10.2	pCi/g					09/07/06	23:42
				Uncert: +/-35.9							
				TPU: +/-35.9							
QC1201175810	170683006	MS									
Iron-55		746	U	-12.6	675	pCi/g	91	(75%-125%)		09/10/06	15:07
				Uncert: +/-44.5	+/-60.5						
				TPU: +/-44.5	+/-73.4						
Batch	565289										
QC1201175815	170683006	DUP									
Nickel-63			U	4.82	U	6.11	pCi/g	0	(0% - 100%)	MXP1	09/08/06 03:13
				Uncert: +/-7.80	+/-9.03						
				TPU: +/-7.80	+/-9.03						
QC1201175817	LCS										
Nickel-63		512			443	pCi/g	87	(75%-125%)		09/08/06	04:16

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

QC Summary

Workorder: 170683

Page 8 of 10

Parmname	NOM	Sample	Qual	QC	Units	RPD%	REC%	Range	Anlst	Date	Time
Rad Liquid Scintillation											
Batch	565289										
QC1201175814	MB										
Nickel-63			U	5.67	pCi/g					09/08/06	02:41
				Uncert: +/-15.2							
				TPU: +/-20.8							
QC1201175816	170683006	MS									
Nickel-63		572	U	4.82	pCi/g		83	(75%-125%)		09/08/06	03:44
				Uncert: +/-7.44							
				TPU: +/-7.44							
Batch	565291										
QC1201175819	170683004	DUP									
Iron-55			U	33.7	pCi/g	0		(0% - 100%)	MXP1	09/08/06	02:42
				Uncert: +/-51.9							
				TPU: +/-52.0							
QC1201175821	LCS										
Iron-55		628		652	pCi/g		104	(75%-125%)		09/08/06	03:15
				Uncert: +/-52.2							
				TPU: +/-64.9							
QC1201175818	MB										
Iron-55			U	-26.7	pCi/g					09/08/06	02:26
				Uncert: +/-35.6							
				TPU: +/-35.6							
QC1201175820	170683004	MS									
Iron-55		711	U	33.7	pCi/g		105	(75%-125%)		09/08/06	02:59
				Uncert: +/-51.9							
				TPU: +/-52.0							
Batch	565293										
QC1201175823	170683004	DUP									
Nickel-63			U	0.395	pCi/g	0		(0% - 100%)	MXP1	09/09/06	04:34
				Uncert: +/-9.40							
				TPU: +/-9.40							
QC1201175825	LCS										
Nickel-63		512		467	pCi/g		91	(75%-125%)		09/09/06	06:38
				Uncert: +/-15.4							
				TPU: +/-21.5							
QC1201175822	MB										
Nickel-63			U	-2.47	pCi/g					09/09/06	03:32
				Uncert: +/-5.58							
				TPU: +/-5.58							
QC1201175824	170683004	MS									
Nickel-63		531	U	0.395	pCi/g		101	(75%-125%)		09/09/06	05:36
				Uncert: +/-9.40							
				TPU: +/-9.40							
Batch	565648										
QC1201176787	170683010	DUP									
Technetium-99			U	0.0126	pCi/g	0		(0% - 100%)	KXR1	09/12/06	14:53
				Uncert: +/-0.193							
				TPU: +/-0.193							

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

QC Summary

Workorder: 170683

Page 9 of 10

Parmname	NOM	Sample	Qual	QC	Units	RPD%	REC%	Range	Anlst	Date	Time
Rad Liquid Scintillation											
Batch	565648										
QC1201176789	LCS										
Technetium-99	13.1			13.2	pCi/g		101	(75%-125%)		09/12/06	15:56
	Uncert:			+/-0.349							
	TPU:			+/-0.480							
QC1201176786	MB										
Technetium-99			U	0.00238	pCi/g					09/12/06	14:21
	Uncert:			+/-0.154							
	TPU:			+/-0.154							
QC1201176788	170683010	MS									
Technetium-99	13.0	U	0.0126	12.1	pCi/g		93	(75%-125%)		09/12/06	15:24
	Uncert:		+/-0.193	+/-0.383							
	TPU:		+/-0.193	+/-0.489							
Batch	565649										
QC1201176791	170683010	DUP									
Carbon-14			0.324	0.204	pCi/g	46		(0% - 100%)	AXD2	09/08/06	07:38
	Uncert:		+/-0.115	+/-0.112							
	TPU:		+/-0.115	+/-0.112							
QC1201176793	LCS										
Carbon-14	7.27			8.39	pCi/g		115	(75%-125%)		09/08/06	09:12
	Uncert:			+/-0.256							
	TPU:			+/-0.288							
QC1201176790	MB										
Carbon-14			U	0.0136	pCi/g					09/08/06	06:51
	Uncert:			+/-0.109							
	TPU:			+/-0.109							
QC1201176792	170683010	MS									
Carbon-14	7.22		0.324	7.14	pCi/g		94	(75%-125%)		09/08/06	08:25
	Uncert:		+/-0.115	+/-0.239							
	TPU:		+/-0.115	+/-0.264							
Batch	565650										
QC1201176795	170683010	DUP									
Tritium		U	4.94	7.42	pCi/g	0		(0% - 100%)	ATH2	09/07/06	01:36
	Uncert:		+/-7.02	+/-7.37							
	TPU:		+/-7.02	+/-7.37							
QC1201176797	LCS										
Tritium	64.5			64.9	pCi/g		101	(75%-125%)		09/07/06	02:09
	Uncert:			+/-10.8							
	TPU:			+/-10.8							
QC1201176794	MB										
Tritium			U	4.55	pCi/g					09/07/06	01:19
	Uncert:			+/-6.87							
	TPU:			+/-6.87							
QC1201176796	170683010	MS									
Tritium	64.7	U	4.94	67.5	pCi/g		104	(75%-125%)		09/07/06	01:52
	Uncert:		+/-7.02	+/-10.9							
	TPU:		+/-7.02	+/-10.9							

GENERAL ENGINEERING LABORATORIES, LLC

2040 Savage Road Charleston SC 29407 - (843) 556-8171 - www.gel.com

QC Summary

Workorder: 170683

Page 10 of 10

Parmname	NOM	Sample Qual	QC	Units	RPD%	REC%	Range	Anlst	Date	Time
----------	-----	-------------	----	-------	------	------	-------	-------	------	------

Notes:

The Qualifiers in this report are defined as follows:

- * A quality control analyte recovery is outside of specified acceptance criteria
- < Result is less than value reported
- > Result is greater than value reported
- A The TIC is a suspected aldol-condensation product
- B Target analyte was detected in the associated blank
- BD Results are either below the MDC or tracer recovery is low
- C Analyte has been confirmed by GC/MS analysis
- D Results are reported from a diluted aliquot of the sample
- H Analytical holding time was exceeded
- J Value is estimated
- N/A Spike recovery limits do not apply. Sample concentration exceeds spike concentration by 4X or more
- R Sample results are rejected
- U Analyte was analyzed for, but not detected above the MDL, MDA, or LOD.
- UI Gamma Spectroscopy--Uncertain identification
- X Consult Case Narrative, Data Summary package, or Project Manager concerning this qualifier
- Y QC Samples were not spiked with this compound
- ^ RPD of sample and duplicate evaluated using +/-RL. Concentrations are <5X the RL
- h Preparation or preservation holding time was exceeded

N/A indicates that spike recovery limits do not apply when sample concentration exceeds spike conc. by a factor of 4 or more.

** Indicates analyte is a surrogate compound.

^ The Relative Percent Difference (RPD) obtained from the sample duplicate (DUP) is evaluated against the acceptance criteria when the sample is greater than five times (5X) the contract required detection limit (RL). In cases where either the sample or duplicate value is less than 5X the RL, a control limit of +/- the RL is used to evaluate the DUP result.


For PS, PSD, and SDILT results, the values listed are the measured amounts, not final concentrations.

Where the analytical method has been performed under NELAP certification, the analysis has met all of the requirements of the NELAC standard unless qualified on the QC Summary.

DISCHARGE CANAL
SURVEY UNIT 9106-0015
RELEASE RECORD

Attachment 2b
Split Sample Assessment Forms
(3 Pages)


Split Sample Assessment Form

Survey Area #: 9106	Survey Unit #: 15	Survey Unit Name: Discharge Canal							
Sample Plan or WPIR#: 2006-021		SML #: 9106-0015-005FS							
Sample Description: Comparison of split samples collected from sample measurement location #05 and analyzed using gamma spectroscopy by an off-site vendor laboratory. The standard sample was <u>9106-0015-005F</u> the comparison sample was <u>9106-0015-005FS</u> .									
STANDARD				COMPARISON					
Radionuclide	Activity Value	Standard Error	Resolution	Agreement Range	Activity Value	Standard Error	Comparison Ratio	Acceptable (Y/N)	
Cs-137	5.89E-02	1.68E-02	4	0.5 2.00	2.22E-01	2.19E-02	3.77	N	
Co-60	9.29E-04	1.40E-02	0	NONE	6.32E-02	1.83E-02	68.03	N/A	
Sr-90	1.33E-02	9.00E-03	1	NONE	1.49E-02	9.95E-03	1.12	N/A	
K-40	1.42E+01	5.20E-01	27	0.75 1.33	1.49E+01	6.00E-01	1.05	Y	
Comments/Corrective Actions: In consideration of the Co-60 & Sr-90 results, guidance for agreement ranges, obtained from USNRC Inspection Procedure 84750, does not address resolution ratios less than 4, therefore, a determination of acceptability for such ratios cannot be made. Since Cs-137 has a likelihood to be tightly bound to organic mater in the sample matrix, one would not neccessarily expect it to be homogenously mixed if processing of the sample-split aliquot is not effective in dispersing organic material uniformly through the sample aliquot. Since K-40 was found to be present at an acceptable level of agreement, no further action is warranted.					Table is provided to show acceptance criteria used to assess split samples.				
					Resolution		Agreement Range		
4	7	0.50	2.00						
8	15	0.60	1.66						
16	50	0.75	1.33						
51	200	0.80	1.25						
> 200		0.85	1.18						
Performed By:				Date:		Reviewed By:		Date:	
				11-13-06				11/13/06	

WPIR – Work Plan and Inspection Record

SML – Sample Measurement Location designation

Split Sample Assessment Form

Survey Area#:	9106	Survey Unit #:	15	Survey Unit Name:	Discharge Canal				
Sample Plan or WPIR#:					2006-0021				
					SML #: 9106-0015-012FS				
Sample Description: Comparison of split samples collected from sample measurement location #12 and analyzed using gamma spectroscopy by an off-site vendor laboratory. The standard sample was 9106-0015-012F, the comparison sample was 9106-0015-012FS.									
STANDARD					COMPARISON				
Radionuclide	Activity Value	Standard Error	Resolution	Agreement Range	Activity Value	Standard Error	Comparison Ratio	Acceptable (Y/N)	
Cs-137	3.47E-01	2.32E-02	15	0.6 1.66	3.28E-01	3.17E-02	0.95	Y	
Co-60	6.55E-01	3.79E-02	17	0.75 1.33	6.26E-01	4.11E-02	0.96	Y	
Sr-90	3.27E-03	8.00E-03	0	NONE	8.15E-03	7.35E-03	2.49	N/A	
K-40	1.18E+01	4.41E-01	27	0.75 1.33	1.24E+01	6.30E-01	1.05	Y	
Comments/Corrective Actions: In consideration of the Sr-90 results, guidance for agreement ranges, obtained from USNRC Inspection Procedure 84750, does not address resolution ratios less than 4, therefore, a determination of acceptability for such ratios cannot be made. Since Cs-137, Co-60 and K-40 was found to be present at an acceptable level of agreement, no further action is warranted.					Table is provided to show acceptance criteria used to assess split samples.				
4		7		0.50		2.00			
8		15		0.60		1.66			
16		50		0.75		1.33			
51		200		0.80		1.25			
> 200				0.85		1.18			
Performed By:			Date:		Reviewed By:			Date:	
			11-13-06					11/13/06	

WPIR – Work Plan and Inspection Record

SML – Sample Measurement Location designation

Split Sample Assessment Form

Survey Area#:	9106	Survey Unit #:	15	Survey Unit Name:	Discharge Canal				
Sample Plan or WPIR#:					2006-0021				
					SML #: 9106-0015-018FS				
Sample Description: Comparison of split samples collected from sample measurement location #18 and analyzed using gamma spectroscopy by an off-site vendor laboratory. The standard sample was 9106-0015-018E, the comparison sample was 9106-0015-018FS.									
STANDARD					COMPARISON				
Radionuclide	Activity Value	Standard Error	Resolution	Agreement Range		Activity Value	Standard Error	Comparison Ratio	Acceptable (Y/N)
Cs-137	3.54E-01	2.76E-02	13	0.60	1.66	3.98E-01	4.93E-02	1.12	Y
Co-60	1.16E+00	5.00E-02	23	0.75	1.33	1.09E+00	6.00E-02	0.94	Y
Sr-90	-1.15E-02	6.80E-03	-2	NONE		1.46E-02	9.10E-03	-1.27	N/A
K-40	1.27E+01	5.45E-01	23	0.75	1.33	1.32E+01	7.70E-01	1.04	Y
Comments/Corrective Actions: In consideration of the Sr-90 results, guidance for agreement ranges, obtained from USNRC Inspection Procedure 84750, does not address resolution ratios less than 4, therefore, a determination of acceptability for such ratios cannot be made. Since Cs-137, Co-60 and K-40 was found to be present at an acceptable level of agreement, no further action is warranted.					Table is provided to show acceptance criteria used to assess split samples.				
					4	7	0.50	2.00	
					8	15	0.60	1.66	
					16	50	0.75	1.33	
51	200	0.80	1.25						
> 200		0.85	1.18						
Performed By:			Date:		Reviewed By:			Date:	
			11-13-06					11/13/06	

WPIR – Work Plan and Inspection Record
SML – Sample Measurement Location designation

DISCHARGE CANAL
SURVEY UNIT 9106-0015
RELEASE RECORD

Attachment 2c
Preliminary Data Forms
(2 Pages)

Preliminary Data Review Form - Samples for the Sign Test

Survey Unit: 9106- 15
 Survey Unit Name: Discharge Canal

Classification: 2
 Survey Media: Water
 Type of Survey: Final Status Survey
 Type of Measurement: Radionuclide Specific
 Number of Measurements: 28
 Operational DCGL: 1

BASIC STATISTICAL QUANTITIES

	Cs-137	Co-60	Sr-90
Minimum Value:	-8.56E-03	-3.79E-03	-1.88E-02
Maximum Value:	5.22E-01	1.16E+00	2.52E-02
Mean:	2.26E-01	2.96E-01	5.37E-03
Median:	2.63E-01	1.41E-01	4.75E-03
Standard Deviation:	1.69E-01	3.57E-01	1.25E-02

RADIONUCLIDE CONCENTRATION (pCi/g)

NUMBER	Cs-137	Co-60	Sr-90
9106-0015-001F	2.56E-02	1.20E-02	2.48E-02
9106-0015-002F	5.22E-01	1.11E+00	-1.88E-02
9106-0015-003F	4.67E-02	1.42E-01	-3.33E-03
9106-0015-004F	-8.56E-03	9.74E-03	1.98E-02
9106-0015-005F	5.89E-02	9.29E-04	1.33E-02
9106-0015-006F	3.22E-01	3.50E-01	8.64E-03
9106-0015-007F	2.85E-01	3.55E-01	2.98E-03
9106-0015-008F	2.15E-01	3.49E-01	1.05E-02
9106-0015-009F	1.19E-02	3.23E-02	1.55E-02
9106-0015-010F	2.53E-01	0.00E+00	3.71E-03
9106-0015-011F	4.93E-01	3.96E-01	1.88E-02
9106-0015-012F	3.47E-01	6.55E-01	3.27E-03
9106-0015-013F	4.43E-01	7.05E-01	5.00E-03
9106-0015-014F	4.43E-02	4.32E-02	2.22E-02
9106-0015-015F	2.08E-01	7.07E-02	2.11E-02
9106-0015-016F	3.02E-01	1.01E-01	-2.59E-03
9106-0015-017F	4.74E-01	2.90E-01	4.49E-03
9106-0015-018F	3.54E-01	1.16E+00	-1.15E-02
9106-0015-019F	9.01E-02	2.38E-01	9.59E-03
9106-0015-020F	9.79E-02	2.03E-01	-8.28E-03
9106-0015-021F	3.98E-01	0.00E+00	-1.17E-02
9106-0015-022F	3.46E-01	6.97E-01	2.53E-03
9106-0015-023F	3.28E-01	1.06E+00	-1.20E-02
9106-0015-024F	6.71E-02	1.15E-01	2.52E-02

9106-0015-025F	1.17E-02	-3.63E-03	1.28E-02
9106-0015-026F	3.23E-01	5.75E-02	6.51E-03
9106-0015-027F	2.73E-01	1.39E-01	3.14E-03
9106-0015-028F	4.90E-03	-3.79E-03	-1.53E-02

Performed By: Oral Marshall

Date: 11-13-06

Independent Review: Robert J. M.


Date: 11-13-06

DISCHARGE CANAL
SURVEY UNIT 9106-0015
RELEASE RECORD

Attachment 2d
Graphical Representation of Data
(6 Pages)

Quantile Plot For Cesium - 137

Survey Unit: 9106-15
 Survey Unit Name: Discharge Canal
 Mean: 2.26E-01 pCi/g

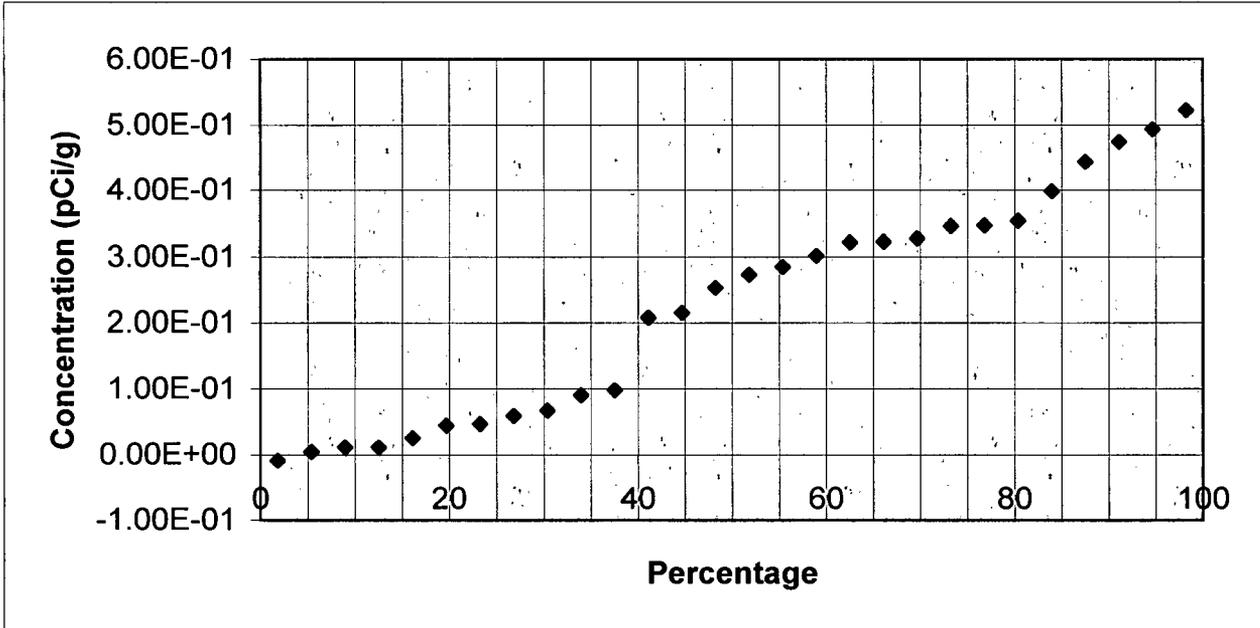

Cs-137	Rank	Percentage	Cs-137	Rank	Percentage
-8.56E-03	1	2 %	2.73E-01	15	52 %
4.90E-03	2	5 %	2.85E-01	16	55 %
1.17E-02	3	9 %	3.02E-01	17	59 %
1.19E-02	4	13 %	3.22E-01	18	63 %
2.56E-02	5	16 %	3.23E-01	19	66 %
4.43E-02	6	20 %	3.28E-01	20	70 %
4.67E-02	7	23 %	3.46E-01	21	73 %
5.89E-02	8	27 %	3.47E-01	22	77 %
6.71E-02	9	30 %	3.54E-01	23	80 %
9.01E-02	10	34 %	3.98E-01	24	84 %
9.79E-02	11	38 %	4.43E-01	25	88 %
2.08E-01	12	41 %	4.74E-01	26	91 %
2.15E-01	13	45 %	4.93E-01	27	95 %
2.53E-01	14	48 %	5.22E-01	28	98 %

Prepared By: Robert [Signature]


Date: 11-13-06

Reviewed By: [Signature]

Date: 11/13/06

Quantile Plot For Cobalt - 60

Survey Unit:
 Survey Unit Name:
 Mean: 2.96E-01 pCi/g

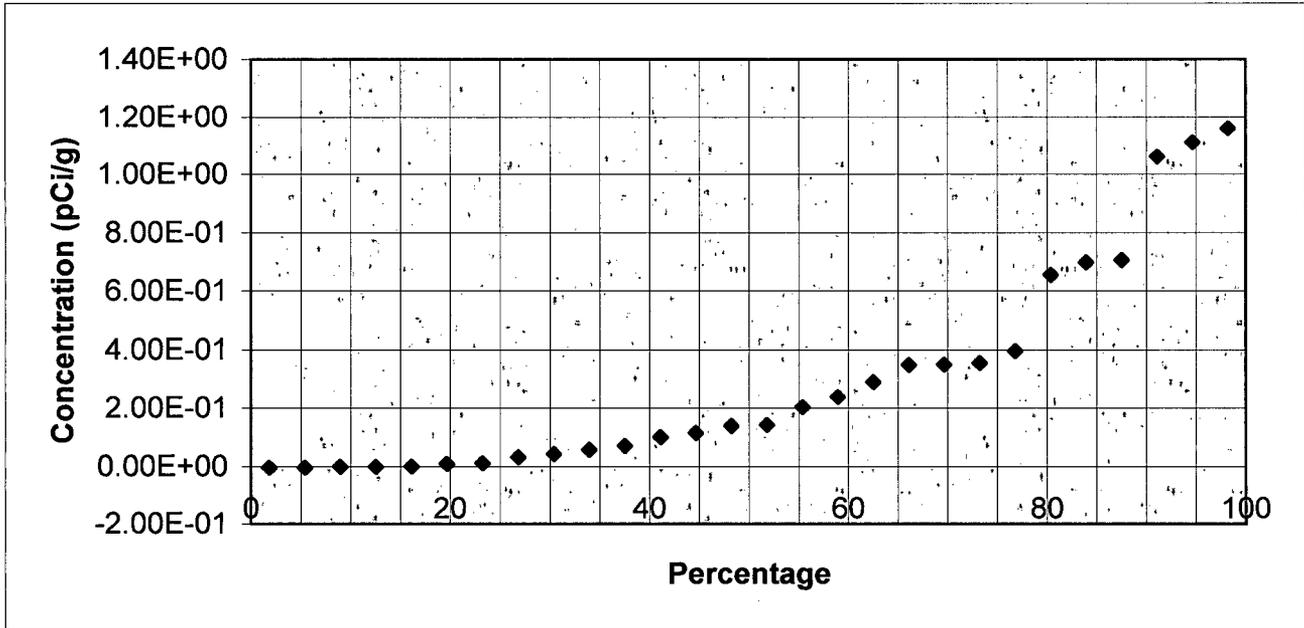

Co-60	Rank	Percentage	Co-60	Rank	Percentage
-3.79E-03	1	2 %	1.42E-01	15	52 %
-3.63E-03	2	5 %	2.03E-01	16	55 %
0.00E+00	3	9 %	2.38E-01	17	59 %
0.00E+00	4	13 %	2.90E-01	18	63 %
9.29E-04	5	16 %	3.49E-01	19	66 %
9.74E-03	6	20 %	3.50E-01	20	70 %
1.20E-02	7	23 %	3.55E-01	21	73 %
3.23E-02	8	27 %	3.96E-01	22	77 %
4.32E-02	9	30 %	6.55E-01	23	80 %
5.75E-02	10	34 %	6.97E-01	24	84 %
7.07E-02	11	38 %	7.05E-01	25	88 %
1.01E-01	12	41 %	1.06E+00	26	91 %
1.15E-01	13	45 %	1.11E+00	27	95 %
1.39E-01	14	48 %	1.16E+00	28	98 %

Prepared By: *Dale Kuntz*


Date: 11-13-06

Reviewed By: *Robert M*

Date: 11-13-06

Quantile Plot For Strontium - 90

Survey Unit:
 Survey Unit Name:
 Mean: 5.37E-03 pCi/g

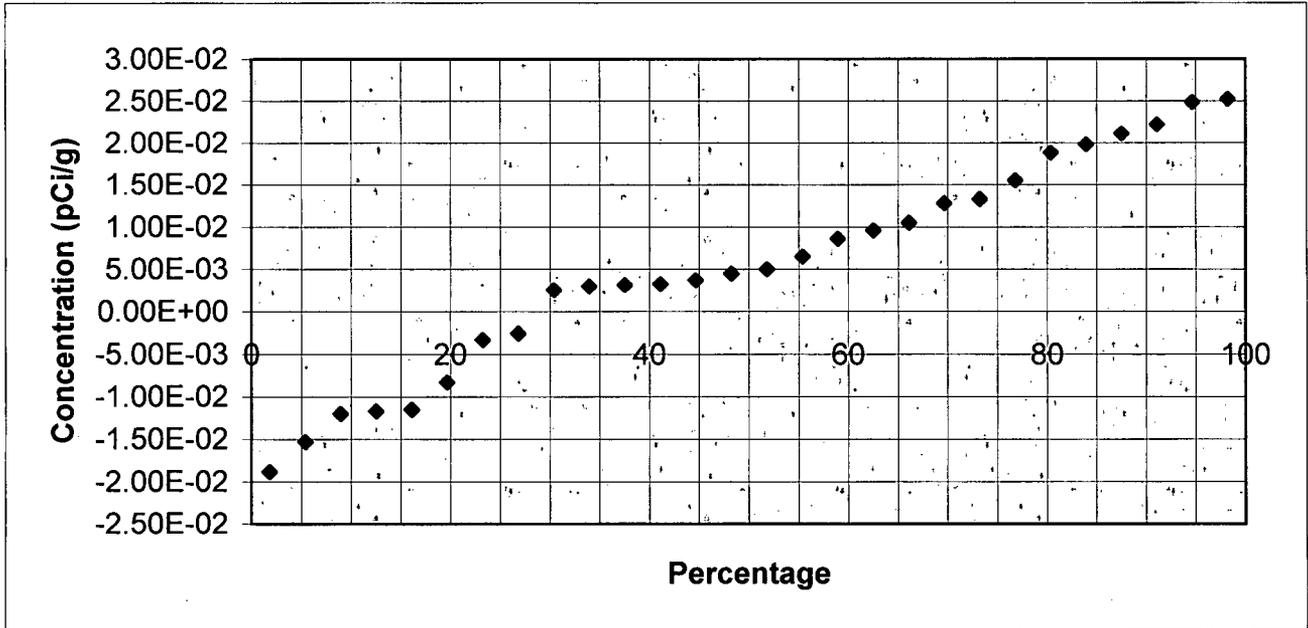

Sr-90	Rank	Percentage	Sr-90	Rank	Percentage
-1.88E-02	1	2 %	5.00E-03	15	52 %
-1.53E-02	2	5 %	6.51E-03	16	55 %
-1.20E-02	3	9 %	8.64E-03	17	59 %
-1.17E-02	4	13 %	9.59E-03	18	63 %
-1.15E-02	5	16 %	1.05E-02	19	66 %
-8.28E-03	6	20 %	1.28E-02	20	70 %
-3.33E-03	7	23 %	1.33E-02	21	73 %
-2.59E-03	8	27 %	1.55E-02	22	77 %
2.53E-03	9	30 %	1.88E-02	23	80 %
2.98E-03	10	34 %	1.98E-02	24	84 %
3.14E-03	11	38 %	2.11E-02	25	88 %
3.27E-03	12	41 %	2.22E-02	26	91 %
3.71E-03	13	45 %	2.48E-02	27	95 %
4.49E-03	14	48 %	2.52E-02	28	98 %

Prepared By: Oal Rowball

Date: 11-13-06


Reviewed By: Robert J. M.

Date: 11-13-06

Frequency Plot For Cesium - 137

Survey Unit: 9106-15
 Survey Unit Name: Discharge Canal

Mean: 0.226 pCi/g

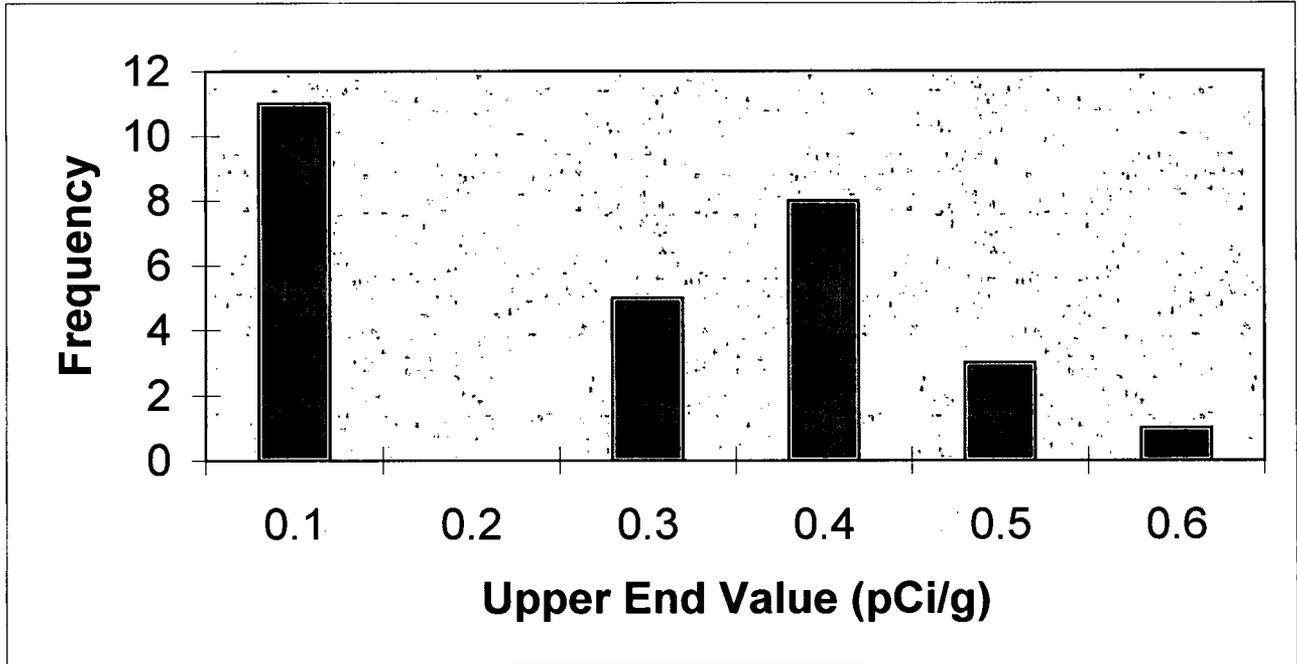

Upper End Value	Observation Frequency	Observation Frequency
0.1	11	39%
0.2	0	0%
0.3	5	18%
0.4	8	29%
0.5	3	11%
0.6	1	4%
Total	28	100%

Prepared By: *Dal Rowell*

Date: 11-13-06


Reviewed By: *Robert M*

Date: 11-13-06

Frequency Plot For Cobalt - 60

Survey Unit: 9106-15
 Survey Unit Name: Discharge Canal

Mean: 0.296 pCi/g

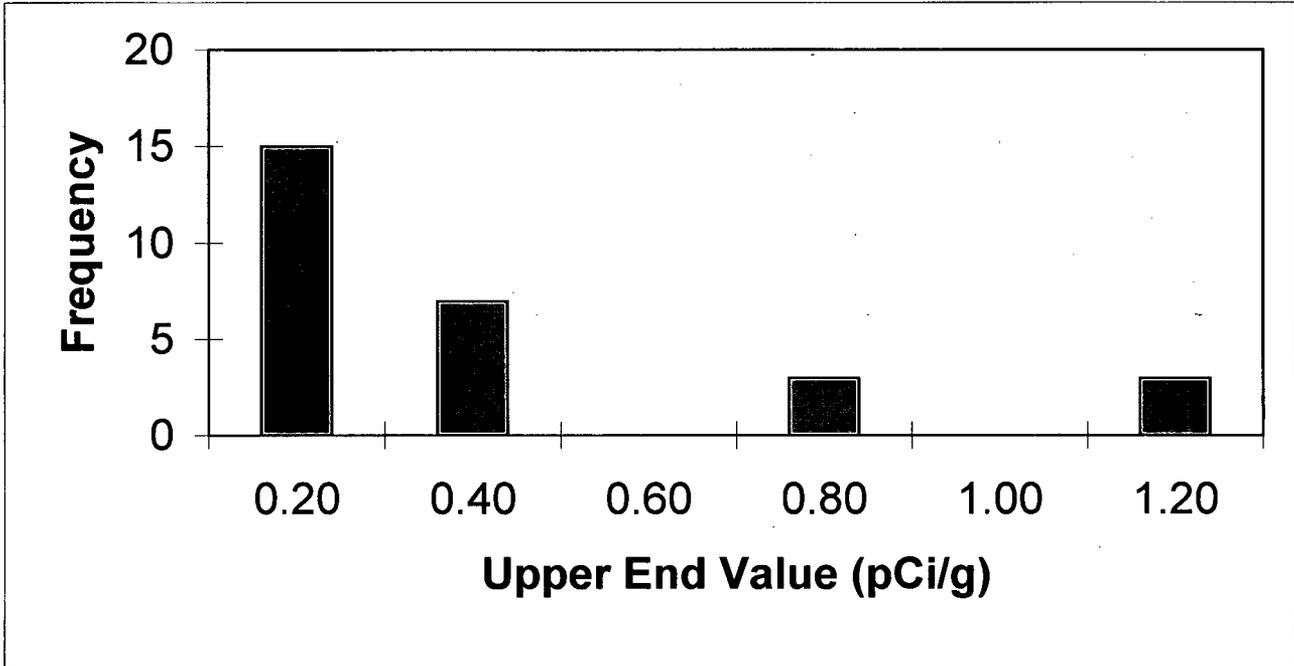

Upper End Value	Observation Frequency	Observation Frequency
0.20	15	47%
0.40	7	22%
0.60	0	0%
0.80	3	9%
1.00	0	0%
1.20	3	9%
Total	28	88%

Prepared By: Robert M

Date: 11-13-06


Reviewed By: EE

Date: 11/13/06

Frequency Plot For Strontium - 90

Survey Unit: 9106-15
 Survey Unit Name: Discharge Canal

Mean: 0.005 pCi/g

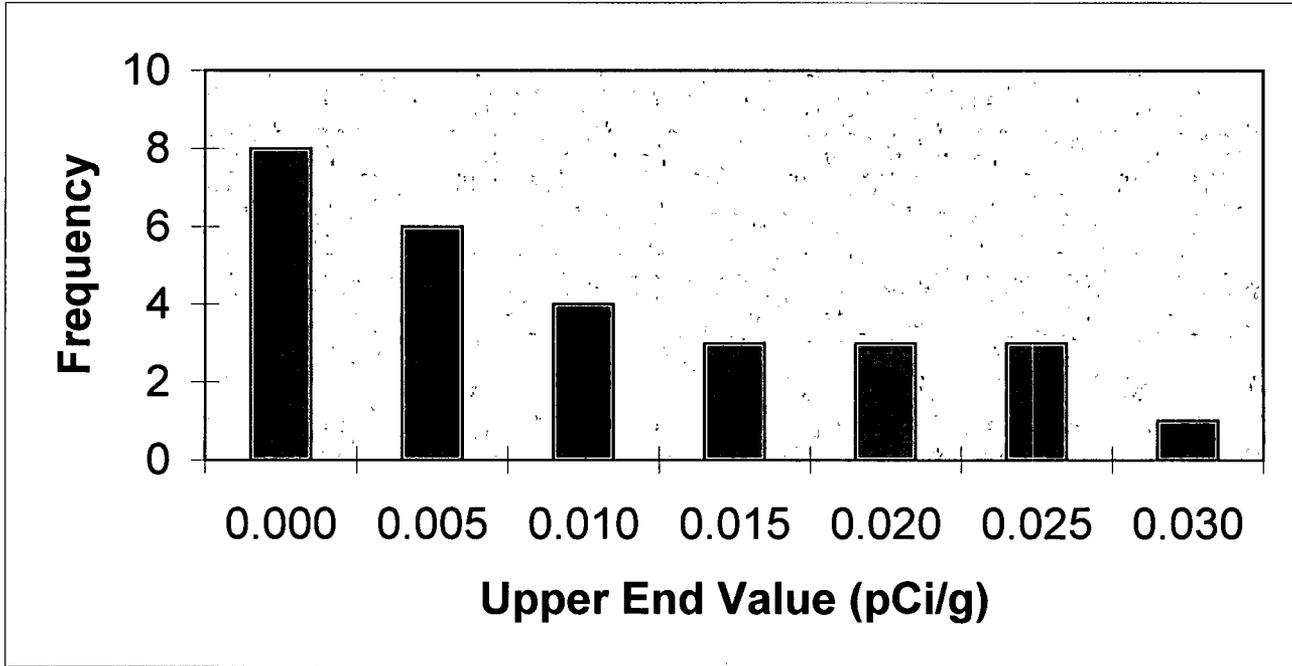

Upper End Value	Observation Frequency	Observation Frequency
0.000	8	25%
0.005	6	19%
0.010	4	13%
0.015	3	9%
0.020	3	9%
0.025	3	9%
0.030	1	3%
Total	28	88%

Prepared By: Robert [Signature]

Date: 11-13-06

Reviewed By: [Signature]

Date: 11/13/06

DISCHARGE CANAL
SURVEY UNIT 9106-0015
RELEASE RECORD

Attachment 2e
Sign Test Calculation
(2 Pages)

Sign Test Calculation Sheet For Multiple Radionuclides

Survey Unit Number: 9106-15															
Survey Unit Name: Discharge Canal															
WP&IR#: 2006-021															
Classification : 1		TYPE I (α error):0.05		TYPE I (β error):0.05											
<table border="1"> <thead> <tr> <th>Radionuclides:</th> <th>Cs-137</th> <th>Co-60</th> <th>Sr-90</th> <th>HTDs</th> </tr> </thead> <tbody> <tr> <td>Survey Design DCGL (pCi/g):</td> <td>6.01</td> <td>2.9</td> <td>1.18</td> <td>1</td> </tr> </tbody> </table>						Radionuclides:	Cs-137	Co-60	Sr-90	HTDs	Survey Design DCGL (pCi/g):	6.01	2.9	1.18	1
Radionuclides:	Cs-137	Co-60	Sr-90	HTDs											
Survey Design DCGL (pCi/g):	6.01	2.9	1.18	1											
Results Cs-137	Results Co-60	Results Sr-90	Results other HTDs	DCGL-Result	Sign										
2.56E-02	1.20E-02	2.48E-02	3.10E-02	9.40E-01	1										
5.22E-01	1.11E+00	-1.88E-02	1.41E-01	4.05E-01	1										
4.67E-02	1.42E-01	-3.33E-03	3.10E-02	9.15E-01	1										
-8.56E-03	9.74E-03	1.98E-02	1.90E-03	9.80E-01	1										
5.89E-02	9.29E-04	1.33E-02	3.10E-02	9.48E-01	1										
3.22E-01	3.50E-01	8.64E-03	3.10E-02	7.87E-01	1										
2.85E-01	3.55E-01	2.98E-03	3.10E-02	7.97E-01	1										
2.15E-01	3.49E-01	1.05E-02	3.10E-02	8.04E-01	1										
1.19E-02	3.23E-02	1.55E-02	3.10E-02	9.43E-01	1										
2.53E-01	0.00E+00	3.71E-03	3.10E-02	9.24E-01	1										
4.93E-01	3.96E-01	1.88E-02	3.10E-02	7.35E-01	1										
3.47E-01	6.55E-01	3.27E-03	3.10E-02	6.83E-01	1										
4.43E-01	7.05E-01	5.00E-03	3.10E-02	6.48E-01	1										
4.43E-02	4.32E-02	2.22E-02	3.10E-02	9.28E-01	1										
2.08E-01	7.07E-02	2.11E-02	-2.88E-02	9.52E-01	1										
3.02E-01	1.01E-01	-2.59E-03	3.10E-02	8.86E-01	1										
4.74E-01	2.90E-01	4.49E-03	3.10E-02	7.86E-01	1										
3.54E-01	1.16E+00	-1.15E-02	2.32E-02	5.28E-01	1										
9.01E-02	2.38E-01	9.59E-03	3.10E-02	8.64E-01	1										
9.79E-02	2.03E-01	-8.28E-03	3.10E-02	8.90E-01	1										
3.98E-01	0.00E+00	-1.17E-02	1.79E-02	9.26E-01	1										
3.46E-01	6.97E-01	2.53E-03	3.10E-02	6.69E-01	1										
3.28E-01	1.06E+00	-1.20E-02	3.10E-02	5.59E-01	1										
6.71E-02	1.15E-01	2.52E-02	3.10E-02	8.97E-01	1										
1.17E-02	-3.63E-03	1.28E-02	3.10E-02	9.58E-01	1										
3.23E-01	5.75E-02	6.51E-03	3.10E-02	8.90E-01	1										
2.73E-01	1.39E-01	3.14E-03	3.10E-02	8.73E-01	1										
4.90E-03	-3.79E-03	-1.53E-02	3.10E-02	9.82E-01	1										

| Number of Positive Differences (S+): | | | | 28 | |

Critical Value: 18

Survey Unit: Meets Acceptance Criterion

Performed By: *Don Rumball*

Date: 11-29-06

Independent Review: *Robert A.*

Date: 11-20-06

DISCHARGE CANAL
SURVEY UNIT 9106-0015
RELEASE RECORD

Attachment 2f
COMPASS DQA Surface Soil Report with
Retrospective Power Curve
(5 Pages)




DQA Surface Soil Report

Assessment Summary

Site: 9106-0015 (19mrem/yr) w/HTDs
Planner(s): Dale Randall
Survey Unit Name: 9106-0015
Report Number: 1
Survey Unit Samples: 28
Reference Area Samples: 0
Test Performed: Sign Test Result: Not Performed
Judgmental Samples: 0 EMC Result: Not Performed
Assessment Conclusion: **Reject Null Hypothesis (Survey Unit PASSES)**

Retrospective Power Curve

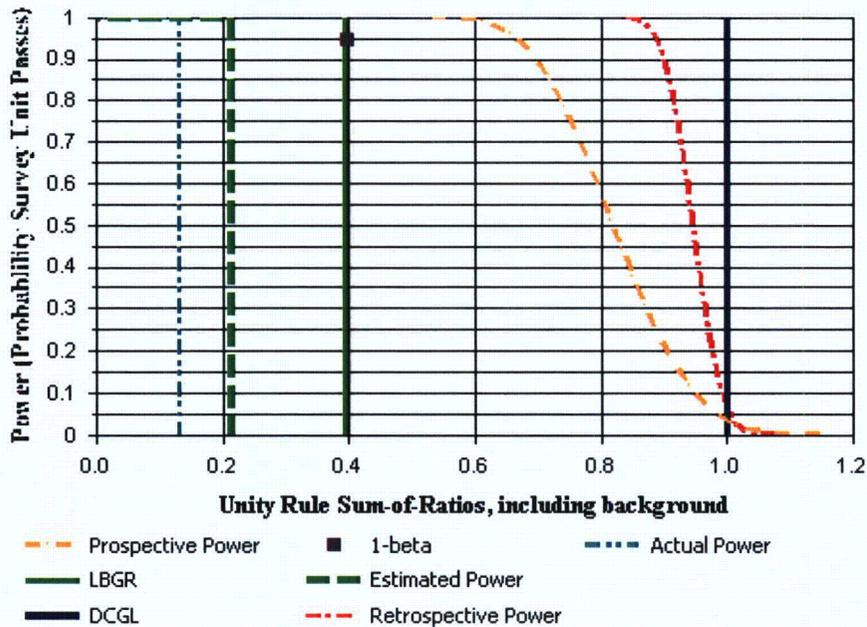



DQA Surface Soil Report

Survey Unit Data

NOTE: Type = "S" indicates survey unit sample.
Type = "R" indicates reference area sample.

Sample Number	Type	Am-241 (pCi/g)	C-14 (pCi/g)	Co-60 (pCi/g)
9106-0015-001F	S	0.1	0.1	0.01
9106-0015-002F	S	0.29	0.21	1.11
9106-0015-003F	S	0.1	0.1	0.14
9106-0015-004F	S	0	0.01	0.01
9106-0015-005F	S	0.1	0.1	0
9106-0015-006F	S	0.1	0.1	0.35
9106-0015-007F	S	0.1	0.1	0.36
9106-0015-008F	S	0.1	0.1	0.35
9106-0015-009F	S	0.1	0.1	0.03
9106-0015-010F	S	0.1	0.1	0
9106-0015-011F	S	0.1	0.1	0.4
9106-0015-012F	S	0.1	0.1	0.66
9106-0015-013F	S	0.1	0.1	0.7
9106-0015-014F	S	0.1	0.1	0.04
9106-0015-015F	S	0	-0.12	0.07
9106-0015-016F	S	0.1	0.1	0.1
9106-0015-017F	S	0.1	0.1	0.29
9106-0015-018F	S	0.19	0.06	1.16
9106-0015-019F	S	0.1	0.1	0.24
9106-0015-020F	S	0.1	0.1	0.2
9106-0015-021F	S	0	-0.05	0
9106-0015-022F	S	0.1	0.1	0.7
9106-0015-023F	S	0.1	0.1	1.06
9106-0015-024F	S	0.1	0.1	0.12
9106-0015-025F	S	0.1	0.1	0
9106-0015-026F	S	0.1	0.1	0.06
9106-0015-027F	S	0.1	0.1	0.14
9106-0015-028F	S	0.1	0.1	0

Sample Number	Type	Cs-137 (pCi/g)	Pu-241 (pCi/g)	SrY-90 (pCi/g)
9106-0015-001F	S	0.03	4.92	0.02
9106-0015-002F	S	0.52	24.6	-0.02
9106-0015-003F	S	0.05	4.92	0
9106-0015-004F	S	-0.01	0	0.02
9106-0015-005F	S	0.06	4.92	0.01
9106-0015-006F	S	0.32	4.92	0.01
9106-0015-007F	S	0.28	4.92	0
9106-0015-008F	S	0.22	4.92	0.01
9106-0015-009F	S	0.01	4.92	0.02
9106-0015-010F	S	0.25	4.92	0
9106-0015-011F	S	0.49	4.92	0.02
9106-0015-012F	S	0.35	4.92	0
9106-0015-013F	S	0.44	4.92	0
9106-0015-014F	S	0.04	4.92	0.02
9106-0015-015F	S	0.21	0	0.02
9106-0015-016F	S	0.3	4.92	0
9106-0015-017F	S	0.47	4.92	0
9106-0015-018F	S	0.35	0	-0.01
9106-0015-019F	S	0.09	4.92	0.01
9106-0015-020F	S	0.1	4.92	-0.01
9106-0015-021F	S	0.4	0	-0.01



DQA Surface Soil Report

Survey Unit Data

NOTE: Type = "S" indicates survey unit sample.
Type = "R" indicates reference area sample.

Sample Number	Type	Cs-137 (pCi/g)	Pu-241 (pCi/g)	SrY-90 (pCi/g)
9106-0015-022F	S	0.35	4.92	0
9106-0015-023F	S	0.33	4.92	-0.01
9106-0015-024F	S	0.07	4.92	0.03
9106-0015-025F	S	0.01	4.92	0.01
9106-0015-026F	S	0.32	4.92	0.01
9106-0015-027F	S	0.27	4.92	0
9106-0015-028F	S	0	4.92	-0.02

Sample Number	Type	Tc-99 (pCi/g)
9106-0015-001F	S	0.13
9106-0015-002F	S	0.39
9106-0015-003F	S	0.13
9106-0015-004F	S	0
9106-0015-005F	S	0.13
9106-0015-006F	S	0.13
9106-0015-007F	S	0.13
9106-0015-008F	S	0.13
9106-0015-009F	S	0.13
9106-0015-010F	S	0.13
9106-0015-011F	S	0.13
9106-0015-012F	S	0.13
9106-0015-013F	S	0.13
9106-0015-014F	S	0.13
9106-0015-015F	S	0
9106-0015-016F	S	0.13
9106-0015-017F	S	0.13
9106-0015-018F	S	0
9106-0015-019F	S	0.13
9106-0015-020F	S	0.13
9106-0015-021F	S	0.28
9106-0015-022F	S	0.13
9106-0015-023F	S	0.13
9106-0015-024F	S	0.13
9106-0015-025F	S	0.13
9106-0015-026F	S	0.13
9106-0015-027F	S	0.13
9106-0015-028F	S	0.13



DQA Surface Soil Report

Modified Data (Unity Rule SOR)

NOTE: Type = "S" indicates survey unit sample.
Type = "R" indicates reference area sample.

Sample Number	Type	Sum-of-Ratios (SOR)
9106-0015-001F	S	0.08
9106-0015-002F	S	0.59
9106-0015-003F	S	0.1
9106-0015-004F	S	0.02
9106-0015-005F	S	0.07
9106-0015-006F	S	0.23
9106-0015-007F	S	0.22
9106-0015-008F	S	0.21
9106-0015-009F	S	0.08
9106-0015-010F	S	0.09
9106-0015-011F	S	0.28
9106-0015-012F	S	0.34
9106-0015-013F	S	0.37
9106-0015-014F	S	0.09
9106-0015-015F	S	0.05
9106-0015-016F	S	0.13
9106-0015-017F	S	0.23
9106-0015-018F	S	0.47
9106-0015-019F	S	0.15
9106-0015-020F	S	0.13
9106-0015-021F	S	0.07
9106-0015-022F	S	0.35
9106-0015-023F	S	0.46
9106-0015-024F	S	0.12
9106-0015-025F	S	0.06
9106-0015-026F	S	0.13
9106-0015-027F	S	0.15
9106-0015-028F	S	0.04



DQA Surface Soil Report

Basic Statistical Quantities Summary

Statistic	Survey Unit	Background	DQO Results
Sample Number	28	N/A	N=15
Mean (SOR)	0.19	N/A	0.21
Median (SOR)	0.13	N/A	N/A
Std Dev (SOR)	0.15	N/A	0.29
High Value (SOR)	0.59	N/A	N/A
Low Value (SOR)	0.02	N/A	N/A
