

June 15, 1990

Docket No. 50-390

APPLICANT: Tennessee Valley Authority

FACILITY: Watts Bar Nuclear Plant, Unit 1

SUBJECT: MINUTES OF MAY 31, 1990, MEETING ON THE STRUCTURAL ADEQUACY OF HVAC DUCT WELDS (TAC R00510)

On May 31, 1990, a meeting was held at the request of the Tennessee Valley Authority (TVA) in Rockville, Maryland between the NRC staff and TVA's representatives. TVA made a presentation regarding the structural adequacy of heating, ventilating and air conditioning (HVAC) welds at Watts Bar, Unit 1. Enclosure 1 is the list of individuals attending the meeting. Enclosure 2 contains the handouts provided by the applicant at the meeting.

Safety-related HVAC ductwork had been installed in 1978 without specific welding requirements from TVA engineering. After engineering requirements were imposed in 1980, subsequent inspections identified partial penetration welds where full penetration welds were required. The staff was concerned that the partial penetration butt welds could fail during and/or following a design basis seismic event.

TVA concluded that the welded ductwork will perform its intended design functions. Additional testing and analyses confirmed the earlier conclusions and TVA will supplement the 50.55(e) final report on this subject by documenting the results of this additional testing. The NRC staff will review this information as part of verification/closure of the unresolved item.

Paul Cortland, Project Engineer
 Project Directorate II-4
 Division of Reactor Projects I/II
 Office of Nuclear Reactor Regulation

- Enclosures:
1. List of Attendees
 2. TVA Presentation Handout

cc w/enclosures:
 See next page

9006220294 900615
 PDR ADOCK 05000390
 A PDC

DFOL
memo-4
act

OFC	: PDII-4/LA	: PDII-4/PM	: MEB/SC	: PDII-4/PM	: PDII-4/D
NAME	: MKrebs <i>MK</i>	: PCortland <i>PC</i>	: DTerao <i>DT</i>	: PTam <i>PT</i>	: FHebdon <i>FH</i>
DATE	: 6/12/90	: 6/12/90	: 6/14/90	: 6/14/90	: 6/15/90

Meeting Summary, Memoranda for Trip Reports or Site Visits

Docket File

NRC PDR

Local PDR

T. Murley/F. Miraglia

J. Partlow

S. Varga

G. Lainas

F. Hebdon

S. Black

M. Krebs

P. Cortland

P. Tam

B. Wilson, Region II

OGC

R. Auluck

D. Terao

G. Georgiev

D. Smith

ACRS (10)

GPA/CA (M. Callahan) (3)

E. Jordan

B. Grimes

J. Scarborough

G. Marcus

L. Norrholm

C. Ader

J. Gray

R. Borchardt

WBN Rdg. File

cc:

Mr. Marvin Runyon, Chairman
Tennessee Valley Authority
ET 12A 7A
400 West Summit Hill Drive
Knoxville, Tennessee 37902

Director
Tennessee Valley Authority
ET 12A 11A
400 West Summit Hill Drive
Knoxville, Tennessee 37902

Mr. John B. Waters, Director
Tennessee Valley Authority
ET 12A 9A
400 West Summit Hill Drive
Knoxville, Tennessee 37902

Mr. W. F. Willis
Chief Operating Officer
ET 12B 16B
400 West Summit Hill Drive
Knoxville, Tennessee 37902

General Counsel
Tennessee Valley Authority
400 West Summit Hill Drive
ET 11B 33H
Knoxville, Tennessee 37902

Mr. Dwight Nunn
Vice President, Nuclear Engineering
Tennessee Valley Authority
6N 38A Lookout Place
1101 Market Street
Chattanooga, Tennessee 37902

Dr. Mark O. Medford
Vice President and Nuclear
Technical Director
Tennessee Valley Authority
6N 38A Lookout Place
Chattanooga, Tennessee 37402-2801

Mr. Edward G. Wallace
Manager, Nuclear Licensing
and Regulatory Affairs
Tennessee Valley Authority
5N 157B Lookout Place
Chattanooga, Tennessee 37402-2801

Mr. Oliver D. Kingsley, Jr.
Senior Vice President, Nuclear Power
Tennessee Valley Authority
6N 38A Lookout Place
1101 Market Street
Chattanooga, Tennessee 37402-2801

Mr. Dan Douthit, Program Manager
Watts Bar Nuclear Plant
Tennessee Valley Authority
P. O. Box 800
Spring City, Tennessee 37381

Mr. R. J. Stevens, Site Licensing Manager
Watts Bar Nuclear Plant
Tennessee Valley Authority
P. O. Box 800
Spring City, Tennessee 37381

Mr. Richard F. Wilson
Vice President, New Projects
Tennessee Valley Authority
6N 38A Lookout Place
Chattanooga, Tennessee 37402-2801

Honorable Robert Aikman, County Judge
Rhea County Courthouse
Dayton, Tennessee 37321

Honorable Johnny Powell, County Judge
Meigs County Courthouse, Route 2
Decatur, Tennessee 37322

Mr. Michael H. Mobley, Director
Division of Radiological Health
T.E.R.R.A. Building, 6th Floor
150 9th Avenue North
Nashville, Tennessee 37219-5404

Regional Administrator, Region II
U.S. Nuclear Regulatory Commission
101 Marietta Street, N.W.
Atlanta, Georgia 30323

Senior Resident Inspector
Watts Bar Nuclear Plant
U.S. Nuclear Regulatory Commission
Route 2, Box 700
Spring City, Tennessee 37381

Tennessee Valley Authority
Rockville Office
11921 Rockville Pike
Suite 402
Rockville, Maryland 20852

ENCLOSURE 1

ATTENDANCE LIST

MEETING ON STRUCTURAL ADEQUACY OF HVAC DUCT WELDS

AT WATTS BAR NUCLEAR PLANT, UNIT 1

May 31, 1990

Name	Affiliation
R. Auluck	NRC/NRR/TVAPD
P. Cortland	NRC/NRR/TVAPD
G. Georgiev	NRC/NRR/TVAPD
D. Smith	NRC/NRR/TVAPD
P. Tam	NRC/NRR/PD II-4
D. Terao	NRC/NRR/TVAPD
J. Adair	TVA/Watts Bar
R. Alley	TVA/Watts Bar
T. Dean	TVA/Watts Bar
D. Etzler	TVA/Watts Bar
W. Horn	TVA/Watts Bar
T. Ippolito	TVA/Rockville
F. Laurent	TVA/Watts Bar
W. Raughley	TVA/Watts Bar
R. Stevens	TVA/Watts Bar Licensing
T. Woods	TVA/Knoxville
G. Egar	APTECH
P. Bezler	Brookhaven National Laboratory

ENCLOSURE 2

TVA DOCUMENTS PRESENTED AT MEETING

1. "Safety-Related Heating, Ventilating, and Air Conditioning Duct Welding"

**MEETING WITH NRC STAFF
ROCKVILLE, MD
MAY 31, 1990**

**SAFETY-RELATED HEATING,
VENTILATING, AND
AIR CONDITIONING
DUCT WELDING**

WATTS BAR NUCLEAR PLANT

TVA

PURPOSE

- RESPONSE TO NRC QUESTIONS REGARDING THE STRUCTURAL ADEQUACY OF THE HVAC DUCT WELDS AT WBN.
- PROVIDE AN OVERVIEW OF THE TOTAL WBN PROGRAM FOR ENSURING STRUCTURAL ADEQUACY
- DISCUSS THE MECHANICAL TESTING OF WELD COUPONS AND PROVIDE THE RESULTS TO SUPPLEMENT THE INSPECTION AND ANALYSIS PREVIOUSLY PERFORMED.
- CONFIRM THE STRUCTURAL ADEQUACY OF THE HVAC DUCTWORK.

AGENDA

- BACKGROUND
- METHOD
- TEST RESULTS
- SUMMARY
- CLOSING COMMENTS

BACKGROUND

• PROBLEM STATEMENT

**INSUFFICIENT QUALITY AND TECHNICAL REQUIREMENTS
LED TO CONCERNS ABOUT THE STRUCTURAL ADEQUACY
OF HVAC WELDS. THESE CONCERNS WERE RAISED
THROUGH CAQs AND EMPLOYEE CONCERNS
AND DOCUMENTED TO NRC IN 50.55(e) REPORTS.**

• SCOPE

SAFETY-RELATED CATEGORY I SYSTEMS

- EMERGENCY GAS TREATMENT SYSTEM
- HYDROGEN COLLECTION SYSTEM
- DIESEL GENERATOR BUILDING BATTERY HOOD EXHAUST
- REACTOR BUILDING PURGE AIR
- AUXILIARY BUILDING GAS TREATMENT SYSTEM DISCHARGE
- POST-ACCIDENT SAMPLING
- CONTROL BUILDING PRESSURIZATION AND SMOKE REMOVAL

• DUCT PARAMETERS

- RECTANGULAR DUCT
 ASTM A570 GRADE 30 (B)
 e.g., 24" to 28" x 96"
 12 GAUGE (.1046)

- ROUND DUCT
 SPIRAL-WELDED DUCT (LOW STRESS)
 ASTM A211
 8" DIAMETER to 36" DIAMETER
 14 GAUGE (.0747) to .134"

- SCHEDULE PIPE
 ASTM A106 GRADE B
 6" DIAMETER to 24" DIAMETER
 1/4" (0.250") to 5/16" (0.375")

METHOD

TVA ACTIONS TO ASSURE STRUCTURAL ADEQUACY OF SAFETY-RELATED HVAC DUCT

- TO DETERMINE WELD PRESENCE

- CONSTRUCTION

WALKDOWN ALL SAFETY-RELATED WELDS
(APPROXIMATELY 10,400 DUCT WELDS)

WELD PRESENCE

NUMBERED WELDS

CLASSIFIED TO TYPE OF WELD

- QUALITY CONTROL

PERFORMED VISUAL SURVEY FOR WELD PRESENCE
AND NOTED OBSERVED DEFECTS.

PERFORMED EDDY CURRENT TESTING FOR WELD
METAL PRESENCE.

TVA

SUMMARY :

**BASED ON THE RESULTS OF THESE EFFORTS, AS
OUTLINED IN OUR 10 CFR 50.55(e) REPORT, TVA HAS
REASONABLE ASSURANCE THAT THERE IS WELD
PRESENCE AT EACH JOINT.**

TVA

• TO DETERMINE STRUCTURAL ADEQUACY

- ENGINEERING

- CONSERVATIVE STRESS ANALYSIS PERFORMED TO DETERMINE MINIMUM WELD REQUIREMENTS**

HIGH STRESS (WORST CASE) - APPROX. 9.75 ksi

- REVIEW OF 10,400 SURVEYS TO IDENTIFY ANY CONDITION THAT WOULD REQUIRE MORE DETAILED EVALUATION**

IDENTIFIED APPROX. 175 RECORDS THAT REQUIRED ADDITIONAL ENGINEERING FIELD EVALUATIONS.

ADDITIONAL CALCS PERFORMED USING AS-BUILT CONFIGURATIONS. ALL WERE ENVELOPED BY WORST-CASE EVALUATIONS.

- COUPON TESTING.**

WELD SAMPLE COUPONS

- 1988 SAMPLES

VISUAL EXAMINATION

PENETRATION MEASUREMENTS

- 1981 SAMPLES

VISUAL EXAMINATION

PENETRATION MEASUREMENTS

MECHANICAL TESTS

- 1990 SAMPLES

VISUAL EXAMINATION

PENETRATION MEASUREMENTS

MECHANICAL TESTS

ASSESSMENT OF STRUCTURAL INTEGRITY OF HVAC WELDS

- INTRODUCTION AND OBJECTIVE
- METHOD OF ANALYSIS
- RESULTS OF STRUCTURAL INTEGRITY ANALYSIS
- REVIEW OF MECHANICAL TESTS
- COMPARISON OF TEST RESULTS WITH PREDICTIONS
- REVIEW OF INSPECTION INFORMATION
- ESTABLISHMENT OF STATISTICALLY BASED "WORST" CASE FOR WELD ATTRIBUTES
- CONCLUSIONS

OBJECTIVES

- PERFORMED STRUCTURAL INTEGRITY ANALYSIS
- COMPARE PREDICTIONS WITH TEST RESULTS
- ESTABLISH MARGINS


METHOD OF ANALYSIS

- **LIMIT LOAD IS CONTROLLING FAILURE MECHANISM**


- **BRITTLE FRACTURE IS NOT A CONCERN**

- **MODELS CONSIDERED :**
 - **LACK OF PENETRATION**
 - **LACK OF WELD**

MODELS

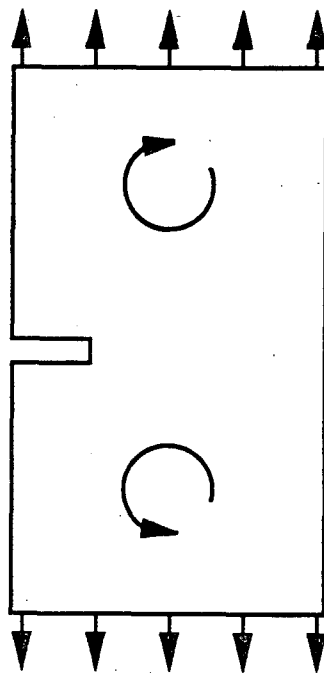

A. EDGE CRACKED PLATE

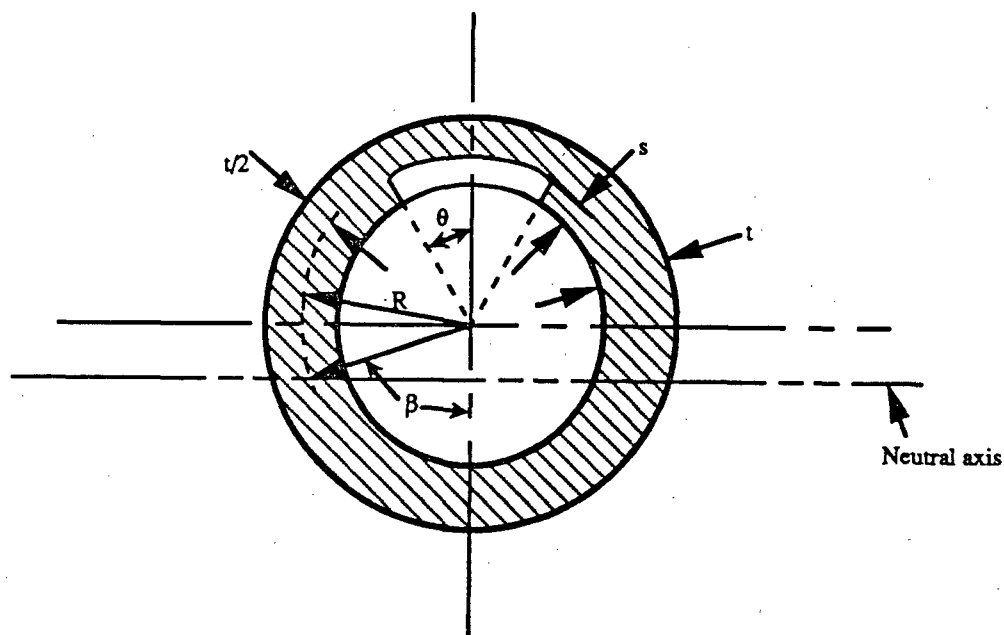

B. CIRCUMFERENTIAL CRACK IN A CYLINDER

RESULTS

LIMIT LOAD CALCULATIONS BASED ON:

- A. MINIMUM BASE METAL PROPERTIES**
- B. WELD METAL PROPERTIES**
- C. FIXED END CONDITIONS VERSUS PINNED ENDS**


WORST CASE WELD ATTRIBUTES

95% / 95%

- LACK OF PENETRATION 53% OF WELD THICKNESS
- LACK OF WELD 28% OF CIRCUMFERENCE


LIMIT LOAD ANALYSIS

EDGE CRACKED PANEL - ASTM A570 GRADE B

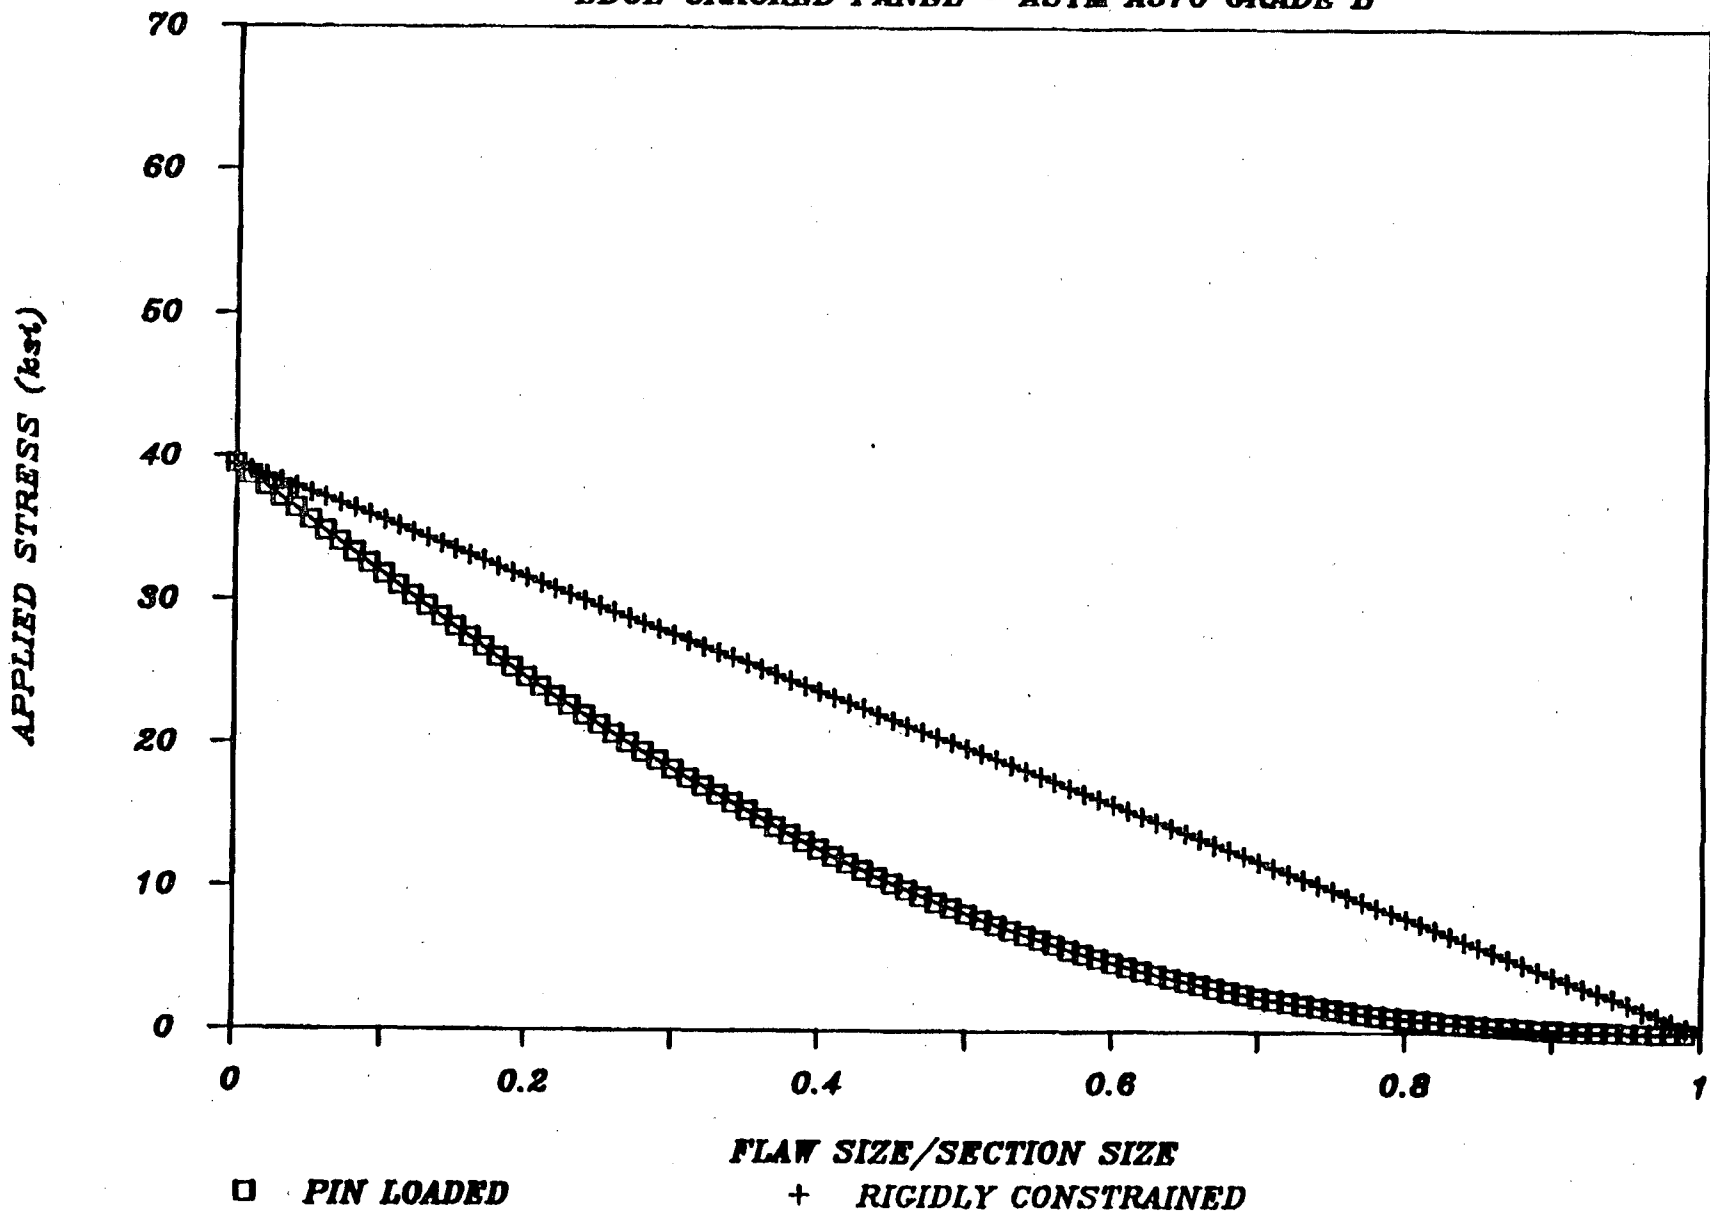


TVA

EDGE CRACKED PANEL -- SIGFLO = 70 KSI

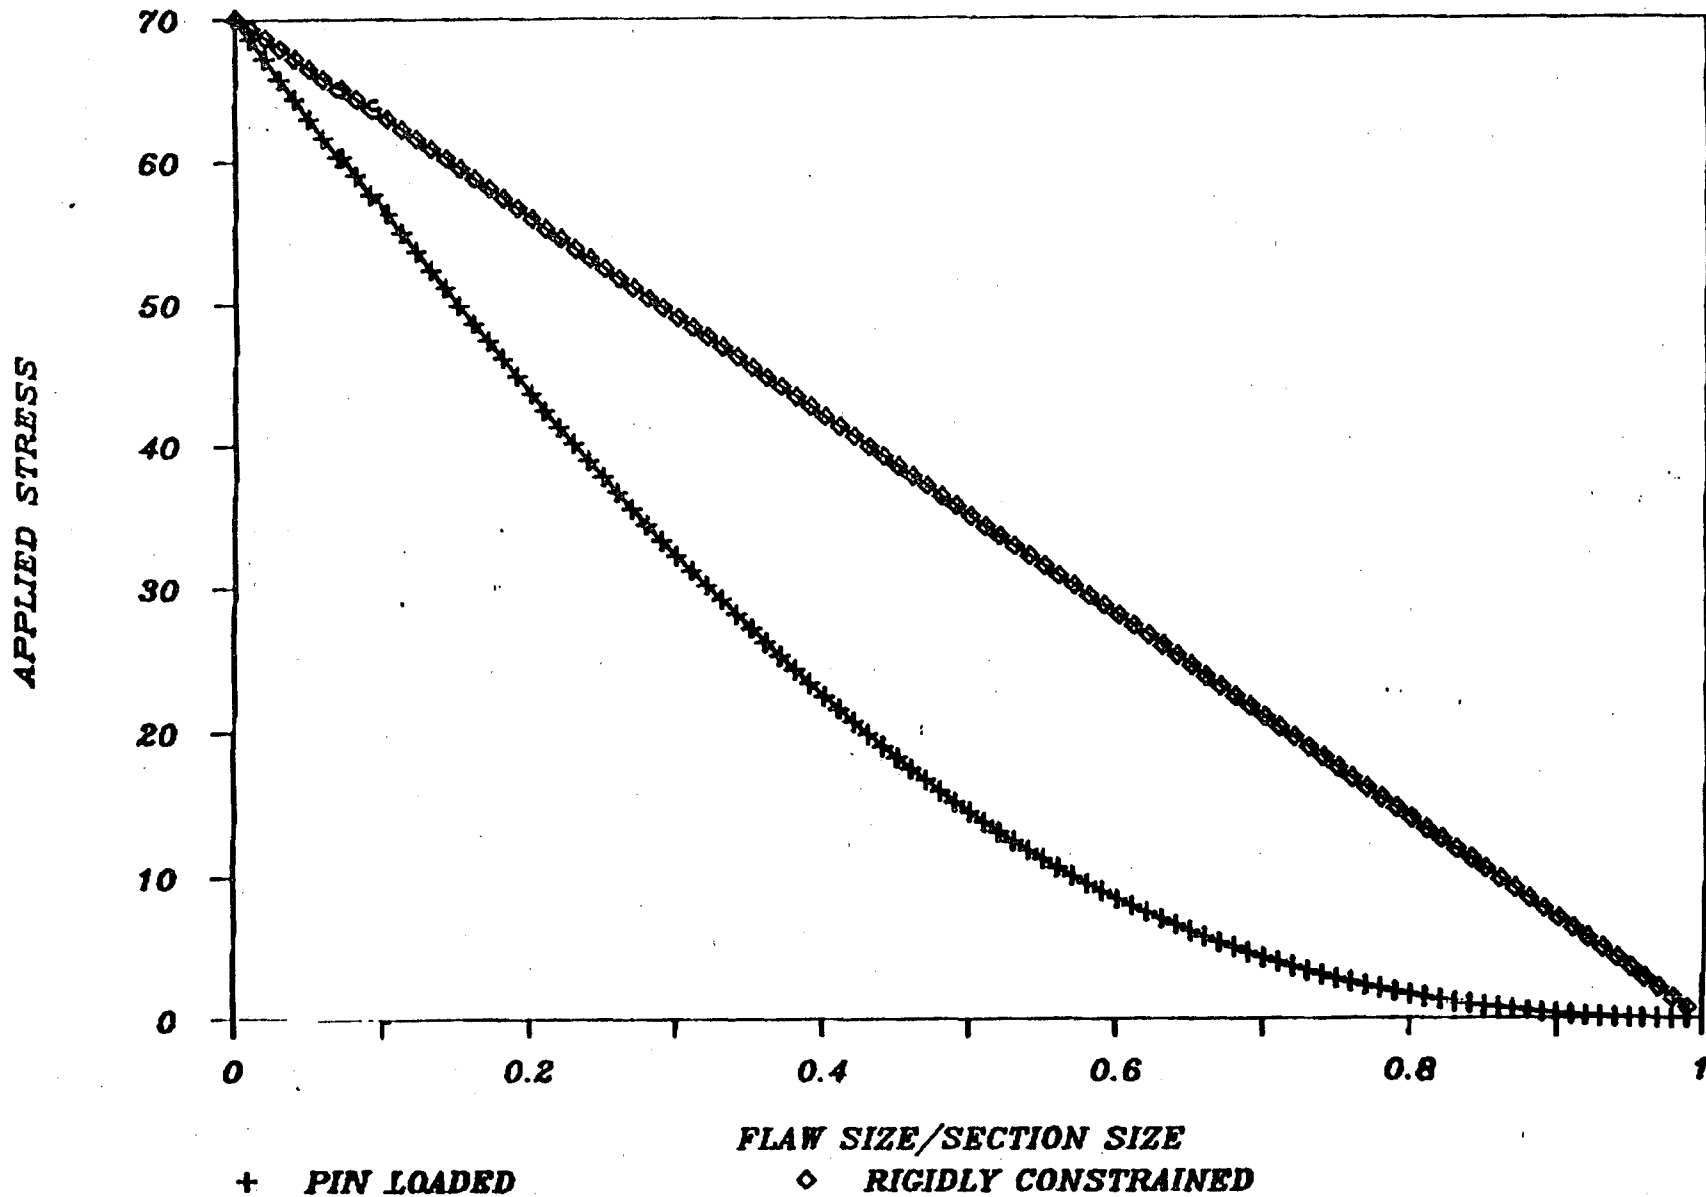


TVA

EDGE CRACKED PANEL

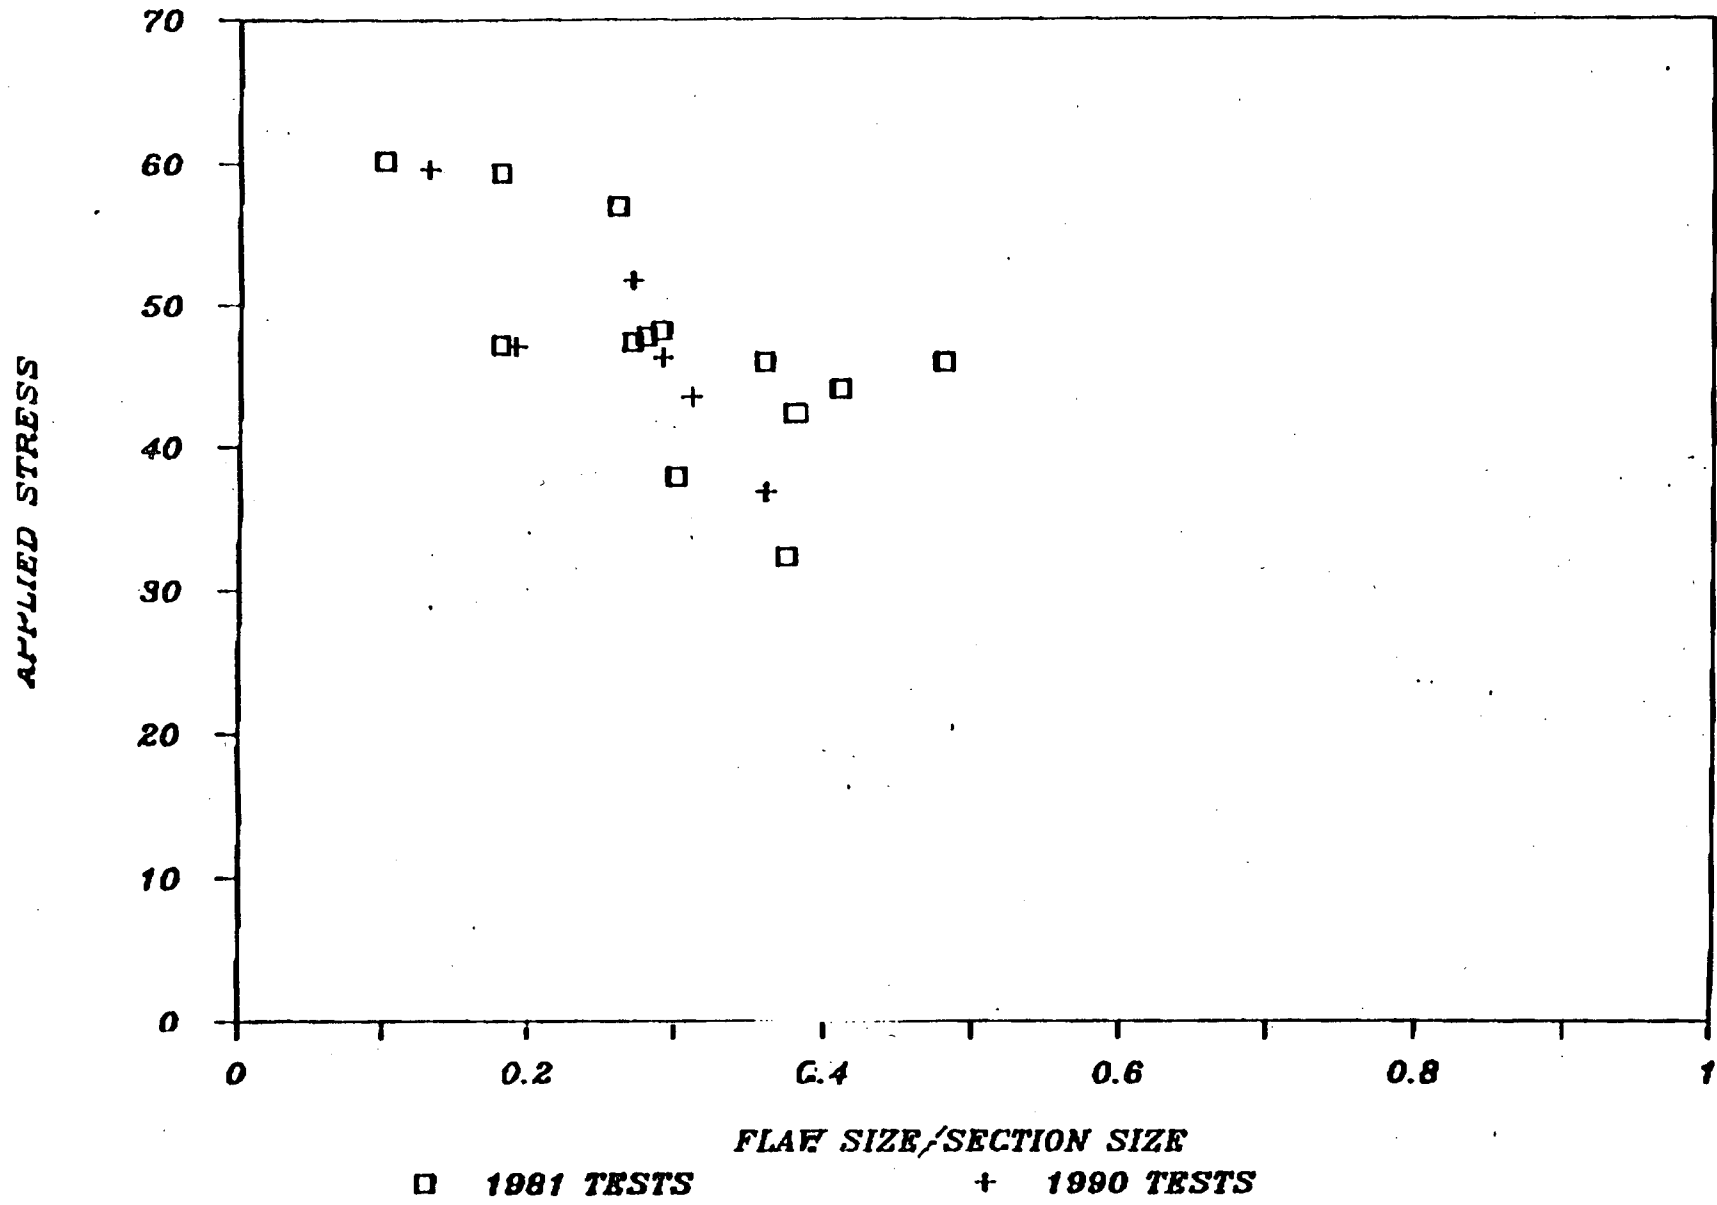

CIRCUMFERENTIALLY CRACKED PIPE

FLOW STRESS = 35 ksi

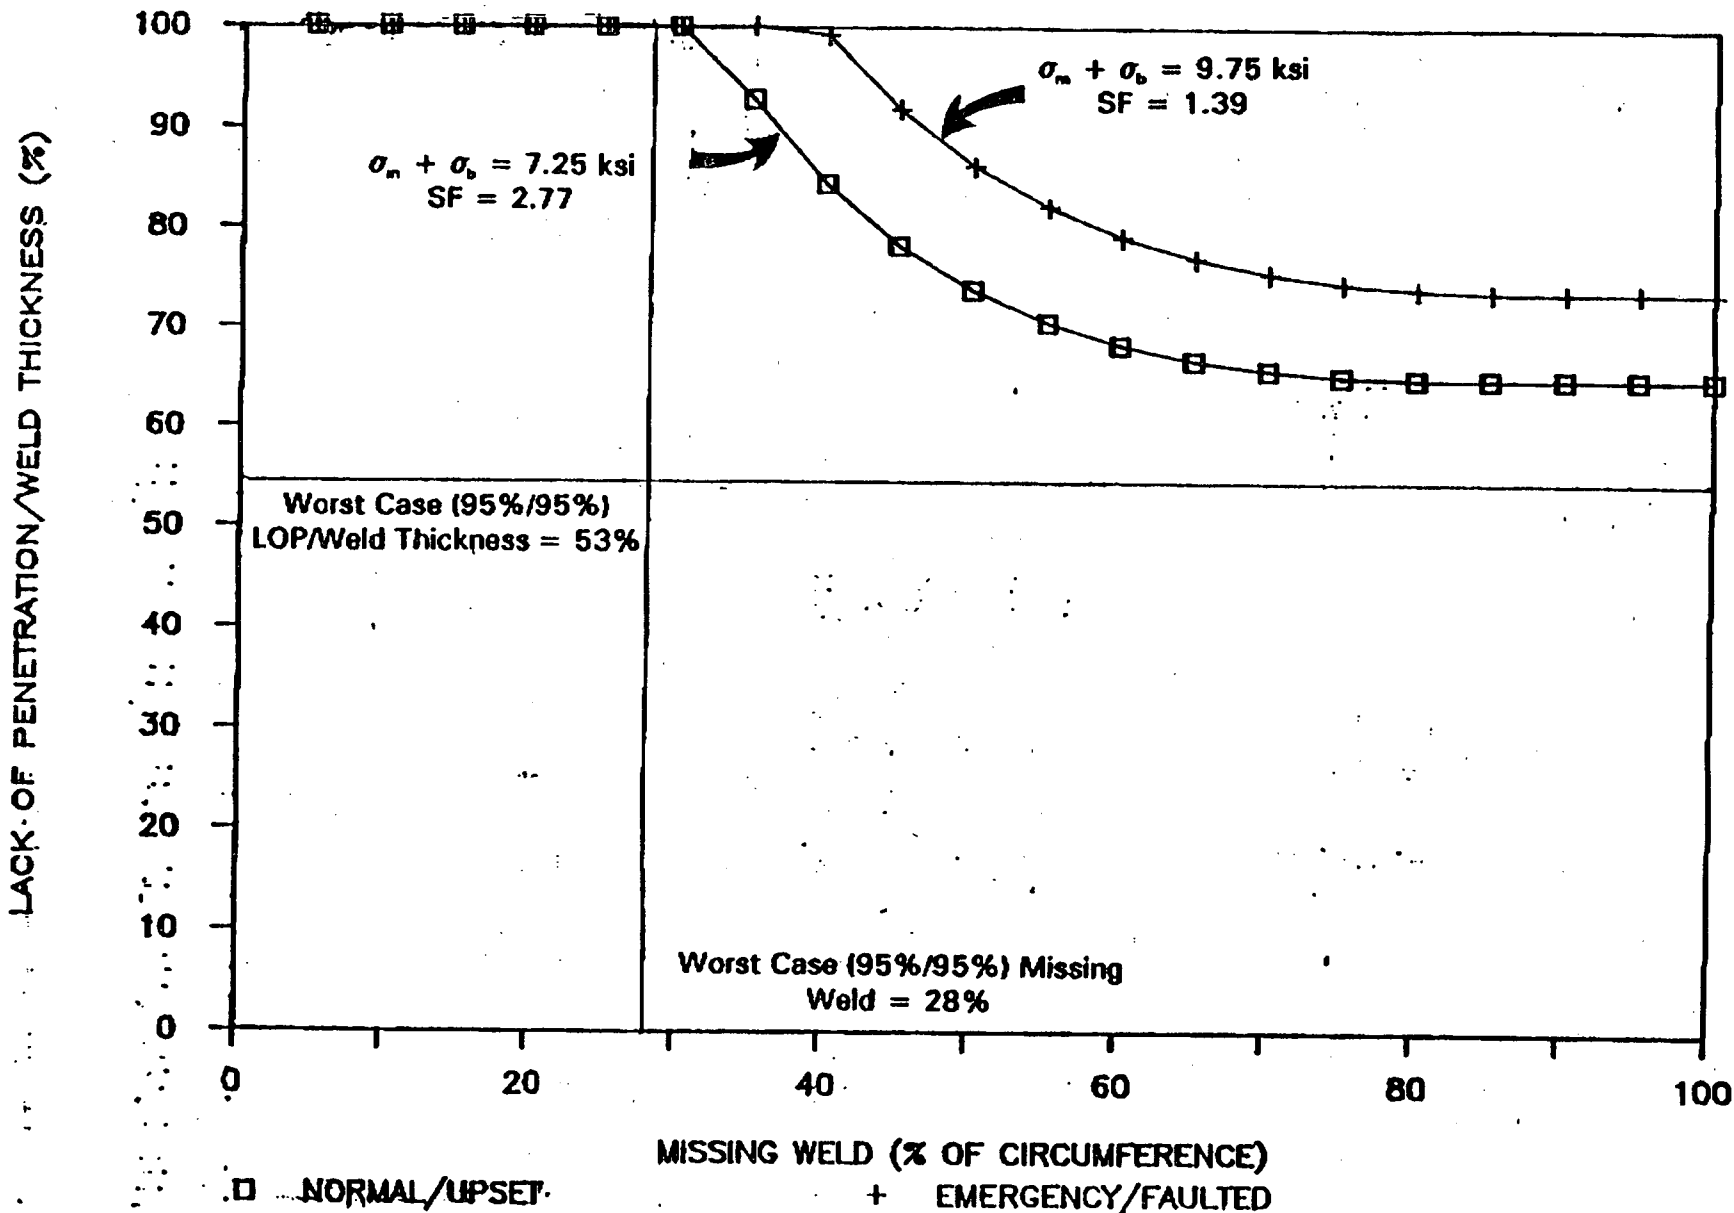

CONCLUSIONS

- SIGNIFICANT MARGINS AGAINST FAILURE STILL RETAINED WITH WORST CASE WELD ATTRIBUTES
- TEST RESULTS CONFIRM THAT PREDICTIVE METHOD IS CONSERVATIVE
- WORST CASE STRESSES FOR OBE AND SSE USED

SUMMARY

- **50.55(e) FINAL REPORT CONCLUDED THE WELDED DUCTWORK WILL PERFORM ITS INTENDED DESIGN FUNCTIONS.**
- **ADDITIONAL TESTING PERFORMED BY TVA AND THE REVIEW OF PREVIOUS RESULTS REAFFIRMED PREVIOUS CONCLUSIONS.**
- **ANALYSIS OF TEST DATA BY APTECH CONFIRMED TVA CONCLUSIONS.**
- **TVA WILL SUPPLEMENT THE 50.55(e) FINAL REPORT ON THIS SUBJECT TO DOCUMENT THE RESULTS OF THIS ADDITIONAL TESTING**
