

Potomac Valley Hospital  
100 Pin Oak Lane  
Keyser, WV 26726

Br 1

Date: December 26, 2008

U.S. Nuclear Regulatory Commission  
Region 1  
Nuclear Materials Licensing Section  
475 Allendale Road  
King of Prussia, PA 19406-1415

03019861

Re: Amendment to License #47-21163-01


To Whom It May Concern:

We have transferred all of our licensed radioactive materials, sealed source and waste, from 167 South Mineral Street, Keyser, WV to the new hospital at 100 Pin Oak Lane, Keyser, WV. We then completed a detailed closeout survey of the 167 South Mineral Street facilities on December 23<sup>rd</sup> and there was no remaining activity or contamination found. The survey meter used was a Ludlum 14C, #204444, with a thin window g.m. detector (model 44-9). The survey meter was calibrated on 5/9/08.

The wipe samples were assayed with a Biodex, AtomLab 930 scaler, #1439014 with sodium iodide probe calibrated 5/9/08, (40% efficiency for C0-57). A copy of the closeout survey is attached for your review.

We request that the 167 South Mineral Street address be removed from our license.

Thank you,



Sincerely,

Michael Makosky  
Administrator

2009 JAN -5 PM 12: 27

RECEIVED  
REGION 1


143178

NUCLEAR MATERIALS-002

Nuclear Medicine  
CLOSEOUT SURVEY/WIPE TEST RESULTS

Date: 12/23/08 Location: Potomac Valley Hospital, 167 S. Mineral Street, Keyser, WV  
 Instruments used: Survey Meter Ludlum 14C, #20444 with 44-9 probe Wipe test Inst. Biodex AtomLab 930 with NaI detector  
 Calibrated: May 9, 2008 Efficiency = 40 % Sensitivity = 92 dpm  
 Survey Performed by: Chris Oberstein RT(R)(M)CNMT Bgnd = 0.02 mr/hr, 28 cpm

Number	Location (see sketch)	mr/hr	dpm/100cm <sup>2</sup>
1	Camera Room Floor	0.02	-79
2	Camera Room Floor	0.02	39
3	Camera Room Floor	0.02	-7
4	Camera Room Floor	0.02	-20
5	Camera Room Floor	0.02	13
6	UPS	0.02	6
7	Camera Room Wall	0.02	32
8	Camera Room Floor	0.02	-7
9	Camera Room Floor	0.02	-14
10	Camera Room Floor	0.02	-53
11	Pt Table	0.02	6
12	Pt Table	0.02	19
13	Pt Table	0.02	-33
14	Camera Room Door	0.02	-46
15	Camera Room Floor	0.02	-33
16	Camera Room Floor	0.02	0
17	Camera Room Floor	0.02	-66
18	Camera Room Floor	0.02	-46
19	Camera Room Floor	0.02	-33
20	Camera Room Wall	0.02	0
21	Computer/Monitor	0.02	-20
22	Camera Room Floor	0.02	19
23	Shipping/Receiving	0.02	-60
24	Camera Room Floor	0.02	-14
25	Camera Room Floor	0.02	-27
26	Camera Room Wall	0.02	26
27	Office Area Floor	0.02	-46
28	Office Area Floor	0.02	-46
29	Office Area Floor	0.02	-14
30	Prep + Storage	0.02	-46
31	Office Area Floor	0.02	-27
32	Office Area Wall	0.02	-33
33	Desk Area	0.02	-60
34	Shelf	0.02	-53

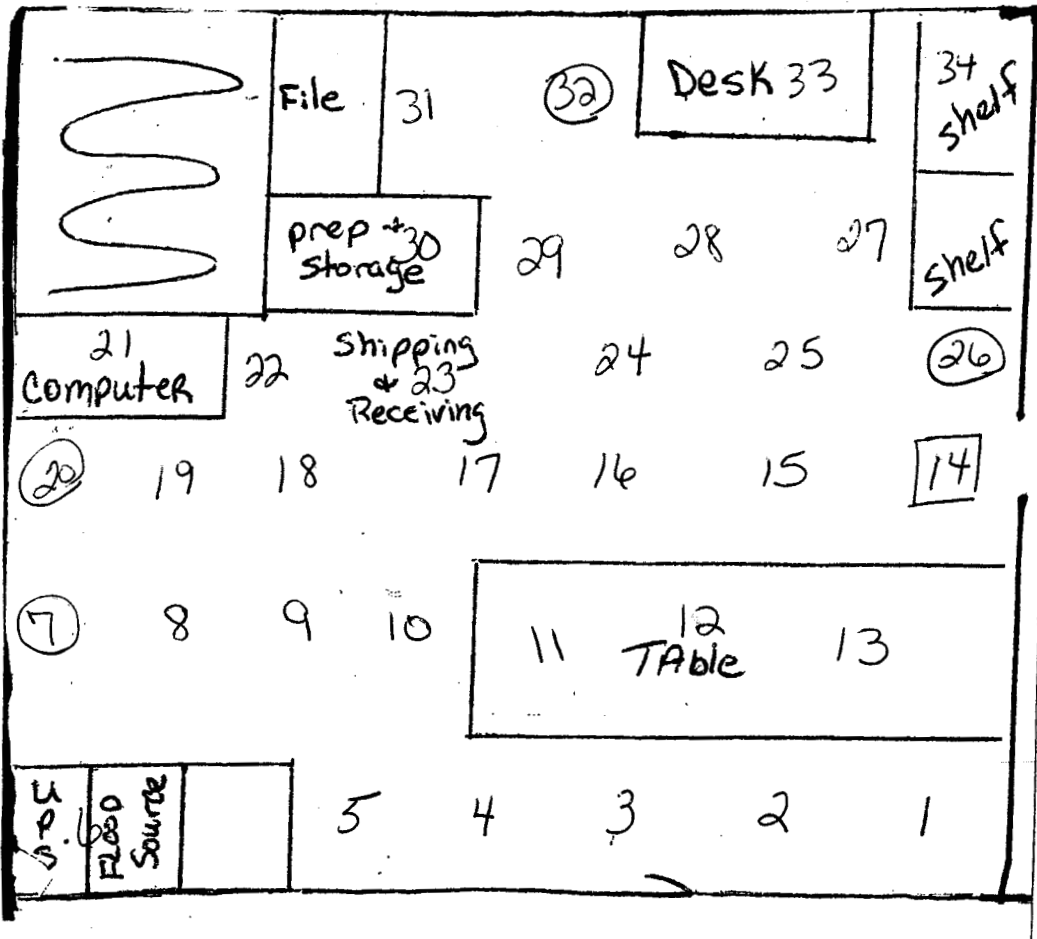

This is to acknowledge the receipt of your letter/application dated

12/26/08, and to inform you that the initial processing which includes an administrative review has been performed.

Approved. 47-21163-C  
There were no administrative omissions. Your application was assigned to a technical reviewer. Please note that the technical review may identify additional omissions or require additional information.

Please provide to this office within 30 days of your receipt of this card

---

A copy of your action has been forwarded to our License Fee & Accounts Receivable Branch, who will contact you separately if there is a fee issue involved.

Your action has been assigned **Mail Control Number** 143178.  
When calling to inquire about this action, please refer to this control number.  
You may call us on (610) 337-5398, or 337-5260.
