APPENDIX B

1R10-001B FACILITY TEST PLAN - QUALIFICATION OF PRIMARY. - CONTAINMENT HYDROGEN/OXYGEN ANALYZERS

8304220564 830420 PDR ADDCK 05000361 PDR

CLASS. LTA. OPERATION | PROGRAM | SECLENCE NO. GEMERAL () ELECTRIC ACV. LIA. SPACE DIVISION PIR NO. - 1510 001 PHILADELPHIA B PROGRAM DEFORMATION REQUEST / RELEASE "USE "C" FOR CLASSIFIED AND "U" FOR U-ICLASSIFIED FALM F. P. Rudek, Program Manager E. Glanfield Off Gas Hydrocon Analyzers Room M4230, VFSC Room N4230 VYSC DATE SENT DATE INFO. REQUINED PROJECT AND REG. NO. REFERENCE DIR. NO. 9/16/74 SUBJECT FACILITIES TEST PLAN - QUALIFICATION OF PRIMARY CONTAINDENT HYDROCEN/CMYGEN AMALYZERS INFORMATION REQUESTED/RELEASED INTRODUCTION

The objective of this test is to subject the primary containment hydrogen and oxygen analyzers to a temperature/pressure profile that will meet the environmental requirements described in GZ-APED Specifications #21A1375, 21A1918, 21A1915 and 21A1796. This will be accomplished by placing the sensor assemblies in a chamber and running a temperature/pressure profile with saturated steam and known concentrations of hydrogen and oxygen for 90 days. Sensor calibration will be checked periodically to verify sensor stability and to verify integrity of the calibration mechanism.

Prior to the temperature/pressure testing, the sensors and/or sensing electrode diffusion barriers under test will be subjected to an integrated dose of 1 x 10 Rad.

Following completion of the 90 day test the sensor (s) will be subjected to additional radiation at a dose, rate of 1 x 10⁵ rad/hr. for a period of 160 hours to complete the prescribed 2.6x10′ Rad. integrated dose.

Abbreviated performance tests will then be conducted as required to insure that the integrity of the system is maintained.

11. GVERALL TEST SHOUENCE

- 1. Abbrevia :ed performance test (if applicable)
- 1 x 10⁷ : ad exposure profile.
 90 day environmental profile.
- 3. 90 day environmental profile
 4. Abbrevia ed performance Tour
- Abbrevia ed performance Test.
 1.6 x 10 Rad exposure on all sensors.
- 6. Abbrevia :ed performance Tast.
- High H₂ concentration exposure test (H₂ sensor only).

*To be performed only if the complete sensor(s) is exposed to 1 x 10 Rad dose.

111. TEST FACILITIES

1. Radiation Testing - Radiation facilities shall be provided that have the capability of providing a garma dose rate of 1.0 x 10 Rad per hour.

	PAGE NO.	ZACTENTION ACCUMACHENTS	
		1 was.	1 2 4 401.
	10-5	- t wes.	C 12 = 11.
B-1			00.07

111. TEST FACILITIES

The initial exposure shall be for an integrated dose of 1 x 10^7 Rad. The final exposure shall be for a total integrated dose of 2.6 x 10^7 Rad per sens

- 2. Abbreviated Performance Test A chamber shall be provided that can mintain 185° +5°F and 95+5% RN for 24 hours. Refer to Figure 1 for a schematic diagram of the required equipment.
- 3. 90 Day Environmental Test Chambers will be used as depicted in Figure 2.
 Adequate bulk head connections shall be provided to permit the necessary
 interconnections including:
 - a. Low voltage instrument lines as required by sensor installation.
 - b. 1/4" copper lines for sensor calibration.
 - c. Thermocouples as required for monitoring sensor body and chamber environmental temperatures.

The chamber shall also have the following interfaces:

- a. Water line: Controlled supply of water for providing the required high humidity conditions for the test.
- b. Pressure gauge (calibrated: 0-100 psia +1.0% full scale).

IV. Test Procedures

Radiation Emposure (Initial)

1 . 15

This test will be conducted with the sensor non-operating and is intended for determination of radiation exposure capability only. The sensor(s) will be placed in a radiation exposure facility exposed to a radiation dose rate of 1 x 10⁵ rad/hr. for a period of 100 hours. (Total Integrated Dose 1 x 10⁷ Rad)

As an alternate to irradiating the complete sensor, membrane material which has been irradiated to the 1 x 10⁷ Rad level at the 1 x 10⁹ rad/nour does rate may be used as the permeation barrier in the sensor assembly to satisfy the pre-environmental test radiation exposure.

2. Abbreviated Performance Test - (24hours). Place the sensor in the test chamber and conduct the initial calibration of the sensor utilizing the calibration and zero gas mixes listed in Table IA or IB as is applicable. The pressure input signal shall be adjusted to the chamber total pressure calibration sequence shall be used to calibrate the sensor. The following readings shall be measured with a D.V.M. connected to the remote indicating meter output terminals. Data also shall indicate the readout of the recorder, panel meter and remote meter where applicable.

NOTE: If temperature compensation is not provided on the sensor a decade box will be employed to simulate the compensation networ:.

- a. Select Span 2 on the sensor electronics panel. Actuate the sensor calibration mechanism using the high calibration gas of the high calibration concentration readout on the instruments. Record the output in the high calibrate block on the data sheet ulated total pressure signal to 30 PSIG and 60 PSIG input levels to the percentage increase of the input signal. Record these outputs on the data sheet. Terminate the high calibration and signal to the 0 PSIG level.
- b. Actuate the sensor calibration mechanism with 100% N₂ and maintain until the instruments indicate 0% on the Span 1 scale and less than 0.1 VDC on the D.V.M.. Record the output in the zero block on the data sheet. Turn off the gas mix at the bottle.
- gas nix after insuring that Span I has been selected on the electronics. When stabilized outputs are obtained, the instruments the output in the low calibrate block on the data sheet. Terminate the low calibration cycle and turn off the gas mixture at the bottle.

After completion of the initial calibration, raise the chamber temperature and RH to 185 ± 5% and 95 ± 5%. Maintain these conditions for the balance of the 24 hour period. Calibration per steps 2a through c above shall be conducted upon stabilization of the sensor output. Calibration checks shall be performed at 5 hour intervals per step 2a through c above except that no further calibration adjustments shall be allowed.

TABLE LA

02 ANALYZER

Normal Environment Low Calibration High Calibration Zero Calibration

Chamber Environment 47. 0₂/N₂ Balance Compressed air

100% N

TABLE 1B

H2 ANALYZER

Normal Environment Low Calibration High Calibration

Chamber Environment 27 H₂/N₂ Balance 42²H₂²7N₂ Balance

- 3. 90 Day Qualification Test
- 3.1 Environmental Profile: (Refer to Figure 2)

Initial Stabilization #(Davs 1 & 2) - 24 hours at 1350 (+50) followed by 24 hours at 200 ± 5°F with a simulated pressure input of 14.7 PSIA. During the 24 hour period, an initial calibration per section IV-2 may be performed if required, however after the first calibration, no further calibration adjustments are allowed. Data shall be recorded on the data sheets as follows:

- 1. Temperature
- 2. Span Adjust knob setting.
- 3. Meter and/or recorder reading.
- 4. Sensor output.
- 5. Simulated prossure signal level.
- 6. Atmosphere being sampled
- 7. Chamber pressure.
- 8. Decade box setting where applicable.**
- 9. Time
- * Stabilization for the purpose of this plan shall mean a change in sensor output of less than 0.1% of full scale in 5 minutes.
- ** NOTE: If temperature compensation is not provided on the sensor a decade box will be employed to simulate the compensation nerwork.
- 3.2 Simulated LCCA (Day 3) Increase the chamber temperature to 340 ± 10° r and pressure to approximately 62 PSIG using steam. Maintain this condition for 15 minutes, and then vent the test chamber until the pressure reaches 35 PSIG. Maintain this condition (340° r ± 10° and 35 PSIG) for three hours. Record test data as per paragraph 3.1 then decrease the temperature according to the next paragraph.

Decrease the chamber temperature to 200 ± 10°F and allow the system to stabilize. If a decade box is used to simulate the temperature compensation network, adjust to the setting used prior to the 340°F excursion and record data as per paragraph 3.1. Maintain these conditions for a minimum of 3 hours after which data should be recorded and the chamber vent valve should be opened to return the chamber to atmospheric pressure (If it is not already there). Close the vent valve and mintain these conditions (200 ± 10°F, 14.7 psia) for a minimum of six hours and then proceed to the long term stabilization portion of the test program.

NOTE: If the performance of either of the sensors appears unusual during or after 340°F exposure the chamber should be cooled and the sensors removed and inspected. Sensors determined to be good (exhibiting no leakage) shall be reinstalled in the test chamber and testing shall continue. Sensors found to be defective shall be removed from the test and a failure analysis shall be conducted.

- 3.3 Long Term Stabilization (Davs 4 through 90) Chamber conditions shall be established at 200 + 10°F with a simulated pressure signal of 0 PSIG. These conditions shall then be maintained for the balance of the 90 day test cycle. Calibration checks per IV-2 a through c above shall be performed at a minimum of once per 120 hours. Adjustments required after the initial calibration cycle under these conditions shall be recorded and discussed with cognizant BWRO personnel. Record outputs in the appropriate blocks on the data sheet.
- 3.4 Radiation Exposure (Final) This test is conducted on a non operating sensor in a manner similar to that described in Paragraph IV-I except that the time of exposure to the 1 x 10⁵ rad/hour dose rate will be 160 hours.
- 3.5 <u>High H. Concentration Exposure</u> After completion of the post radiation Abbreviated Performance Test, the H₂ sensor shall be tested in a hydrogen/nitrogen atmosphere at 200°F. This atmosphere shall be a mix greater than 52 H₂. Record the sensor outputs, gas concentration and chamber temperature.

V. DATA & REPORTING

Standing Instructions will be prepared for each test sequence by GE Quality Assurance. Data sheets will be included.

A final qualification test report will be written at completion of all testing.

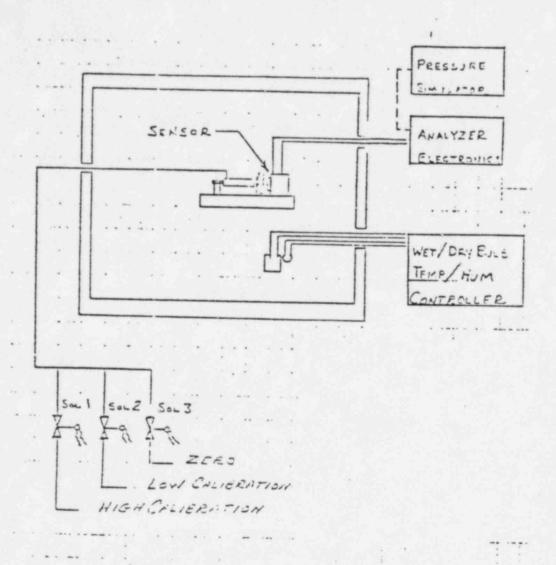


Figure 1. H_2/O_2 Containment Sensor Acceptance Test System Arrangement

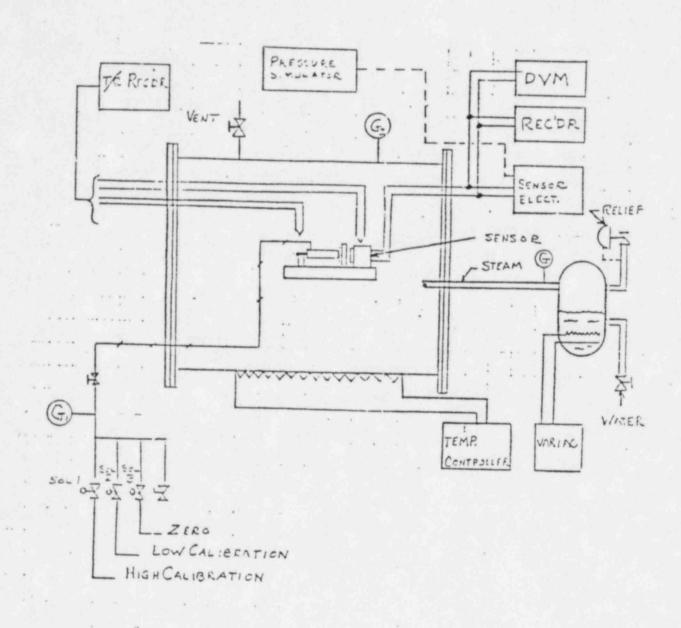


FIGURE 2. H2/02 CONTAINMENT SENSOR TEMP., PRESS., HUM., TEST SYSTEM

\$023-508-17-18-0
