9-223

NMC
Committed to Nuclear Excellence

FEEL THE POWER
JOURNEY OF EXCELLENCE
POINT BEACH • U1R28

Point Beach Nuclear Plant
U1R28
OCC Interactive Turnover

Meeting Agenda
Saturday, May 15, 2004

Start Time: **1800** **NSB Cafeteria**

ATTENDEES
Shift Outage Directors
Shift Outage Managers (SOM)
Operations Coordinators (SOC)
Maintenance Coordinators (MOC)
Engineer / Projects Coordinators (EOM)
Rad Protection Manager (RPM)
Site Safety Coordinator (SSC)
Shutdown Safety Assessor (SSA)
Site Management (SSM)
General Supervisors
First Line Supervisors

Agenda
1. Safety Issue Discussion (SSC)
2. Radiation Protection (RPM)
3. Operations Coordinator Turnover (SOC)
4. Shutdown Safety Assessment (SSA)
5. Maintenance Coordinator Turnover (MOC)
6. Engineering Coordinator Turnover (EOM)
7. Major Projects Update (EOM)
8. Schedule Review (SOM)
9. Management Expectations (SSM)
10. ACEMAN Assessment Results (SOM)
11. Shift Goals (SOM)

Items Included in Daily Package:
- Site Communication
- Safety Snippet
- Outage Alara Report
- Outage Status Report
- Shutdown Safety Assessment
- ~~Defined Critical Path~~ Not available 5/15/04
- Work Activity Risk Assignment
- Outage Schedule

BRIEFING NOTES

21-96

Information in this record was deleted in accordance with the Freedom of Information Act, exemptions 4
FOIA/PA-2004-0282

NMC
Committed to Nuclear Excellence

FEEL THE POWER
JOURNEY OF EXCELLENCE
POINT BEACH • U1R28

Point Beach Nuclear Plant
U1R28 Refueling Outage

Safety Topic for week of May 9-15
Theme for the week
This week's theme covers Emergency Situations. Be it weather, fire or a medical emergency, are we ready to respond to those unexpected situations?
Daily Safety Snippets
Sunday
"You would be shocked if you found your emergency egress path blocked"
Material is beginning to come out of containment as a lot of work is wrapping up. Don't pile up tools and equipment in the walkway even for short periods of time. Always keep the egress paths open for use.
Monday
"If strong winds start to blow, do you know where to go?"
Do you know the proper location to go in the event of a tornado warning if you are in the trailers, turbine hall or PAB? NP1.9.21 covers the site's various shelter areas. Plan ahead and take the time now to review the NP with your group.
Tuesday
"Make sure to cleanup or a fire may start during heat up.
OE15310 Indian Point 3 – An oil vapor extractor for the main boiler feed pump failed. The tag out used to repair the extractor resulted in an increased leakage of oil from the pump bearings onto lagging. A special log was created to monitor the leakage, but no plan existed for dealing with the safety hazards. Maintenance repaired the extractor, returning it to service. The next day a portion of oil soaked lagging on a main boiler feed pump caught fire and was quickly extinguished by an alert watchstander.
Wednesday
"Take heed - Don't block emergency equipment you may need."
Last week on the 66ft of containment, the NRC noticed we blocked access to 2 fire extinguishers mounted on the stairwell handrail. A scaffold was built in the area that made access questionable. We then added a number of bags of insulation it made access impossible. Just a question – Why is the NRC finding this instead of us? .
Thursday
"What number do you call if your co-worker takes a serious fall?"
What is the plant's emergency number? 2911. This number is only to be used for emergency situations. Two weeks ago a work group was having trouble getting through to operations to communicate a change in equipment status. Rather than waiting, the individual involved decided to contact the control room via the emergency number. Needless to say this was not an appropriate use of 2911.
Friday
"Make sure your fire watch is alert to keep someone from getting hurt"
OE12607 – LaSalle – A worker using an acetylene torch for cutting through a structural member that was behind a metal wall panel. Wall insulation behind the member began to burn. The alert fire watch extinguished the fire within one minute of it beginning and no significant damage occurred.
Saturday
"Debris buildup may result in an unplanned heat up"
OE14899 River Bend Station – A small fire occurred under the exhaust piping on a diesel generator during testing. The fire was observed during routine checks of the generator and the control room was immediately notified. The control room unloaded the generator while the operator extinguished the fire. The cause was insulation debris that accumulated around the hot piping over time.

Point Beach Nuclear Plant Outage 1R28

DAY 41

Supporting Operational Excellence

Outage Radiation Performance

Path

Picture

Meets

Doesn't Meet Exceeds

Definition/Goal

This indicator measures cumulative dose radiation exposure and total number of personnel-contamination events (PCE's > 5000 cpm) during refueling outages. The dose indicator is measured in Rem and individual PCE events.

Meets:	**<=75 Rem**	**Actual Cum.**	
Exceeds:	**<=71 Rem**	**Dose:**	**55.049 Rem**
Meets: <= 18	**Exceeds: <= 12**	**Actual PCE's:**	**9**

Responsible Manager/Owner

Stu Thomas

Analysis and Actions

Day 41 - May 14
Actual = 0.169
Cumulative = 55.049
Cumulative Forecast = 55.131

Daily PCE goal reforecast on 4/23. Daily dose reforecast on 5/8/04.

Reactor Head Repair Dose for May 14th is 1.328 vs. goal of 2.430.
RV Head Total Dose is 10.354.

Personnel Contamination Events

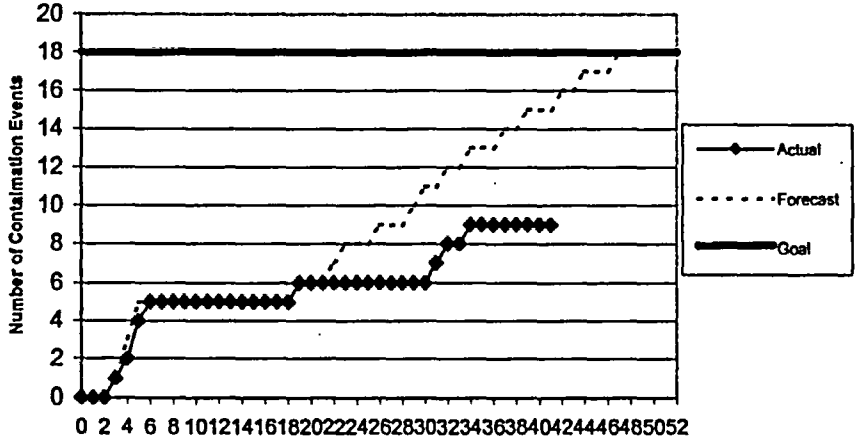

Cummulative Dose Exposure

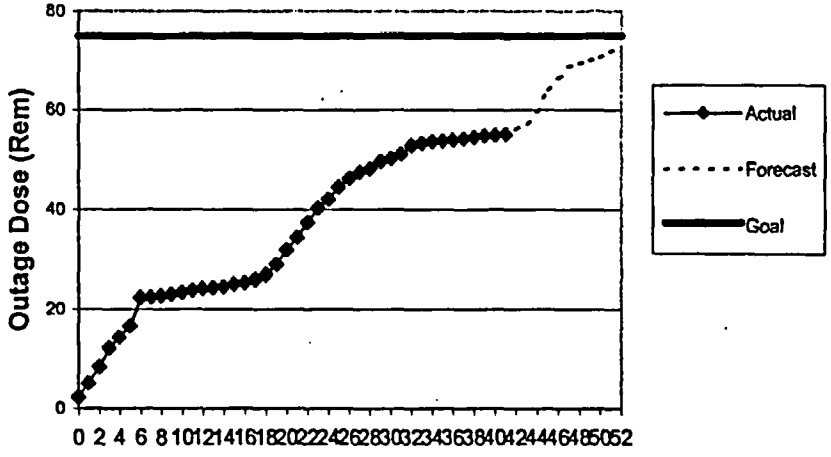

NMC
Committed to Nuclear Excellence

Outage Status Report

Plant: Point Beach Unit 1 **Day:** Saturday **Today's Date / Time:** 5/15/04 1600

Outage Duration: Day 42 Of Refueling Outage Number U1R28

Safety Status

Industrial - Within the last 12 hours

OSHA Recordables 0 First Aid cases 0 Near misses 0

Total for this outage 1

Summary:

Radiological

Dose to date 55.049 Projected to date * 55.131 Outage Goal ≤75 R

Difference -.082 * Reforecast on 5/8 Number of PCEs 9

Summary: Reactor Head Repair Dose for May 14th is 1.328 vs. goal of 2.430. RV Head Total Dose is 10.354.

Nuclear

Significant human performance errors and events in last 24 hours 0

Summary:

Plant Status

Mode: ☐ Hot Standby *(Mode 3)* ☐ Hot Shutdown *(Mode 4)* ☐ Cold Shutdown *(Mode 5)* ☒ Refueling Shutdown *(Mode 6)*

RCS: Temperature: 81 Pressure: Vented to Atmosphere RV Level: Rod Latch Height

Time to Boil: 30 hours

4x4

Shutdown Safety Assessment Protected Equipment:

Major Activities Completed in Last 24 Hours	Critical Path and Near Critical Path Activities (Next 24 Hours)
• Containment Spray Restoration	• Complete Cooldown & Final NDE of Reactor Head Repair Area
• Upper Internals Lift Rig Paint Stripping	• Upper Internals Lift Rig NDE
• Respond to Unit 2 Reactor Trip	• Secondary Systems Recovery
	• U2 Reactor Trip Recovery

Significant Outstanding Issues

Date	Issue	Due	Responsibility
5/03/04	Reactor Vessel Head Repair Penetration #26	5/16/04	John Walsh
5/13/04	1P-1A RCP Motor Oil	5/15/04	Dan Laing
5/14/04	T-26 Steam Generator Blowdown Tank	5/17/04	Scott Manthei

Upcoming Major Milestones

	Scheduled		*Actual*			*Scheduled*		*Actual*	
	Date	Time	Date	Time		Date	Time	Date	Time
Cooldown <200°	4/03/04	2100	4/03/04	2230	RCS Fill & Vent	4/23/04	1500		
Head Lift	4/09/04	0900	4/21/04	1550	Heatup >200°	4/25/04	0900		
Refueled	4/14/04	0300	5/02/04	1848	Reactor Critical	4/28/04	0800		
RV Headset	4/18/04	1900			On-Line	4/30/04	0100		

PBNP SHUTDOWN SAFETY ASSESSMENT AND FIRE CONDITION CHECKLIST

OUTAGE SAFETY ASSESSMENT

UNIT: 1 DATE: May 15, 2004 TIME: 1530

KEY SAFETY FUNCTIONS:

REACTIVITY:	GREEN
CORE COOLING:	GREEN
POWER AVAILABLE:	GREEN
INVENTORY:	GREEN
CONTAINMENT:	YELLOW
SFP COOLING:	NA

PROTECTED EQUIPMENT:

COMMENTS:

RCS Time to Boil is 30 hours. Using NP 10.3.6 Time To Boil curves.
Fire Protection Condition IV: Credit is taken for fire rounds as fire prevention contingency

ex4

Run Date 15MAY04 14:11

Work Activity Risk Assignment

U	ACT ID	WO ST	GRP	HPE RISK	EQUIPMENT	Activity Description	Cal ID	DUR	START	FINISH
CONSTRUCTION ENG - L. GAUTHIER										
1	CEI600R027	76	CE8	DR-Y ML-Y ORT3-Y R-M	R-1	48 HOUR COOLDOWN OF REPAIRED AREA	1	10	13MAY04 22:00A	15MAY04 21:59
1	CEI600R029	76	CE8	DR-Y ML-Y ORT3-Y R-M	R-1	FINAL NDE OF REACTOR HEAD REPAIR AREA	1	12	15MAY04 22:00*	16MAY04 09:59
1	CEI600G020	76	CE8	DR-Y ML-Y ORT3-Y R-M	R-1	SETUP AND PREPARE MOCKUP FOR NOZZLE	1	45	16MAY04 10:00*	18MAY04 06:59
1	CEI600R049	76	CE8	DR-Y ML-Y ORT3-Y R-M	R-1	P-26 - REMOVE NOZZLE EXTENSION	1	2	16MAY04 10:00	16MAY04 11:59
1	CEI600R050	76	CE8	DR-Y ML-Y ORT3-Y R-M	R-1	P-26 - CHAMFER GRIND	1	4	16MAY04 12:00	16MAY04 15:59
1	CEI600R055	76	CE8	DR-Y ML-Y ORT3-Y R-M	R-1	PREP TO INSTALL THERMAL SLEEVE AT P-26	1	5	16MAY04 16:00	16MAY04 20:59
1	SDI600G010	76	CE8	DR-Y ML-Y ORT3-Y R-M	R-1	REVISE PACKAGETO GRIND OUT OVERLAP	1	72	17MAY04 07:00*	20MAY04 06:59
1	SE-I600-A	76	CE8	DR-Y ML-Y ORT3-Y R-M	R-1	SR MGMT DECISION TO GRIND OVERLAP	1	0	17MAY04 12:00*	
ELECTRICAL MAINTENANCE										
1	EM0215224	76	EM	DR-N ML-N ORT3-N R-M	W-003B-M	PERFORM MCE W-003B-M	1	4	16MAY04 13:00*	16MAY04 16:59
I&C - C. RHODEN & R. YOUNG										
1	IC5.11TMGA	76	IC1	DR-Y ML-Y ORT3-N R-M	ICP-05.011	CHECK TAVG HIGH SELECTOR	D	3	16MAY04 08:00*	16MAY04 10:59
1	IC2.19	76	IC1	DR-N ML-N ORT3-N R-M	ICP-02.019	ICP 2.19 SAFEGUARDS LOGIC TEST	5	6	17MAY04 06:00*	17MAY04 11:59
OPERATIONS										
1	ORT-006	77	OPS	DR-N ML-N ORT3-N R-M	O-RT-006	ORT 6 CS SEQUENCE	1	6	16MAY04 08:00*	16MAY04 13:59

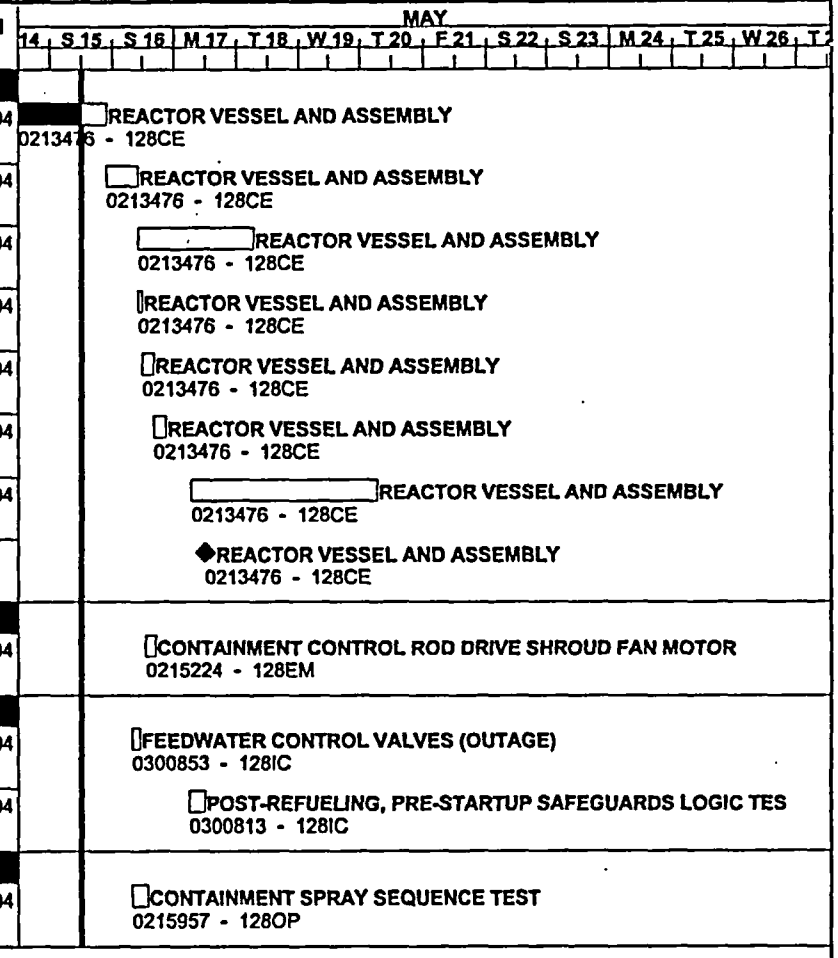

Early Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

NMC / WE
PBNP U1 Refueling 28 Outage

LT-81 HUMAN ERROR RISK BARCHART
FL-81 HUMAN ERROR POTENTIAL

U1R28 WORKING SCHEDULE

after 15MAY04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF
APPLETON METERING GROUP											
1	1	AP0215127B	APM	76	X-01-A	I X-01-A PERFORM CAL OF SUDDEN PRESSURE RELAY	1	15MAY04 09:00A	15MAY04 12:59	DR-N ML-N ORT3-N R-N	0
2	1	AP0215128	APM	76	X-01-B	X-01-B - INSPECT CAL AND SET	16	15MAY04 13:00	17MAY04 10:59	DR-Y ML-Y ORT3-N R-N	0
3	1	AP0215129	APM	76	X-01-C	X-01-C - INSPECT CAL AND SET	16	17MAY04 11:00	19MAY04 08:59	DR-Y ML-Y ORT3-N R-N	0
APPLETON RELAY GROUP											
4	1	AP0303688	APR	76	A-01	CALIBRATE 1A-01 NON-TECH SPEC RELAYS	52	11MAY04 08:00A	21MAY04 09:59	DR-N ML-N ORT3-N R-N	225
5	1	AP0215122	APR	76	A52-04	P-1A UNDERFREQ. RELAY FUNCTIONAL TEST	6	17MAY04 12:00	18MAY04 08:59	DR-N ML-N ORT3-N R-N	0
APPLETON STATION GROUP											
6	0	L151OOS-3	APS		F52-151	LINE 151 OUT OF SERVICE (SECOND TIME)	7*	14MAY04 07:00A	15MAY04 18:59	DR-N ML-N ORT3-N R-N	0
7	0	ATC151-3	APS		F52-151	ATC WORK AT NORTH APPLETON SUB STATION	5	14MAY04 08:00A	15MAY04 16:59	DR-N ML-N ORT3-N R-N	0
8	0	L151SI-3	APS		F52-151	SWITCHING LINE 151 IN	2	15MAY04 17:00	15MAY04 18:59	DR-N ML-N ORT3-N R-N	180
9	1	AP0215099	APS	76	F89-112	SPECT/CLEAN/LUBRICAT OPERATOR	3	17MAY04 08:00	17MAY04 10:59	DR-N ML-N ORT3-N R-N	0
10	0	AP0304870A	APS	76	H52-DHPVR-	DELIVER H52-05 TO MAINTENANCE SHOP	6	17MAY04 08:00	17MAY04 13:59	DR-N ML-N ORT3-N R-N	0
11	1	AP0215099A	APS	76	F89-112	STROKE OPERATOR DURING TAGGING EVOLUTION	1	17MAY04 11:00	17MAY04 11:59	DR-N ML-N ORT3-N R-N	162
BOP MECHANICAL ENGINEERING											
12	0	BM307011SS	BMS		D-105	COLLECT AIR FLOW DATA (DOOR CLOSED)	3	17MAY04 08:00*	17MAY04 10:59		695
CONSTRUCTION ENGINEERING GROUP											
13	0	CE0310577	CE	76	Z-065A	Z-65A INSTALL MR 03-044	40	10MAY04 07:00A	21MAY04 14:59		131
14	0	CE0311772	CE	76	Z-065A	Z-65A INSTALL HEAT TRACE - MR 03-044	40	10MAY04 07:00A	21MAY04 14:59		131
15	0	CE307011SS	CE	76	D-105	PRE-JOB BRIEF D-105 REPLACEMENT	4	17MAY04 07:00*	17MAY04 10:59	DR-N ML-Y ORT3-N R-N	0
16	0	CE0307011A	CE	76	D-105	PRE-STAGE EQUIPMENT FOR D-105 REPLACEMENT	8	17MAY04 11:00*	18MAY04 10:59	DR-N ML-Y ORT3-N R-N	16

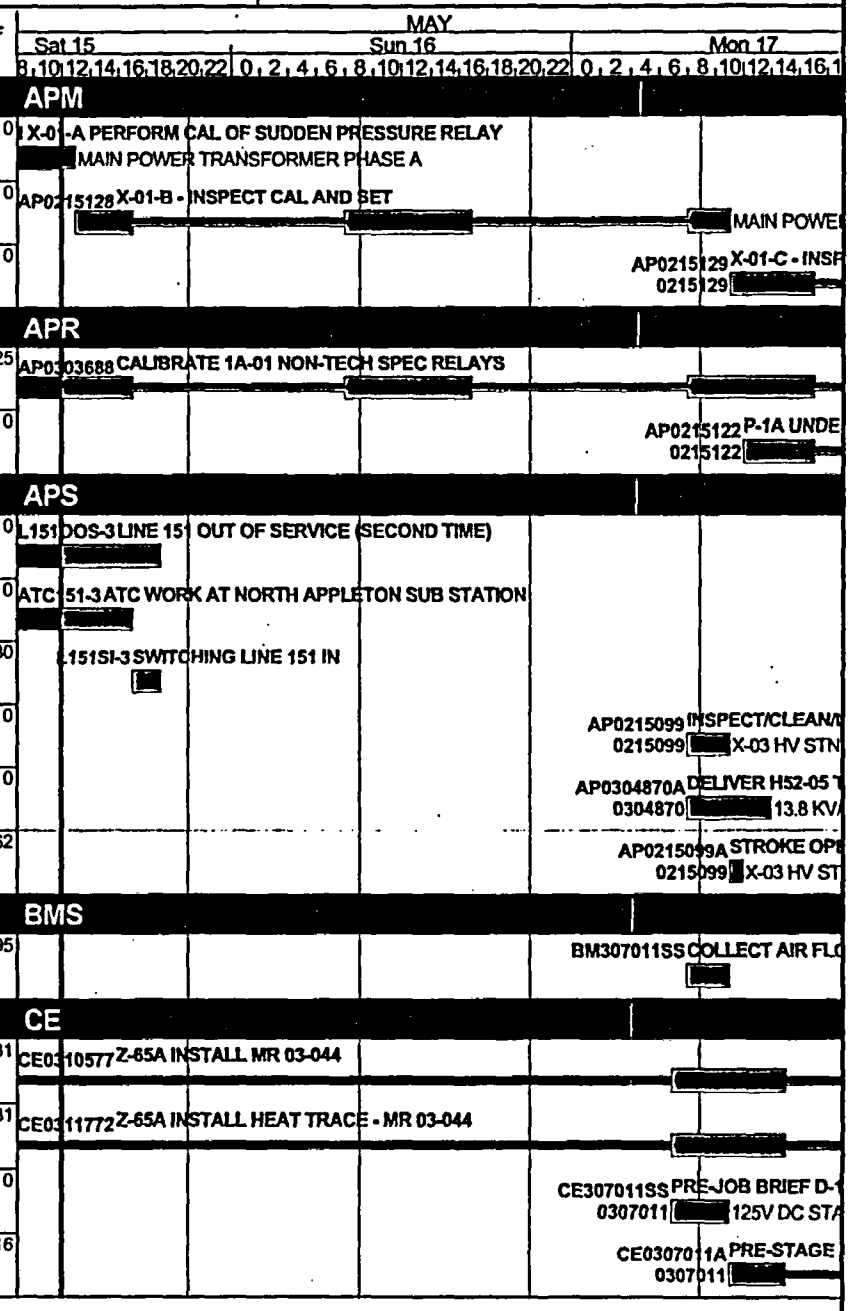

© Primavera Systems, Inc.

LT-03 STANDARD PUBLICATION
FL-03 Execution Publication Set

U1R28 WORKING SCHEDULE

after 15MAY04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF
CONSTRUCTION ENG - K. GRASSO											
17	0	CE0306041	CE1	76	INTAKE CRI	INSPECT CRIB, INSTALL BUOYS AND FISH	12	05APR04 10:00A	17MAY04 13:59	DR-Y ML-Y ORT3-Y R-N	246
INSULATION - NPS - D. CHERNEY											
18	1	CE30000TI	CE3	76	TG-01-T	ENCAPSULATE INSULATION ON HP	10	01MAY04 12:00A	17MAY04 16:59	DR-Y ML-Y ORT3-Y R-N	201
19	1	CE26TOHTI	CE3	77	IST-SISI	REINSULATE - FAC PROG - TURB HALL 26	72	04MAY04 20:00A	21MAY04 14:59	DR-Y ML-Y ORT3-Y R-N	267
20	1	CE44CGATI	CE3	76	INSUL-MS	REINSULATE - FAC PROG - CTMT 44 FT GEN	35	12MAY04 17:00A	16MAY04 22:59	DR-Y ML-Y ORT3-Y R-N	16
21	0	CE309512TI	CE3	77	SERVICE	INSTALL INSULATION 1SW-2861	2	13MAY04 20:00A	15MAY04 20:59	DR-Y ML-Y ORT3-Y R-N	169
22	1	CE44TGATI	CE3	77	IST-SISI	REINSULATE - FAC PROG - TRB HALL 44 FT	23	17MAY04 15:00*	18MAY04 21:59	DR-Y ML-Y ORT3-Y R-N	212
SCAFFOLDING - NPS - J. HAESE											
23	1	CE26TOHSR	CE4	77	IST-SISI	REM SCAFF - FAC PROG - TURB HALL 26 FT	23	01MAY04 09:00A	17MAY04 14:59	DR-Y ML-Y ORT3-Y R-N	355
24	1	CE08TOHSR	CE4	77	IST-SISI	REMOVE SCAFF - FAC PROG - TURB HALL 8 FT	32	05MAY04 10:00A	18MAY04 22:59	DR-Y ML-Y ORT3-Y R-N	211
25	1	CE215202SR	CE4	76	P-001A-M	REMOVE SCAFFOLDING FOR P-1A-M	4	15MAY04 18:00*	15MAY04 21:59	DR-Y ML-Y ORT3-Y R-N	276
26	1	CE408152SR	CE4	87	SC-00955-O	REMOVE SCAFFOLDING FOR SC-955-O	5	15MAY04 18:00*	15MAY04 22:59		244
27	1	CE66C001SR	CE4		P-001B-M	REMOVE SCAFFOLDING FOR B RCP MOTOR	10	16MAY04 10:00	16MAY04 19:59	DR-Y ML-Y ORT3-Y R-N	151
28	1	P1402-SR	CE4	77	Z-022	REMOVE SCAFFOLDING - Z-22 INTERNALS LIFT	10	17MAY04 06:00*	17MAY04 15:59	DR-Y ML-Y ORT3-Y R-N	0
29	1	CE300867SR	CE4	76	ICP-05.047	REMOVE SCAFFOLDING FOR ICP 5.47	4	17MAY04 07:00	17MAY04 10:59	DR-Y ML-Y ORT3-Y R-N	239
30	1	CE933444SR	CE4	76	W-001C2-A	REMOVE SCAFFOLDING FOR W-1C2-A	5	17MAY04 14:00	17MAY04 18:59	DR-Y ML-Y ORT3-Y R-N	231
31	1	CE44CGASR	CE4	77	IST-SISI	REMOVE SCAFFOLDING FOR FAC PROG	4	17MAY04 15:00	17MAY04 18:59	DR-Y ML-Y ORT3-Y R-N	231
32	1	CE213968SR	CE4	82	TG-01-G	REMOVE SCAFFOLDING FOR MAIN GENERATOR	5	17MAY04 15:00	17MAY04 19:59	DR-Y ML-Y ORT3-Y R-N	0
CONSTRUCTION ENG - G. GOZDZIALSKI											
33	1	CE0407589C	CE5	76	T-026	T-026 - BD TANK PIPING / INPINGMENT PLATE	4	07MAY04 07:00A	15MAY04 15:59	DR-Y ML-Y ORT3-Y R-N	2

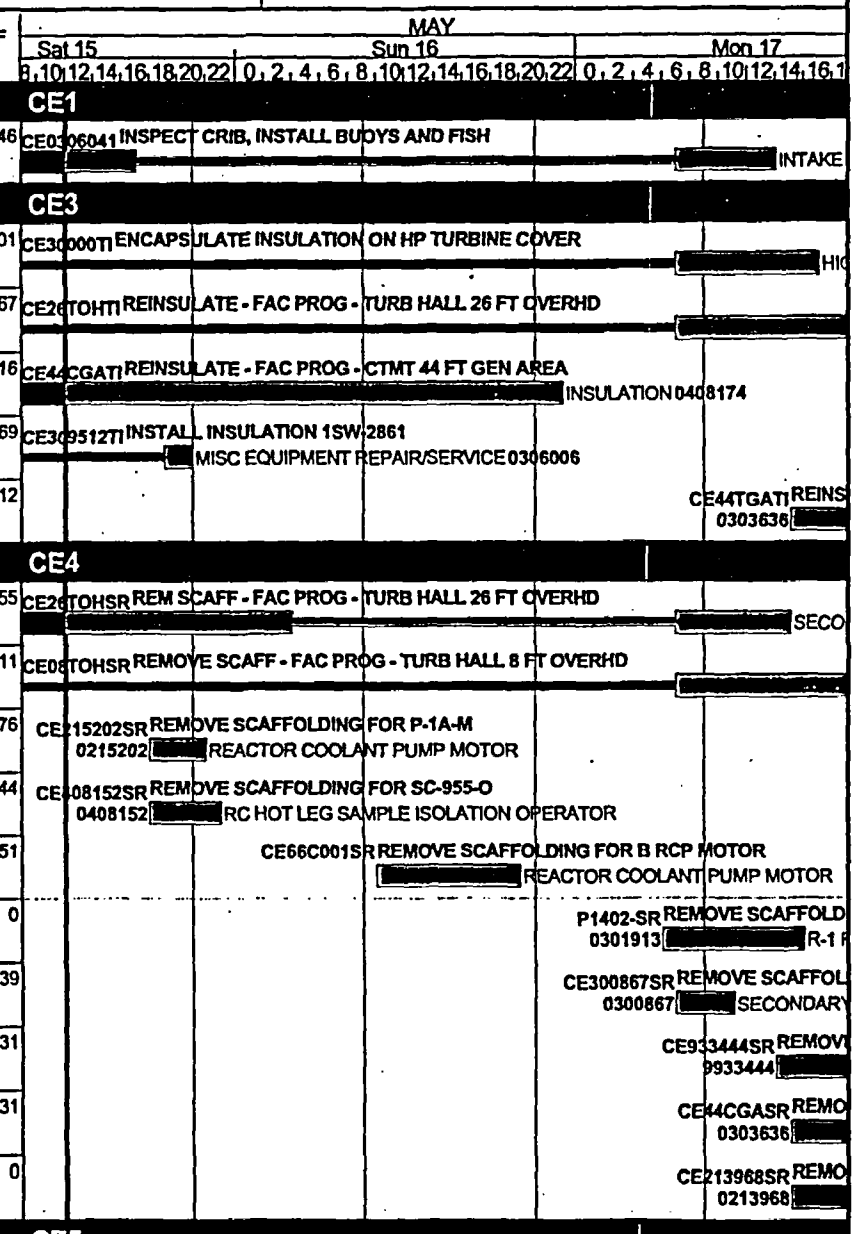

© Primavera Systems, Inc.

U1R28 WORKING SCHEDULE

after 15MAY04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF
CONSTRUCTION ENG - G. GOZDZIALSKI											
34	1	CE9929774	CE5	77	Z	INSTALL/MOD PLATFORMS	27	10MAY04 10:00A	20MAY04 09:59	DR-Y ML-Y ORT3-Y R-N	49
35	1	CE9933444	CE5	82	W-001C1	W-1C2-A, RE-WELD DAMPER PLENUM	12	15MAY04 09:00A	17MAY04 13:59		0
36	1	CE0408110	CE5	20	PIPING EB-	MS-2085 ELBOW - REMOVE STANCHION	10	16MAY04 07:00*	16MAY04 16:59	DR-Y ML-Y ORT3-Y R-N	0
37	1	CE0407589B	CE5	76	T-026	CLOSEOUT BD TANK FOLLOWING REPAIRS	20	17MAY04 08:00*	19MAY04 09:59	DR-Y ML-Y ORT3-Y R-N	0
38	1	CE0408118	CE5	76	MISC	REPAIR FLOOR BEAM SOUTH OF 1T-026	8	17MAY04 10:00	18MAY04 09:59	DR-Y ML-Y ORT3-Y R-N	0
CONSTRUCTION ENG - S. CARTER											
39	0	CE0210986	CE6	77	SEC	SEC SUPPORT MR 99-011*B	168	05APR04 07:00A	14JUN04 14:59	DR-N ML-N ORT3-N R-N	3
40	0	CE0210989	CE6	76	SEC	SEC, INSTALL NEW EQUIP MR 99-011*E	168	05APR04 08:00A	14JUN04 14:59	DR-N ML-N ORT3-N R-N	3
41	0	CE0210990	CE6	76	SEC	SEC REM ABANDONED EQUIP MR 99-011*F	171	03MAY04 08:00A	15JUN04 09:59	DR-N ML-N ORT3-N R-N	0
CONSTRUCTION ENG - L. GAUTHIER											
42	1	CEI600R027	CE8	76	R-1	48 HOUR COOLDOWN OF REPAIRED AREA	10	13MAY04 22:00A	15MAY04 21:59	DR-Y ML-Y ORT3-Y R-M	0
43	1	CEI600R029	CE8	76	R-1	FINAL NDE OF REACTOR HEAD REPAIR AREA	12	15MAY04 22:00*	16MAY04 09:59	DR-Y ML-Y ORT3-Y R-M	0
44	1	CEI600R049	CE8	76	R-1	P-26 - REMOVE NOZZLE EXTENSION	2	16MAY04 10:00	16MAY04 11:59	DR-Y ML-Y ORT3-Y R-M	0
45	1	CEI600G020	CE8	76	R-1	SETUP AND PREPARE MOCKUP FOR NOZZLE	45	16MAY04 10:00*	18MAY04 06:59	DR-Y ML-Y ORT3-Y R-M	0
46	1	CEI600R050	CE8	76	R-1	P-26 - CHAMFER GRIND	4	16MAY04 12:00	16MAY04 15:59	DR-Y ML-Y ORT3-Y R-M	0
47	1	CEI600R055	CE8	76	R-1	PREP TO INSTALL THERMAL SLEEVE AT	5	16MAY04 16:00	16MAY04 20:59	DR-Y ML-Y ORT3-Y R-M	15
48	1	SDI600G010	CE8	76	R-1	REVISE PACKAGETO GRIND OUT OVERLAP	72	17MAY04 07:00*	20MAY04 06:59	DR-Y ML-Y ORT3-Y R-M	0
49	1	SE-I600-A	CE8	76	R-1	SR MGMT DECISION TO GRIND OVERLAP	0	17MAY04 12:00*		DR-Y ML-Y ORT3-Y R-M	96
CHEMISTRY											
50	1	CH0300362	CH	77	CHEM-SAMPL	RCS CL TSR 3.4.5.2	72	16MAY04 06:00*	22MAY04 11:59		262

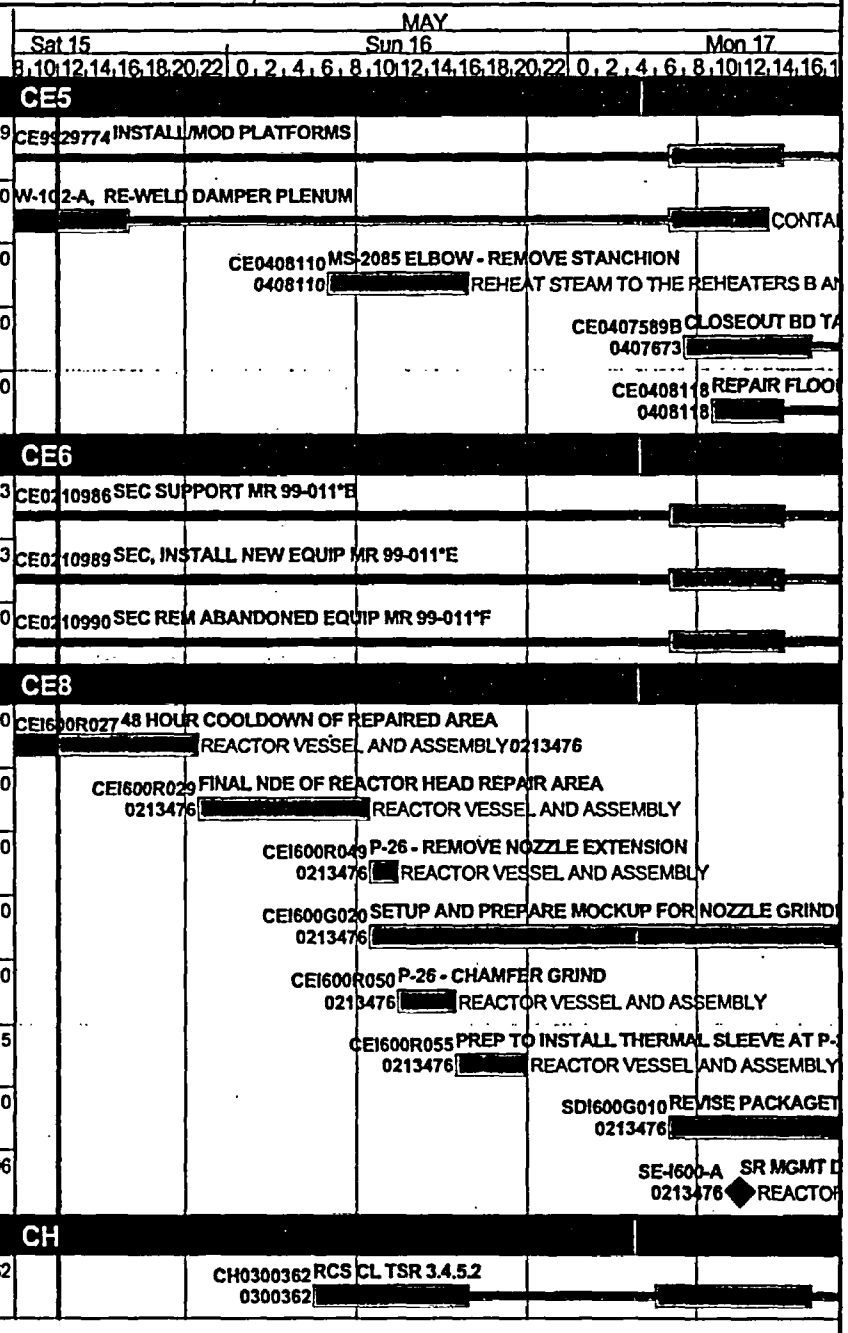

© Primavera Systems, Inc.

U1R28 WORKING SCHEDULE

after 15MAY04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF
CHEMISTRY											
51	1	CH0300375	CH	77	CHEM-SAMPL	RCS DO TSR 3.4.5.1	72	16MAY04 06:00*	22MAY04 11:59		262
52	1	CH0300405	CH	77	CHEM-SAMPL	RCS BORON SR 3.9.1.1	72	16MAY04 06:00*	22MAY04 11:59		262
53	1	CAMP-113BC	CH		CAMP-113	CAMP-113 N2 SPARGE AND SAMPLE B STEAM	3	16MAY04 08:00	16MAY04 10:59	DR-N ML-N ORT3-N R-N	0
54	1	CAMP-113AC	CH		CAMP-113	CAMP-113 N2 SPARGE AND SAMPLE A STEAM	3	16MAY04 20:00	16MAY04 22:59	DR-Y ML-Y ORT3-N R-N	0
55	1	CH0300431	CH	77	CHEM-SAMPL	RCS GROSS ACTIVITY SR 3.04.16.01	6	17MAY04 07:00*	17MAY04 12:59		316
56	1	CH0300418	CH	77	CHEM-SAMPL	RCS FL TSR 3.4.5.3	8	17MAY04 07:00*	17MAY04 14:59		314
57	2	CH0300541	CH	77	CHEM-SAMPL	RCS FL TSR 3.4.5.3	8	17MAY04 07:00*	17MAY04 14:59		314
58	0	CH0300199	CH	77	CHEM-SAMPL	BAST BORON TSR 3.5.1.2	40	17MAY04 07:00*	21MAY04 14:59		131
59	1	CH0300389	CH	77	CHEM-SAMPL	SGBDFO GAMMA SCAN	40	17MAY04 07:00*	21MAY04 14:59		131
60	1	CH0300444	CH	77	CHEM-SAMPL	RE-229 ISOTOPIC	40	17MAY04 07:00*	21MAY04 14:59		131
61	2	CH0300485	CH	77	CHEM-SAMPL	RCS BORON SR 3.9.1.1	40	17MAY04 07:00*	21MAY04 14:59		131
62	2	CH0300502	CH	77	CHEM-SAMPL	RCS CL TSR 3.4.5.2	40	17MAY04 07:00*	21MAY04 14:59		131
63	2	CH0300515	CH	77	CHEM-SAMPL	RCS DO TSR 3.4.5.1	40	17MAY04 07:00*	21MAY04 14:59		131
64	2	CH0300528	CH	77	CHEM-SAMPL	SGBDFO GAMMA SCAN	40	17MAY04 07:00*	21MAY04 14:59		131
65	2	CH0300554	CH	77	CHEM-SAMPL	RE-229 ISOTOPIC	40	17MAY04 07:00*	21MAY04 14:59		131
ENGINEERING - PREDICTIVE MAINTENANCE											
66	0	EE0208969	EEP	77	G-01	THERMAL VECTOR DATA COLLECTION	4	16MAY04 08:00*	16MAY04 11:59		208
67	1	EE0302137	EEP	76	P-058	P-058 - POST MAINTENANCE	1	17MAY04 07:00*	17MAY04 07:59	DR-Y ML-Y ORT3-Y R-N	122
ELECTRICAL MAINTENANCE											
68	1	EM0215241	EM	76	41/1E02	RMP 9308, DS-II BREAKER	14	06MAY04 19:00A	17MAY04 00:59	DR-N ML-N ORT3-N R-N	65

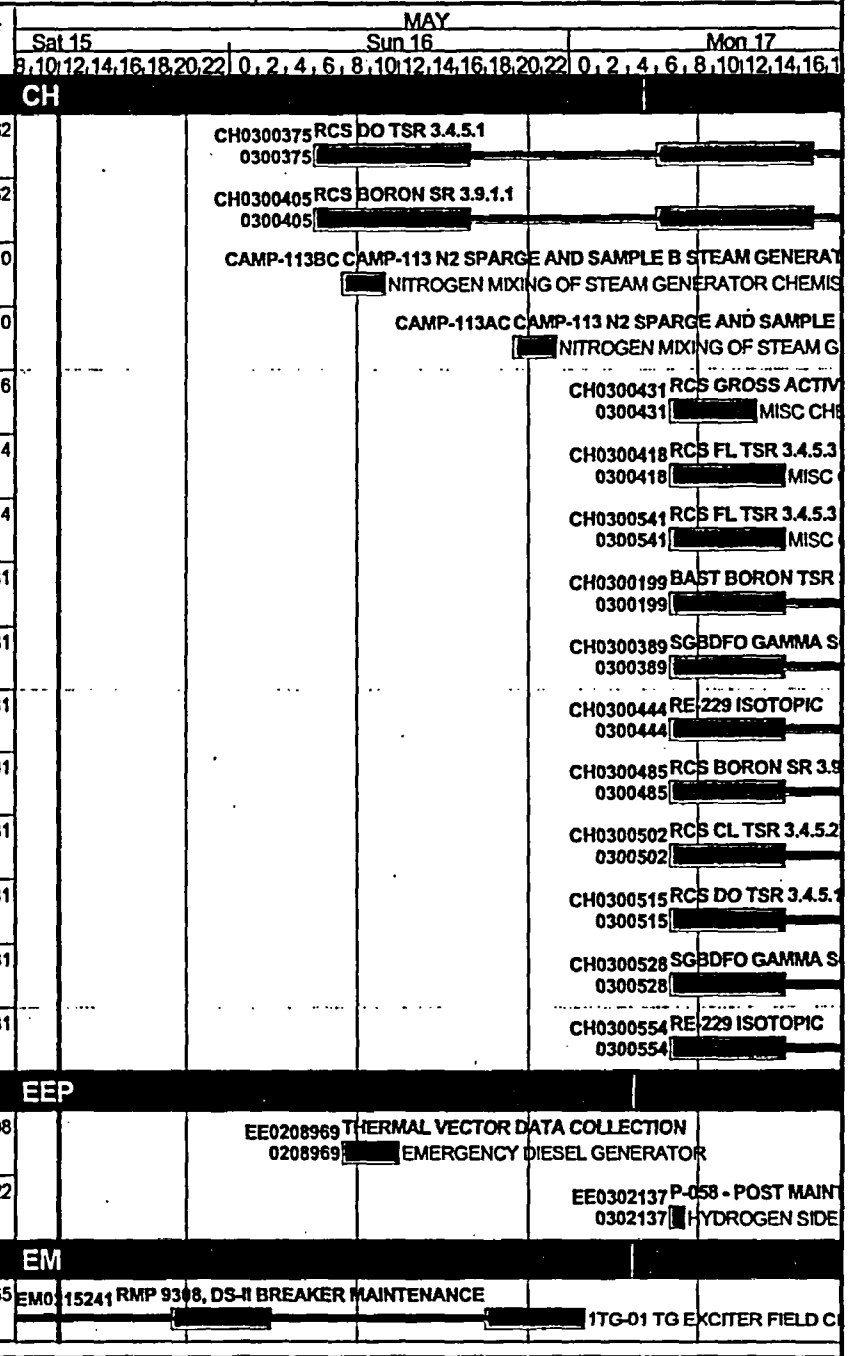

© Primavera Systems, Inc.

U1R28 WORKING SCHEDULE

after 15MAY04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF
ELECTRICAL MAINTENANCE											
69	1	EM0212645	EM	76	W-003B-M	1W-3B-M REPLACE MOTOR BEARINGS	5	09MAY04 09:00A	15MAY04 16:59	DR-N ML-N ORT3-N R-N	11
70	1	EM0216170	EM	76	FIRE-BARRI	PERFORM RMP 58 FIRE BARRIER	8	09MAY04 21:00A	16MAY04 01:59	DR-N ML-Y ORT3-N R-N	100
71	1	EM0215202	EM	76	P-001A-M	P-1A-M PERFORM OIL CHANGE/FLUSH	1	12MAY04 00:00A	15MAY04 12:59	DR-N ML-Y ORT3-N R-N	0
72	0	EM0407638C	EM	76	Z-014	TROUBLESHOOT/REPAIR TB CRANE (SMALL	6	12MAY04 12:00A	16MAY04 12:59		327
73	1	EM0215228	EM	76	W-003B	W-3B-M INSPECT AND MAINTAIN FAN AND	5	14MAY04 07:00A	15MAY04 16:59	DR-N ML-N ORT3-N R-N	172
74	1	EM0312035A	EM	76	P-028B-M	1P-28B-M PERFORM POST MCE TEST	3	15MAY04 11:00A	15MAY04 14:59	DR-Y ML-Y ORT3-N R-N	0
75	1	EM0216539	EM	76	TG-01-VARM	REMOVE TEMPORARY METERING T-MOD	2	15MAY04 12:00*	15MAY04 13:59	DR-N ML-N ORT3-N R-N	0
76	1	EM0216169	EM	77	COM	TEST ALL GAI-TRONICS	4	15MAY04 12:00*	15MAY04 15:59	DR-N ML-Y ORT3-N R-N	285
77	0	EM0215134	EM	77	COM	GAI-TRONICS TEST	15	15MAY04 12:00*	16MAY04 02:59	DR-N ML-Y ORT3-N R-N	727
78	0	EM0405897Z	EM	76	D-106	D-106 PERFORM EQUALIZING CHARGE	108	15MAY04 12:00	19MAY04 23:59	DR-N ML-Y ORT3-N R-N	0
79	1	EM0306911	EM	76	TG-01-VARM	1TG-1-VARM READS HIGH "REPLACE	8	15MAY04 14:00*	15MAY04 21:59	DR-N ML-N ORT3-N R-N	207
80	1	EM0215199B	EM	76	P-001A-M	P-001A FINAL PMT PER 9002-12	10	15MAY04 14:00	15MAY04 23:59	DR-N ML-N ORT3-N R-N	0
81	0	EM0304828	EM	77	P-001A/B-M	INSPECT SPARE RCP MOTOR	4	15MAY04 20:00*	15MAY04 23:59		730
82	0	EM0304873	EM	76	A52-DHVR-1	P-028A - BREAKER MAINTENANCE 1200-34	24	15MAY04 20:00*	16MAY04 19:59	DR-Y ML-Y ORT3-N R-N	0
83	1	EM9937213	EM	76	Z-022	Z-022 - REPLACE CUT LIGHT WIRING	10	15MAY04 21:00	16MAY04 06:59	DR-N ML-N ORT3-N R-N	23
84	1	EAMRCP-B1	EM	76	P-001A-M	REPLACE 'A' RCP FLOOR PANEL	2	16MAY04 00:00	16MAY04 01:59	DR-Y ML-Y ORT3-N R-N	360
85	1	EM0215205	EM	76	P-001B-M	INSPECT AND MAINTAIN REACTOR COOLANT	10	16MAY04 00:00	16MAY04 09:59		0
86	1	EM0215203	EM	87	P-001A-M	P-001A-M - 2ND MCE TEST (1A52-04/1A-01)	3	16MAY04 01:00	16MAY04 03:59	DR-Y ML-Y ORT3-N R-N	0
87	0	EM0304874A	EM	76	A52-DHVR-1	1P-01A PM BKR TESTING AT CUBICLE	4	16MAY04 04:00	16MAY04 07:59	DR-Y ML-Y ORT3-N R-N	215

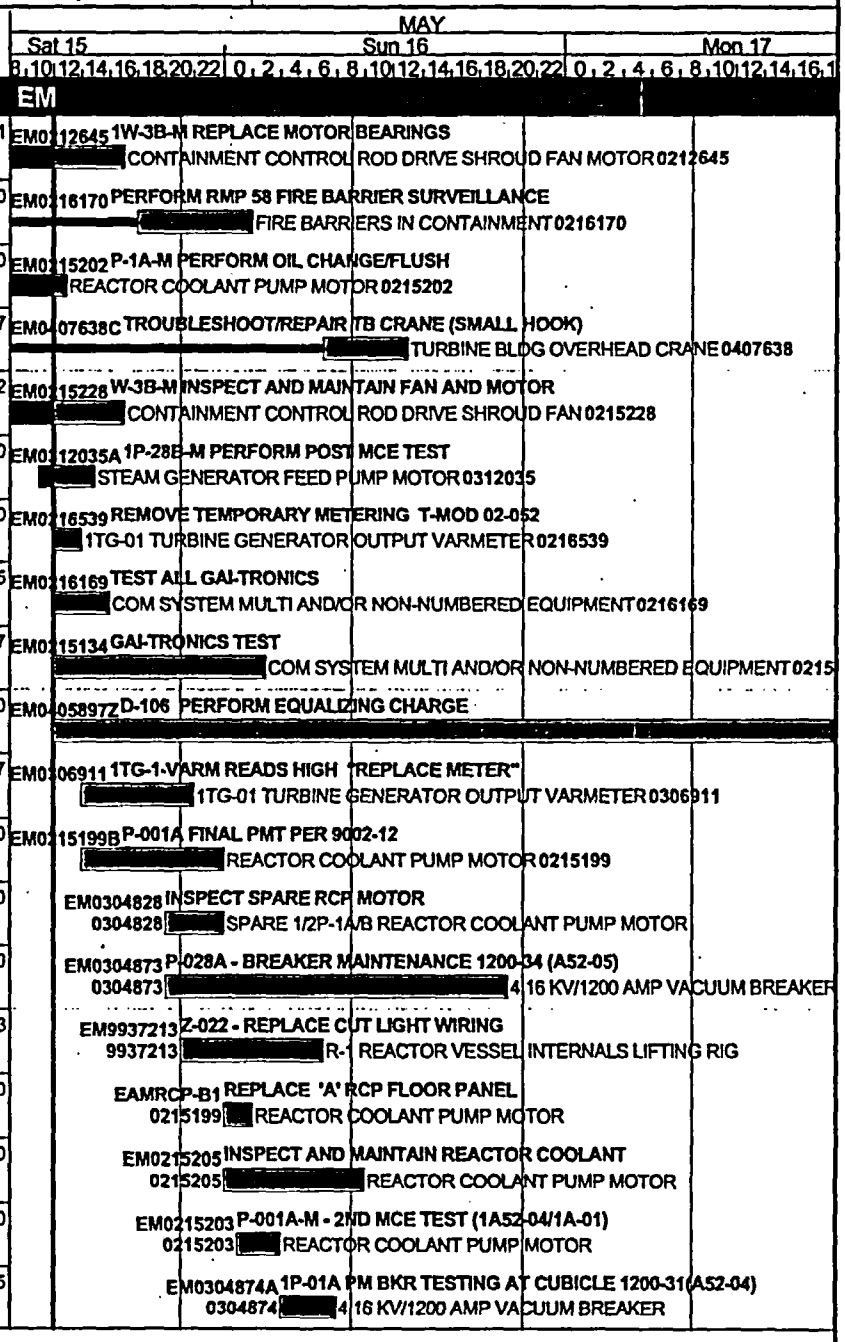

© Primavera Systems, Inc.

U1R28 WORKING SCHEDULE

after 15MAY04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF
ELECTRICAL MAINTENANCE											
88	0	EM0406353	EM	76	D-05	INSPECT CELLS FOR ELECTROLYTE	1	16MAY04 07:00*	16MAY04 07:59		0
89	1	EM0215222	EM	75	W-001C2-M	LUBRICATE 1W-1C2 MOTOR BEARINGS	2	16MAY04 07:00*	16MAY04 08:59		31
90	0	EM0306039	EM	77	ISFSI BLDG	ISFSI SECURITY BLDG MAINTENANCE -	8	16MAY04 07:00*	16MAY04 14:59		715
91	0	EM0309138	EM	76	D-106	STATION BATTERY INSP PER RMP 9046-1	3	16MAY04 08:00*	16MAY04 10:59		0
92	0	EM0305246	EM	77	D-502	MONTHLY G-05 STARTING BATTERY	4	16MAY04 11:00*	16MAY04 14:59		0
93	1	EM0215224	EM	76	W-003B-M	PERFORM MCE W-003B-M	4	16MAY04 13:00*	16MAY04 16:59	DR-N ML-N ORT3-N R-M	0
94	0	EM0305252	EM	77	D-503	MONTHLY G-05 BLACK START DIESEL	5	16MAY04 15:00*	16MAY04 19:59		0
95	0	EM9932294	EM	76	A52-DHVR-1	1200-34 1P28A/AUX SWITCH GUARD	2	16MAY04 18:00	16MAY04 19:59	DR-Y ML-Y ORT3-N R-N	14
96	0	EM0407602	EM	76	A52-DHVR-1	REMOVE S/N 1200-35 FROM CUBICLE A52-04	1	16MAY04 19:00	16MAY04 19:59	DR-N ML-Y ORT3-N R-N	14
97	0	EM0305238	EM	76	D-501	MONTHLY G-05 GT GENERATOR 120V DC	6	16MAY04 20:00*	17MAY04 01:59		0
98	0	EM0305230	EM	76	D-23	MONTHLY SECURITY SYSTEM BATTERY	4	17MAY04 02:00*	17MAY04 05:59	DR-N ML-Y ORT3-N R-N	25
99	0	EM0301793	EM	76	H52-HK-200	BREAKER MAINTENANCE HK-2000	16	17MAY04 05:00	17MAY04 20:59	DR-N ML-Y ORT3-N R-N	153
100	1	EM0215246	EM	76	62/A01	CAL AND TEST 62/A01 RELAY PER 1RMP	6	17MAY04 06:00	17MAY04 11:59	DR-N ML-N ORT3-N R-N	0
101	1	EM0400344A	EM	76	P-028A-M	1P-28A-M PERFORM LEAK CHECKS AT NOP /	2	17MAY04 10:00	17MAY04 11:59	DR-Y ML-Y ORT3-Y R-N	187
102	1	EM0215122	EM	76	A52-04	ASSIST APR DURING P-1A RELAY	6	17MAY04 12:00	18MAY04 08:59	DR-N ML-N ORT3-N R-N	0
103	0	EM0304870	EM	76	H52-DHPVR-	BREAKER MAINTENANCE	16	17MAY04 14:00	18MAY04 05:59	DR-Y ML-Y ORT3-N R-N	2
104	0	EM9925005	EM	76	A52-DHVR-3	3000-1 1X02-1A01 CELL SWITCH INSPECTION	1	17MAY04 17:00*	17MAY04 17:59	DR-N ML-N ORT3-N R-N	164
105	0	EM0301792A	EM	76	A52-DHVR-3	BKR MAINT. PORTION AT CUBICLE (A52-01)	4	17MAY04 17:00*	17MAY04 20:59	DR-N ML-N ORT3-N R-N	0

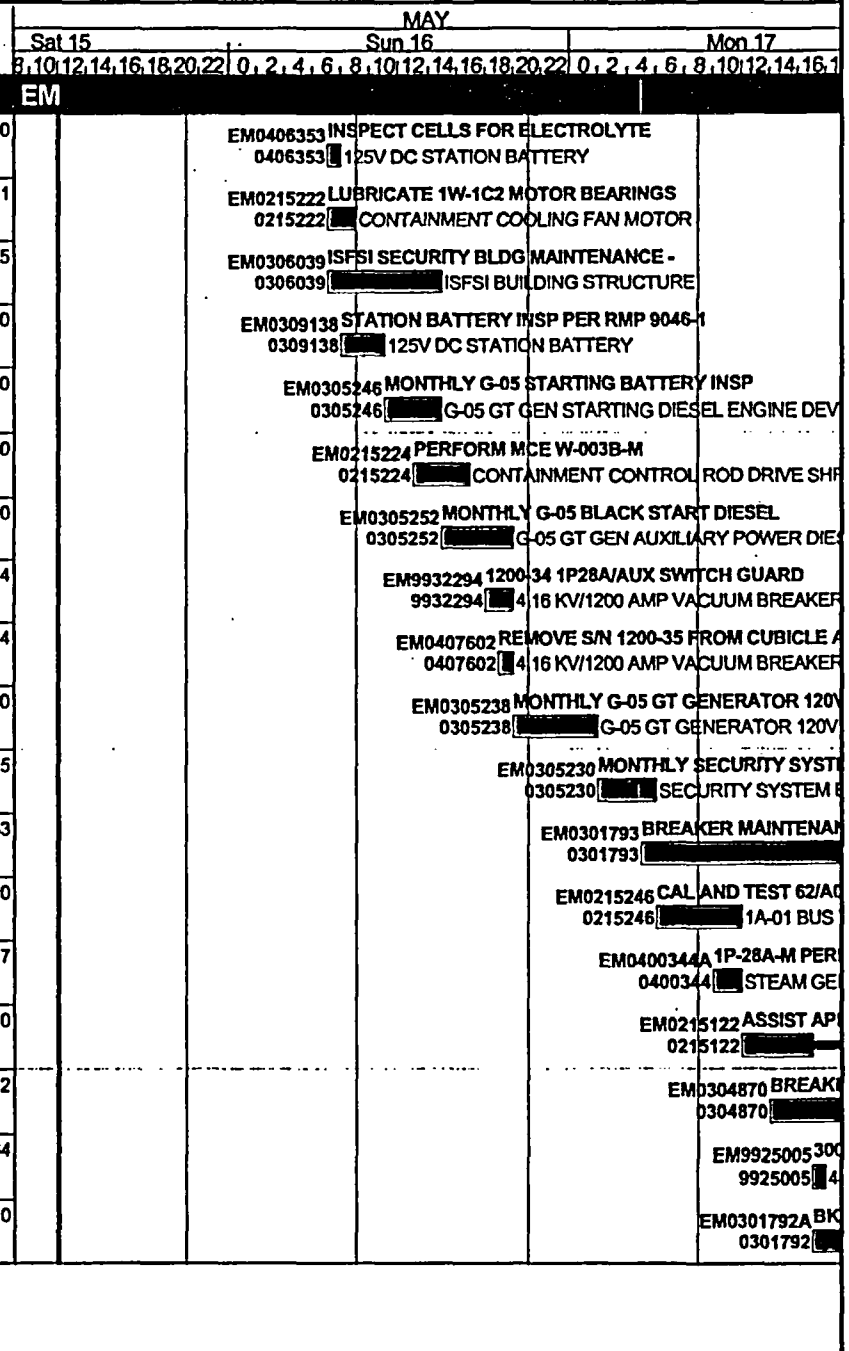

U1R28 WORKING SCHEDULE

after 15MAY04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF
ELECTRICAL VALVE TEAM - EMV											
106	1	B52-427CE	EMV	76	B-42	BUS STAB PMT "1RC-596"	1	15MAY04 12:00	15MAY04 12:59	DR-N ML-N ORT3-N R-N	210
107	1	EM0215240	EMV	76	162-A	MS-2019 & 2020 LOSS OF VOLTAGE TEST -	6	16MAY04 13:00*	16MAY04 20:59	DR-N ML-N ORT3-N R-N	0
108	0	EM0405880C	EMV	78	W-013B1	W-013B1 REMOVE JUMPER PER IWP	4	17MAY04 10:00	17MAY04 13:59	DR-N ML-N ORT3-N R-N	0
109	1	B52-428ME	EMV	76	B-42	BUS STAB PMT "W-13B2"	1	17MAY04 15:00	17MAY04 15:59	DR-N ML-N ORT3-N R-N	690
ENGINEERING PROGRAMS - INSPECTION SERVICES EPI											
110	1	NG44TFC1EV	EPI	77	IST-SISI	ENG EVAL FOR FAC PROG - TURB HALL 44	1	05APR04 12:00A	17MAY04 14:59	DR-Y ML-Y ORT3-Y R-N	0
111	1	NG44CFC1EV	EPI	77	IST-SISI	ENG EVAL FOR FAC PROG - CTMT 44FT GEN	1	29APR04 08:00A	17MAY04 14:59	DR-Y ML-Y ORT3-Y R-N	0
FACILITIES GROUP - UTILITY GROUP FG1											
112	0	FG0309581	FG1	76	Z-066A	Z-066A(ETC)SEAL LEAKS/MANHOLE	12	11MAY04 06:00A	17MAY04 16:59	DR-Y ML-Y ORT3-Y R-N	2
113	1	Z22FG030	FG1	77	Z-022	Z-022 - INTERNALS LIFT RIG - STRIP PAINT FOR	9	15MAY04 09:00A	15MAY04 20:59	DR-Y ML-Y ORT3-Y R-N	0
114	1	FG302663RP	FG1	76	FS-02852	PAINT FS-2852	8	15MAY04 22:00*	16MAY04 05:59		24
115	1	FG0212694	FG1	76	PIPING HB-	1PIPING HB-19 REPAINT	72	16MAY04 02:00*	19MAY04 01:59	DR-Y ML-Y ORT3-Y R-N	0
116	1	FG0408118	FG1	76	MISC	LEAD ABATEMENT ON FLOOR BEAM SOUTH OF	6	16MAY04 08:00*	16MAY04 13:59	DR-Y ML-Y ORT3-Y R-N	17
117	1	Z22FG035	FG1	77	Z-022	Z-22 INTERNALS LIFT RIG - PAINT WELDS	8	16MAY04 17:00	17MAY04 00:59	DR-Y ML-Y ORT3-Y R-N	0
118	1	Z22FG038	FG1	77	Z-022	Z-22 INTERNALS LIFT RIG - PAINT CURE TIME	168	17MAY04 01:00	24MAY04 00:59	DR-Y ML-Y ORT3-Y R-N	191
119	0	FG0300155	FG1	77	MISC	REMOVE VEGETATION IN ISOLATION ZONES	35	17MAY04 06:00*	20MAY04 07:59	DR-Y ML-Y ORT3-Y R-N	288
FACILITIES GROUP - MTN MECH OPER NORTH FG2											
120	0	FG0300135	FG2	77	HX-378A	SERVICE HX-378A SBCC COMP RM AC UNIT	10	16MAY04 07:00*	16MAY04 16:59	DR-Y ML-Y ORT3-Y R-N	713
FACILITIES GROUP - BOB WIENSCH FG3											
121	0	FG0307325	FG3	76	DOOR-065	REPLACE MORTISE LOCKSET	4	16MAY04 18:00*	16MAY04 21:59		282

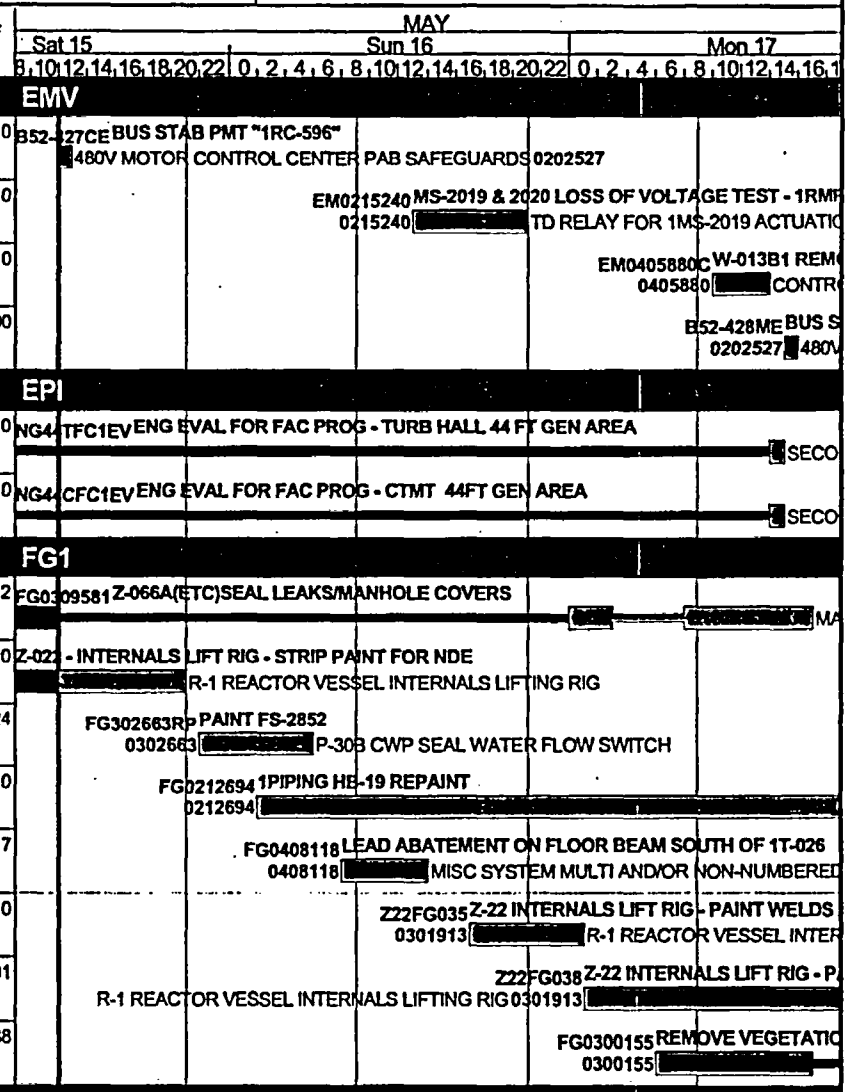

U1R28 WORKING SCHEDULE

after 15MAY04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF
RADIATION PROTECTION (OLD)											
122	0	HP0301854	HP	77	HP RMS	QUARTERLY FUNCTIONAL TEST OF RMS	40	16MAY04 18:00*	20MAY04 00:59		246
I&C MAINTENANCE											
123	1	IC-CV-F&V2	IC		SOP-CV-003	FILL & VENT FI-115 & FI-116 PER SOP-CV-003	1	12MAY04 11:00A	17MAY04 06:59	DR-Y ML-Y ORT3-N R-N	201
124	0	IC0311805	IC	76	FS-00230	RE-230 CLEAN FLOW SWITCH	1	14MAY04 13:00A	15MAY04 12:59	DR-Y ML-Y ORT3-Y R-N	290
125	1	IC0408320	IC		LRC-LW-003	LRC-LW-3 FAILS HIGH	21	15MAY04 11:00A	16MAY04 14:59	DR-Y ML-Y ORT3-Y R-N	535
126	1	ICIALEAK	IC	76	IA	IA LEAK INSPECTION	30	16MAY04 06:00*	18MAY04 13:59	DR-Y ML-Y ORT3-Y R-N	157
127	1	IC5.9RTRAL	IC	76	ICP-05.009	VERIFY ROTOR STOPPED ALARM CLEAR	1	16MAY04 12:00	16MAY04 12:59	DR-Y ML-Y ORT3-Y R-N	180
128	1	IC0306628A	IC	76	S-06050A	1S-6050A REPLACE PROBE GAP	2	16MAY04 12:00	16MAY04 13:59	DR-Y ML-Y ORT3-Y R-N	179
129	1	IC5.54A	IC	76	ICP-05.054	P59B SO B/U PUMP START FUNCTION	3	16MAY04 12:00	16MAY04 14:59	DR-Y ML-Y ORT3-Y R-N	178
130	0	IC0300623	IC	76	ICP-13.001	RMS CALS - GROUP 2	2	17MAY04 06:00*	17MAY04 07:59	DR-Y ML-Y ORT3-Y R-N	9
I&C - C. RHODEN & R. YOUNG											
131	1	IC5.47-1	IC1	76	ICP-05.047	SECONDARY LEVEL CONTROLLERS AND SWIT	9	19APR04 11:00A	16MAY04 09:59	DR-Y ML-Y ORT3-Y R-N	0
132	1	IC5.47A	IC1	76	ICP-05.047	VERIFY DRN BOTTLE LVL ALARMS	1	15MAY04 07:00A	15MAY04 12:59	DR-Y ML-Y ORT3-Y R-N	407
133	1	IC5.11TMGA	IC1	76	ICP-05.011	CHECK TAVG HIGH SELECTOR	3	16MAY04 08:00*	16MAY04 10:59	DR-Y ML-Y ORT3-N R-M	107
134	1	ICORT6	IC1		O-RT-006	ORT 6 CS SEQUENCE - IC SUPPORT	6	16MAY04 08:00	16MAY04 13:59	DR-N ML-N ORT3-N R-N	162
135	1	IC5.47D	IC1	76	ICP-05.047	VERIFY GEN LVL ALMS	1	16MAY04 09:00	16MAY04 09:59	DR-Y ML-Y ORT3-Y R-N	406
136	1	IC2.19	IC1	76	ICP-02.019	ICP 2.19 SAFEGUARDS LOGIC TEST	6	17MAY04 06:00*	17MAY04 11:59	DR-N ML-N ORT3-N R-M	0
I&C - J. SCHMOLDT & R. YOUNG											
137	2	IC0301009	IC2	76	ICP-06.021	CHEMICAL AND VOLUME CONTROL SYSTEM	11	10MAY04 18:00A	16MAY04 04:59	DR-Y ML-Y ORT3-Y R-N	0
138	0	IC0300710	IC2	77	HP-07736	CLEAN CONTAMINATION MONITOR	11	13MAY04 18:00A	16MAY04 04:59	DR-Y ML-Y ORT3-Y R-N	275

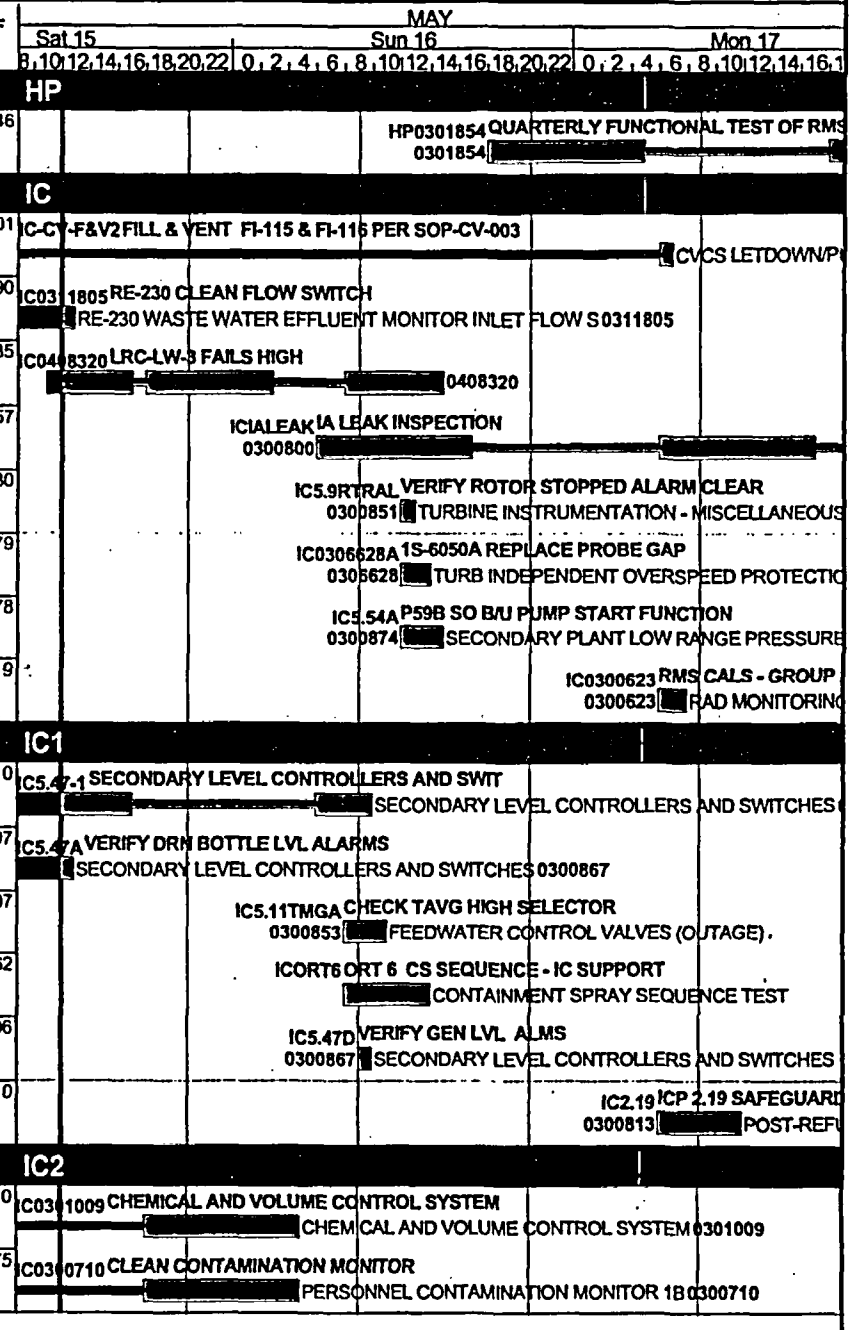

© Primavera Systems, Inc.

U1R28 WORKING SCHEDULE

after 15MAY04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF
I&C - J. SCHMOLDT & R. YOUNG											
139	1	IC2.10	IC2	76	ICP-02.010	NI SR PRE CRITICALITY TEST	2	15MAY04 18:00*	15MAY04 19:59	DR-N ML-N ORT3-N R-N	0
140	1	ICPRE-COMP	IC2		REI 10.1	MOVE REACTIVITY COMPUTER TO	10	15MAY04 19:00*	16MAY04 04:59	DR-Y ML-Y ORT3-Y R-N	163
141	1	IC2.9	IC2	76	ICP-02.009	ICP 2.9 INTERMEDIATE RANGE TEST	1	15MAY04 20:00	15MAY04 20:59	DR-N ML-Y ORT3-N R-N	0
142	1	IC2.15A	IC2	76	ICP-02.015	ICP 2.15 RP PERMISSIVE/NI LOGIC	3	15MAY04 21:00	15MAY04 23:59	DR-Y ML-Y ORT3-N R-N	49
I&C - M. KENNETT											
143	1	IC0300795A	IC5	76	I&C MISC	REACTOR PROTECTION LGC CAB RELAY	5	13MAY04 11:00A	15MAY04 16:59	DR-Y ML-Y ORT3-Y R-N	0
144	1	IC5.8	IC5	76	ICP-05.008	TURBINE SUPERVISORY INST CALS	43	14MAY04 06:00A	19MAY04 10:59	DR-Y ML-Y ORT3-Y R-N	0
145	1	ICTUVIBSUP	IC5	76	T-SUPERVIS	INSTALL TURBINE VIBRATION SENSORS	43	14MAY04 06:00A	19MAY04 10:59	DR-Y ML-Y ORT3-Y R-N	0
146	1	IC0302663A	IC5	76	FS-02852	1FS-2852 FLOW SW SET UP AND CAL - 2ND	3	17MAY04 06:00*	17MAY04 08:59	DR-Y ML-Y ORT3-Y R-N	0
I&C VALVE TEAM											
147	1	IC5.49D	ICV	76	ICP-05.049	ICP 5.49 CS-2273 HEATER BYPASS LIMIT	1	15MAY04 08:00A	15MAY04 12:59	DR-Y ML-Y ORT3-Y R-N	70
148	1	IC0214110	ICV	76	MS-02018	MS-2018 POST INSPECTION	7	16MAY04 07:00*	16MAY04 13:59	DR-Y ML-Y ORT3-N R-N	0
149	1	ICMS2018	ICV	76	MS-02018-O	MS-2018 MSIV DIAGNOSTIC	7	16MAY04 07:00*	16MAY04 13:59	DR-Y ML-Y ORT3-N R-N	0
MECHANICAL MAINTENANCE MM1 RIDINGS/ BRITTINGHAM											
150	1	MM9924975A	MM1	76	HS-1	HS-1, REBUILD & TEST SNUBBER (SHOP)	27	26APR04 06:00A	17MAY04 16:59	DR-Y ML-Y ORT3-N R-N	55
151	1	MM-8856A1	MM1	82	HX-015A	HX-015A - PERFORM SW LEAK CHECK & INSTALL	6	16MAY04 06:00*	16MAY04 11:59	DR-Y ML-Y ORT3-N R-N	0
152	1	MM0215948	MM1	77	O-RF-510.2	RF-510.2, MOVE Z-23B LATCH TOOL OUT OF	6	16MAY04 06:00*	16MAY04 11:59	DR-Y ML-Y ORT3-N R-N	256
153	1	MM-8856A	MM1	82	W-001A1	W-1A1, FME CLOSE OUT INSPECTION (AFTER SW	1	16MAY04 12:00	16MAY04 12:59	DR-Y ML-Y ORT3-N R-N	1
154	1	MM-8857A1	MM1	82	HX-015B	HX-15B, PERFORM SW LEAK CHECK & INSTALL	6	17MAY04 12:00	18MAY04 06:59	DR-Y ML-Y ORT3-N R-N	0
155	1	MM-8858A	MM1	82	W-001C1	W-1C1, FME CLOSE OUT INSPECTION	1	17MAY04 14:00	17MAY04 14:59	DR-Y ML-Y ORT3-N R-N	2

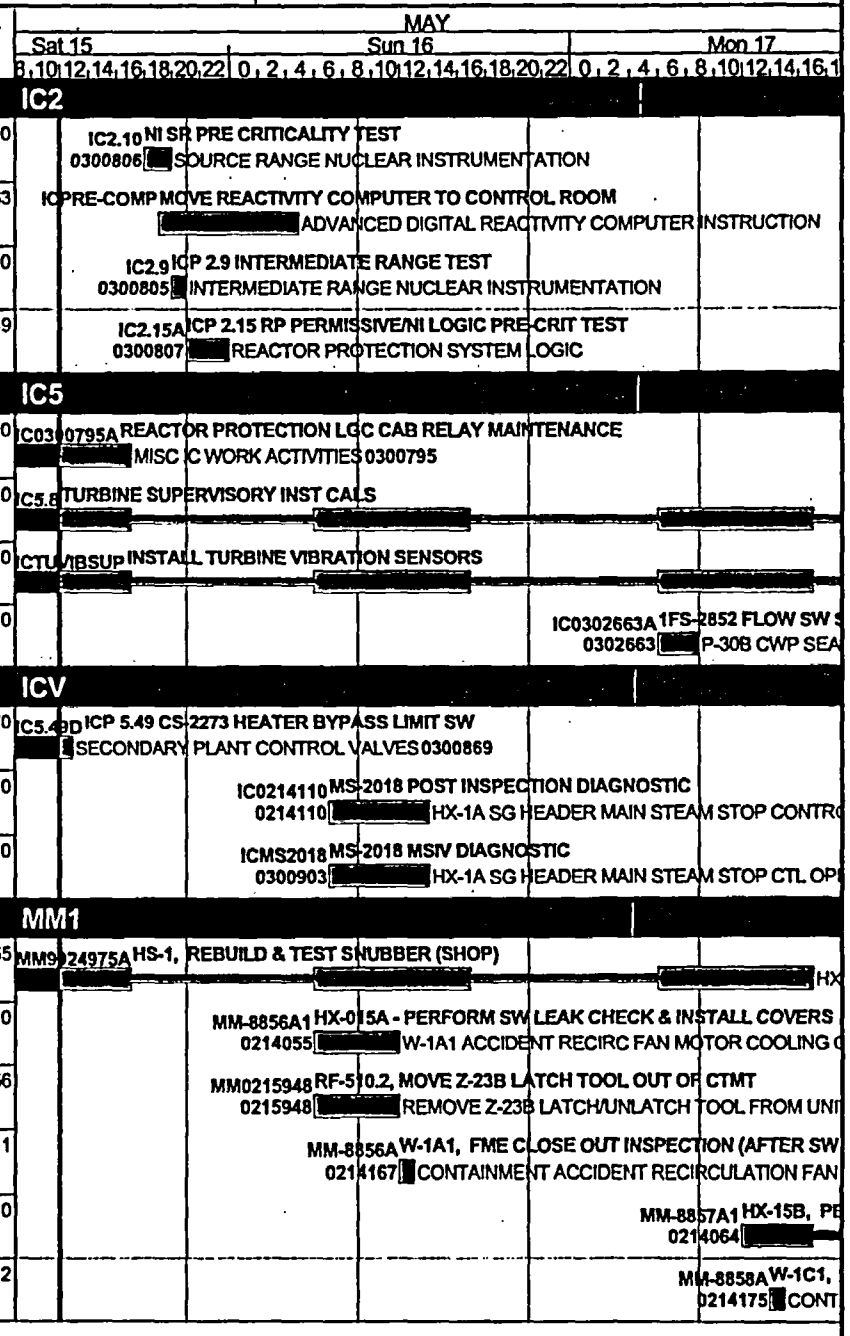

U1R28 WORKING SCHEDULE

after 15MAY04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF
MECHANICAL MAINTENANCE MM1 RIDINGS/ BRITTINGHAM											
156	1	Z22MM040	MM1	77	Z-022	Z-22 INTERNALS LIFT RIG - MOVE TO CAVITY	2	17MAY04 17:00	17MAY04 18:59	DR-Y ML-Y ORT3-N R-N	0
MECHANICAL MAINTENANCE MM2 BONENFANT (BOP)											
157	1	MM0304995	MM2	76	P-028B	P-028B - OVERHAUL MAIN FEED PUMP	5	30APR04 15:00A	15MAY04 16:59	DR-Y ML-Y ORT3-N R-N	0
158	1	MM9919654	MM2	77	P-028B	1P-28B STOP OIL LEAK/INSTALL BAFFLE	15	06MAY04 05:00A	16MAY04 15:59	DR-Y ML-Y ORT3-N R-N	0
159	0	MM0201475	MM2	76	VNTB	INSPECT/SERVICE OPS SHOP HVAC EQUIP	4	12MAY04 10:00A	15MAY04 15:59		0
160	0	MM0405942	MM2	77	IA-06335	IA-6335 TEST BY 5/21/04 (SPARE)	3	15MAY04 06:00A	15MAY04 14:59		336
161	0	MM0201626	MM2	76	W-017	LUBRICATE, INSPECT AND MAINTAIN FAN	2	15MAY04 13:00*	15MAY04 14:59	DR-Y ML-Y ORT3-N R-N	0
162	0	MM0201642	MM2	76	W-086	LUBRICATE FAN BEARINGS	4	15MAY04 14:00	15MAY04 17:59	DR-Y ML-Y ORT3-N R-N	0
163	0	MM0301086	MM2	76	HX-038B	INSPECT AND MAINTAIN AC UNIT	4	15MAY04 18:00*	15MAY04 21:59		337
164	1	MM0301116	MM2	77	P-028A	DRAW OIL SAMPLE FOR ANALYSIS	2	15MAY04 21:00*	15MAY04 22:59	DR-Y ML-Y ORT3-N R-N	0
165	1	MM0301117	MM2	77	P-028B	DRAW OIL SAMPLE FOR ANALYSIS	2	15MAY04 23:00*	16MAY04 00:59	DR-Y ML-Y ORT3-N R-N	334
166	0	MM0201849	MM2	76	HX-038A1/A	CLEAN AND INSPECT HX UNIT	6	16MAY04 06:00	16MAY04 11:59		0
167	2	MM0301161	MM2	77	ELECT PENE	INSPECT AND MAINTAIN Q3 AND Q58	4	16MAY04 07:00*	16MAY04 10:59		329
168	0	MM0309581A	MM2	76	Z-066A	BRODERSON CRANE SUPPORT FOR	10	17MAY04 06:00*	17MAY04 15:59		313
169	1	MM0301106	MM2	76	P-011A	CHANGE OIL, FLUSH BEARINGS AND CLEAN	6	17MAY04 09:00	17MAY04 14:59		0
MECHANICAL VALVE, VANDERVELDE/KENNEY											
170	1	MM0214110	MMV	76	MS-02018	MS-2018 - OPEN & INSPECT VALVE -	19	03MAY04 22:00A	16MAY04 06:59	DR-Y ML-Y ORT3-N R-N	0
NON-DESTRUCTIVE TESTING											
171	1	NG44CFC1ND	NDE	77	IST-SISI	NDE FOR FAC PROG - CONTAINMENT 44 FT	4	26APR04 08:00A	17MAY04 12:59	DR-Y ML-Y ORT3-Y R-N	98
172	1	EP0301909	NDE	77	U1-CONTAIN	VISUAL INSPECTION OF CTMT LINER PLATE	5	30APR04 08:00A	17MAY04 12:59	DR-Y ML-Y ORT3-Y R-N	98

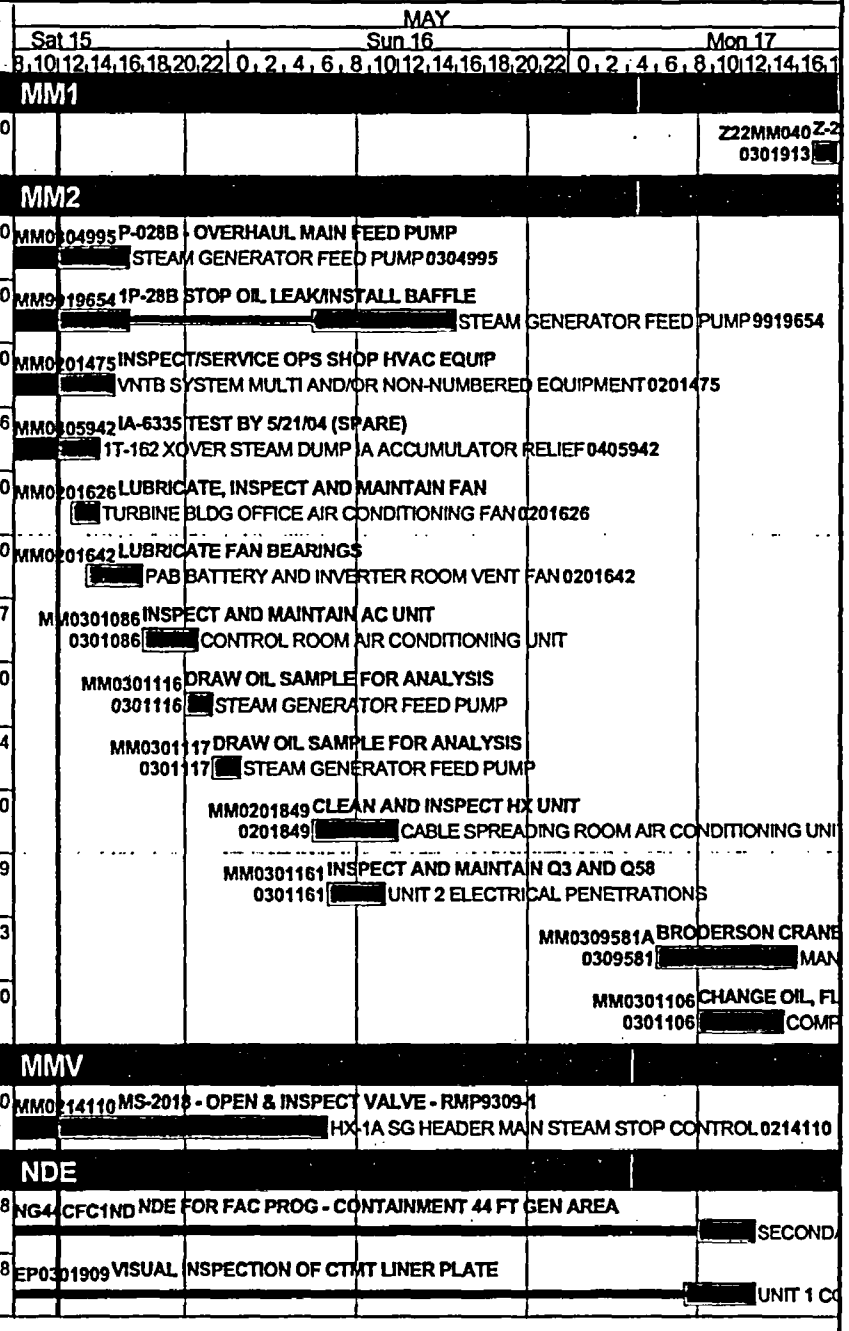

U1R28 WORKING SCHEDULE

after 15MAY04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF
NON-DESTRUCTIVE TESTING											
173	1	ND0407589B	NDE	76	T-026	T-026 - NDE / RADIOGRAPHY OF PIPING	8	12MAY04 19:00A	17MAY04 02:59	DR-Y ML-Y ORT3-Y R-N	2
174	1	P1402NDE	NDE	77	Z-022	Z-022 - INTERNALS LIFT RIG NDE EXAM (MT)	10	16MAY04 07:00*	16MAY04 16:59	DR-Y ML-Y ORT3-Y R-N	0
175	1	ND0408110	NDE	20	PIPING EB-	MS-2085 ELBOW - INSPECT EXPOSED AREA	2	16MAY04 17:00	16MAY04 18:59	DR-Y ML-Y ORT3-Y R-N	711
176	1	ND0408118	NDE	76	MISC	T-26 BEAM - DETERMINE EXTENT OF REPAIR	3	17MAY04 07:00	17MAY04 09:59	DR-Y ML-Y ORT3-Y R-N	0
OPERATIONS RELIEFS											
177	0	OP0215335	OP0	77	O-PC-077.4	DRY PIPE SYSTEM CHECK	8	15MAY04 12:00*	16MAY04 12:59		207
OPERATIONS MIDSHIFT											
178	0	OP0301293	OP1	76	O-PC-MIDS	OPERATIONS MID SHIFT WEEKLY ROUTINE	35	14MAY04 00:00A	20MAY04 06:59		182
179	0	OP0301314	OP1	76	O-PC-049.7	WEEKLY VERIFICATION OF FACADE FREEZE	1	16MAY04 00:00*	16MAY04 00:59		216
OPERATIONS DAYSHIFT											
180	0	OP0301332	OP2	76	O-PC-DAYS	OPERATIONS DAY SHIFT WEEKLY ROUTINE	7	10MAY04 08:00A	16MAY04 11:59	DR-Y ML-Y ORT3-Y R-N	208
181	0	OP0301351	OP2	76	O-PC-012.1	G-01 EDG VIBRATION (QUARTERLY)	1	16MAY04 08:00*	16MAY04 08:59		211
182	0	OP0301353	OP2	76	O-PC-012.3	G-01 COOLANT SAMPLING	1	16MAY04 08:00*	16MAY04 08:59		211
183	0	OP0301359	OP2	76	PT-FP-003	ELECTRIC MOTOR-DRIVEN FIRE PUMP	1	17MAY04 08:00*	17MAY04 08:59		204
184	2	OP0301614	OP2	76	TS-ECCS-00	SAFEGUARD SYSTEMS VALVE AND LOCK	1	17MAY04 08:00*	17MAY04 08:59		204
185	0	OP0301346	OP2	76	O-PC-043.1	CLEAN AIR BREATHERS/OIL STRAINER ON	2	17MAY04 08:00*	17MAY04 09:59		203
OPERATIONS SWINGSHIFT											
186	0	OP0301394	OP3	76	O-PC-SWING	OPS SWING SHIFT WEEKLY ROUTINE	28	12MAY04 16:00A	18MAY04 22:59		189
187	0	OP0301428	OP3	76	O-PC-078.3	MONTHLY NORTH SERVICE BUILDING	1	15MAY04 16:00*	15MAY04 16:59		216
188	0	OP0301326	OP3	76	O-IT-0072	IT-72, SERVICE WATER VALVES	11	15MAY04 16:00*	16MAY04 19:59		206

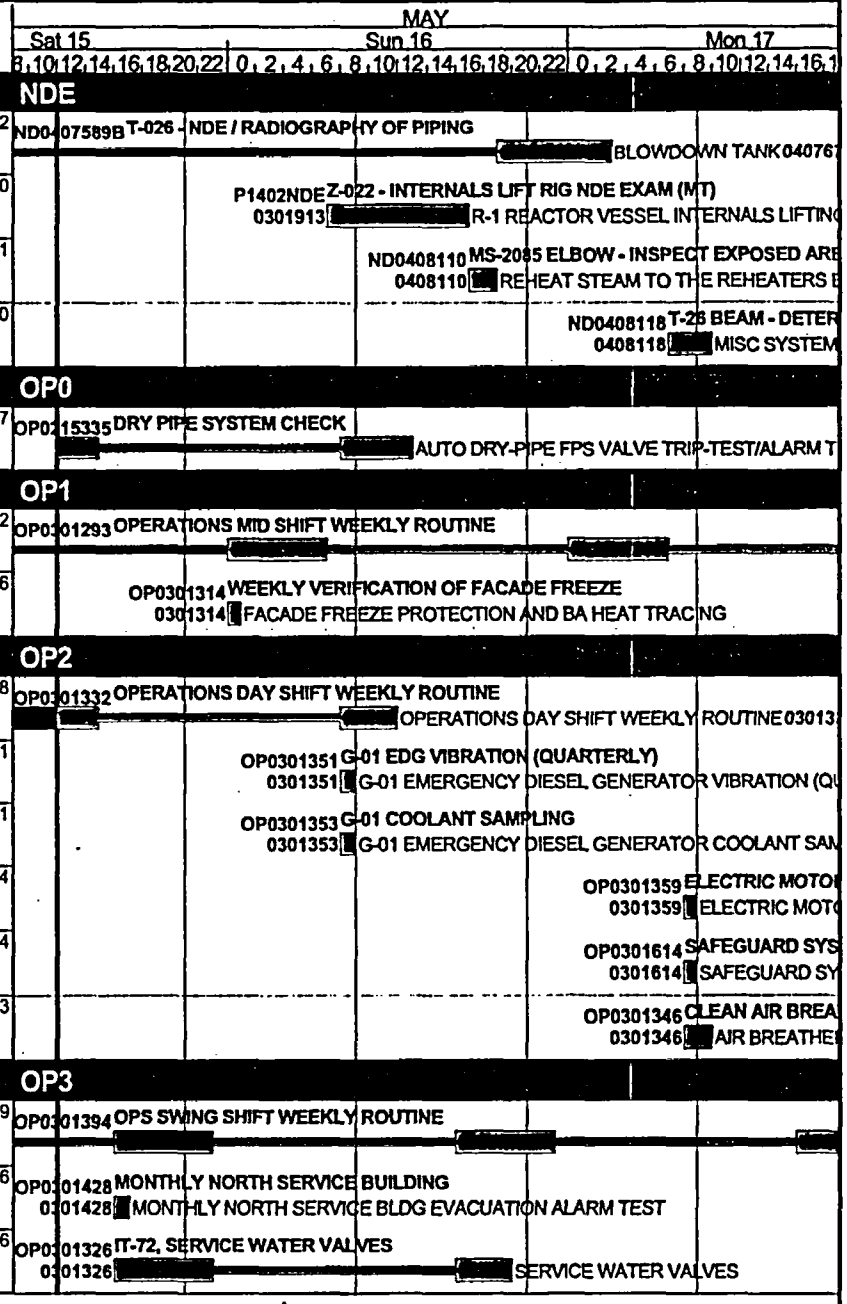

© Primavera Systems, Inc.

U1R28 WORKING SCHEDULE

after 15MAY04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF
OPERATIONS SWINGSHIFT											
189	0	OP0209766	OP3	76	O-PC-053	VERIFY MSR SHELL SIDE HIGH LEVEL	2	16MAY04 16:00*	16MAY04 17:59		208
190	2	U2GNDR016	OP3		TG-01	DRAIN U2 MAIN ELECTRICAL	1	16MAY04 18:00	16MAY04 18:59		207
191	2	U2GNDR017	OP3		TG-01	DRAIN U2 MAIN ELECTRICAL	1	16MAY04 18:00*	16MAY04 18:59		0
192	1	OP0301556	OP3	77	O-PC-025	PURIFY RWST	1	17MAY04 16:00*	17MAY04 16:59		202
OPERATIONS											
193	1	CVCSPMT	OPS		CV	PERFORM CVCS WALKDOWN FOR PMT	8	12MAY04 08:00A	15MAY04 19:59	DR-N ML-N ORT3-N R-N	246
194	1	B52-427C	OPS	76	B-42	BUS STAB PMT "1RC-596"	1	15MAY04 12:00*	15MAY04 12:59	DR-N ML-N ORT3-N R-N	279
195	1	IT-740	OPS	77	O-IT-0740	IT-740, MAIN STEAM BLOWDOWN	1	15MAY04 12:00	15MAY04 12:59	DR-N ML-N ORT3-N R-N	331
196	1	OP0303383	OPS	76	SC-00966B	SC-966B - PMT STROKE PER IT 60	1	15MAY04 12:00	15MAY04 12:59	DR-Y ML-Y ORT3-N R-N	0
197	1	EP0403494A	OPS	76	PT-RCS-1	OPERATING SUPPORT OF INITIAL RCS	4	15MAY04 12:00	15MAY04 15:59	DR-Y ML-Y ORT3-N R-N	242
198	1	O-RT-065	OPS	77	O-RT-065	LLRT OF RE-211/212 RETURN LINE	4	15MAY04 12:00	15MAY04 15:59	DR-Y ML-Y ORT3-N R-N	0
199	1	IT-330	OPS	77	O-IT-0330	CNMT ISO VALVES STROKE TEST	6	15MAY04 12:00	15MAY04 17:59	DR-Y ML-Y ORT3-N R-N	326
200	1	CL13B010	OPS		CL-13B	CONDENSATE VALVE LINEUPS	10	15MAY04 12:00	15MAY04 21:59	DR-Y ML-Y ORT3-N R-N	0
201	1	OP0303382	OPS	82	SC-00953	SC-953 -PMT STROKE PER IT 60	1	15MAY04 15:00*	15MAY04 15:59	DR-N ML-N ORT3-N R-N	238
202	1	O-RT-036B	OPS	77	O-RT-036	POST LLRT PZR LIQUID SAMPLE LINE	4	15MAY04 15:00	15MAY04 18:59	DR-N ML-N ORT3-N R-N	235
203	1	IT-580	OPS	77	O-IT-0580	PASS LEAKAGE TEST	4	15MAY04 16:00	15MAY04 19:59	DR-Y ML-Y ORT3-N R-N	292
204	1	OI48-050	OPS		T-036	FILL MFP P-28B LUBE OIL RESERVIORS	4	15MAY04 17:00*	15MAY04 20:59	DR-N ML-N ORT3-N R-N	0
205	1	OP13A120	OPS		OP-13A	FILL CONDENSER HOTWELL	4	15MAY04 22:00	16MAY04 01:59	DR-Y ML-Y ORT3-N R-N	232
206	1	OP13A110	OPS		TG-01-T	PLACE TURBINE ON TURNING GEAR	2	16MAY04 00:00*	16MAY04 01:59	DR-N ML-N ORT3-N R-N	0

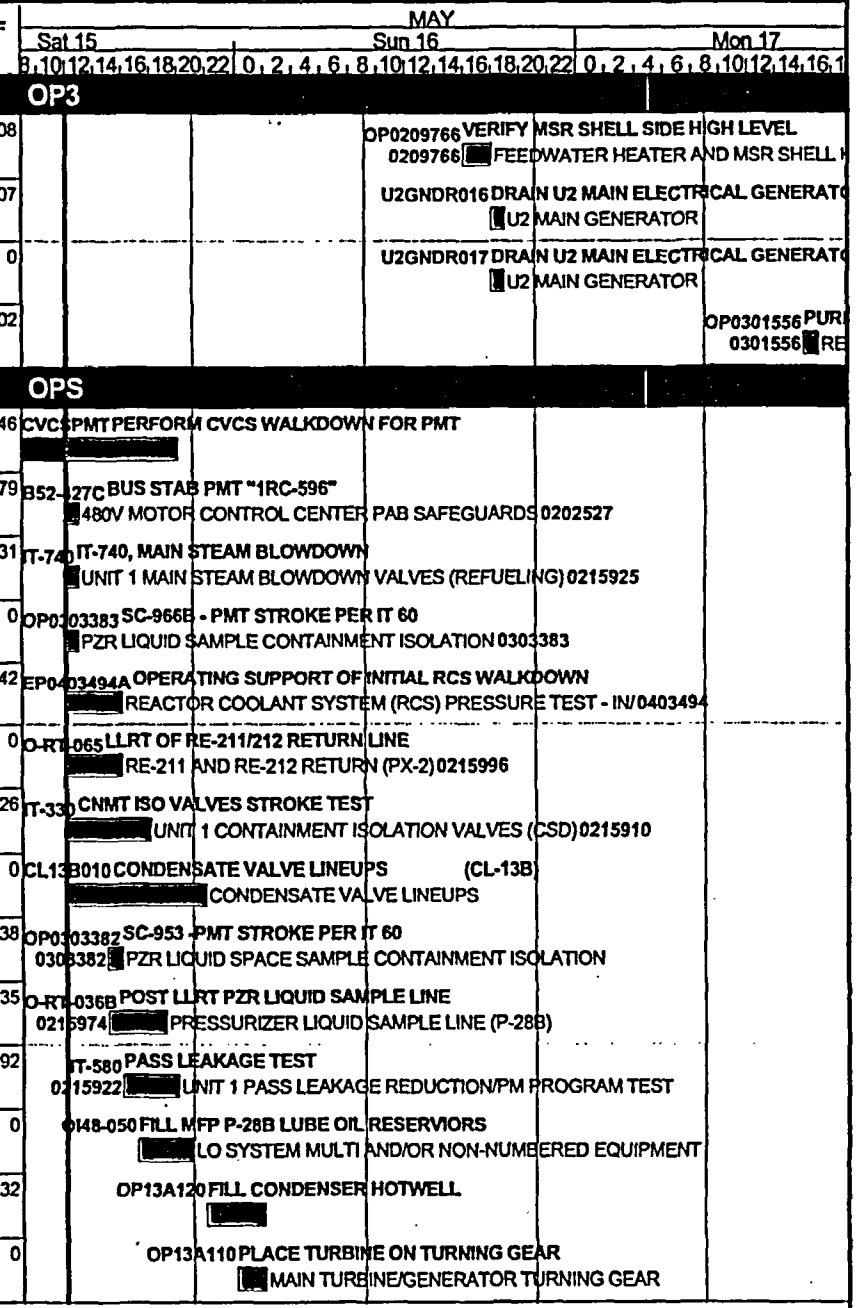

© Primavera Systems, Inc.

U1R28 WORKING SCHEDULE

after 15MAY04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF
OPERATIONS											
207	1	ORT-006	OPS	77	O-RT-006	ORT 6 CS SEQUENCE	6	16MAY04 08:00*	16MAY04 13:59	DR-N ML-N ORT3-N R-M	0
208	1	IT-280A	OPS	77	O-IT-0280A	MSIV STROKE TEST, IT-280A	4	16MAY04 14:00	16MAY04 17:59		0
209	1	OI32-030	OPS		OI-32	GENERATOR 60# AIR TEST	24	16MAY04 15:00*	17MAY04 14:59	DR-N ML-N ORT3-N R-N	0
210	1	X03-010	OPS		X-03	IPTE BRIEF TO DE-ENERGIZE X-03	2	17MAY04 01:00*	17MAY04 02:59	DR-N ML-N ORT3-N R-N	0
211	1	X03-020	OPS		X-03	DEENERGIZE X-03	2	17MAY04 03:00	17MAY04 04:59	DR-N ML-N ORT3-N R-N	0
212	1	B52-428M	OPS	76	B-42	BUS STAB PMT "W-13B2"	1	17MAY04 15:00	17MAY04 15:59	DR-N ML-N ORT3-N R-N	0
213	0	OP0310365A	OPS		G-02	ALIGN G02 TO 1A05 & 2A05 PER OI-35A	1	17MAY04 15:00*	17MAY04 15:59		0
214	0	OP0405880	OPS	78	W-013B1	W-013B1 PMT PER IWP 01-128*E-FN	2	17MAY04 15:00	17MAY04 16:59	DR-N ML-N ORT3-N R-N	0
215	0	OP0310365C	OPS		G-02	PROTECT G02	14*	17MAY04 15:00	18MAY04 04:59		0
216	1	Z22OPS01	OPS	77	Z-022	Z-22, MOVE MANIPULATOR AWAY	1	17MAY04 16:00	17MAY04 16:59		0
PRODUCTION PLANNING											
217	1	MSA25Z	PPG		MILESTONE	END S/G A CL-1E WORK OUTSIDE CONTAINMENT	0	16MAY04 08:00	16MAY04 07:59	DR-N ML-N ORT3-N R-N	271
218	1	VNCCA51Z	PPG		MILESTONE	END CONTAINMENT FAN COOLERS A WORK	0	16MAY04 14:00	16MAY04 13:59	DR-N ML-N ORT3-N R-N	47
219	1	RCX01Z	PPG		MILESTONE	CLOSE ROD DRIVE CONTROL WORK	0	16MAY04 17:00	16MAY04 16:59	DR-N ML-N ORT3-N R-N	149
220	1	CSB12Z	PPG		MILESTONE	END FEED PUMP P28B WORK WINDOW	0	16MAY04 20:00	16MAY04 19:59	DR-N ML-N ORT3-N R-N	343
221	1	MSX01Z	PPG		MILESTONE	END MAIN STEAM SECONDARY WORK	0	17MAY04 00:00	16MAY04 23:59	DR-N ML-N ORT3-N R-N	270
222	1	CWX01Z	PPG		MILESTONE	END CIRC WATER & CONDENSER WORK	0	17MAY04 09:00	17MAY04 08:59	DR-N ML-N ORT3-N R-N	199
223	1	CSA12Z	PPG		MILESTONE	CLOSE FEED PUMP P28A WORK WINDOW	0	17MAY04 10:00	17MAY04 09:59	DR-N ML-N ORT3-N R-N	0
224	1	4KVA01Z	PPG		A-01	CLOSE A01 BUS RELATED WORK	0	17MAY04 13:00	17MAY04 12:59	DR-N ML-N ORT3-N R-N	193

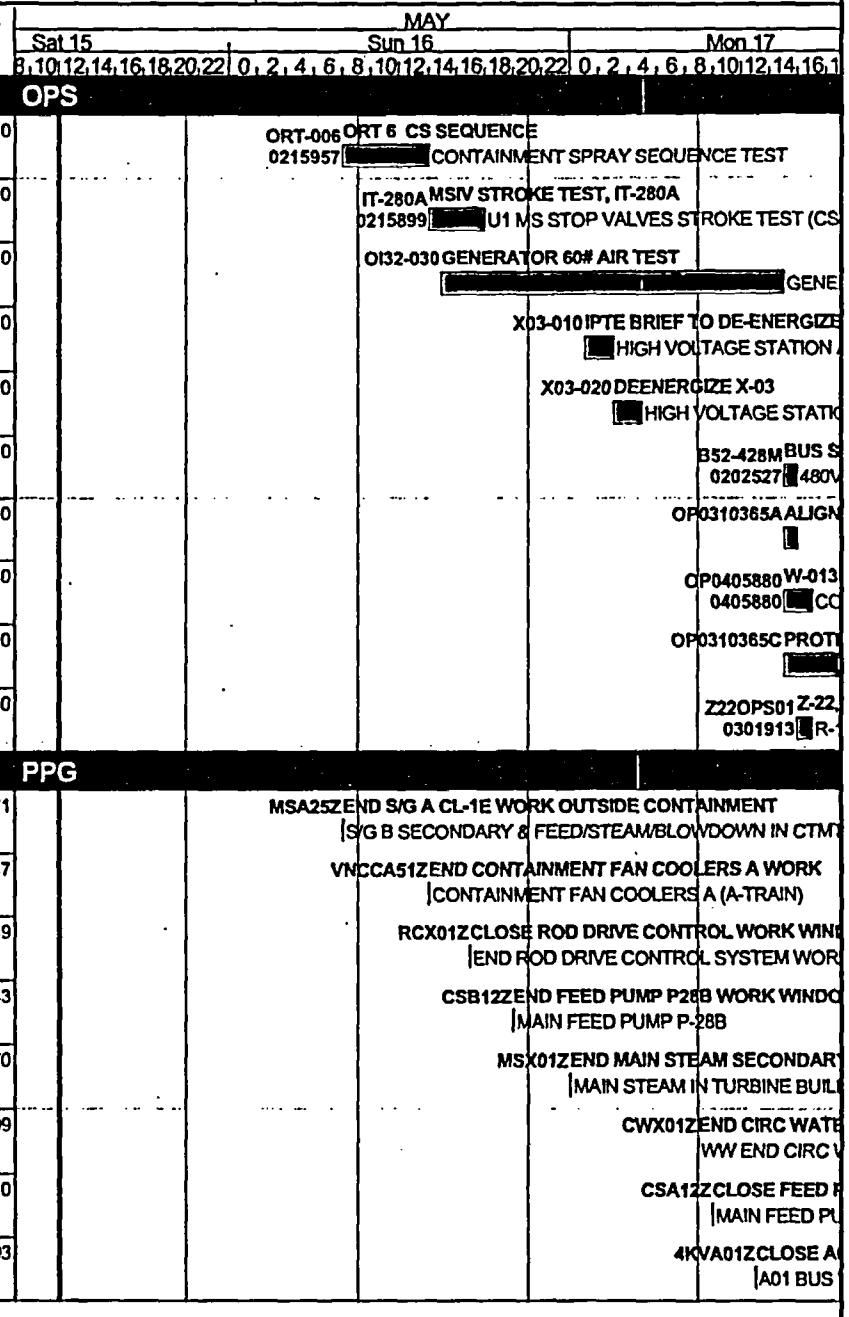

© Primavera Systems, Inc.

U1R28 WORKING SCHEDULE

after 15MAY04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF
PRODUCTION PLANNING											
225	1	VNCCB51Z	PPG		MILESTONE	END CONTAINMENT FAN COOLERS C WORK	0	17MAY04 17:00	17MAY04 16:59	DR-N ML-N ORT3-N R-N	28
LAUNDRY DECON - T. ENGLEMAN											
226	1	RPJF-152D	RP1		JOB FILE 1	NIGHT SHIFT UPPER CAVITY DECON BRIEF	5	16MAY04 18:00*	16MAY04 22:59	DR-Y ML-Y ORT3-Y R-N	70
227	1	Z22RP007	RP1	77	Z-022	Z-22 CONSTRUCT SCAFFOLD	4	17MAY04 02:00	17MAY04 05:59	DR-Y ML-Y ORT3-Y R-N	0
228	1	RPJF-152C	RP1		JOB FILE 1	DAY SHIFT UPPER CAVITY DECON BRIEF	5	17MAY04 06:00*	17MAY04 10:59	DR-Y ML-Y ORT3-Y R-N	61
229	1	Z22RP045	RP1	77	Z-022	Z-22 REMOVE LDA WALLS	1	17MAY04 16:00	17MAY04 16:59	DR-Y ML-Y ORT3-Y R-N	0
SITE DESIGN MECHANICAL											
230	1	SD-I600-93	SDM	76	R-1	ADDRESS ONGOING ISSUES WITH RELIEF	143	13MAY04 13:00A	21MAY04 10:59	DR-Y ML-Y ORT3-Y R-N	0
SITE DESIGN STRUCTURAL (CIVIL)											
231		SD_GSI-191	SDS		CONT	ENGINEERING WALKDOWN - SUMP	27	08APR04 08:00A	20MAY04 09:59	DR-Y ML-Y ORT3-Y R-N	49
SECURITY GROUP											
232	0	SE0311772A	SEC	76	Z-065A	SECURITY SUPPORT Z-065A - MR 03-044	48	10MAY04 07:00A	24MAY04 14:59		123
TURBINE GENERATOR GROUP											
233	1	TGSUPPORT	TGG		TG-01-T	PROVIDE CRANE, RIGGER, AND	89	13APR04 09:00A	21MAY04 15:59	DR-Y ML-Y ORT3-Y R-N	214
WORK CONTROL CENTER											
234	1	CL-2B	WCC		CL 2B	MODE 6 TO MODE 5 CHECKLIST	227*	25APR04 08:00A	24MAY04 22:59	DR-N ML-N ORT3-N R-N	0
235	1	CL-2E	WCC		CL 2E	MODE 3 TO MODE 2 CHECKLIST	396*	02MAY04 19:00A	31MAY04 23:59	DR-N ML-N ORT3-N R-N	0
236	1	CL-2F	WCC		CL 2F	MODE 2 TO MODE 1 CHECKLIST	416*	02MAY04 19:00A	01JUN04 19:59	DR-N ML-N ORT3-N R-N	0
237	1	T-0472-R	WCC		RM-3200C	1 RM RM-3200C IC REV0-1	1	15MAY04 12:00	15MAY04 12:59	DR-Y ML-Y ORT3-Y R-N	69
238	1	T-7110-R	WCC		TG-01-G	1 TU TG-01-G EM REV5-1	1	15MAY04 12:00	15MAY04 12:59	DR-Y ML-Y ORT3-Y R-N	52
239	0	T210718R	WCC		W-085-M	REMOVE TAG (0 VNBI W-85 EM REV0-1)	1	15MAY04 12:00	15MAY04 12:59	DR-Y ML-Y ORT3-N R-N	0

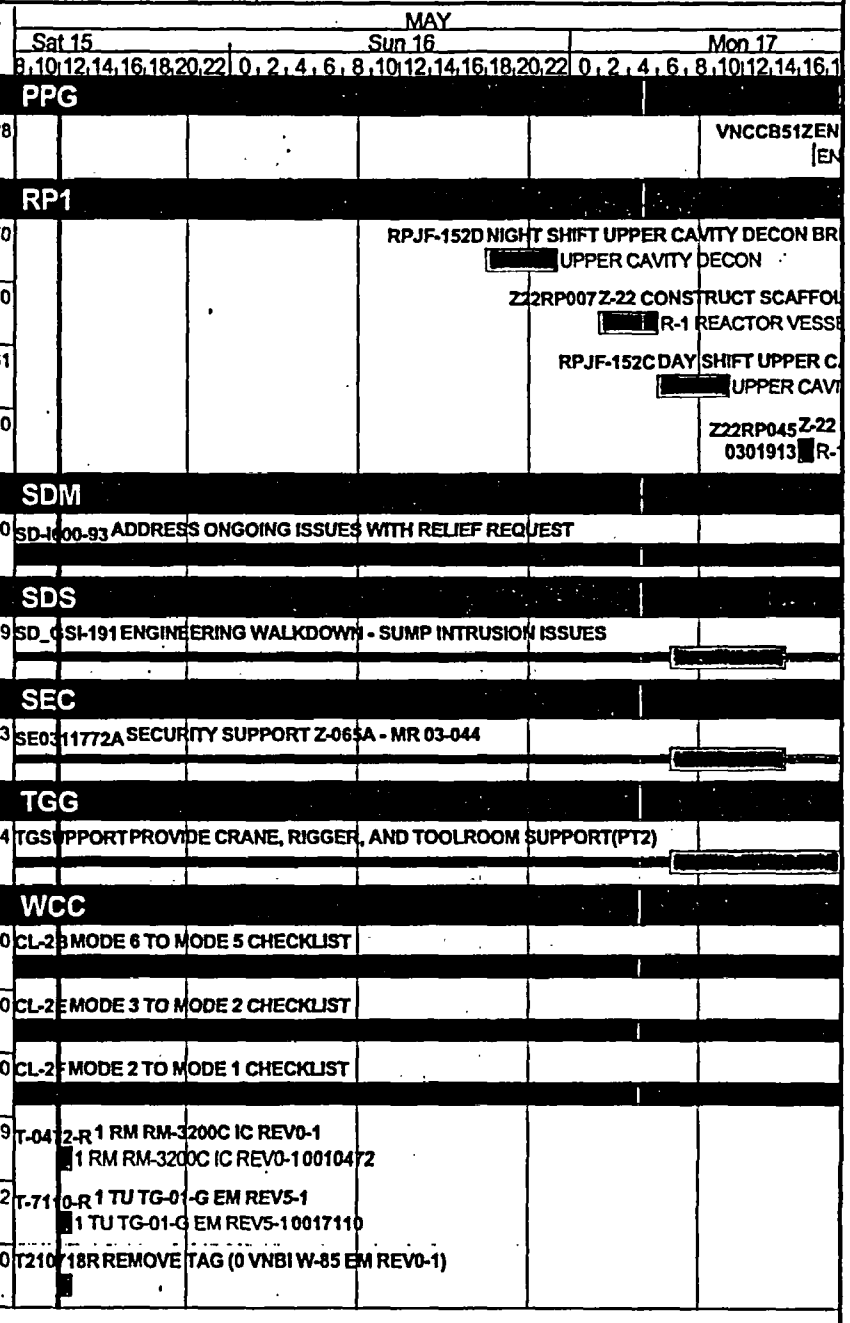

© Primavera Systems, Inc.

U1R28 WORKING SCHEDULE

after 15MAY04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF
WORK CONTROL CENTER											
240	1	T-0510-R	WCC		W-1B1/1B2	1 VNCC W-1B1/1B2 MM REV0-1	3	15MAY04 12:00	15MAY04 14:59		70
241	1	T-3310-R	WCC		P-001A-M	1 RC P-1A-M RMP 9002-1 EM REV1-1	1	15MAY04 13:00	15MAY04 13:59		0
242	0	T201642H	WCC		W-086	HANG TAG (0 VNBI W-86 MM REV0-1)	1	15MAY04 13:00	15MAY04 13:59	DR-Y ML-Y ORT3-N R-N	0
243	1	T-1763-R	WCC		SC-966B	1 SC SC-966B MMV REV0-1	2	15MAY04 13:00	15MAY04 14:59		0
244	0	T201626R	WCC		W-017	REMOVE TAG (0 VNTBO W-17 MM REV0-1)	1	15MAY04 15:00	15MAY04 15:59	DR-Y ML-Y ORT3-N R-N	738
245	1	T-7048-R	WCC		P-28B	1 CS P-28B EM REV2-1	3	15MAY04 15:00	15MAY04 17:59	DR-Y ML-Y ORT3-N R-N	26
246	0	T201475R	WCC		VNTB	REMOVE TAG (0 VNTB VNTB MM REV0-2)	1	15MAY04 16:00	15MAY04 16:59		737
247	0	T201642R	WCC		W-086	REMOVE TAG (0 VNBI W-86 MM REV0-1)	1	15MAY04 18:00	15MAY04 18:59	DR-Y ML-Y ORT3-N R-N	220
248	1	T-3180-H	WCC		P-001A-M	1 RC P-1A-M BALANCE EM REV0-1	1	15MAY04 21:00	15MAY04 21:59		0
249	1	T-3180-R	WCC		P-001A-M	1 RC P-1A-M BALANCE EM REV0-1	1	16MAY04 00:00	16MAY04 00:59		537
250	1	T-3322-R	WCC		P-001A-M	RC P-1A-M RMP 9002-1 EM REV2-1	1	16MAY04 00:00	16MAY04 00:59		0
251	1	T-2407-H	WCC		RMP	1 4.16KV RMP 9364-1 UMBILICAL CORD EM	1	16MAY04 01:00	16MAY04 01:59		34
252	0	T201849H	WCC		HX-038A1/A	HANG TAG (0 VNCSR HX-38A1/A2 MM REV0-1)	1	16MAY04 03:00*	16MAY04 03:59		2
253	2	T301009R	WCC		ICP-06.021	REMOVE TAG (2 CV F-39A IC REV 0-1)	1	16MAY04 05:00	16MAY04 05:59		724
254	1	T-2709-R	WCC		MS-2018	1 MS MS-2018 MMV REV0-1	1	16MAY04 07:00	16MAY04 07:59		0
255	1	T-8293-H	WCC		HX-1B	1 MS HX-1B SMP OPS REV1-1	1	16MAY04 07:00	16MAY04 07:59	DR-Y ML-Y ORT3-Y R-N	0
256	1	T-8293-R	WCC		HX-1B	1 MS HX-1B SMP OPS REV1-1	1	16MAY04 11:00	16MAY04 11:59	DR-Y ML-Y ORT3-Y R-N	73
257	0	T201849R	WCC		HX-038A1/A	REMOVE TAG (0 VNCSR HX-38A1/A2 MM REV0-1)	1	16MAY04 12:00	16MAY04 12:59		717
258	1	T-5553-R	WCC		HX-15A	1 VNCC HX-15A MM REV2-1	2	16MAY04 12:00	16MAY04 13:59		0

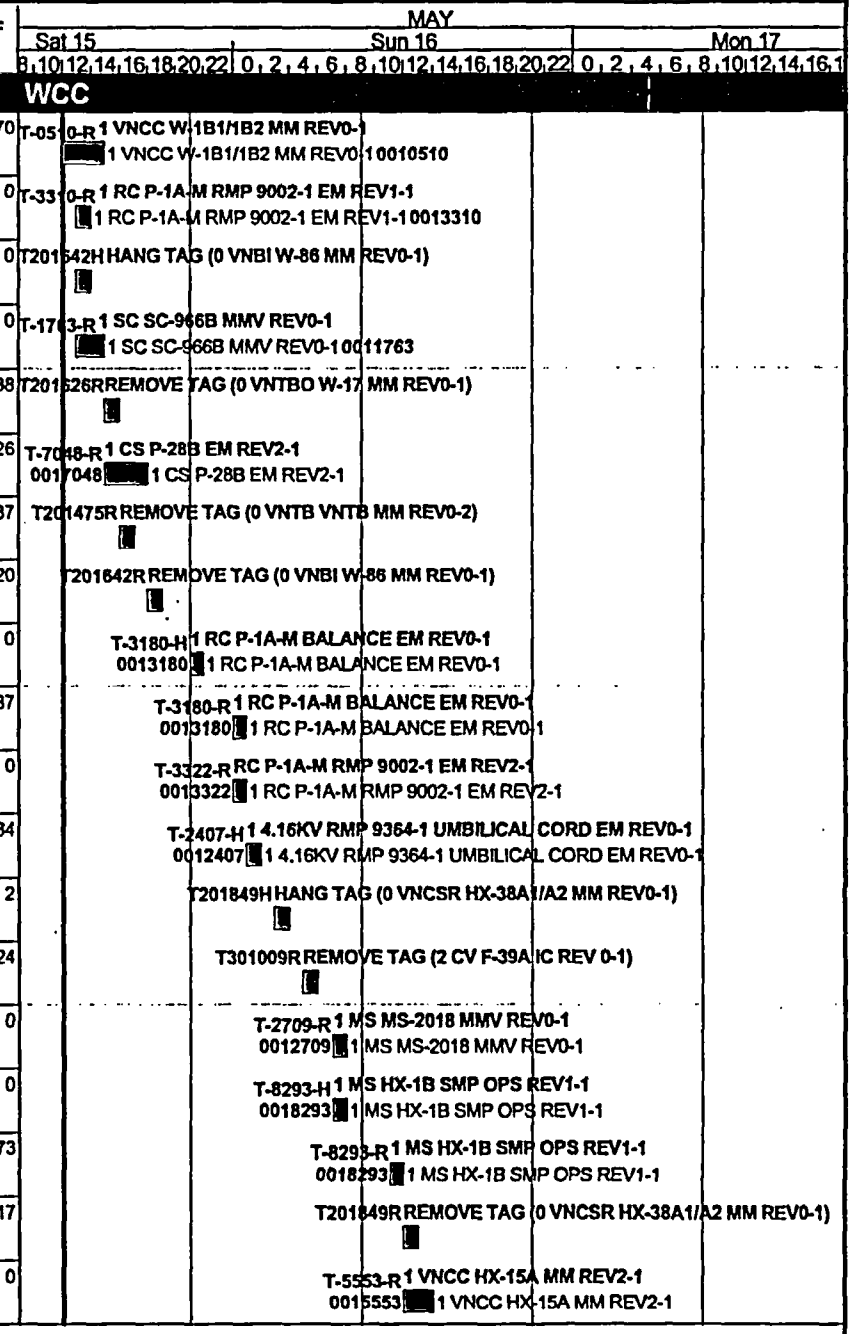

© Primavera Systems, Inc.

U1R28 WORKING SCHEDULE

after 15MAY04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF
WORK CONTROL CENTER											
259	1	T-1302-R	WCC		P-028B	1 CS P-28B MM REV0-1	4	16MAY04 16:00	16MAY04 19:59	DR-Y ML-Y ORT3-Y R-N	0
260	1	T-0677-H	WCC		ICP-10.24	1 ESF ICP-10.24 IC REV0-1	1	16MAY04 18:00	16MAY04 18:59		23
261	1	T-8170-H	WCC		TG-01-T	1 TU TG-01-T REV9-1	1	16MAY04 18:00	16MAY04 18:59	DR-Y ML-Y ORT3-Y R-N	710
262	1	T-8868-H	WCC		HX-1A	1 MS HX-1A WLU MMV REV3-1	1	16MAY04 18:00	16MAY04 18:59		0
263	1	T-8930-H	WCC		HX-1A	1 MS HX-1A SMP OPS REV1-1	1	16MAY04 18:00	16MAY04 18:59		1
264	1	T-5947-H	WCC		MAIN	1 MS MAIN STEAM MMV REV2-1	2	16MAY04 18:00	16MAY04 19:59	DR-N ML-N ORT3-N R-N	0
265	1	T-5949-H	WCC		T-23	1 FD T-23 MMV REV2-1	2	16MAY04 18:00	16MAY04 19:59		0
266	1	T-8868-R	WCC		HX-1A	1 MS HX-1A WLU MMV REV3-1	1	16MAY04 19:00	16MAY04 19:59		0
267	1	T-5947-R	WCC		MAIN	1 MS MAIN STEAM MMV REV2-1	1	16MAY04 20:00	16MAY04 20:59		3
268	1	T-5948-R	WCC		T-23	1 FD T-23 MMV REV1-1	1	16MAY04 20:00	16MAY04 20:59		3
269	1	T-5949-R	WCC		T-23	1 FD T-23 MMV REV2-1	4	16MAY04 20:00	16MAY04 23:59		270
270	1	T-1643-R	WCC		RMP-9133	1 AF RMP-9133 EM REV0-1	1	16MAY04 21:00	16MAY04 21:59		118
271	1	T-8930-R	WCC		HX-1A	1 MS HX-1A SMP OPS REV1-1	1	16MAY04 23:00	16MAY04 23:59		0
272	1	T-7043-R	WCC		P-028A-M	1 CS P-28A-M EM REV0-1	1	17MAY04 04:00	17MAY04 04:59	DR-Y ML-Y ORT3-Y R-N	0
273	1	T-7047-H	WCC		P-028A-M	1 CS P-28A-M EM REV1-1	1	17MAY04 04:00	17MAY04 04:59	DR-Y ML-Y ORT3-Y R-N	0
274	1	T-0964-H	WCC		62/A01	1 MRR 62/A01 RMP 9302-1 EM REV0-1	1	17MAY04 05:00	17MAY04 05:59		0
275	1	T-3778-H	WCC		F89-112	1 345KV F89-112 APS REV0-1	2	17MAY04 05:00	17MAY04 06:59		1
276	1	T301106H	WCC		P-011A	HANG TAG (1 CC P-11A MM REV0-1)	1	17MAY04 08:00*	17MAY04 08:59		0
277	1	T-7047-R	WCC		P-028A-M	1 CS P-28A-M EM REV1-1	1	17MAY04 09:00	17MAY04 09:59	DR-Y ML-Y ORT3-Y R-N	0

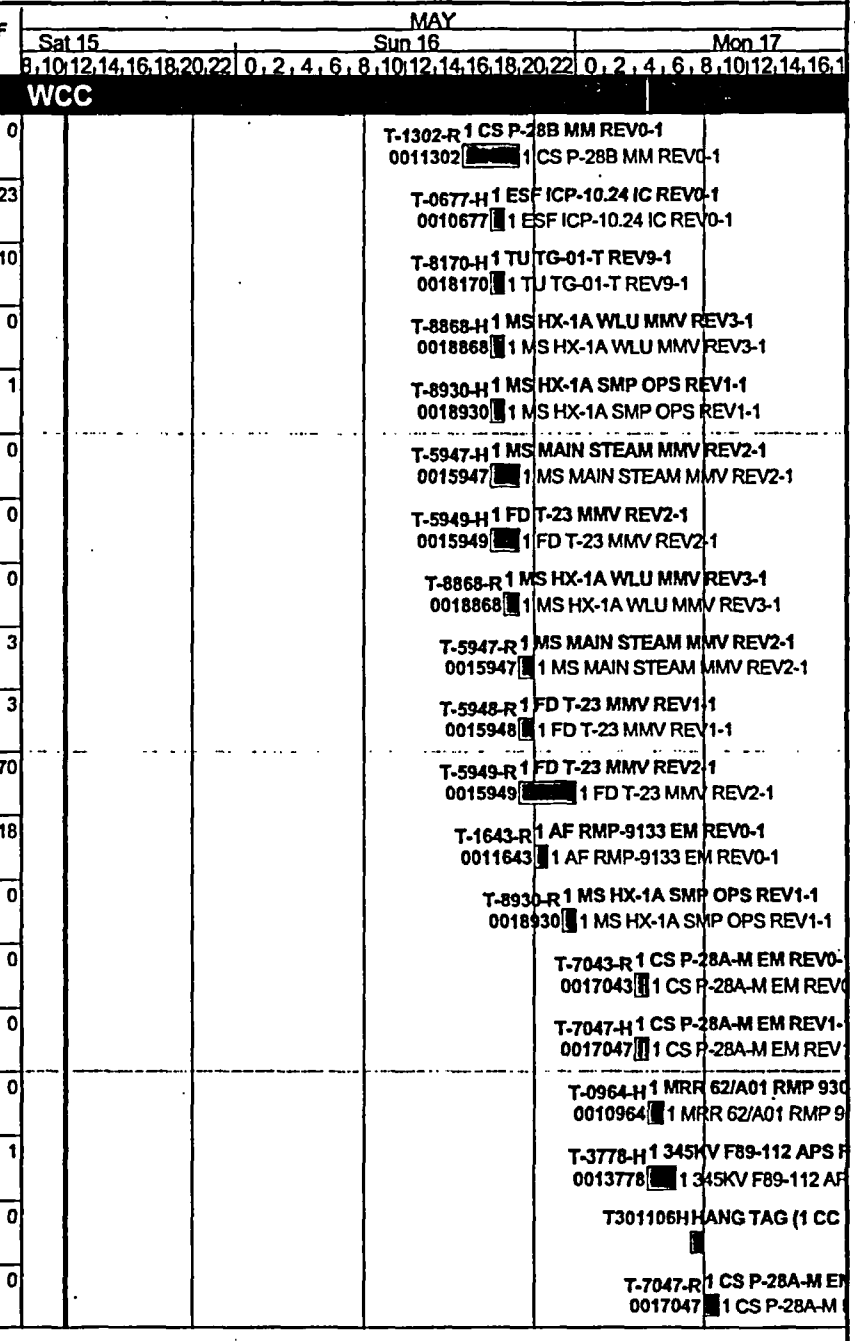

© Primavera Systems, Inc.

U1R28 WORKING SCHEDULE

after 15MAY04 12:00
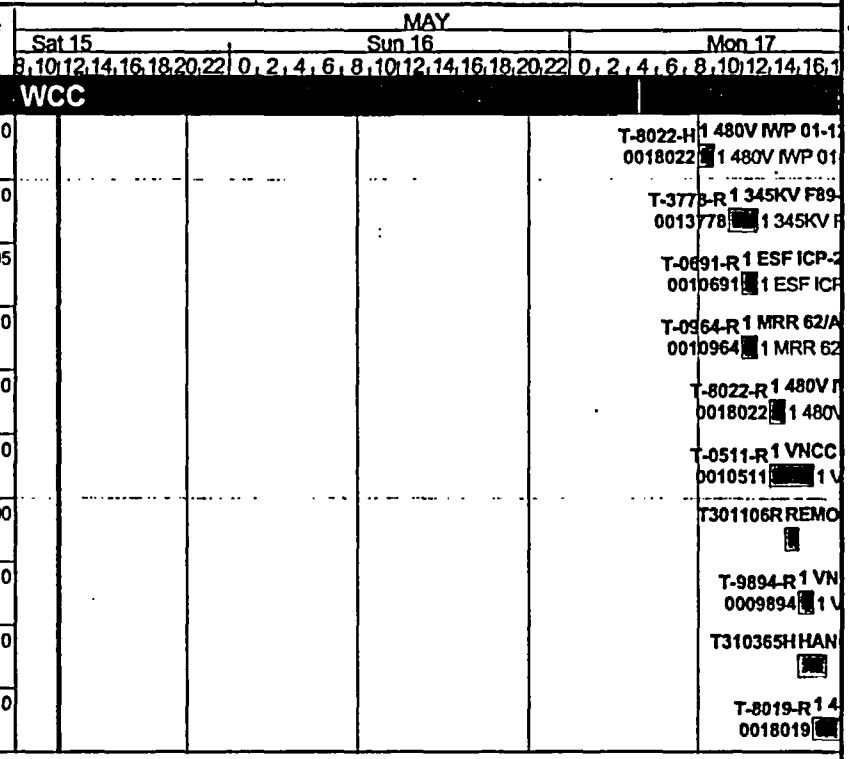
#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	RISK	MF
WORK CONTROL CENTER											
278	1	T-8022-H	WCC		IWP	1 480V IWP 01-128*E-FN (W-13B1) EM REV0-2	1	17MAY04 09:00*	17MAY04 09:59	DR-N ML-N ORT3-N R-N	0
279	1	T-3778-R	WCC		F89-112	1 345KV F89-112 APS REV0-1	2	17MAY04 11:00	17MAY04 12:59		0
280	1	T-0691-R	WCC		ICP-2.19	1 ESF ICP-2.19 IC REV0-1	1	17MAY04 12:00	17MAY04 12:59		205
281	1	T-0964-R	WCC		62/A01	1 MRR 62/A01 RMP 9302-1 EM REV0-1	1	17MAY04 12:00	17MAY04 12:59	DR-Y ML-Y ORT3-Y R-N	0
282	1	T-8022-R	WCC		IWP	1 480V IWP 01-128*E-FN (W-13B1) EM REV0-2	1	17MAY04 14:00	17MAY04 14:59	DR-N ML-N ORT3-N R-N	0
283	1	T-0511-R	WCC		W-1C1/1C2	1 VNCC W-1C1/1C2 MM REV0-1	3	17MAY04 14:00	17MAY04 16:59		0
284	1	T301106R	WCC		P-011A	REMOVE TAG (1 CC P-11A MM REV0-1)	1	17MAY04 15:00	17MAY04 15:59		690
285	1	T-9894-R	WCC		W-001C1	1 VNCC W-1C1/1C2 EM REV0-1	1	17MAY04 16:00	17MAY04 16:59		0
286	0	T310365H	WCC		HX-055A-1	HANG TAG (0 DG G-1 HX-55A1/2 MM REV0-4)	2	17MAY04 16:00	17MAY04 17:59		0
287	1	T-8019-R	WCC		W-013B1	1 480V IWP 01-128*E-FN (W-13B1) CAUT REV0-1	2	17MAY04 17:00	17MAY04 18:59	DR-N ML-N ORT3-N R-N	0
