NMC
Committed to Nuclear Excellence

FEEL THE POWER
JOURNEY OF EXCELLENCE
POINT BEACH • U1R28

Point Beach Nuclear Plant
U1R28
OCC Interactive Turnover

Meeting Agenda
Wednesday, June 2, 2004

Start Time: **1800** **NSB Cafeteria**

BRIEFING NOTES

ATTENDEES
Shift Outage Directors
Shift Outage Managers (SOM)
Operations Coordinators (SOC)
Maintenance Coordinators (MOC)
Engineer / Projects Coordinators (EOM)
Rad Protection Manager (RPM)
Site Safety Coordinator (SSC)
Shutdown Safety Assessor (SSA)
Site Management (SSM)
General Supervisors
First Line Supervisors

Agenda
1. Safety Issue Discussion (SSC)
2. Radiation Protection (RPM)
3. Operations Coordinator Turnover (SOC)
4. Shutdown Safety Assessment (SSA)
   a. Containment Fire Loading
      SAT / UNSAT → Review Deficiencies
5. Maintenance Coordinator Turnover (MOC)
6. Engineering Coordinator Turnover (EOM)
7. Major Projects Update (EOM)
8. Schedule Review (SOM)
9. Management Expectations (SSM)
10. ACEMAN Assessment Results (SOM)
11. Shift Goals (SOM)

Items Included in Daily Package:
- Site Communication
- Safety Snippet
- Outage Alara Report
- Outage Status Report
- Shutdown Safety Assessment
- Defined Critical Path
- Work Activity Risk Assignment
- Outage Schedule

Information in this record was deleted in accordance with the Freedom of Information Act, exemptions 4
FOIA 2004-0282

V-65

NMC
Committed to Nuclear Excellence

FEEL THE POWER
JOURNEY OF EXCELLENCE
POINT BEACH • U1R28

Point Beach Nuclear Plant
U1R28 Refueling Outage

Safety Topic for week of May 30 – June 5, 2004
Theme for the week
This week's focus is looking back at our **reported injuries so far in 2004**. There were 52 injuries to workers on the site so far this year. That's almost more than we typically see in 2 years! **That's an injury every 3 days!** Our goal is NONE. ***Let's review what going on and discuss how to prevent anything else from occurring in 2004.***
Daily Safety Snippets
Sunday
"Twist and strains are no one's gains"
Mechanic Electrician was removing a temporary rigging fixture from a roof beam and felt a strain in the upper back. *Remember your Save A Back training!*
Monday
"Stretching before you work may reduce the strains that lurk."
An engineer experienced severe back pain upon exiting containment. The employee was bending in order to exit the accident fan coolers prior to the incident. Medical treatment was necessary and this was an OSHA recordable event.
Tuesday
"If your backfield is in motion, use a zone defense."
Contract electrician was pulling wire for a conduit through a junction box for the security upgrade project. While bending over to retrieve a pull string, the wind caught the junction box door. It swung and struck the employee in the back.
Wednesday
"It's too late for learning when your skin is already burning."
There have been **3** incidents in the past month where individuals contacted hot equipment and minor burns resulted. Two in maintenance – one was during welding activity, the second was when an employee came in contact with a hot muffler on a pump. The third was when one of the M&M Lunch employees placed her hand on a hot grill. *What human performance barriers are we missing here?*
Thursday
"Where danger lingers, watch your fingers"
What is the most likely injury the site has? Given the age of the work force, it should be strains. But it's hand injuries! **22** injuries so far this year! Example – chem. tech was removing a glass funnel from tygon tubing. The funnel separated from the stem, resulting in a minor finger laceration. *The wrong technique was used for doing this work.*
Friday
"Never gamble with more than you can handle"
Two situations to review here. One was a RP worker and contractor trying to maneuver material through a security door. Rather than calling security, they figured they could "beat the door." They beat it all right. And the contractor suffered a leg injury from the steel hitting him. The second was an OAII carrying a large box through a door. She ended up catching hitting her hand on the doorframe. *How can we prevent these injuries?*
Saturday
"The brain is mightier than the brawn"
Contract insulator struck his head on an I-beam while reaching for material. He was wearing the right PPE, but felt neck discomfort from the hit. The worker knew the beam was a potential hazard, but did not take the time to soften it prior to beginning his work.

Point Beach Nuclear Plant Outage 1R28

DAY 59

Supporting Operational Excellence

Outage Radiation Performance

Path

Picture

Meets

Doesn't Meet Exceeds

Definition/Goal

This indicator measures cumulative dose radiation exposure and total number of personnel-contamination events (PCE's > 5000 cpm) during refueling outages. The dose indicator is measured in Rem and individual PCE events.

Meets:	<=92 Rem	Actual Cum.	
Exceeds:	<=88 Rem	Dose:	85.608 Rem
Meets: <= 18	Exceeds: <= 12	Actual PCE's:	11

Responsible Manager/Owner

Stu Thomas

Analysis and Actions

Day 59 - June 1
Actual = 0.157
Cumulative = 85.608
Cumulative Forecast =91.992

Personnel Contamination Events

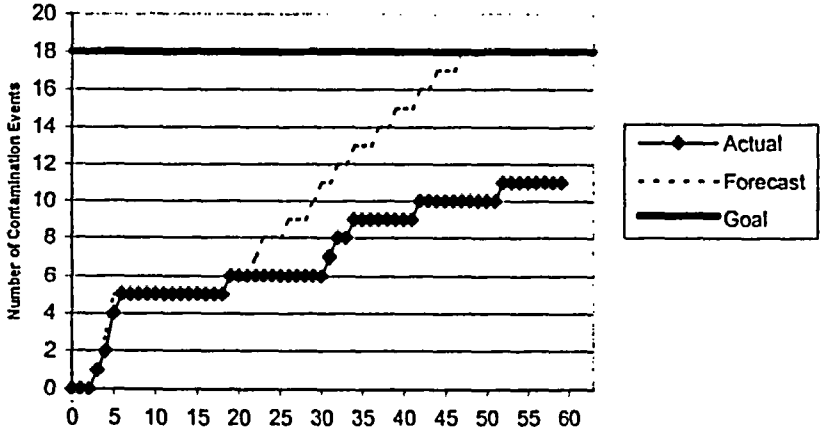

Cummulative Dose Exposure

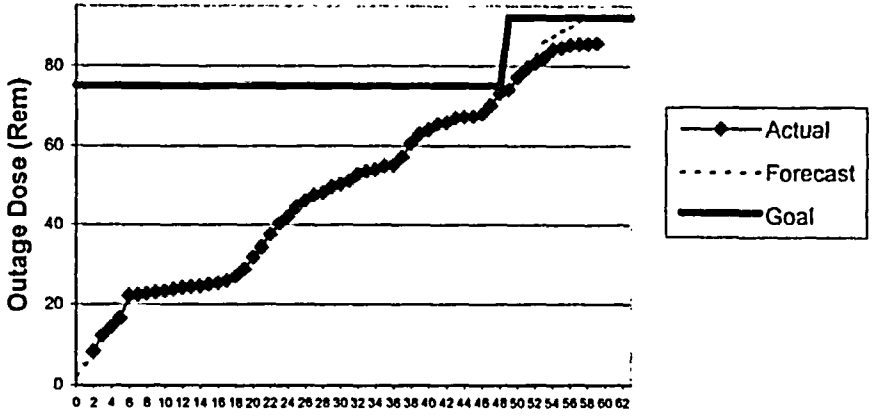

NMC
Committed to Nuclear Excellence

Outage Status Report

Plant: Point Beach Unit 1 **Day:** Wednesday **Today's Date / Time:** 6/02/04 1500

Outage Duration: Day 60 Of Refueling Outage Number U1R28

Safety Status

Industrial - Within the last 12 hours

OSHA Recordables 0 First Aid cases 0 Near misses 0

Total for this outage 1

Summary:

Radiological

Dose to date 85.608 Projected to date *91.992 Outage Goal ≤92 R

Difference -6.384 * Reforecast on 5/23 Number of PCEs 11

Summary:

Nuclear

Significant human performance errors and events in last 24 hours 0

Summary:

Plant Status

Mode: ☐ Hot Standby *(Mode 3)* ☒ Hot Shutdown *(Mode 4)* ☐ Cold Shutdown *(Mode 5)* ☐ Refueling Shutdown *(Mode 6)*

RCS: Temperature: 240° Pressure: 325 psig RV Level: Pressurizer Solid

Time to Boil: N/A

Shutdown Safety Assessment Protected Equipment:

- None

Major Activities Completed in Last 24 Hours	Critical Path and Near Critical Path Activities (Next 24 Hours)
• TS-30 High & Low Head SI Check Valve Test • TS-10 Upper Containment Hatch Pressure Test • IT-530E LRPM Test of RHR System • Heatup RCS to 190°F • Cold Rod Functional Testing • Completed Containment Purge Testing • IT-1A SI Pump & Valve Test • Established Containment Integrity • Entered Mode 4 Hot Shutdown • Heatup RCS to 240°F	• RCS Heatup to 250-270°F • Establish Pzr Bubble • Secure RHR • Start RHR Common Work • Enter Mode 3

Significant Outstanding Issues

Date	Issue	Due	Responsibility
5/17/04	Rx Head Relaxation Request	6/04/04	Jim Schweitzer

Upcoming Major Milestones

	Scheduled		Actual			Scheduled		Actual	
	Date	Time	Date	Time		Date	Time	Date	Time
Cooldown <200°	4/03/04	2100	4/03/04	2230	RCS Fill & Vent	4/23/04	1500	5/31/04	0653
Head Lift	4/09/04	0900	4/21/04	1550	Heatup >200°	4/25/04	0900	6/2/04	1341
Refueled	4/14/04	0300	5/02/04	1848	Reactor Critical	4/28/04	0800		
RV Headset	4/18/04	1900	5/23/04	1338	On-Line	4/30/04	0100		

PBNP SHUTDOWN SAFETY ASSESSMENT AND FIRE CONDITION CHECKLIST

OUTAGE SAFETY ASSESSMENT

UNIT: 1 DATE: June 2, 2004 TIME: 1400

KEY SAFETY FUNCTIONS:

REACTIVITY:	GREEN
CORE COOLING:	GREEN
POWER AVAILABLE:	GREEN
INVENTORY:	GREEN
CONTAINMENT:	GREEN
SFP COOLING:	NA

PROTECTED EQUIPMENT:

COMMENTS:

Ex4

- One flow path for both Reactivity and Inventory changed from 1) charging pump P-2C via the auxiliary charging line, to 2) RWST to the 'B' Safety Injection train to reflect the isolation of the auxiliary charging line.
- Instrument Air Compressor K-2B removed from Unit 2 protected equipment list for maintenance.

Defined Critical Path

U	ID	DESCRIPTION	OD	RD	Cal	U	SYS	EQID	TF
02JUN04 00:00									
1	CAMP-112	RCS OXYGEN REMOVAL WITH HYDRAZINE	3	1	1	1	RC	CAMP-112	0
1	OP1A-032	VERIFY RCS OXYGEN IN SPEC	1	1	1	1	RC	OP-1A	3
1	OP1A200F	HEATUP RCS TO 200 DEGREES	1	1	1	1	RC	OP-1A	0
1	COLDSDNY	RCS ENTERS HOT SHUTDOWN	0	0	1	1	XX	MILESTONE	0
1	OP1A250F	HEATUP RCS TO 250 - 270 deg F	3	3	1	1	RC	OP-1A	0
1	OP1A-050	HEATUP PRESSURIZER	4	4	1	1	RC	OP-1A	0
1	OP1A-060	ESTABLISH PZR BUBBLE	1	1	1	1	RC	OP-1A	0
1	OP7B-010	SECURE OPERATING RHR PUMPS	1	1	1	1	RH	OP-7B	0
Op	RHX01A	START RHR COMMON WORK	0	0	1	1	RH	MILESTONE	0
1	B52-424M	BUS STAB PMT "1RH-701"	2	2	1	1	480V	B-42	0
1	B52-424ME	BUS STAB PMT "1RH-701"	4	4	1	1	480V	B-42	0
03JUN04 00:00									
1	T-6316-H	1 RH RH-700 EM REV1-1	1	1	1	1	RH	RH-700	2
1	T-0482-H	1 SI SI-852A EM REV0-1	2	2	1	1	SI	SI-852A	4
1	OP7B-020	COOLDOWN AND BORATE RHR	6	6	1	1	RH	OP-7B	0
1	OP1A300F	HEATUP RCS TO 295 - 305 deg F	1	1	1	1	RC	OP-1A	4
1	EM0215176	RH-700 MOV ACTUATOR CHECK-OUT	12	12	1	1	RH	RH-00700-O	2
1	TS-030C	TS-30 (SECTION 5.23) TEST OF SI-867B	1	1	1	1	SI	O-TS-030	0

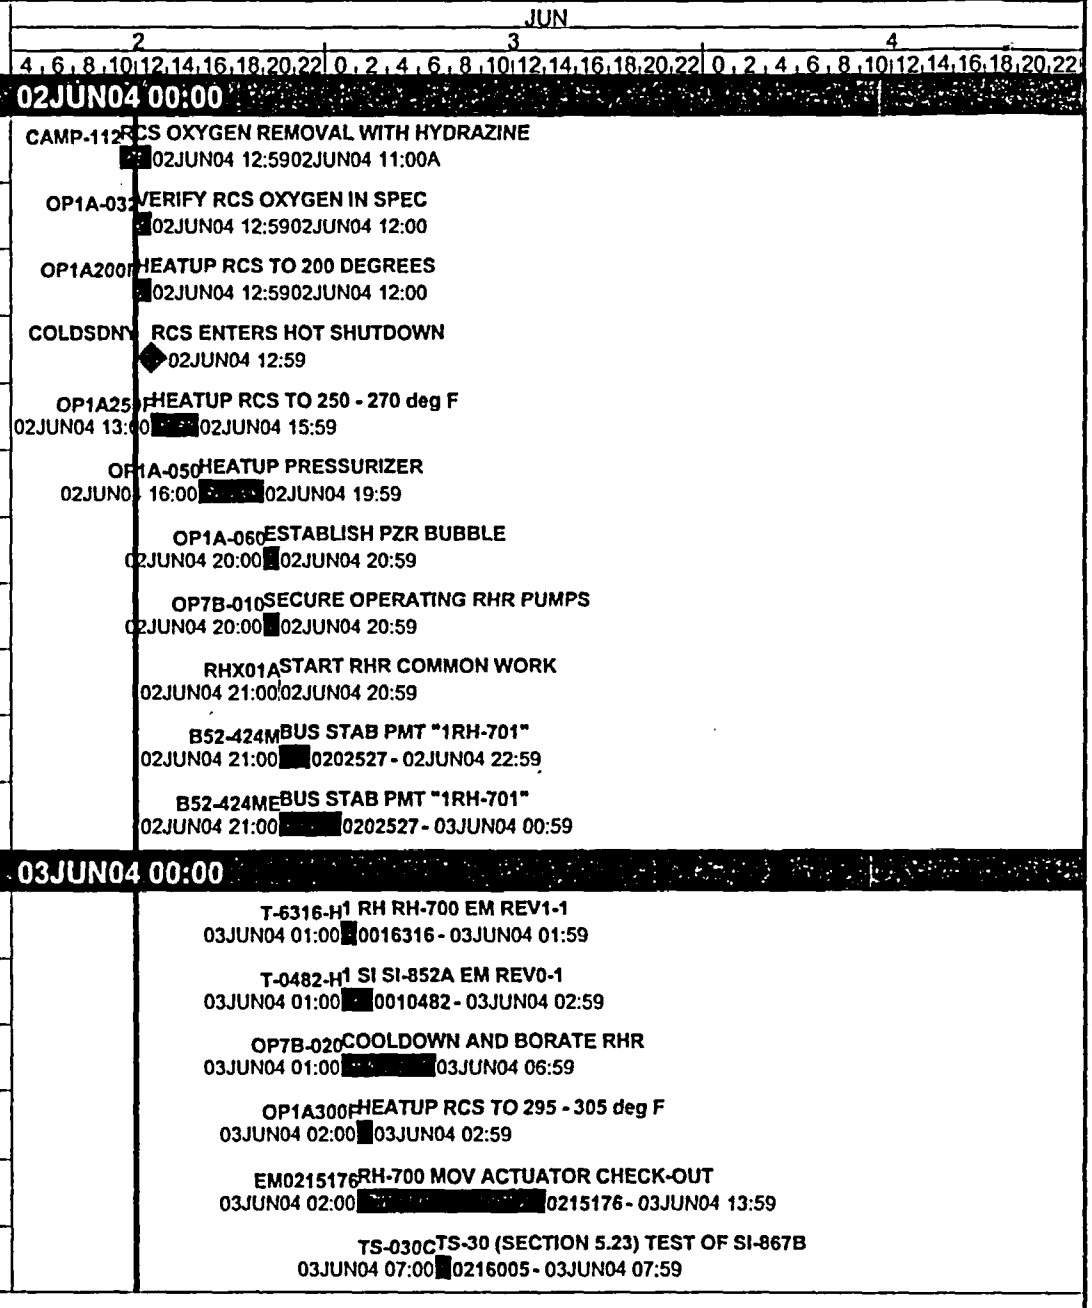

© Primavera Systems, Inc.

Defined Critical Path

U	ID	DESCRIPTION	OD	RD	Cal	U	SYS	EQID	TF
03JUN04 00:00									
1	EM0403305	SI-852A-O PERFORM STEM LUBE AND FBJ INSPECTION	10	10	1	1	SI	SI-00852A-	0
1	OP1A-090	DISABLE LTOP	1	1	1	1	RC	OP-1A	0
1	IT-290B	IT-290B, 1P-29 AFP OVERSPEED TEST	4	4	1	1	AF	O-IT-0290B	0
1	MM0214127A	MM SUPPORT FOR P-29-T OVERSPEED TRIP TEST	4	4	1	1	AF	P-029	0
1	IT-090A	ATMOSPHERIC STEAM DUMP VALVES STROKE	1	1	1	1	MS	O-IT-0090A	4
1	T-2076-H	1 AF P-29 RECOUPLE MM REV0-1	2	2	1	1	AF	P-029	0
1	OP0215176A	RH-700 MOV ACTUATOR OPS PMT PER O-IT-003D	1	1	1	1	RH	RH-00700-O	2
1	T-6316-R	1 RH RH-700 EM REV1-1	1	1	1	1	RH	RH-700	2
CP	MM0214127C	P-29-T RECOUPLE	2	2	1	1	AF	P-029	0
1	RHX01Z	END RHR COMMON WORK	0	0	1	1	RH	MILESTONE	2
1	OP0403305	SI-852A-O PERFORM PMT STROKE	1	1	1	1	SI	SI-00852A-	0
1	T-2076-R	1 AF P-29 RECOUPLE MM REV0-1	1	1	1	1	AF	P-029	0
1	T-9265-R	1 AF P-29 UNCOUPLED DSS REV0-1	1	1	1	1	AF	P-29	0
1	MAYX350F	RCS TEMP MAY EXCEED 350 F	0	0	1	1	XX	ADMIN MS	0
1	OP1A370F	HEATUP RCS TO 370 deg F	2	2	1	1	RC	OP-1A	0
1	OP1A-095	VERIFY RHR VALVE OPERABILITY	2	2	1	1	RC	OP-1A ATT.	0
1	OP1A0650	RAISE RCS PRESSURE TO 650 PSIG	1	1	1	1	RC	OP-1A	0
1	OP1A0800	RAISE RCS PRESSURE TO 800 PSIG	1	1	1	1	RC	OP-1A	0

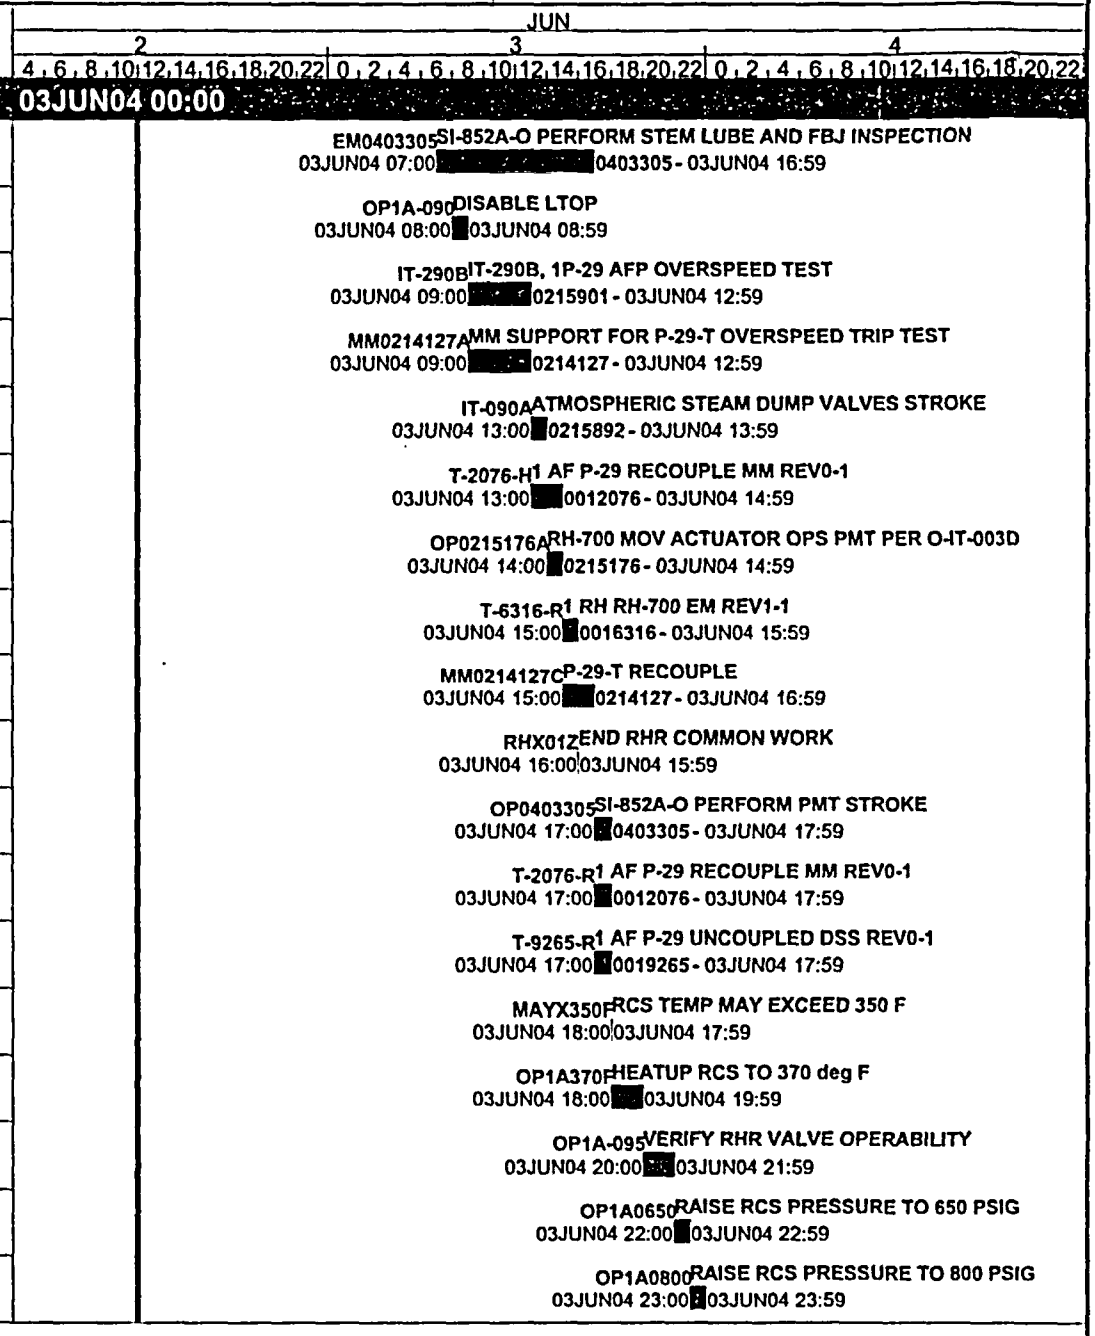

© Primavera Systems, Inc.

Defined Critical Path

U	ID	DESCRIPTION	OD	RD	Cal	U	SYS	EQID	TF
03JUN04 00:00									
1	OP1A450F	HEATUP RCS TO 450 - 470 deg F	5	5	1	1	RC	OP-1A	0
04JUN04 00:00									
1	B52-424F	BUS STAB PMT "1SI-841B"	1	1	1	1	480V	B-42	0
1	B52-424FE	BUS STAB PMT "1SI-841B"	2	2	1	1	480V	B-42	0
1	OP1A-040	ALIGN SI ACCUMULATORS	2	2	1	1	SI	OP-1A	0
1	OP1A500F	RAISE RCS TEMP/PRESS TO 547/2235	5	5	1	1	RC	OP-1A	0
1	IC2.17-1	ICP 2.17 REACTOR PROTECTION LOGIC TEST	4	4	1	1	RP	ICP-02.017	4
1	RESP-3.1B	OBTAIN FINAL RCS RTD DATA PER RESP 3.1	1	1	1	1	MMS	RESP 3.1	2
1	IT-230-A	INITIATE RCS LEAK TEST	0	0	1	1	RC	O-IT-0230	0
1	NOP-NOT	RCS AT NOP NOT NOL	0	0	1	1	XX	MILESTONE	0
1	ICRTDSWOFF	REMOVE LOOP RTD SWITCHING UNIT	1	1	1	1	RP	RP	2
1	IT-230-B	ADJUST RCS TO TEST PRESSURE	2	2	1	1	RC	O-IT-0230	0
1	IC10.1RES	ESF RESISTANCE CHECKS (ICP-10.001)	1	1	1	1	ESF	ICP-10.001	2
1	IC2.20-1	RX PROTECTION ANN VERIFICATION (ICP-02.020-1)	2	2	1	1	MMS	ICP-02.020	2
1	OP1A-130	REINSTALL INSUL AFTER RCS LEAK TEST	3	3	1	1	MS	INSUL-MS	4
1	EP0403495A	OPERATING SUPPORT OF FINAL RCS WALKDOWN	4	4	1	1	RC	PT-RCS-1	4
1	CESG001TI	REINSTALL INSULATION ON SG A AND B PRI MANWAYS	6	6	1	1	MS	INSUL-MS	4
1	PT-RCS-001	RCS PRESSURE TEST PER 1-PT-RCS-001	8	8	1	1	RC	PT-RCS-1	0

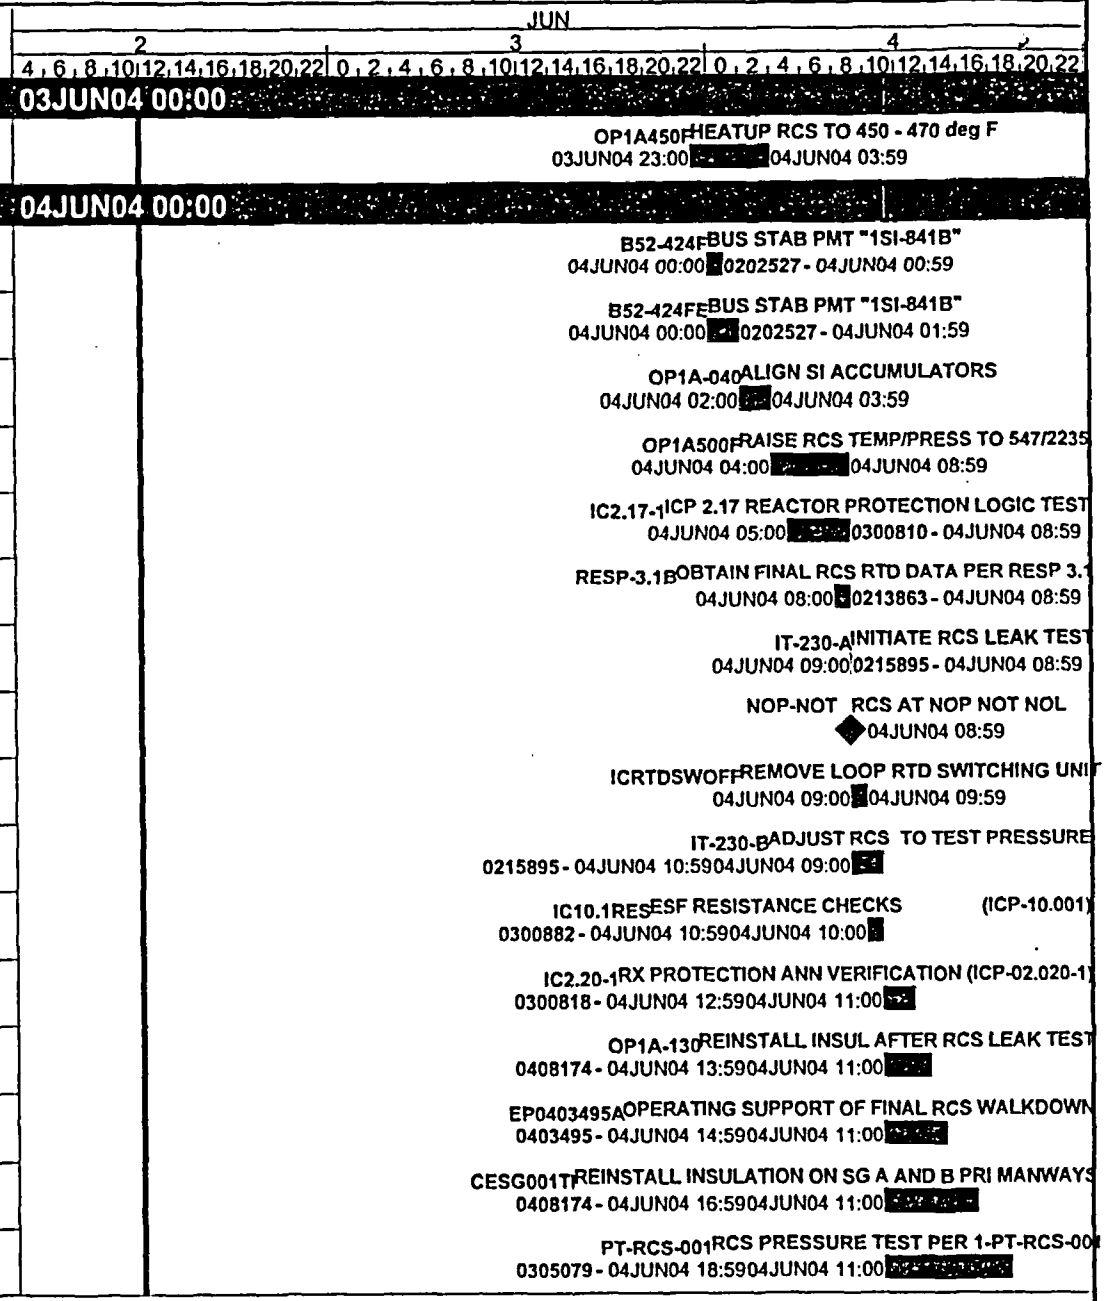

© Primavera Systems, Inc.

Defined Critical Path

U	ID	DESCRIPTION	OD	RD	Cal	U	SYS	EQID	TF
04JUN04 00:00									
1	IC2.20-2	RX PROTECTION SW VERIFICATION (ICP-02.020-2)	2	2	1	1	MMS	ICP-02.020	2
1	RESP-3.1PR	CLOSE REACTOR TRIP BREAKERS FOR RPI TESTING	0	0	1	1	MMS	RESP 3.1	2
1	IC4.29-2ZR	RPI ZERO ADJUST	3	3	1	1	RPI	ICP-04.029	2
1	CESGA001SR	REMOVE SCAFFOLDING FOR S/G A HANDHOLES	8	8	1	1	MS	HX-001A	4
1	CESGB001SR	REMOVE SCAFFOLDING FOR S/G B HANDHOLES	8	8	1	1	MS	HX-001B	4

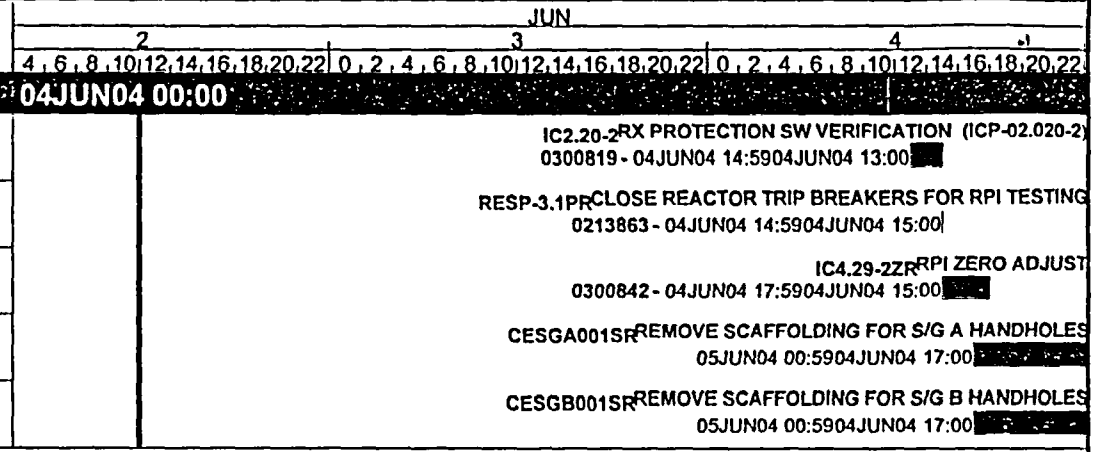

11

© Primavera Systems, Inc.

Work Activity Risk Assignment

U	ACT ID	WO ST	GRP	HPE RISK	EQUIPMENT	Activity Description	Cal ID	DUR	START	FINISH
CHEMISTRY										
2	CH0300495	76	CH	DR-Y ML-Y ORT3-Y R-M	CHEM-SAMPLING	UNIT 2 SI ACCUMULATOR SAMPLING/	Z	1	03JUN04 10:00	03JUN04 10:59
I&C MAINTENANCE										
2	IC0310325	76	IC	DR-Y ML-Y ORT3-Y R-M	FM	2FM DISPLAY STICKS	Z	8	03JUN04 10:00	04JUN04 09:59
2	IC0407745	76	IC	DR-Y ML-Y ORT3-Y R-M	LT-00939	LT-939 DRY LEG DRAIN CHECK	Z	1	03JUN04 10:00	03JUN04 10:59
1	IC2.20-1	76	IC	DR-N ML-Y ORT3-N R-M	ICP-02.020	RX PROTECTION ANN VERIFICATION (ICP-02.020-1)	1	2	04JUN04 11:00	04JUN04 12:59
1	IC2.20-2	76	IC	DR-N ML-Y ORT3-N R-M	ICP-02.020	RX PROTECTION SW VERIFICATION	1	2	04JUN04 13:00	04JUN04 14:59
NON-DESTRUCTIVE TESTING										
1	SD-I600-97	76	NDE	DR-Y ML-Y ORT3-Y R-M	R-1	INSPECT PENETRATION 26 DURING IT-230	1	1	04JUN04 11:00	04JUN04 11:59
REACTOR ENGINEERING										
1	REI-10.1A	76	PRE	DR-Y ML-Y ORT3-Y R-M	REI 10.1	USE REI 10.1 TO SET UP THE ADRC.	1	2	04JUN04 09:00	04JUN04 10:59
SITE DESIGN MECHANICAL										
1	SD-I600-98	76	SDM	DR-Y ML-Y ORT3-Y R-M	R-1	REACTOR HEAD INSPECTION RELAXATION	1	1	03JUN04 17:00	03JUN04 17:59
1	SD-I600-94	76	SDM	DR-Y ML-Y ORT3-Y R-M	R-1	MOD 03-041 - HEAD REPAIR CONDITIONAL ACCEPTANCE	1	1	04JUN04 11:00	04JUN04 11:59

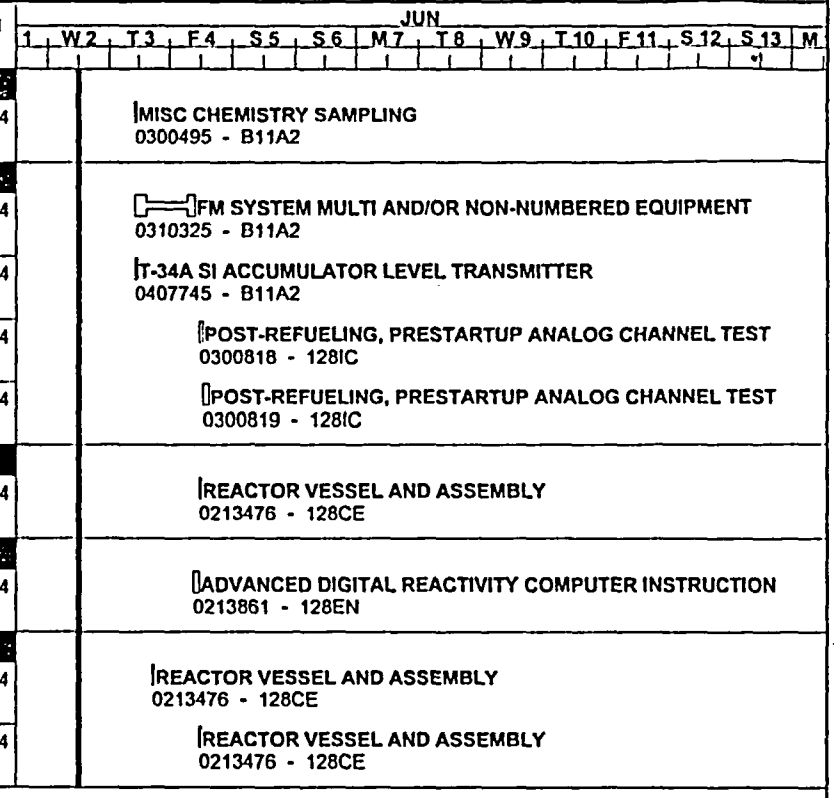

Early Bar
Progress Bar
Critical Activity

© Primavera Systems, Inc.

NMC / WE
PBNP U1 Refueling 28 Outage

LT-81 HUMAN ERROR RISK BARCHART
FL-81 HUMAN ERROR POTENTIAL

U1R28 WORKING SCHEDULE

after 02JUN04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	MF
ADMINISTRATIVE SERVICES										
1	0	EMPFOR4C	ADM		MEETING	EMPLOYEE FORUM	2	02JUN04 12:00*	02JUN04 13:59	504
APPLETON METERING GROUP										
2	1	AP0215133	APM	76	TG-01-G	GENERATOR METERS ON C-01 CALIBRATION	11	31MAY04 10:00A	03JUN04 14:59	0
APPLETON RELAY GROUP										
3	1	AP0215126	APR	76	F52-122	TRIP F52-122 FROM PROTECTIVE	1	02JUN04 08:00A	02JUN04 12:59	0
4	1	AP0303688A	APR	76	A-01	(CONT) CALIBRATE 1A-01 NON-TECH SPEC	50	03JUN04 08:00*	08JUN04 12:59	136
APPLETON STATION GROUP										
5	2	AP0307284	APS	76	X-01-A	COOLING SYSTEM INSPECTION/CLEANING	26	01JUN04 08:00A	05JUN04 10:59	165
CONSTRUCTION ENGINEERING GROUP										
6	0	CE0406128	CE	76	M-2005-6-4	M-2005-6-40-E05 REPAIR PENETRATION	8	03JUN04 07:00*	03JUN04 14:59	111
INSULATION - NPS - D. CHERNEY										
7	1	CE44TGATI	CE3	87	IST-SISI	REINSULATE - FAC PROG - TRB HALL 44 FT	110	17MAY04 14:00A	11JUN04 09:59	0
8	1	TG-30950	CE3	82	TG-01-T	REINSTALL HP TURBINE INSULATION	59	26MAY04 15:00A	07JUN04 22:59	56
9	0	CE216332TI	CE3	77	SERVICE	INSTALL INSULATION FOR 1FD-204B	19	01JUN04 09:00A	03JUN04 14:59	96
10	1	CE300867TI	CE3	87	ICP-05.047	INSTALL INSULATION FOR LS-2377A/B	12	02JUN04 08:00A	03JUN04 07:59	103
11	0	CE927251TI	CE3	77	SERVICE	INSTALL INSULATION FOR 1MS-117	6	02JUN04 15:00*	02JUN04 20:59	0
12	0	CE927250TI	CE3	77	SERVICE	INSTALL INSULATION FOR 1MS-116	6	03JUN04 07:00*	03JUN04 12:59	98
13	0	CE303871TI	CE3	77	SERVICE	INSTALL INSULATION FOR 1MS-42	8	03JUN04 07:00*	03JUN04 14:59	8
14	0	CE301715TI	CE3	77	SERVICE	INSTALL INSULATION FOR 1MS-111 VALVE	10	03JUN04 15:00*	04JUN04 08:59	86
15	1	CE407600TI	CE3	76	INSUL-MS	INSTALL INSULATION FOR 1MS-282	6	04JUN04 09:00	04JUN04 14:59	80

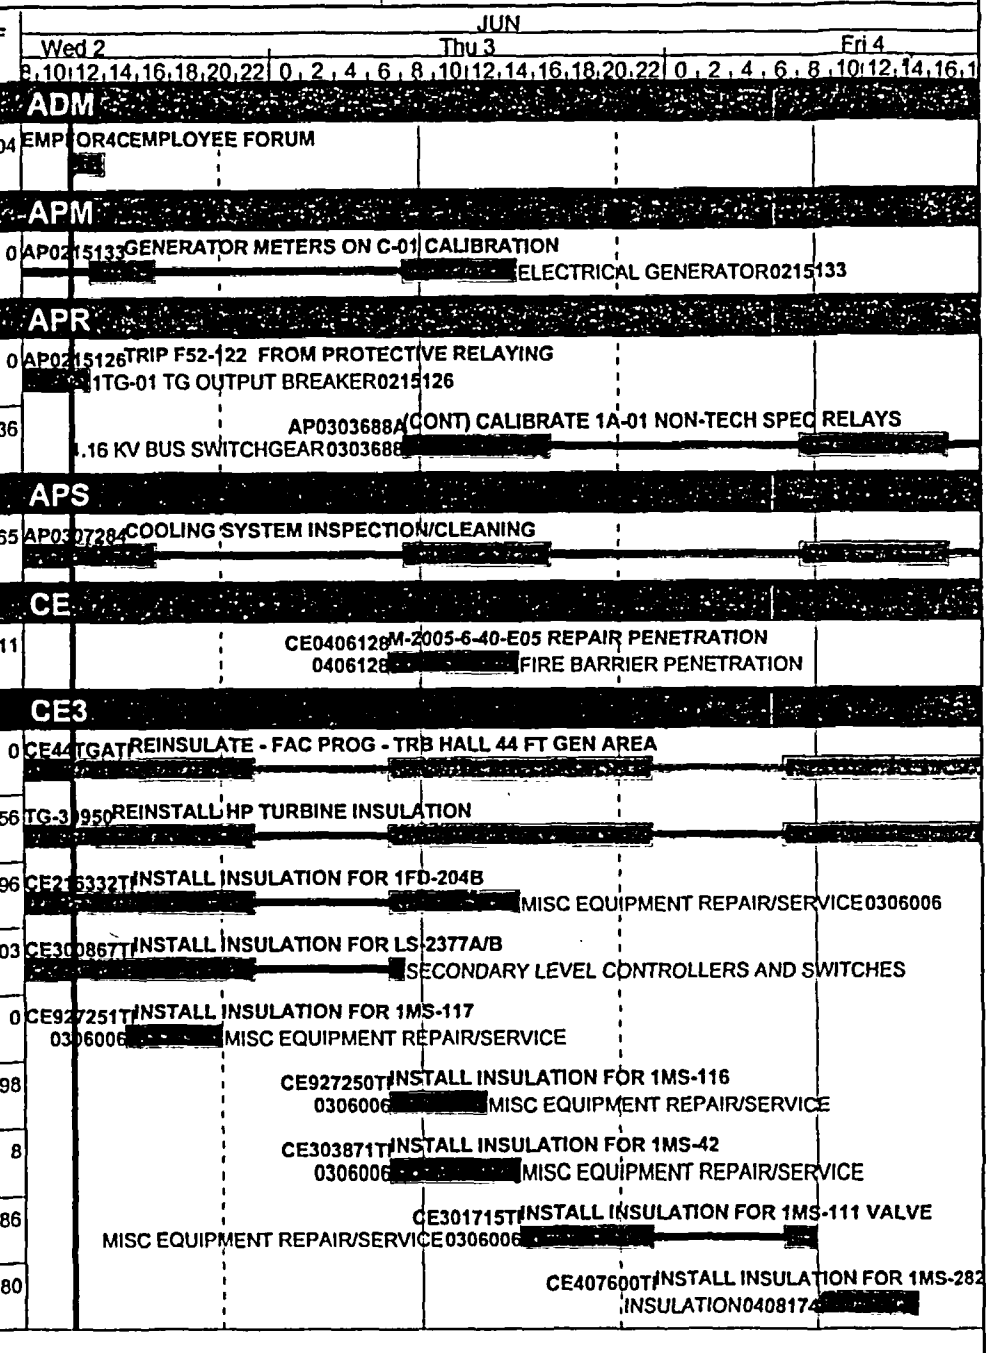

© Primavera Systems, Inc.

LT-03 STANDARD PUBLICATION
FL-03 Execution Publication Set

U1R28 WORKING SCHEDULE

after 02JUN04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	MF
NSULATION - NPS - D. CHERNEY										
16	1	CE407597TR	CE3	76	INSUL-MS	1MS-228 REPACK VALVE	8	04JUN04 09:00	04JUN04 16:59	78
17	1	OP1A-130	CE3	76	INSUL-MS	REINSTALL INSUL AFTER RCS LEAK TEST	3	04JUN04 11:00	04JUN04 13:59	0
18	1	CE311945TI	CE3	76	INSUL-MS	INSTALL INSULATION FOR PZR MANWAY	4	04JUN04 11:00	04JUN04 14:59	455
19	1	CESG001TI	CE3	76	INSUL-MS	REINSTALL INSULATION ON SG A	6	04JUN04 11:00	04JUN04 16:59	0
20	1	CE212702TI	CE3	76	INSUL-MS	INSTALL INSULATION FOR 1MS-220	10	04JUN04 11:00	04JUN04 20:59	162
SCAFFOLDING - NPS - J. HAESE										
21	1	CE214031SR	CE4	82	CV-00257	REMOVE SCAFFOLDING FOR	8	03JUN04 07:00*	03JUN04 14:59	48
22	1	CE927251SR	CE4	82	MS-00117	REMOVE SCAFFOLDING FOR	4	03JUN04 15:00	03JUN04 18:59	92
23	1	CE303871SR	CE4	82	MS-00042	REMOVE SCAFFOLDING FOR	4	04JUN04 07:00*	04JUN04 10:59	44
24	1	CESGA001SR	CE4		HX-001A	REMOVE SCAFFOLDING FOR S/G	8	04JUN04 17:00	05JUN04 00:59	4
25	1	CESGB001SR	CE4		HX-001B	REMOVE SCAFFOLDING FOR S/G	8	04JUN04 17:00	05JUN04 00:59	4
CONSTRUCTION ENG - S. CARTER										
26	0	CE0210986	CE6	77	SEC	SEC SUPPORT MR 99-011*B	91	05APR04 07:00A	17JUN04 14:59	31
27	0	CE0210989	CE6	76	SEC	SEC, INSTALL NEW EQUIP MR 99-011*E	91	05APR04 08:00A	17JUN04 14:59	31
28	0	CE0210990	CE6	76	SEC	SEC REM ABANDONED EQUIP MR 99-011*F	107	03MAY04 08:00A	21JUN04 14:59	15
CHEMISTRY										
29	1	CH0300364	CH	77	CHEM-SAMPL	RCS CL TSR 3.4.5.2	33	30MAY04 05:00A	05JUN04 11:59	200
30	1	CH0300377	CH	77	CHEM-SAMPL	RCS DO TSR 3.4.5.1	33	30MAY04 05:00A	05JUN04 11:59	200
31	1	CH0300407	CH	77	CHEM-SAMPL	RCS BORON SR 3.9.1.1	33	30MAY04 05:00A	05JUN04 11:59	200

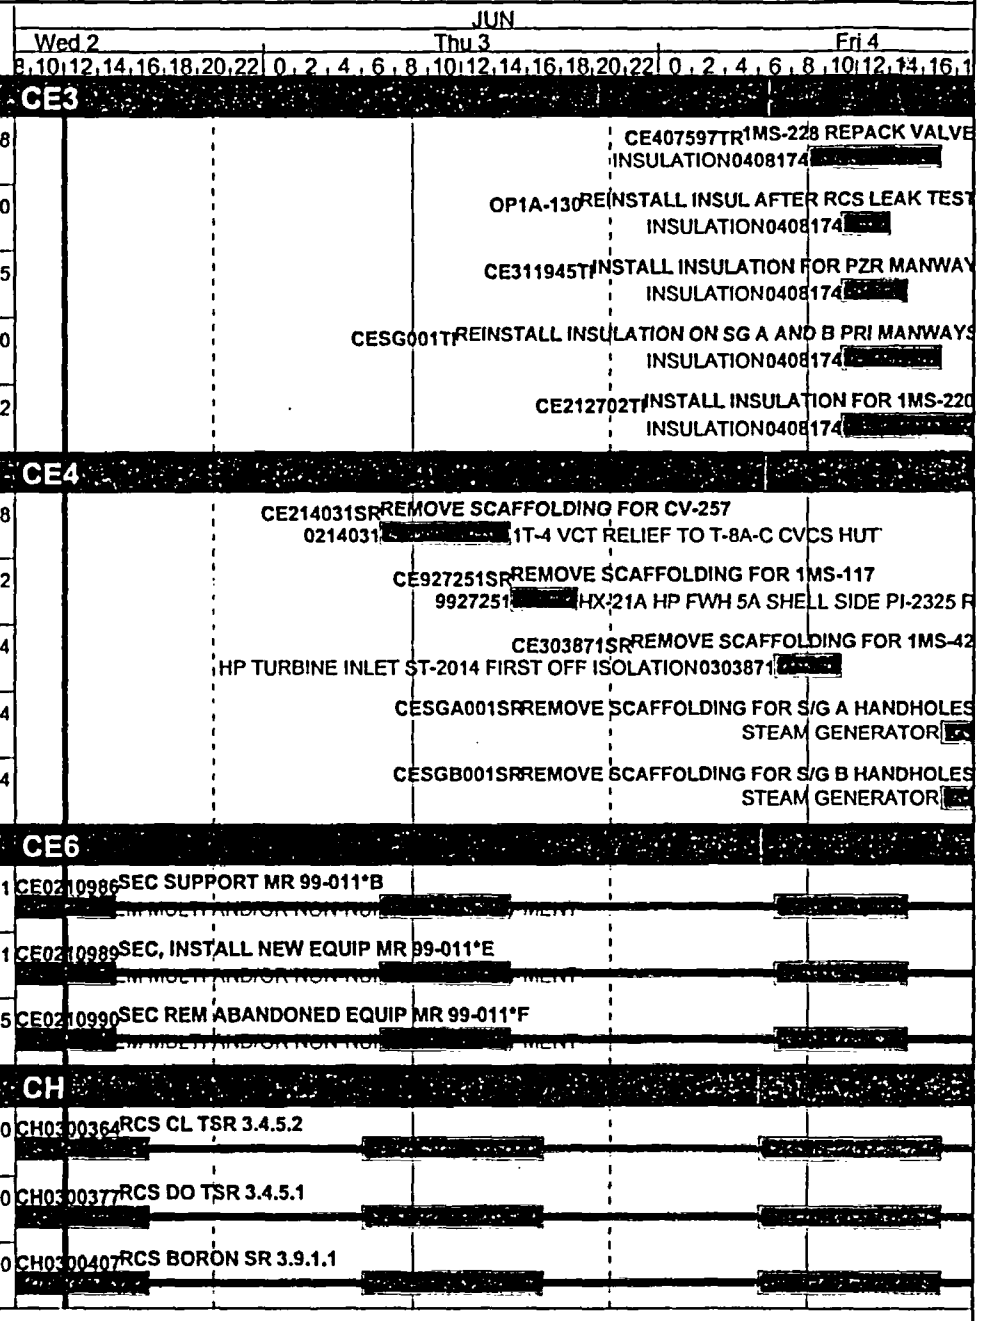

© Primavera Systems, Inc.

U1R28 WORKING SCHEDULE

after 02JUN04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	MF
CHEMISTRY										
32	0	CH0300201	CH	77	CHEM-SAMPL	BAST BORON TSR 3.5.1.2	16	31MAY04 07:00A	04JUN04 11:59	106
33	1	CH0300391	CH	77	CHEM-SAMPL	SGBDFO GAMMA SCAN	16	31MAY04 07:00A	04JUN04 11:59	106
34	1	CH0300446	CH	77	CHEM-SAMPL	RE-229 ISOTOPIC	16	31MAY04 07:00A	04JUN04 11:59	106
35	2	CH0300487	CH	77	CHEM-SAMPL	RCS BORON SR 3.9.1.1	16	31MAY04 07:00A	04JUN04 11:59	106
36	2	CH0300504	CH	77	CHEM-SAMPL	RCS CL TSR 3.4.5.2	16	31MAY04 07:00A	04JUN04 11:59	106
37	2	CH0300517	CH	77	CHEM-SAMPL	RCS DO TSR 3.4.5.1	16	31MAY04 07:00A	04JUN04 11:59	106
38	2	CH0300530	CH	77	CHEM-SAMPL	SGBDFO GAMMA SCAN	16	31MAY04 07:00A	04JUN04 11:59	106
39	2	CH0300556	CH	77	CHEM-SAMPL	RE-229 ISOTOPIC	16	31MAY04 07:00A	04JUN04 11:59	106
40	1	OP1A-032	CH		OP-1A	VERIFY RCS OXYGEN IN SPEC	1	02JUN04 12:00	02JUN04 12:59	3
41	0	CH0300237	CH	77	CHEM-SAMPL	SFP BORON SR 3.7.11.1	1	03JUN04 07:00*	03JUN04 07:59	118
42	0	CH0300250	CH	77	CHEM-SAMPL	WASTEWATER EFFLUENT COMPOSITE	1	03JUN04 07:00*	03JUN04 07:59	118
43	1	CH0300466	CH	77	CHEM-SAMPL	RWST BORON SR 3.05.04.3	1	03JUN04 07:00*	03JUN04 07:59	118
44	2	CH0300595	CH	77	CHEM-SAMPL	RWST BORON SR 3.05.04.3	1	03JUN04 07:00*	03JUN04 07:59	118
45	2	CH0300495	CH	76	CHEM-SAMPL	UNIT 2 SI ACCUMULATOR	1	03JUN04 10:00	03JUN04 10:59	115
46	1	OP1A-120	CH		OP-1A	SAMPLE S/G'S FOR AMMONIA	2	04JUN04 06:00	04JUN04 07:59	25
ENGINEERING - PREDICTIVE MAINTENANCE										
47	2	EE0302357	EEP	77	W-001A1	INSPECT CONT FAN (VIBRATION/LUBE)	2	03JUN04 10:00*	03JUN04 11:59	114
48	2	EE0302359	EEP	77	W-001B1	INSPECT CONT FAN (VIBRATION/LUBE)	2	03JUN04 10:00*	03JUN04 11:59	114
49	2	EE0302361	EEP	77	W-001C1	INSPECT CONT FAN (VIBRATION/LUBE)	2	03JUN04 10:00*	03JUN04 11:59	114

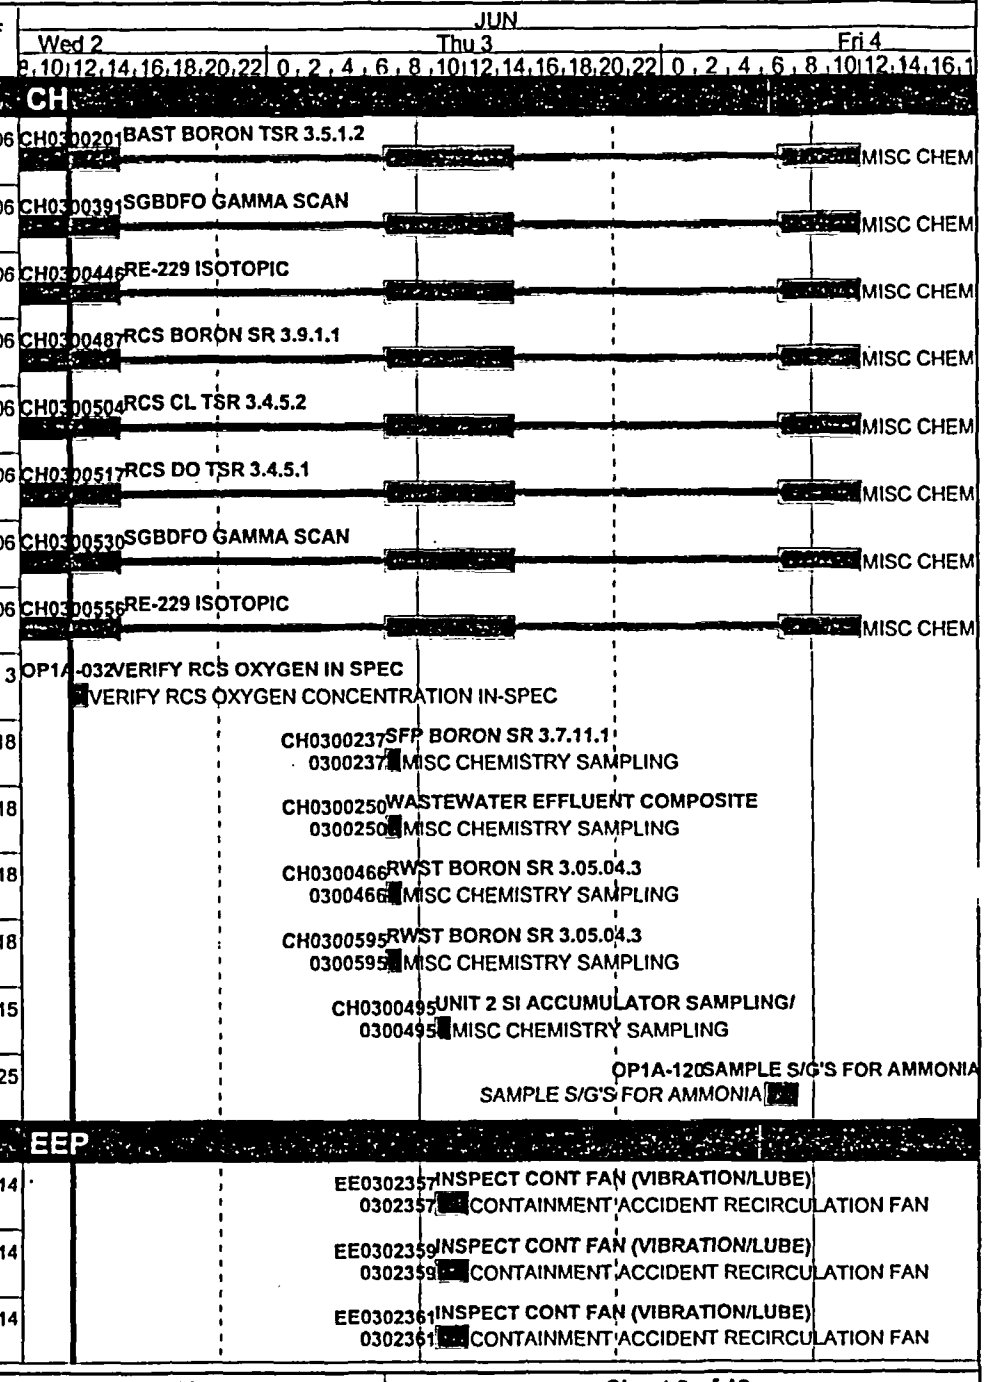

© Primavera Systems, Inc.

U1R28 WORKING SCHEDULE

after 02JUN04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	MF
ENGINEERING - PREDICTIVE MAINTENANCE										
50	2	EE0302363	EEP	77	W-001D1	INSPECT CONT FAN (VIBRATION/LUBE)	2	03JUN04 10:00*	03JUN04 11:59	114
51	0	EE0302303	EEP	77	PAB	PAB VIBRATION ROUTE DATA	40	04JUN04 07:00*	10JUN04 14:59	71
52	0	EE0302309	EEP	77	PAB	PAB-CA - VIBRATION ROUTE DATA	40	04JUN04 07:00*	10JUN04 14:59	71
53	1	EE-RCP-Q3	EEP	76	P-001B-M	TAKE VIBRATION READING "A" RCP AT	1	04JUN04 09:00	04JUN04 09:59	173
54	1	EE-RCP-Q4	EEP	82	P-001B-M	TAKE VIBRATION READING "B" RCP AT	1	04JUN04 09:00	04JUN04 09:59	173
55	1	EE0304995	EEP	82	P-028B	P-028B - POST MAINTENANCE	2	04JUN04 15:00*	04JUN04 16:59	100
56	1	EE0306054	EEP	82	P-028A	P-028A - POST MAINTENANCE	2	04JUN04 15:00	04JUN04 16:59	100
ELECTRICAL MAINTENANCE										
57	0	EM0305219	EM	76	D-48	MONTHLY COMMUNICATION	1	02JUN04 09:00A	02JUN04 12:59	0
58	0	EM0307011I	EM	76	D-105	PERFORM RMP 9046 12 MONTH CHECKS	1	02JUN04 09:00A	02JUN04 12:59	0
59	0	EM0309665	EM	76	W-183B-M	MCE ANALYZE MOTOR (1B52-401B/1B-40)	1	02JUN04 09:00A	02JUN04 12:59	0
60	1	EM0301236	EM	76	TE-00031	TE-31 NOISY/OSCILL SEVERAL DEGREES	3	02JUN04 09:00A	02JUN04 14:59	62
61	2	EM0302205	EM	76	G-07	GREASE GENERATOR BEARINGS	1	02JUN04 11:00A	02JUN04 12:59	505
62	0	EM0408083	EM	76	EL-LTG IV	INSPECT, TEST, CLEAN AND ADD WATER	15	02JUN04 12:00*	03JUN04 15:59	0
63	0	EM0309140	EM	76	D-106	STATION BATTERY INSP PER RMP 9046-1	3	02JUN04 13:00*	02JUN04 15:59	502
64	0	EM0309669	EM	76	W-185A-M	MCE ANALYZE MOTOR (1B52-403B/1B-40)	4	02JUN04 13:00	02JUN04 16:59	501
65	0	EM0307011J	EM	76	D-105	PERFORM RMP 9046 92 DAY CHECKS	6	02JUN04 13:00	02JUN04 18:59	0
66	1	EMGNDOUT	EM		X-01	ELECTRICAL REMOVE GROUNDS FOR MAIN	1	02JUN04 14:00	02JUN04 14:59	94
67	0	EM0301792A	EM	76	A52-DHVR-3	(A52-01) BKR MAINT. PORTION AT CUBICLE	4	02JUN04 14:00*	02JUN04 17:59	91

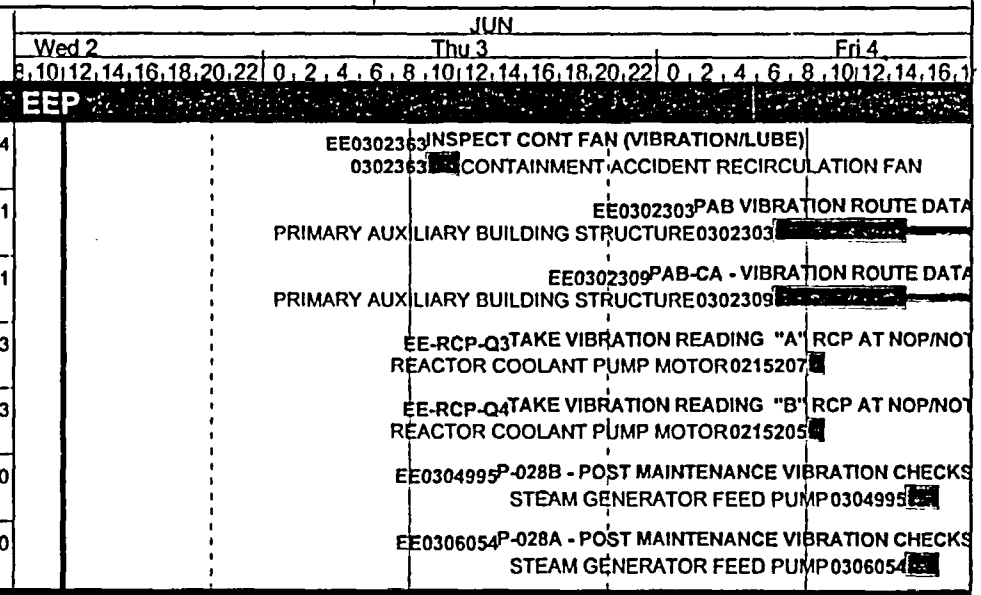

© Primavera Systems, Inc.

U1R28 WORKING SCHEDULE

after 02JUN04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	MF
ELECTRICAL MAINTENANCE										
68	1	EM0301549A	EM	77	O-TS-043	SUPPORT TS-43 AMP READINGS	5	02JUN04 16:00	02JUN04 20:59	497
69	0	EM0305372	EM	77	EL-LTG	TSC/SBCC/MTN SHOP EMERGENCY LIGHTING	24	02JUN04 18:00*	04JUN04 19:59	0
70	0	EM0305374	EM	77	EL-LTG	INSPECT, TEST, CLEAN AND ADD WATER	24	02JUN04 18:00*	04JUN04 19:59	10
71	0	EM0307011K	EM	76	D-105	S/U D-107 AND PLACE ON D-105	2	02JUN04 21:00	02JUN04 22:59	0
72	0	EM0307011L	EM	76	D-105	INITIAL EQUALIZE CHARGE ON D-105	48	02JUN04 23:00	04JUN04 22:59	0
73	0	EM0210793	EM	76	EL-LTG I	TWO YEAR TEST OF EMERGENCY LIGHTING	24	03JUN04 06:00*	05JUN04 07:59	204
74	0	EM0407283	EM	77	Z-675	WIRE ROPE INSPECTION	8	03JUN04 07:00*	03JUN04 14:59	479
75	0	EM0305373	EM	77	EL-LTG	INSPECT, TEST, CLEAN AND ADD WATER	24	03JUN04 16:00*	06JUN04 06:59	194
76	0	EM9933757	EM	76	B52-DB25-0	SPARE BKR MAINTENANCE	40	03JUN04 18:00*	07JUN04 21:59	140
77	1	EM0216166	EM	76	E-01	CHECK EXCITER GROUND DETECTION	2	03JUN04 20:00*	03JUN04 21:59	0
78	0	EM0310873	EM	76	P-033-M	P-33-M MCE ANALYZE MOTOR (0B52-432H)	4	03JUN04 20:00*	03JUN04 23:59	0
79	0	EM0305618	EM	76	P-031B-M	P-31B-M OIL CHANGE	5	03JUN04 20:00*	04JUN04 00:59	0
80	1	EM0312035B	EM	76	P-028B-M	1P-28B-M PERFORM COUPLED PMT RUN	4	04JUN04 09:00*	04JUN04 12:59	0
81	0	EM0407638E	EM	76	Z-014	PERFORM REPAIRS TB CRANE (SMALL HOOK)	10	04JUN04 12:00*	05JUN04 10:59	193
82	1	EM0400344A	EM	76	P-028A-M	1P-28A-M PERFORM LEAK CHECKS AT NOP /	2	04JUN04 15:00	04JUN04 16:59	61
ELECTRICAL VALVE TEAM										
83	1	B52-424ME	EMV	76	B-42	BUS STAB PMT "1RH-701"	4	02JUN04 21:00	03JUN04 00:59	0
84	1	EM0215176	EMV	76	RH-00700-O	RH-700 MOV ACTUATOR	12	03JUN04 02:00	03JUN04 13:59	0
85	1	EM0213737A	EMV	76	RH-00720	1RH-720 PACKING LEAK, ADJUST(RHR	2	03JUN04 07:00	03JUN04 08:59	1

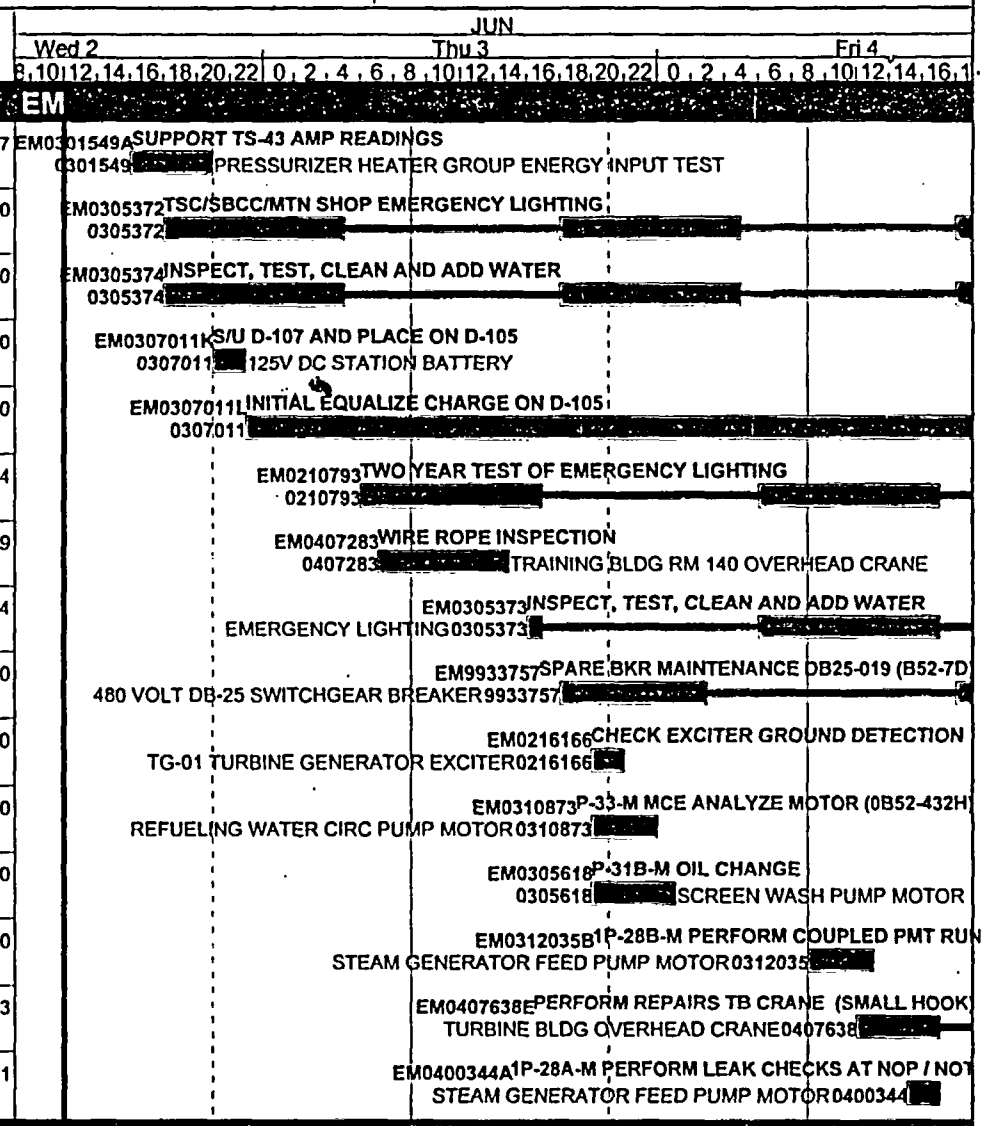

U1R28 WORKING SCHEDULE

after 02JUN04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	MF
ELECTRICAL VALVE TEAM - EMV										
86	1	EM0403305	EMV	76	SI-00852A-	SI-852A-O PERFORM STEM LUBE AND FBJ	10	03JUN04 07:00	03JUN04 16:59	0
87	1	EM0302205A	EMV	76	RH-00701	1RH-701 PACKING LEAK, ADJUST(RHR	2	03JUN04 10:00	03JUN04 11:59	41
88	1	B52-424FE	EMV	76	B-42	BUS STAB PMT "1SI-841B"	2	04JUN04 00:00	04JUN04 01:59	0
89	0	EM0405880C	EMV	78	W-013B1	W-013B1 REMOVE JUMPER PER IWP	4	04JUN04 08:00*	04JUN04 11:59	0
90	1	B52-428ME	EMV	76	B-42	BUS STAB PMT "W-13B2"	1	04JUN04 13:00	04JUN04 13:59	456
ENGINEERING PROGRAMS - INSPECTION SERVICES - EPI										
91	0	EP0405867	EPI	77	BALCM	VT-2 EXAMINATION FOR LEAKAGE (BALCM)	11	01JUN04 10:00A	03JUN04 14:59	111
92	1	EP0301905	EPI	76	SI	VT-2 ASME XI PERIODIC PRESSURE	4	04JUN04 09:00	04JUN04 12:59	6
93	1	EP0216335	EPI	82	SI-00845A	PMT OF 1SI-845A PER 1-PT-SI-8	1	04JUN04 11:00	04JUN04 11:59	7
94	1	PT-RCS-001	EPI	76	PT-RCS-1	RCS PRESSURE TEST PER 1-PT-RCS-001	8	04JUN04 11:00	04JUN04 18:59	0
95	1	PT-CV-001	EPI	76	CV	VT-2 CVCS PER 1-PT-CV-001	4	04JUN04 15:00	04JUN04 18:59	10
ENGINEERING PROGRAMS - TEST SERVICES - EPT										
96	1	EM-BMFP-P3	EPT	76	P-028B-M	P28B OBTAIN COUPLED VIB AND CURRENT	4	04JUN04 09:00*	04JUN04 12:59	38
FACILITIES GROUP - UTILITY GROUP - FG1										
97	1	CTMT-040	FG1		SUMMARY	CTMT INTEGRITY HATCH OPERATION	71*	28MAY04 23:00A	05JUN04 10:59	0
FACILITIES GROUP - MTN MECH OPER NORTH - FG2										
98	0	FG0302085	FG2	77	LIGHTING	RELAMP MERCURY VAPOR LAMPS IN U1	16	03JUN04 07:00*	04JUN04 14:59	103
FACILITIES GROUP - BOB WIENSCH - FG3										
99	1	FG213478SR	FG3	87	CPP-56	CPP-56 REMOVE SCAFFOLDING	27	31MAY04 10:00A	04JUN04 16:59	206
100	0	FG0302080	FG3	77	MANHOLE PM	PUMP ELECTRICAL MANHOLE SUMPS	8	04JUN04 07:00*	04JUN04 14:59	103

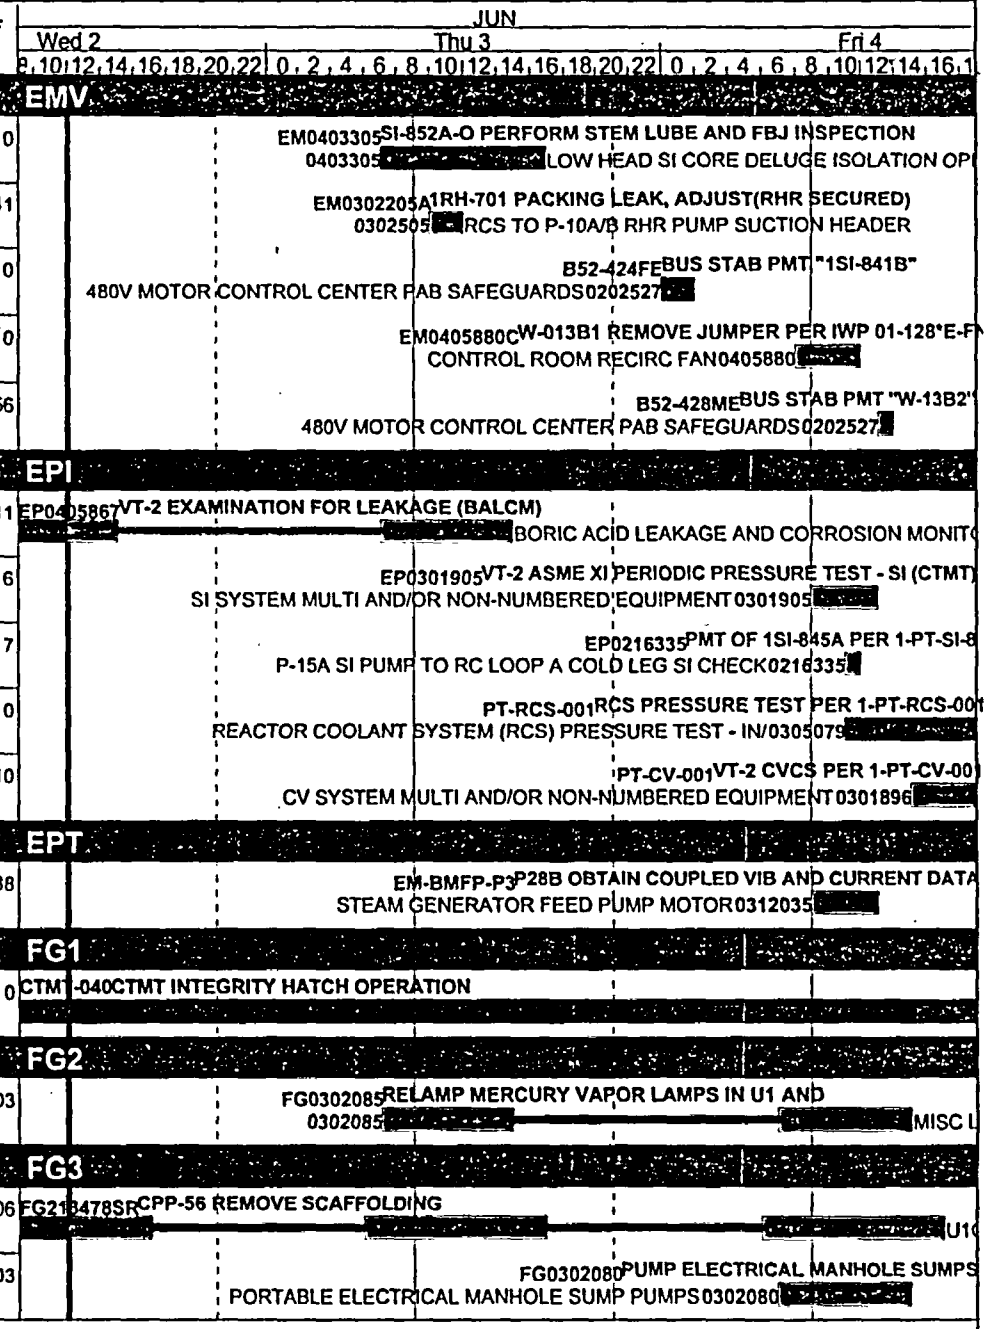

U1R28 WORKING SCHEDULE

after 02JUN04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	MF
RADIATION PROTECTION (OLD)										
101	0	RE-211-B11	HP		HP RMS	RE-211/212 AIR SAMPLE CHANGE OUT	1	03JUN04 00:00*	03JUN04 00:59	493
102	2	HP0301567A	HP	77	O-PC-024	RP BRIEF U2 CONTAINMENT ENTRY	1	03JUN04 09:00*	03JUN04 09:59	0
I&C MAINTENANCE										
103	0	IC0403277	IC	76	RE-00240	RE-240 FAILED HIGH	3	02JUN04 09:00A	02JUN04 14:59	179
104	0	IC0407569	IC	76	RE-00238	SPURIOUS ALARMS. TROUBLESHOOT/REPAIR	3	02JUN04 09:00A	02JUN04 14:59	119
105	1	ICPRE-COMP	IC		REI 10.1	MOVE REACTIVITY COMPUTER TO	10	02JUN04 18:00*	03JUN04 03:59	29
106	2	IC0407745	IC	76	LT-00939	LT-939 DRY LEG DRAIN CHECK	1	03JUN04 10:00	03JUN04 10:59	115
107	2	IC0310325	IC	76	FM	2FM DISPLAY STICKS	8	03JUN04 10:00	04JUN04 09:59	108
108	1	IC300795A1	IC	79	I&C MISC	REACTOR PROTECTION LGC CAB	3	04JUN04 05:00	04JUN04 07:59	21
109	1	IC0310061A	IC	79	LC-00471B-	1LC-471B-YA REPLACE TEST RELAY	4	04JUN04 05:00	04JUN04 08:59	20
110	1	IC0406155A	IC	79	LC-00471B-	1LC-431A-YA REPLACE TEST RELAY	4	04JUN04 05:00	04JUN04 08:59	20
111	1	IC2.17-1	IC	76	ICP-02.017	ICP 2.17 REACTOR PROTECTION LOGIC	4	04JUN04 05:00	04JUN04 08:59	0
112	1	ICRTDSWOFF	IC		RP	REMOVE LOOP RTD SWITCHING UNIT	1	04JUN04 09:00	04JUN04 09:59	0
113	1	IC10.1RES	IC	76	ICP-10.001	ESF RESISTANCE CHECKS	1	04JUN04 10:00	04JUN04 10:59	0
114	1	IC2.20-1	IC	76	ICP-02.020	RX PROTECTION ANN VERIFICATION	2	04JUN04 11:00	04JUN04 12:59	0
115	1	IC2.20-2	IC	76	ICP-02.020	RX PROTECTION SW VERIFICATION	2	04JUN04 13:00	04JUN04 14:59	0
116	1	ICN42SETUP	IC		N-00042	SETUP FOR LOW PWR PHYSICS TEST	1	04JUN04 15:00	04JUN04 15:59	13
117	1	IC4.29-2ZR	IC	76	ICP-04.029	RPI ZERO ADJUST	3	04JUN04 15:00	04JUN04 17:59	0

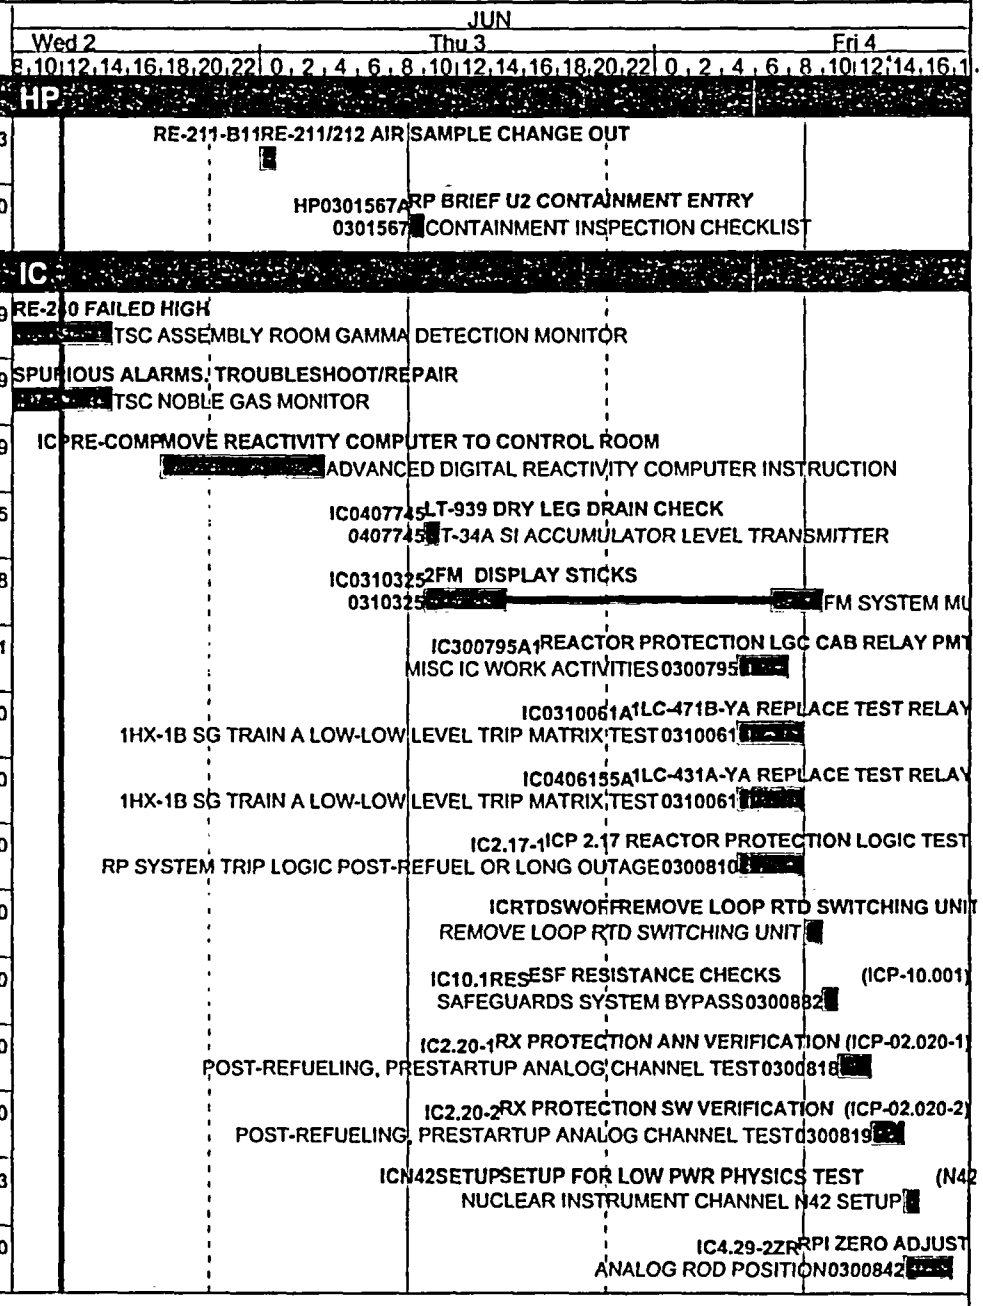

U1R28 WORKING SCHEDULE

after 02JUN04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	MF
I&C - C. RHODEN										
118	0	IC0300726	IC1	76	FACP-008	BATTERY REPLACEMENT	2	02JUN04 18:00*	02JUN04 19:59	229
I&C - J. SCHMOLDT & R. YOUNG										
119	0	IC0302217	IC2	76	LI-05858	F-236 MOVE LEVEL INDICATOR	8	04JUN04 07:00	04JUN04 14:59	0
120	0	IC0309023	IC2	76	C-102	C-102 ALARM TEST PROBLEM	8	04JUN04 07:00	04JUN04 14:59	0
I&C - M. KENNETT										
121	0	IC0300685	IC5	76	C-025	MONTHLY PM ON DMIMS SYSTEM	1	02JUN04 09:00A	02JUN04 12:59	121
MECHANICAL MAINTENANCE MM1 RIDINGS/ BRITTINGHAM										
122	1	MM0407618	MM1	76	RH-00720	1RH-720 PERFORM VT OF STUD	3	03JUN04 07:00	03JUN04 09:59	0
123	1	MM0214052B	MM1	82	HX-001A	HOT RETORQUE HX-1A HANDHOLES @ ~400°	4	03JUN04 20:00	03JUN04 23:59	9
124	1	MM0214054B	MM1	76	HX-001B	HOT RETORQUE HX-1B HAND HOLES @~ 400°	4	03JUN04 20:00	03JUN04 23:59	9
125	1	MM0214145	MM1	76	SNUBBERS	INSPECT STEAM GENERATOR AND MAIN	4	04JUN04 09:00*	04JUN04 12:59	16
MECHANICAL MAINTENANCE MM2 BONENFANT (BOP)										
126	1	MM0408498	MM2	76	Z-104A	1Z-104A REPAIR STRAINER	29	29MAY04 08:00A	03JUN04 16:59	0
127	0	MM0214209	MM2	76	HX-279	HVAC UNIT INSPECTION	1	02JUN04 07:00A	02JUN04 12:59	0
128	0	MM0301076	MM2	76	F-235	BIMONTHLY MAIN DRIVE LUBRICATION	1	02JUN04 07:00A	02JUN04 12:59	0
129	0	MM0201620	MM2	76	K-002B	SEMIANNUAL COMPRESSOR	7	02JUN04 11:00A	02JUN04 19:59	0
130	0	MM0400519	MM2	76	IA-00229	IA-229 REPLACE VALVE	7	02JUN04 11:00A	02JUN04 19:59	0
131	0	MM0405759	MM2	76	K-002B	K-2B OIL LEAK	7	02JUN04 11:00A	02JUN04 19:59	0
132	0	MM0301078	MM2	76	F-237	BIMONTHLY MAIN DRIVE LUBRICATION	3	02JUN04 13:00	02JUN04 15:59	0
133	0	MM0301077	MM2	76	F-236	BIMONTHLY MAIN DRIVE LUBRICATION	3	02JUN04 16:00	03JUN04 07:59	0

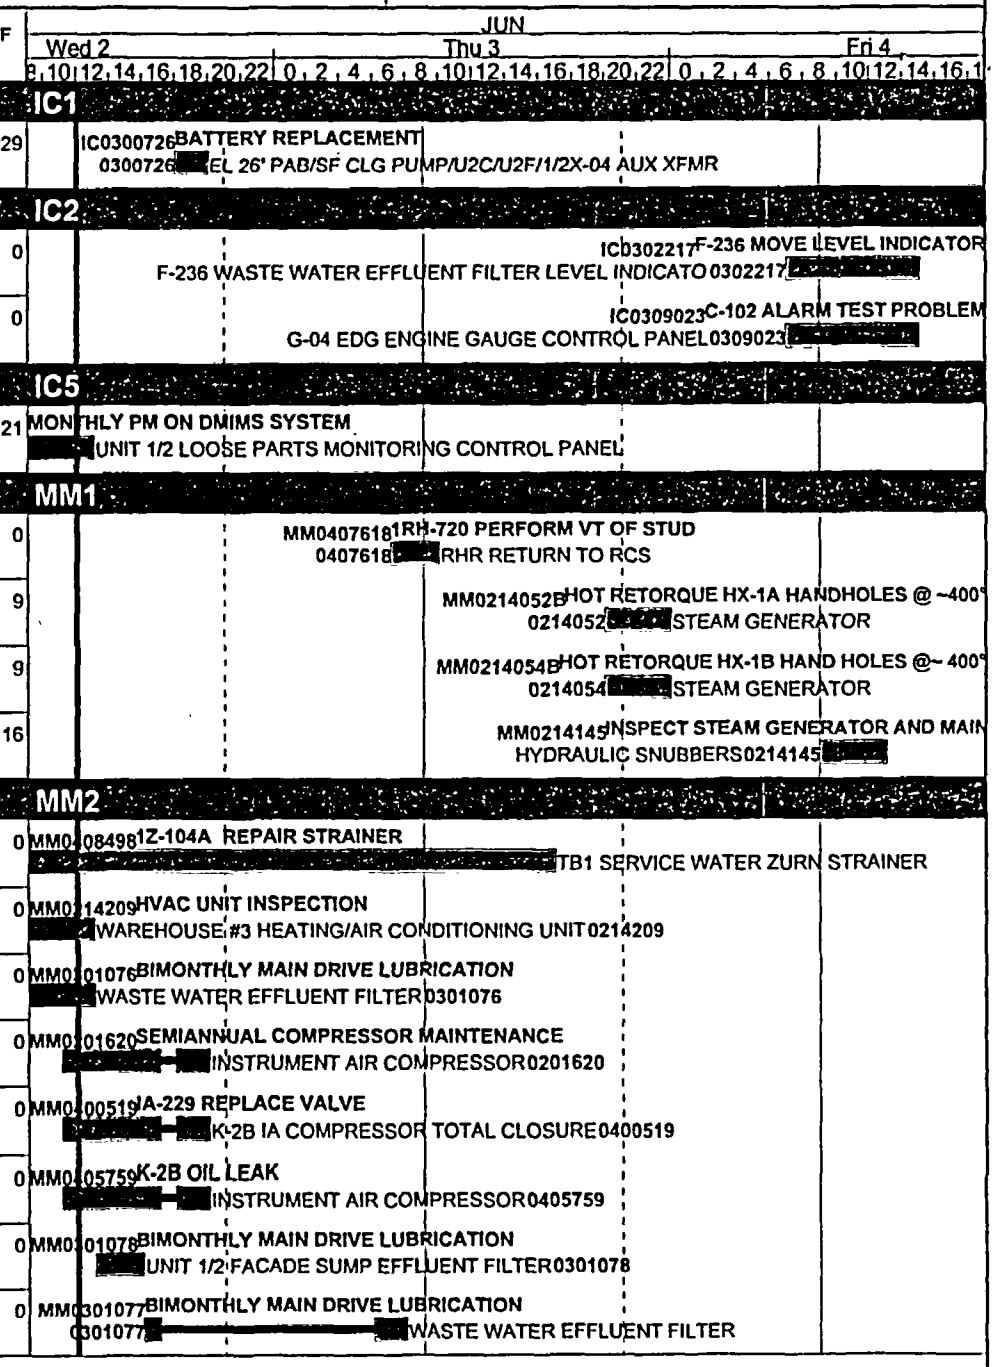

U1R28 WORKING SCHEDULE

after 02JUN04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	MF
MECHANICAL MAINTENANCE MM2 BONENFANT (BOP)										
134	1	MM0306095	MM2	76	Z-027-2	LUBRICATE AND MAINTAIN SCREEN	2	02JUN04 18:00	02JUN04 19:59	0
135	1	MM0306097	MM2	76	Z-027-3	LUBRICATE AND MAINTAIN SCREEN	2	02JUN04 20:00	02JUN04 21:59	0
136	1	MM0306099	MM2	76	Z-027-4	LUBRICATE AND MAINTAIN SCREEN	2	02JUN04 22:00	02JUN04 23:59	0
137	1	MM0309351	MM2	76	Z-027-1	LUBRICATE AND MAINTAIN SCREEN	2	03JUN04 00:00	03JUN04 01:59	0
138	1	MM0400324D	MM2	76	VNPSE-0321	1VNPSE-3212, REPLACE GRATING	6	03JUN04 07:00*	03JUN04 12:59	194
139	0	MM0310385	MM2	76	HX-055B-1	GL 89-13 HX/OPEN, CLOSE AND CLEAN	8	03JUN04 07:00	03JUN04 14:59	0
140	0	MM0310395	MM2	76	HX-055B-2	GL 89-13 HX/OPEN, CLOSE AND CLEAN	8	03JUN04 07:00	03JUN04 14:59	0
141	1	MM0214127A	MM2	76	P-029	MM SUPPORT FOR P-29-T OVERSPEED	4	03JUN04 09:00	03JUN04 12:59	0
142	1	MM0214127C	MM2	76	P-029	P-29-T RECOUPLE	2	03JUN04 15:00	03JUN04 16:59	0
143	2	MM0306101	MM2	76	Z-027-3	LUBRICATE AND MAINTAIN SCREEN	2	03JUN04 18:00	03JUN04 19:59	0
144	2	MM0309345	MM2	76	Z-027-1	LUBRICATE AND MAINTAIN SCREEN	2	03JUN04 20:00	03JUN04 21:59	0
145	1	MM0301106	MM2	76	P-011A	CHANGE OIL, FLUSH BEARINGS AND CLEAN	6	03JUN04 21:00	04JUN04 02:59	0
146	2	MM0309347	MM2	76	Z-027-2	LUBRICATE AND MAINTAIN SCREEN	2	03JUN04 22:00	03JUN04 23:59	0
147	2	MM0309349	MM2	76	Z-027-4	LUBRICATE AND MAINTAIN SCREEN	2	04JUN04 00:00	04JUN04 01:59	0
148	0	MM0201662	MM2	76	W-210	CLEAN AND INSPECT MOTOR AND FAN	4	04JUN04 06:00	04JUN04 09:59	0
149	2	MM0304865	MM2	76	YS-03587	2YS-3587 REPLACE STRAINER - MOD	32	04JUN04 06:00	06JUN04 15:59	0
150	0	MM0201664	MM2	76	W-211	INSPECT FAN AND LUBRICATE	4	04JUN04 10:00	04JUN04 13:59	0
NON-DESTRUCTIVE TESTING										
151	0	EP9927269A	NDE	77	S	CONDUCT CIVIL/STRUCTURAL	16	24MAY04 10:00A	04JUN04 11:59	106

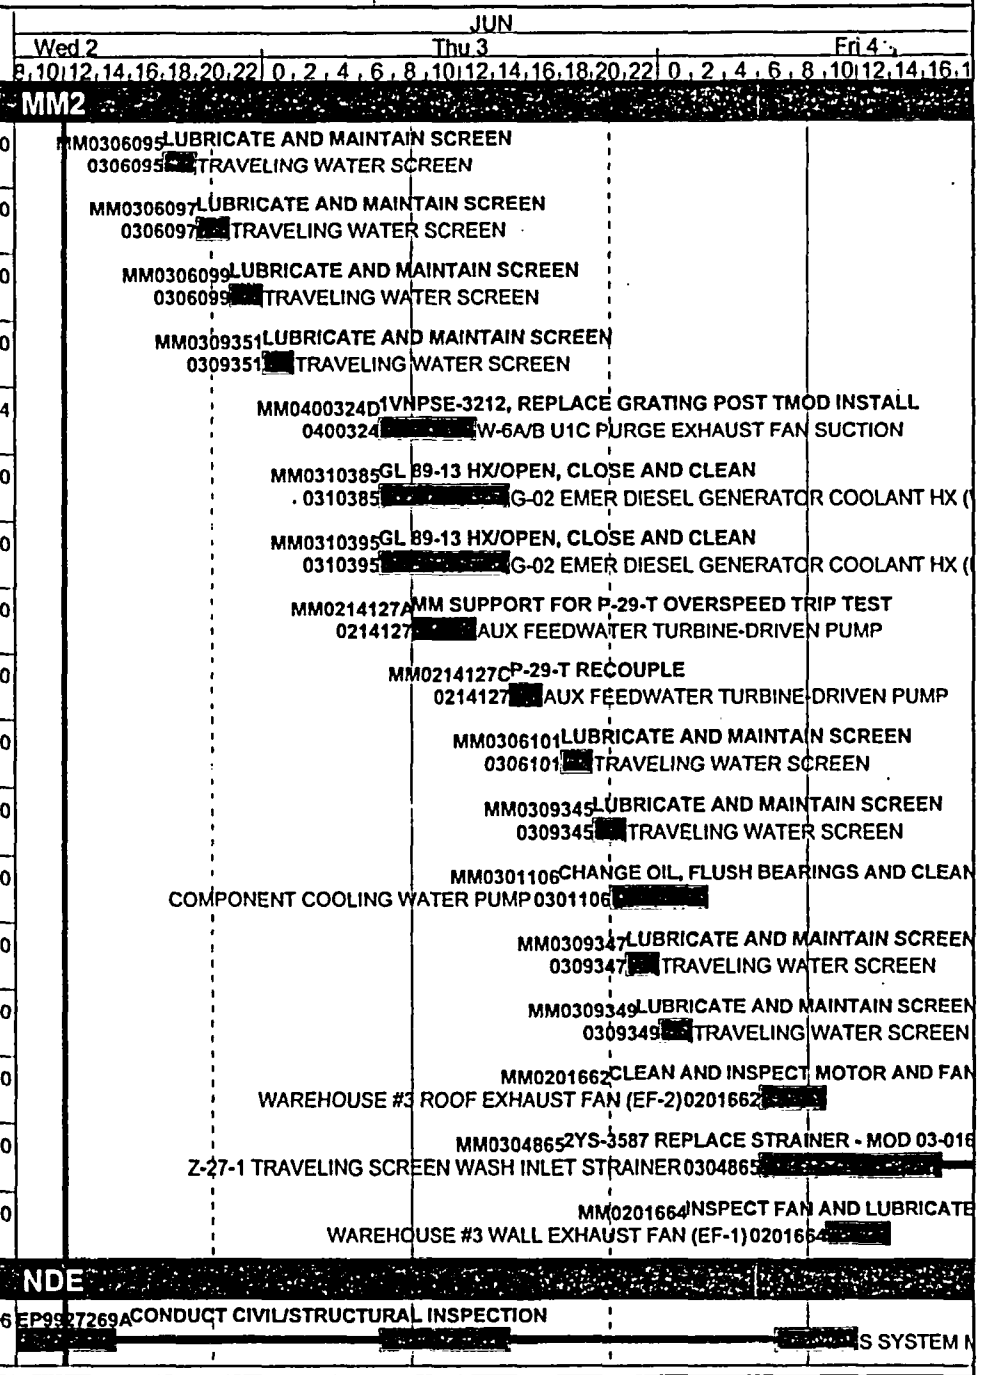

© Primavera Systems, Inc.

U1R28 WORKING SCHEDULE

after 02JUN04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	MF
NON-DESTRUCTIVE TESTING										
152	0	EP9927270A	NDE	77	S	CONDUCT CIVIL/STRUCTURAL	16	24MAY04 10:00A	04JUN04 11:59	106
153	1	NG-SGAHHVI	NDE	87	HX-001A	INSP S/G A HANDHOLES DURING	1	04JUN04 09:00	04JUN04 09:59	19
154	1	NG-SGBHHVI	NDE	87	HX-001B	INSP S/G B HANDHOLES DURING	1	04JUN04 09:00	04JUN04 09:59	19
155	1	EAMRCP-VT	NDE	82	P-001A-M	P-001A - SIGN-OFF IN 9002-12 AFTER IT-230	1	04JUN04 11:00*	04JUN04 11:59	171
156	1	EZMRCP-VT	NDE	82	P-001B-M	P-001B - SIGN-OFF IN 9002-12 AFTER IT-230	1	04JUN04 11:00	04JUN04 11:59	171
157	1	SD-I600-97	NDE	76	R-1	INSPECT PENETRATION 26	1	04JUN04 11:00	04JUN04 11:59	171
OPERATIONS RELIEFS										
158	0	OP0301238	OP0	77	O-PC-073.4	FP VALVE POSITION VERIFICATION CHECK	27	01JUN04 07:00A	07JUN04 14:59	95
159	0	OP0301278	OP0	77	PT-FP-006	FP CONTROL VALVE POSITION	27	01JUN04 07:00A	07JUN04 14:59	95
160	0	OP0301243	OP0	77	O-PC-021.4	WEEKLY MISCELLANEOUS DATA	5	02JUN04 12:00*	02JUN04 16:59	501
161	0	OP0308991	OP0	77	O-PC-078.7	TRN/NES BLDG FP WET PIPE SYS CHECK	5	02JUN04 12:00*	02JUN04 16:59	501
162	0	OP0311110	OP0	77	O-IT-0007A	IT-07A, P-32A SERVICE WATER PUMP	4	02JUN04 20:00*	02JUN04 23:59	5
163	2	OP0301568	OP0	77	TS-CONT-00	CONT ISOL VALVE AND FLANGE CHECKS	2	03JUN04 07:00*	03JUN04 08:59	485
OPERATIONS MIDSHIFT										
164	0	OP0301295	OP1	76	O-PC-MIDS	OPERATIONS MID SHIFT WEEKLY	7	28MAY04 00:00A	03JUN04 06:59	140
165	0	OP0301308	OP1	77	TS-EP-001	POWER AVAILABILITY VERIFICATIONS	1	03JUN04 00:00*	03JUN04 00:59	146
166	0	OP0301325	OP1	77	O-PC-010.2	SW PUMP SHIFTING AND CW PUMP BUMPS	2	04JUN04 00:00*	04JUN04 01:59	138
167	1	OP0301491	OP1	77	O-TS-010AB	TS-10A, U1C AIR LOCK DOOR SEAL TEST	2	04JUN04 00:00*	04JUN04 01:59	138
168	2	OP0301575	OP1	77	O-TS-010AB	TS-10A, U2C AIR LOCK DOOR SEAL TEST	2	04JUN04 00:00*	04JUN04 01:59	138

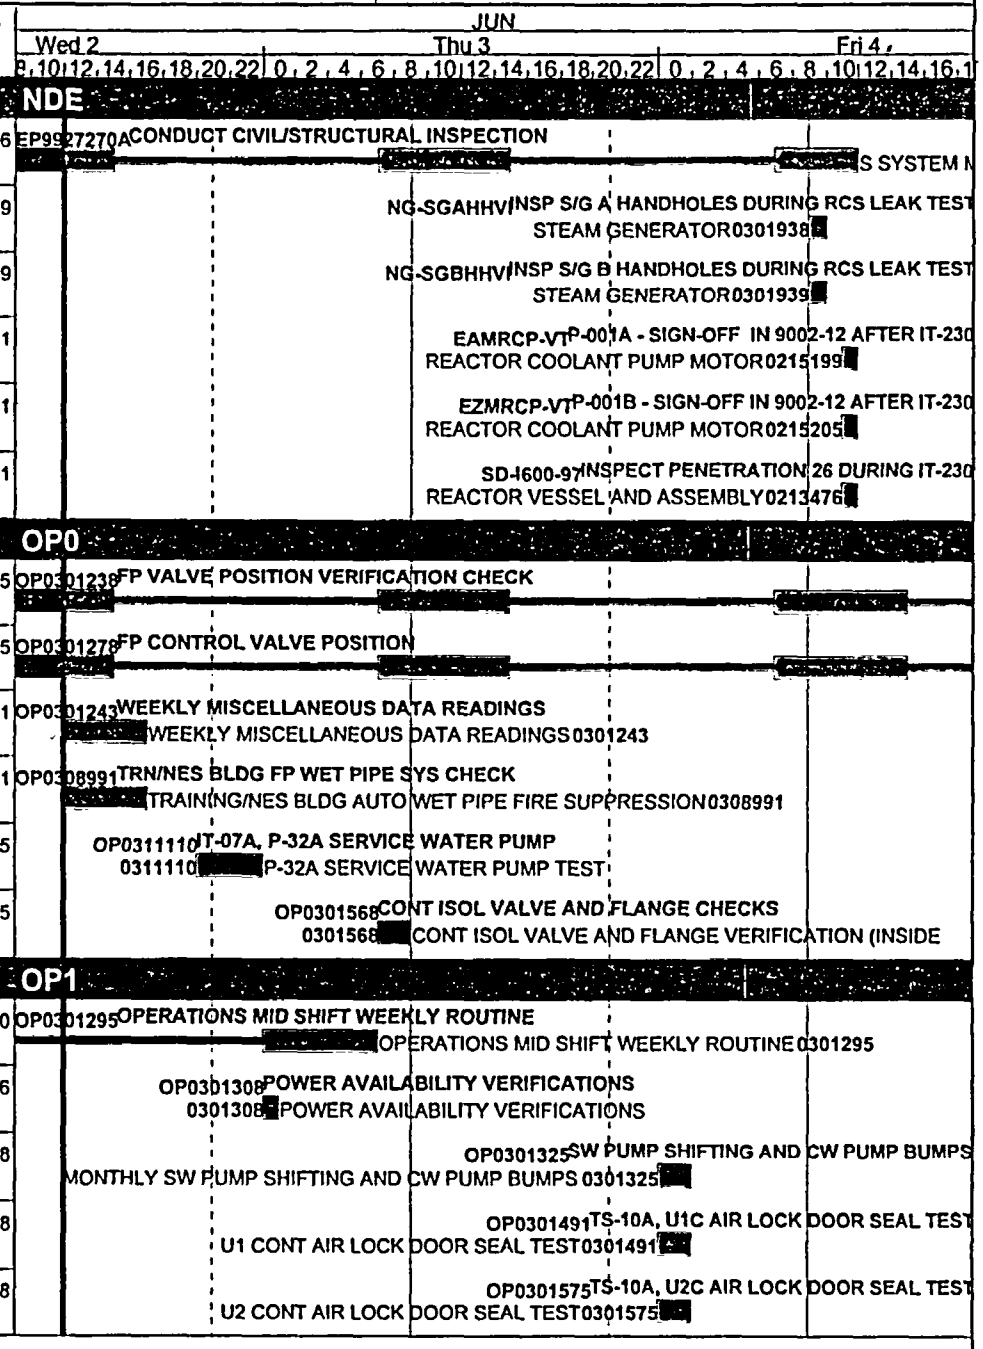

© Primavera Systems, Inc.

LT-03 STANDARD PUBLICATION
FL-03 Execution Publication Set

U1R28 WORKING SCHEDULE

after 02JUN04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	MF
OPERATIONS MIDSHIFT										
169	0	OP0301296	OP1	77	O-PC-MIDS	OPERATIONS MID SHIFT WEEKLY	49	04JUN04 00:00*	10JUN04 06:59	91
OPERATIONS DAYSHIFT										
170	0	OP0301335	OP2	76	O-PC-DAYS	OPERATIONS DAY SHIFT WEEKLY	31	01JUN04 08:00A	06JUN04 14:59	118
171	0	OP0301375	OP2	77	TS-SW-001	SW VALVE POSITION VERIFICATION	2	03JUN04 08:00*	03JUN04 09:59	144
172	0	OP0301377	OP2	77	O-PC-008.2	MONTHLY AFW PUMP DISCHARGE PIPING	1	04JUN04 08:00*	04JUN04 08:59	138
173	0	OP0301379	OP2	77	TS-AFW-002	AF SYSTEM VALVE AND LOCK CHECKS	1	04JUN04 08:00*	04JUN04 08:59	138
OPERATIONS SWINGSHIFT										
174	1	OP0301550	OP3	77	O-PC-001.2	TB1 MONTHLY HEATING/VENTILATION	3	19MAY04 16:00A	02JUN04 18:59	144
175	0	OP0301397	OP3	77	O-PC-SWING	OPS SWING SHIFT WEEKLY ROUTINE	28	30MAY04 16:00A	05JUN04 22:59	119
176	0	OP0301412	OP3	77	O-PC-029	LOAD TEST G-05, G-501	3	02JUN04 14:00*	02JUN04 16:59	501
177	0	OP0308223	OP3	77	O-PC-045.1	BLOWDOWN AIR RECEIVERS	1	02JUN04 16:00*	02JUN04 16:59	146
178	2	U2GNDR025	OP3		TG-01	DRAIN U2 MAIN ELECTRICAL	1	02JUN04 20:00	02JUN04 20:59	0
179	0	OP0301446	OP3	77	O-PC-009.1	MONTHLY SHIFTING OF IA COMPRESSORS/	6	04JUN04 16:00*	04JUN04 21:59	127
OPERATIONS										
180	1	CAMP-112	OPS		CAMP-112	RCS OXYGEN REMOVAL WITH	1	02JUN04 11:00A	02JUN04 12:59	0
181	1	OP1A200F	OPS		OP-1A	HEATUP RCS TO 200 DEGREES	1	02JUN04 12:00	02JUN04 12:59	0
182	2	OP0301567B	OPS		W-043A	START U2 CLEANUP FAN	24	02JUN04 12:00	03JUN04 11:59	482
183	1	OP1A250F	OPS		OP-1A	HEATUP RCS TO 250 - 270 deg F	3	02JUN04 13:00	02JUN04 15:59	0
184	1	OI32-020	OPS		OI-32	ESTABLISH H2 ATMOSPHERE IN GEN	20	02JUN04 15:00*	03JUN04 10:59	0

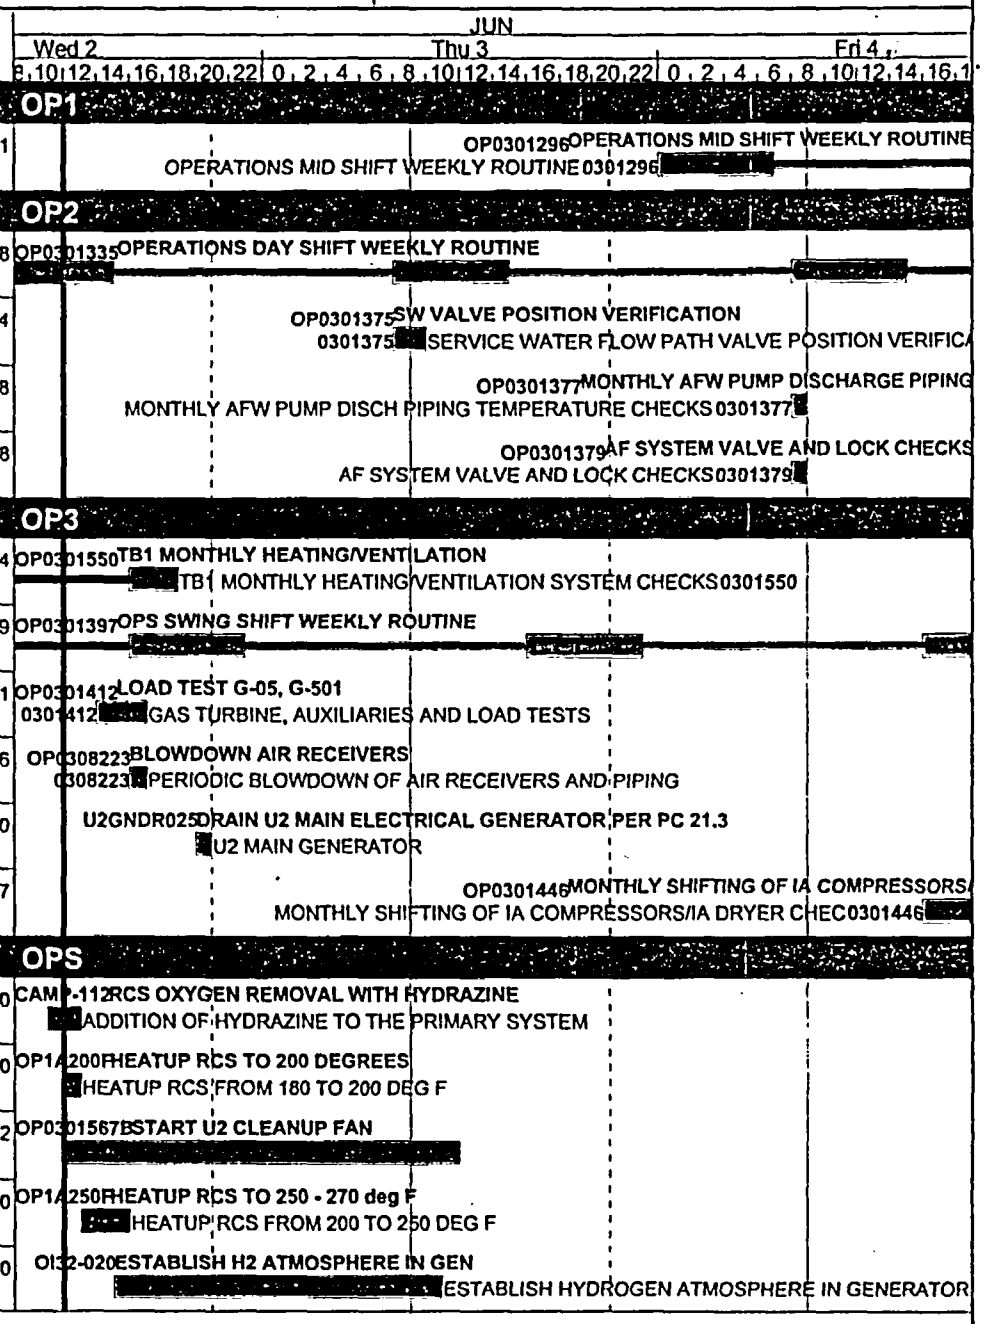

© Primavera Systems, Inc.

U1R28 WORKING SCHEDULE

after 02JUN04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	MF
OPERATIONS										
185	1	OP1A-050	OPS		OP-1A	HEATUP PRESSURIZER	4	02JUN04 16:00	02JUN04 19:59	0
186	1	OP0301549	OPS	77	O-TS-043	TS-43, PZR HEATER GROUP ENERGY INPUT	5	02JUN04 16:00*	02JUN04 20:59	0
187	1	TS-043	OPS		T-001	PRESSURIZER HEATER TEST	5	02JUN04 16:00	02JUN04 20:59	0
188	1	OP1A-060	OPS		OP-1A	ESTABLISH PZR BUBBLE	1	02JUN04 20:00	02JUN04 20:59	0
189	1	OP7B-010	OPS		OP-7B	SECURE OPERATING RHR PUMPS	1	02JUN04 20:00	02JUN04 20:59	0
190	1	OP0300941	OPS	82	RH-00626-O	PMT STROKE OF RH-626 PER IT-390	1	02JUN04 21:00	02JUN04 21:59	18
191	1	OP1A-080	OPS		OP-1A	ESTABLISH NORMAL PZR LEVEL	1	02JUN04 21:00	02JUN04 21:59	4
192	1	B52-424M	OPS	76	B-42	BUS STAB PMT "1RH-701"	2	02JUN04 21:00	02JUN04 22:59	0
193	1	PC-023.5	OPS		O-PC-023.5	CHARGING PUMP ROTATION/PM	3	02JUN04 21:00	02JUN04 23:59	494
194	1	OI79-030	OPS		OI-79	ESTABLISH VACUUM	12	03JUN04 00:00*	03JUN04 11:59	66
195	1	OP7B-020	OPS		OP-7B	COOLDOWN AND BORATE RHR	6	03JUN04 01:00	03JUN04 06:59	0
196	1	OP1A300F	OPS		OP-1A	HEATUP RCS TO 295 - 305 deg F	1	03JUN04 02:00	03JUN04 02:59	4
197	1	OP1A-210	OPS		OP-1A	RCS LITHIUM ADDITIONS	2	03JUN04 03:00	03JUN04 04:59	37
198	0	OP0310385B	OPS	76	HX-055B-1	ALIGN 2-A05 TO G-01 PER OI-35A	1	03JUN04 05:00*	03JUN04 05:59	0
199	0	OP0310385A	OPS	76	HX-055B-1	PROTECT G-01 DIESEL	12*	03JUN04 05:00	03JUN04 16:59	0
200	1	TS-030C	OPS	77	O-TS-030	TS-30 (SECTION 5.23) TEST OF SI-867B	1	03JUN04 07:00	03JUN04 07:59	0
201	0	OPSCONTB11	OPS		MEETING	OPERATIONS CONTINUING CRC	2	03JUN04 07:00*	03JUN04 08:59	485
202	1	SOPCC002G	OPS		SOP-CC-002	VERIFY CCW FLOWS TO RCP'S AND XSLTDN	2	03JUN04 07:00	03JUN04 08:59	9

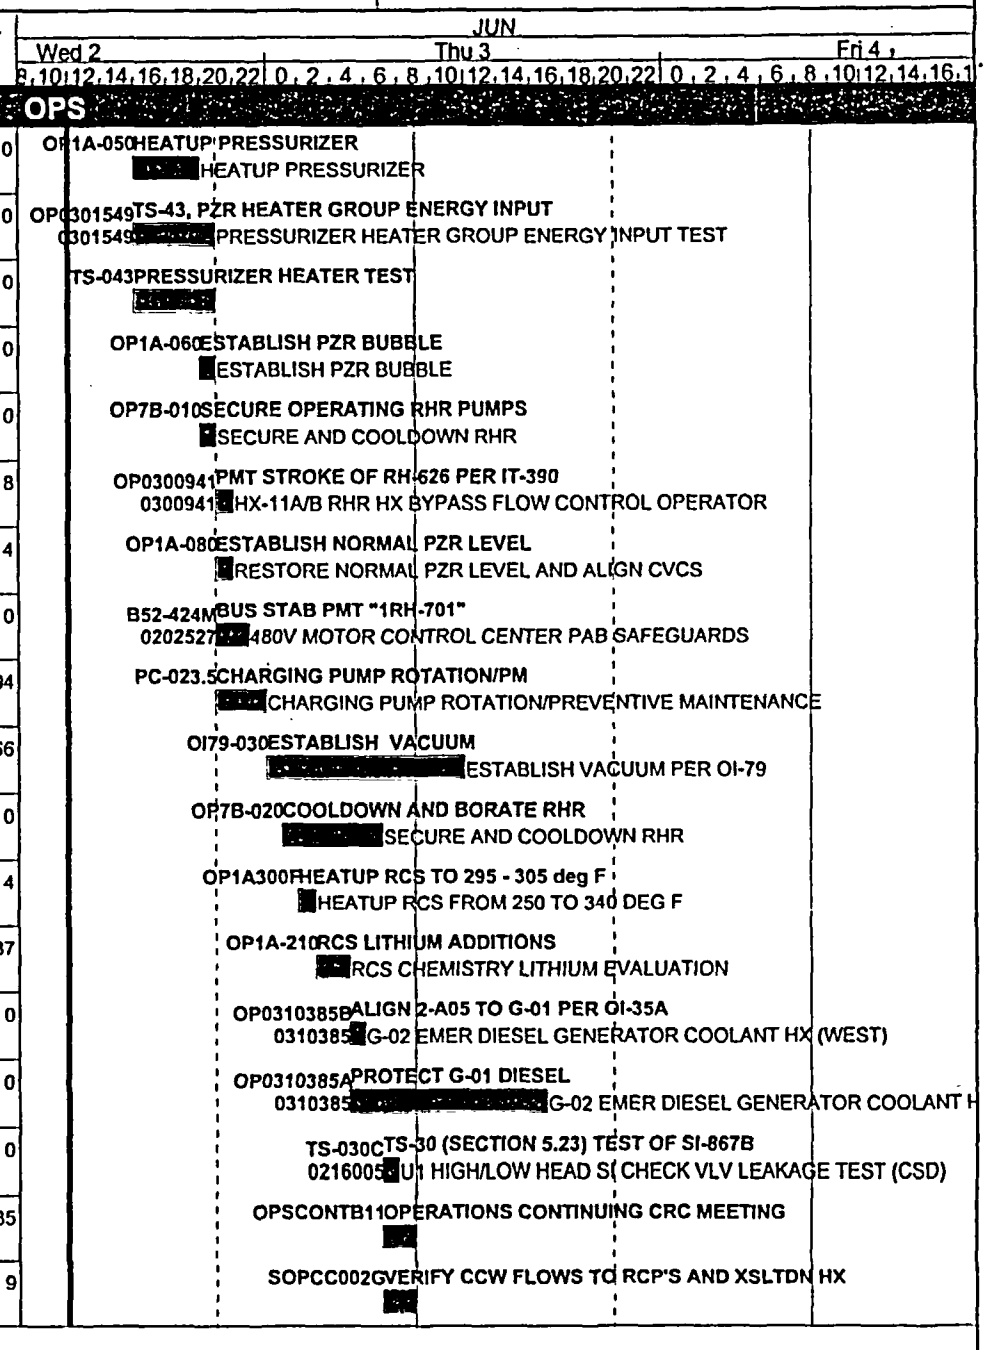

© Primavera Systems, Inc.

U1R28 WORKING SCHEDULE

after 02JUN04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	MF
OPERATIONS										
203	1	OP1A-070	OPS		OP-1A	ALIGN MAIN & AUX FEED AUTO OPS	1	03JUN04 08:00	03JUN04 08:59	9
204	1	OP1A-090	OPS		OP-1A	DISABLE LTOP	1	03JUN04 08:00	03JUN04 08:59	0
205	1	OP1A350F	OPS		OP-1A	HEATUP RCS TO 340 - 345 deg F	1	03JUN04 09:00	03JUN04 09:59	8
206	1	OP0301544	OPS	77	O-TS-032	TS-32, MISCELLANEOUS	3	03JUN04 09:00	03JUN04 11:59	6
207	1	IT-290B	OPS	76	O-IT-0290B	IT-290B, 1P-29 AFP OVERSPEED TEST	4	03JUN04 09:00	03JUN04 12:59	0
208	1	TS-PAM-001	OPS		TS-PAM-001	MISCELLANEOUS EQUIPMENT CHECKS	2	03JUN04 10:00	03JUN04 11:59	0
209	1	OP13A030	OPS		OP-13A	ESTABLISH H2 COOLER COND FLOW	2	03JUN04 11:00	03JUN04 12:59	66
210	1	SIM-RXSU-B	OPS		ADMIN	REACTOR STARTUP SIM INFO SHARING,	3	03JUN04 12:00*	03JUN04 14:59	38
211	1	IT-090A	OPS	77	O-IT-0090A	ATMOSPHERIC STEAM DUMP VALVES STROKE	1	03JUN04 13:00	03JUN04 13:59	0
212	1	OP0215176A	OPS	76	RH-00700-O	RH-700 MOV ACTUATOR OPS PMT	1	03JUN04 14:00	03JUN04 14:59	0
213	1	SIM-RXSU-C	OPS		ADMIN	REACTOR STARTUP SIM INFO SHARING,	3	03JUN04 15:00*	03JUN04 17:59	35
214	0	OP0310385C	OPS	76	HX-055B-1	RE-ALIGN 2-A05 TO G-02 PER OI-35A	1	03JUN04 16:00	03JUN04 16:59	10
215	1	OP0301566	OPS	77	O-IT-0012	IT-12, 1P-11A/B CCW PUMPS/VALVES,	2	03JUN04 16:00*	03JUN04 17:59	476
216	0	OP0301448	OPS	77	O-TS-009	TS-9, CONTROL ROOM H/V SYSTEM CHECKS	24	03JUN04 16:00*	04JUN04 15:59	454
217	1	OP0403305	OPS	76	SI-00852A-	SI-852A-O PERFORM PMT STROKE	1	03JUN04 17:00	03JUN04 17:59	0
218	1	OP1A370F	OPS		OP-1A	HEATUP RCS TO 370 deg F	2	03JUN04 18:00	03JUN04 19:59	0
219	1	PT-SI-8A	OPS		SI-00845A	LINE UP EVENT V TEST RIG PER 1-PT-SI-8	2	03JUN04 18:00	03JUN04 19:59	15
220	1	OP1A-095	OPS		OP-1A ATT.	VERIFY RHR VALVE OPERABILITY	2	03JUN04 20:00	03JUN04 21:59	0

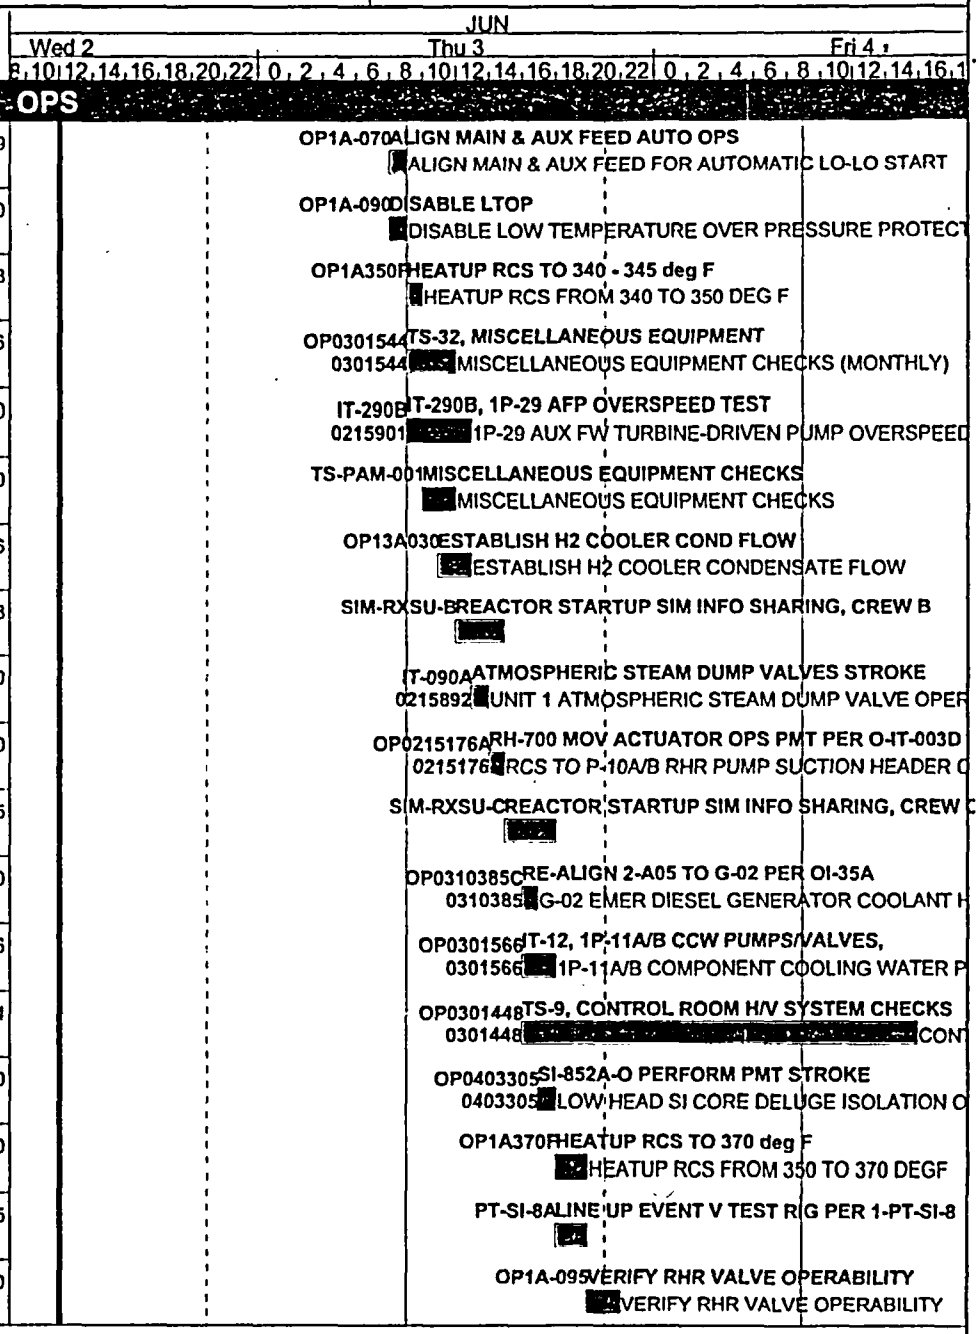

© Primavera Systems, Inc.

U1R28 WORKING SCHEDULE

after 02JUN04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	MF
OPERATIONS										
221	1	OP1A0650	OPS		OP-1A	RAISE RCS PRESSURE TO 650 PSIG	1	03JUN04 22:00	03JUN04 22:59	0
222	1	OP1A0800	OPS		OP-1A	RAISE RCS PRESSURE TO 800 PSIG	1	03JUN04 23:00	03JUN04 23:59	0
223	1	OP1A450F	OPS		OP-1A	HEATUP RCS TO 450 - 470 deg F	5	03JUN04 23:00	04JUN04 03:59	0
224	1	B52-424F	OPS	76	B-42	BUS STAB PMT "1SI-841B"	1	04JUN04 00:00	04JUN04 00:59	0
225	2	OP0301636B	OPS	87	O-PC-025A.	RESTORE RECIRC OF RWST	1	04JUN04 00:00	04JUN04 00:59	469
226	1	OP1A-040	OPS		OP-1A	ALIGN SI ACCUMULATORS	2	04JUN04 02:00	04JUN04 03:59	0
227	0	OP0309023B	OPS	76	C-102	ALIGN 2A06 TO G-03 PER OI-35A	1	04JUN04 03:00*	04JUN04 03:59	3
228	0	OP0309023A	OPS	76	C-102	PROTECT G-03 EDG	13*	04JUN04 03:00	04JUN04 15:59	0
229	1	RETEST09	OPS		RETESTS	WCC RUN S-9 REPORT FOR RCS >540 DEG F	0	04JUN04 04:00	04JUN04 03:59	5
230	1	CL07A010	OPS		CL-7A	COMPLETE SI HEATUP CHECKLIST	1	04JUN04 04:00	04JUN04 04:59	0
231	1	P29-PMT	OPS		P-029	PERFORM PMT RUN OF P-29	3	04JUN04 04:00	04JUN04 06:59	22
232	1	PC-7	OPS	77	O-PC-007	LEAK TEST REACTOR COOLANT GAS VENT	4	04JUN04 04:00	04JUN04 07:59	21
233	1	OP1A500F	OPS		OP-1A	RAISE RCS TEMP/PRESS TO	5	04JUN04 04:00	04JUN04 08:59	0
234	1	OP1A-100	OPS		OP-1A	REDUCE PZR LEVEL TO 20%	1	04JUN04 05:00	04JUN04 05:59	0
235	1	OP1A-110	OPS		OP-1A	CL 4B, HOT VALVE CHECKLIST	6	04JUN04 06:00	04JUN04 11:59	17
236	1	IT-230-A	OPS	77	O-IT-0230	INITIATE RCS LEAK TEST	0	04JUN04 09:00	04JUN04 08:59	0
237	1	RETEST10	OPS		RETESTS	WCC RUN S-10 REPORT FOR RX	0	04JUN04 09:00	04JUN04 08:59	0
238	1	RETEST11	OPS		RETESTS	WCC RUN S-11 REPORT FOR STEAM IN	0	04JUN04 09:00	04JUN04 08:59	0

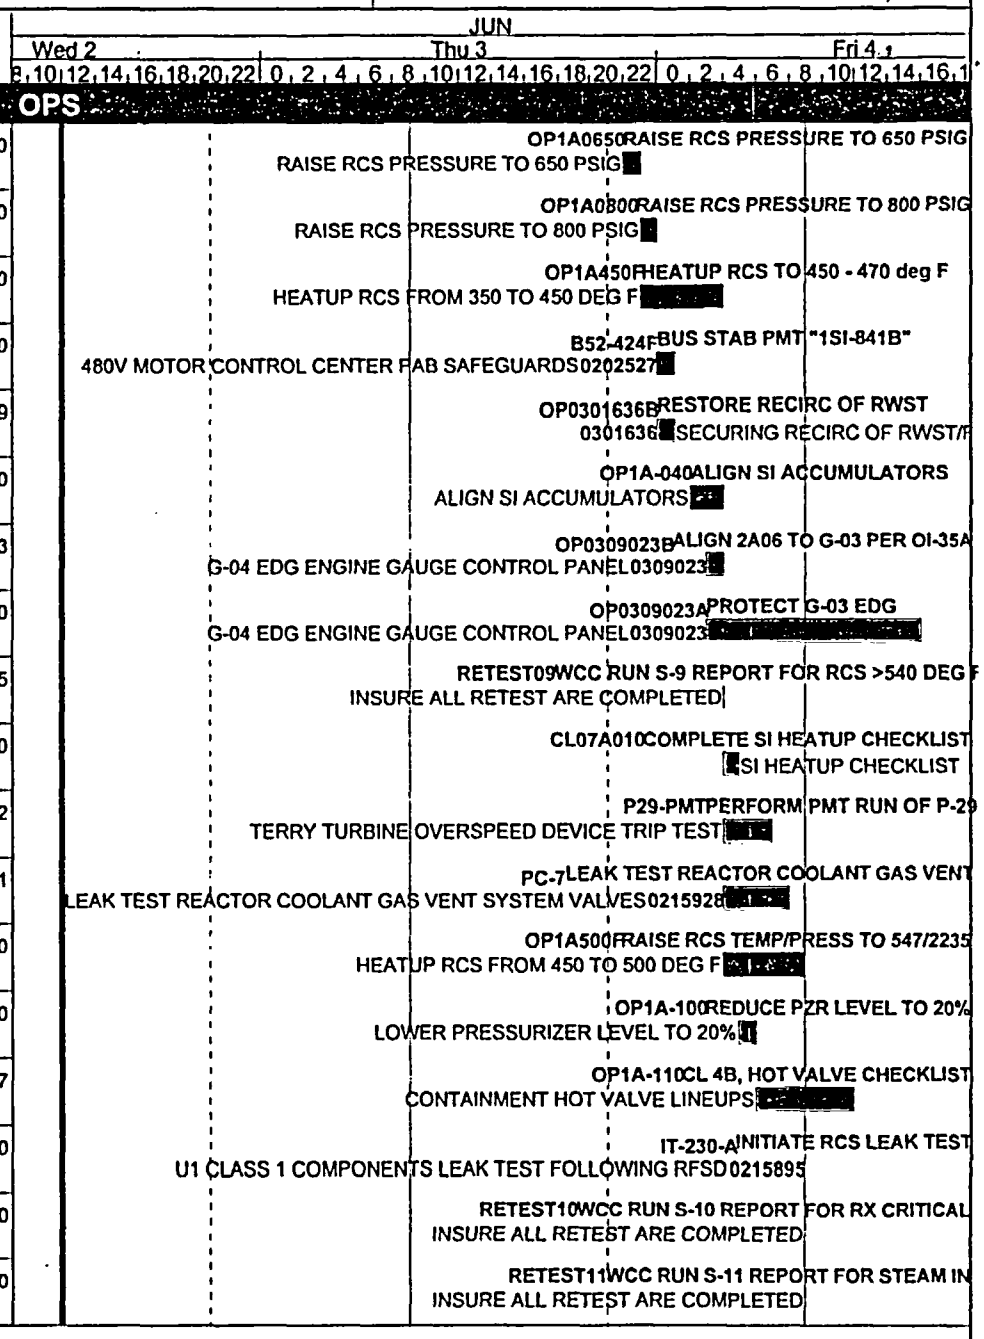

© Primavera Systems, Inc.

U1R28 WORKING SCHEDULE

after 02JUN04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	MF
OPERATIONS										
239	1	RETEST12	OPS		RETESTS	WCC RUN S-12 REPORT FOR SYNC	0	04JUN04 09:00	04JUN04 08:59	0
240	1	RETEST13	OPS		RETESTS	WCC RUN S-13 REPORT FOR 5%	0	04JUN04 09:00	04JUN04 08:59	0
241	1	RETEST14	OPS		RETESTS	WCC RUN S-14 REPORT FOR 25%	0	04JUN04 09:00	04JUN04 08:59	0
242	1	RETEST15	OPS		RETESTS	WCC RUN S-15 REPORT FOR 50%	0	04JUN04 09:00	04JUN04 08:59	0
243	1	RETEST16	OPS		RETESTS	WCC RUN S-16 REPORT FOR 75%	0	04JUN04 09:00	04JUN04 08:59	0
244	1	RETEST17	OPS		RETESTS	WCC RUN S-17 REPORT FOR 100%	0	04JUN04 09:00	04JUN04 08:59	101
245	1	IT-230-B	OPS	77	O-IT-0230	ADJUST RCS TO TEST PRESSURE	2	04JUN04 09:00	04JUN04 10:59	0
246	1	OI14-070	OPS		OI-14	ESTABLISH SG BLOWDOWN	5	04JUN04 09:00	04JUN04 13:59	0
247	1	OP13A010	OPS		OP-13A	ALIGN & START MAIN FEED PUMP	6	04JUN04 09:00	04JUN04 14:59	0
248	1	EP0403495A	OPS	76	PT-RCS-1	OPERATING SUPPORT OF FINAL RCS	4	04JUN04 11:00	04JUN04 14:59	4
249	1	B52-428M	OPS	76	B-42	BUS STAB PMT "W-13B2"	1	04JUN04 13:00	04JUN04 13:59	0
250	0	OP0405880	OPS	78	W-013B1	W-013B1 PMT PER IWP 01-128*E-FN	2	04JUN04 13:00	04JUN04 14:59	0
251	0	OP0309023C	OPS	76	C-102	ALIGN 2A06 TO G-04 PER OI-35A	1	04JUN04 15:00	04JUN04 15:59	454
PRODUCTION PLANNING										
252	1	CL20-020	PPG		CL-20	CONTAINMENT CLOSEOUT	2	02JUN04 10:00A	02JUN04 13:59	63
253	1	COLDSDNY	PPG		MILESTONE	RCS ENTERS HOT SHUTDOWN	0		02JUN04 12:59	0
254	1	ENFPC01U	PPG		MILESTONE	ENTER S/D FIRE PROT COND I	0	02JUN04 13:00	02JUN04 12:59	505
255	1	RHX01A	PPG		MILESTONE	START RHR COMMON WORK	0	02JUN04 21:00	02JUN04 20:59	0
256	1	ADMIN-82	PPG		ADMIN	Startup Readiness Meeting to Exit Hot	4	03JUN04 10:00	03JUN04 13:59	0

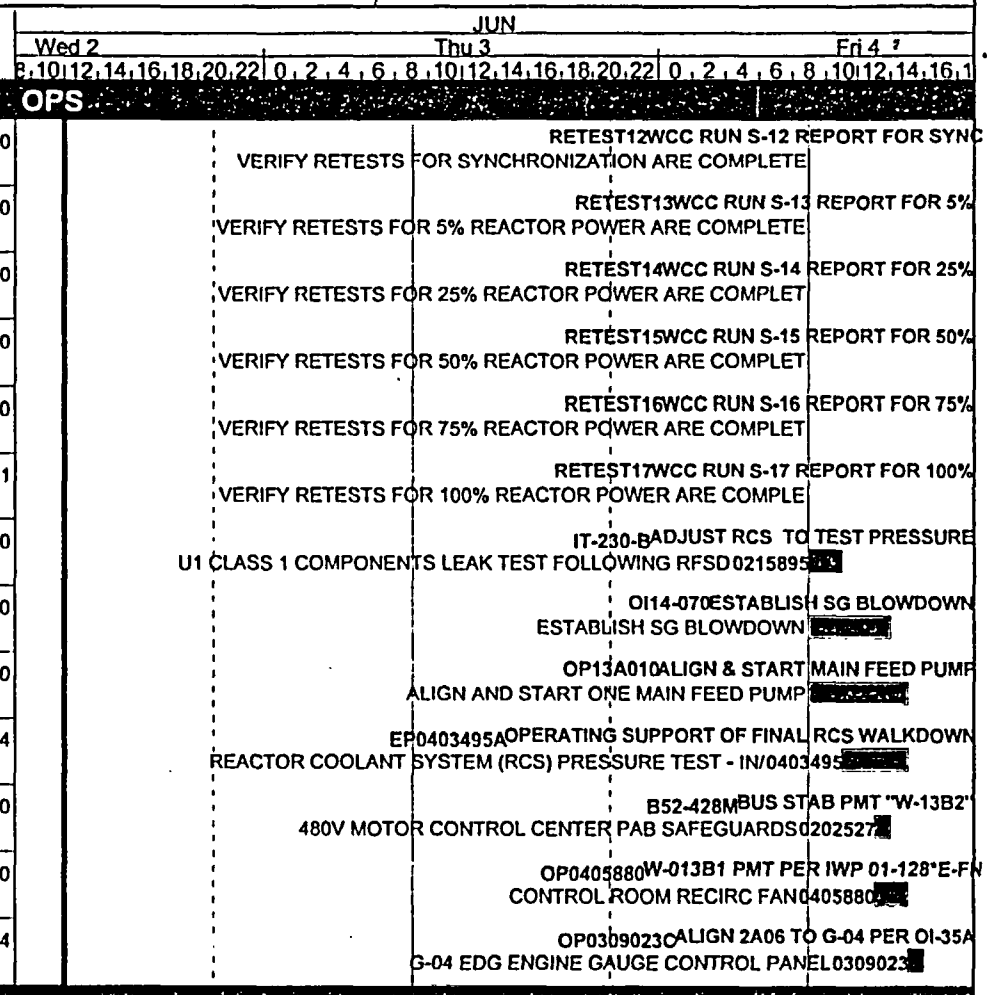

© Primavera Systems, Inc.

U1R28 WORKING SCHEDULE

after 02JUN04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	MF
PRODUCTION PLANNING										
257	1	RHX01Z	PPG		MILESTONE	END RHR COMMON WORK	0	03JUN04 16:00	03JUN04 15:59	0
258	1	MAYX350F	PPG		ADMIN MS	RCS TEMP MAY EXCEED 350 F	0	03JUN04 18:00	03JUN04 17:59	0
259	1	TUX01Z	PPG		MILESTONE	CLOSE MAIN TURB & AUXILIARIES WORK	0	03JUN04 22:00	03JUN04 21:59	56
261	1	CSB12Z	PPG		MILESTONE	END FEED PUMP P28B WORK WINDOW	0	04JUN04 09:00	04JUN04 08:59	0
260	1	NOP-NOT	PPG		MILESTONE	RCS AT NOP NOT NOL	0		04JUN04 08:59	0
REACTOR ENGINEERING										
262	1	RESP-3.1B	PRE	77	RESP 3.1	OBTAIN FINAL RCS RTD DATA PER RESP 3.1	1	04JUN04 08:00	04JUN04 08:59	0
263	1	REI-10.1A	PRE	76	REI 10.1	USE REI 10.1 TO SET UP THE ADRC.	2	04JUN04 09:00	04JUN04 10:59	4
264	1	RESP-3.1PR	PRE	77	RESP 3.1	CLOSE REACTOR TRIP BREAKERS FOR RPI	0	04JUN04 15:00	04JUN04 14:59	0
RADIATION PROTECTION										
265	1	RPJF-101L	RP		DEPOST CTM	POST CONTAINMENT HATCH FOR HEATUP	4	02JUN04 17:00*	02JUN04 20:59	0
266	1	RPJF-101M	RP		DEPOST CTM	DEPOST INTERNAL AREA POSTINGS	4	02JUN04 21:00	03JUN04 00:59	0
267	1	RPJF-101O	RP		DEPOST CTM	POST LHRA AT CONTAINMENT	1	03JUN04 01:00	03JUN04 01:59	0
268	1	RPJF-101P	RP		DEPOST CTM	REMOVE LHRA POSTINGS IN	1	03JUN04 02:00	03JUN04 02:59	50
LAUNDRY DECON - T. ENGLEMAN										
269	0	RPSH007	RP1		SHIELDING	INSTALL SHIELDING AROUND FRISK	16	02JUN04 18:00*	04JUN04 00:59	173
270	1	RPJF-101N	RP1		DEPOST CTM	REMOVE INTERNAL AREA SOPs, PC &	4	02JUN04 21:00	03JUN04 00:59	0
SITE DESIGN MECHANICAL										
271	1	SD-I600-98	SDM	76	R-1	REACTOR HEAD INSPECTION	1	03JUN04 17:00	03JUN04 17:59	0
272	1	SD-I600-94	SDM	76	R-1	MOD 03-041 - HEAD REPAIR CONDITIONAL	1	04JUN04 11:00	04JUN04 11:59	171

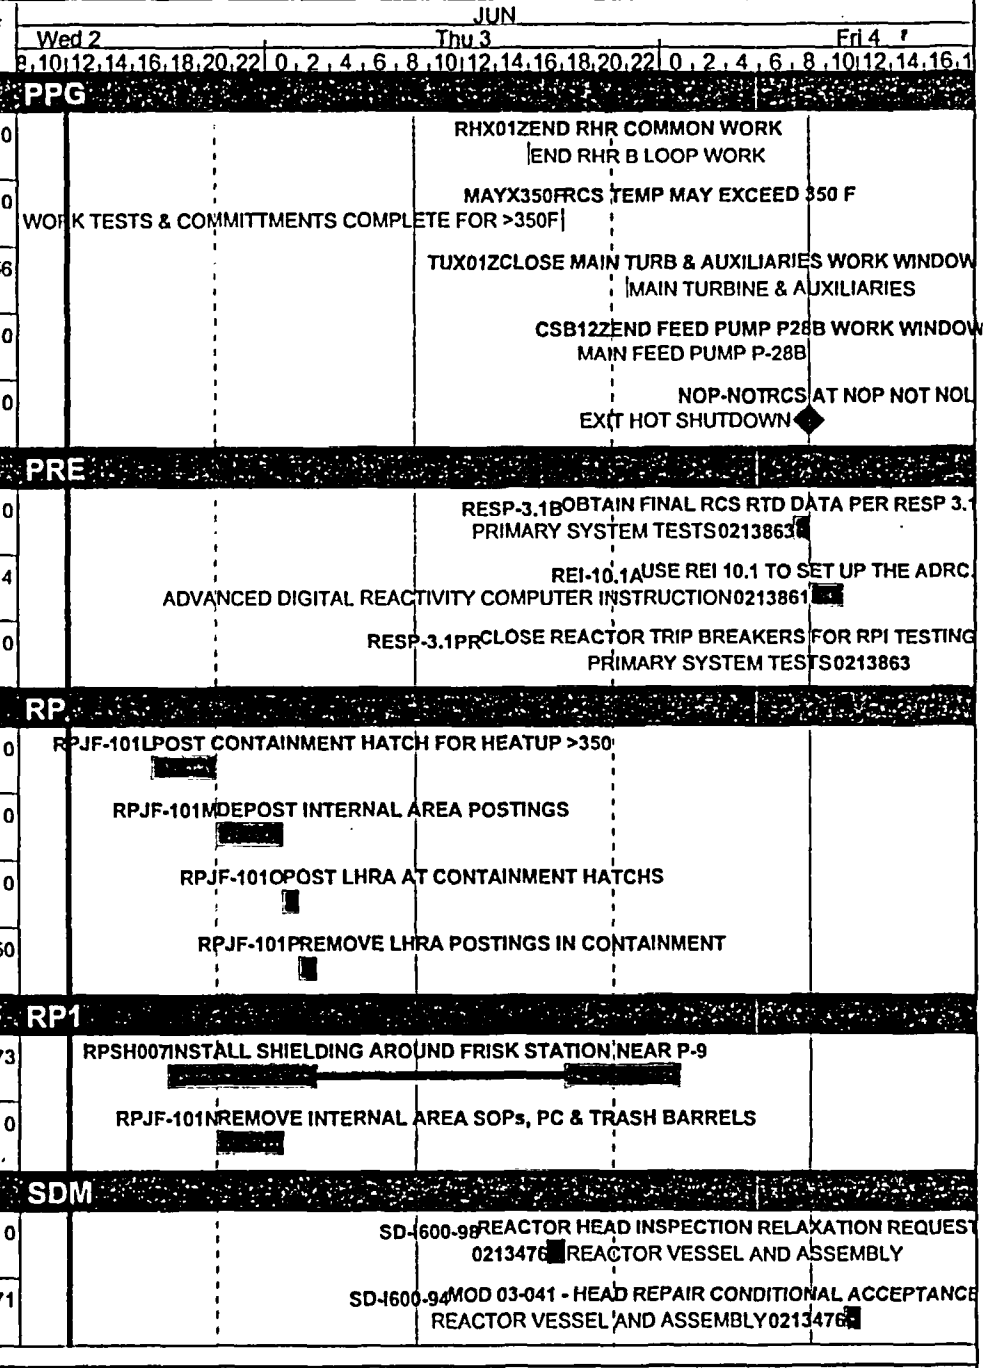

U1R28 WORKING SCHEDULE

after 02JUN04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	MF
WORK CONTROL CENTER										
273	1	CL-2E	WCC		CL 2E	MODE 3 TO MODE 2 CHECKLIST	63*	02MAY04 19:00A	05JUN04 02:59	0
274	1	CL-2F	WCC		CL 2F	MODE 2 TO MODE 1 CHECKLIST	85*	02MAY04 19:00A	06JUN04 00:59	0
275	1	CL-2C	WCC		CL 2C	MODE 5 TO MODE 4 CHECKLIST	1*	26MAY04 19:00A	02JUN04 12:59	0
276	1	CL-2D	WCC		CL 2D	MODE 4 TO MODE 3 CHECKLIST	22*	26MAY04 19:00A	03JUN04 09:59	0
277	1	T-9276-R	WCC		P-28B	1 CS P-28B MM REV3-1	1	31MAY04 09:00A	02JUN04 12:59	44
278	1	RETEST08	WCC		RETESTS	WCC RUN S-8 REPORT FOR RCS >350 DEG F	0	02JUN04 12:00	02JUN04 11:59	21
279	0	T301077H	WCC		F-236	HANG PERMIT (0 STP F-236 MM REV0-3)	1	02JUN04 12:00*	02JUN04 12:59	3
280	0	T301078H	WCC		F-237	HANG PERMIT (0 STP F-237 MM REV0-3)	1	02JUN04 12:00*	02JUN04 12:59	0
281	1	T306095H	WCC		Z-027-1/2/	HANG PERMIT (1 CW Z-27-1/2/3/4 MM REV0-1)	1	02JUN04 12:00*	02JUN04 12:59	5
282	1	T-8689-R	WCC		102-1/TG-0	1 MRR 102-1/TG-01 CE REV3-1	1	02JUN04 13:00	02JUN04 13:59	0
283	0	T214209R	WCC		HX-279	REMOVE TAG (0 VNWH HX-279 MM REV0-1)	1	02JUN04 13:00	02JUN04 13:59	504
284	0	T301076R	WCC		F-235	REMOVE PERMIT (0 STP F-235 MM REV0-3)	1	02JUN04 13:00	02JUN04 13:59	504
285	1	T-0693-R	WCC		OI-32B	1 HG OI-32B OPS REV0-1	1	02JUN04 14:00	02JUN04 14:59	0
286	0	T301078R	WCC		F-237	REMOVE PERMIT (0 STP F-237 MM REV0-3)	1	02JUN04 16:00	02JUN04 16:59	501
287	0	T307011R	WCC		D-105	REMOVE TAG (0 125V D-105 EM REV0-3)	2	02JUN04 19:00	02JUN04 20:59	0
288	0	T201620R	WCC		K-002B	REMOVE TAG (0 IA K-2B MM REV0-1)	1	02JUN04 20:00	02JUN04 20:59	497
289	0	T-7624-R	WCC		IA-00229	0 IA K-2B FIN REV0-1 (IN 2004 FOLDER)	2	02JUN04 20:00	02JUN04 21:59	496
290	0	T201664H	WCC		W-211	HANG TAG (0 VNWH W-211 MM REV0-1)	1	03JUN04 00:00*	03JUN04 00:59	33

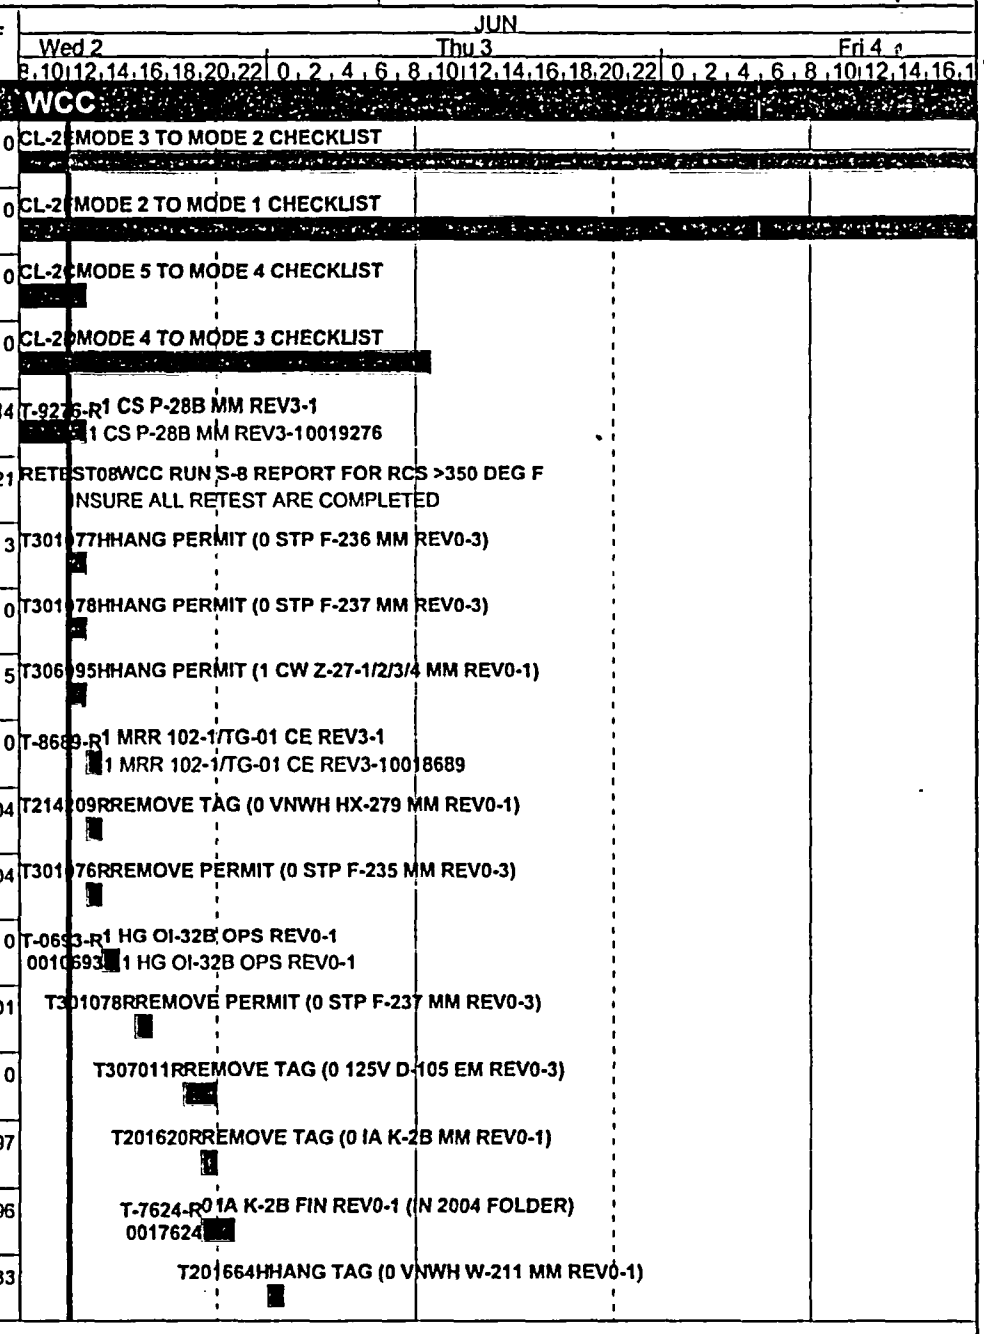

© Primavera Systems, Inc.

U1R28 WORKING SCHEDULE

after 02JUN04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	MF
WORK CONTROL CENTER										
291	1	T-6316-H	WCC		RH-700	1 RH RH-700 EM REV1-1	1	03JUN04 01:00	03JUN04 01:59	0
292	1	T-0482-H	WCC		SI-852A	1 SI SI-852A EM REV0-1	2	03JUN04 01:00	03JUN04 02:59	4
293	1	T306095R	WCC		Z-027-1/2/	REMOVE PERMIT (1 CW Z-27-1/2/3/4 MM REV0-1)	1	03JUN04 02:00	03JUN04 02:59	491
294	0	T310385H	WCC		HX-055B-1	HANG TAG (0 DG G-2 HX-55B1/B2 MM	1	03JUN04 06:00	03JUN04 06:59	0
295	0	T301077R	WCC		F-236	REMOVE PERMIT (0 STP F-236 MM REV0-3)	1	03JUN04 08:00	03JUN04 08:59	485
296	0	T212184R	WCC		T-119A	REMOVE TAG (0 WT TM-02-037 REMOVAL	1	03JUN04 12:00	03JUN04 12:59	481
297	2	T306101H	WCC		Z-027-1/2/	HANG PERMIT (2 CW Z-27-1/2/3/4 MM REV0-1)	1	03JUN04 12:00*	03JUN04 12:59	5
298	1	T-2076-H	WCC		P-029	1 AF P-29 RECOUPLE MM REV0-1	2	03JUN04 13:00	03JUN04 14:59	0
299	1	T-6316-R	WCC		RH-700	1 RH RH-700 EM REV1-1	1	03JUN04 15:00	03JUN04 15:59	0
300	1	T-7754-R	WCC		TG-01-G	1 TU TG-01-G APM REV0-1	1	03JUN04 15:00	03JUN04 15:59	6
301	0	T310385R	WCC		HX-055B-1	REMOVE TAG (0 DG G-2 HX-55B1/B2 MM	1	03JUN04 15:00	03JUN04 15:59	0
302	1	T-2076-R	WCC		P-029	1 AF P-29 RECOUPLE MM REV0-1	1	03JUN04 17:00	03JUN04 17:59	0
303	1	T-8228-R	WCC		Z-013	1 Z Z-13 CAUTION TAG OPS REV0-1	1	03JUN04 17:00	03JUN04 17:59	0
304	1	T-9221-R	WCC		Z-104A	1 SW Z-104A MM REV0-1	1	03JUN04 17:00	03JUN04 17:59	476
305	1	T-9265-R	WCC		P-29	1 AF P-29 UNCOUPLED DSS REV0-1	1	03JUN04 17:00	03JUN04 17:59	0
306	1	T-0482-R	WCC		SI-852A	1 SI SI-852A EM REV0-1	1	03JUN04 18:00	03JUN04 18:59	475
307	1	T301106H	WCC		P-011A	HANG TAG (1 CC P-11A MM REV0-1)	1	03JUN04 20:00*	03JUN04 20:59	0
308	1	T-8169-R	WCC		TG-01-T	1 TU TG-01-T REV6.2-1	1	03JUN04 21:00	03JUN04 21:59	0

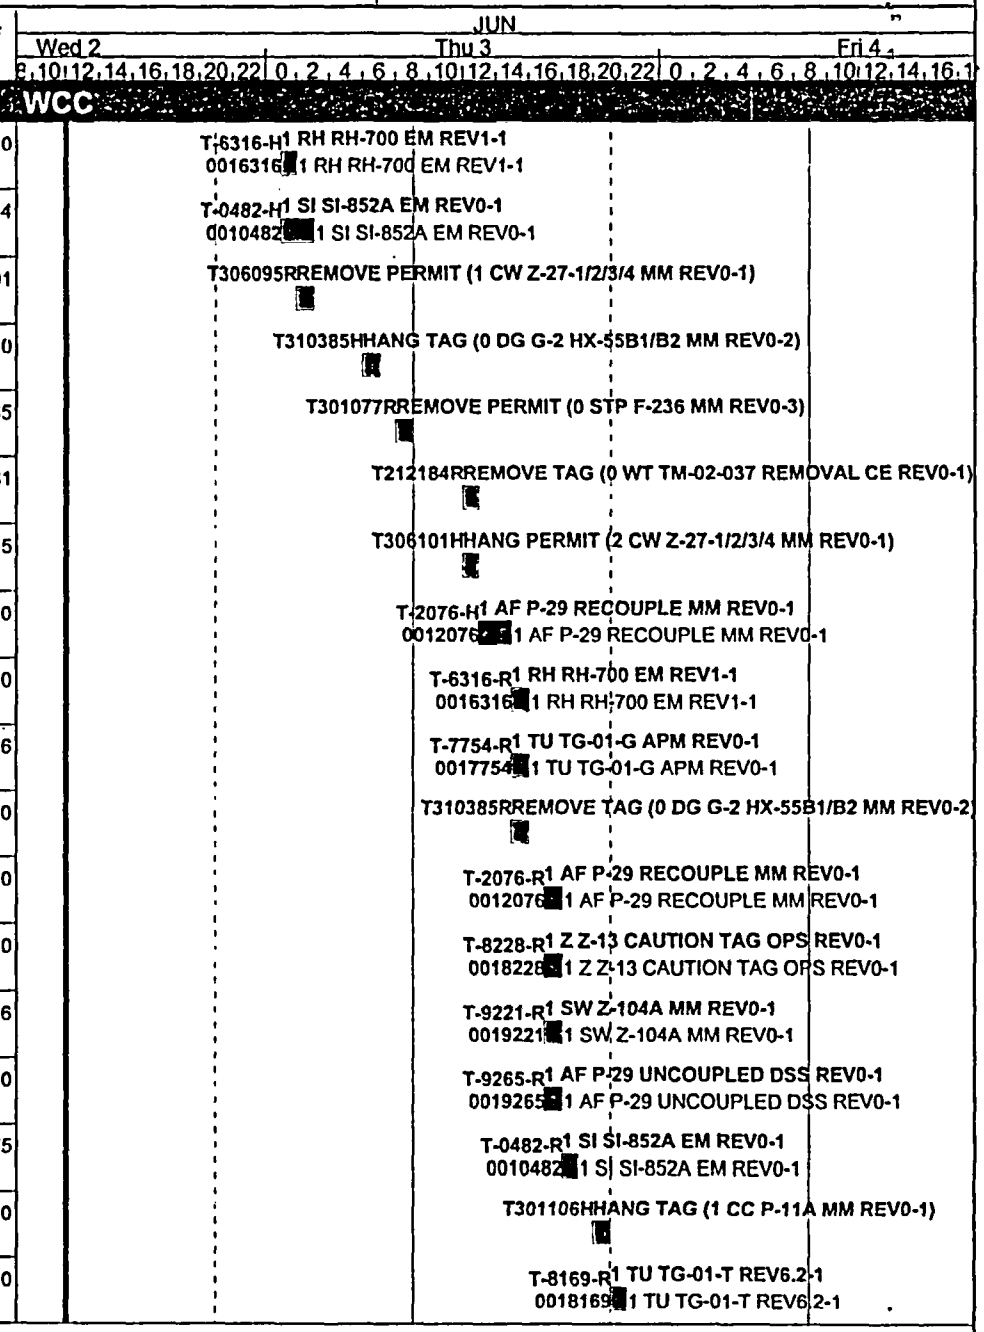

© Primavera Systems, Inc.

U1R28 WORKING SCHEDULE

after 02JUN04 12:00

#	U	ID	RESP	WO ST	EQID	DESCRIPTION	RD	ES	EF	MF
WORK CONTROL CENTER										
309	0	T201662H	WCC		W-210	HANG TAG (0 VNWH W-210 MM REV0-1)	1	04JUN04 00:00*	04JUN04 00:59	5
310	0	T302217H	WCC		F-236	HANG TAG (0 STP F-236 MM REV0-1)	1	04JUN04 00:00*	04JUN04 00:59	6
311	0	T305618R	WCC		P-031B-M	REMOVE TAG (0 CW P-31B-M EM REV0-1)	1	04JUN04 01:00	04JUN04 01:59	468
312	2	T306101R	WCC		Z-027-1/2/	REMOVE PERMIT (2 CW Z-27-1/2/3/4 MM REV0-1)	1	04JUN04 02:00	04JUN04 02:59	467
313	1	T301106R	WCC		P-011A	REMOVE TAG (1 CC P-11A MM REV0-1)	1	04JUN04 03:00	04JUN04 03:59	466
314	2	T304865H	WCC		YS-03587	HANG TAG (2 CW YS-3587 MM REV0-1)	1	04JUN04 05:00*	04JUN04 05:59	0
315	1	T-8022-H	WCC		IWP	1 480V IWP 01-128*E-FN (W-13B1) EM REV0-2	1	04JUN04 07:00*	04JUN04 07:59	0
316	0	T201662R	WCC		W-210	REMOVE TAG (0 VNWH W-210 MM REV0-1)	1	04JUN04 10:00	04JUN04 10:59	459
317	1	T-8022-R	WCC		IWP	1 480V IWP 01-128*E-FN (W-13B1) EM REV0-2	1	04JUN04 12:00	04JUN04 12:59	0
318	0	T201664R	WCC		W-211	REMOVE TAG (0 VNWH W-211 MM REV0-1)	1	04JUN04 14:00	04JUN04 14:59	455
319	0	T302217R	WCC		F-236	REMOVE TAG (0 STP F-236 MM REV0-1)	1	04JUN04 15:00	04JUN04 15:59	454
320	1	T-8019-R	WCC		W-013B1	1 480V IWP 01-128*E-FN (W-13B1) CAUT REV0-1	2	04JUN04 15:00	04JUN04 16:59	0
321	0	T201997H	WCC		W-013B1	HANG TAG (0 VNCR W-13B1 MM REV0-1)	1	04JUN04 17:00*	04JUN04 17:59	0

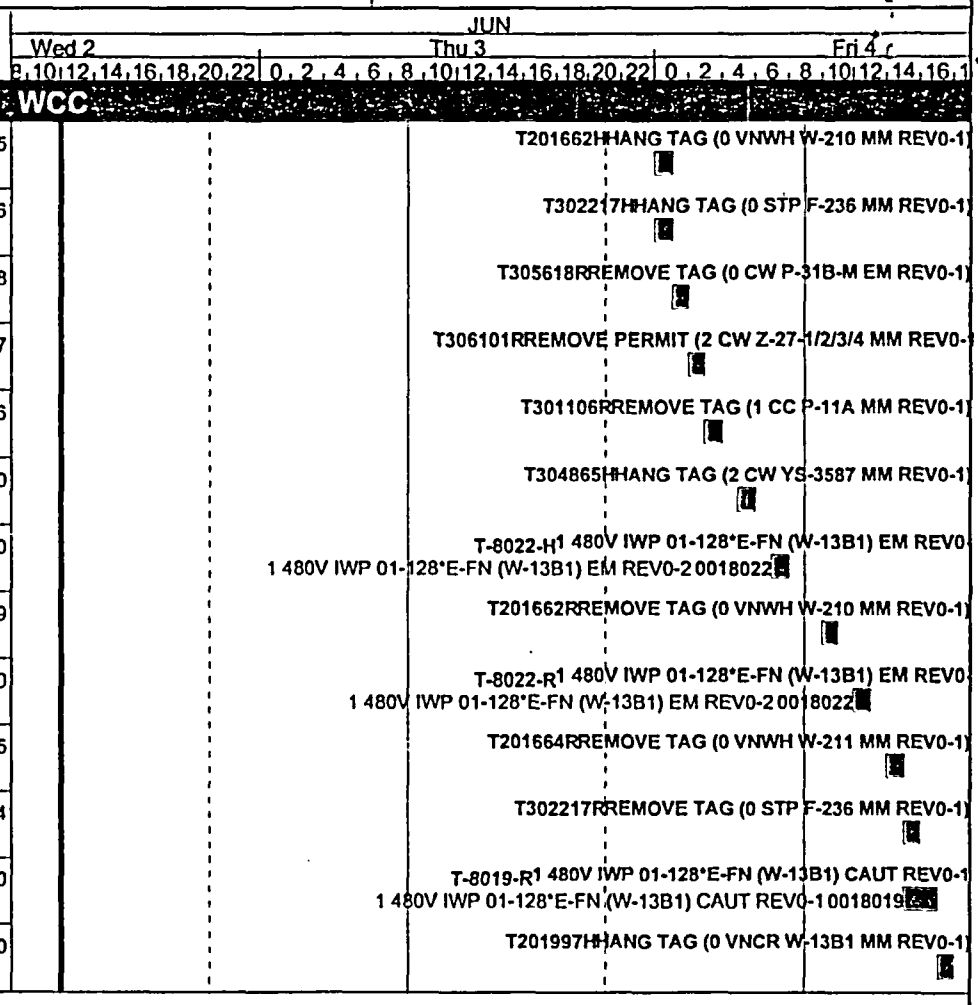

© Primavera Systems, Inc.

LT-03 STANDARD PUBLICATION
FL-03 Execution Publication Set
