Run Date 29NOV05 06:54

PMgr - M. Rutkoske
SPENT FUEL POOL LEAK
LT-AS

KEY DELIVERABLE
KEY DELIVERABLE

ITEM	PROJ	Cal ID	IPEC	WONO	ID	Activity Description	Early start	Early finish	Orig Dur	% Comp	PMGR	RESP INDIV	Predecessors	Successors
SPENT FUEL POOL LEAK														
Spent Fuel Pool Leak/FSB Install Wells														
Rutkoske, Michael														
4742	SFPLXXXX1A	3	SFPL	FPLER01	AZ	DEVELOP FINAL REPORT	31OCT05A	30DEC05	41*	22	RUTKOSKE,	EVERS, BOB	SFPLER01AB	
4741	SFPLXXXX1A	1	SFPL	FPLER01	A1	REVIEW PER DC149	04NOV05A	25NOV05	8	0	RUTKOSKE,	SKONIECZNY	SFPLER01AB	SFPLER01DE
4754	SFPLXXXX1A	1	SFPL	FPLER01	C2	ORDER MULTI LEVEL SAMPLE	13NOV05	15NOV05	3	0	RUTKOSKE,	SANTIS, HA	SFPLER01B2, SFPLER01C1, SFPLER01CA	SFPLER01C3*
4754	SFPLXXXX1A	3	SFPL	FPLER01	C3	RECEIVE MULTI LEVEL SAMPLE	16NOV05	01DEC05	10	0	RUTKOSKE,	SANTIS, HA	SFPLER01C2*	SFPLER01C4*
4750	SFPLXXXX1A	1	SFPL	FPLER01	B3	RETURN TO SERVICE FOR FSB WELL		21NOV05*	0	0	RUTKOSKE,	SKONIECZNY	SFPLER01C4	
4754	SFPLXXXX1A	3	SFPL	FPLER01	C4	INSTALL MULTI LEVEL SAMPLES	02DEC05	05DEC05	2	0	RUTKOSKE,	SANTIS, HA	SFPLER01C3*	SFPLER01B3, SFPLER01C5*
4754	SFPLXXXX1A	3	SFPL	FPLER01	C5	INSTALL CASINGS ALONG WITH FLOOR	06DEC05	11JAN06	25	0	RUTKOSKE,	SANTIS, HA	SFPLER01C4*	SFPLER01C6*
4754	SFPLXXXX1A	3	SFPL	FPLER01	C6	TEST CASINGS ALONG WITH FLOOR	12JAN06	13JAN06	2	0	RUTKOSKE,	SANTIS, HA	SFPLER01C5*	
Spent Fuel Pool Leak/Install Site Wells														
Rutkoske, Michael														
4763	SFPLXXXX1B	3	SFPL	FPLER01	E#	INSTALL STILL WELLS	17NOV05A	14NOV05	2	50	RUTKOSKE,	KULAGA, J	SFPLER01EG	SFPLER01E2*
4763	SFPLXXXX1B	3	SFPL	FPLER01	E4	APPROVE DESIGN	14NOV05	14NOV05	1	0	RUTKOSKE,	EVERS, BOB	SFPLER01DA, SFPLER01EF	SFPLER01CB
4765	SFPLXXXX1B	3	SFPL	FPLER01	E2	VACUUM DRILL SITE WELLS	15NOV05	08FEB06	58	0	RUTKOSKE,	KULAGA, J	SFPLER01CB, SFPLER01E#*, SFPLER01E%, SFPLER01E1,	SFPLER01E@, SFPLER01EH, SFPLER01LU*
4766	SFPLXXXX1B	3	SFPL	FPLER01	LU	DRILL MW-38 (#9)	09FEB06*	10FEB06	2	0	RUTKOSKE,	KULAGA, J	SFPLER01E2*, SFPLER01E@	SFPLER01LW*

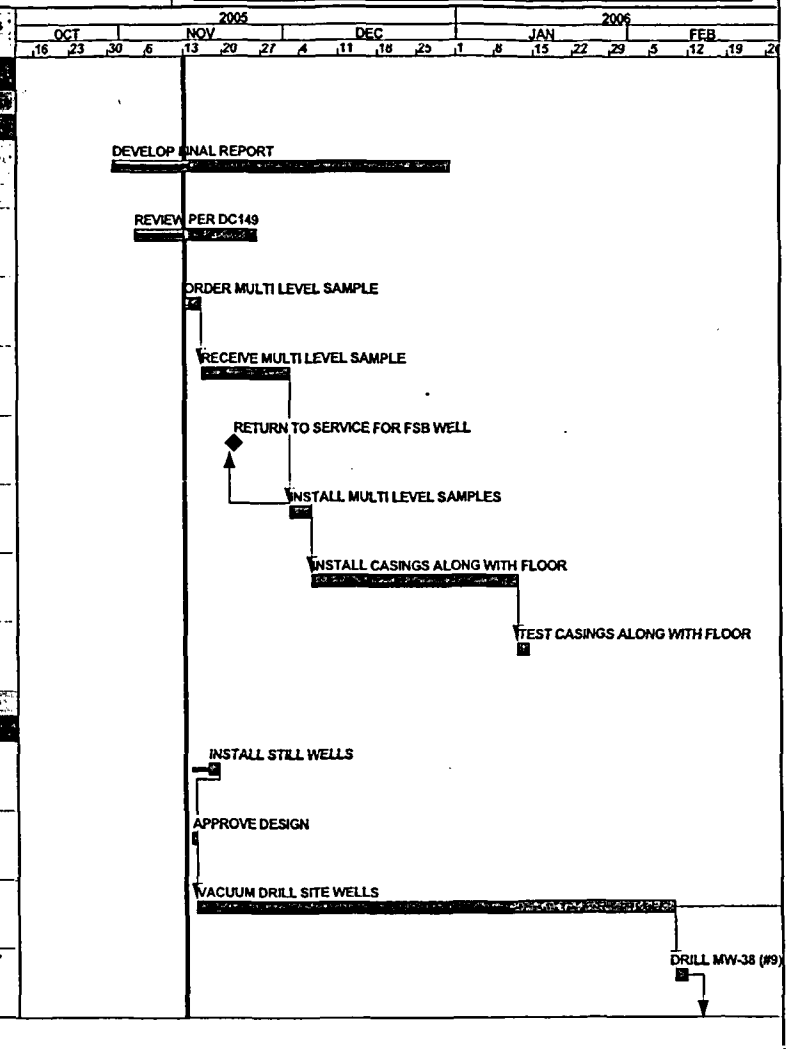

ITEM	PROJ	Cal ID	IPEC	WONO	ID	Activity Description	Early start	Early finish	Orig Dur	% Comp	PMGR	RESP INDIV	Predecessors	Successors
4766	SFPLXXXX1B	3	SFPL	FPLER01	LW	INSTALL WELL MW-38 (#9)	14FEB06	14FEB06	1	0	RUTKOSKE,	KULAGA, J	SFPLER01LU*	SFPLER01EI*, SFPLER01EN*
4766	SFPLXXXX1B	3	SFPL	FPLER01	EI	PREP WELL MW-38 (#9)	15FEB06	16FEB06	2	0	RUTKOSKE,	KULAGA, J	SFPLER01LW*	SFPLER01EN*, SFPLER01EV*
4766	SFPLXXXX1B	3	SFPL	FPLER01	EN	DRILL #2	15FEB06	16FEB06	2	0	RUTKOSKE,	KULAGA, J	SFPLER01EI*, SFPLER01LW*	SFPLER01EO*
4766	SFPLXXXX1B	3	SFPL	FPLER01	EO	INSTALL WELL #2	17FEB06	17FEB06	1	0	RUTKOSKE,	KULAGA, J	SFPLER01EN*, SFPLER01EV*	SFPLER01EQ*
4766	SFPLXXXX1B	3	SFPL	FPLER01	EV	RTS WELL MW-38 (#9)	17FEB06	21FEB06	2	0	RUTKOSKE,	KULAGA, J	SFPLER01EI*	SFPLER01EO*, SFPLER01NA*
4766	SFPLXXXX1B	3	SFPL	FPLER01	EQ	PREP WELL #2	21FEB06	22FEB06	2	0	RUTKOSKE,	KULAGA, J	SFPLER01EO*	SFPLER01E9*, SFPLER01EP*, SFPLER01NB*
4766	SFPLXXXX1B	3	SFPL	FPLER01	NA	RAD MONITORING SECTION WELL MW-38 (#9)	22FEB06	23FEB06	2	0	RUTKOSKE,	AXELSON	SFPLER01EV*	
4766	SFPLXXXX1B	3	SFPL	FPLER01	E9	RTS WELL #2	23FEB06	24FEB06	2	0	RUTKOSKE,	KULAGA, J	SFPLER01EQ*	SFPLER01ER*, SFPLER01ND*
4766	SFPLXXXX1B	3	SFPL	FPLER01	EP	DRILL #3	23FEB06	24FEB06	2	0	RUTKOSKE,	KULAGA, J	SFPLER01EQ*	
4766	SFPLXXXX1B	3	SFPL	FPLER01	ER	INSTALL WELL #3	23FEB06	23FEB06	1	0	RUTKOSKE,	KULAGA, J	SFPLER01E9*	SFPLER01EX*
4766	SFPLXXXX1B	3	SFPL	FPLER01	NB	PACKER/LOGGER WELL #2	23FEB06	24FEB06	2	0	RUTKOSKE,	KULAGA, J	SFPLER01EQ*	SFPLER01NC*
4766	SFPLXXXX1B	3	SFPL	FPLER01	EW	DRILL #4	24FEB06	27FEB06	2	0	RUTKOSKE,	KULAGA, J	SFPLER01EX*	SFPLER01EY*
4766	SFPLXXXX1B	3	SFPL	FPLER01	EX	PREP WELL #3	24FEB06	27FEB06	2	0	RUTKOSKE,	KULAGA, J	SFPLER01ER*	SFPLER01ES*, SFPLER01EW*, SFPLER01NE*
4766	SFPLXXXX1B	3	SFPL	FPLER01	NC	MULTI LEVEL SAMPLE WELL #2	27FEB06	16MAR06	14	0	RUTKOSKE,	KULAGA, J	SFPLER01NB*	
4766	SFPLXXXX1B	3	SFPL	FPLER01	ND	RAD MONITORING SECTION WELL #2	27FEB06	28FEB06	2	0	RUTKOSKE,	AXELSON	SFPLER01E9*	
4766	SFPLXXXX1B	3	SFPL	FPLER01	ES	RTS WELL #3	28FEB06	01MAR06	2	0	RUTKOSKE,	KULAGA, J	SFPLER01EX*	SFPLER01EY*, SFPLER01NG*

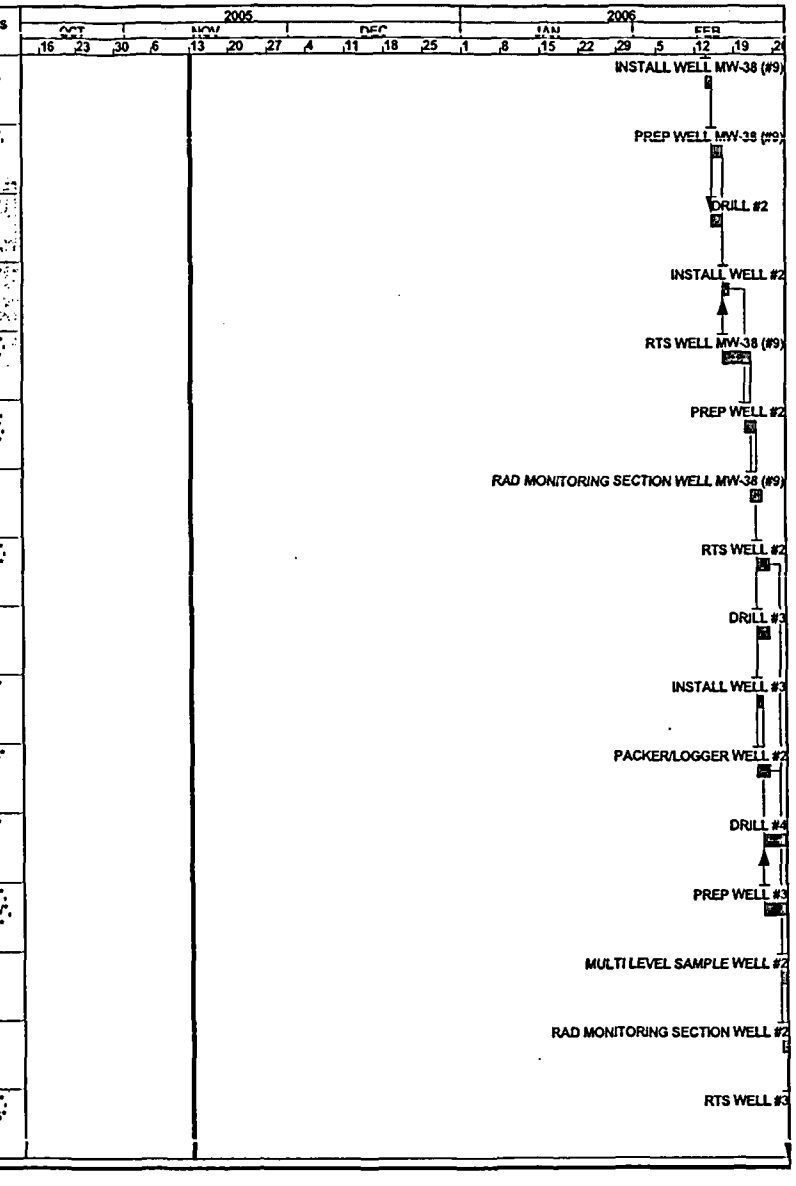

ITEM	PROJ	Cal ID	IPEC	WONO	ID	Activity Description	Early start	Early finish	Orig Dur	% Comp	PMGR	RESP INDIV	Predecessors	Successors
4766	SFPLXXXX1B	3	SFPL	FPLER01	EY	INSTALL WELL #4	28FEB06	28FEB06	1	0	RUTKOSKE,	KULAGA, J	SFPLER01ES*, SFPLER01EW*	SFPLER01LB*
4766	SFPLXXXX1B	3	SFPL	FPLER01	NE	PACKER/LOGGER WELL #3	28FEB06	01MAR06	2	0	RUTKOSKE,	KULAGA, J	SFPLER01EX*	SFPLER01NF*
4766	SFPLXXXX1B	3	SFPL	FPLER01	LA	DRILL #5	01MAR06	02MAR06	2	0	RUTKOSKE,	KULAGA, J	SFPLER01LB*	SFPLER01LC*
4766	SFPLXXXX1B	3	SFPL	FPLER01	LB	PREP WELL #4	01MAR06	02MAR06	2	0	RUTKOSKE,	KULAGA, J	SFPLER01EY*	SFPLER01LA*, SFPLER01LD*, SFPLER01NH*
4766	SFPLXXXX1B	3	SFPL	FPLER01	NF	MULTI LEVEL SAMPLE	02MAR06	21MAR06	14	0	RUTKOSKE,	KULAGA, J	SFPLER01NE*	
4766	SFPLXXXX1B	3	SFPL	FPLER01	NG	RAD MONITOR SECTION WELL #3	02MAR06	03MAR06	2	0	RUTKOSKE,	AXELSON	SFPLER01ES*	
4766	SFPLXXXX1B	3	SFPL	FPLER01	LC	INSTALL WELL #5	03MAR06	03MAR06	1	0	RUTKOSKE,	KULAGA, J	SFPLER01LA*, SFPLER01LD*	SFPLER01LG*
4766	SFPLXXXX1B	3	SFPL	FPLER01	LD	RTS WELL #4	03MAR06	06MAR06	2	0	RUTKOSKE,	KULAGA, J	SFPLER01LB*	SFPLER01LC*, SFPLER01NJ*
4766	SFPLXXXX1B	3	SFPL	FPLER01	NH	PACKER / LOGGER WELL #4	03MAR06	06MAR06	2	0	RUTKOSKE,	KULAGA, J	SFPLER01LB*	SFPLER01NI*
4766	SFPLXXXX1B	3	SFPL	FPLER01	LF	DRILL #6	06MAR06	07MAR06	2	0	RUTKOSKE,	KULAGA, J	SFPLER01LG*	SFPLER01LH*
4766	SFPLXXXX1B	3	SFPL	FPLER01	LG	PREP WELL #5	06MAR06	07MAR06	2	0	RUTKOSKE,	KULAGA, J	SFPLER01LC*	SFPLER01LF*, SFPLER01LI*, SFPLER01NK*
4766	SFPLXXXX1B	3	SFPL	FPLER01	NI	MULTI LEVEL SAMPLE WELL #4	07MAR06	24MAR06	14	0	RUTKOSKE,	KULAGA, J	SFPLER01NH*	
4766	SFPLXXXX1B	3	SFPL	FPLER01	NJ	RAD MONITORING SECTION WELL #4	07MAR06	08MAR06	2	0	RUTKOSKE,	KULAGA, J	SFPLER01LD*	
4766	SFPLXXXX1B	3	SFPL	FPLER01	LH	INSTALL WELL #6	08MAR06	08MAR06	1	0	RUTKOSKE,	KULAGA, J	SFPLER01LF*, SFPLER01LI*	SFPLER01LL*
4766	SFPLXXXX1B	3	SFPL	FPLER01	LI	RTS WELL #5	08MAR06	09MAR06	2	0	RUTKOSKE,	KULAGA, J	SFPLER01LG*	SFPLER01LH*, SFPLER01NM*
4766	SFPLXXXX1B	3	SFPL	FPLER01	NK	PACKER / LOGGER WELL #5	08MAR06	09MAR06	2	0	RUTKOSKE,	KULAGA, J	SFPLER01LG*	SFPLER01NL*

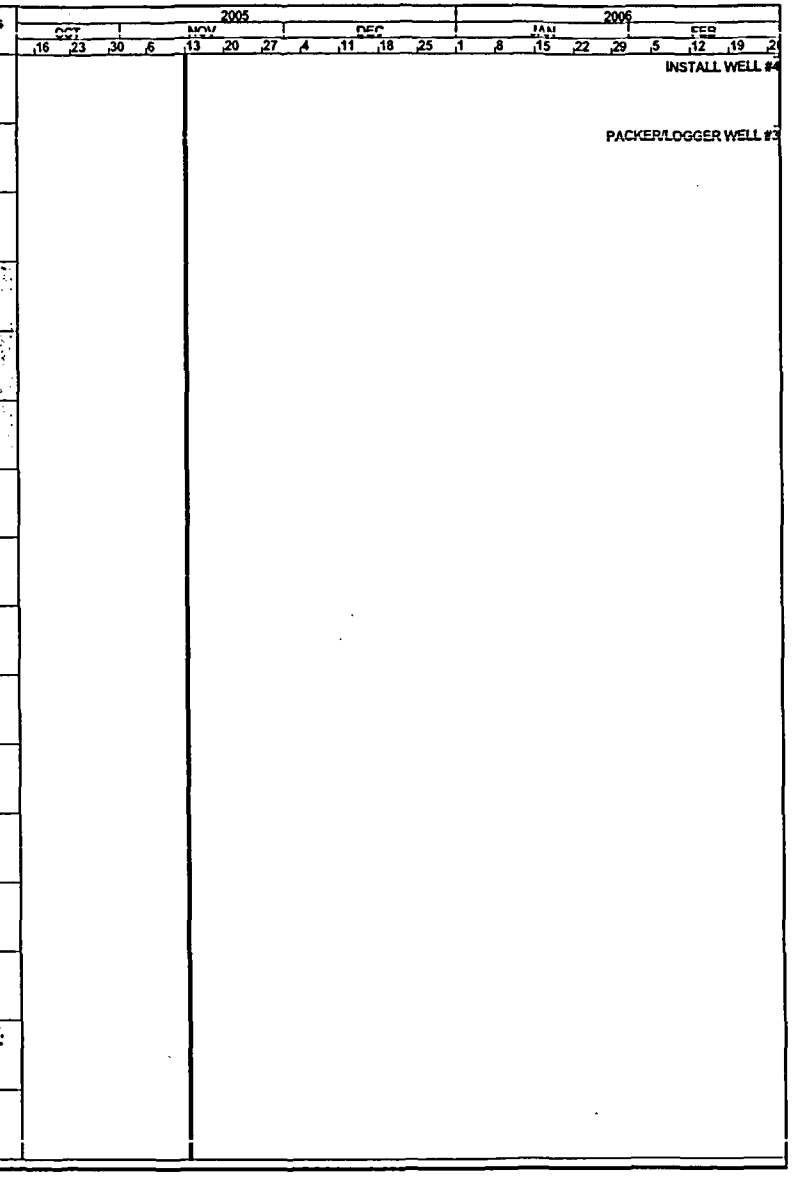

ITEM	PROJ	Cal ID	IPEC	WONO	ID	Activity Description	Early start	Early finish	Orig Dur	% Comp	PMGR	RESP INDIV	Predecessors	Successors
4766	SFPLXXXX1B	3	SFPL	FPLER01	LK	DRILL #7	09MAR06	10MAR06	2	0	RUTKOSKE,	KULAGA, J	SFPLER01LL*	SFPLER01LM*
4766	SFPLXXXX1B	3	SFPL	FPLER01	LL	PREP WELL #6	09MAR06	10MAR06	2	0	RUTKOSKE,	KULAGA, J	SFPLER01LH*	SFPLER01LK*, SFPLER01LN*, SFPLER01NN*
4766	SFPLXXXX1B	3	SFPL	FPLER01	NL	MULTI LEVEL SAMPLE WELL #5	10MAR06	29MAR06	14	0	RUTKOSKE,	KULAGA, J	SFPLER01NK*	
4766	SFPLXXXX1B	3	SFPL	FPLER01	NM	RAD MONITORING SECTION WELL #5	10MAR06	13MAR06	2	0	RUTKOSKE,	AXELSON	SFPLER01LI*	
4766	SFPLXXXX1B	3	SFPL	FPLER01	LM	INSTALL WELL #7	13MAR06	13MAR06	1	0	RUTKOSKE,	KULAGA, J	SFPLER01LK*, SFPLER01LN*	SFPLER01LQ*
4766	SFPLXXXX1B	3	SFPL	FPLER01	LN	RTS WELL #6	13MAR06	14MAR06	2	0	RUTKOSKE,	KULAGA, J	SFPLER01LL*	SFPLER01LM*, SFPLER01NP*
4766	SFPLXXXX1B	3	SFPL	FPLER01	NN	PACKER / LOGGER WELL #6	13MAR06	14MAR06	2	0	RUTKOSKE,	KULAGA, J	SFPLER01LL*	SFPLER01NO*
4766	SFPLXXXX1B	3	SFPL	FPLER01	LP	DRILL #8	14MAR06	15MAR06	2	0	RUTKOSKE,	KULAGA, J	SFPLER01LQ*	SFPLER01LR*
4766	SFPLXXXX1B	3	SFPL	FPLER01	LQ	PREP WELL #7	14MAR06	15MAR06	2	0	RUTKOSKE,	KULAGA, J	SFPLER01LM*	SFPLER01LP*, SFPLER01LS*, SFPLER01NQ*
4766	SFPLXXXX1B	3	SFPL	FPLER01	NO	MULTI LEVEL SAMPLE WELL #6	15MAR06	03APR06	14	0	RUTKOSKE,	KULAGA, J	SFPLER01NN*	
4766	SFPLXXXX1B	3	SFPL	FPLER01	NP	RAD MONITORING SECTION WELL #6	15MAR06	16MAR06	2	0	RUTKOSKE,	AXELSON	SFPLER01LN*	
4766	SFPLXXXX1B	3	SFPL	FPLER01	LR	INSTALL WELL #8	16MAR06	16MAR06	1	0	RUTKOSKE,	KULAGA, J	SFPLER01LP*, SFPLER01LS*	SFPLER01LV*
4766	SFPLXXXX1B	3	SFPL	FPLER01	LS	RTS WELL #7	16MAR06	17MAR06	2	0	RUTKOSKE,	KULAGA, J	SFPLER01LQ*	SFPLER01LR*, SFPLER01NS*
4766	SFPLXXXX1B	3	SFPL	FPLER01	NQ	PACKER / LOGGER WELL #7	16MAR06	17MAR06	2	0	RUTKOSKE,	KULAGA, J	SFPLER01LQ*	SFPLER01NR*
4766	SFPLXXXX1B	3	SFPL	FPLER01	LV	PREP WELL #8	17MAR06	20MAR06	2	0	RUTKOSKE,	KULAGA, J	SFPLER01LR*	SFPLER01LX*, SFPLER01NT*
4766	SFPLXXXX1B	3	SFPL	FPLER01	NR	MULTI LEVEL SAMPLE WELL #7	20MAR06	06APR06	14	0	RUTKOSKE,	KULAGA, J	SFPLER01NQ*	

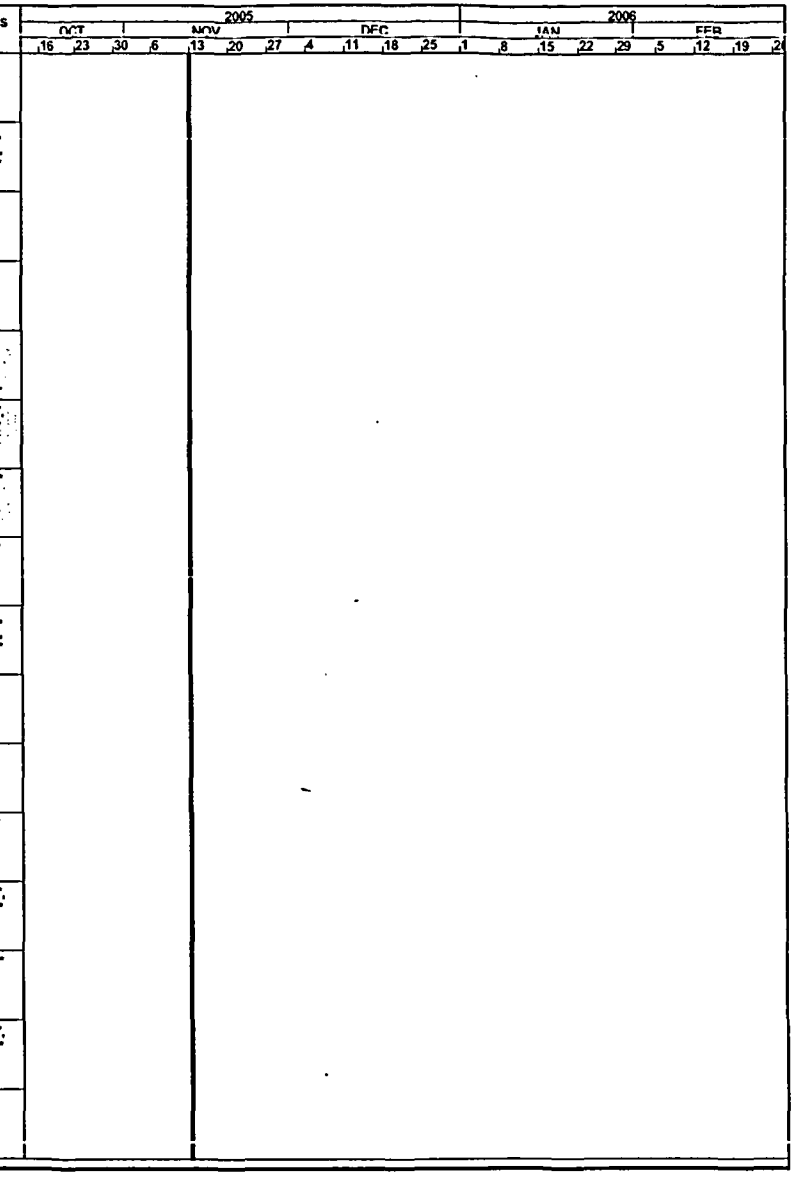

ITEM	PROJ	Cal ID	IPEC	WONO	ID	Activity Description	Early start	Early finish	Orig Dur	% Comp	PMGR	RESP INDIV	Predecessors	Successors
4766	SFPLXXXX1B	3	SFPL	FPLER01	NS	RAD MONITORING SECTION WELL #7	20MAR06	21MAR06	2	0	RUTKOSKE,	AXELSON	SFPLER01LS*	
4766	SFPLXXXX1B	3	SFPL	FPLER01	LX	RTS WELL #8	21MAR06	22MAR06	2	0	RUTKOSKE,	KULAGA, J	SFPLER01LV*	SFPLER01EH*, SFPLER01NV*
4766	SFPLXXXX1B	3	SFPL	FPLER01	NT	PACKER / LOGGER WELL #8	21MAR06	22MAR06	2	0	RUTKOSKE,	KULAGA, J	SFPLER01LV*	SFPLER01NU*
4766	SFPLXXXX1B	3	SFPL	FPLER01	EH	SURVEY/RELEASE DRILL EQUIPMENT	23MAR06	28MAR06	4	0	RUTKOSKE,	AXELSON	SFPLER01E2, SFPLER01LX*	
4766	SFPLXXXX1B	3	SFPL	FPLER01	NU	MULTI LEVEL SAMPLE WELL #8	23MAR06	11APR06	14	0	RUTKOSKE,	KULAGA, J	SFPLER01NT*	
4766	SFPLXXXX1B	3	SFPL	FPLER01	NV	RAD MONITORING SECTION WELL #8	23MAR06	24MAR06	2	0	RUTKOSKE,	AXELSON	SFPLER01LX*	
Spent Fuel Pool Leak/South Wall Collection Mod														
Rutkoske/Michael														
4767	SFPLXXXX1C	3	SFPL	FPLER01	E5	DEVELOP COLLECTION MOD	16OCT05A	16NOV05	22*	86	RUTKOSKE,	NUTA, DRAG		SFPLER01EA, SFPLER01EJ*
4769	SFPLXXXX1C	3	SFPL	FPLER01	EA	ORDER MATERIALS	17NOV05A	18NOV05	5	0	RUTKOSKE,	SANTIS, HA	SFPLER01E5	SFPLER01EB
4767	SFPLXXXX1C	3	SFPL	FPLER01	EJ	REVIEW MOD	17NOV05	28NOV05	6	0	RUTKOSKE,	NUTA, DRAG	SFPLER01E5*	SFPLER01EK*
4767	SFPLXXXX1C	3	SFPL	FPLER01	EK	INCORPORATE COMMENTS	29NOV05	02DEC05	4	0	RUTKOSKE,	NUTA, DRAG	SFPLER01EJ*	SFPLER01E8*
4768	SFPLXXXX1C	3	SFPL	FPLER01	E8	PERFORM EQRT	05DEC05*	07DEC05	3	0	RUTKOSKE,	NUTA, DRAG	SFPLER01EK*	SFPLER01E6*
4768	SFPLXXXX1C	3	SFPL	FPLER01	E6	APPROVE MOD	07DEC05	07DEC05	1	0	RUTKOSKE,	NUTA, DRAG	SFPLER01E8*	SFPLER01E7*
4757	SFPLXXXX1C	3	SFPL	FPLER01	E7	DEVELOP WORK ORDER	08DEC05	09DEC05	2	0	RUTKOSKE,	SANTIS, HA	SFPLER01E6*	SFPLER01EB*
4770	SFPLXXXX1C	3	SFPL	FPLER01	EB	READY TO WORK	12DEC05	12DEC05	1	0	RUTKOSKE,	SANTIS, HA	SFPLER01E7*, SFPLER01EA	SFPLER01EC*
4771	SFPLXXXX1C	3	SFPL	FPLER01	EC	INSTALL PENETRATION INTO PIPE PEN	13DEC05	19DEC05	5	0	RUTKOSKE,	SANTIS, HA	SFPLER01EB*	SFPLER01EE

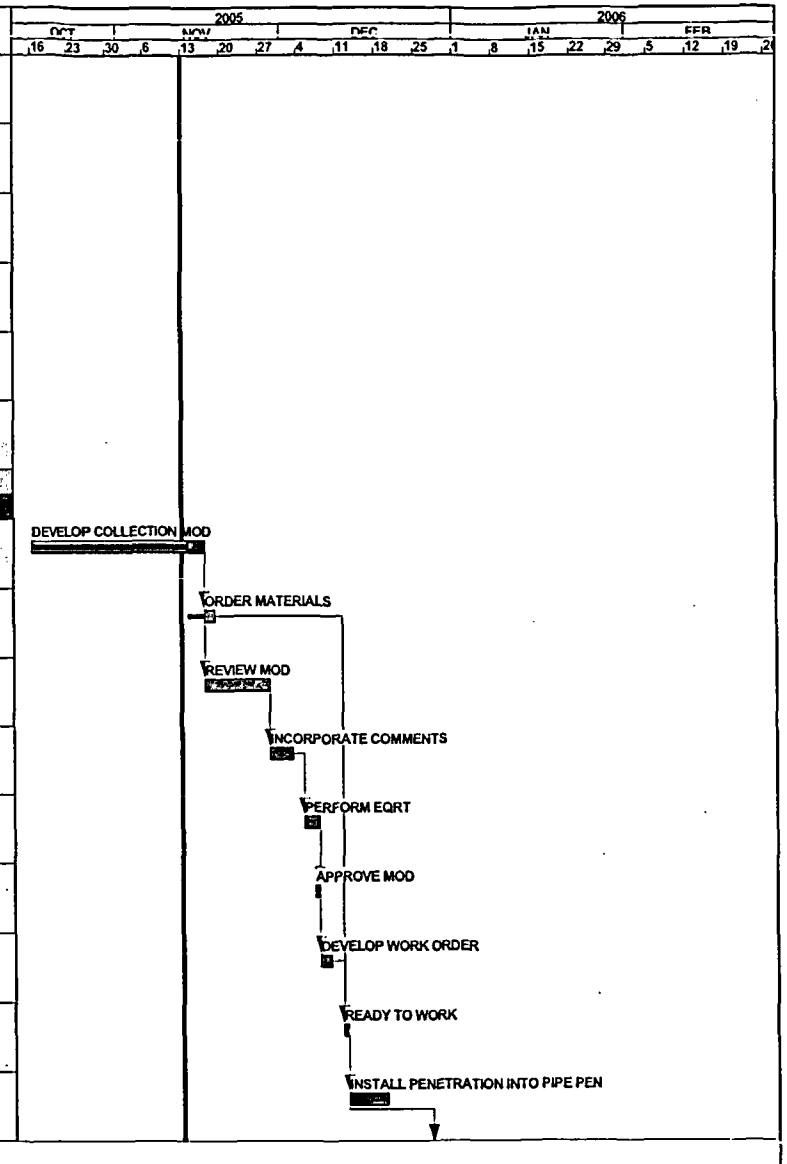

ITEM	PROJ	Cal ID	IPEC	WONO	ID	Activity Description	Early start	Early finish	Orig Dur	% Comp	PMGR	RESP INDIV	Predecessors	Successors
4773	SFPLXXXX1C	3	SFPL	FPLER01	39	RETURN TO SERVICE		27DEC05*	0	0	RUTKOSKE,	NUTA, DRAG	SFPLER01ED	SFPLER01FA*
4771	SFPLXXXX1C	3	SFPL	FPLER01	EE	PRE FAB COLLECTION DEVICE	28DEC05*	04JAN06	5	0	RUTKOSKE,	SANTIS, HA	SFPLER01EC	SFPLER01ED*
4774	SFPLXXXX1C	3	SFPL	FPLER01	FA	START CLOSEOUT PROCESS	28DEC05	04JAN06	5	0	RUTKOSKE,	NUTA, DRAG	SFPLER0139*	SFPLER01FZ*
4772	SFPLXXXX1C	3	SFPL	FPLER01	ED	INSTALL COLLECTION MOD	05JAN06*	11JAN06	5	0	RUTKOSKE,	SANTIS, HA	SFPLER01EE*	SFPLER0139, SFPLER01E&*
4776	SFPLXXXX1C	3	SFPL	FPLER01	FZ	DCP CLOSEOUT	05JAN06	01FEB06	20	0	RUTKOSKE,	NUTA, DRAG	SFPLER01FA*	
4772	SFPLXXXX1C	3	SFPL	FPLER01	E&	DEVELOP PROCEDURE FOR COLLECTION	12JAN06	13JAN06	2	0	RUTKOSKE,	PETERS	SFPLER01ED*	
Spent Fuel Pool Leak/Liner Inspection														
Rutkoske/Michek														
4772	SFPLXXXX1D	3	SFPL	FPLER01	GE	PLAN FOR DIVING EVOLUTION	24OCT05A	06DEC05	15	0	RUTKOSKE,	DESCHAMPS,		
4772	SFPLXXXX1D	3	SFPL	FPLER01	GF	RECOMMEND CAMERA ETC FOR SFP FLOOR/WALL	24OCT05A	09DEC05	15	0	RUTKOSKE,	DEEDS, PAU		SFPLER01G3*
4771	SFPLXXXX1D	3	SFPL	FPLER01	G4	PREPARE 50.59	14NOV05	29NOV05	10	0	RUTKOSKE,	DRAKE, RIC	SFPLER01GP	SFPLER01GS*
4771	SFPLXXXX1D	3	SFPL	FPLER01	GO	ENGINEERING EVALUATION FOR LINER COATING	14NOV05*	02DEC05	13	0	RUTKOSKE,	BHALLA, GO	SFPLER01GN	SFPLER01GP, SFPLER01GW
4771	SFPLXXXX1D	3	SFPL	FPLER01	GS	DEVELOP WO FOR LINER REPAIR	30NOV05	20DEC05	15	0	RUTKOSKE,	DRAKE, RIC	SFPLER01G4*, SFPLER01GW	SFPLER01GV*
4772	SFPLXXXX1D	3	SFPL	FPLER01	G3	PLAN - CAMERA INSPECT FLOOR & INACCESSIBLE WALLS	12DEC05	23DEC05	10	0	RUTKOSKE,	DEEDS, PAU	SFPLER01GF*	
4771	SFPLXXXX1D	3	SFPL	FPLER01	GV	MAKE LINER REPAIR	21DEC05	21DEC05	1	0	RUTKOSKE,	DRAKE, RIC	SFPLER01GP, SFPLER01GS*, SFPLER01GT, SFPLER01GU	SFPLER01GX*
4771	SFPLXXXX1D	3	SFPL	FPLER01	GX	REVIEW INDICATIONS OF POOL LEAK	21DEC05	28DEC05	5	0	RUTKOSKE,	DEEDS, PAU	SFPLER01GV*	

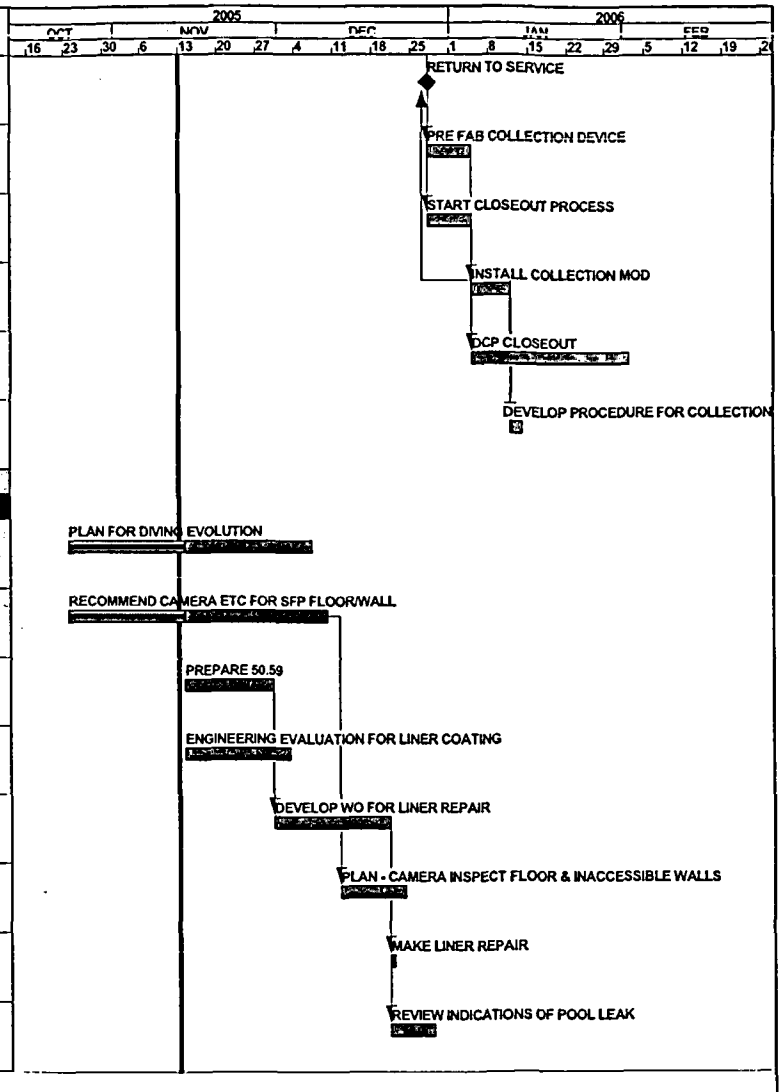
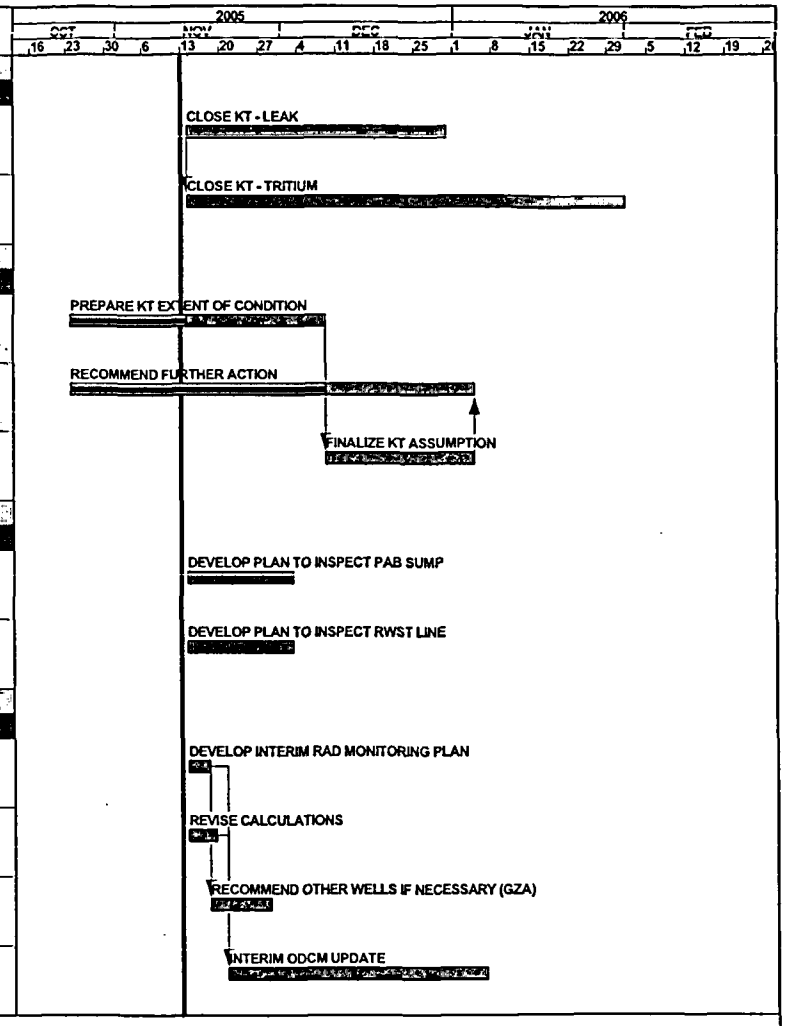
ITEM	PROJ	Cal ID	IPEC	WONO	ID	Activity Description	Early start	Early finish	Orig Dur	% Comp	PMGR	RESP INDIV	Predecessors	Successors
Spent Fuel Pool Leak/KT Analysis Leak														
Rutkoske, Michael														
4776	SFPLXXXX1E	3	SFPL	FPLER01	IB	CLOSE KT - LEAK	14NOV05	30DEC05	32	0	RUTKOSKE,	BODE, PAUL	SFPLER01ID	SFPLER01IC, SFPLER01IE*
4776	SFPLXXXX1E	3	SFPL	FPLER01	IE	CLOSE KT - TRITIUM	14NOV05	31JAN06	53	0	RUTKOSKE,	BODE, PAUL	SFPLER01IB*	
Spent Fuel Pool Leak/KT Site Monitoring														
Rutkoske, Michael														
4776	SFPLXXXX1F	3	SFPL	FPLER01	JA	PREPARE KT EXTENT OF CONDITION	24OCT05A	08DEC05	3	0	RUTKOSKE,	BODE, PAUL		SFPLER01JB*
4776	SFPLXXXX1F	3	SFPL	FPLER01	JC	RECOMMEND FURTHER ACTION	24OCT05A	04JAN06	3	0	RUTKOSKE,	BODE, PAUL	SFPLER01JB*	
4776	SFPLXXXX1F	3	SFPL	FPLER01	JB	FINALIZE KT ASSUMPTION	09DEC05	04JAN06	3	0	RUTKOSKE,	BODE, PAUL	SFPLER01JA*	SFPLER01JC*
Spent Fuel Pool Leak/Extent of Condition														
Rutkoske, Michael														
4776	SFPLXXXX1G	3	SFPL	FPLER01	KC	DEVELOP PLAN TO INSPECT PAB SUMP	14NOV05*	02DEC05	13	0	RUTKOSKE,	DEEDS, PAU		
4776	SFPLXXXX1G	3	SFPL	FPLER01	KD	DEVELOP PLAN TO INSPECT RWST LINE	14NOV05*	02DEC05	13	0	RUTKOSKE,	DEEDS, PAU		
Spent Fuel Pool Leak/Radiological Monitoring														
Rutkoske, Michael														
4776	SFPLXXXX1H	3	SFPL	FPLER01	MA	DEVELOP INTERIM RAD MONITORING PLAN	14NOV05*	17NOV05	4*	0	RUTKOSKE,	AXELSON		SFPLER01MG, SFPLER01MH*
4776	SFPLXXXX1H	3	SFPL	FPLER01	MB	REVISE CALCULATIONS	14NOV05	18NOV05	5	0	RUTKOSKE,	AXELSON	SFPLER01MC*, SFPLER01MD*	SFPLER01MG*
4776	SFPLXXXX1H	3	SFPL	FPLER01	MH	RECOMMEND OTHER WELLS IF NECESSARY (GZA)	18NOV05	28NOV05	5	0	RUTKOSKE,	AXELSON	SFPLER01MA*	
4776	SFPLXXXX1H	3	SFPL	FPLER01	MG	INTERIM ODCM UPDATE	21NOV05	06JAN06	31	0	RUTKOSKE,	AXELSON	SFPLER01MA, SFPLER01MB*
