Radiological Decontamination and Decommissioning
(D&D)

Final Status Survey Report

APRIL 2000

NMRC Rockville Annex
12300 Washington Avenue
Rockville, Maryland 20852

Prepared by
Radiation Safety Office
Naval Medical Research Center
Bethesda, Maryland

TABLE OF CONTENTS

I. Dedication and Acknowledgements. 5

II. Overview. 7

III. Abbreviations and Definitions. 9
- A. Abbreviations and Acronyms. 9
- B. Key Terms and Definitions. 10

IV. Executive Summary. 15
- A. Purpose. 15
- B. Plan. 15
- C. Conclusions 16

V. Reason for Decommissioning. 18

VI. Guidance for Decommissioning Efforts. 19

VII. Conceptual Model and Site Information. 20
- A. Potential Radioactive Contaminants. 20
- B. Potential Contaminated Areas. 21
- C. Impacted Areas – Known and Potential. 22
- D. Potential Contaminated Media. 26
- E. Conceptual Model for Decommissioning. 26

VIII. Decommissioning Activities. 28
- A. Objective 28
- B. Cost Estimates for Decommissioning Activities. 28
- C. Release Limits and Dose Pathway Modeling. . . 29
- D. Criteria for License Termination. 29
- E. Derived Concentration Guideline Levels (DCGLs). 30
- F. Pre-Survey Safety Actions. 33
- G. Background/Baseline Levels. 33
- H. Survey Units. 33
- I. Quality Assurance and Quality Control. . . . 34
- J. Field Measurement Methods and Instrumentation. 36
  - 1. Field Measurements. 36
  - 2. Instruments, Equipment, Measurements and Sampling Techniques 38

K. Sampling and Preparation for Laboratory Measurements. 39
1. Field Sample Preparation and Preservation. 39
2. Other Measurements and Sampling Locations. 40

IX. Decontamination Procedures. 41

X. Final Status Survey. 42
A. Overview. 42
B. Survey Preparations. 42
C. Survey Design. 44
D. Conducting Surveys. 48
E. Data Conversion. 49
F. Evaluating and Documenting Survey Results. . 50

XI. References. 52

XII. Appendices. 54

A. Conceptual Model and Floor Diagrams. 55
A-1. Conceptual Model. 56
A-2. Floor Diagram, First Floor, NMRC Rockville Annex. 57
A-3. Floor Diagram, Second Floor, NMRC Rockville Annex. 58

B. Documents and Photographs. 59
B-1. Documents. 60
B-2. Photographs. 61

C. Standard Operating Procedures and Quality Assurance Program. 62
C-1. Radiological D&D Action Plan Checklist. 63
C-2. Checklist for Impacted Class 3 Areas or Survey Units. 66
C-3. Checklist for Non-impacted Areas or Survey Units. 68
C-4. Sample Collection Procedures. 70
C-5. Sample Control. 72
C-6. Data Analysis Procedures. 73

C-7. Equipment and Instrument Procedures. . 75
C-8. Source-Standards, Background-Standards, and Reference-Background Measurements. 77

D. Quality Assurance Information and Data. . . .78
D-1. Training Information and Certificates .79
D-2. Service and Calibration Certificates for Instruments, Equipment and Check Sources 83
D-3. Instrument and Equipment Quality Control Data 84
D-4. Quality Assurance Checklist. 114

E. Survey Unit Release Reports (Narratives, Data, Floor Plans, and Grid Maps). 116
E-1. Lists of Survey Units, Data Tables, and Figures. 117
E-2. Rockville Annex Second Floor, Non-impacted Areas. 124
E-3. Rockville Annex First Floor, Non-impacted Areas. 128
E-4. Rockville Annex Second Floor, Impacted Class 3 Areas. 133
E-5. Rockville Annex First Floor, Impacted Class 3 Areas and other Non-impacted Areas. 195

I. DEDICATION AND ACKNOWLEDGEMENTS

DEDICATION

This work is dedicated in memory of my father, Mr. John S. Gaiter, Sr. (May 1, 1932 - August 19, 1999) and my youngest sister, Bergenia R. Gaiter (June 13, 1967 - October 11, 1999).

ACKNOWLEDGMENTS

Without the noteworthy contributions, support and assistance of numerous persons, this work would not have been possible.

NMRC Radiological Decontamination and Decommissioning (D&D) Team

- Schleurious L. Gaiter; LCDR, MSC, USN: Radiation Safety Officer, Decommissioning Officer, and Quality Control Officer
- Saifeddin Ahmad; Assistant Radiation Safety Officer, Team Leader, Lead Health Physics Technician, Chief of Office and Laboratory Operations
- Willie Deadwyler; Team Leader, Health Physics Technician, Chief of Field Operations
- Carolyn Hall; Technical Writer, Chief Editor, Publications Officer
- Glen Garth; Health Physics Assistant, Data Processing Specialist
- Rodney McGhee; Health Physics Assistant, Data Processing Specialist
- HM2 Michelle McGhee; USN: Safety Assistant

Command and Navy Personnel

- Dr. Charles Odeyale; Ph.D., NMRC Environmental and Chemical Hygiene Officer
- HM1 James Bruce; USN, Hazardous Materials Technician
- Daniel Fischer; NMRC Safety Assistant
- Stephen Krauz; LT, MSC, USN, Supply Officer
- Veronica Serrano; NMRC Purchase and Contract Specialist
- Raymond Albright; NMRC Purchase and Contract Specialist
- Donald Chandler; NMRC BRAC Officer
- Sandra Hawkins; NMRC Comptroller
- Regina Hunt; NMRC Historian
- Michael Bush; LT, MSC, USN, Navy Environmental Health Center
- Paul Tveten, Navy Environmental Health Center
- Sandy J. Wolff, LCDR, MSC, USN, Navy Environmental Health Center

II. OVERVIEW

This document, the Naval Medical Research Center (NMRC) Rockville Annex Radiological Decontamination and Decommissioning (D&D) Final Status Survey Report, was prepared in support of NMRC's decommissioning efforts. This report includes all survey results, reference background readings, check-source evaluations, calculations, procedures, problems/deviations from plans, recommendations for survey-site status, and other pertinent information.

This report describes the actions and levels of effort that NMRC undertook to demonstrate to regulatory authorities that the vacated NMRC Rockville Annex site meets the release criteria for unrestricted future use. To achieve this objective, guidance provided in the Multi-Agency Survey and Site Investigation Manual (MARSSIM, ref 11.1) and other regulatory documents were followed and parameters chosen to meet or exceed the release criteria.

The NMRC Historical Site Assessment (HSA, ref 11.2) served as the primary document for information regarding potential contaminants, potential contaminated areas, and potential contaminated media.

Since 1986, the NMRC leased the privately held industrial property from a commercial realty management group. The NMRC Rockville Annex is located at 12300 Washington Avenue, Rockville, Maryland 20852 and is housed in a 10,717-square foot, two-story masonry building. The first floor contained administrative offices and research laboratories. The second story comprised research laboratories, offices and common areas. The Annex housed laboratories involved in enteric and malarial research. Medical studies and biomedical research were conducted which involved the use of chemicals and other hazardous materials, biological materials, animals and animal products, and radiological materials. All the surrounding properties are located within Rockville city limits and are predominantly for industrial and commercial uses (ref 11.3, ESA 1997).

NMRC's history of military medical research during 1986 to 1999 at the Annex site included the use of sealed and unsealed radioactive materials. The sealed-source use involved the use of a single, 300-Curie, Cesium-137 gamma irradiator. Required, semi-annual leak test results for the gamma irradiator provided assurance of no residual Cesium-137 contamination at the Annex. The use of unsealed radioactive materials in laboratories, rooms, and areas dictated that some level of decommissioning was required for each area of radioactive material use to ensure and document compliance with the regulatory release criteria for unrestricted use.

The radioactive contaminants of concern were Hydrogen-3, Carbon-14, Phosphorus-32, Sulfur-35, and Chromium-51.

The examination for potential radioactive contaminants included surveys, direct measurements, sampling and analysis, and scanning with appropriate instruments and equipment. The examinations included:

(1) all accessible floor space,

(2) the lower half of all walls extending up approximately two meters from the floor, and

(3) other selected locations.

The survey units were classified as either Impacted Class 3 or Non-impacted. There were no survey sites classified as Impacted Class 1 or Class 2, which are the two remaining classifications requiring the most extensive decommissioning effort. Selected Annex common areas, restrooms, and non-impacted areas were evaluated for potential radioactive contamination. After equipment, materials and wastes were removed from radioactive-materials-use areas, residual contamination was confined to small areas within a small percentage of the survey units.

The 4-month decommissioning period began in January 2000 and was concluded in April 2000. The cost of performing the necessary decommissioning efforts included instrument and equipment costs, materials, supplies and contracted labor.

III. Abbreviations and Definitions

A. ACRONYMS AND ABBREVIATIONS

µCi	Micro-Curie
µR/hr	Micro-Roentgens per hour (exposure rate)
Annex	NMRC Rockville Annex Laboratories, Washington Avenue, Rockville, MD
BRAC	Base Realignment and Closure
BUMED	Bureau of Medicine and Surgery
CFR	Code of Federal Regulations
cpm	Counts per minute
D&D	decontamination and decommissioning
DOD	Department of Defense
DOT	Department of Transportation
dpm	Disintegrations per minute
Gy	Gray, SI unit of absorbed dose, 1 Gy = 100 rads
Irradiator	Sealed-source, Cesium-137 gamma irradiator
MDA	Minimum detectable activity
NEHC	Navy Environmental Health Center
NMRC	Naval Medical Research Center, formerly NMRI
NMRI	Naval Medical Research Institute
NNMC	National Naval Medical Center
NRC	U. S. Nuclear Regulatory Commission
NRMP	NMRC's Navy Radioactive Materials Permit
NUREG	Nuclear Regulatory Guide
R, R/hr	Roentgen (exposure), Roentgens per hour
Rad, Rad/hr	Rad (dose), Rads per hour (dose rate)
RAM	Radioactive materials
Rem, Rem/hr	Rem (dose equivalent), Rem per hour
SOP	Standard operating procedure
Sv	Sievert, SI unit of dose equivalent, 1 Sv = 100 rems
US	United States
USN	United States Navy
WSSC	Washington Suburban Sanitary Commission

B. KEY TERMS AND DEFINITIONS (reference 11.1, MARSSIM)

α, Alpha	The specified maximum probability of Type I error; i.e.; the maximum probability of rejecting the null hypothesis when it is true. Alpha is referred to as the size of the test. Alpha reflects the amount of evidence the decision maker would like to see before abandoning the null hypothesis.
Area	A term referring to any portion of a site, up to and including the entire site.
Background radiation	Radiation from cosmic sources, naturally occurring radioactive material, radon, and global fallout as it exists in the environment from testing of nuclear explosive devices or from nuclear accidents. Background radiation does not include radiation from source, byproduct, or special nuclear materials regulated by the Federal or State agency.
Becquerel (Bq)	The unit of radioactivity equivalent to one nuclear transformation per second.
β, Beta	The probability of a Type II error, i.e., the probability of accepting the null hypothesis when it is false. The compliment of beta (1-β) is referred to as the power of test.
Beta emitter	A radioactive material emitting beta particles. Beta particles are electrons emitted from the nucleus during radioactive decay.
Byproduct material	Licensed or radioactive material regulated by the NRC.
Class 1 areas	Impacted areas with the highest potential for contamination or insufficient evidence to support reclassification as Class 2 or 3.
Class 2 areas	Impacted areas with low potential for delivering a dose above the release criterion and little or no potential for small areas of elevated activity.

Class 3 areas	Impacted areas with little or no potential for delivering a dose above the release criterion and little or no potential for small areas of elevated activity.
Classification	The act or result of separating areas or survey units into one of the three designated classes: Class 1 area, Class 2 area, or Class 3 area.
Cleanup standard	A numerical limit set by a regulatory agency as a requirement for releasing a site after cleanup.
Contamination	The presence of residual radioactivity in excess of levels which are acceptable for release of a site or facility for unrestricted use.
Curie	A unit of radioactivity equal to 37 billion becquerels.
Derived Concentration Guideline Level (DCGL)	A derived, radionuclide-specific activity concentration within a survey unit corresponding to the release criterion. The DCGL is based on the spatial (uniform) distribution of the contaminant and hence is derived differently for the non-parametric statistical test ($DCGL_w$) and the elevated measurement comparison ($DCGL_{EMC}$). DCGLs are derived from activity/dose relationships through various exposure pathway scenarios.
Decommission	To remove (as a facility) safely from service and reduce residual radioactivity to a level that permits release of the property for unrestricted use and termination of the Nuclear Regulatory Commission license or Navy radioactive material permit.
Decommissioning	The process of removing a facility or site from operation, followed by decontamination, and license termination (or termination of authorization for operation) if appropriate.
Decontamination	The removal of radiological contaminants from persons, objects, or areas to within regulatory levels.

Direct measurement	Radioactivity measurement obtained by placing the detector near the surface or media being surveyed. An indication of the resulting radioactivity level is read out directly.
Final status survey	Measurements and sampling to describe the radiological conditions of a site, following completion of decontamination activities (if warranted) in preparation for release.
Gamma (γ) radiation	Penetrating high-energy, short-wavelength electromagnetic radiation (similar to X-rays) emitted during radioactive decay. Gamma rays are very penetrating and require dense materials (such as lead or steel) for shielding.
Impacted areas	Any area that is not classified as non-impacted. Areas with a possibility of containing residual radioactivity in excess of natural background or fallout levels.
Investigation level	A derived media-specific, radionuclide-specific concentration or activity level of radioactivity that is based on the regulatory release criteria and triggers a response that further investigation or action is necessary if exceeded.
MARSSIM	Multi-Agency Radiation Survey and Site Investigation Manual (DOE,DOD, EPA, NRC); provides for conducting decommissioning activities to satisfy regulatory release criteria.
Non-impacted areas	Areas where there is no reasonable possibility (extremely low probability) of residual contamination.
Non-parametric test	A test based on relatively few assumptions about the underlying probability distributions of the measurements. As a consequence, non-parametric tests are generally valid for a fairly broad class of distributions. The Wilcoxon Rank Sum test and the Sign test are examples of non-parametric tests.

Outlier	Measurements that are unusually large or small relative to the rest and therefore are suspect of misrepresenting the population from which they were collected.
Radioactive material (RAM)	Solid, liquid or gaseous material that contains radionuclides regulated by the NRC.
Radioactive waste	Solid or liquid trash or excess material that contains radionuclides regulated by the NRC.
Release criterion	A regulatory limit expressed in terms of dose or risk; compliance demonstration is simply a decision as to whether or not a survey unit meets the release criterion.
Residual radioactivity	Radioactivity in structures, materials, soil, groundwater, and other media at a site resulting from activities under the cognizant organization's control.
Scanning	An evaluation technique performed by moving a detection device over a surface at a specified speed and distance above the surface to detect radiation.
Sign test	A non-parametric statistical test used to demonstrate compliance with the release criterion when the radionuclide of interest is not present in background and the distribution of the data is not symmetric.
Site	Any installation, facility, or discrete, physically separate parcel of land, or any building or structure or portion thereof, that is being considered for survey and investigation.
Survey	A systematic evaluation and documentation of radiological measurements with a correctly calibrated instrument or instruments that meet the sensitivity required by the objective of the evaluation.

Survey unit	A geographical area consisting of a room, hallway, structures or land areas of specified size and shape for which a separate decision will be made whether the unit attains the cleanup standard; are established to facilitate the survey process and the statistical analysis of the survey data.
Wilcoxon test	A non-parametric statistical test used to demonstrate compliance with the release criterion when the radionuclide of interest is present in background and the distribution of the data is not symmetric.

IV. EXECUTIVE SUMMARY

A. PURPOSE

A final status decommissioning survey was conducted to determine the presence and extent of any radiological health hazards in the building used by NMRC at the National Naval Medical Center (NNMC) Bethesda campus and at the Rockville Annex. All necessary actions were taken to verify that any residual radioactivity in the vacated NMRC buildings was in compliance with regulatory guidelines for the decontamination of facilities prior to release for unrestricted use.

B. PLAN

- Develop and implement an approved decontamination and decommissioning plan.
- Stop all work involving the use of radioactive materials.
- Dispose, remove or transfer all licensed, radioactive materials and equipment to authorized recipients.
- Minimize hazardous and low-level radioactive waste generated.
- Decontaminate known areas of contamination to background levels.
- Meet regulatory radiological, environmental, and safety regulations.
- Control costs and complete closure within the allocated timeframe.
- Prepare final status survey reports.

A radiological survey plan was developed to survey over 10,000 square feet with portable instrumentation and to take and analyze over 2,000 swipe samples and more than 150 direct readings throughout the Rockville Annex. The work history and probability of residual radioactive material were used to identify areas selected for surveying and sampling. The closure operations used basic engineering principles and common industrial practices.

Those few areas where low-level radioactivity in excess of permissible limits was detected were remediated and released for unrestricted use. The results of final status surveys for all but one survey area revealed no detectable radiation level greater than background.

A double sink in room 115 was used to dispose of radioactive liquid wastes in accordance with 10 CFR 20. Because residual radioactivity (tritium) was detected in the sink and drain, the drain assembly and pipes and were removed and disposed as solid radioactive (tritium) waste. The drainpipe was cut nearly flush with the wall beneath the sink. The interior and exterior surfaces of the drainpipe stub were decontaminated on numerous occasions and radioactivity levels were greatly reduced.

After completing final status survey efforts for this drain stub, it was determined that no further decontamination efforts were necessary and that the residual-radioactivity level was approximately 20 times lower than the NRC screening values for residual contamination.

C. CONCLUSIONS

The plan described in item B above has been fully implemented, completed, and documented.

The decontamination and decommissioning efforts involved the satisfactory performance of final status

surveys for 100% (29 of 29) Impacted Class 3 units and 100% (38 of 38) Non-impacted units.

Operations involving the use of licensed, radioactive materials at the NMRC Rockville Annex have had no adverse effect on the leased commercial building. All radioactive materials as a result of NMRC operations have been removed from the building. Regulatory agency criteria for release of the building for unrestricted use have been fulfilled.

V. REASON FOR DECOMMISSIONING

Base Realignment and Closure (BRAC) legislation passed and signed into law in 1995 mandated that the Naval Medical Research Center (NMRC) relocate some of its programs and research efforts and cease operations at the NNMC campus in Bethesda, Maryland and at the NMRC Rockville Annex in 1999.

NMRC, the Navy's largest medical research facility, opened its doors in Bethesda on October 27, 1942 to conduct research, development, tests, and evaluations to enhance the health, safety, and readiness of Navy and Marine Corps personnel in the effective performance of peacetime and contingency missions. NMRC had specific environmental obligations to fulfill before terminating the lease of the NMRC Rockville Annex building. These obligations involved the completion of biological, chemical, environmental and radiological decommissioning efforts.

VI. GUIDANCE FOR DECOMMISSIONING EFFORTS

Regulatory guidance for conducting this radiological decommissioning activity was obtained from various sources. The Environmental Protection Agency (EPA), the Nuclear Regulatory Commission (NRC), and the Department of Energy (DOE) are responsible for the release of sites following cleanup. These responsibilities apply to facilities under the control of Federal agencies, such as the DOE and the Department of Defense (DOD), and to sites licensed by the NRC and its Agreement States. Some states have responsibilities for similar sites under their control.

The NRC requires the radiological decommissioning of sites, buildings and outdoor areas where licensed activities have ceased radiological operations, even while licensed activities continue to be conducted at other site locations. Use of licensed materials at the leased building in Rockville, Maryland ceased in October 1999. This site required decommissioning and return to the owner for unrestricted use.

The detailed guidance provided in the Multi-Agency Survey and Site Investigation Manual (MARSSIM, ref 11.1) was used for planning, implementing, and evaluating environmental and facility radiological surveys that NMRC conducted to demonstrate compliance with the current dose-based regulation (10CFR20.1402, ref 11.4). Other regulatory documents (referenced in Section XI.) were used to provide estimates for derived concentration guideline values, dose modeling, and other necessary information and techniques.

The MARSSIM provides a nationally consistent consensus approach to conducting radiation surveys and investigations at potentially contaminated sites. The decommissioning that follows remediation will normally require a demonstration to the responsible federal or state agency that the cleanup effort was successful and that the release criterion was met. In MARSSIM, this demonstration is given the name "final status survey." The MARSSIM assists site personnel and others in performing or assessing such a demonstration.

Unique site-specific cases did not arise that required a modified approach beyond what is presently described in MARSSIM.

VII. CONCEPTUAL MODEL AND SITE INFORMATION

A. POTENTIAL RADIOACTIVE CONTAMINANTS

The potential radioactive contaminants included Hydrogen-3 (tritium), Carbon-14, Phosphorus-32, Sulfur-35, and Chromium-51. No gaseous or solid radioactive materials were used. Radioactive materials were obtained and used as liquid solutions. There was no likely potential for airborne release of radioactive materials. Therefore, ceiling surfaces were not evaluated or surveyed for residual contamination. Low-level radioactive liquid and solid wastes were generated and properly disposed. Liquid aqueous wastes were collected by the user and turned into the NMRC Radiation Safety Office. The NMRC Radiation Safety Office maintained liquid-waste disposal logs and disposed the aqueous waste into the sewer via a designated laboratory sink in accordance with regulatory limits.

NMRC Annex researchers and technicians who used radioactive materials were required to maintain separate waste containers for each isotope used. Further segregation occurred for liquids, solids, carcasses, scintillation vials, and sharps. All radioactive material (RAM) wastes were turned in to the Radiation Safety Office for tracking, storage and subsequent disposal and/or transfer. Logbooks were maintained. Burial of waste was prohibited. Solid waste disposal via decay-in-storage occurred for shorter half-life RAM (< 65 days). Long half-life RAM wastes were transferred to the National Naval Medical Center (NNMC) at Bethesda, Maryland, for transfer to a commercial contractor.

Solid wastes were packaged by the researchers and technicians and turned in to the Radiation Safety Office for storage and subsequent disposal. The review of NMRC records included summaries of NMRC's annual receipts (inventories) of radioactive materials, annual solid radioactive waste disposal

logbook entries, and annual sanitary sewer disposal of liquid radioactive materials logbook entries.

B. POTENTIAL CONTAMINATED AREAS

All available NMRC daily, weekly, monthly, and quarterly wipe test and survey monitoring results (1986-1999) were reviewed for evidence of residual contamination in the NMRC Annex building. Incident and spills records were also reviewed. When contamination was detected during the course of decommissioning the NMRC Annex building, characterization surveys, remediation actions, and remedial action surveys were completed and documented in the final survey summaries.

In October 1993, a spill/contamination incident occurred at the Rockville Annex involving the unauthorized use and spill of micro-curie quantities of Phosphorus-32 (P-32), inadequate post-use monitoring, and non-reporting of broken glass tubes containing P-32 during the use of a laboratory centrifuge unit. Contamination was spread to various locations at the site; decontamination events occurred to clean up as much as possible and the residual radioactivity was covered until radiation decay occurred. No other spills occurred since then. No residual radioactivity remains at the Rockville site in 2000 from that 1993 spill.

Table 1 provides a list of all NMRC Annex survey sites. These sites included offices, lunchrooms, lavatories, storage areas, common areas, laboratories, equipment rooms, and radiological waste storage rooms.

C. IMPACTED AREAS - KNOWN AND POTENTIAL

Impacted areas have some potential for residual contamination. Impacted areas are further divided into three classifications. **Table 1** provides a list of Impacted Class 3 Areas and Non-impacted Areas. No NMRC Annex areas were classified as Impacted Class 1 or 2.

1. CLASS 1 AREAS

Class 1 areas are impacted areas that, prior to remediation, are expected to have concentrations of residual radioactivity that exceed the DCGL (DCGL is defined in MARSSIM as derived concentration guideline levels or action limits). None of the Annex survey sites were classified as Class 1.

2. CLASS 2 AREAS

Class 2 areas are impacted areas that, prior to remediation, are not likely to have concentrations of residual activity that exceed the DCGL. None of the Annex survey sites were classified as Class 2.

3. CLASS 3 AREAS

Class 3 areas are impacted areas that have a low probability of containing residual radioactivity. **Table 1** lists NMRC Annex Impacted Class 3 Areas. Of the approximately 67 NMRC Annex survey units, 29 were classified as Impacted Class 3. The Impacted Class 3 sites consisted of rooms where radioactive materials were used or stored.

4. NON-IMPACTED AREAS

Non-impacted areas have no reasonable potential for residual contamination. **Table 1** lists NMRC Annex Non-impacted Areas. These non-impacted areas were offices, common areas, and other non-radioactive-material-use areas.

Table 1. NMRC Rockville Annex Impacted Class 3 Areas and Non-impacted Areas

BUILDING	ROOM OR AREA	DESCRIPTION	ISOTOPES OF CONCERN	D&D CLASSIFICATION
Annex	100	Office		Non-impacted
Annex	102	Office		Non-impacted
Annex	103	Office		Non-impacted
Annex	104	Office		Non-impacted
Annex	105	Machine room		Non-impacted
Annex	106	Lavatory		Non-impacted
Annex	107	Lavatory		Non-impacted
Annex	108	Office		Non-impacted
Annex	109	Office/Duty Room		Non-impacted
Annex	110	Laboratory	H3,C14,P32, S35, Cr51	Impacted, Class 3
Annex	110A	Office	H3,C14,P32, S35, Cr51	Impacted, Class 3
Annex	110B	Office	H3,C14,P32, S35, Cr51	Impacted, Class 3
Annex	111	Equipment Storage	H3,C14,P32, S35, Cr51	Impacted, Class 3
Annex	112	Sterilizer Room/Lab	H3,C14,P32, S35, Cr51	Impacted, Class 3
Annex	113	Laboratory	H3,C14,P32, S35, Cr51	Impacted, Class 3
Annex	114	Laboratory	H3,C14,P32, S35, Cr51	Impacted, Class 3
Annex	115	Laboratory	H3,C14,P32, S35, Cr51	Impacted, Class 3
Annex	116	Dark Room		Non-impacted
Annex	117	Storage Room		Non-impacted
Annex	Halls	First floor halls		Non-impacted
Annex	Halls	Second floor halls		Non-impacted
Annex	LDR	Loading Dock Room	H3,C14,P32, S35, Cr51	Impacted, Class 3
Annex	LDS	Loading Dock Storage	H3,C14,P32, S35, Cr51	Impacted, Class 3
Annex	RWL	RAM Waste Locker	H3,C14,P32, S35, Cr51	Impacted, Class 3
Annex	Stair A	Stairway A (two floors)		Non-impacted
Annex	Stair B	Stairway B (two floors)		Non-impacted

Table 1 (continued). NMRC Rockville Annex Impacted Class 3 Areas and Non-impacted Areas

BUILDING	ROOM OR AREA	DESCRIPTION	ISOTOPES OF CONCERN	D&D CLASSIFICATION
Annex	118	Insect Room		Non-impacted
Annex	118A	Insect/Animal Room		Non-impacted
Annex	118B	Insect Room		Non-impacted
Annex	118C	Insect Room		Non-impacted
Annex	123	Laboratory	H3,C14,P32, S35, Cr51	Impacted, Class 3
Annex	124	Cold Room	H3,C14,P32, S35, Cr51	Impacted, Class 3
Annex	125	Insect Room	H3,C14,P32, S35, Cr51	Impacted, Class 3
Annex	126	Laboratory	H3,C14,P32, S35, Cr51	Impacted, Class 3
Annex	127	Laboratory	H3,C14,P32, S35, Cr51	Impacted, Class 3
Annex	128	Laboratory	H3,C14,P32, S35, Cr51	Impacted, Class 3
Annex	201	Laboratory	H3,C14,P32, S35, Cr51	Impacted, Class 3
Annex	202	Office		Non-impacted
Annex	203	Office		Non-impacted
Annex	204	Office		Non-impacted
Annex	205	Office		Non-impacted
Annex	206	Office		Non-impacted
Annex	207	Office		Non-impacted
Annex	208	Conference Room		Non-impacted
Annex	209	Office		Non-impacted
Annex	210	Office		Non-impacted
Annex	211	Office		Non-impacted
Annex	212	Lunchroom		Non-impacted
Annex	213	Freezer/Storage	H3,C14,P32, S35, Cr51	Impacted, Class 3
Annex	213A	Storage	H3,C14,P32, S35, Cr51	Impacted, Class 3
Annex	213B	Gamma Counter	H3,C14,P32, S35, Cr51	Impacted, Class 3

Table 1 (continued). NMRC Rockville Annex Impacted Class 3 Areas and Non-impacted Areas

BUILDING	ROOM OR AREA	DESCRIPTION	ISOTOPES OF CONCERN	D&D CLASSIFICATION
Annex	214A	Laboratory		Non-impacted
Annex	214B	Laboratory		Non-impacted
Annex	214C	Laboratory		Non-impacted
Annex	215	Laboratory		Non-impacted
Annex	215A	Animal Room		Non-impacted
Annex	216	Animal Room		Non-impacted
Annex	217	Laboratory		Non-impacted
Annex	218	Storage	H3,C14,P32, S35, Cr51	Impacted, Class 3
Annex	218A	Cold Room	H3,C14,P32, S35, Cr51	Impacted, Class 3
Annex	218B	Cold Room	H3,C14,P32, S35, Cr51	Impacted, Class 3
Annex	219	Laboratory	H3,C14,P32, S35, Cr51	Impacted, Class 3
Annex	219A	Laboratory	H3,C14,P32, S35, Cr51	Impacted, Class 3
Annex	219B	Laboratory	H3,C14,P32, S35, Cr51	Impacted, Class 3
Annex	220	Laboratory	H3,C14,P32, S35, Cr51	Impacted, Class 3
Annex	221	Tissue Culture	H3,C14,P32, S35, Cr51	Impacted, Class 3
Annex	222	Lavatory		Non-impacted
Annex	223	Lavatory		Non-impacted
Annex	224	Lavatory, female		Non-impacted

D. POTENTIAL CONTAMINATED MEDIA

The potential contaminated media were building surfaces such as walls, floors, workbenches, sinks and shelves.

E. CONCEPTUAL MODEL FOR DECOMMISSIONING

For the convenience of scheduling necessary radiological activities and to maximize the use of available resources, NMRC's Decontamination and Decommissioning (D&D) Plan was divided into four distinct phases. The NMRC Annex was the first phase to undergo radiological D&D efforts. The other three phases included the NMRC diving buildings, main NMRC buildings, and NMRC Building 150. **Table 2** summarizes the NMRC Annex Radiological D&D Conceptual Model Information. To accommodate radiological monitoring and surveys, some of the survey units were sub-divided.

TABLE 2. NMRC Annex Radiological D&D Conceptual Model Information

Number of Survey Units		Floor Area (square feet)	
Non-impacted Areas	Impacted Class 3 Areas	Non-impacted Areas	Impacted Class 3 Areas
40	29	4,115	6,602

The examination for potential radioactive contaminants included direct measurements using a gas proportional counter, sampling and analysis using a liquid scintillation counter, scanning with appropriate instruments and equipment, and data analyses. For Impacted Class 3 areas, the survey unit examinations included:

(1) all accessible floor space,

(2) the lower half of all walls extending up approximately two meters from the floor, and

(3) other selected locations.

After equipment, materials and wastes were removed from radioactive-materials-use areas, it was found that residual contamination was confined to small areas within a small percentage of the survey units.

VIII. DECOMMISSIONING ACTIVITIES

A. OBJECTIVE

The objective of this decommissioning effort was to demonstrate that the sites are suitable for unrestricted release in accordance with the criteria for decommissioning in Subpart E, "Radiological Criteria for License Termination," of 10 CFR Part 20, "Standards of Protection Against Radiation" (ref 11.4).

To achieve this objective, guidance provided in MARSSIM and other regulatory documents was followed. Parameters were chosen to ensure that the following objectives were met:

(1) Identification of the premises and radiological operations;

(2) Demonstration that reasonable efforts were planned to reduce/eliminate residual contamination to as low as practicable;

(3) Documentation of decontamination and decommissioning plan and survey standard operating procedures;

(4) Preparation of the Final Status Survey Report.

B. COST ESTIMATES FOR DECOMMISSIONING ACTIVITIES

Cost estimates were prepared to approximate the cost for various decommissioning activities, including labor, materials, equipment, services, shipping expenses, and other related expenses. Estimates from commercial firms were received regarding some of NMRC's planned decommissioning efforts. In addition, estimates for equipment purchases and disposals were obtained. One vendor quoted a labor rate of $55.00 per hour for technician support working under NMRC supervision. The manpower, equipment and other

essential resources for the radiological D&D operations at the NMRC Annex cost approximately $50,000.

C. RELEASE LIMITS AND DOSE PATHWAY MODELING

The release limits, which include fixed and loose surface contamination, were based upon the NRC guideline screening values. Because NMRC established action limits at a fraction of NRC screening values, dose modeling was not required. Site-specific parameters were not required and were not developed. Dose/pathway modeling was not required because detectable radioactivity was remediated to background levels by decontamination efforts or removal of the contaminated media.

D. CRITERIA FOR LICENSE TERMINATION (NUREG-1549)

The criteria for releasing a site for unrestricted use is described below; the criteria for releasing a site for unrestricted and restricted use are summarized in **Table 3.**

Subpart E, 10 CFR 20, paragraph 20.1402 - Criteria for unrestricted use - a site is considered acceptable for unrestricted use if the residual radioactivity that is distinguishable from background radiation results in a Total Effective Dose Equivalent (TEDE) to an average member of the critical group that does not exceed 25 mrem/yr, including that from groundwater sources of drinking water, and the residual radioactivity has been reduced to levels that are as low as reasonably achievable (ALARA).

Table 3. Summary of 10 CFR Part 20 Subpart E

	Unrestricted Use	Restricted Release	
Dose Criterion	25 mrem TEDE per year peak annual dose to the average member of the critical group	25 mrem TEDE per year peak annual dose to the average member of the critical group while controls are in place	100 mrem or 500 mrem TEDE per year peak annual dose to the average member of the critical group upon failure of controls
Time Frame	1000 years	1000 years	1000 years
Other Requirements	ALARA	ALARA, financial assurance, public participation	ALARA, financial assurance, public participation

E. DERIVED CONCENTRATION GUIDELINE LEVELS (DCGLS)

A concentration of residual radioactivity distinguishable from background that, if distributed uniformly throughout a survey unit, would result in a total effective dose equivalent (TEDE) of 25 millirems per year to an average member of the critical group is called the derived concentration guideline level(DCGL).

Residual levels of radioactive material that correspond to allowable radiation dose standards are calculated (derived) by analysis of various pathways and scenarios (direct radiation, inhalation, ingestion, etc.) through which exposures occur. These derived levels, DCGLs, usually refer to average levels of radiation or radioactivity above appropriate background levels.

For NMRC, as would be the case for the majority of MARSSIM users, the applicable DCGLs were obtained using regulatory agency guidance (screening values)

based on default values. Other users may elect to perform site-specific pathway modeling to determine

DCGLs. In both cases, the DCGL is based on the spatial distribution of the contaminant, and each derivation can produce different values depending on the specific radionuclide distribution and pathway modeling. Because residual activity levels, when found, were reduced to background levels, DCGLs or screening values were compared directly to survey data to demonstrate compliance. It is understood that this simple approach would not have been possible if more than one radionuclide was present (in the contaminated area). Residual radioactivity limits for the radionuclides present at the site were predetermined. NMRC action limits were set at a small fraction of D&D screening values and were set such that the NRC release criteria would be satisfied.

Table 4 provides the NRC D&D screening values for common radionuclides. The screening values provided in **Table 4** will serve as basis for establishing the action limits or DCGLs for NMRC's D&D final status survey data analysis. NMRC's action limit will be set at a small fraction of applicable NRC screening values, 700 dpm, for H-3 and C-14 swipe analyses and be set at a level of two to three times background levels for all other measurements (e.g., beta-gamma scans and fixed-contamination evaluations). Procedures provided in the MARSSIM and 10 CFR 20, Appendix B, would have been used if multiple radionuclides were present. Also provided in **Table 4** are NMRC action limits for other beta emitters and gamma emitters.

Table 4. Acceptable License Termination Screening Values of Common Radionuclides for Building Surface Contamination

Radionuclide	Symbol	Acceptable screening levels[1] for unrestricted release (dpm/100 cm^2)[2]	NMRC Action Limits (dpm/100 cm^2)
Hydrogen-3 (Tritium)	^{3}H	1.2E+08	700
Carbon-14	^{14}C	3.7E+06	700
Sodium-22	^{22}Na	9.5E+03	
Sulfur-35	^{35}S	1.3E+07	700
Chlorine-36	^{36}Cl	5.0E+05	
Manganese-54	^{54}Mn	3.2E+04	
Iron-55	^{55}Fe	4.5E+06	
Cobalt-60	^{60}Co	7.1E+03	700
Nickel-63	^{63}Ni	1.8E+06	
Strontium-90	^{90}Sr	8.7E+03	
Technitium-99	^{99}Tc	1.3E+06	
Iodine-129	^{129}I	3.5E+04	
Cesium-137	^{137}Cs	2.8E+04	
Iridium-192	^{192}Ir	7.4E+04	
Other beta emitters	^{32}P, ^{33}P, ^{45}Ca		700
Other gamma emitters	^{51}Cr, ^{57}Co, ^{125}I		700

[1] Screening levels are based on the assumption that the fraction of removable surface contamination is equal to 0.1. For cases when the fraction of removable contamination is undetermined or higher than 0.1, users may assume, for screening purposes, that 100% of surface contamination is removable, and therefore the screening values should be decreased by a factor of 10. Alternatively, users having site-specific data on the fraction of removable contamination (e.g., within the 10% to 100% range) may calculate the site-specific screening levels using DandD Version 1.

[2] Units are disintegrations per minute per 100 square centimeters (dpm/100 cm^2). One dpm is equivalent to 0.0167 becquerel (Bq). The screening values represent surface concentrations of individual radionuclides that would be deemed in compliance with the 0.25 Sv/year (25 mrem/year) unrestricted dose limit in 10 CFR 20.1402. For radionuclides in a mixture, the "sum of fractions" rule applies; see 10 CFR Part 20, Appendix B, Note 4. Refer to NRC Draft Guidance DG-4006 for further information on application of the values in this table.

F. PRE-SURVEY SAFETY ACTIONS

Pre-survey walk-through inspections were conducted to identify and remedy safety concerns before the designated sites were surveyed.

G. BACKGROUND/BASELINE LEVELS

The primary contaminants of interest (H-3, C-14, P-32, S-35, and Cr-51) did not occur in background at the survey sites, or the background levels were small fractions of the radionuclide-specific $DCGL_w$ values. Therefore, the survey unit radiological conditions, in dpm, were compared directly to the NMRC action limit (a small fraction of the DCGL). Reference area background surveys were conducted on each day that impacted areas were surveyed. The reference area background survey data is included in this final status survey report.

From the vicinity of a survey site or group of survey sites, background survey-meter readings were recorded, and background swipe samples were collected, analyzed and documented.

H. SURVEY UNITS

A survey unit was defined as a physical area consisting of a specified size and shape for which a separate decision will be made as to whether or not that area exceeds the release criterion. The survey unit is the primary entity for demonstrating compliance with the release criteria.

Per MARSSIM, survey units should be limited in size based on classification, exposure pathway modeling assumptions, and site-specific conditions. The suggested areas for survey units are provided in **Table 5** as follows:

Table 5. Suggested Areas for Survey Units (MARSSIM, Roadmap Table 1)

CLASSIFICATION		SUGGESTED AREA
Class 1	Structures	Up to 100 m^2 floor area
	Land Areas	Up to 2,000 m^2
Class 2	Structures	100 to 1,000 m^2
	Land Areas	2,000 to 10,000 m^2
Class 3	Structures	No limit
	Land Areas	No limit

A NMRC survey unit was defined as a room or other discrete area. Every room and area in the NMRC Annex was examined for residual contamination. Large rooms or areas were sub-divided into smaller sections to facilitate surveying and monitoring. All known licensed-materials use and/or storage areas were classified as Class 3 survey units. Offices, hallways, lavatories, and other common non-license-material-use areas were treated as non-impacted areas. As a quality control (QC) measure, all survey units or areas received some level of survey effort.

I. QUALITY ASSURANCE AND QUALITY CONTROL

Quality Control (QC) and Quality Assurance (QA) measures were incorporated into the decommissioning efforts to ensure the security and integrity of the data and procedures. Maintenance and calibration of equipment were key considerations. In addition, daily and weekly quality control checks for all monitoring equipment and instruments were performed, analyzed and recorded. Periodic training was provided to maintain a competent work force. Redundant survey efforts, which included collecting and analyzing numerous additional swipe samples were planned, completed and documented.

Quality control measures and standard operating procedures were implemented before initiating decommissioning actions. Quality control procedures and data for ensuring the validity of survey results

are included in this report in Appendix D. These procedures and plans included:

(1) properly calibrated instrumentation,

(2) necessary replicate, reference and blank measurements, and

(3) comparison of field measurement results to laboratory sample analyses.

For comparison of survey data to DCGLs, the survey data obtained from swipe-analyses via laboratory measurements was reported in dpm. The swipe analyses results for H-3 and C-14 were compared directly to the NMRC Radiological action limits in **Table 4**.

Data verification ensured that operating procedures were implemented as prescribed. Data verification means that deficiencies or problems that occurred during implementation were documented and presented in this report. This also means that NMRC D&D efforts were assessed regularly and findings were documented. Corrective actions were reviewed for adequacy and appropriateness and documented in response to findings. Data verification activities included, but are not limited to, inspections, QC checks, surveillance, technical reviews, performance evaluations and audits.

To ensure that the conditions requiring corrective actions were identified and addressed promptly, data verification activities were initiated as part of sample collection and data preparation phases of the survey.

The performance of tasks by personnel was compared to standard procedures and was assessed using inspections, surveillance and audits. Self-assessments and independent assessments were planned, scheduled and performed as part of the survey. Self-assessment also means that personnel performing the work were required to document and report deficiencies

or problems that they encountered to the D&D supervisor.

The performance of equipment such as radiation detectors or measurement was monitored using control charts. Control charts were be used to record the results of quantitative QC checks such as background and daily calibration or performance checks. Control charts were used to document instrument and measurement system performance on a daily or as-needed basis to identify conditions requiring real-time corrective actions. Periodic technical reviews may be requested as an independent-assessment measure.

Data validation activities ensured that the results of data collection activities supported the objectives of the survey. Data verification compared the collected data with the investigational levels (action limits) or DCGLs provided in **Table 4**.

J. FIELD MEASUREMENT METHODS AND INSTRUMENTATION

1. FIELD MEASUREMENTS

Surveys for decommissioning required the collection of two types of radiological data:

(1) direct field measurements using portable instruments and

(2) sample analyses using fixed laboratory equipment or systems.

For either type of measurement, the selection and proper use of appropriate instruments were the most critical factors in assuring that the survey accurately determined the radiological status of the site. **Table 6** summarizes equipment and instrument sensitivities for laboratory and field measurements.

Table 6. Typical Measurement Sensitivities for Laboratory Radiometric Procedures (MARSSIM, Chapter 7)

Sample Type	Radionuclides or Radiation Measured	Procedure	Approximate Measurement Sensitivity
Smears (filter paper)	Gross beta	Gas-flow proportional counter; 5-min count	10 dpm
		End window GM with scaler; 5-min count (unshielded detector)	80 dpm
	Low energy beta (H-3, C-14)	Liquid scintillation spectrometer; 5-min count	30 dpm
Soil Sediment	Co-60	Germanium detector (25% relative efficiency) with multi-channel analyzer; pulse height analyzer; 200-min count	0.04 – 0.1 Bq/g (1-3 pCi/g)
Water	Gross beta	Gas-flow proportional counter; 100-ml sample, 200-min count	0.04 Bq/L (1 pCi/L)
	Co-60	Germanium detector (25% relative efficiency) with multi-channel analyzer; pulse height analyzer; 3.5L sample, 16-hour count	0.4 Bq/L (10 pCi/L)
	H-3	Liquid scintillation spectrometer; 5-min count	100 Bq/L (300 pCi/L)

2. INSTRUMENTS, EQUIPMENT, MEASUREMENT AND SAMPLING TECHNIQUES

Instruments for alpha detection were not required. Instrumentation and equipment were selected such that radiation detection procedures (scanning, direct measurements, and sample analyses) could be completed for the radionuclides of interest. Specifications and calibrations of radioactive check sources and radiation-monitoring equipment and instruments are provided in Appendix D, sections 3 and 4, respectively.

For beta radiation detection, the following instruments and equipment were used:

(1) Samples were analyzed using standard procedures and calibrated liquid scintillation counters.

(2) Scanning was performed using appropriate Geiger-Mueller detectors with pancake probes or digital-scaler, gas proportional counter with appropriate detectors.

For gamma radiation detection, scanning was performed using appropriate Geiger-Mueller detectors with appropriate probes.

Exposure rate measurements, when necessary, were obtained using appropriate instrumentation.

A combination of two approaches was used for scanning Class 3 areas. The two approaches included uniformly scanning for the radionuclides of interest and/or performing scans in areas with the greatest potential for residual contamination based on professional judgment and the objectives of the survey. The investigation level was set at an elevated activity reading that exceeded 2 to 3 times the background readings.

Appropriate calibration check sources were obtained to perform instrument background and check-source (quality assurance and quality control) checks.

Instrument response (background and check source) was tested and recorded a minimum of once daily – prior to beginning the day's measurements – to ensure continued acceptable operation. If an instrument's response did not satisfy the established acceptable range, the instrument was removed from use until the reason for the deviation could be determined and resolved and acceptable response again demonstrated. If repair and/or recalibration were necessary, acceptable response ranges were reestablished and documented.

K. SAMPLING AND PREPARATION FOR LABORATORY MEASUREMENTS

1. FIELD SAMPLE PREPARATION AND PRESERVATION

Proper sample preparation and preservation are essential parts of any radioactivity-sampling program. The sampling objectives were specified in the D&D Standard Operating Procedures (D&D SOP) manual and Appendix C. Precise records of sample collection and handling were performed to ensure that data obtained from different locations or timeframes were correctly compared.

According to MARSSIM, Chapter 7, field and preparation of building surfaces, including smear samples, is generally not required. Smear samples were collected from randomly selected locations and other areas, labeled, packaged, tracked, and delivered to the on-site counting laboratory for analyses.

2. OTHER MEASUREMENTS AND SAMPLING LOCATIONS

In addition to building surface areas, there were numerous other locations where measurements and/or sampling were performed. Examples include items of equipment and furnishings, workbenches, shelves, building fixtures, drains, ducts, and piping. Many of these items or locations had both internal and external surfaces, requiring evaluation. Each such location classified as impacted was scanned and individual measurements and/or sampling were performed. Non-impacted locations were also surveyed, but at lower frequencies, consistent with contamination potential and findings as the survey progressed.

IX. DECONTAMINATION PROCEDURES

Using the guidance, procedures, and checklists provided in the MARSSIM, characterization surveys, reclassification of survey areas, remedial actions, and remediation-action support surveys were performed and documented, when necessary. When contamination was identified in a survey unit, characterization surveys (via scanning or swipe-sample counting) were performed to determine the extent of the contamination. After a characterization survey was completed, remedial actions were completed. The remediation actions consisted of repeated washings or scrubbing or removal of the contaminated media. Waste generated from this process was treated as radioactive waste and disposed of accordingly. Remediation action surveys were completed following iterations of decontamination efforts to measure the effectiveness of the efforts. Final surveys of the contaminated areas were completed and documented.

X. FINAL STATUS SURVEY

A. OVERVIEW

The guidance provided in MARSSIM, Section 5.5, Final Status Surveys, was closely followed. The final status surveys were performed to demonstrate that residual radioactivity in each survey unit satisfied the predetermined release criteria for unrestricted future use. The survey provided data to demonstrate that all radiological conditions did not exceed the established DCGLs or NMRC action limits.

In demonstrating that the objective was met, the null hypothesis (H_o) tested was that residual contamination exceeded the release criterion; the alternate hypothesis (H_a) was that residual contamination met the release criterion. Two statistical tests could be used to evaluate data from final status surveys. For contaminants that are present in background, the Wilcoxon Rank Sum (WRS) test would be used. When contaminants are not present in background, the Sign test is used.

Since contaminants at the Annex were not present in background in significant amounts, the Sign test was used. Statistical parameters (α and β) were chosen such that there was less than a 5% probability that radioactivity would be reported present when it was really absent (Type I error) or reported absent when it was really present (Type II error).

B. SURVEY PREPARATIONS

Residual radioactivity limits for the radionuclides present at the site were selected. NMRC action limits or investigational levels were equivalent to a small fraction of D&D screening values and were set such that the NRC release criteria were satisfied. **Table 4** provides the NRC D&D screening values for NMRC isotopes of concern (ref 11.13), action plan values,

and NMRC's residual radioactivity limits. Guidance in **Table** 7 was used to interpret the survey results.

Table 7. Interpretation of Sample Measurements When No Reference Area Is Used (MARSSIM, Table 2.5)	
SURVEY UNIT MEASUREMENT RESULTS	CONCLUSION
All concentrations are less than $DCGL_w$ (or NMRC action limit)	Survey unit meets release criteria
Average concentration is greater than $DCGL_w$ (or NMRC action limit)	Survey unit fails
Any concentration is greater than $DCGL_w$ and average concentration is less than $DCGL_w$	Conduct Sign test and elevated measurement comparison

Representative reference (background) areas were selected for the survey units. Reference areas were selected from non-impacted areas and were:

(1) free of contamination from site operations,

(2) exhibited similar physical, chemical, and biological characteristics as the survey unit, and

(3) had similar construction, but had no history of radioactive operations.

The Annex building is a two-story structure. If swipe samples were collected for impacted survey units on the first floor during a day's operations, background samples were collected on the first floor as well. Similarly, if swipe samples were collected in impacted areas on the second floor during a day's operations then background samples were collected from second floor locations.

Survey instruments were selected based upon the techniques to be employed (scanning, direct

measurements, and sampling) and the radionuclides of concern. The selected instruments were capable of detecting the contamination at 10-50% of the DCGLs.

The survey unit was prepared before conducting the final survey by clearing and providing access to the areas to be surveyed, including the floor, lower walls, workbenches, shelves and fixtures.

Reference coordinate systems using grid maps were established and followed.

C. Survey Design

Sample collection and analysis procedures were developed and implemented as D&D Standard Operating Procedures in Appendix C. All Radiological workers received initial and periodic training.

The number of data points for statistical tests were determined using the assumption that the radionuclides were not present in background. The Sign test was used. The number of samples for Class 3 areas were determined using the following statistical values, Type I error where $\alpha = 0.025$, Type II error where $\beta = 0.025$, and the relative shift, $\Delta/\sigma_s = 2$. The relative shift was determined by using data from a contaminated area and the formulae provided in MARSSIM. The data and the determination of the relative shift are provided in **Table 8**. The number of data points, N, was determined to be 21. Per MARSSIM, this N value added an extra 20% to account for unusable data or uncertainty in the value of N.

The number of random data samples collected for each Impacted Class 3 survey unit was 21. Additional samples/measurements were taken for Quality Control and to allow for possible loss of data and increased sampling with survey units. The additional data points were not used when conducting statistical tests of survey data. In conjunction with completing

surveys for all impacted areas, reference background readings and samples were collected.

Table 8. Determination of the Relative Shift, Δ/σ, using swipe data from a contaminated area

Let Δ = 2500 dpm - 700 dpm

Basis of Δ: one-half of the conservative Regulatory Guide 1.86 contamination limit of 5,000 dpm and NMRC action limit of 700 dpm

In this table, σ is calculated using H-3 swipe data from a contaminated area

Sample Number	H-3, dpm
1	345
2	700
3	621
4	391
5	2884
6	160
7	205
8	203
9	153
10	2892
11	642
12	1009
13	74
14	43
15	104
16	67
17	1161
18	172
19	51
20	58
21	77
22	2795
23	110
24	183
Average	629
Standard deviation	913
Set Δ = 2500 - 700 dpm	1800
Δ/σ, calculated	1.97 ~= 2

Table 9 provides recommended survey coverage for structures and land areas (MARSSIM, table 5.9).

Table 9. Recommended Survey Coverage For Structures and Land Areas

AREA CLASSIFICATION	STRUCTURES		LAND AREAS	
	Surface Scans	Surface Activity Measurements	Surface Scans	Soil Samples
Class 1	100%	Number of data points from statistical tests and additional measurements may be necessary for small areas of elevated activity	100%	Number of data points from statistical tests and additional measurements may be necessary for small areas of elevated activity
Class 2	10 to 100% (10 to 50% for upper walls and ceilings) Systematic and Judgmental	Number of data points from statistical tests	10 to 100% Systematic and Judgmental	Number of data points from statistical tests
Class 3	Judgmental	Number of data points from statistical tests	Judgmental	Number of data points from statistical tests

Sampling locations for Impacted Class 3 areas utilized a rectangular grid system that used a local landmark, such as doors in survey units. Grid systems were established for the impacted survey sites to:

- Facilitate systematic selection of measuring/sampling locations,
- Provide a mechanism for referencing a measurement/sample back to a specific location so that the same survey point can be relocated, and
- Provide a convenient means for determining average activity levels.

The grids consisted of a system of intersecting lines created by using colored, paper or plastic adhesive tape and referenced to a fixed site location or benchmark. The grid lines were arranged in a perpendicular pattern, dividing the survey location into approximately one-meter squares or blocks. Grid patterns on horizontal surfaces were identified numerically on one axis and numerically on the other axis. Grids on vertical surfaces are shown as flat surfaces on the grid maps. Grid maps used during the survey efforts are provided with the data and summaries in Appendix XII. Gridding was limited to the floor and lower (up to 2 meters height) walls.

Because radioactive-material use during the last 10 years has involved the use of small quantities in liquid form in hoods or workbench areas, only the lower two meters of the walls in Impacted Class 3 areas will be surveyed. No airborne residual contamination is anticipated.

For the Class 3 survey units, the locations of the 21 random data points were determined using lists of random numbers. Additional measurements were selected to ensure good coverage of the survey unit and to survey selected areas within the survey unit.

Quality control procedures for ensuring the validity of survey results were included in D&D Standard Operating Procedures. These procedures included:

(1) survey procedures and techniques,

(2) sample collection and processing procedures,

(3) data-analysis procedures,

(4) equipment and instrument procedures, and

(5) source-standards, background-standards and reference-background measurements.

D. CONDUCTING SURVEYS

The reference (background) area measurements and sampling were performed and documented.

Final status survey activities were conducted. The activities included:

(1) performing surface scans of Class 3 areas and a percentage of non-impacted areas,

(2) conducting surface activity measurements and sampling at previously selected sampling locations, and

(3) conducting additional direct measurements and sampling at locations based on professional judgment.

Necessary investigation activities, including remediation and re-survey were performed and documented. Reclassifications of survey units were not required.

Measurement and sample locations were documented on grid maps. The grids with sample locations and sample

numbers are provided in Appendix E with survey data for each impacted survey unit.

Observations, abnormalities, and deviations from the standard operating procedures were documented.

E. DATA CONVERSION

Data conversion was not required for results obtained by evaluating swipe samples using the liquid scintillation counter. The results for each swipe sample were reported in dpm for both H-3 and C-14 for an area of approximately 100 cm^2. Data conversion was required for surface activity measurements that were obtained using a hand-held, gas proportional detector. Guidance provided in chapter 6 of MARSSIM was used to convert the meter readings to the conventional surface activity units of dpm per 100 cm^2. **Table 10** provides the applicable MARSSIM equation and a sample calculation.

Table 10. Data Conversion for Direct Readings of Surface Activity Using a Gas Proportional Detector

MARSSIM formula 6-4:

$$\frac{dpm}{(100\ cm^2)} = \frac{(C_s/T_s)-(C_b/T_b)}{(E_i \times (A/100))}$$

where, A = physical probe area in cm^2, E_i = instrument efficiency, sample and background count times, T_s and T_b in minutes, C_s = sample counts during time T_s, and C_b = background counts during time, T_b

Note: Interpret negative values of the calculated dpm as equal to zero.

Sample calculation:

Let A = 126 cm^2; $T_s = T_b = 1$ min; $E_i = 15\%$;
$C_s = 361$ and $C_b = 211$

$$\frac{dpm}{(100\ cm^2)} = \frac{((361/1)-(211/1))}{(0.15 * (126/100))} = 794$$

F. EVALUATING AND DOCUMENTING SURVEY RESULTS

Samples were analyzed using the procedures detailed in the SOP and Appendix C. Swipe-sample results in dpm were compared directly to DCGL values and NMRC action limits. Individual measurements and sample concentrations were first compared to DCGL levels for evidence of small areas of elevated activity. No additional data comparisons were necessary. The initial swipe results or results following remediation efforts did not exceed NMRC action limits.

Verification of assumptions of statistical tests was not necessary. Per MARSSIM, Appendix B, "The results of the survey should be compared to derived concentration guideline levels (DCGLs) using an appropriate statistical test, such as Student's t test

or Wilcoxon test. If all measurements are less than the $DCGL_w$, then statistics do not need to be addressed because the conclusions are obvious. If the mean of the measurements exceeds the $DCGL_w$, the survey unit obviously fails to demonstrate compliance and the statistics do not need to be addressed."

Survey results for each survey unit were compared with NMRC residual radioactivity investigational levels or action levels. These action levels represented small fractions of DCGLs (NRC D&D screening values). Elevated measurement comparisons were not performed and were not needed.

This final status survey report includes the standard operating procedures, quality assurance information and procedures, data, results, interpretations, deviations from standard procedures, and other applicable information.

XI. REFERENCES

11.1 **NUREG-1575**, MARSSIM, Multi-Agency Survey and Site Investigation Manual (December 1997).

11.2 **NMRC Historical Site Assessment**, Naval Medical Research Center (NMRC, formerly NMRI), June 1999.

11.3 **ESA 1997**, Environmental Site Assessment, Naval Medical Research Institute (NMRI), by the Environmental Company, Inc., May 1998.

11.4 **10CFR20.1402**, Title 10, Code of Federal Regulations, Part 20 - Standards for Protection Against Radiation, Subpart E.

11.5 **NUREG-1500**, Working Draft Regulatory Guide on Release Criteria for Decommissioning: NRC's Staff Draft for comment, August 1994.

11.6 **NUREG-1501**, Background as a Residual Radioactivity Criterion for Decommissioning, Draft Report for Comment, August 1994.

11.7 **NUREG-1505**, A Non-parametric Statistical Methodology for Design and Analysis of Final Status Decommissioning Surveys.

11.8 **NUREG-1507**, Minimum Detectable Concentrations with Typical Radiation Survey Instruments for various Contaminants and Field Conditions, December 1997.

11.9 **NUREG-1549**, Decision Methods for Dose Assessment to Comply With Radiological Criteria for License Termination (Draft, July 1998).

11.10 **NUREG/CR-5512**, Residual radioactive Contamination from Decommissioning (Draft, April 1996).

11.11 **NUREG/CR-5849**, manual for Conducting Radiological Surveys in Support of License Termination, Draft for comment June 1992 (superseded by NUREG-1575, MARSSIM).

11.12 **Draft Regulatory Guide DG-4006**, Demonstrating Compliance with the Radiological Criteria for License Termination (supersedes NUREG 1500), August 1998.

11.13 **Federal Register**, Volume 63, Number 222, November 18, 1998, page 64134.

11.14 **REG GUIDE 1.86**, Nuclear Regulatory Commission Regulatory Guide 1.86 (1974).

XII. APPENDICES

A. Conceptual Model and Site Diagram

B. Documents, Figures and Photographs

C. Standard Operating Procedures and Quality Assurance Program

D. Survey Unit Release Reports (Narratives, Data, Floor Plans, and Grid Maps)

E. Quality Assurance Information and Data

APPENDIX A. CONCEPTUAL MODEL AND FLOOR DIAGRAMS

Appendix A-1. CONCEPTUAL MODEL

NMRC D&D Phase II (1/2000- 4/2000)
NMRC Rockville Annex location (1 building)

Contaminants of concern:
H-3, C-14, P-32, S-35, Cr-51

BUILDING SURFACE CLASSIFICATIONS

	Number Of Survey Units	Total Area (SF)
Non-impacted	38	4,617
Impacted Class 3	29	7,595
Totals	67	12,212

Appendix A-2. FLOOR DIAGRAM, FIRST FLOOR, ROCKVILLE ANNEX

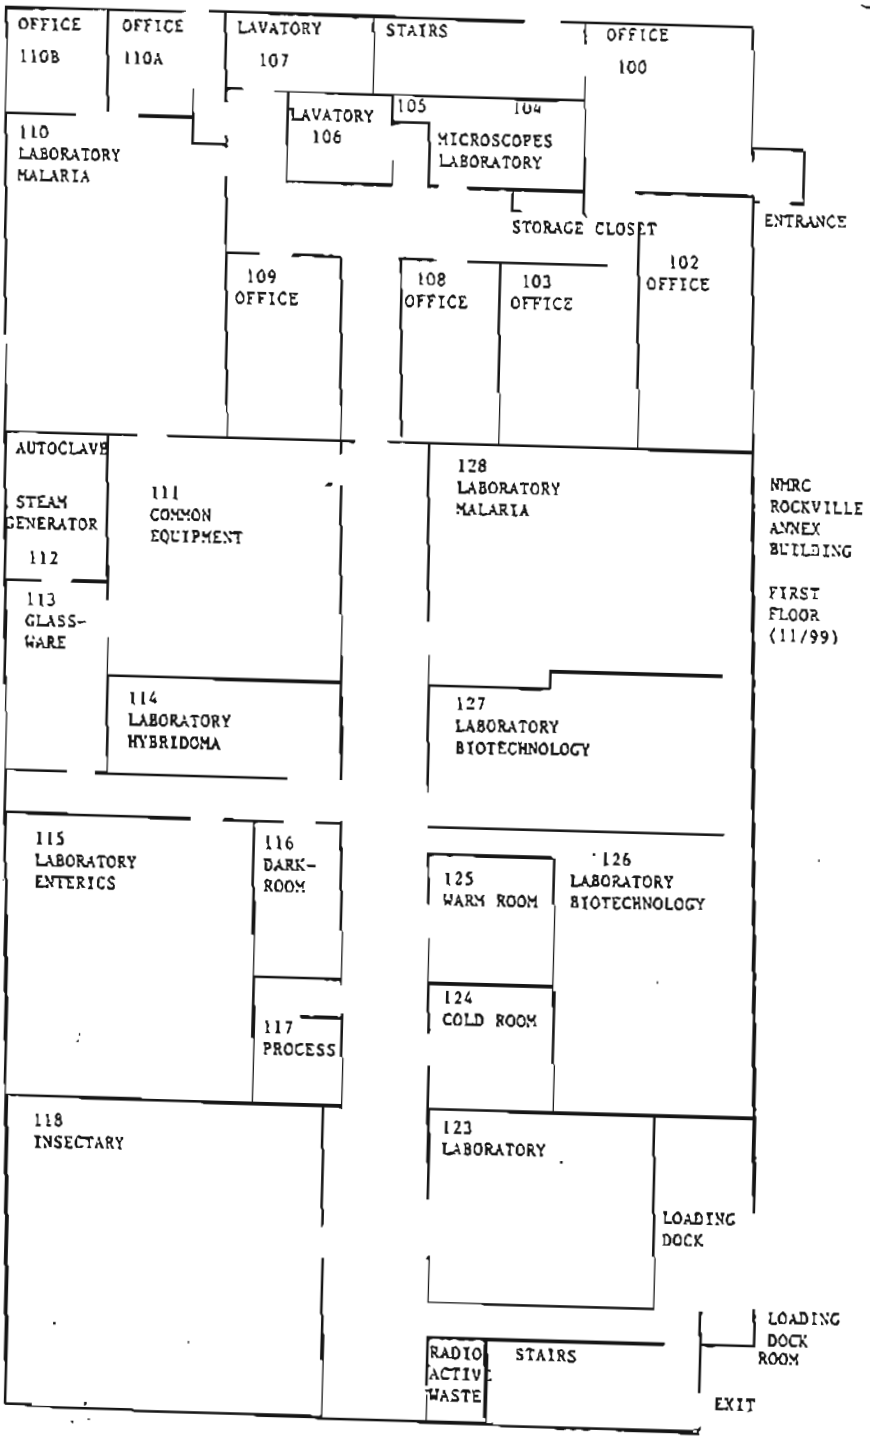
OFFICE
110B
OFFICE
110A
LAVATORY
107
STAIRS
OFFICE
100
LAVATORY
106
105
104
MICROSCOPES
LABORATORY
110
LABORATORY
MALARIA
STORAGE CLOSET
ENTRANCE
109
OFFICE
108
OFFICE
103
OFFICE
102
OFFICE
AUTOCLAVE
STEAM
GENERATOR
112
111
COMMON
EQUIPMENT
128
LABORATORY
MALARIA
NMRC
ROCKVILLE
ANNEX
BUILDING
FIRST
FLOOR
(11/99)
113
GLASS-
WARE
114
LABORATORY
HYBRIDOMA
127
LABORATORY
BIOTECHNOLOGY
115
LABORATORY
ENTERICS
116
DARK-
ROOM
125
WARM ROOM
126
LABORATORY
BIOTECHNOLOGY
124
COLD ROOM
117
PROCESS
118
INSECTARY
123
LABORATORY
LOADING
DOCK
LOADING
DOCK
ROOM
RADIO
ACTIVE
WASTE
STAIRS
EXIT

Appendix A-3. FLOOR DIAGRAM, SECOND FLOOR, ROCKVILLE ANNEX

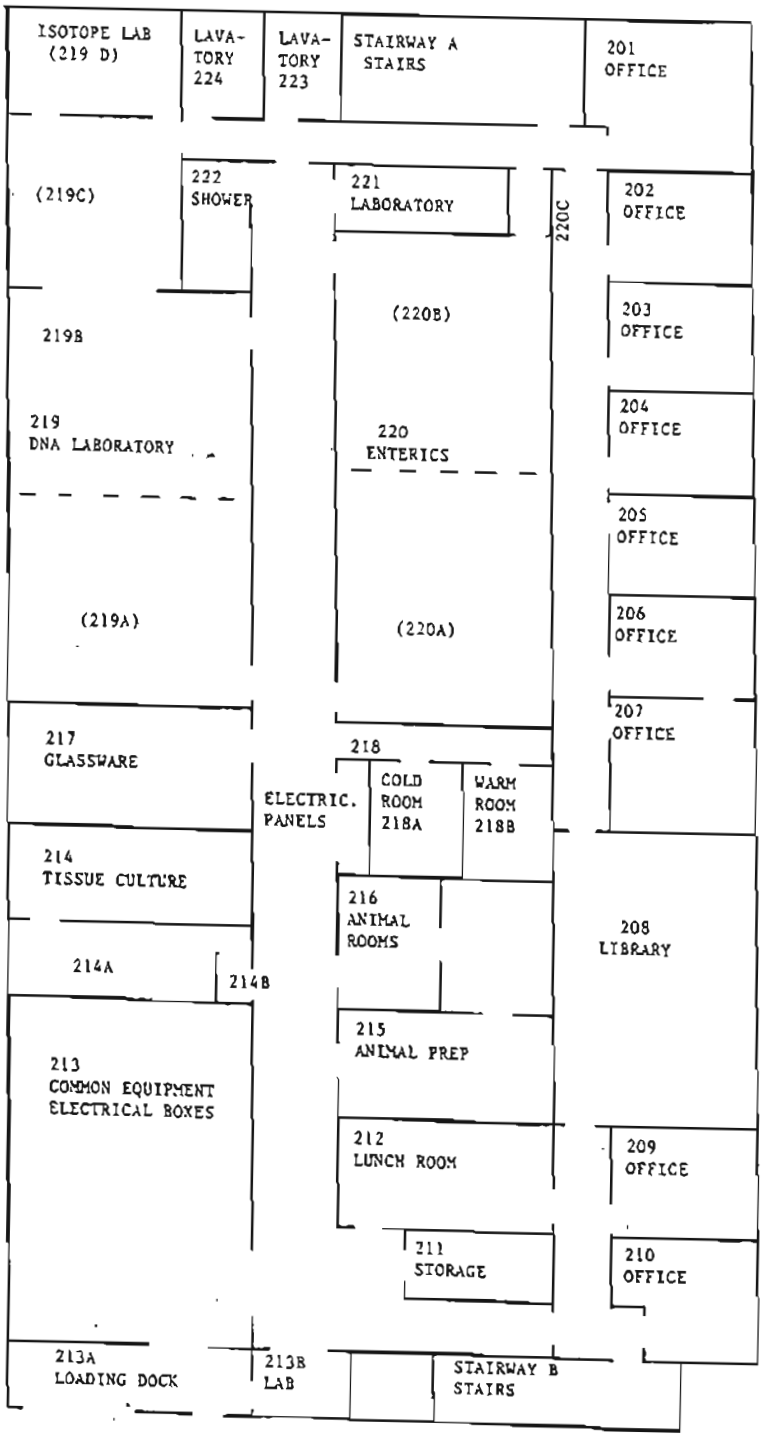

NMRC
ROCKVILLE
ANNEX
BUILDING

SECOND
FLOOR
(11/99)

APPENDIX B. DOCUMENTS AND PHOTOGRAPHS

Appendix B-1. DOCUMENTS

Annex Lease Documents

Annex Gamma Irradiator Decommissioning Documents

W.M. RICKMAN CONSTRUCTION CO.

15215 SHADY GROVE ROAD • ROCKVILLE, MD 20850 • (301) 840-2011 FAX (301) 840-5992

September 16, 1999

Department of The Navy
Engineering Field Activity Chesapeake
Washington Navy Yard Building 212
901 M Street, S. E.
Washington, DC 20374-5018

Attn: Linda G. Ertumen - Head, Real Estate Contracting Officer

Re: 12300 Washington Avenue - Lease Contract
Nos. N6247796RP00044 and N6247796RP00056

Dear Ms. Ertumen,

The W. M. Rickman Construction Company has enjoyed having the Navy as our tenant at the Washington Avenue facility. We want to wish you continued success when you occupy your new research facility.

We ask that you provide the following documents as the Navy vacates the Washington Avenue facility.

1.) A report that the building has been decontaminated and is free of biohazards.

2.) A report that radioactive isotopes have been removed and the building is clean from radioactivity.

3.) All chemicals have been removed from the premises.

4.) A report that the building is clear of mosquitoes used in research. (extermination report)

5.) Hepa Filter(s) have been removed from premises.

Please contact me at (301) 840-2011 to schedule a "walk-thru" at the facility and if you have questions concerning these issues.

Sincerely,

Ross L. Englehart

Ross L. Englehart
Director of Facilities

xc: Lisa Petro

DEPARTMENT OF THE NAVY
NAVAL MEDICAL RESEARCH CENTER
NATIONAL NAVAL MEDICAL CENTER
8901 WISCONSIN AVENUE
BETHESDA, MARYLAND 20889-5607

IN REPLY REFER TO.

NOV 19 1998

From Commanding Officer, Naval Medical Research Center
To: Commanding Officer, Engineering Field Activity-Chesapeake
901 M Street, SE, Building 212, Code 24, Washington, DC 20374-5018
Via: Chief, Bureau of Medicine and Surgery (MED-33)
2300 E Street, NW, Washington, DC 20372-5300

Subj : REQUEST RENEWAL OF LEASES

Encl: (1) Move Schedule as of 28 September 1998

1. Request that Engineering Field Activity-Chesapeake take action to renew U.S. Government Leases N6247796RPOO044 and N6247796RPOO056 which provide for first and second floors at 12300 Washington Avenue, Rockville, Maryland, respectively.

2. Based on moving schedule provided by enclosure (1), request that Lease N6247796RPOO044 be renewed for a term of six (6) months beginning I June 1999 and expiring 30 November 1999. Request that Lease N6247796RPOO056 be renewed for a term of three (3) months beginning I September 1999 and expiring 30 November 1999.

3. My point of contact is Mr. P. Cheng who can be reached at COM. (301) 295-1049 or DSN 295-1049 and/or FAX (301) 295-1362.

D. Alexander
By direction

Blind Copy to:
CO
XO
DFA
Dr. C. G. Hayes
CAPT S. L. Hoffman
Mr. D. Chandler
Dr. G. A. Dasch
Mrs. S. Hawkins
LCDR S. L. Gaiter
LT S. Krauz
Mr. M. O'Hare
Mr. K. Johnson
UTC L. Wilson
HMI Henderson

BY SEPARATE CORRESPONDENCE, THIS LEASE WAS EXTENDED ANOTHER 6 MONTHS. THE EXTENSION OF THE LEASE INCLUDED THE TERM THROUGH 31 MAY 2000.

JL SHEPHERD & ASSOCIATES
1010 ARROYO AVE., SAN FERNANDO, CALIFORNIA 91340-1822
818-898-2361 FAX 818-361-8095

CERTIFICATION OF SOURCE/DEVICE POSSESSION TRANSFER

This document is to certify that on or about February 29, 2000, J.L. Shepherd and Associates took possession of and title to (1) Each Gammator 50B Irradiator, S.N.#:1146, with approximately 400 Curies of Cesium-137 (as of November, 1973), from The Naval Medical Research Center, Rockville Annex, 12300 Washington Ave., Room 111, Rockville, MD, 20852.

This transfer preparation took place under the direct supervision of J.L. Shepherd and Associates' engineer, under JLS&A'S State of California Radioactive Materials License and applicable 49CFR and CA Title 17 Transportation requirements, working under J.L. Shepherd and Associates, State of California Radioactive Materials License 1777-19, Amendment 78, Expiration Date 10/11/95, with State of California issued Letter of Timely Renewal, Dated September 21, 1995, in accordance with 10CFR40.51, 49CFR, all regulatory agency licensing and transportation requirements. J.L. Shepherd and Associates per the attached license, or our designated hot cell facility, is licensed to receive, possess and store this source/device.

Naval Medical Research Institute
LCDR Gaiter

Dated: 2/29/00

Mary Shepherd
Vice-President
J.L. Shepherd and Associates

Dated: 2/21/00

D. TERRY STOUT TECH 3-1-2000

SHEPHERD & ASSOCIATES
1010 ARROYO AVE, SAN FERNANDO, CALIFORNIA 91340-1822
818-898-2361 FAX 818-361-8095

TRIP REPORT

JLS&A REPRESENTATIVE: DOYLE TERRY STOTT

DATE: 2/29/00 HOURS: 6 COMPLETE: YES or NO

==========

CUSTOMER'S NAME: NAVAL MEDICAL RESEARCH CENTER

CONTACT: S. AHMAD/LCDR GAITER PHONE #: (301)295-0002/3653

ADDRESS: 12300 WASHINGTON AVE./ROOM 111
ROCKVILLE ANNEX
ROCKVILLE MD 20852

P.O.#: N32398-00-M-0248
N3239800RC7Z019

JOB #: 984584

DEVICE: SEE BELOW S.N. 1146

REASON FOR VISIT: SERVICE CALL FOR JLS TECHNICIAN TO DECOMMISSION/TAKE POSSESSION OF GAMMATOR 50B IRRADIATOR, S.N.#:1146, WITH APPROXIMATELY 400 CURIES OF Cs-137 AS OF NOVEMBER, 1973.

STATEMENT OF WORK: DECOMMISSION AND SHIP TO TISEC

PARTS USED: None

PARTS REQUIRED TO COMPLETE: None

FUTURE MAINTENANCE REQUIRED: None

The following signatures acknowledge that the above work has been performed satisfactorily.

Saifuddin Ahmad
CUSTOMER'S SIGNATURE

Doyle Terry Stott
JLS&A REPRESENTATIVE

ORDER FOR SUPPLIES OR SERVICES

(Contractor must submit four copies of invoice.)

Form Approved
OMB No 0704-0187
Expires Aug 31, 1992

Public reporting burden for this collection of information is estimated to average 1 hour per response, including the time for reviewing instructions, searching existing data sources, gathering and maintaining the data needed, and completing and reviewing the collection of information. Send comments regarding this burden estimate or any other aspect of this collection of information, including suggestions for reducing this burden, to Department of Defense, Washington Headquarters Services, Directorate for Information Operations and Reports, 1215 Jefferson Davis Highway, Suite 1204, Arlington, VA 22202-4302, and to the Office of Management and Budget, Paperwork Reduction Project (0704-0187), Washington, DC 20503

PLEASE DO NOT RETURN YOUR FORM TO EITHER OF THESE ADDRESSES.
SEND YOUR COMPLETED FORM TO THE PROCUREMENT OFFICIAL IDENTIFIED IN ITEM 6.

1. CONTRACT / PURCH ORDER NO: N32398-00-M-0248
2. DELIVERY ORDER NO.:
3. DATE OF ORDER (YYMMDD): 00 February 15
4. REQUISITION / PURCH REQUEST NO: N3239800RC7Z019
5. PRIORITY: 3

6. ISSUED BY — CODE N32398
Procurement Department
Naval Medical Research Center
8901 Wisconsin Avenue - Bethesda, Maryland 20889
Contracting Officer: Veronica Serrano (301) 295-3793

7. ADMINISTERED BY (If other than 6) — CODE

8. DELIVERY FOB: [X] DEST [ ] OTHER (See Schedule if other)

9. CONTRACTOR — CODE 29345 — FACILITY CODE
NAME AND ADDRESS:
J.L. SHEPHERD AND ASSOCIATES
ATTENTION MARY SHEPHERD
1010 ARROYO AVENUE
SAN FERNANDO, CALIFORNIA 91340-1822

10. DELIVER TO FOB POINT BY (Date) (YYMMDD): 00 February 28
11. MARK IF BUSINESS IS: [X] SMALL [ ] SMALL DISADVANTAGED [ ] WOMEN-OWNED
12. DISCOUNT TERMS: Net 30 Days
13. MAIL INVOICES TO: Receipt Control / NMRC
8901 Wisconsin Avenue - Bldg 17 - Rm 132

14. SHIP TO — CODE N32398
Naval Medical Research Center / Safety Office
8901 Wisconsin Avenue / Building 17
Bethesda, Maryland 20889
Attention: LCDR Gaiter (301)295-3653/S. Ahmad 295-0002

15. PAYMENT WILL BE MADE BY — CODE N68892
DFAS
Charleston, South Carolina
Contractor Federal ID #: 952477911

MARK ALL PACKAGES AND PAPERS WITH CONTRACT OR ORDER NUMBER

16. TYPE OF ORDER
DELIVERY: This delivery order is issued on another Government agency or in accordance with and subject to terms and conditions of above numbered contract.
PURCHASE [X]: Reference your Written Quote Mary Shepherd: REF #: JLS-6124 furnish the following on terms specified herein.
ACCEPTANCE. THE CONTRACTOR HEREBY ACCEPTS THE OFFER REPRESENTED BY THE NUMBERED PURCHASE ORDER AS IT MAY PREVIOUSLY HAVE BEEN OR IS NOW MODIFIED, SUBJECT TO ALL OF THE TERMS AND CONDITIONS SET FORTH, AND AGREES TO PERFORM THE SAME.

NAME OF CONTRACTOR | SIGNATURE | TYPED NAME AND TITLE | DATE SIGNED (YYMMDD)

If x is marked, supplier must sign Acceptance and return the following number of copies:

17. ACCOUNTING AND APPROPRIATION DATA

ITEM NO	APPROPRIATION SYMBOL AND SUBHEAD	OBJECT CLASS.	BUREAU CONT NO.	SUB-ALLOT	AUTH'N ACCT'G ACTY	TRANS TYPE	PROPERTY ACCT ACTY	COUN-TRY	COST CODE	AMOUNT
AA	1701319 B6ZZ	250	32398	0	068892	2D	C7Z019		32398007700O	$5,550.00

18 ITEM NO.	19 SCHEDULE OF SUPPLIES / SERVICE	20. QUANTITY ORDERED / ACCEPTED *	21 UNIT	22. UNIT PRICE	23 AMOUNT
	For Questions Concerning Billing/Payment Call: (301)295-2188 For Questions Concerning The Content Of This Purchase Order Please Call: Veronica Serrano (301) 295-3793 **********				
0001	SERVICE CONTRACT: Decommissioning of Gammairradiator Gammator Model #: 50B / Serial #: 1146 SERVICE LOCATION Rockville Annex / 12300 Washington Avenue / Room 111 Rockville, Maryland 20852 NOTE: Decommissioning Should Be Complete Before Lease Expires (Statement Of Work Page 2)	1	Job	5,550.00	5,550.00

* If quantity accepted by the Government is same as quantity ordered, indicate by X. If different, enter actual quantity accepted below quantity ordered and encircle.

24. UNITED STATES OF AMERICA
BY: Veronica Serrano/Feb. 15, 2000 — Veronica Serrano — CONTRACTING / ORDERING OFFICER

25. TOTAL: $5,550.00
29. DIFFERENCES:

26. QUANTITY IN COLUMN 20 HAS BEEN: [ ] INSPECTED [ ] RECEIVED [ ] ACCEPTED AND CONFORMS TO THE CONTRACT EXCEPT AS NOTED
SIGNATURE OF AUTHORIZED GOVERNMENT REPRESENTATIVE

27. SHIP NO.: [ ] PARTIAL [ ] FINAL
28. D.O. VOUCHER NO.
30. INITIALS
32. PAID BY: CUSTOMER
33. AMOUNT VERIFIED CORRECT FOR
31. PAYMENT: [ ] COMPLETE [ ] PARTIAL [ ] FINAL
34. CHECK NUMBER
35. BILL OF LADING NO.

36. I certify this account is correct and proper for payment.
DATE | SIGNATURE AND TITLE OF CERTIFYING OFFICER

37. RECEIVED AT | 38. RECEIVED BY (Print) | 39. DATE RECEIVED (YYMMDD) | 40. TOTAL CONTAINERS | 41. S/R ACCOUNT NUMBER | 42. S/R VOUCHER NO.

ORDER FOR IPPLIES OR SERVICES
(Comi ary Continuation Sheet)

Public reporting burden for this collection of informr is estimated to average 1 hour per response, including the time for reviewing instructions, searching existing data sources, gathering and maintaining it needed, and completing and reviewing the collection of information. Send comments regarding this burden estimate or any other aspect of this colle information, including suggestions for reducing this burden, to Washington Headquarters Services, Directorate for Information Operations and Repo 15 Jefferson Davis Highway, Suite 1204, Arlington, VA 22202-4302, and to the Office of Management and Budget, Paperwork Reduction Project (0704-018 shington, DC 20503.

Approved
Jo. 074-0187
es Aug 31, 1992

1. CONTRACTOR	2. PURCHASE OR DELIVERY ORDER NUMBER	3. DATE OF ORDER	4. PAGE NO.	5. NO. OF PAGES
J.L. Shepherd & Associates 1010 Arroyo Avenue - San Fernando, California 91340-1822	N32398-00-M-0248	February 15, 2000	2	3

6. ISSUED BY	7. CONTRACT NUMBER	8. VENDOR INVOICE NUMBER	9. RECEIVING REPORT NUMBER
Procurement Department 8901 Wisconsin Avenue - Bethesda, Maryland 20889			

10. ITEM NO.	11. SCHEDULE OF SUPPLIES/SERVICES	12. QUANTITY ORDERED*	13. QUANTITY ACCEPTED*	14. UNIT	15. UNIT PRICE	16. AMOUNT	17. RETAIL a. UNIT PRICE	b. EXTENSION
	Statement Of Work Decommissioning of Gammator: Model 50B / Serial # 1146 A) Contractor shall take possession of the source and device upon arrival of engineer for the purpose of decommissioning. B) Contractor shall provide Type B shipping container (overpack) required for transporting the irradiator to the Contractor's address. C) Contractor shall prepare the irradiator for shipment and prepare all required shipping documentation. This includes complete disassembly for shipment. D) All shipping charges have been included in total quoted cost. E) Costs includes local 1-day rental of 6,000 pound fork lift with 10' lift to: - off-load the truck - uncrate the Type B shipping container - load the Gammator into the shipping container and re-load truck (Clauses By Reference Page 3)							

CUSTOMER

* The supplies or services listed in the "Quantity Ordered" column were inspected and accepted, and quantities shown therein were received, unless otherwise noted in the "Quantity Accepted" column.

18. DATE Feb 15, 2000
February 15, 2000

19. AUTHORIZED GOVERNMENT REPRESENTATIVE
Veronica Serrano
Veronica Serrano / Contracting Officer

gammator β

gamma irradiator

an interdisciplinary tool for life sciences, physical sciences, technician training

PAGE-KAUFMAN-DALY INC.
(301) 789-2900
80 OLD ANNAPOLIS ROAD
LINTHICUM HEIGHTS, MARYLAND 21090

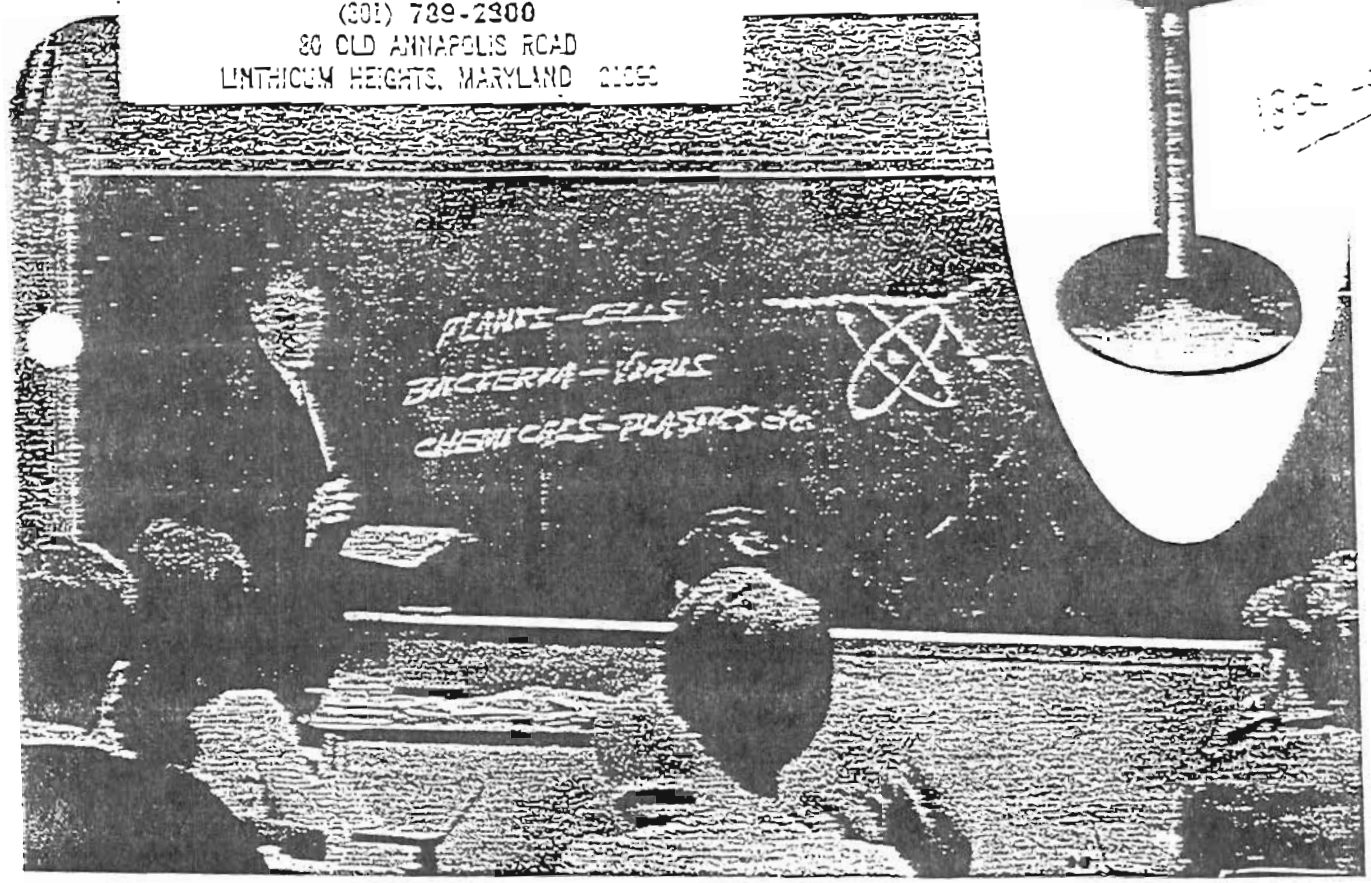

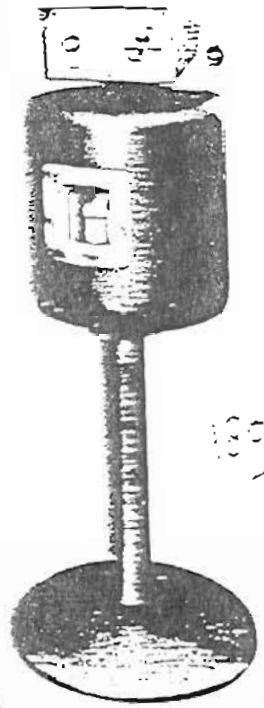

CURRICULA .... A NECESSARY NEW ADVANCE FOR SCIENTIFIC CURRICULA .... A NECESSARY NEW ADVANCE



K·S·E KEWAUNEE SCIENTIFIC ENGINEERING
Adrian, Michigan 49221 • Phone [illegible]

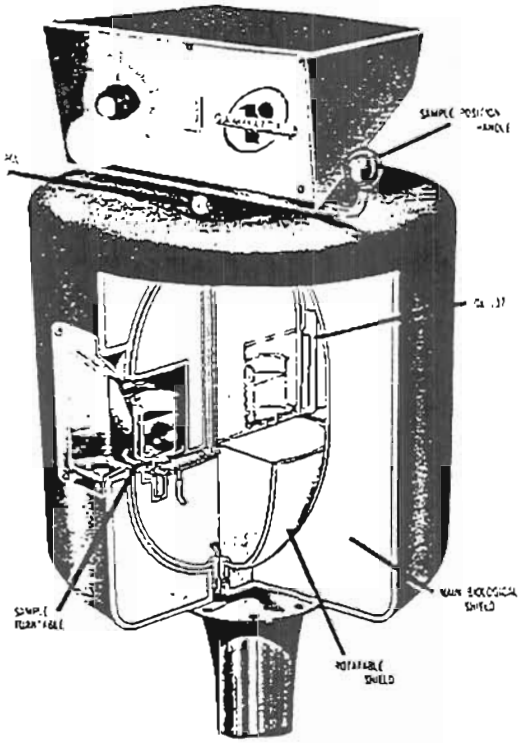

UNIT CHARACTERISTICS

EXPOSURE CHAMBER SIZE — 3" dia. by 4" high.

IRRADIATION INTENSITY — 35,000 Roentgen/hr. at center line of exposure chamber. See Radiation Level [illegible]

[illegible] UNIFORMITY — uniformity achieved by rotatio[illegible] sample at 4.5 rpm

POWER SOURCE REQUIRED — std. wall outlet

HEIGHT OVERALL — 60" max.

SAMPLE PORT HEIGHT FROM FLOOR — 41"

DIAMETER: IRRADIATOR — 18"
BASE — 24"

WEIGHT — 1850#

SOURCE CHARACTERISTICS

SOURCE MATERIAL — Cs-137 — Chloride

SOURCE STRENGTH — 400 curies ±5%

SOURCE HALF-LIFE — 30 years

GAMMA ENERGY — 0.662 Mev (from Barium 137 daughter)

CESIUM 134 CONTENT — less than 1%

RADIATION LEVELS IN CHAMBER

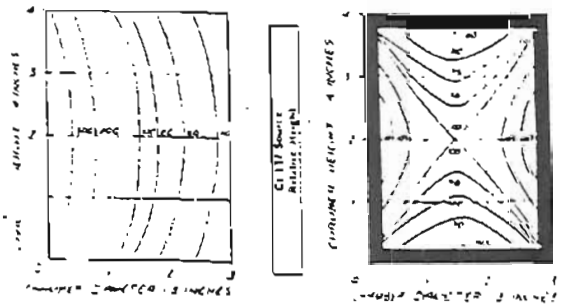

Chamber with Turntable Stationary — Chamber with Turntable Rotating

ISODOSE CURVES
RELATIVE DOSE RATE
(IN AIR)

OPERATION — Simplicity and safety are the key features. Material to be irradiated is placed in the plastic vial or cup and centered on the sample turntable. A small fractional horsepower motor, located inside the instrument housing, is turned on to rotate the turntable if dose rate averaging is desired. The irradiation chamber is then turned 180° by using the sample position handle on top until the sample receives the desired exposure rate. While most experiments will be conducted at the full irradiate position, it is possible to achieve lower exposure rates by not rotating the chamber through the complete 180° turn. Calibration curves are furnished with the instrument so you can select the proper degree of turn for lower dose rates. The exposure timer may be started as soon as the chamber is in the proper irradiation position. At the completion of the desired irradiation time as signalled by the "attention" bell, the timer should be turned off, the irradiation chamber revolved to the starting position, the motor shut off, and the sample removed.

CHAMBER DOSIMETRY — Radiation levels within the sample chamber decrease with distance from the line source, providing a maximum spatial variation of 7 to 1; sufficient to show the effect of exposure rate dependence or to perform attenuation experiments. Normally, rotation of the turntable will be used for exposure averaging to provide an exposure uniformity of ±5% across any horizontal plane. The most frequently used central 80% of the chamber volume is uniform to ±10%

Determination of absolute values were made both by condenser type R-chambers and by sodium formate capsules. Mapping of the field variations throughout the chamber was accomplished using sensitive miniature thermoluminescent rods and ribbons. (Courtesy of Harshaw Chemical Co.)

SOURCE SAFETY — The radioactive material is completely contained within two welded, stainless steel concentric capsules which are locked within a third cavity by a shielding plug.

The cesium isotope is first encased in a 20 mil stainless steel capsule which is welded closed. This capsule is then encapsulated in another stainless steel capsule which is heli-arc welded to exacting specifications. Each capsule must show no leakage under test conditions which are sensitive to 10^{-6} cc/sec. The doubly encapsulated source is set into a source holder tube which provides a third high integrity barrier between the radioactive material and the sample irradiation chamber. The source is held in this tube by a shielding plug which is locked into place by a high strength weld.

RADIATION PROTECTION — These irradiators have been designed to reduce the radiation reaching the exterior of the unit to such a low value that it can be used safely in an unrestricted area, as defined by U.S. Atomic Energy Commission regulations. The radiation levels are less than 0.5 mr/hr at 5 cm. from the surface of the outside shell.

NO INDUCED RADIOACTIVITY — The radioactive material itself, which emits the gamma ray, plays no direct part in the processing function. It does not affect food or other material being processed, just as a fire in a radio or TV transmitting station does not cause a fire in your home. The radioistotope is the transmitter, the material being processed is the receiver, the gamma rays are the processing mechanism. When material has been processed and is removed from the radiation field, it has been "turned off". It does not hold or retain gamma rays. It is not radioactive! It is as safe as the starting material, or safer.

LICENSING — The state or federal license (as applicable) is required to possess radioactive material in the quantity contained in Gammator irradiators. Details of the Gammator design have been registered with the U.S. Atomic Energy Commission, Division of Materials Licensing. This registration enables any responsible institution to obtain the necessary license rapidly.

K·S·E/RI's gammator B

BRINGS TO THE CLASSROOM the experimental capabilities of a nuclear laboratory.

Now students can learn by doing. For the first time it is possible to lift the study of radiation from the text book and bring it to life in the classroom.

Students may learn by direct experimentation about the extraordinary uses and effects of radiation. With the Gammator, students may explore the burgeoning new applications and industries which rely on radiation to achieve results that cannot be obtained by any other means.

curricula affected

BIOLOGY | CHEMISTRY | HOME ECONOMICS | PHYSICS



typical experiments

NATURE OF RADIATION — Ionization, effect on film, attenuation, absorption.

GENETICS — Observe effect on bacteria, molds, yeast, protozoa, fruit flies, chick and frog embryo, seeds, etc.

CELL EFFECTS — Observe how varying exposures produce sprout stimulation, sprout inhibition, and dormancy variation (potato, onion, wheat, grass).

BACTERIAL REDUCTION — Determine survival curves for insects, bacteria, fungi, molds.

FOOD PRESERVATION — Ionization equivalent of pasteurization and sterilization in achieving food purity.

CRYSTAL DEFECTS — Observe change in color and optical properties caused by energy absorption in glass. Demonstrate recovery through thermal annealing.

DYES — Demonstrate effect of radiation on dyes. Show how color change can be used as dosimeter.

PLASTICS — Demonstrate cross-linking of plastics, thermal stability.

the gamma irradiation story

The use of gamma radiation as a major new processing technique — in food processing, in medical supply sterilization, in chemical reactions, and in agriculture — is one more major step in rounding out the capability of radioisotopes as a beneficial servant of mankind. Its impact on food processing alone has such tremendous potential that it is described in government publications as "a revolution in food processing" and as the first new processing technique since thermal canning.

Until recently radioisotopes have served mankind primarily by acting as "tracer" — or "tagged" atoms. Their ability to behave in the same chemical or physical manner as their non-radioactive counter parts, and yet emit a characteristic signal to announce their location, has added greatly to our store of knowledge. In this manner radioisotopes are used as a "tool". Now they can perform a vastly different and even more important function — a processing method.

Progress in research by both industry and government in such areas as polymerization and a wide range of industrial applications indicates that gamma irradiation is on the threshold of significant expansion into a major industry. Such progress demands and is dependent upon the teaching of radiation in our schools.

K·S·E KEWAUNEE SCIENTIFIC ENGINEERING
Adrian, Michigan 49221 • Phone 313/263-5731

Appendix B-2. PHOTOGRAPHS

Photo Number	Photo Name	Page Number
P-1	NMRC Rockville Annex Building - Exterior	61-a
P-2	NMRC Rockville Annex Building - Room 114	61-b
P-3	NMRC Rockville Annex Building - Room 126	61-c
P-4	NMRC Rockville Annex Building - Room 201C	61-d
P-5	NMRC Rockville Annex Building - Room 213A	61-e
P-6	NMRC Rockville Annex Building - Room 213B	61-f
P-7	NMRC Rockville Annex Building - Room 213C	61-g

Photo P-1

NMRC Rockville Annex Building

Photo P-2

NMRC Rockville Annex Building - 114 (after plastic tape was used to generate grids on floor and walls)

Photo P-3

NMRC Rockville Annex Building - Room 126 (after plastic tape was used to generate grids on floor and walls)

Photo P-4

NMRC Rockville Annex Building - Room 201C (after plastic tape was used to generate grids on floor and walls)

Photo P-5

NMRC Rockville Annex Building - Room 213A (after plastic tape was used to generate grids on floor and walls)

Photo P-6

NMRC Rockville Annex Building - Room 213B (after plastic tape was used to generate grids on floor and walls)

Photo P-7

NMRC Rockville Annex Building - Room 213C (after plastic tape was used to generate grids on floor and walls)

APPENDIX C. STANDARD OPERATING PROCEDURES AND QUALITY ASSURANCE PROGRAM

Appendix C-1. Radiological D&D Action Plan Checklist

1. Select appropriate monitoring instruments and equipment and ensure satisfactory daily and weekly calibration checks for your selected instruments. Record serial numbers. Choose from:

_____ Ludlum Model 3 with pancake probe (beta)
_____ Ludlum Model 3 with 1inch diameter NaI probe (gamma)
_____ Ludlum with 2-inch diameter NaI probe (gamma)
_____ Cart-mounted gas proportional counter (beta; not H-3)
_____ Hand-held gas proportional counter (beta; not H-3)
_____ Liquid scintillation counter (beta and gamma)
_____ Gamma Counter (gamma)

2. Select materials to take to the scene. In addition to items you deem appropriate, the following items may be needed:

_____ tape measure or meter stick or yard stick
_____ water in a spray bottle
_____ zip lock bags to secure paper swipes after sampling
_____ pens, note pad, chalk
_____ D&D forms
_____ paper swipes
_____ masking tape and reinforced tape
_____ scissors
_____ tool kit

3. Pre-Survey Activities

_____ Review room layouts and floor diagrams for survey units to be monitored.
_____ Verify possession of room diagrams and generic grid diagrams.
_____ Select a list of random numbers for each survey unit that is classified as Impacted Class 3 (known RAM-use area).
_____ Use a grid map of the size closely fitting the size of the survey unit, mark the locations of the random measurements. Use the digits of each random number to simulate a position on the grid map.

_____ As soon as samples have been analyzed, assemble a D&D information package for submission to the Project Manager/Technical Writer. Your D&D information package should include:

(a) completed action checklist,
(b) floor plans and grid maps with locations of sample annotated on the grid,
(c) a completed summary sheet for the completed survey units,
(d) list or order of swipe sample loading and LSC data printouts, and
(e) a summary of deviations from procedures, problems encountered, and remediation actions, and other information (if applicable).

_____ Pre-label swipes for field sample collection; use a labeling technique that ensures the ability to track all samples throughout the collection and processing periods. Place the swipes for a particular area or room in a sealable plastic bag or fold the swipes into a latex glove after the swipe samples have been taken.

4. Survey and Monitoring Activities

_____ Prepare the survey unit (room, office, or other area)

(a) remedy safety or other items of concern that may impact your work,
(b) if necessary remove excess materials,
(c) if necessary, use masking tape, chalk lines or other means to mark grid lines within the survey unit

_____ Perform background data collection for each instrument that will be used; choose a non-radiation area where construction materials and environment is similar to the selected survey units; additional information:

(a) For scanning instruments, record the meters' responses after a 1-minute stability period; ensure proper battery check.
(b) For gamma and liquid scintillation counter background data collection, collect 21 samples for each counter, building and/or floor, if necessary.
(c) For scaler counts (gas proportional or NaI), record a select number of 1-minute background counts and desired-location counts.
(d) Perform background measurements on the day of selected measurements.
(e) The same background data can be used for multiple survey units.

_____ Perform scanning operations using appropriate instruments; hold the probe at a one to three inch distance from the floor or wall; scan at a rate of approximately one foot per second; annotate all "hot" spots on the survey grid map by recording the maximum observed reading. Record any readings other than background.

Appendix C-2. CHECKLIST FOR IMPACTED CLASS 3 AREAS OR SURVEY UNITS (known radiation use or storage locations)

Team Leader, Chief of Field Operations

1. Prepare grid floor maps and select random swipe locations (using sets of random numbers) and additional (control) swipe locations (as needed).

2. Grid the room (survey unit) and perform the swipes at the designated locations.

3. Oversee operations and monitor the day's progress.

4. Deliver swipe samples and survey summary sheets to the Chief of Office and Laboratory Operations for processing.

TEAM MEMBERS

1. Prepare the room or area for surveying. Remove debris and excess materials. Practice safety first. Remedy unsafe conditions before beginning survey efforts.

2. Label the background swipes -> B1 - B21. Perform the reference background swipes for each floor, if necessary. A set of background swipes is required for each floor and each day that swipes for impacted areas are collected. Collect the reference background samples from non-impacted areas in proximity to survey units to be surveyed.

3. Label the standard control swipes -> C1 - C5. Perform the standard controls: C1-floor inside room at door; C-2-floor outside room at door, C3-inside doorknob, C4-outside doorknob, and C5-inside light switch at door. Use additional controls as needed to ensure good swiping coverage in the survey unit.

4. Prepare a sketch of the room with door(s) and draw in lab benches or other built-ins.

5. Number the benches and proceed to perform additional control swipes -> staring with C6, C7, etc. or the consecutive C- number.

6. Using a survey meter, beta-gamma scan all drawers and shelves.

7. Using a survey meter, beta-gamma scan 50-100% of floor and wall areas.

8. Document the room number for the above actions; include date, serial numbers of meters, room number, and the total number of control (C1-C5, or other). Annotate quality control concerns or issues on survey summary sheets.

9. Verify the quantity and sequence of the swipes. Place the swipes in a latex glove and then insert into a labeled plastic bag when transporting samples. Deliver the swipes and other information to the Laboratory and Office Team leader for processing.

Appendix C-3. Checklist for Non-Impacted Areas or Survey Units (radiation-free labs, offices, lavatories, storage areas, closets, hallways, stairways, and other common areas and rooms)

Team Leader, Chief of Field Operations

1. Oversee operations and monitor the day's progress.

2. Deliver swipe samples and survey summary sheets to the Chief of Office and Laboratory Operations for processing.

Team Members

1. Prepare the room or area for surveying. Remove debris and excess materials. Practice safety first.

2. If impacted areas will be surveyed, label background swipes -> B1 - B21. Perform the reference background swipes for each floor, if necessary. Collect the reference background samples from non-impacted areas in proximity to survey units to be surveyed.

3. Label the standard control swipes -> C1 - C5. Perform the standard controls: C1-floor inside room at door; C-2-floor outside room at door, C3-inside door knob, C4-outside doorknob, and C5-inside light switch at door. Use additional controls as needed to ensure good swiping coverage in the survey unit.

4. Using a survey meter, beta-gamma scan 10-50% of floor and wall areas.

5. Document the room number for the above actions; include date, serial numbers of meters, room number, and the total number of control (C1-C5, or other). Annotate quality control concerns or issues on survey summary sheets.

6. Verify the quantity and sequence of the swipes. Place the swipes in a latex glove and then insert into a labeled plastic bag when transporting samples. Deliver the swipes and other information to the Office and Laboratory Team leader for processing.

Appendix C-4. Sample Collection Procedures

Team Leader, Chief of Office and Laboratory Operations

1. Perform daily quality control equipment and instrument checks before initiating the day's field and laboratory operations. Record appropriate data. Investigate and document observations that are outside the norm.

2. Ensure that adequate supplies are on hand, including swipes, liquid scintillation counter (LSC) fluid, batteries, calibrated meters and instruments, and other materials.

3. Coordinate the training of personnel who will assist in sample-analysis operations

4. Coordinate the servicing of equipment and instruments.

5. Audit swipe-sample packages and survey-summary sheets received from the Chief of Field Operations. Resolve inconsistencies or discrepancies before analyzing the samples using the laboratory liquid scintillation counter (LSC) or gamma counter.

6. Prepare the samples for evaluation by loading individual swipes into 7-milli-liter glass vials and topping off the vials with biodegradable liquid scintillation fluid or appropriate vials for gamma counting without topping off with fluid. Label the caps of each vial by assigning sequential numbers. Load the vials into racks into the LSC or gamma counter. For LSC evaluations, to prevent elevated results due to chemi-luminescence, store the samples for two to three hours out of ambient light before counting the samples. Chemi-luminescence may be attributed to the swipe or its contents interacting with the LSC fluid. For LSC evaluations, select and initiate the dual-dpm (H-3 and C-14) protocol for evaluating the swipe samples. For gamma counting samples, follow procedures provided in the vendor's operating manual.

7. Monitor the progress of the LSC operations during the swipe evaluations.

8. Remove the computer printout of the swipe evaluations. For each survey unit or data set, make appropriate annotations on the computer printout.

9. Review the data and the survey summary sheets to verify that they match. Resolve discrepancies.

10. Report all questionable observations, discrepancies and deviations from procedures.

11. Submit the LSC printout, grid maps, and survey summaries to the Quality Control Officer for review.

12. Assist the Quality Control Officer as needed.

Appendix C-5. Sample Control. Sample control procedures were implemented to ensure the integrity of samples, sample identification, collection, chain of custody, and retention.

1. Samples collected were traceable from the time collected through the analysis phase, during the retention period, and until they were disposed of properly.

   - Sample Custody: All samples collected were maintained under secure conditions. There were fewer than five individuals in the chain-of-custody.

   - Transfer of Custody and Shipment: Samples collected were delivered directly to the laboratory operations office.

   - Sample Packaging: Samples were collected, labeled, and placed in bags at the point of generation by trained personnel. These bags were brought directly to the laboratory operations office. The bags were opened and inventoried by the chief of laboratory operations before evaluation.

2. Samples were retained in storage for as long as feasible to support data analysis. Samples, when analyzed, were retained in secure storage until after final report review and then disposed.

Appendix C-6. Data Analysis Procedures

1. Survey information packets were delivered to the Quality Control Officer for review and incorporation into the final status report. The survey information packets consisted of computer printouts of liquid scintillation (LSC) counter or gamma counter results, grid maps (for impacted survey units), survey summary sheets, and other supportive information.

2. The number of samples to be collected for impacted class 3 areas were determined using guidance provided in MARSSIM and analysis results for a known contaminated area. The number of random, statistical data samples collected for each impacted area was 21. An exception to the 21 samples taken for an impacted area was when 100% of the grid locations were sampled. For each impacted area surveyed, 21 reference background samples were also collected. Additional swipes, called control swipes, were collected to ensure good coverage of sampling within a survey unit and to sample selected locations.

3. At least five control samples were collected for each impacted and non-impacted survey unit. These five control swipes were collected using a pre-selected set of locations within each survey unit.

4. For each impacted survey unit, applicable survey data was assembled and analyzed. This data consisted of reference background data, direct surface readings, scanning results, and LSC swipe evaluations. The direct surface readings required conversion from cpm values to readings in dpm per 100 cm^2. After the data conversion of the direct readings, all survey data was then compared directly to the NMRC direct reading action limit of 2,000 dpm. The NMRC action limit represented a value that was a small fraction of the NMRC screening values or DCGLs. Scanning results were called satisfactory when results did not exceed two to three times the background readings. Any individual reading that exceeded the NMRC action limit or the scanning limit was further investigated. For any area exceeding the limits, remediation efforts were completed until subsequent surveys yielded results that were below NMRC action limits. Additional scanning and swipes were completed as deemed

necessary. All results have been included in this final report.

5. For non-impacted survey units (common areas, offices, storage rooms, halls, and stairs), control swipes for selected areas were collected and analyzed. In addition, 10-50% of the floor area was beta-gamma scanned.

6. All original computer printouts, grid maps, survey summary sheets and applicable documents have been maintained for inclusion in permanent, radiation-safety-program files.

7. Grid maps with applicable sample locations have been included in this final report.

8. All data entries in the final report were verified (for accuracy and completeness) by at least two persons on the D&D team.

Appendix C-7. Equipment and Instrument Procedures

1. All equipment and instruments designated for use in NMRC radiological D&D operations were properly calibrated and kept in a secure location when not in use. Operators were trained in the proper use of the equipment and instruments.

2. Daily operational and check-source tests were performed and documented by trained personnel.

3. Radiation equipment and instruments were used for direct surveys, scanning, and sample analyses.

   a. FIXED CONTAMINATION MEASUREMENTS. Direct surveys or measurements for fixed contamination were performed using a portable gas proportional detector. Prior to its daily quality control tests, the detector was purged with gas per the manufacturer's operating procedures. Readings for one-minute samples were collected for desired locations. The primary isotopes of concern were Carbon-14 and Sulfur-35.

   b. WALK-THROUGH SURVEYS. Scan surveys were performed using portable, Geiger-Mueller (GM) meters with either pancake probes or gamma scintillation probes. The beta-gamma scanning consisted of walk-through surveys carried out by holding the detector probe approximately one to two inches above the floor or area and walking slowly (about one foot per second) through the specific site—stopping when increases in count rates were observed. Areas where the count rates exceeded two to three times background were investigated by a more detailed survey in the suspect area. Scanning practices included using the audible response of the meter for detection and, after stabilization, using the meter response for measurement. The primary isotopes of concern included Carbon-14, Sulfur-35, Phosphorus-32 and Chromium-51.

   c. REMOVABLE SURFACE CONTAMINATION SURVEYS (Swipes/Smears and Swabs). Swipes (swipes, smears and swabs) were collected as deemed necessary to determine if radioactivity above the limit was removable (or loose). Swipes were performed by lightly misting the area with a water spray and wiping

a 100 cm^2 surface (applying moderate pressure) with a dry filter paper (swipe/smear/swab). Swipes were evaluated using a liquid scintillation or gamma counter, depending upon the isotopes of concern for the survey unit. For liquid-scintillation-counter evaluations, tritium (H-3) and Carbon-14 were the principal isotopes of concern.

4. Information about the D&D radiological monitoring equipment and instruments is provided in Appendix D. Documents summarizing instrument calibrations and specifications are provided in Appendix D.

Appendix C-8. Source-Standards, Background-Standards, and Reference-Background Measurements

1. All available source standards (Hydrogen-3, Carbon-14, and Iodine-129) and background standards were collected for use during the duration of the radiological decontamination and decommissioning operations.

2. NIST-traceable, source standards (Carbon-14 and Cobalt-60) were purchased and kept stored in a secure location. Only trained and authorized personnel handled the check sources and used the sources to verify proper instrument response to radioactivity.

3. Daily-check-source and operational calibration checks were performed. Document results, maintaining logs and control charts as necessary.

4. Inventories and leak tests of check sources were performed, at least semi-annually. The leak tests and documentation satisfied regulatory requirements.

5. Information about the various check sources used during the D&D effort is provided in Appendix D.

APPENDIX D. QUALITY ASSURANCE INFORMATION AND DATA

Appendix D-1. Training Information and Certificates

All personnel who participated in radiological decontamination and decommissioning (D&D) efforts received a level of training commensurate with the work assignments and level of participation. The incumbent Radiation Safety Officer, LCDR S. L. Gaiter, held the primary D&D positions of Decommissioning Officer and Quality Control Officer. The Chief of Office and Laboratory Operations was the incumbent Assistant Radiation Safety Officer, Mr. Saifeddin Ahmad. The Chief of Field Operations, Mr. Willie Deadwyler, had previously held numerous positions as a Navy radiation health technician. The personnel listed above received basic radiation safety training and instrument training in conjunction with their participation in NMRC D&D efforts. Mr. Glen Garth and Mr. Rodney McGhee received basic radiation safety training and on-the-job training. Mr. Garth and Mr. McGhee worked under the direct supervision of Mr. Ahmad or Mr. Deadwyler. Ms. Carolyn Hall served as the Project Coordinator and Editor. Her assignments were completed in an office environment or infrequent visits to the field. LCDR Gaiter or Mr. Ahmad performed all radiological materials-handling and decontamination work.

Document D-1 provides training and experience information for LCDR Gaiter. **Documents D-2** through **D-11** provide pertinent radiation safety training certificates for the participants in the NMRC radiological D&D efforts. **Table D-1** lists the training documents included in this final report.

Table D-1. TRAINING INFORMATION AND CERTIFICATES

Document Number	Training Certificate or Form
D-1-1	Training and Experience of Authorized Radioisotope User, LCDR Gaiter
D-1-2	Radiation Safety Training, LCDR Gaiter
D-1-3	Ludlum Measurements Instruments, LCDR Gaiter
D-1-4	Radiation Safety Training, Mr. Ahmad
D-1-5	Ludlum Measurements Instruments, Mr. Ahmad
D-1-6	Radiation Safety Training, Mr. Deadwyler
D-1-7	Ludlum Measurements Instruments, Mr. Deadwyler
D-1-8	Radiation Safety Training, Ms. Hall
D-1-9	Ludlum Measurements Instruments, Ms. Hall
D-1-10	Radiation Safety Training, Mr. Garth
D-1-11	Radiation Safety Training, Mr. McGhee

DOCUMENT D-1-1. TRAINING AND EXPERIENCE OF AUTHORIZED RADIOISOTOPE USERS
(TYPE OR PRINT LEGIBLY)

A. GENERAL INFORMATION

AUTHORIZATION NUMBER:	DATE OF APPLICATION: 31 March 1999
NAME OF AUTHORIZED USER *(LAST, FIRST, MI)* **Gaiter, Schleurious L.**	RANK / GS GRADE: LCDR, MSC,USN
ORGANIZATION / ORGANIZATION DIVISION: Naval Medical Research Center, Safety Program	BUILDING AND ROOM NUMBER: All NMRC Bethesda and Rockville Buildings

B. CERTIFICATIONS N/A

SPECIALTY BOARD	CATEGORY	DATE CERTIFIED
American Academy of Health Physics	Part I of II (Associate Member status)	7/1995

C. FORMAL EDUCATION

TYPES OF LICENSES : None

TERRITORY OR STATE IN WHICH LICENSED *(MD, DDS, DVM, ETC): N/A*

HIGHER EDUCATIONAL INSTITUTIONS ATTENDED	MAJOR COURSE OF STUDY AND DATES ATTENDED	DEGREE, DIPLOMA OR CERTIFICATE RECEIVED AND DATE
Florida Community College (FCC), Jacksonville, FL	Pre-Engineering	Associate in Arts, 4/1978
University of Florida (UF), Gainesville, FL	Chemical Engineering	B.S. Chemical Engineering, 12/1981
University of Florida (UF)	Chemical Engineering	Master of Science, 4/1983
Georgetown University (GU) Washington, DC	Radiation Science	Master of Science, 2/1995

D. TRAINING RECEIVED IN BASIC RADIOISOTOPE HANDLING TECHNIQUES

FIELD OF TRAINING A	LOCATION AND DATES OF TRAINING *(INCLUDE COURSE TITLE IF KNOWN)* B	TYPE AND LENGTH OF TRAINING LECTURE/ LABORATORY COURSES *(HOURS)* C	SUPERVISED LABORATORY EXPERIENCE *(HOURS)* D
1. RADIATION PHYSICS AND INSTRUMENTATION	Navy Radiation Health Officer Course, 1988 Radiologic Physics I, GU, 1991 Health Physics, GU, 1992 Radiation Detection, GU, 1993 Radiation Dosimetry, GU, 1993 Health Physicist/Instructor, Armed Forces Radiobiology Research Institute (AFRRI), Bethesda, MD, Radiation Safety Officer, NMRC, Bethesda	160 hours 30 hours 30 hours 20 hours lectures; 20 hours lab experience 20 hours lectures; 20 hours lab experience work experience (1990-1995) work experience (1995-1999)	
2. RADIATION PROTECTION	Navy Radiation Health Officer Course, 1988 Operational Health Physics, GU, 1992 Radiation Biology, GU, 1993 Health Physicist/Instructor, AFRRI Radiation Safety Officer, NMRC, Bethesda	160 hours 30 hours 30 hours work experience (1990-1995) work experience (1995-1999)	
3. MATHEMATICS PERTAINING TO THE USE AND MEASUREMENT OF RADIOACTIVITY	Navy Radiation Health Officer Course, 1988 Radiologic Physics I, GU, 1991 Health Physics, GU, 1992 Health Physics Internships I and II Radiation Detection, GU, 1993 Radiation Dosimetry, GU, 1993 Health Physicist/Instructor, AFRRI Radiation Safety Officer, NMRC, Bethesda	160 hours 30 hours 30 hours 150 hours laboratory experience 20 hours lectures; 20 hours lab experience 20 hours lectures; 20 hours lab experience work experience (1990-1995) work experience (1995-1999)	
4. RADIATION BIOLOGY	Radiation Biology, GU, 1993 Medical Effects of Nuclear Weapons Courses, AFRRI, 1990-1995	30 hours 300 hours	
5. RADIOPHARMACEUTICAL CHEMISTRY	N/A	N/A	

PAGE 1

E. ACTUAL EXPERIENCE WITH RADIOISOTOPES (SEALED AND/OR UNSEALED SOURCE)

ISOTOPE	MAXIMUM AMOUNT	WHERE EXPERIENCE WAS GAINED	DURATION OF EXPERIENCE	TYPE OF USE
Cobalt-60 (sealed) Cesium-137 (sealed)	150,000 Ci 14,500 Ci	AFRRI, Bethesda, MD NMRC, Bethesda, MD	1990-1995 1995-1999	Open-air irradiations Closed-chamber irradiations; provided training to users
H-3 C-14 P-32 P-33 Ca-45 Cr-51 I-125	50 Ci 10 Ci 10 Ci 25 mCi 10 mCi 5 Ci 1 Ci	NMRC, Bethesda, MD	1995-1999	Receipt, handling, monitoring and disposal of unsealed materials for use by Authorized Users performing biomedical research efforts

F. EXPERIENCE WITH RADIATION PRODUCING DEVICES *(X-RAY MACHINES, IRRADIATORS, ETC.)*

DEVICES	WHERE EXPERIENCE WAS GAINED	DURATION OF EXPERIENCE	TYPE OF USE
Gamma Irradiators (Cesium-137) Shepherd Mark I (9000 Ci) Best Industries Model (2500 Ci) Isomedix Gammator Unit (300 Ci)	NMRC, Bethesda, MD	1995-1999	Train personnel and maintain units for use by staff scientist, technicians, and other researchers to irradiate specimens, non-human animals, cells, etc.

G. CERTIFICATION

I CERTIFY THAT THE ABOVE INFORMATION PROVIDED HEREON IS TRUE AND COMPLETE TO THE BEST OF MY KNOWLEDGE.

SIGNATURE OF APPLICANT DATE SIGNED

PAGE 2 TRAININING AND EXPERIENCE OF AUTHORIZED RADIOISOTOPE USERS

Certificate of Training

This Certifies That

Schleurious Gaiter

has successfully completed the 1-day course of instruction for

Radiation Safety Training

February 23, 2000

Presented By

CSI-Radiation Safety
481 North Frederick Avenue, Suite 302
Gaithersburg, Maryland 20877

For

Naval Medical Research Center
Bethesda, MD

Ray Johnson

Raymond Johnson, C.H.P., P.E.
Training Director

Certificate of Completion

This certifies that

Schleurious Gaiter

has successfully completed a 8 hour training session on Calibration and Repair of Ludlum Measurements Instruments.

Given on December 20, 1999

Donald G. Ludlum
President
Ludlum Measurements, Inc

Certificate of Training

This Certifies That

Saifeddin Ahmad

has successfully completed the 1-day course of instruction for

Radiation Safety Training

February 23, 2000

Presented By

CSI-Radiation Safety
481 North Frederick Avenue, Suite 302
Gaithersburg, Maryland 20877

For

Naval Medical Research Center
Bethesda, MD

Ray Johnson

Raymond Johnson, C.H.P., P.E.
Training Director

Certificate of Completion

This certifies that

Saifedlin Ahmad

has successfully completed a 8 hour training session on Calibration and Repair of Ludlum Measurements Instruments.

Given on December 20, 1999

Donald G. Ludlum
President
Ludlum Measurements, Inc.

Certificate of Training

This Certifies That

Willie Deadwyler

has successfully completed the 16-hour course of instruction for

Fundamentals of Radiation Safety

November 9-10, 1999

Presented By

CSI-Radiation Safety Training
481 North Frederick Avenue, Suite 302
Gaithersburg, Maryland 20877

in association with

Radiation Service Organization, Inc.
Post Office Box 1526
Laurel, Maryland 20725

Ray Johnson

Raymond Johnson, C.H.P., P.E.
Training Director

Certificate of Completion

This certifies that

Willie Deadwyler

has successfully completed a 8 hour training session on Calibration and Repair of Ludlum Measurements Instruments.

Given on December 20, 1999

Donald G. Ludlum
President
Ludlum Measurements, Inc.

Certificate of Training

This Certifies That

Carolyn Hall

has successfully completed the 16-hour course of instruction for

Fundamentals of Radiation Safety

November 9-10, 1999

Presented By

CSI-Radiation Safety Training
481 North Frederick Avenue, Suite 302
Gaithersburg, Maryland 20877

in association with

Radiation Service Organization, Inc.
Post Office Box 1526
Laurel, Maryland 20725

Raymond Johnson, C.H.P., P.E.
Training Director

Certificate of Completion

This certifies that

Carolyn Hall

has successfully completed a 8 hour training session on Calibration and Repair of Ludlum Measurements Instruments.

Given on December 20, 1999

Donald G. Ludlum
President
Ludlum Measurements, Inc

Certificate of Training

This Certifies That

Glen Garth

has successfully completed the 1-day course of instruction for

Radiation Safety Training

February 23, 2000

Presented By

CSI-Radiation Safety
481 North Frederick Avenue, Suite 302
Gaithersburg, Maryland 20877

For

Naval Medical Research Center
Bethesda, MD

Ray Johnson

Raymond Johnson, C.H.P., P.E.
Training Director

Certificate of Training

This Certifies That

Rodney McGhee

has successfully completed the 1-day course of instruction for

Radiation Safety Training

February 23, 2000

Presented By

CSI-Radiation Safety
481 North Frederick Avenue, Suite 302
Gaithersburg, Maryland 20877

For

Naval Medical Research Center
Bethesda, MD

Ray Johnson

Raymond Johnson, C.H.P., P.E.
Training Director

SEAL
1994

Appendix D-2. Service and Calibration Certificates for Instruments, Equipment, and Check Sources

Table D-2 lists the service and calibration certificates for the instruments, equipment and check sources used in the D&D effort described in this final report.

Table D-2. SERVICE AND CALIBRATION CERTIFICATES FOR INSTRUMENTS, EQUIPMENT AND CHECK SOURCES

Document Number	Service and/or Calibration Certificate
D-2-1	Packard Liquid Scintillation Counter, S/N 403848, 4/5/99
D-2-2	Packard Liquid Scintillation Counter, S/N 403848, 3/10/00
D-2-3	Packard Liquid Scintillation Counter, S/N 403848, 4/6/00
D-2-4	Statement of Data Analysis by Packard, 4/7/00
D-2-5	EG&G Wallac, Inc. Gamma Counter, S/N 82-324, 8/23/99
D-2-6	Bicron Meter, S/N B602G, 7/22/99
D-2-7	Ludlum Model 3, S/N 54537, 7/22/99
D-2-8	Ludlum Model 3, S/N 114886, 7/22/99
D-2-9	Ludlum Model 3, S/N 121461, 8/12/99
D-2-10	Ludlum Model 3, S/N 121816, 2/22/00
D-2-11	Ludlum Model 3, S/N 132946, 2/22/00
D-2-12	Certificate of Participation, Reports of Traceability to NIST, Analytics, Inc., 1999
D-2-13	Certificate of Calibration, Analytics, Inc., Carbon-14 check source, S/N 58806A-530
D-2-14	Certificate of Calibration, Analytics, Inc., Carbon-14 check source, S/N 58807-530
D-2-15	Certificate of Calibration, Analytics, Inc., Cobalt-60 check source, S/N 58808-530
D-2-16	Certificate of Calibration, Analytics, Inc., Cobalt-60 check source, S/N 58809-530
D-2-17	Certificate of Calibration, Ludlum Measurements, Inc., Model 2350-1, S/N 157674, Gas Proportional Unit with Detectors
D-2-18	Certificate of Calibration, Ludlum Measurements, Inc., Model 2350-1, S/N 157669, Gas Proportional Unit with Detectors

Packard
A Packard Company

CUSTOMER NAME: S. Ahmad

CUSTOMER TEL: (3 295-0002

RECEIPT FOR SERVICE

BILL TO:

DIST	TERR	ZONE	PAYEE NO.	CUSTOMER NUMBER	SERV ORDER #
433	31	1	064316		6 405442

DEPARTMENT: Bldg. 17 Receipts Control Section Room S-20

PACKARD SYSTEM SERIAL NUMBER: B25001 - 403848

INSTITUTION'S NAME: Naval Medical Research Center

RIC SYSTEM SERIAL NUMBER: - - - - - 9

ADDRESS: 8901 Wisconsin Avenue

CALL NUMBER: 82933

CITY: Bethesda STATE: MD COUNTRY: ZIP: 20889-5607

COPY TO:

DATE OF SERVICE MO	DAY	YEAR	SERVICE HOURS	TRAVEL HOURS
4	5	99	1 0	2 5
TOTALS			1 0	2 5

ITEM #	PART NUMBER OF REPLACED ITEM	PART DESCRIPTION	QUANTITY	UNIT PRICE	TOTAL PRICE
1	165507 5	Printer ribbon cartridge	1	27 00	27 00
2					
3					
4					
5					
6					
7					
8					
9					
10					

PARTS TRANSFER ITEM _____ PAYEE # _____ TOTAL MATERIAL 27 00

SUMMARY OF CHARGES TO CUSTOMER

ITEM	HOURS	RATES	CHARGES
ZONE ___ MIN.	1 0	350.00	350 00
LABOR			
SUB TOTAL			350 00
MATERIAL			27 00
SHIPPING CHARGES			
VENDOR CHARGES			
SUB TOTAL			27 00
TRAVEL			
TAX			
MISC.			
TOTAL			377 00

EXPLANATION: Instrument Calibration and preventative maintenance. Normalize/Calibrated. Cleaned and lubricated printer, replaced ribbon. Cleaned fan filter, checked cooling fans. Blew dust from keyboard & detector & static controller. Cleaned sample changer deck & monitor face. Adjusted drag plate tension detector and to improve sample changer operation. Inspected and lubricated external std. Checked and reset error log; Approx. 3,319 elevator cycles since 27 Apr 98.

^{3}H EFF. 66.6% BKG. 7 CPM

^{14}C EFF. 96.4% BKG. 23 CPM

^{125}I EFF. _____ BKG. _____

CUSTOMER'S P.O. (IF MISSING EXPLAIN) N3239899RC77019

CUSTOMER SIGNATURE: Saifuddin Ahmad

TSE SIGNATURE: Robert L Palmer

REASON FOR SERVICE PRIMARY	SECONDARY	TYPE OF SERVICE
0 OPERATOR ERROR 1 POWER SUPPLY 2 MECHANICAL/ ELECTROMECHANCIAL 3 ANALOG 4 DIGITAL 5 SOFTWARE & FIRMWARE 6 UPDATE 7 NO PROBLEM FOUND	0 INCORRECT OPERATION 1 OUTSIDE SYSTEM SPECS 2 ADJUST 3 REPAIR 4 REPLACE 5 MECHANICAL 6 ANALOG 7 DIGITAL 8 SOFT & FIRMWARE 9 OTHER (PLEASE EXPLAIN)	44 LOAN 50 WARRANTY 51 ENG. CHANGES 52 TRAINING / APPLICATION SUPPORT 55 INSTALLATION 63 SALES ASSIST / DEMO / SHOW 6C COMPREHENSIVE AGREEMENT (1) 64 COMPREHENSIVE AGREEMENT (2) 6D DEPOT REPAIR 6L LIMITED USE AGREEMENT 6P PM ONLY AGREEMENT 68 BILLABLE SERVICE 69 PREVENTIVE MAINTENANCE 71 SALE
7	9	6 8

CUSTOMER COPY

Packard
A Packard BioScience Company

CUSTOMER NAME: S. AHMAD

CUSTOMER TEL: 301-295-0002

RECEIPT FOR SERVICE

BILL TO: RECEIPT CONTROL SECTION
N.M.R.C.

DEPARTMENT 8401 WISCONSIN AVE.
BLDG 17, RM. 132 BETHESDA, MD 20889-5607

INSTITUTION'S NAME
NAVAL MEDICAL RESEARCH CTR.

ADDRESS 8401 WISCONSIN AVE
RADIATION SFTY. BLDG 17, ROOM 10

CITY: BETHESDA STATE: MD COUNTRY: ZIP: 20889-5607

DIST	TERR	ZONE	PAYEE NO	CUSTOMER NUMBER	SERVICE ORDER #
413		1	05430		6 412773

PACKARD SYSTEM SERIAL NUMBER: B2500-403848

RIC SYSTEM SERIAL NUMBER: 9

CALL NUMBER

COPY TO:

DATE OF SERVICE MO	DAY	YEAR	SERVICE HOURS	TRAVEL HOURS
3	10	00	60	25
TOTALS				

ITEM #	PART NUMBER OF REPLACED ITEM	PART DESCRIPTION	QUANTITY	UNIT PRICE	TOTAL PRICE
1					
2					
3					
4					
5					
6					
7					
8					
9					
10					

PARTS TRANSFER ITEM ____ PAYEE # ____ TOTAL MATERIAL

SUMMARY OF CHARGES TO CUSTOMER

ITEM	HOURS	RATES	CHARGES
ZONE 1 MIN.	10	390	390 00
LABOR	50	195	975 00
SUB TOTAL			1365 00
MATERIAL			
SHIPPING CHARGES			
VENDOR CHARGES			
SUB TOTAL			
TRAVEL			
TAX			
MISC.			
TOTAL			1365 00

EXPLANATION: INSPECTED COUNTER. CLEANED DETECTOR ASSEMBLY. CLEANED AND LUBRICATED SAMPLE CHANGER. CALIBRATED HIGH VOLTAGE CHECKED 3H & C14 EFFICIENCIES.
NOTE:
ALTHOUGH THIS COUNTER IS NOT Y2K COMPLIANT (CORRECT DATE CANNOT BE ENTERED.); THE CORRECTED DPM VALUES FOR 3H AND C14 ARE CORRECT. THE 3H AND C14 QUENCH CURVES INSTALLED ARE NOT DEPENDANT UPON A DATE, BUT ARE DEPENDENT UPON THE ACTUAL DPM'S IN THE QUENCH STDS AT THE TIME THE CURVES WERE INSTALLED

3H EFF. 60.9% BKG. 16
14C EFF. 96.3% BKG. 20
I125 EFF. ____ BKG. ____

CUSTOMER'S P.O. (IF MISSING EXPLAIN) N3239800RC72023

CUSTOMER SIGNATURE Safeddin Ahmad 10/3/00

TSE SIGNATURE Bob McAllister

REASON FOR SERVICE

PRIMARY	SECONDARY
0 OPERATOR ERROR	0 INCORRECT OPERATION
1 POWER SUPPLY	1 OUTSIDE SYSTEM SPECS
2 MECHANICAL/ ELECTROMECHANCIAL	2 ADJUST
3 ANALOG	3 REPAIR
4 DIGITAL	4 REPLACE
5 SOFTWARE & FIRMWARE	5 MECHANICAL
6 UPDATE	6 ANALOG
7 NO PROBLEM FOUND	7 DIGITAL
	8 SOFT & FIRMWARE
	9 OTHER (PLEASE EXPLAIN)

TYPE OF SERVICE

44 LOAN
50 WARRANTY
51 ENG. CHANGES
52 TRAINING / APPLICATION SUPPORT
55 INSTALLATION
63 SALES ASSIST / DEMO / SHOW
6C COMPREHENSIVE AGREEMENT (1)
64 COMPREHENSIVE AGREEMENT (2)
6D DEPOT REPAIR
6L LIMITED USE AGREEMENT
6P PM ONLY AGREEMENT
68 BILLABLE SERVICE
69 PREVENTIVE MAINTENANCE
71 SALE

68

CUSTOMER COPY

Packard
A Packard Company

CUSTOMER NAME: NNMC

CUST R TEL:

RECEIPT FOR SERVICE

BILL TO:	DIST	TERR	ZONE	PAYEE NO.	CUSTOMER NUMBER	SERV. ORDER #
	413	32	1	3364		6 404587

DEPARTMENT	PACKARD SYSTEM SERIAL NUMBER
	-40384 8

INSTITUTION'S NAME	RIC SYSTEM SERIAL NUMBER
	- - - - - 9

ADDRESS	CALL NUMBER
	95258

CITY	STATE	COUNTRY	ZIP	COPY TO:

DATE OF SERVICE MO	DAY	YEAR	SERVICE HOURS	TRAVEL HOURS
04	06	00	2 00	1 00
TOTALS				

ITEM #	PART NUMBER OF REPLACED ITEM	PART DESCRIPTION	QUANTITY	UNIT PRICE	TOTAL PRICE
1					
2					
3					
4					
5					
6					
7					
8					
9					
10					

PARTS TRANSFER ITEM_____ PAYEE #_____ TOTAL MATERIAL

SUMMARY OF CHARGES TO CUSTOMER			
ITEM	HOURS	RATES	CHARGES
ZONE_____ MIN.			
LABOR			
SUB TOTAL			
MATERIAL			
SHIPPING CHARGES			
VENDOR CHARGES			
SUB TOTAL			
TRAVEL			
TAX			
MISC.			
TOTAL			

EXPLANATION: Removed sample changer deck. Removed and checked PMT's. Reseated PMT's in sockets. Checked mechanical movement of elevator. Cleaned cocktail from elevator body. Re-~~assembled~~ connected instrument. Performed customers QC test x 5AC. Results looked good

CUSTOMER'S P.O. (IF MISSING EXPLAIN)

CUSTOMER SIGNATURE

TSE SIGNATURE

REASON FOR SERVICE PRIMARY	SECONDARY	TYPE OF SERVICE
0 OPERATOR ERROR 1 POWER SUPPLY 2 MECHANICAL/ ELECTROMECHANCIAL 3 ANALOG 4 DIGITAL 5 SOFTWARE & FIRMWARE 6 UPDATE 7 NO PROBLEM FOUND	0 INCORRECT OPERATION 1 OUTSIDE SYSTEM SPECS 2 ADJUST 3 REPAIR 4 REPLACE 5 MECHANICAL 6 ANALOG 7 DIGITAL 8 SOFT & FIRMWARE 9 OTHER (PLEASE EXPLAIN)	44 LOAN 50 WARRANTY 51 ENG. CHANGES 52 TRAINING / APPLICATION SUPPORT 55 INSTALLATION 63 SALES ASSIST / DEMO / SHOW 6C COMPREHENSIVE AGREEMENT (1) 64 COMPREHENSIVE AGREEMENT (2) 6D DEPOT REPAIR 6L LIMITED USE AGREEMENT 6P PM ONLY AGREEMENT 68 BILLABLE SERVICE 69 PREVENTIVE MAINTENANCE 71 SALE
7	5	6 8

^{3}H EFF. 60 BKG. 10

^{14}C EFF. 96.0 BKG. 15.9

^{125}I EFF._____ BKG._____

CUSTOMER COPY

Packard
A Packard BioScience Company

DATE:04/07/2000

FAX# 301-295-5651

TO: Dr. Jaifeddin Ahmad

FROM: TOM GERBER

RE: Packard B2500 LSA

I have analyzed your data and have found the data to be in control. The procedure that I used was to take 2 square roots of the mean and look for random events on both sides of the mean. The data should stay within 677 counts 95 % of the time. It passes this test quite well. An assumption that I made is that the CPM value was taken at 1 minute.

Thank you,
Tom Gerber

EG&G WALLAC, INC.
9238 Gaither Rd, Gaithersburg, Maryland 20877 (800) 638-6710

SERVICE REPORT

39915

Q. A. DATA

AGE - MONTHS		
	0-3	4-11

REPAIR DATE MO. DAY YR.	JOB NUMBER	EMPLOYEE NO.
8/23/99	115615	9663

INSTRUMENT LOCATION

USER: Radiation Safety
TELEPHONE: (301) 2950002
ORGANIZATION: Naval Medical Research Ctr.
DEPARTMENT: BLD 17, Rm 516
STREET: 8901 Wisconsin Ave
CITY: Bethesda STATE: MD ZIP: 20889

MODEL	SERIAL	DEPART	ARRIVE	COMPLETE	PROBLEM	REPAIR
1282	820324	8 00	9 00	11 00	21	21

☒ P. O. NO. ☐ WARRANTY ☐ CONTRACT ☐ RENTAL
NUMBER

IF INCOMPLETE:

DEPART	ARRIVE	COMPLETE

PROBLEM CODES

01 NO FAULT
02 OPERATOR ERROR
03 SCHEDULED PREVENTIVE MAINTENANCE
04 UNKNOWN FAILURE
10 MECHANICAL ADJUSTMENT FAILURE
11 MECHANICAL COMPONENT FAILURE
20 ELECTRICAL ADJUSTMENT FAILURE
21 ELECTRICAL COMPONENT FAILURE
30 SOFTWARE FAILURE INSTRUMENT
31 SOFTWARE FAILURE INTERNAL
40 REAGENT FAILURE

REPAIR CODES

01 NO ACTION
02 TRAINED AND REPEAT
03 PREVENTIVE MAINTENANCE
10 ADJUST MECHANICS
11 REPLACE MECHANICAL PARTS & ADJUST
20 ADJUST ELECTRONICS
21 REPLACE ELECTRICAL COMPONENTS & ADJUST
30 REBOOT INSTRUMENT
31 REBOOT COMPUTERS
32 REPLACE FAULTY SOFTWARE
33 UPGRADE TO NEW VERSION SOFTWARE
40 REPEAT ASSAY
41 REPLACE REAGENT

PROBLEM

PM
WILL NOT INITIALIZE!
(BAD CPU Bd - ECC)

ACTION TAKEN

Replaced ECC Bd BAD Power Switch, checked Alignments, Conveyor, Teeth, cleaned, counting chamber, checked Efficiency F-129: 64.5%
Background: 42

SOFTWARE VERSION: ULTIMATE III V1.5
DVM

PARTS USED

QUAN	DESCRIPTION	PART NUMBER	UNIT PRICE	TOTAL PRICE
1	ECC Bd CPU	10847527	605 00	605 00
1	Power Switch	11845021	12 00	12 00

TOTAL PARTS $ 617 00

TOTAL LABOR $ 350 00

LABOR HOURS 2 @ $ 175 00

OTHER CHARGES (Description)

$

TRAVEL ZONE 1 CHARGE $ 125 00

TOTAL CHARGE ▶ $ 1142 00

I/O DEVICES AND BETA PLATE ACCESSORIES

PART NUMBER	S/N
COMPUTER	USER
MONITOR	USER

ALL WORK HAS BEEN DONE TO MY SATISFACTION AND THE EQUIPMENT IS IN ACCEPTABLE WORKING CONDITION UNLESS CALL IS MARKED INCOMPLETE.

Saifeddin Ahmed
CUSTOMER SIGNATURE

HRC
ENGINEER INITIALS

EG&G WALLAC

Gamma Preventive Maintenance

Wallac Inc.
9238 Gaither Road
Gaithersburg, MD 20877
(800) 638-6710

Date 8-23-99 Engineer Harry Collins
Job # 115615 Contract # None
Model 1282 Serial # 820 324
Instrument Software Version ULTRATERM III Ver 1.5

(Leave yellow copy of this PM form and spectrum plot inside the instrument.)

BEFORE PM		AFTER PM		SPECTRUM PLOT	
I-129 Efficiency	64.5 %	I-129 Efficiency	64.5 %	I-129	☐
Background	42 cpm	Background	40 cpm	CS137	☐

MECHANICAL TESTS			ELECTRICAL TESTS		
Counterweights		☒	Sensors		☒
Tube Shields		☒	Display/Keyboard		☒
Elevator Tips/Forks		☒	ID Decoder		☒
Conveyor	Belts	☒	Power Line	120 vac	☒
	Chains/Teeth	☒	Low Volt DC	+/- 5 +/- 12	☒
	Clutches	☒	Battery		☒
	Motors/Brakes	☒	Master Clear	15.79 vdc	☒
Lubrication	Elevator	☒	Power Up	9.57 vdc	☒
Sensors	Levers	☒	High Voltage		
	Position	☒	1 1033 2 3 4 5		
Test Meter			6 7 8 9 10		
Model	Kluke 75		11 12 13 14 15		
Serial #	55660519		16 17 18 19 20		

1260/1261		1470	
Sample Switch	☐	Fan	☐
Detector LED Grounds	☐	Video	☐
1282		Power Switch	☐
Fan	☒	Disk Drives	☐
Slide Arm	☒	Robotics	☐

I/O DEVICES AND SOFTWARE		TESTS	
Printer		Printout Clarity	☐
Model	Serial #	Ribbon	☐
		Mechanical (gears, platen, motors, print head)	☐
		Cables	☐
VDU/PC		Fan	☐
Model	Serial # USER	Keyboard	☐
Monitor		Disk Drives	☐
Model	Serial # USER	Video	☐
		Cables	☐
Computer Software			
Type	ULTRATERM III	Version	1.5

Customer's Signature Saifeddin Ahmad

Engineer's Signature Harry R. Collins

DOC 4.09.035 Rev. 2

White Copy - Customer *Yellow Copy - With Instrument* *Pink Copy - Instrument File*

RSO, Inc.
P.O. Box 1526
Laurel, MD 20725
(301) 953-2482

RSO Order No. 1315

Certificate of Calibration

ISSUED TO: Naval Medical Research
Bethesda, MD 20889-5607
CONTACT: HM3 AHMAD
PHONE: (301) 295-0001

PO NO:

INSTRUMENT: BICRON
MODEL: SURVEYOR 50
TYPE: RATEMETER
SN: B602G

RSO, Inc. certifies that on 07/22/1999 the above described instrument was calibrated using a radioactive source to determine the efficiency for a specific radionuclide(s) and using electronically generated pulse for the linearity.

The results are tabulated below. Calibration is traceable to NIST.

Calibration Data

	RANGE	EXPECTED	OBSERVED		C.F.
X	1.00	100.00	100.000	cpm	1.000
		500.00	500.000	cpm	1.000
X	10.00	1000.00	1000.000	cpm	1.000
		5000.00	5000.000	cpm	1.000
X	100.00	10000.00	10000.000	cpm	1.000
		50000.00	50000.000	cpm	1.000
				C.F. AVERAGE	1.000

Probe type(s) Probe1: PANCAKE Probe2: Probe3:

MODEL	SER#	WINDOW	GEOMETRY	VOLT	ISOTOPE 1	EFF.(%)	ISOTOPE 2	EFF.(%)	ISOTOPE 3	EFF.(%)	ISOTOPE 4	EFF.(%)
PGM	B716G	OPEN	CONTACT	900	32P*	31	35S**	7	33P***	14	45Ca**	7

* Simulated using 90Sr with source at contact with probe.
** Simulated using 14C with source at contact with probe.
*** Simulated using 99Tc with source at contact with probe.
** Simulated using 14C with source at contact with probe.

INSTRUMENT CHECKS

BATTERY CHECK: NORMAL
CHECK SOURCE 1: NA READING:
CHECK SOURCE 2: READING:

ENVIRONMENTAL

TEMP: 25°C
PRESS: 755 mmHg
HUMID: 65 %

THE SUGGESTED RECALIBRATION DATE FOR THIS INSTRUMENT IS 07/22/2000

Calibrated By: Dorsey Austin Reviewed By: Cal Date: 07/22/1999

Maryland License MD-33-021-01

RSO, Inc.
P.O. Box 1526
Laurel, MD 20725
(301) 953-2482

RSO Order No. 1315

Certificate of Calibration

ISSUED TO: Naval Medical Research
Bethesda, MD 20889-5607
CONTACT: HM3 AHMAD
PHONE: (301) 295-0001

PO NO:

INSTRUMENT: LUDLUM
MODEL: 3
TYPE: RATEMETER
SN: 54537

RSO, Inc. certifies that on 07/22/1999 the above described instrument was calibrated using a radioactive source to determine the efficiency for a specific radionuclide(s) and using electronically generated pulse for the linearity.

The results are tabulated below. Calibration is traceable to NIST.

Calibration Data

	RANGE	EXPECTED	OBSERVED		C.F.
X	0.10	100.00	100.000	cpm	1.000
		300.00	300.000	cpm	1.000
X	1.00	1000.00	1000.000	cpm	1.000
		3000.00	3000.000	cpm	1.000
X	10.00	10000.00	10000.000	cpm	1.000
		30000.00	30000.000	cpm	1.000
X	100.00	100000.00	100000.000	cpm	1.000
		300000.00	300000.000	cpm	1.000
				C.F. AVERAGE	1.000

Probe type(s) Probe1: PANCAKE Probe2: Probe3:

MODEL	SER#	WINDOW	GEOMETRY	VOLT	ISOTOPE 1	EFF.(%)	ISOTOPE 2	EFF.(%)	ISOTOPE 3	EFF.(%)	ISOTOPE 4	EFF.(%)
44-9	39815	OPEN	CONTACT	900	32P*	29	35S**	7	33P***	14	45Ca**	7

* Simulated using 90Sr with source at contact with probe.
** Simulated using 14C with source at contact with probe.
*** Simulated using 99Tc with source at contact with probe.
** Simulated using 14C with source at contact with probe.

INSTRUMENT CHECKS

BATTERY CHECK: NORMAL
CHECK SOURCE 1: NA READING:
CHECK SOURCE 2: READING:

ENVIRONMENTAL

TEMP: 25°C
PRESS: 755 mmHg
HUMID: 65 %

THE SUGGESTED RECALIBRATION DATE FOR THIS INSTRUMENT IS 07/22/2000

Calibrated By: Rodney Austin Reviewed By: GDS Cal Date: 07/22/1999

Maryland License MD-33-021-01

RSO, Inc.
P.O. Box 1526
Laurel, MD 20725
(301) 953-2482

RSO Order No. 1315

Certificate of Calibration

ISSUED TO: Naval Medical Research
Bethesda, MD 20889-5607
CONTACT: HM3 AHMAD
PHONE: (301) 295-0001

PO NO:

INSTRUMENT: LUDLUM
MODEL: 3
TYPE: RATEMETER
SN: 114886

RSO, Inc. certifies that on 07/22/1999 the above described instrument was calibrated using a radioactive source to determine the efficiency for a specific radionuclide(s) and using electronically generated pulse for the linearity.

The results are tabulated below. Calibration is traceable to NIST.

Calibration Data

	RANGE	EXPECTED	OBSERVED		C.F.
X	0.10	100.00	100.000	cpm	1.000
		400.00	400.000	cpm	1.000
X	1.00	1000.00	1000.000	cpm	1.000
		4000.00	4000.000	cpm	1.000
X	10.00	10000.00	10000.000	cpm	1.000
		40000.00	40000.000	cpm	1.000
X	100.00	100000.00	100000.000	cpm	1.000
		400000.00	400000.000	cpm	1.000
				C.F. AVERAGE	1.000

Probe type(s) Probe1: SCINTILATOR Probe2: Probe3:

MODEL	SER#	WINDOW	GEOMETRY	VOLT	ISOTOPE 1	EFF.(%)	ISOTOPE 2	EFF.(%)	ISOTOPE 3	EFF.(%)	ISOTOPE 4	EFF.(%)
44-21	132842	OPEN	CONTACT	750	32P*	34	125I**	18	51Cr***	1		

* Simulated using 90Sr with source at contact with probe.
** Simulated using 129I with sourse at contact with probe.
*** Simulated using 133Ba with source at contact with probe.

INSTRUMENT CHECKS

BATTERY CHECK: NORMAL
CHECK SOURCE 1: NA READING:
CHECK SOURCE 2: READING:

ENVIRONMENTAL

TEMP: 25°C
PRESS: 755 mmHg
HUMID: 65 %

THE SUGGESTED RECALIBRATION DATE FOR THIS INSTRUMENT IS 07/22/2000

Calibrated By: Dorsey Austin

Reviewed By: GDS

Cal Date: 07/22/1999

Maryland License MD-33-021-01

RSO, Inc.
P.O. Box 1526
Laurel, MD 20725
(301) 953-2482

RSO Order No. 1361

Certificate of Calibration

ISSUED TO: Naval Medical Research
Bethesda, MD 20889-5607
CONTACT: HM3 Ahmad
PHONE: (301) 295-0001

PO NO: CC

INSTRUMENT: LUDLUM
MODEL: 3
TYPE: RATEMETER
SN: 121461

RSO, Inc. certifies that on 08/12/1999 the above described instrument was calibrated using a radioactive source to determine the efficiency for a specific radionuclide(s) and using electronically generated pulse for the linearity.

The results are tabulated below. Calibration is traceable to NIST.

Calibration Data

	RANGE	EXPECTED	OBSERVED		C.F.
X	0.10	100.00	100.000	cpm	1.000
		400.00	400.000	cpm	1.000
X	1.00	1000.00	1000.000	cpm	1.000
		4000.00	4000.000	cpm	1.000
X	10.00	10000.00	10000.000	cpm	1.000
		40000.00	40000.000	cpm	1.000
X	100.00	100000.00	100000.000	cpm	1.000
		400000.00	400000.000	cpm	1.000
				C.F. AVERAGE	1.000

Probe type(s) Probe1: SCINTILATOR Probe2: Probe3:

MODEL	SER#	WINDOW	GEOMETRY	VOLT	ISOTOPE 1	EFF.(%)	ISOTOPE 2	EFF.(%)	ISOTOPE 3	EFF.(%)	ISOTOPE 4	EFF.(%)
44-21	121786	OPEN	CONTACT	1050	125I*	17	32P**	29	51Cr***	1		

* Simulated using 129I with sourse at contact with probe..
** Simulated using 90Sr with source at contact with probe.
*** Simulated using 133Ba with source at contact with probe.

INSTRUMENT CHECKS

BATTERY CHECK: NORMAL
CHECK SOURCE 1: NA READING:
CHECK SOURCE 2: READING:

ENVIRONMENTAL

TEMP: 25°C
PRESS: 750 mmHg
HUMID: 65 %

THE SUGGESTED RECALIBRATION DATE FOR THIS INSTRUMENT IS 08/12/2000

Calibrated By: Dorsey Austin

Reviewed By: Cal Date: 08/12/1999

Maryland License MD-33-021-01

RSO, Inc.
P.O. Box 1526
Laurel, MD 20725
(301) 953-2482

Certificate of Calibration

RSO Order No. 1761

ISSUED TO: Naval Medical Research
8901 Wisconsin Ave.
Bethesda, MD 20889-5607
CONTACT: S. Ahmad
PHONE: (301) 295-0002

PO NO:

INSTRUMENT: LUDLUM
MODEL: 3
TYPE: RATEMETER
SN: 121816

RSO, Inc. certifies that on 02/22/2000 the above described instrument was calibrated using a radioactive source to determine the efficiency for a specific radionuclide(s) and using electronically generated pulse for the linearity.
The results are tabulated below. Calibration is traceable to NIST.

Calibration Data

	RANGE	EXPECTED	OBSERVED		C.F.
x	.1	100	100	cpm	1.00
		500	500	cpm	1.00
x	1	1000	1000	cpm	1.00
		5000	5000	cpm	1.00
x	10	10000	10000	cpm	1.00
		5000	5000	cpm	1.00
x	100	100000	100000	cpm	1.00
		500000	500000	cpm	1.00
				C.F. AVERAGE	1.00

Probe type(s) Probe1: PANCAKE Probe2: Probe3:

MODEL	SER#	WINDOW	GEOMETRY	VOLT	ISOTOPE 1	EFF.(%)	ISOTOPE 2	EFF.(%)	ISOTOPE 3	EFF.(%)	ISOTOPE 4	EFF.(%)
44-9	119401	FIXED	CONTACT	906	14C*	7	32P**	35	33P***	14		

* 35S=7%, 45Ca=7%; Simulated using 14C with source at contact with probe.
** Simulated using 90Sr with source at contact with probe.
*** Simulated using 99Tc with source at contact with probe.

INSTRUMENT CHECKS

BATTERY CHECK: NORMAL
CHECK SOURCE 1: READING:
CHECK SOURCE 2: READING:

ENVIRONMENTAL

TEMP: 26°C
PRESS: 768 mmHg
HUMID: 55 %

THE SUGGESTED RECALIBRATION DATE FOR THIS INSTRUMENT IS 02/22/2001

Calibrated By: Richard Emmons Reviewed By: DB Cal Date: 02/22/2000

Maryland License MD-33-021-01

1440

RSO, Inc.
P.O. Box 1526
Laurel, MD 20725
(301) 953-2482

RSO Order No. 1761

Certificate of Calibration

ISSUED TO: Naval Medical Research
8901 Wisconsin Ave.
Bethesda, MD 20889-5607
CONTACT: S. Ahmad
PHONE: (301) 295-0002

PO NO:

INSTRUMENT: LUDLUM
MODEL: 3
TYPE: RATEMETER
SN: 132946

RSO, Inc. certifies that on 02/22/2000 the above described instrument was calibrated using a radioactive source to determine the efficiency for a specific radionuclide(s) and using electronically generated pulse for the linearity.
The results are tabulated below. Calibration is traceable to NIST.

Calibration Data

	RANGE	EXPECTED	OBSERVED		C.F.
x	.1	100	100	cpm	1.00
		400	400	cpm	1.00
x	1	1000	1000	cpm	1.00
		4000	4000	cpm	1.00
x	10	10000	10000	cpm	1.00
		40000	40000	cpm	1.00
x	100	100000	100000	cpm	1.00
		400000	400000	cpm	1.00
			C.F. AVERAGE		1.00

Probe type(s) Probe1: SCINTILATOR Probe2: Probe3:

MODEL	SER#	WINDOW	GEOMETRY	VOLT	ISOTOPE 1	EFF.(%)	ISOTOPE 2	EFF.(%)	ISOTOPE 3	EFF.(%)	ISOTOPE 4	EFF.(%)
44-21	135670	FIXED	CONTACT	756	125I*	16	51Cr**	2.6				

* Simulated using 129I with sourse at contact with probe.
** Simulated using 133Ba with source at contact with probe, using correction factor of X0.1

INSTRUMENT CHECKS

BATTERY CHECK: NORMAL
CHECK SOURCE 1: READING:
CHECK SOURCE 2: READING:

ENVIRONMENTAL

TEMP: 27°C
PRESS: 768 mmHg
HUMID: 55 %

THE SUGGESTED RECALIBRATION DATE FOR THIS INSTRUMENT IS 02/22/2001

Calibrated By: Richard Emmons Reviewed By: DB Cal Date: 02/22/2000

Maryland License MD-33-021-01

1447

U.S. DEPARTMENT OF COMMERCE
National Institute of Standards & Technology
Gaithersburg, MD 20899

Certificate of Participation

Analytics, Incorporated
Atlanta, Georgia

is a participant for the period January 1, 1999, through December 31, 1999, in a radioactivity measurements assurance program conducted by the National Institute of Standards and Technology, in cooperation with the Nuclear Energy Institute. Continued participation is evidenced by dated Reports of Traceability issued for particular radionuclides, which indicate the deviation of the participant's reported value from that measured by the National Institute of Standards and Technology. The significance of these Reports is addressed below.*

For the Director,

Lisa R. Karam, Group Leader
Radioactivity Group
Physics Laboratory

*As guidance for the proper use of Reports of Traceability, it should be emphasized that the National Institute of Standards and Technology is concerned only with fostering good measurements capability and consistency with the national measurements system. The assurance of the proper application of that capability to the ultimate consumer products is the responsibility of each manufacturer of these products and of the Federal regulatory agencies.

A continuing traceability program in radioactivity demonstrates, to the degree established by the periodic assays of calibrated radioactivity samples, a continuing competence to maintain the instrument systems and standards necessary for accurate measurement. Such a program cannot, however, endorse each and every measurement nor the final product, any more than a spot check can vouch for every unchecked item. Care should be taken, therefore, not to imply such endorsement. The proper use of this Report is governed by section 200.114 of Title 15 of the Code of Federal Regulations. These regulations may be met if Reports are quoted only in their entirety. Excerpts out of context may be misleading.

ANALYTICS

1380 Seaboard Industrial Blvd.
Atlanta, Georgia 30318 · U.S.A.

Phone (404) 352-8677
Fax (404) 352-2837

CERTIFICATE OF CALIBRATION

Standard Radionuclide Source

58806A-530

C-14 32 mm Diameter x 3 mm Thick Plastic Disk

This standard radionuclide source was prepared using an aliquot measured gravimetrically from a master radionuclide solution standard. The master radionuclide solution standard was calibrated by the Department Des Applications Et De La Metrologie Des Rayonnements Ionisants (DAMRI), Paris, France, as number 22453. ANALYTICS maintains traceability to the National Institute of Standards and Technology through Measurements Assurance Programs as described in USNRC Reg. Guide 4.15, Revision 1. After source preparation the calibration was checked by beta counting using a gas flow proportional counter.

ISOTOPE:	C-14
ACTIVITY (dps):	5049
HALF-LIFE:	5730 years
CALIBRATION DATE:	November 18, 1999 12:00 EST
TOTAL UNCERTAINTY*:	5.0%

*99% Confidence Level

Diameter of active area: 16 mm. Source covering 0.5 mg/cm^2 mylar.

No expiration date has been given for this source due to the fragile nature of the mylar covering. This source should be carefully tested for leakage at least every six months. If leakage is detected this source should be disposed of by approved radioactive waste disposal procedures.

P O NUMBER N32398-99-M-0228, Item 1

SOURCE PREPARED BY: M Taskaeva
M. Taskaeva, Radiochemist

Q A APPROVED: 11-19-99

ANALYTICS

1380 Seaboard Industrial Blvd.
Atlanta, Georgia 30318 - U.S.A.

Phone (404) 352-8677
Fax (404) 352-2837

CERTIFICATE OF CALIBRATION

Standard Radionuclide Source

58807-530

C-14 32 mm Diameter x 3 mm Thick Plastic Disk

This standard radionuclide source was prepared using an aliquot measured gravimetrically from a master radionuclide solution standard. The master radionuclide solution standard was calibrated by the Department Des Applications Et De La Metrologie Des Rayonnements Ionisants (DAMRI), Paris, France, as number 22453. ANALYTICS maintains traceability to the National Institute of Standards and Technology through Measurements Assurance Programs as described in USNRC Reg. Guide 4.15, Revision 1. After source preparation the calibration was checked by beta counting using a gas flow proportional counter.

ISOTOPE:	C-14
ACTIVITY (dps):	5347
HALF-LIFE:	5730 years
CALIBRATION DATE:	November 18, 1999 12:00 EST
TOTAL UNCERTAINTY*:	5.0%

*99% Confidence Level

Diameter of active area: 16 mm. Source covering 0.5 mg/cm^2 mylar.

No expiration date has been given for this source due to the fragile nature of the mylar covering. This source should be carefully tested for leakage at least every six months. If leakage is detected this source should be disposed of by approved radioactive waste disposal procedures.

P O NUMBER N32398-99-M-0228, Item 1

SOURCE PREPARED BY: MTaskaeva
M. Taskaeva, Radiochemist

Q A APPROVED: DM Mof 11-19-99

ANALYTICS

1380 Seaboard Industrial Blvd.
Atlanta, Georgia 30318 · U.S.A.

Phone (404) 352-8677
Fax (404) 352-2837

CERTIFICATE OF CALIBRATION

Standard Radionuclide Source

58808-530

Co-60 32 mm Diameter x 3 mm Thick Plastic Disk

This standard radionuclide source was prepared using aliquots measured gravimetrically from calibrated master liquid radionuclide solutions. The master sources were calibrated with an ion chamber that was calibrated by the National Physical Laboratory, Teddington, U.K., and is directly traceable to national standards.

Radionuclide purity and calibration were checked using a germanium gamma spectrometer system. The nuclear decay rate and assay date for this source are given below.

ANALYTICS maintains traceability to the National Institute of Standards and Technology through Measurements Assurance Programs as described in USNRC Reg. Guide 4.15, Revision 1.

ISOTOPE:	Co-60
ACTIVITY (dps):	3.599 E+04
HALF-LIFE:	5.2714 years
CALIBRATION DATE:	November 18, 1999 12:00 EST
TOTAL UNCERTAINTY*:	4.8%
SYSTEMATIC:	4.5%
RANDOM:	0.3%

*99% confidence level.

Diameter of active area: 25 mm. Source covering 0.85 mg/cm^2 mylar.

No expiration date has been given for this source due to the fragile nature of the mylar covering. This source should be carefully tested for leakage at least every six months. If leakage is detected this source should be disposed of by approved radioactive waste disposal procedures.

P O NUMBER N32398-99-M-0228, Item 2

SOURCE PREPARED BY: M Taskaeva
M. Taskaeva, Radiochemist

Q A APPROVED: SM Mt 11-19-99

ANALYTICS

1380 Seaboard Industrial Blvd.
Atlanta, Georgia 30318 · U.S.A.

Phone (404) 352-8677
Fax (404) 352-2837

CERTIFICATE OF CALIBRATION

Standard Radionuclide Source

58809-530

Co-60 32 mm Diameter x 3 mm Thick Plastic Disk

This standard radionuclide source was prepared using aliquots measured gravimetrically from calibrated master liquid radionuclide solutions. The master sources were calibrated with an ion chamber that was calibrated by the National Physical Laboratory, Teddington, U.K., and is directly traceable to national standards.

Radionuclide purity and calibration were checked using a germanium gamma spectrometer system. The nuclear decay rate and assay date for this source are given below.

ANALYTICS maintains traceability to the National Institute of Standards and Technology through Measurements Assurance Programs as described in USNRC Reg. Guide 4.15, Revision 1.

ISOTOPE:	Co-60
ACTIVITY (dps):	3.730 E+04
HALF-LIFE:	5.2714 years
CALIBRATION DATE:	November 18, 1999 12:00 EST
TOTAL UNCERTAINTY*:	4.8%
SYSTEMATIC:	4.5%
RANDOM:	0.3%

*99% confidence level.

Diameter of active area: 25 mm. Source covering 0.85 mg/cm^2 mylar.

No expiration date has been given for this source due to the fragile nature of the mylar covering. This source should be carefully tested for leakage at least every six months. If leakage is detected this source should be disposed of by approved radioactive waste disposal procedures.

P O NUMBER N32398-99-M-0228, Item 2

SOURCE PREPARED BY: M Taskaeva
M. Taskaeva, Radiochemist

Q A APPROVED: 11-19-99

Designer and Manufacturer of Scientific and Industrial Instruments

CERTIFICATE OF CALIBRATION

LUDLUM MEASUREMENTS, INC.
POST OFFICE BOX 810 PH. 915-235-5494
501 OAK STREET FAX NO. 915-235-4672
SWEETWATER, TEXAS 79556, U.S.A.

CUSTOMER NAVAL MEDICAL RESEARCH CTR ORDER NO. 237400

Ludlum Measurements, Inc. Model 2350-1 Serial No. 157674

Cal. Date 27-Sep-99 Cal Due Date 27-Sep-00 Cal. Interval 1 Year Meterface N/A

Check mark ☑ applies to applicable instr. and/or detector IAW mfg. spec. T. 76 °F RH 56 % Alt 700.8 mm Hg

☑ New Instrument Instrument Received ☐ Within Toler. +-10% ☐ 10-20% ☐ Out of Tol. ☐ Requiring Repair ☐ Other-See comments

☑ Mechanical check
☑ F/S Resp. check
☑ Audio check
☑ Ratemeter Linearity check
☑ Data Log check
☑ Calibrated in accordance with LMI SOP 14.8 rev 12/05/89.

☑ Reset check
☑ Alarm Setting check
☑ Integrated Dose check
☑ Overload check

☑ Window Operation
☑ Battery check (Min. Volt) 4.4 VDC
☑ Recycle Mode check
☑ Scaler Readout check
☑ Calibrated in accordance with LMI SOP 14.9 rev 12/19/89.

☑ Input Sens. Linearity
Threshold Dial Ratio 100 = 4 mV

☑ HV Readout (2 points) Ref./Inst. 498 / 500 V Ref./Inst. 2002 / 2000 V

COMMENTS: *Firmware: 37122N27*

I/O firmware : 37123N05 Resolution for 44-10 ≈ 9.36 % for Cs137. Model 2350-1 and all probes calibrated using 6 ft. cable only. See ATTACHMENT 1 for efficiencies.

Gamma Calibration: GM detectors positioned perpendicular to source except for M 44-9 in which the front of probe faces source.

	Probe Model	Serial #	High Voltage	Threshold	Units/ Time Base	Dead Time Correction Factor	Calibration Constant	Linearity ±10%*
Detector # 1	LMI43-68	PR149314	1750	100	7 / 1	2.342273E-05	1.000000E+00	
Detector # 2	LMI43-68	PR149314	1750	100	7 / 1	2.342273E-05	1.000000E+00	
Detector # 3	LMI43-68	PR149314	1750	100	7 / 1	2.342273E-05	1.000000E+00	
Detector # 4	LMI43-37	PR148947	1800	100	7 / 1	2.361271E-05	1.000000E+00	
Detector # 5	LMI43-37	PR148947	1800	100	7 / 1	2.361271E-05	1.000000E+00	
Detector # 6	LMI43-37	PR148947	1800	100	7 / 1	2.361271E-05	1.000000E+00	
Detector # 7	LMI44-10	PR164841	1200	250	4 / 2	1.577578E-05	5.406332E+10	✓
Detector # 8	LMI44-10	PR164841	1200	250	4 / 2	1.577578E-05	5.406332E+10	✓
Detector # 9	LMI44-10	PR164841	1200	250	4 / 2	1.577578E-05	5.406332E+10	✓
Detector # 10	PEAK	CO-60	660	560	7 / 1	0.000000E+00	1.000000E+00	
Detector # 11	PEAK	CO-60	660	560	7 / 1	0.000000E+00	1.000000E+00	
Detector # 12	PEAK	CO-60	660	560	7 / 1	0.000000E+00	1.000000E+00	
Detector # 13	PEAK	CS-137	660	321	7 / 1	0.000000E+00	1.000000E+00	
Detector # 14	LMI44-10	PR164841	1200	250	7 / 1	1.577578E-05	1.000000E+00	
Detector #								
Detector #								

Units: 0 – rad, 1 – Gray, 2 – rem, 3 – Sv, 4 – R, 5 – C/Kg, 6 – Disintegrations, 7 – Counts, 8 – Ci/cm sq., 9 – Bq/cm sq.
Time Base: 0 – Seconds, 1 – Minutes, 2 – Hours

* See attached detector documentation, if applicable.

Digital Readout	REFERENCE CAL. POINT	INSTRUMENT RECEIVED	INSTRUMENT METER READING*	REFERENCE CAL. POINT	INSTRUMENT RECEIVED	INSTRUMENT METER READING*
	400kcpm		399969	400cpm		400
	40kcpm		40014	40cpm		40
	4kcpm		4004			

Ludlum Measurements, Inc. certifies that the above instrument has been calibrated by standards traceable to the National Institute of Standards and Technology, or to the calibration facilities of other International Standards Organization members, or have been derived from accepted values of natural physical constants or have been derived by the ratio type of calibration techniques. The calibration system conforms to the requirements of ANSI/NCSL Z540-1-1994 and ANSI N323-1978. State of Texas Calibration License No. LO-1963

Reference Instruments and/or Sources: Cs-137 Gamma S/N

☐ 1162 ☐ G112 ☐ M565 ☐ 5105 ☐ T1008 ☑ T879 ☑ ESS2 ☐ ESS1 ☐ Neutron Am-241 Be S/N T-304

Alpha S/N ____ ☑ Beta S/N 635/83, I-659, 422-44 (Tc99 C14 Sr32) ☑ Other Am241 ~ 1.73µCi/I 129 0.076 µCi

☑ m 500 S/N 141233 ☑ Multimeter S/N 59120574

Calibrated By: Elias Chavez Date 27-SEP-99

Reviewed By: Eric Hernandez Date 27-SEP-99

FORM C44A 07/30/99

This certificate shall not be reproduced except in full, without the written approval of Ludlum Measurements, Inc.

LUDLUM MEASUREMENTS, INC.
501 OAK ST./PO BOX 810
SWEETWATER, TEXAS 79556
Phone: 915/235-5494 800/622-0828(USA)
Fax: 915/235-4672

DESIGNER AND MANUFACTURER OF
Scientific and Industrial Instruments

ATTACHMENT 1

4 π efficiencies for 43-68 :

Efficiencies for 43-68 taken at 1750v.

Factory background ≈ 261cpm

Ca45 and P33 were substituted with Tc99
Tc99 is ≈ 38.55% net
Tc99 reading ≈ 8568 net

S35 was substituted with C14
C14 is ≈ 10.82% net
C14 reading ≈ 33740 net

I 125 was substituted with I 129
I 129 is ≈ 0.25% net
I 129 reading is ≈ 428 net

P 32 was substituted with Si 32
Si 32 is ≈ 35% net
Si 32 reading is ≈ 34460 net

4 π efficiencies for 43-37 :

Efficiencies for 43-37 taken at 1800v.

Factory background ≈ 908cpm

Ca45 and P33 were substituted with Tc99
Tc99 is ≈ 35.9% net
Tc99 reading ≈ 8223 net

S35 was substituted with C14
C14 is ≈ 10.42% net
C14 reading is ≈ 32507 net

I 125 was substituted with I 129
I 129 is ≈ 0.44% net
I 129 reading is ≈ 738 net

P 32 was substituted with Si 32
Si 32 is ≈ 35.16% net
Si 32 reading is ≈ 34521 net

4 π efficiency for 44-10 :

Efficiencies for 44-10 taken at 1200v. using Det.14 and 1 minute counts.

Factory background ≈ 7508 cpm

Co 57 is ≈ 28.70 % net
Co 57 reading is ≈ 25801 cpm net

Co 60 is ≈ 22.17 % net
Co 60 reading is ≈ 9045 cpm net

Cs137 is ≈ 12.13 % net
Cs137 reading is ≈ 1854 cpm net

Elvis Chaney 27-SEP-99

DETECTOR SETUP CHECK LIST REPORT

The following list is stored as detector setup D14 in the Model 2350.
Today's date is 09/27/1999.
The current time of day is: 09:36:33.

I have verified the list below
has NO discrepancies with the DETECTOR SETTINGS TABLE: EC

Comments:

Model 2350 Serial # =	157674.
User I.D. =	
High Voltage =	1200 volts.
Threshold =	250.
Window =	100,Off.
Overload Current =	40.0 micro amperes.
Scaler Count Time =	60 seconds.
Readout Units =	counts.
Readout Time Base =	min.
Readout Range Multiplier =	auto.
Detector Dead Time =	1.577578E-05.
Detector Calibration Constant =	1.000000E+00.
Detector Model =	LMI44-10.
Detector Serial # =	PR164841.
Ratemeter Alarm Setting =	1.000000E+09.
Scaler Alarm Setting =	1000000.
Integrated Dose Alarm Setting =	1.000000E+09.
Low Count Alarm Setting =	X.
Operating Battery Voltage =	6.1 volts.

Designer and Manufacturer
of
Scientific and Industrial
Instruments

LUDLUM MEASUREMENTS, INC.
POST OFFICE BOX 810 PH. 915-235-5494
501 OAK STREET FAX NO. 915-235-4672
SWEETWATER, TEXAS 79556, U.S.A.

Model 2350 Bench Test Data

Customer NAVAL MEDICAL RESEARCH CTR Date 25-Sep-99 Order #. 237400

Model 2350-1 Serial No. 157674 Detector 44-10 Serial No. PR164841

Source Cs137 21mCi, 2.47mCi

High Voltage 1200 V As Found _____ V. Input 10.00 mV As Found _____ mV.

Cal. Constant 5.406332E+10 as found _____

Dead Time 1.577578E-05 as found _____

Alarm Setting: Ratemeter EC ~~1000000000.000000~~ 0.002000 as found _____

Scaler 1000000.000000 as found _____

Integrated dose 1000000000.0000 as found _____

Overload ☐ On ☑ Off as found ☐ On ☐ Off Window 100 (OFF) as found _____

Detector Received: ☐ Within Toler. +-10% ☐ 10-20% ☐ Out of Tol. ☐ Requiring Repair ☐ Other-See comments

Reference Point	"As Found" Readings: Meter Reading	After Adjustment Readings: Meter Reading
2.0 mR/hr		1.93 mR/hr
1.5		1.50
1.0		1.03
500 µR/hr		508 µR/hr
200		204
150		149
100		102

Other Calibrated using 6 ft. cable.

Signature Elias Chavez Date 25-SEP-99

FORM C6-1 09/08/97

Designer and Manufacturer
of
Scientific and Industrial
Instruments

LUDLUM MEASUREMENTS, INC.
POST OFFICE BOX 810 PH. 915-235-5494
501 OAK STREET FAX NO. 915-235-4672
SWEETWATER, TEXAS 79556, U.S.A.

Bench Test Data For Detector

Detector 44-10 Serial No. PR164841

Customer NAVAL MEDICAL RESEARCH CTR Order #. 237400

Counter 2350-1 Serial No. 157674 Counter Input Sensitivity 10.00 mV

Count Time 6 SEC. Distance Source to Detector Surface

Other Cal Constant = 1.000000E+00 Dead Time = 1.577578E-05

High Voltage	Background	Isotope Am241 Size ≈1.13μG	Isotope Size	Isotope Size	Isotope Size
1000	573	11013			
1050	609	12508			
1100	636	12519			
1150	567	12753			
1200	586	12879			
1250	592	12803			
1300	618	12934			
1350	608	12954			
1400	622	12883			

Signature Elias Chavez Date 25-SEP-99

FORM C4A 02/23/94

Designer and Manufacturer of Scientific and Industrial Instruments

CERTIFICATE OF CALIBRATION

LUDLUM MEASUREMENTS, INC.
POST OFFICE BOX 810 PH. 915-235-5494
501 OAK STREET FAX NO. 915-235-4672
SWEETWATER, TEXAS 79556, U.S.A.

C OMER NAVAL MEDICAL RESEARCH CTR ORDER NO. 237400

I Ludlum Measurements, Inc. Model 2350-1 Serial No. 157669

Cal. Date 27-Sep-99 Cal Due Date 27-Sep-00 Cal. Interval 1 Year Meterface N/A

Check mark ☑ applies to applicable instr. and/or detector IAW mfg. spec. T. 76 °F RH 56 % Alt 700.8 mm Hg

☑ New Instrument Instrument Received ☐ Within Toler. +-10% ☐ 10-20% ☐ Out of Tol. ☐ Requiring Repair ☐ Other-See comments

☑ Mechanical check ☑ Input Sens. Linearity

☑ F/S Resp. check ☑ Reset check ☑ Window Operation

☑ Audio check ☑ Alarm Setting check ☑ Battery check (Min. Volt) 4.4 VDC

☑ Ratemeter Linearity check ☑ Integrated Dose check ☑ Recycle Mode check

☑ Data Log check ☑ Overload check ☑ Scaler Readout check Threshold Dial Ratio 100 = 4 mV

☑ Calibrated in accordance with LMI SOP 14.8 rev 12/05/89. ☐ Calibrated in accordance with LMI SOP 14.9 rev 12/19/89.

☑ HV Readout (2 points) Ref./Inst. 499 / 500 V Ref./Inst. 1998 / 2000 V

COMMENTS: *Firmware: 37122N27*

I/O firmware : 37123N05 Resolution for 44-10 ≈ 9.36 % for Cs137. Model 2350-1 and all probes calibrated using 6 ft. cable only. See ATTACHMENT 1 for efficiencies.

Gamma Calibration: GM detectors positioned perpendicular to source except for M 44-9 in which the front of probe faces source.

	Probe Model	Serial #	High Voltage	Threshold	Units/ Time Base	Dead Time Correction Factor	Calibration Constant	Linearity ±10%*
Detector # 1	LMI43-68	PR149314	1750	100	7 / 1	2.342273E-05	1.000000E+00	
Detector # 2	LMI43-68	PR149314	1750	100	7 / 1	2.342273E-05	1.000000E+00	
Detector # 3	LMI43-68	PR149314	1750	100	7 / 1	2.342273E-05	1.000000E+00	
Detector # 4	LMI43-37	PR148947	1800	100	7 / 1	2.361271E-05	1.000000E+00	
Detector # 5	LMI43-37	PR148947	1800	100	7 / 1	2.361271E-05	1.000000E+00	
De 6	LMI43-37	PR148947	1800	100	7 / 1	2.361271E-05	1.000000E+00	
De # 7	LMI44-10	PR164841	1200	250	4 / 2	1.577578E-05	5.406332E+10	✓
Detector # 8	LMI44-10	PR164841	1200	250	4 / 2	1.577578E-05	5.406332E+10	✓
Detector # 9	LMI44-10	PR164841	1200	250	4 / 2	1.577578E-05	5.406332E+10	✓
Detector # 10	PEAK	CO-60	660	560	7 / 1	0.000000E+00	1.000000E+00	
Detector # 11	PEAK	CO-60	660	560	7 / 1	0.000000E+00	1.000000E+00	
Detector # 12	PEAK	CO-60	660	560	7 / 1	0.000000E+00	1.000000E+00	
Detector # 13	PEAK	CS-137	660	321	7 / 1	0.000000E+00	1.000000E+00	
Detector # 14	LMI44-10	PR164841	1200	250	7 / 1	1.577578E-05	1.000000E+00	
Detector #								
Detector #								

Units: 0 – rad, 1 – Gray, 2 – rem, 3 – Sv, 4 – R, 5 – C/Kg, 6 – Disintegrations, 7 – Counts, 8 – Ci/cm sq., 9 – Bq/cm sq.

Time Base: 0 – Seconds, 1 – Minutes, 2 – Hours

* See attached detector documentation, if applicable.

Digital Readout	REFERENCE CAL. POINT	INSTRUMENT RECEIVED	INSTRUMENT METER READING*	REFERENCE CAL. POINT	INSTRUMENT RECEIVED	INSTRUMENT METER READING*
	400kcpm		399905	400cpm		400
	40kcpm		39993	40cpm		40
	4kcpm		4000			

Ludlum Measurements, Inc. certifies that the above instrument has been calibrated by standards traceable to the National Institute of Standards and Technology, or to the calibration facilities of other International Standards Organization members, or have been derived from accepted values of natural physical constants or have been derived by the ratio type of calibration techniques. The calibration system conforms to the requirements of ANSI/NCSL Z540-1-1994 and ANSI N323-1978. State of Texas Calibration License No. LO-1963

Reference Instruments and/or Sources: Cs-137 Gamma S/N

☐ 1162 ☐ G112 ☐ M565 ☐ 5105 ☐ T1008 ☑ T879 ☑ E552 ☐ E551 ☐ Neutron Am-241 Be S/N T-304

Alpha S/N ☑ Beta S/N 635/83 (T299), I-659 (C14), 422-44 (S132) ☑ Other Am241 ~1.73µCi/I 129 0.076 µCi

☑ m 500 S/N 141233 ☑ Multimeter S/N 59120574

Calibrated By: Elias Chavez Date 27-SEP-99

Reviewed By: Eric Turner Date 27-Sept-99

FORM C44A 07/30/99

This certificate shall not be reproduced except in full, without the written approval of Ludlum Measurements, Inc.

LUDLUM MEASUREMENTS, INC.
501 OAK ST./PO BOX 810
SWEETWATER, TEXAS 79556
Phone: 915/235-5494 800/622-0828(USA)
Fax: 915/235-4672

DESIGNER AND MANUFACTURER OF *Scientific and Industrial Instruments*

ATTACHMENT 1

4 π efficiencies for 43-68 :

Efficiencies for 43-68 taken at 1750v.

Factory background ≈ 261cpm

Ca45 and P33 were substituted with Tc99
Tc99 is ≈ 38.55% net
Tc99 reading ≈ 8568 net

S35 was substituted with C14
C14 is ≈ 10.82% net
C14 reading ≈ 33740 net

I 125 was substituted with I 129
I 129 is ≈ 0.25% net
I 129 reading is ≈ 428 net

P 32 was substituted with Si 32
Si 32 is ≈ 35% net
Si 32 reading is ≈ 34460 net

4 π efficiencies for 43-37 :

Efficiencies for 43-37 taken at 1800v.

Factory background ≈ 908cpm

Ca45 and P33 were substituted with Tc99
Tc99 is ≈ 35.9% net
Tc99 reading ≈ 8223 net

S35 was substituted with C14
C14 is ≈ 10.42% net
C14 reading is ≈ 32507 net

I 125 was substituted with I 129
I 129 is ≈ 0.44% net
I 129 reading is ≈ 738 net

P 32 was substituted with Si 32
Si 32 is ≈ 35.16% net
Si 32 reading is ≈ 34521 net

4 π efficiency for 44-10 :

Efficiencies for 44-10 taken at 1200v. using Det.14 and 1 minute counts.

Factory background ≈ 7508 cpm

Co 57 is ≈ 28.70 % net
Co 57 reading is ≈ 25801 cpm net

Co 60 is ≈ 22.17 % net
Co 60 reading is ≈ 9045 cpm net

Cs137 is ≈ 12.13 % net
Cs137 reading is ≈ 1854 cpm net

Elias Chavez 27-SEP-99

DETECTOR SETUP CHECK LIST REPORT

The following list is stored as detector setup D14 in the Model 2350.
Today's date is 09/27/1999.
The current time of day is: 09:33:46.

I have verified the list below
has NO discrepancies with the DETECTOR SETTINGS TABLE: EC

Comments:

Model 2350 Serial # =	157669.
User I.D. =	.
High Voltage =	1200 volts.
Threshold =	250.
Window =	100,Off.
Overload Current =	40.0 micro amperes.
Scaler Count Time =	60 seconds.
Readout Units =	counts.
Readout Time Base =	min.
Readout Range Multiplier =	auto.
Detector Dead Time =	1.577578E-05.
Detector Calibration Constant =	1.000000E+00.
Detector Model =	LMI44-10.
Detector Serial # =	PR164841.
Ratemeter Alarm Setting =	1.000000E+09.
Scaler Alarm Setting =	1000000.
Integrated Dose Alarm Setting =	1.000000E+09.
Low Count Alarm Setting =	X.
Operating Battery Voltage =	6.2 volts.

Designer and Manufacturer
of
Scientific and Industrial
Instruments

LUDLUM MEASUREMENTS, INC.
POST OFFICE BOX 810 PH. 915-235-5494
501 OAK STREET FAX NO. 915-235-4672
SWEETWATER, TEXAS 79556, U.S.A.

Model 2350 Bench Test Data

Customer NAVAL MEDICAL RESEARCH CTR Date 25-Sep-99 Order #. 237400

Model 2350-1 Serial No. 157669 Detector 44-10 Serial No. PR164841

Source Cs137 21mCi, 2.47 mCi

High Voltage 1200 V As Found _____ V. Input 10.00 mV As Found _____ mV.

Cal. Constant 5.406332E+10 as found _____

Dead Time 1.577578E-05 as found _____

Alarm Setting: Ratemeter 0.002000 as found _____

Scaler 1000000.000000 as found _____

Integrated dose 1000000000.0000 as found _____

Overload ☐ On ☑ Off as found ☐ On ☐ Off Window 100 (OFF) as found _____

Detector Received: ☐ Within Toler. +-10% ☐ 10-20% ☐ Out of Tol. ☐ Requiring Repair ☐ Other-See comments

Reference Point	"As Found" Readings: Meter Reading	After Adjustment Readings: Meter Reading
2.0 mR/hr		1.93 mR/hr
1.5		1.50
1.0		1.03
500 μR/hr		508 μR/hr
200		204
150		148
100		102

Other Calibrated using 6 ft. cable.

Signature Elias Chavez Date 25-SEP-99

FORM C6-1 09/08/97

Designer and Manufacturer
of
Scientific and Industrial
Instruments

LUDLUM MEASUREMENTS, INC.
POST OFFICE BOX 810 PH. 915-235-5494
501 OAK STREET FAX NO. 915-235-4672
SWEETWATER, TEXAS 79556, U.S.A.

Bench Test Data

Detector 43-68 Serial No. PR149314 Order #. 237400

Customer NAVAL MEDICAL RESEARCH CTR

Counter 2350-1 Serial No. 157669 Counter Input Sensitivity 4.00 mV

Count Time 1 min. Distance Source to Detector Surface

Other Cal Constant = 1.000000E+00 Dead Time = 2.342273E-05 Plateau w/6 ft. cable.

High Voltage	Background	Isotope Tc99 Size 22.9Kdpm	Isotope C14 Size 0.140μCi	Isotope Si32 Size 98,168dpm	Isotope I129 Size 0.076μCi
1550	146	7106	28,360	12,794	310
1600	192	8139	32,185	22,419	495
1650	235	8420	33,878	32,120	658
1700	231	8349	34001	33,724	662
1750	261	8829	34,545	34,721	689
1800	265	8869	37,897	38,106	924
1850	2198	31277	801,985	669,736	1073

Gas proportional detector count rate decreased ≤ 10% after 15 hour static test using 39" cable.

Signature Elias Chavez Date 25-SEP-98

Ludlum Measurements, Inc. certifies that the above instrument has been calibrated by standards traceable to the National Institute of Standards and Technology, or to the calibration facilities of other International Standards Organization members, or have been derived from accepted values of natural physical constants or have been derived by the ratio type of calibration techniques. The calibration system conforms to the requirements of ANSI/NCSL Z540-1-1994 and ANSI N323-1997. State of Texas Calibration License No. LO-1963

FORM C4D 09/17/98

Designer and Manufacturer
of
Scientific and Industrial
Instruments

LUDLUM MEASUREMENTS, INC.
POST OFFICE BOX 810 PH. 915-235-5494
501 OAK STREET FAX NO. 915-235-4672
SWEETWATER, TEXAS 79556, U.S.A.

Bench Test Data

Detector 43-37 Serial No. PR148947 Order #. 237400

Customer NAVAL MEDICAL RESEARCH CTR

Counter 2350-1 Serial No. 157669 Counter Input Sensitivity 4.00 mV

Count Time 1 minute Distance Source to Detector Surface

Other Cal Constant = 1.000000E+00 Dead Time = 2.361271E-05 Plateau w/6ft. cable.

High Voltage	Background	Isotope Tc99 Size 22,800dpm	Isotope C14 Size 0.140μCi	Isotope S132 Size 98,168dpm	Isotope I129 Size 0.076μCi
1550	118	2787	13537	3985	294
1600	242	4330	19548	7559	511
1650	388	6228	27468	13230	694
1700	635	7837	30858	21851	1027
1750	824	8760	32323	32023	1505
1800	908	9131	33415	35429	1646
1850	954	9120	33605	35693	1805
1900	991	9214	34319	35922	1774

☑ Gas proportional detector count rate decreased ≤ 10% after 15 hour static test using 39" cable.

Signature Elias Chavez Date 25-SEP-99

Ludlum Measurements, Inc. certifies that the above instrument has been calibrated by standards traceable to the National Institute of Standards and Technology, or to the calibration facilities of other International Standards Organization members, or have been derived from accepted values of natural physical constants or have been derived by the ratio type of calibration techniques. The calibration system conforms to the requirements of ANSI/NCSL Z540-1-1994 and ANSI N323-1997. State of Texas Calibration License No. LO-1963

Appendix D-3. Instrument and Equipment Quality Control Data

Table D-3-1 provides the daily quality-control data obtained by evaluating tritium (H-3), Carbon-14 (C-14) and background standards on the in-house Packard Liquid Scintillation Counter that was used to evaluate all swipes for H-3 and C-14 contamination.

Other pertinent equipment information is as follows:

Packard Liquid Scintillation Counter
Model: 2500TR
Serial Number: 403848
Calibration date: 10 March 2000
Efficiencies: H-3 = 60.9%; C-14 = 96.3%
Packard Check (standard) sources:
H-3 (activity < 0.2µCi = 267600 dpm, date 17 May 93)
C-14 (activity < 0.1µCi = 136200 dpm, date 17 May 93)
Background (May 1993)

Table D-3-1 provides quality-control data for liquid-scintillation-counter evaluations in the form of dpm values which were obtained by evaluating H-3 and C-14 radioactive (check source) standards and a background standard. QC data was collected, on a minimum, each day that samples were evaluated and/or equipment tests performed. The upper warning limit (UWL) and lower warning limits (LWL) for H-3 and C-14 were obtained by calculating the mean and adding or subtracting 5% of the mean values for H-13 and C-14. The first ten sets of data (1/19/00-2/4/00) were used to calculate the UWL and LWL for H-3 and C-14. When dpm readings were obtained that exceeded the UWL or LWL, investigations were conducted. If inconsistent operation was evident, the instrument would have been taken out of service and replaced with another instrument or the vendor called for assistance.

Note: Instrument calibration performed by vendor on 3/10/00; the vendor on 4/6/00 performed maintenance service; QC checks were performed by the vendor and it was determined that the instrument was working properly.

Table D-3-1. Quality Control Data - Packard Liquid Scintillation Counter Daily Evaluations of H-3, C-14 and Background Standards

Instrument Use: Beta-Gamma Counting for loose surface contamination

DPM Values: Mean value for H-3 =170631; Mean value for C-14 = 135664

QC Date	H-3			C-14			Background (C-14 channel)
	DPM	UWL	LWL	DPM	UWL	LWL	DPM
1/19/00	170573	179162	142447	135519	142447	128881	9
1/20/00	170156	179162	142447	135595	142447	128881	5
1/21/00	169786	179162	142447	135742	142447	128881	11
1/24/00	169724	179162	142447	135937	142447	128881	3
1/27/00	169876	179162	142447	134805	142447	128881	3
1/28/00	169708	179162	142447	135914	142447	128881	7
2/1/00	170667	179162	142447	136135	142447	128881	6
2/2/00	172562	179162	142447	135692	142447	128881	8
2/3/00	171476	179162	142447	135380	142447	128881	6
2/4/00	171783	179162	142447	135919	142447	128881	5
2/7/00	171460	179162	142447	135801	142447	128881	2
2/8/00	171475	179162	142447	135478	142447	128881	7
2/9/00	170774	179162	142447	135808	142447	128881	9
2/10/00	171733	179162	142447	135762	142447	128881	11
2/11/00	171433	179162	142447	135625	142447	128881	4
2/14/00	171341	179162	142447	135616	142447	128881	5
2/15/00	170767	179162	142447	136250	142447	128881	1
2/16/00	171125	179162	142447	136030	142447	128881	6
2/17/00	170122	179162	142447	135130	142447	128881	7
2/18/00	171538	179162	142447	136421	142447	128881	2
2/22/00	171187	179162	142447	135679	142447	128881	8
2/23/00	170449	179162	142447	135378	142447	128881	7
2/24/00	170161	179162	142447	135978	142447	128881	10
2/25/00	170708	179162	142447	136330	142447	128881	5
2/28/00	170363	179162	142447	136677	142447	128881	1
2/29/00	169704	179162	142447	136105	142447	128881	7
3/1/00	170894	179162	142447	136667	142447	128881	3
3/2/00	170568	179162	142447	135452	142447	128881	6
3/3/00	169353	179162	142447	135742	142447	128881	11
3/6/00	169402	179162	142447	135795	142447	128881	7
3/7/00	170117	179162	142447	135779	142447	128881	8
3/8/00	170261	179162	142447	136068	142447	128881	10
3/9/00	169343	179162	142447	136548	142447	128881	5

3/10/00	170124	179162	142447	136041	142447	128881	6
3/13/00	170482	179162	142447	135716	142447	128881	7
3/14/00	168454	179162	142447	135604	142447	128881	4
3/15/00	169482	179162	142447	136194	142447	128881	4
3/16/00	169274	179162	142447	135433	142447	128881	2
3/17/00	169113	179162	142447	136035	142447	128881	6
3/20/00	168952	179162	142447	135484	142447	128881	11
3/21/00	170135	179162	142447	136005	142447	128881	6
3/22/00	169263	179162	142447	136441	142447	128881	3
3/23/00	169197	179162	142447	135920	142447	128881	1
3/24/00	169311	179162	142447	136396	142447	128881	8
3/27/00	169187	179162	142447	134581	142447	128881	5
3/28/00	170543	179162	142447	135647	142447	128881	9
3/29/00	169356	179162	142447	135799	142447	128881	6
3/30/00	168609	179162	142447	136585	142447	128881	6
3/31/00	168114	179162	142447	135115	142447	128881	11
4/3/00	168368	179162	142447	135449	142447	128881	9
4/4/00	169815	179162	142447	136440	142447	128881	1
4/5/00	170876	179162	142447	135859	142447	128881	4
4/6/00	169462	179162	142447	136061	142447	128881	13
4/7/00	169412	179162	142447	135993	142447	128881	1
4/11/00	167894	179162	142447	135638	142447	128881	4
4/12/00	168861	179162	142447	135409	142447	128881	11
4/13/00	167436	179162	142447	135514	142447	128881	6
4/14/00	167649	179162	142447	135896	142447	128881	
4/17/00	168492	179162	142447	135267	142447	128881	2
4/18/00	167391	179162	142447	135261	142447	128881	3
4/19/00	168016	179162	142447	135729	142447	128881	8
4/20/00	168549	179162	142447	134965	142447	128881	8
4/21/00	168412	179162	142447	135453	142447	128881	7
4/24/00	167776	179162	142447	135662	142447	128881	11
4/25/00	167959	179162	142447	136325	142447	128881	12
4/26/00	167591	179162	142447	135617	142447	128881	4
4/27/00	165803	179162	142447	135901	142447	128881	4
4/28/00	167727	179162	142447	135095	142447	128881	6
5/1/00	166078	179162	142447	135681	142447	128881	4
5/2/00	167768	179162	142447	135673	142447	128881	11
5/3/00	166859	179162	142447	136478	142447	128881	1
5/4/00	165253	179162	142447	135087	142447	128881	12
5/5/00	166271	179162	142447	134972	142447	128881	4
5/8/00	166602	179162	142447	134720	142447	128881	2

Table D-3-2 provides the daily quality-control data obtained by evaluating an Iodine-129 (sealed-source) standard using a Wallac Gamma Counter.

Other pertinent equipment information is as follows:

Instrument: Wallac LKB Model 1282 Gamma Counter Serial Number: 324 Calibration Date: 23 Aug 99 Efficiencies: Cr-51 = 3.7 % Check Source: I-129 (rod-shaped; batch number: 8203, catalog number: 1270-102; activity: 0.0221 µCi; calibration date: July 1982; half life: 15.7 million years, 40 keV gamma at 7.5%)

Table D-3-2 provides daily quality-control data for the gamma counter. The data was obtained by evaluating a I-129 (sealed-source) standard. The upper warning limit (UWL) and lower warning limits (LWL) for I-129 cpm values were obtained by calculating the mean and adding or subtracting 5% of the mean for I-129 cpm values. The first 30 sets of data (3/23/00) were used to calculate the UWL and LWL for I-129. If dpm readings were obtained that exceeded the UWL or LWL, investigations would have been conducted. If inconsistent operation was evident, the instrument would have been taken out of service and replaced with another instrument or the vendor called for assistance.

Table D-3-2. Quality Control Data - Daily Evaluations of I-129 Standard Using the Wallac LKB Model 1282 Gamma Counter

Instrument Use: Gamma Counting for loose surface contamination

CPM Values: Mean = 30261, UWL = 31774, LWL = 28748

QC Date	Iodine-129		
	CPM	UWL	LWL
3/23/00	30549	31774	28748
3/23/00	30342	31774	28748
3/23/00	29939	31774	28748
3/23/00	30337	31774	28748
3/23/00	30135	31774	28748
3/23/00	30079	31774	28748
3/23/00	30624	31774	28748
3/23/00	30190	31774	28748
3/23/00	29959	31774	28748
3/23/00	30306	31774	28748
3/23/00	30602	31774	28748
3/23/00	30253	31774	28748
3/23/00	30298	31774	28748
3/23/00	30261	31774	28748
3/23/00	30343	31774	28748
3/23/00	29969	31774	28748
3/23/00	30235	31774	28748
3/23/00	30167	31774	28748
3/23/00	30226	31774	28748
3/23/00	30396	31774	28748
3/24/00	29992	31774	28748
3/27/00	30253	31774	28748
3/28/00	30234	31774	28748
3/29/00	30268	31774	28748
3/30/00	30264	31774	28748
3/31/00	30268	31774	28748
4/3/00	30376	31774	28748
4/4/00	29942	31774	28748
4/5/00	30215	31774	28748
4/6/00	29954	31774	28748
4/7/00	30283	31774	28748

4/10/00	30432	31774	28748
4/11/00	30431	31774	28748
4/12/00	30305	31774	28748
4/13/00	30385	31774	28748
4/14/00	30127	31774	28748
4/18/00	30366	31774	28748
4/19/00	30307	31774	28748
4/20/00	30572	31774	28748
4/21/00	30099	31774	28748
4/24/00	30320	31774	28748
4/25/00	30233	31774	28748
4/26/00	30649	31774	28748
4/27/00	30340	31774	28748
4/28/00	30307	31774	28748
5/1/00	30366	31774	28748
5/2/00	30053	31774	28748
5/3/00	30202	31774	28748
5/4/00	30235	31774	28748
5/5/00	30612	31774	28748

Tables D-3-3 through **D-3-12** provide the daily quality control data obtained by evaluating Carbon-14 or Cobalt-60 check sources using portable beta and beta-gamma detection meters.

Table D-3-3. DAILY QUALITY CONTROL PORTABLE METER CHECK SHEET AND DATA					
Instrument: Ludlum Model 3		Serial Number: 114886		Calibration Date: 7/22/99	
Meter Use: Beta-Gamma Scanning for fixed or loose surface contamination					
Check Source: Cobalt-60; 1.008 µCi; calibration date: 18 Nov 99; Serial number: 58807-530					
Meter Calibration Isotope/Efficiencies: P-32, I-125, Cr-51: 34%, 18%, 1%					
UWL = Upper Warning Limit = mean + 5% of mean (mean was calculated using the first 10 cpm readings = 152000) LWL = Lower Warning Limit = mean - 5% of mean					
DATE	BATTERY CHECK	BACKGROUND (CPM)	CHECK SOURCE READING (CPM)		
			CPM	UWL	LWL
1/19/00	OK	< 300	150000	159600	144400
1/20/00	OK	< 350	150000	159600	144400
1/21/00	OK	< 350	150000	159600	144400
1/24/00	OK	< 300	150000	159600	144400
1/27/00	OK	< 350	150000	159600	144400
1/28/00	OK	< 350	150000	159600	144400
2/1/00	OK	< 400	160000	159600	144400
2/2/00	OK	< 350	150000	159600	144400
2/3/00	OK	< 350	150000	159600	144400
2/4/00	OK	< 300	160000	159600	144400
2/7/00	OK	< 300	150000	159600	144400
2/8/00	OK	< 350	150000	159600	144400
2/9/00	OK	< 350	150000	159600	144400
2/10/00	OK	< 350	150000	159600	144400
2/11/00	OK	< 350	150000	159600	144400
2/14/00	OK	< 350	150000	159600	144400
2/15/00	OK	< 350	150000	159600	144400
2/16/00	OK	< 350	150000	159600	144400
2/17/00	OK	< 300	150000	159600	144400
2/18/00	OK	< 300	150000	159600	144400
2/22/00	OK	< 300	150000	159600	144400

2/23/00	OK	< 350	150000	159600	144400
2/24/00	OK	< 350	150000	159600	144400
2/25/00	OK	< 350	150000	159600	144400
2/28/00	OK	< 300	150000	159600	144400
2/29/00	OK	< 300	150000	159600	144400
3/1/00	OK	< 350	150000	159600	144400
3/2/00	OK	< 350	150000	159600	144400
3/3/00	OK	< 300	150000	159600	144400
3/6/00	OK	< 350	150000	159600	144400
3/7/00	OK	< 350	150000	159600	144400
3/8/00	OK	< 350	150000	159600	144400
3/9/00	OK	< 350	150000	159600	144400
3/10/00	OK	< 350	150000	159600	144400
3/13/00	OK	< 350	150000	159600	144400
3/14/00	OK	< 350	150000	159600	144400
3/15/00	OK	< 350	150000	159600	144400
3/16/00	OK	< 350	150000	159600	144400
3/17/00	OK	< 350	150000	159600	144400
3/20/00	OK	< 350	150000	159600	144400
3/21/00	OK	< 350	150000	159600	144400
3/22/00	OK	< 300	150000	159600	144400
3/23/00	OK	< 350	150000	159600	144400
3/24/00	OK	< 350	150000	159600	144400
3/27/00	OK	< 350	150000	159600	144400
3/28/00	OK	< 350	150000	159600	144400
3/29/00	OK	< 350	150000	159600	144400
3/30/00	OK	< 350	150000	159600	144400
3/31/00	OK	< 350	150000	159600	144400
4/3/00	OK	< 350	150000	159600	144400
4/4/00	OK	< 400	150000	159600	144400
4/5/00	OK	< 350	150000	159600	144400
4/6/00	OK	< 350	150000	159600	144400
4/7/00	OK	< 350	150000	159600	144400
4/10/00	OK	< 350	150000	159600	144400
4/11/00	OK	< 350	150000	159600	144400
4/12/00	OK	< 350	150000	159600	144400
4/13/00	OK	< 350	150000	159600	144400
4/14/00	OK	< 350	150000	159600	144400
4/17/00	OK	< 350	150000	159600	144400
4/18/00	OK	< 350	150000	159600	144400
4/19/00	OK	< 350	150000	159600	144400
4/20/00	OK	< 350	150000	159600	144400

4/21/00	OK	< 350	150000	159600	144400
4/24/00	OK	< 350	150000	159600	144400
4/25/00	OK	< 350	150000	159600	144400
4/26/00	OK	< 350	150000	159600	144400
4/27/00	OK	< 350	150000	159600	144400
4/28/00	OK	< 350	150000	159600	144400
5/1/00	OK	< 350	150000	159600	144400
5/2/00	OK	< 350	150000	159600	144400
5/3/00	OK	< 350	150000	159600	144400
5/4/00	OK	< 350	150000	159600	144400
5/5/00	OK	< 350	150000	159600	144400

Table D-3-4. DAILY QUALITY CONTROL PORTABLE METER CHECK SHEET AND DATA

Instrument: Ludlum Model 3	Serial Number: 132946	Calibration Date: 2/22/00

Instrument Use: Beta-Gamma Scanning for fixed or loose surface contamination

Check Source: Cobalt-60; 1.008 µCi; calibration date: 18 Nov 99; Serial number: 58807-530

Meter Calibration Isotope/Efficiencies: I-125, Cr-51: 16%, 2.6%

UWL = Upper Warning Limit = mean + 5% (mean was calculated using the first 10 cpm readings = 160000)
LWL = Lower Warning Limit = mean - 5%

DATE	BATTERY CHECK	BACKGROUND (CPM)	CHECK SOURCE READING (CPM)		
			CPM	UWL	LWL
3/15/00	OK	< 300	160000	168000	152000
3/16/00	OK	< 300	160000	168000	152000
3/17/00	OK	< 300	160000	168000	152000
3/20/00	OK	< 350	160000	168000	152000
3/21/00	OK	< 350	160000	168000	152000
3/22/00	OK	< 300	160000	168000	152000
3/23/00	OK	< 350	160000	168000	152000
3/24/00	OK	< 350	160000	168000	152000
3/27/00	OK	< 350	160000	168000	152000
3/28/00	OK	< 350	160000	168000	152000
3/29/00	OK	< 350	160000	168000	152000
3/30/00	OK	< 350	160000	168000	152000
3/31/00	OK	< 350	160000	168000	152000
4/3/00	OK	< 350	160000	168000	152000
4/4/00	OK	< 400	160000	168000	152000
4/5/00	OK	< 350	160000	168000	152000
4/6/00	OK	< 350	160000	168000	152000
4/7/00	OK	< 350	160000	168000	152000
4/10/00	OK	< 300	160000	168000	152000
4/11/00	OK	< 350	160000	168000	152000
4/12/00	OK	< 350	160000	168000	152000
4/13/00	OK	< 350	160000	168000	152000
4/14/00	OK	< 350	160000	168000	152000
4/17/00	OK	< 300	160000	168000	152000
4/18/00	OK	< 350	160000	168000	152000

4/19/00	OK	< 350	160000	168000	152000
4/20/00	OK	< 300	160000	168000	152000
4/21/00	OK	< 300	160000	168000	152000
4/24/00	OK	< 350	160000	168000	152000
4/25/00	OK	< 300	160000	168000	152000
4/26/00	OK	< 300	160000	168000	152000
4/27/00	OK	< 300	160000	168000	152000
4/28/00	OK	< 300	160000	168000	152000
5/1/00	OK	< 350	160000	168000	152000
5/2/00	OK	< 350	160000	168000	152000
5/3/00	OK	< 350	160000	168000	152000
5/4/00	OK	< 350	160000	168000	152000
5/5/00	OK	< 300	160000	168000	152000

Table D-3-5. DAILY QUALITY CONTROL PORTABLE METER CHECK SHEET AND DATA

Instrument: Ludlum Model 3	Serial Number: 121461	Calibration Date: 8/12/99

Instrument Use: Beta-Gamma Scanning for fixed or loose surface contamination

Check Source: Cobalt-60; 1.008 µCi; calibration date: 18 Nov 99; Serial number: 58807-530

Meter Calibration Isotope/Efficiencies: P-32, I-125, Cr-51: 17%, 29%, 1%

UWL = Upper Warning Limit = mean + 5% (mean was calculated using the first 10 cpm readings = 150500)
LWL = Lower Warning Limit = mean - 5%

DATE	BATTERY CHECK	BACKGROUND (CPM)	CHECK SOURCE READING (CPM)		
			CPM	UWL	LWL
1/19/00	OK	< 300	140000	158025	142975
1/20/00	OK	< 350	150000	158025	142975
1/21/00	OK	< 300	145000	158025	142975
1/24/00	OK	< 400	150000	158025	142975
1/27/00	OK	< 350	150000	158025	142975
1/28/00	OK	< 350	150000	158025	142975
2/1/00	OK	< 400	160000	158025	142975
2/2/00	OK	< 300	160000	158025	142975
2/3/00	OK	< 350	150000	158025	142975
2/4/00	OK	< 350	150000	158025	142975
2/7/00	OK	< 350	160000	158025	142975
2/8/00	OK	< 350	150000	158025	142975
2/9/00	OK	< 300	150000	158025	142975
2/10/00	OK	< 300	150000	158025	142975
2/11/00	OK	< 350	150000	158025	142975
2/14/00	OK	< 350	150000	158025	142975
2/15/00	OK	< 350	150000	158025	142975
2/16/00	OK	< 350	150000	158025	142975
2/17/00	OK	< 300	150000	158025	142975
2/18/00	OK	< 300	150000	158025	142975
2/22/00	OK	< 300	150000	158025	142975
2/23/00	OK	< 350	150000	158025	142975
2/24/00	OK	< 350	150000	158025	142975
2/25/00	OK	< 350	150000	158025	142975
2/28/00	OK	< 300	150000	158025	142975

2/29/00	OK	< 350	150000	158025	142975
3/1/00	OK	< 350	150000	158025	142975
3/2/00	OK	< 350	150000	158025	142975
3/3/00	OK	< 300	150000	158025	142975
3/6/00	OK	< 350	150000	158025	142975
3/7/00	OK	< 350	150000	158025	142975
3/8/00	OK	< 350	150000	158025	142975
3/9/00	OK	< 350	150000	158025	142975
3/10/00	OK	< 300	150000	158025	142975
3/13/00	OK	< 350	150000	158025	142975
3/14/00	OK	< 350	150000	158025	142975
3/15/00	OK	< 350	150000	158025	142975
3/16/00	OK	< 350	150000	158025	142975
3/17/00	OK	< 350	150000	158025	142975
3/20/00	OK	< 350	150000	158025	142975
3/21/00	OK	< 300	150000	158025	142975
3/22/00	OK	< 300	150000	158025	142975
3/23/00	OK	< 350	150000	158025	142975
3/24/00	OK	< 350	150000	158025	142975
3/27/00	OK	< 350	150000	158025	142975
3/28/00	OK	< 350	150000	158025	142975
3/29/00	OK	< 350	150000	158025	142975
3/30/00	OK	< 300	150000	158025	142975
3/31/00	OK	< 300	150000	158025	142975
4/3/00	OK	< 300	150000	158025	142975
4/4/00	OK	< 350	150000	158025	142975
4/5/00	OK	< 350	150000	158025	142975
4/6/00	OK	< 350	150000	158025	142975
4/7/00	OK	< 350	150000	158025	142975
4/10/00	OK	< 350	150000	158025	142975
4/11/00	OK	< 350	150000	158025	142975
4/12/00	OK	< 350	150000	158025	142975
4/13/00	OK	< 300	150000	158025	142975
4/14/00	OK	< 300	150000	158025	142975
4/17/00	OK	< 350	150000	158025	142975
4/18/00	OK	< 350	150000	158025	142975
4/19/00	OK	< 350	150000	158025	142975
4/20/00	OK	< 350	150000	158025	142975
4/21/00	OK	< 350	150000	158025	142975
4/24/00	OK	< 350	150000	158025	142975
4/25/00	OK	< 350	150000	158025	142975
4/26/00	OK	< 350	150000	158025	142975

4/27/00	OK	< 350	150000	158025	142975
4/28/00	OK	< 300	150000	158025	142975
5/1/00	OK	< 300	150000	158025	142975
5/2/00	OK	< 350	150000	158025	142975
5/3/00	OK	< 300	150000	158025	142975
5/4/00	OK	< 350	150000	158025	142975
5/5/00	OK	< 350	150000	158025	142975

Table D-3-6. DAILY QUALITY CONTROL PORTABLE METER CHECK SHEET AND DATA

Instrument: Ludlum Model 3	Serial Number: 121730	Calibration Date: 7/22/99

Instrument Use: Beta-Gamma Scanning for fixed or loose surface contamination

Check Source: Cobalt-60; 1.008 µCi; calibration date: 18 Nov 99; Serial number: 58807-530

Meter Calibration Isotope/Efficiencies: P-32, I-125, Cr-51: 32%, 16%, 1%

UWL = Upper Warning Limit = mean + 5% (mean was calculated using the first 10 cpm readings = 155000)
LWL = Lower Warning Limit = mean - 5%

DATE	BATTERY CHECK	BACKGROUND (CPM)	CHECK SOURCE READING (CPM)		
			CPM	UWL	LWL
1/19/00	OK	< 300	150000	162750	147250
1/20/00	OK	< 350	150000	162750	147250
1/21/00	OK	< 300	150000	162750	147250
1/24/00	OK	< 350	150000	162750	147250
1/27/00	OK	< 350	150000	162750	147250
1/28/00	OK	< 350	160000	162750	147250
2/1/00	OK	< 300	160000	162750	147250
2/2/00	OK	< 300	160000	162750	147250
2/3/00	OK	< 350	160000	162750	147250
2/4/00	OK	< 300	160000	162750	147250
2/7/00	OK	< 350	160000	162750	147250
2/8/00	OK	< 350	160000	162750	147250
2/9/00	OK	< 350	160000	162750	147250
2/10/00	OK	< 350	160000	162750	147250
2/11/00	OK	< 350	150000	162750	147250
2/14/00	OK	< 350	160000	162750	147250
2/15/00	OK	< 350	160000	162750	147250
2/16/00	OK	< 350	160000	162750	147250
2/17/00	OK	< 350	150000	162750	147250
2/18/00	OK	< 300	160000	162750	147250
2/22/00	OK	< 350	160000	162750	147250
2/23/00	OK	< 300	160000	162750	147250
2/24/00	OK	< 300	160000	162750	147250
2/25/00	OK	< 300	160000	162750	147250
2/28/00	OK	< 300	160000	162750	147250

2/29/00	OK	< 350	160000	162750	147250
3/1/00	OK	< 350	160000	162750	147250
3/2/00	OK	< 350	160000	162750	147250
3/3/00	OK	< 350	160000	162750	147250
3/6/00	OK	< 350	160000	162750	147250
3/7/00	OK	< 350	160000	162750	147250
3/8/00	OK	< 350	160000	162750	147250
3/9/00	OK	< 350	160000	162750	147250
3/10/00	OK	< 300	160000	162750	147250
3/13/00	OK	< 350	160000	162750	147250
3/14/00	OK	< 350	160000	162750	147250
3/15/00	PROBE	BROKEN	ON	THIS	DATE

Table D-3-7. DAILY QUALITY CONTROL PORTABLE METER CHECK SHEET AND DATA

Instrument: Ludlum Model 3	Serial Number: 121816	Calibration Date: 2/22/00

Instrument Use: Beta Scanning for fixed or loose surface contamination

Check Source: CARBON-14; 0.145 µCi; calibration date: 18 Nov 99; Serial number: 58809-530

Meter Calibration Isotope/Efficiencies: C-14,P-32, P-33, S-35, CA-45: 7%, 35%, 14%, 7%, 7%

UWL = Upper Warning Limit = mean + 5% (mean was calculated using the first 10 cpm readings = 26000)
LWL = Lower Warning Limit = mean - 5%

DATE	BATTERY CHECK	BACKGROUND (CPM)	CHECK SOURCE READING (CPM)		
			CPM	UWL	LWL
3/17/00	OK	< 100	26000	27300	24700
3/20/00	OK	< 100	26000	27300	24700
3/21/00	OK	< 100	26000	27300	24700
3/22/00	OK	< 100	26000	27300	24700
3/23/00	OK	< 100	26000	27300	24700
3/24/00	OK	< 100	26000	27300	24700
3/27/00	OK	< 100	26000	27300	24700
3/28/00	OK	< 100	26000	27300	24700
3/29/00	OK	< 100	26000	27300	24700
3/30/00	OK	< 100	26000	27300	24700
3/31/00	OK	< 100	26000	27300	24700
4/3/00	OK	< 100	26000	27300	24700
4/4/00	OK	< 100	26000	27300	24700
4/5/00	OK	< 100	26000	27300	24700
4/6/00	OK	< 100	26000	27300	24700
4/7/00	OK	< 100	26000	27300	24700
4/10/00	OK	< 100	26000	27300	24700
4/11/00	OK	< 100	26000	27300	24700
4/12/00	OK	< 100	26000	27300	24700
4/13/00	OK	< 100	26000	27300	24700
4/14/00	OK	< 100	26000	27300	24700
4/17/00	OK	< 100	26000	27300	24700
4/18/00	OK	< 100	26000	27300	24700
4/19/00	OK	< 100	26000	27300	24700
4/20/00	OK	< 100	26000	27300	24700

4/21/00	OK	< 100	26000	27300	24700
4/24/00	OK	< 100	26000	27300	24700
4/25/00	OK	< 100	26000	27300	24700
4/26/00	OK	< 100	26000	27300	24700
4/27/00	OK	< 100	26000	27300	24700
4/28/00	OK	< 100	26000	27300	24700
5/1/00	OK	< 100	26000	27300	24700
5/2/00	OK	< 100	26000	27300	24700
5/3/00	OK	< 100	26000	27300	24700
5/4/00	OK	< 100	26000	27300	24700
5/5/00	OK	< 100	26000	27300	24700

Table D-3-8. DAILY QUALITY CONTROL PORTABLE METER CHECK SHEET AND DATA

Instrument: Ludlum Model 3	Serial Number: 54537	Calibration Date: 7/22/99

Instrument Use: Beta Scanning for fixed or loose surface contamination

Check Source: CARBON-14; 0.145 µCi; calibration date: 18 Nov 99; Serial number: 58809-530

Meter Calibration Isotope/Efficiencies: C-14,P-32, P-33, S-35, CA-45: 7%, 35%, 14%, 7%, 7%

UWL = Upper Warning Limit = mean + 5% (mean was calculated using the first 10 cpm readings = 20600)
LWL = Lower Warning Limit = mean - 5%

DATE	BATTERY CHECK	BACKGROUND (CPM)	CHECK SOURCE READING (CPM)		
			CPM	UWL	LWL
1/19/00	OK	< 50	19000	21630	19570
1/20/00	OK	< 100	18000	21630	19570
1/21/00	OK	< 100	21000	21630	19570
1/24/00	OK	< 100	21000	21630	19570
1/27/00	OK	< 50	21000	21630	19570
1/28/00	OK	< 50	21000	21630	19570
2/1/00	OK	< 50	22000	21630	19570
2/2/00	OK	< 50	21000	21630	19570
2/3/00	OK	< 50	21000	21630	19570
2/4/00	OK	< 50	21000	21630	19570
2/7/00	OK	< 100	20000	21630	19570
2/8/00	OK	< 100	21000	21630	19570
2/9/00	OK	< 100	21000	21630	19570
2/10/00	OK	< 100	21000	21630	19570
2/11/00	OK	< 100	21000	21630	19570
2/14/00	OK	< 100	22000	21630	19570
2/15/00	OK	< 150	21000	21630	19570
2/16/00	OK	< 100	22000	21630	19570
2/17/00	OK	< 100	21000	21630	19570
2/18/00	OK	< 150	21000	21630	19570
2/22/00	OK	< 100	21000	21630	19570
2/23/00	OK	< 100	22000	21630	19570
2/24/00	OK	< 100	22000	21630	19570
2/25/00	OK	< 100	21000	21630	19570
2/28/00	OK	< 100	21000	21630	19570

2/29/00	OK	< 100	21000	21630	19570
3/1/00	OK	< 100	20000	21630	19570
3/2/00	OK	< 100	21000	21630	19570
3/3/00	OK	< 100	20000	21630	19570
3/6/00	OK	< 100	20000	21630	19570
3/7/00	OK	< 100	22000	21630	19570
3/8/00	OK	< 100	21000	21630	19570
3/9/00	OK	< 100	21000	21630	19570
3/10/00	OK	< 100	21000	21630	19570
3/13/00	OK	< 100	21000	21630	19570
3/14/00	OK	< 100	22000	21630	19570
3/15/00	OK	< 100	21000	21630	19570
3/16/00	OK	< 100	22000	21630	19570
3/17/00	OK	< 100	22000	21630	19570
3/20/00	OK	< 100	22000	21630	19570
3/21/00	OK	< 100	22000	21630	19570
3/22/00	OK	< 100	22000	21630	19570
3/23/00	OK	< 100	22000	21630	19570
3/24/00	OK	< 100	22000	21630	19570
3/27/00	OK	< 100	22000	21630	19570
3/28/00	OK	< 100	21000	21630	19570
3/29/00	OK	< 100	22000	21630	19570
3/30/00	OK	< 100	22000	21630	19570
3/31/00	OK	< 100	22000	21630	19570
4/3/00	OK	< 100	22000	21630	19570
4/4/00	OK	< 100	22000	21630	19570
4/5/00	OK	< 100	22000	21630	19570
4/6/00	OK	< 100	21000	21630	19570
4/7/00	OK	< 100	21000	21630	19570
4/10/00	OK	< 100	22000	21630	19570
4/11/00	OK	< 100	21000	21630	19570
4/12/00	OK	< 100	21000	21630	19570
4/13/00	OK	< 100	22000	21630	19570
4/14/00	OK	< 100	22000	21630	19570
4/17/00	OK	< 100	22000	21630	19570
4/18/00	OK	< 100	22000	21630	19570
4/19/00	OK	< 100	22000	21630	19570
4/20/00	OK	< 100	22000	21630	19570
4/21/00	OK	< 100	22000	21630	19570
4/24/00	OK	< 100	22000	21630	19570
4/25/00	OK	< 100	21000	21630	19570
4/26/00	OK	< 100	22000	21630	19570

4/27/00	OK	< 100	22000	21630	19570
4/28/00	OK	< 100	21000	21630	19570
5/1/00	OK	< 100	22000	21630	19570
5/2/00	OK	< 100	21000	21630	19570
5/3/00	OK	< 100	22000	21630	19570
5/4/00	OK	< 100	22000	21630	19570
5/5/00	OK	< 100	22000	21630	19570

Table D-3-9. DAILY QUALITY CONTROL PORTABLE METER CHECK SHEET AND DATA

Instrument: Bicron Survey 50	Serial Number: B602G	Calibration Date: 7/22/99

Instrument Use: Beta Scanning for fixed or loose surface contamination

Check Source: CARBON-14; 0.145 µCi; calibration date: 18 Nov 99; Serial number: 58809-530

Meter Calibration Isotope/Efficiencies: P-32, P-33, S-35, CA-45: 31%, 7%, 14%, 7%

UWL = Upper Warning Limit = mean + 5% (mean was calculated using the first 10 cpm readings = 21500)
LWL = Lower Warning Limit = mean - 5%

DATE	BATTERY CHECK	BACKGROUND (CPM)	CHECK SOURCE READING (CPM)		
			CPM	UWL	LWL
1/19/00	OK	< 50	20000	22575	20425
1/20/00	OK	< 50	21000	22575	20425
1/21/00	OK	< 80	24000	22575	20425
1/24/00	OK	< 50	22000	22575	20425
1/27/00	OK	< 50	22000	22575	20425
1/28/00	OK	< 50	22000	22575	20425
2/1/00	OK	< 60	21000	22575	20425
2/2/00	OK	< 50	21000	22575	20425
2/3/00	OK	< 60	21000	22575	20425
2/4/00	OK	< 60	21000	22575	20425
2/7/00	OK	< 80	21000	22575	20425
2/8/00	OK	< 100	20000	22575	20425
2/9/00	OK	< 100	21000	22575	20425
2/10/00	OK	< 100	21000	22575	20425
2/11/00	OK	< 60	21000	22575	20425
2/14/00	OK	< 100	20000	22575	20425
2/15/00	OK	< 100	20000	22575	20425
2/16/00	OK	< 100	21000	22575	20425
2/17/00	OK	< 100	21000	22575	20425
2/18/00	OK	< 100	21000	22575	20425
2/22/00	OK	< 60	21000	22575	20425
2/23/00	OK	< 100	21000	22575	20425
2/24/00	OK	< 80	21000	22575	20425
2/25/00	OK	< 80	21000	22575	20425
2/28/00	OK	< 100	21000	22575	20425

2/29/00	OK	< 80	21000	22575	20425
3/1/00	OK	< 80	20000	22575	20425
3/2/00	OK	< 100	20000	22575	20425
3/3/00	OK	< 100	20000	22575	20425
3/6/00	OK	< 100	21000	22575	20425
3/7/00	OK	< 100	22000	22575	20425
3/8/00	OK	< 80	22000	22575	20425
3/9/00	OK	< 80	21000	22575	20425
3/10/00	OK	< 80	22000	22575	20425
3/13/00	OK	< 50	21000	22575	20425
3/14/00	OK	< 50	21000	22575	20425
3/15/00	OK	< 80	22000	22575	20425
3/16/00	OK	< 50	21000	22575	20425
3/17/00	OK	< 50	21000	22575	20425
3/20/00	OK	< 80	20000	22575	20425
3/21/00	OK	< 80	22000	22575	20425
3/22/00	OK	< 80	22000	22575	20425
3/23/00	OK	< 100	22000	22575	20425
3/24/00	OK	< 80	21000	22575	20425
3/27/00	OK	< 80	22000	22575	20425
3/28/00	OK	< 80	22000	22575	20425
3/29/00	OK	< 100	21000	22575	20425
3/30/00	OK	< 80	21000	22575	20425
3/31/00	OK	< 80	22000	22575	20425
4/3/00	OK	< 80	21000	22575	20425
4/4/00	OK	< 80	22000	22575	20425
4/5/00	OK	< 80	22000	22575	20425
4/6/00	OK	< 80	22000	22575	20425
4/7/00	OK	< 80	22000	22575	20425
4/10/00	OK	< 60	21000	22575	20425
4/11/00	OK	< 80	21000	22575	20425
4/12/00	OK	< 80	21000	22575	20425
4/13/00	OK	< 80	21000	22575	20425
4/14/00	OK	< 80	22000	22575	20425
4/17/00	OK	< 60	22000	22575	20425
4/18/00	OK	< 80	22000	22575	20425
4/19/00	OK	< 80	21000	22575	20425
4/20/00	OK	< 80	21000	22575	20425
4/21/00	OK	< 80	21000	22575	20425
4/24/00	OK	< 80	22000	22575	20425
4/25/00	OK	< 80	22000	22575	20425
4/26/00	OK	< 80	21000	22575	20425

4/27/00	OK	< 80	22000	22575	20425
4/28/00	OK	< 80	22000	22575	20425
5/1/00	OK	< 80	21000	22575	20425
5/2/00	OK	< 80	22000	22575	20425
5/3/00	OK	< 80	22000	22575	20425
5/4/00	OK	< 80	22000	22575	20425
5/5/00	OK	< 80	22000	22575	20425

Table D-3-10. DAILY QUALITY CONTROL PORTABLE METER CHECK SHEET AND DATA

Instrument: Ludlum Model 3	Serial Number: 121816	Calibration Date: 2/22/00

Instrument Use: Beta Scanning for fixed or loose surface contamination

Check Source: CARBON-14; 0.145 µCi; calibration date: 18 Nov 99; Serial number: 58809-530

Meter Calibration Isotope/Efficiencies: C-14, P-32, P-33, S-35, CA-45: 7%, 35%, 14%, 7%, 7%

UWL = Upper Warning Limit = mean + 3 sigma = 26139
(mean was calculated using all cpm readings = 21344; sigma = standard deviation = 1600)
LWL = Lower Warning Limit = mean - 3 * sigma = 16548

DATE	BATTERY CHECK	BACKGROUND (CPM)	CHECK SOURCE READING (CPM)		
			CPM	UWL	LWL
1/19/00	OK	< 100	20000	26139	16548
1/20/00	OK	< 100	15000	26139	16548
1/21/00	OK	< 100	21000	26139	16548
1/24/00	OK	< 100	24000	26139	16548
1/27/00	OK	< 50	25000	26139	16548
1/28/00	OK	< 50	21000	26139	16548
2/1/00	OK	< 50	21000	26139	16548
2/2/00	OK	< 50	21000	26139	16548
2/3/00	OK	< 50	21000	26139	16548
2/4/00	OK	< 50	22000	26139	16548
2/7/00	OK	< 100	21000	26139	16548
2/8/00	OK	< 100	22000	26139	16548
2/9/00	OK	< 100	21000	26139	16548
2/10/00	OK	< 100	21000	26139	16548
2/11/00	OK	< 100	20000	26139	16548
2/14/00	OK	< 100	21000	26139	16548
2/15/00	OK	< 100	21000	26139	16548
2/16/00	OK	< 100	22000	26139	16548
2/17/00	OK	< 80	21000	26139	16548
2/18/00	OK	< 100	21000	26139	16548
2/22/00	OK	< 100	22000	26139	16548
2/23/00	OK	< 100	22000	26139	16548
2/24/00	OK	< 100	22000	26139	16548
2/25/00	OK	< 100	22000	26139	16548

2/28/00	OK	< 100	20000	26139	16548
2/29/00	OK	< 100	22000	26139	16548
3/1/00	OK	< 100	21000	26139	16548
3/2/00	OK	< 100	22000	26139	16548
3/3/00	OK	< 100	21000	26139	16548
3/6/00	OK	< 100	22000	26139	16548
3/7/00	OK	< 100	21000	26139	16548
3/8/00	OK	< 100	24000	26139	16548
3/9/00	METER	TAKEN	OUT	OF	SERVICE

Table D-3-11. DAILY QUALITY CONTROL PORTABLE METER CHECK SHEET AND DATA

Instrument: Ludlum Model 2350-1	Serial Number: 157674	Calibration Date: 11/18/99
Probe Model/Serial Number: 43-37/149314	Probe: 126cm^2 gas detector	
Instrument Use: Beta Scanning for fixed surface contamination		
Check Source: CARBON-14; 0.145 µCi; calibration date: 18 Nov 99; Serial number: 58809-530		
Notes: Mid-day and End-of-day readings were recorded on days that the instrument was used for radiological monitoring of survey units. Daily QC checks consisted of comparing same-day CPM values.		

DATE	BATTERY VOLTAGE	CPM, POST PURGING WITH P-10 GAS (T-0)	CPM, POST PURGING WITH P-10 GAS (T-10)	CPM, MID DAY READING	CPM, END OF DAY READING
3/28/00	5.9	44922	44740		
3/29/00	5.5	43781	44538		
3/30/00	5.7	44433	44391		
3/31/00	5.6	44214	44052	44992	43262
4/3/00	5.5	45342	45686		
4/4/00	5.6	44675	44888		
4/5/00	5.5	44515	44781	44529	
4/6/00	5.5	45079	45010	44935	45651
4/7/00	5.4	44616	44779	46105	
4/10/00	5.4	44584	44126		
4/11/00	5.4	45057	45266	45183	
4/12/00	5.3	44310	45043	44624	
4/13/00	5.3	45633	45571		
4/14/00	5.3	44848	44448		42976
4/17/00	5.2	44850	44678		
4/18/00	5.2	45564	45241	45614	44376
4/19/00	5.2	45752	45743		45756
4/20/00	5.1	44782	44600	45013	
4/21/00	5.1	44832	45178		
4/24/00	6.3	45560	45554	44437	
4/25/00	6.1	45446	45212		
4/26/00	6.0	44910	45422	44943	44122

4/27/00	6.0	45002	45138	44387	
4/28/00	6.0	44118	44554		43771
5/1/00	5.9	46016	46555	46466	45494
5/2/00	5.8	44891	44695	44040	43221
5/3/00	5.7	46076	45761	43370	
5/4/00	5.6	44819	44616		
5/5/00	5.6	42944	NOT	USED	

Table D-3-12. DAILY QUALITY CONTROL PORTABLE METER CHECK SHEET AND DATA

Instrument: Ludlum Model 2350-1	Serial Number: 157674	Calibration Date: 11/18/99
Probe Model/Serial Number: 43-37/148947	Probe: 582cm^2 gas detector	

Instrument Use: Beta Scanning for fixed surface contamination

Check Source: CARBON-14; 0.145 µCi; calibration date: 18 Nov 99; Serial number: 58809-530

Notes: Mid-day and end-of-day readings were recorded on days that the instrument was used for radiological monitoring of survey units. Daily QC checks consisted of comparing same-day CPM values.

DATE	BATTERY VOLTAGE	CPM, POST PURGING WITH P-10 GAS (T-0)	CPM, POST PURGING WITH P-10 GAS (T-10)	CPM, MID DAY READING	CPM, END OF DAY READING
3/28/00	5.9	44837	44672		
3/29/00	5.4	43313	43322		
3/30/00	5.7	45122	43346		
3/31/00	5.6	43939	43725	43839	42103
4/3/00	5.6	43532	43488		
4/4/00	5.6	42930	42763		39020
4/5/00	5.5	44658	45066	44073	
4/6/00	5.5	43345	43194	44745	43264
4/7/00	5.4	48062	47715	44503	
4/10/00	5.4	43402	43626		
4/11/00	5.4	44316	43874	42530	
4/12/00	5.4	44847	43458	41096	40547
4/13/00	5.3	43555	43591		
4/14/00	5.3	44004	43881		43996
4/17/00	5.2	44876	44291		
4/18/00	5.2	45312	45565	42341	44979
4/19/00	5.2	47748	48067		43140
4/20/00	5.1	47982	48215	45984	
4/21/00	5.1	47204	46576		
4/24/00	6.3	45551	45282		
4/25/00	6.1	45396	46749		
4/26/00	6.0	44868	44387		

4/27/00	6.0	45295	45009	42548	
4/28/00	6.0	45525	45424		43220
5/1/00	5.9	44254	43733	43161	43250
5/2/00	5.8	47994	47003	43598	
5/3/00	5.7	45166	45155	39031	
5/4/00	5.6	45259	45494		
5/5/00	5.7	42944	41404		
5/8/00	5.7	45554	44264		
5/9/00	5.7	44210	44036		

Appendix D-4. Quality Assurance Checklist (included in sections of the final status survey report)

Building number or location:
Monitoring Date(s):

___ Appropriate and satisfactory daily and weekly calibration checks were completed for the selected survey monitoring equipment and instruments.

___ Selected meters with current calibrations for the isotopes of concern.

___ Survey maps or floor plans (for all survey units) and grid maps (for known RAM-use areas) were available.

___ Background checks were performed when impacted areas were monitored.

___ For known RAM-use survey units, additional checks were performed (workbenches, shelves, sinks, basins, traps, floor at sinks and entrances, wall at hoods and sinks, and/or other areas as deemed appropriate).

___ Mean values, single sample values, and background values were below the action limits, indicating no contamination was found.

___ Representative floor plans, sketches, and photographs were available.

___Deviation from survey plans and objectives were documented.

___Extent of remediation actions were documented.

___ All selected survey units passed D&D tests; units are recommended for unrestricted release.

___ Additional Checks/Data passed D&D tests; unit is recommended for unrestricted release.

Notes: Tests included complying with applicable elements of the MARSSIM Final Status Survey checklist, mean-value and single-value comparisons of survey-unit data to action limits (DCGLs), mean-value comparison to background, completion of required monitoring, and satisfactory scan monitoring results.

Quality Assurance/Control Leader:

APPENDIX E. SURVEY UNIT RELEASE REPORTS (NARRATIVES, DATA, FLOOR PLANS, AND GRID MAPS)

XII. APPENDIX E

Appendix E-1. List of Survey Units, Data Tables, and Figures

A NMRC survey unit was defined as a room or other discrete area. Every room in every NMRC building was first examined for consideration as a survey unit. After review of current and historical survey monitoring results and licensed-material use, NMRC Rockville Annex survey units were classified as either Non-impacted or Impacted Class 3. No NMRC Rockville Annex survey unit was classified as Class 1 or Class 2.

Per MARSSIM, survey units should be limited in size based on classification, exposure pathway modeling assumptions, and site-specific conditions. In some instance, large rooms were subdivided into sections; each section was then treated as a unique survey unit.

Table 12-1-1 provides a list of tables associated with the completion of the final status surveys for the Non-impacted areas and Impacted Class 3 areas. These tables provide the actual data, reported in dpm per 100 cm^2, obtained by evaluating swipe samples using a liquid scintillation counter.

Table 12-1-2 provides a list of figures associated with the completion of the final status surveys for the Impacted-Class 3 areas. These figures depict the grid map and survey sampling locations for the impacted areas.

Table 12-1-3 provides a summary of the NMRC Rockville Annex survey units. Each survey unit was classified as either Non-impacted or Impacted Class 3. **Table 12-1-3** also lists discrete rooms or areas. In some instances, a room may have been sub-divided to accomplish a workable survey unit. These sub-divisions are indicated in column three of **Table 12-1-3** as parenthesized comments.

Table 12-1-1. List of Tables

NUMBER	DESCRIPTION	PAGE NUMBER
12-1-3	NMRC Rockville Annex Survey Units	122
12-2-1	RADIOLOGICAL FINAL STATUS SURVEY SUMMARIES -- NMRC Rockville Annex, Second Floor Non-impacted Areas	125
12-2-2	RADIOLOGICAL FINAL STATUS SURVEY DATA -- NMRC Rockville Annex, Second Floor Non-impacted Areas	126
12-3-1	RADIOLOGICAL FINAL STATUS SURVEY SUMMARIES -- NMRC Rockville Annex, First Floor Non-impacted Areas	129
12-3-2	RADIOLOGICAL FINAL STATUS SURVEY DATA -- NMRC Rockville Annex, First Floor Non-impacted Areas	130
12-3-3	RADIOLOGICAL FINAL STATUS SURVEY DATA -- NMRC Rockville Annex, Background Data, First Floor Non-impacted Areas	131
12-4-1	RADIOLOGICAL FINAL STATUS SURVEY SUMMARIES -- NMRC Rockville Annex, Second Floor Impacted Class 3 Areas	135
12-4-2A	Final Status Survey Summary For Direct Readings of Impacted Survey Units Using a Gas Proportional Counter	137
12-4-2B	Final Status Survey Summary for Direct Readings of Impacted Survey Units Using a Gas Proportional Counter	138
12-4-3A	Final Status Survey Summary For Direct Readings of Impacted Survey Units Using a Gas Proportional Counter	139
12-4-3B	Final Status Survey Summary For Direct Readings of Impacted Survey Units Using a Gas Proportional Counter	140
12-4-4A	Final Status Survey Summary For Direct Readings Using a Gas Proportional Counter	141
12-4-4B	Final Status Survey Summary For Direct Readings Using a Gas Proportional Counter	142
12-4-5	Annex 201 - Random Statistical Survey Data	143
12-4-6	Annex 201 - Additional Select Samples	144
12-4-7	Annex 213-1 - Random Statistical Samples	146
12-4-8	Annex 213-1 - Additional Select Samples	147
12-4-9	Annex 213-2 - Random Statistical Samples	149
12-4-10	Annex 213-2 - Additional Select Samples	150
12-4-11	Annex 213A - Summary for 100% Coverage	152
12-4-12	Annex 213A - Additional Select Samples	154

12-4-13	Annex 213B - Random Statistical Samples	156
12-4-14	Annex 213B - Additional Select Samples	158
12-4-15	Annex 218 - Summary for 100% Coverage	160
12-4-16	Annex 218 - Additional Select Samples	162
12-4-17	Annex 218A - Summary for 100% Coverage	164
12-4-18	Annex 218A - Additional Select Samples	165
12-4-19	Annex 218B - Summary for 100% Coverage	167
12-4-20	Annex 218B - Additional Select Samples	168
12-4-21	Annex 219-1 - Random Statistical Samples	170
12-4-22	Annex 219-1 - Additional Select Samples	171
12-4-23	Annex 219-2 - Random Statistical Samples	173
12-4-24	Annex 219-2 - Additional Select Samples	174
12-4-25	Annex 219A - Random Statistical Samples	176
12-4-26	Annex 219A - Additional Select Samples	177
12-4-27	Annex 219B - Random Statistical Samples	179
12-4-28	Annex 219B - Additional Select Samples	180
12-4-29	Annex 219B - Quality Control Samples	181
12-4-30	Annex 220-1 - Random Statistical Samples	183
12-4-31	Annex 220-1 - Additional Select Samples	184
12-4-32	Annex 220-2 - Random Statistical Samples	186
12-4-33	Annex 220-2 - Additional Select Samples	187
12-4-34	Annex 220-3 - Summary for 100% Coverage	189
12-4-35	Annex 220-3 - Additional Select Samples	190
12-4-36	Annex 221 - Random Statistical Samples	192
12-4-37	Annex 221 - Additional Select Samples	193
12-5-1	Final Status Survey Summaries, NMRC Rockville Annex, First Floor Impacted Class 3 Areas and Other Areas	197
12-5-2	Annex 110-1 - Random Statistical Samples	199
12-5-3	Annex 110-1 - Additional Select Samples	200
12-5-4	Annex 110-2 - Random Statistical Samples	202
12-5-5	Annex 110-2 - Additional Select Samples	203
12-5-6	Annex 110A - Random Statistical Samples	205
12-5-7	Annex 110A - Additional Select Samples	206
12-5-8	Annex 110B - Random Statistical Samples	208
12-5-9	Annex 110B - Additional Select Samples	209
12-5-10	Annex 111 - Random Statistical Samples	211
12-5-11	Annex 111 - Additional Select Samples	212
12-5-12	Annex 112 - Random Statistical Samples	214
12-5-13	Annex 112 - Additional Select Samples	215
12-5-14	Annex 113 - Summary for 100% Coverage	217
12-5-15	Annex 113 - Additional Select Samples	219
12-5-16	Annex 114 - Random Statistical Samples	221
12-5-17	Annex 114 - Additional Select Samples	222
12-5-18	Annex 115 - Random Statistical Samples	224
12-5-19	Annex 115 - Additional Select Samples	225

12-5-20	Annex 115 - Sink, pre-decontamination surveys	228
12-5-21a	Annex 115 - Sink, post-decontamination surveys	229
12-5-21b	Annex 115 - Sink, post-decontamination surveys	230
12-5-22	Annex 123 - Random Statistical Samples	231
12-5-23	Annex 123 - Additional Select Samples	232
12-5-24	Annex 124 - Summary for 100% Coverage	234
12-5-25	Annex 124 - Additional Select Samples	235
12-5-26	Annex 125 - Summary for 100% Coverage	237
12-5-27	Annex 125 - Additional Select Samples	238
12-5-28	Annex 126 - Random Statistical Samples	240
12-5-29	Annex 126 - Additional Select Samples	241
12-5-30	Annex 127 - Random Statistical Samples	243
12-5-31	Annex 127 - Additional Select Samples	244
12-5-32	Annex 128-1 - Random Statistical Samples	246
12-5-33	Annex 128-1 - Additional Select Samples	247
12-5-34	Annex 128-2 - Random Statistical Samples	249
12-5-35	Annex 128-2 - Additional Select Samples	250
12-5-36	Annex 1st Floor Hallways - Random Statistical Survey Data	252
12-5-37	Annex 2nd Floor hallways - Additional or Control Survey Data	255
12-5-38	Annex Stair A - Control and Selected Samples	257
12-5-39	Annex Stair B - Control and Selected Samples	258
12-5-40	Annex Loading Dock Area - 100% Sampling	260
12-5-41	Annex Loading Dock Storage - 100% Sampling	263
12-5-42	Annex Radiation Waste Locker (RWL) - 100% Statistical Survey Data (pre-decontamination surveys)	265
12-5-43	Annex Radiation Waste Locker - 100% Statistical Survey Data (post-decontamination surveys)	268
12-5-44	Annex Storage Closet - 100% Coverage	270

Table 12-1-2. List of Figures (Grid Maps annotated with survey-data locations)

Number	Description	Page Number
12-4-1	Grid Map for Rockville Annex, Room 201	145
12-4-2	Grid Map for Rockville Annex, Room 213-1	148
12-4-3	Grid Map for Rockville Annex, Room 213-2	151
12-4-4	Grid Map for Rockville Annex, Room 213A	155
12-4-5	Grid Map for Rockville Annex, Room 213B	159
12-4-6	Grid Map for Rockville Annex, Room 218	163
12-4-7	Grid Map for Rockville Annex, Room 218A	166
12-4-8	Grid Map for Rockville Annex, Room 218B	169
12-4-9	Grid Map for Rockville Annex, Room 219-1	172
12-4-10	Grid Map for Rockville Annex, Room 219-2	175
12-4-11	Grid Map for Rockville Annex, Room 219A	178
12-4-12	Grid Map for Rockville Annex, Room 219B	182
12-4-13	Grid Map for Rockville Annex, Room 220-1	185
12-4-14	Grid Map for Rockville Annex, Room 220-2	188
12-4-15	Grid Map for Rockville Annex, Room 220-3	191
12-4-16	Grid Map for Rockville Annex, Room 221	194
12-5-1	Grid Map for Rockville Annex, Room 110-1	201
12-5-2	Grid Map for Rockville Annex, Room 110-2	204
12-5-3	Grid Map for Rockville Annex, Room 110A	207
12-5-4	Grid Map for Rockville Annex, Room 110B	210
12-5-5	Grid Map for Rockville Annex, Room 111	213
12-5-6	Grid Map for Rockville Annex, Room 112	216
12-5-7	Grid Map for Rockville Annex, Room 113	220
12-5-8	Grid Map for Rockville Annex, Room 114	223
12-5-9	Grid Map for Rockville Annex, Room 115	227
12-5-10	Grid Map for Rockville Annex, Room 123	233
12-5-11	Grid Map for Rockville Annex, Room 124	236
12-5-12	Grid Map for Rockville Annex, Room 125	239
12-5-13	Grid Map for Rockville Annex, Room 126	242
12-5-14	Grid Map for Rockville Annex, Room 127-1	245
12-5-15	Grid Map for Rockville Annex, Room 128	248
12-5-16	Grid Map for Rockville Annex, Room 128-2	251
12-5-17	Grid Map, Rockville Annex, First Floor Halls	254
12-5-18	Grid Map, Rockville Annex, Loading Dock Room	262
12-5-19	Grid Map, Rockville Annex, Loading Dock Storage	264
12-5-20	Grid Map, Rockville Annex, Radioactive Waste Locker (RWL)	269
12-5-21	Grid Map for Rockville Annex, hall Closet (near RWL)	271

Table 12-1-3. NMRC Rockville Annex Survey Units

DATE COMPLETED	BUILDING	ROOM OR AREA	DESCRIPTION	ISOTOPES OF CONCERN	D&D CLASSIFICATION
3/28/00	Annex	RWL	RAM Waste Locker	H3,C14,P32, S35, Cr51	Impacted, Class 3
3/28/00	Annex	LDS	Loading Dock Storage	H3,C14,P32, S35, Cr51	Impacted, Class 3
3/28/00	Annex	LDR	Loading Dock Room	H3,C14,P32, S35, Cr51	Impacted, Class 3
2/14/00	Annex	Halls	First floor hallways		Non-impacted
2/22/00	Annex	Halls	Second floor hallways		Non-impacted
3/28/00	Annex	Stair B	Stairway B (two floors)		Non-impacted
2/10/00	Annex	Stair A	Stairway A (two floors)		Non-impacted
2/9/00	Annex	100	Office		Non-impacted
2/9/00	Annex	102	Office		Non-impacted
2/9/00	Annex	103	Office		Non-impacted
2/9/00	Annex	104	Office		Non-impacted
2/9/00	Annex	105	Machine room		Non-impacted
2/9/00	Annex	106	Lavatory		Non-impacted
2/9/00	Annex	107	Lavatory		Non-impacted
2/9/00	Annex	108	Office		Non-impacted
2/9/00	Annex	109	Office/Duty Room		Non-impacted
2/11/00	Annex	110B	Office	H3,C14,P32, S35, Cr51	Impacted, Class 3
2/11/00	Annex	110A	Office	H3,C14,P32, S35, Cr51	Impacted, Class 3
2/14/00	Annex	110 (110-1, 110-2)	Laboratory	H3,C14,P32, S35, Cr51	Impacted, Class 3
2/16/00	Annex	111	Equipment Storage	H3,C14,P32, S35, Cr51	Impacted, Class 3
2/17/00	Annex	112	Sterilizer Room/Laboratory	H3,C14,P32, S35, Cr51	Impacted, Class 3
2/17/00	Annex	113	Laboratory	H3,C14,P32, S35, Cr51	Impacted, Class 3
2/11/00	Annex	114	Laboratory	H3,C14,P32, S35, Cr51	Impacted, Class 3
2/16/00	Annex	115	Laboratory	H3,C14,P32, S35, Cr51	Impacted, Class 3
2/10/00	Annex	116	Dark Room		Non-impacted
2/10/00	Annex	117	Storage Room		Non-impacted
2/10/00	Annex	118C	Insect Room		Non-impacted
2/10/00	Annex	118B	Insect Room		Non-impacted
2/10/00	Annex	118A	Insect/Animal Room		Non-impacted
2/10/00	Annex	118	Insect Room		Non-impacted
2/11/00	Annex	123	Laboratory	H3,C14,P32, S35, Cr51	Impacted, Class 3
2/17/00	Annex	124	Cold Room	H3,C14,P32, S35, Cr51	Impacted, Class 3
2/17/00	Annex	125	Insect Room	H3,C14,P32, S35, Cr51	Impacted, Class 3
2/14/00	Annex	126	Laboratory	H3,C14,P32, S35, Cr51	Impacted, Class 3

2/11/00	Annex	127	Laboratory	H3,C14,P32, S35, Cr51	Impacted, Class 3
2/14/00	Annex	128 (128-1, 128-2)	Laboratory	H3,C14,P32, S35, Cr51	Impacted, Class 3
2/8/00	Annex	201	Laboratory	H3,C14,P32, S35, Cr51	Impacted, Class 3
1/19/00	Annex	202	Office		Non-impacted
1/24/00	Annex	203	Office		Non-impacted
1/21/00	Annex	204	Office		Non-impacted
1/24/00	Annex	205	Office		Non-impacted
1/21/00	Annex	206	Office		Non-impacted
1/19/00	Annex	207	Office		Non-impacted
1/21/00	Annex	208	Conference Room		Non-impacted
1/21/00	Annex	209	Office		Non-impacted
1/21/00	Annex	210	Office		Non-impacted
1/21/00	Annex	211	Office		Non-impacted
1/21/00	Annex	212	Lunchroom		Non-impacted
2/15/00	Annex	213B	Gamma Counter	H3,C14,P32, S35, Cr51	Impacted, Class 3
2/17/00	Annex	213A	Storage	H3,C14,P32, S35, Cr51	Impacted, Class 3
2/8/00	Annex	213 (213-1, 213-2)	Freezer/Storage	H3,C14,P32, S35, Cr51	Impacted, Class 3
1/24/00	Annex	214 (214-1, 214-2, 214-3)	Laboratory		Non-impacted
1/24/00	Annex	215A	Animal Room		Non-impacted
1/24/00	Annex	215	Laboratory		Non-impacted
1/24/00	Annex	216	Animal Room		Non-impacted
1/24/00	Annex	217	Laboratory		Non-impacted
2/15/00	Annex	218B	Cold Room	H3,C14,P32, S35, Cr51	Impacted, Class 3
2/15/00	Annex	218A	Cold Room	H3,C14,P32, S35, Cr51	Impacted, Class 3
2/15/00	Annex	218	Storage	H3,C14,P32, S35, Cr51	Impacted, Class 3
2/4/00	Annex	219B	Laboratory	H3,C14,P32, S35, Cr51	Impacted, Class 3
2/3/00	Annex	219A	Laboratory	H3,C14,P32, S35, Cr51	Impacted, Class 3
2/3/00	Annex	219 (219-1, 219-2)	Laboratory	H3,C14,P32, S35, Cr51	Impacted, Class 3
2/2/00	Annex	220 (220-1, 220-2, 220-3)	Laboratory	H3,C14,P32, S35, Cr51	Impacted, Class 3
2/1/00	Annex	221	Tissue Culture	H3,C14,P32, S35, Cr51	Impacted, Class 3
1/24/00	Annex	222	Lavatory		Non-impacted
1/24/00	Annex	223	Lavatory		Non-impacted
1/24/00	Annex	224	Lavatory, female		Non-impacted

XII. APPENDIX E

Appendix E-2. Rockville Annex, Second Floor, Non-impacted Areas

- Location: NMRC Rockville Annex, Second Floor Non-impacted Areas

- Monitoring Date(s): 19, 21, and 24 Jan 00

- Radioactive Contaminants of Concern: None

- Minimum Control Beta Swipe Locations (performed for every survey unit): (1) floor at door in room; (2) floor at door outside room; (3) doorknob in room; (4) doorknob outside room; and (5) light switch inside room.

- Survey Instrument Information:
  - Beta meters -- serial numbers (background CPM): 11030 (<100CPM), 54537 (<100 CPM)
  - Gamma meters -- serial numbers (background CPM): 114886 (<300 CPM), 121730 (<200 CPM), 121886 (<300 CPM)
  - Liquid Scintillation Counter: Packard 2500TR, S/N 403848

- Radiation-detection Action Limits:
  - 2 to 3 times background for beta and gamma scans
  - 500 - 700 dpm or higher for either H-3 or C-14 beta swipes counted using a liquid scintillation counter

- Summary of Radiological Scans and Swipe Results:
  - Background level for all beta and gamma scans
  - All H-3 and C-14 beta swipe results below Action Limits

- Contamination and Remedial Actions: None

- Conclusion: The radiological monitoring results for all survey units addressed in this section meet the criteria for release for unrestricted use.

TABLE 12-2-1. RADIOLOGICAL FINAL STATUS SURVEY SUMMARIES
NMRC Rockville Annex, Second Floor Non-impacted Areas

Date	Room number or area (Survey Unit)	Beta and/or Gamma Scan Monitoring (check if yes)	Maximum Random or Control beta (H-3 or C-14) swipe result (DPM)	Recommend Survey Unit for radiological clearance (Y/N)
1/19/00	202	Y	123	Y
1/24/00	203	Y	187	Y
1/21/00	204	Y	66	Y
1/24/00	205	Y	76	Y
1/21/00	206	Y	18	Y
1/19/00	207	Y	96	Y
1/21/00	208	Y	147	Y
1/21/00	209	Y	93	Y
1/21/00	210	Y	112	Y
1/21/00	211	Y	54	Y
1/21/00	212	Y	46	Y
1/24/00	214 (214-1, 214-2, 214-3)	Y	97	Y
1/24/00	215	Y	79	Y
1/24/00	216	Y	102	Y
1/24/00	217	Y	83	Y
1/24/00	222	Y	67	Y
1/24/00	223	Y	27	Y
1/24/00	224	Y	168	Y

TABLE 12-2-2. RADIOLOGICAL FINAL STATUS SURVEY DATA
NMRC Rockville Annex, Second Floor Non-impacted Areas

Swipe locations: (1) floor at door in room; (2) floor at door outside room; (3) doorknob in room; (4) doorknob outside room; and (5) light switch inside room. * denotes extra data for additional doorways or select swipe locations

Date	Room number or area (Survey Unit)	Controls - Beta Swipe Results for H-3					Controls - Beta Swipe Results for C-14				
		#1	#2	#3	#4	#5	#1	#2	#3	#4	#5
1/19/00	202	24	12	26	33	123	8	2	14	6	3
1/24/00	203	20	10	94	187	58	8	5	5	4	10
1/21/00	204	50	65	27	65	19	4	10	6	2	11
1/24/00	205	76	32	55	44	34	11	6	11	6	3
1/21/00	206	8	18	18	6	13	15	6	17	10	9
1/19/00	207	96	47	22	0	50	7	7	7	8	9
1/21/00	208	14	13	38	147	1	12	9	4	0	12
1/21/00	208*	10	17	41	37	3	12	6	3	4	7
1/21/00	209	34	23	52	93	17	10	12	6	0	7
1/21/00	210	7	12	112	65	18	12	12	4	7	11
1/21/00	211	23	32	54	48	21	9	5	4	4	4
1/21/00	212	14	34	0	46	8	10	6	12	3	4
1/21/00	212*	7	6	24	4	14	13	15	12	12	5
1/24/00	214	28	21	97	48	44	8	7	6	7	12
1/24/00	215	21	25	79	62	60	15	5	11	9	3
1/24/00	216	10	29	23	70	102	9	9	6	3	4
1/24/00	217	0	11	83	14	56	11	15	8	8	5
1/24/00	222	27	17	48	28	67	8	8	3	14	6
1/24/00	223	6	8	20	28	25	8	10	4	8	6
1/24/00	224	13	14	100	168	18	9	9	2	0	8
Average		24	22	51	60	38	10	8	7	6	7
Standard Devi-ation		24	15	33	53	33	3	3	4	4	3
Maximum Value		96	65	112	187	123	15	15	17	14	12

Quality Assurance Checklist

Building number or location: NMRC Rockville Annex, Second Floor Non-impacted Areas
Monitoring Date(s): 19, 21, and 24 Jan 00

Y - Appropriate and satisfactory daily and weekly calibration checks were completed for the selected survey monitoring equipment and instruments.

Y - Selected meters with current calibrations for the isotopes of concern.

Y - Survey maps or floor plans (for all survey units) and grid maps (for known RAM-use areas) were available.

Y - Background checks were performed when impacted areas were monitored.

Y - For known RAM-use survey units, additional checks were performed (workbenches, shelves, sinks, basins, traps, floor at sinks and entrances, wall at hoods and sinks, and/or other areas as deemed appropriate).

Y - Mean values, single sample values, and background values were below the action limits, indicating no contamination was found.

Y - Representative floor plans, sketches, and photographs were available.

Y - Deviation from survey plans and objectives were documented.

Y - Extent of remediation actions were documented.

Y - All selected survey units passed D&D tests; units are recommended for unrestricted release.

Y - Additional Checks/Data passed D&D tests; unit is recommended for unrestricted release.

Notes: Tests included complying with applicable elements of the MARSSIM Final Status Survey checklist, mean-value and single-value comparisons of survey-unit data to action limits (DCGLs), mean-value comparison to background, completion of required monitoring, and satisfactory scan monitoring results.

Quality Assurance Leader: Schleurious L. Gaiter, LCDR, MSC, USN

XII. APPENDIX E

Appendix E-3. Rockville Annex, First Floor, Non-impacted Areas

- Location: NMRC Rockville Annex, First Floor Non-impacted Areas

- Monitoring Date(s): 10-11 Feb 00

- Radioactive Contaminants of Concern: None

- Minimum Control Beta Swipe Locations (performed for every survey unit): (1) floor at door in room; (2) floor at door outside room; (3) doorknob in room; (4) doorknob outside room; and (5) light switch inside room.

- Survey Instrument Information:
  - Beta meters -- serial numbers (background CPM): 11030 (<100CPM), 54537 (<100 CPM)
  - Gamma meters -- serial numbers (background CPM): 114886 (<300 CPM), 121730 (<200 CPM), 121886 (<300 CPM)
  - Liquid Scintillation Counter: Packard 2500TR, S/N 403848

- Radiation-detection Action Limits:
  - 2 to 3 times background for beta and gamma scans
  - 500 - 700 dpm or higher for either H-3 or C-14 beta swipes counted using a liquid scintillation counter

- Summary of Radiological Scans and Swipe Results:
  - Background level for all beta and gamma scans
  - All H-3 and C-14 beta swipe results below Action Limits

- Contamination and Remedial Actions: None

- Conclusion: The radiological monitoring results for all survey units addressed in this section meet the criteria for release for unrestricted use.

TABLE 12-3-1. RADIOLOGICAL FINAL STATUS SURVEY SUMMARIES
NMRC Rockville Annex, First Floor Non-impacted Areas

Date	Room number or area (Survey Unit)	Beta and/or Gamma Scan Monitoring (check if yes)	Maximum Random or Control beta (H-3 or C-14) swipe result (DPM)	Recommend Survey Unit for radiological clearance (Y/N)
2/9/00	100	Y	24	Y
2/9/00	102	Y	27	Y
2/9/00	103	Y	24	Y
2/9/00	104	Y	26	Y
2/9/00	105	Y	21	Y
2/9/00	106	Y	23	Y
2/9/00	107	Y	27	Y
2/9/00	108	Y	19	Y
2/9/00	109	Y	20	Y
2/10/00	116	Y	107	Y
2/10/00	117	Y	36	Y
2/10/00	118	Y	48	Y
2/10/00	118A	Y	24	Y
2/10/00	118B	Y	35	Y
2/10/00	118C	Y	23	Y

TABLE 12-3-2. RADIOLOGICAL FINAL STATUS SURVEY DATA
NMRC Rockville Annex, First Floor Non-impacted Areas

Swipe locations: (1) floor at door in room; (2) floor at door outside room; (3) doorknob in room; (4) doorknob outside room; and (5) light switch inside room. * denotes extra data for additional doorways

Date	Room number or area (Survey Unit)	Controls - Beta Swipe Results for H-3					Controls - Beta Swipe Results for C-14				
		#1	#2	#3	#4	#5	#1	#2	#3	#4	#5
2/9/00	100	11	24	13	24	22	12	6	5	15	7
2/9/00	100*	8	7	11	15	14	8	4	11	11	14
2/9/00	102	8	14	18	24	27	9	3	8	11	18
2/9/00	103	11	24	6	13	17	9	13	13	5	9
2/9/00	104	16	12	14	17	18	9	9	26	22	8
2/9/00	105	14	10	16	21	0	14	8	12	10	10
2/9/00	106	11	15	23	8	12	2	4	7	11	17
2/9/00	107	3	22	18	27	14	7	6	10	10	6
2/9/00	108	8	18	15	16	19	14	16	4	11	6
2/9/00	109	11	19	17	9	20	7	7	5	10	11
2/10/00	116	68	107	48	19	20	15	10	11	12	11
2/10/00	116*	39					6				
2/10/00	117	10	36	26	17	18	22	3	8	13	18
2/10/00	117*	22					2				
2/10/00	118	25	15	42	26	30	6	6	15	8	7
2/10/00	118*	48					5				
2/10/00	118A	19	6	3	6	11	6	11	6	3	10
2/10/00	118A*	24					11				
2/10/00	118B	35	3	30	21	11	10	10	14	10	3
2/10/00	118B*	28	28				10	6			
2/10/00	118C	13	23	14	5	22	12	4	17	8	5

TABLE 12-3-3. RADIOLOGICAL FINAL STATUS SURVEY DATA
NMRC Rockville Annex, Background Data, First Floor Non-impacted Areas

LIQUID SCINTILLATION COUNTER EVALUATION OF BACKGROUND SWIPES FOR H-3 AND C-14

Date	2/9/00		2/10/00		2/11/00	
	H-3	C-14	H-3	C-14	H-3	C-14
Swipe #1	24	5	18	7	31	1
Swipe #2	10	12	17	12	19	5
Swipe #3	25	13	13	8	49	15
Swipe #4	22	12	19	11	42	2
Swipe #5	8	53	29	13	11	7
Swipe #6	29	6	22	15	45	5
Swipe #7	17	18	0	18	32	3
Swipe #8	8	15	18	15	30	6
Swipe #9	11	10	13	15	31	8
Swipe #10	7	13	13	11	23	7
Swipe #11	6	17	24	11	20	7
Swipe #12	18	9	27	6	19	12
Swipe #13	7	13	12	7	14	11
Swipe #14	25	22	16	8	27	2
Swipe #15	19	9	9	14	26	15
Swipe #16	16	8	15	11	25	8
Swipe #17	25	15	19	5	9	11
Swipe #18	21	11	25	9	12	15
Swipe #19	8	10	17	10	52	9
Swipe #20	25	12	24	7	29	11
Swipe #21	28	10	23	15	46	6
Average	17	14	18	11	28	8
Standard Deviation	8	10	7	4	13	4
Maximum Value	29	53	29	18	52	15

Quality Assurance Checklist

Building number or location: NMRC Rockville Annex, First Floor Non-impacted Areas
Monitoring Date(s): 9, 10 Feb 00

Y - Appropriate and satisfactory daily and weekly calibration checks were completed for the selected survey monitoring equipment and instruments.

Y - Selected meters with current calibrations for the isotopes of concern.

Y - Survey maps or floor plans (for all survey units) and grid maps (for known RAM-use areas) were available.

Y - Background checks were performed when impacted areas were monitored.

Y - For known RAM-use survey units, additional checks were performed (workbenches, shelves, sinks, basins, traps, floor at sinks and entrances, wall at hoods and sinks, and/or other areas as deemed appropriate).

Y - Mean values, single sample values, and background values were below the action limits, indicating no contamination was found.

Y - Representative floor plans, sketches, and photographs were available.

Y - Deviation from survey plans and objectives were documented.

Y - Extent of remediation actions were documented.

Y - All selected survey units passed D&D tests; units are recommended for unrestricted release.

Y - Additional Checks/Data passed D&D tests; unit is recommended for unrestricted release.

Notes: Tests included complying with applicable elements of the MARSSIM Final Status Survey checklist, mean-value and single-value comparisons of survey-unit data to action limits (DCGLs), mean-value comparison to background, completion of required monitoring, and satisfactory scan monitoring results.

Quality Assurance Leader: Schleurious L. Gaiter, LCDR, MSC, USN

XII. APPENDIX E

Appendix E-4. Rockville Annex, Second Floor, Impacted Class 3 Areas

- Location: NMRC Rockville Annex, Second Floor Impacted Class 3 Areas
- Monitoring Date(s): 1, 2, 3, 4, 8, 15, 16 Feb 00
- Radioactive Contaminants of Concern: Beta- and gamma-radiation emitters, Tritium (H-3), Carbon-14 (C-14), Phosphorus-32 (P-32), Sulfur-35 (S-35), and Chromium-51 (Cr-51).
- Minimum Control Beta Swipe Locations (performed for every survey unit): (1) floor at door in room; (2) floor at door outside room; (3) doorknob in room; (4) doorknob outside room; and (5) light switch inside room.
- Survey Instrument Information:
  - Beta meters -- serial numbers (background CPM): 11030 (<100CPM), 54537 (<100 CPM)
  - Gamma meters -- serial numbers (background CPM): 114886 (<300 CPM), 121730 (<200 CPM), 121886 (<300 CPM)
  - Liquid Scintillation Counter: Packard 2500TR, S/N 403848
- Radiation-detection Action Limits:
  - 2 to 3 times background for beta and gamma scans
  - 500 - 700 dpm or higher for either H-3 or C-14 beta swipes counted using a liquid scintillation counter
- Summary of Radiological Scans and Swipe Results:
  - Background level for all beta and gamma scans
  - All H-3 and C-14 beta swipe results below Action Limits
- Contamination and Remedial Actions: Room 220 (shown as results for survey unit 220-1). Beta/gamma scanning resulted in elevated readings for an isolated floor area, measuring approximately 4 square feet. Decontamination efforts consisted of

removing and disposing of the vinyl floor tiles and scrubbing the area with soap and water. Subsequent scanning and swipe-sample analysis revealed no elevated readings from the scans or swipe analyses.

- **Conclusion: The radiological monitoring results for all survey units addressed in this section meet the criteria for release for unrestricted use.**

TABLE 12-4-1. RADIOLOGICAL FINAL STATUS SURVEY SUMMARIES
NMRC Rockville Annex, Second Floor Impacted Class 3 Areas

Date	Room number or area (Survey Unit)	Beta and/or Gamma Scan Monitoring (check if yes)	Maximum Background beta (H-3 or C-14) swipe result (DPM)	Maximum Random or Control beta (H-3 or C-14) swipe result (DPM)	Recommend Survey Unit for radiological clearance (Y/N)
2/8/00	201	Y	25	32	Y
2/8/00	213-1	Y	25	57	Y
2/8/00	213-2	Y	25	26	Y
2/17/00	213A	Y	15	68	Y
2/15/00	213B	Y	31	49	Y
2/15/00	218	Y	31	28	Y
2/15/00	218A	Y	31	40	Y
2/15/00	218B	Y	31	19	Y
2/3/00	219-1	Y	57	117	Y
2/3/00	219-2	Y	57	53	Y
2/3/00	219A	Y	57	80	Y
2/4/00	219B	Y	49	104	Y
2/2/00	220-1	Y	53	126	Y
2/2/00	220-2	Y	53	73	Y
2/2/00	220-3	Y	53	69	Y
2/1/00	221	Y	76	336	Y

Quality Assurance Checklist

Building number or location: NMRC Rockville Annex, Second Floor Impacted Areas
Monitoring Date(s): 1, 2, 3, 4, 8, 15, 17 Feb 00

Y - Appropriate and satisfactory daily and weekly calibration checks were completed for the selected survey monitoring equipment and instruments.

Y - Selected meters with current calibrations for the isotopes of concern.

Y - Survey maps or floor plans (for all survey units) and grid maps (for known RAM-use areas) were available

Y - Background checks were performed when impacted areas were monitored.

Y - For known RAM-use survey units, additional checks were performed (workbenches, shelves, sinks, basins, traps, floor at sinks and entrances, wall at hoods and sinks, and/or other areas as deemed appropriate).

Y - Mean values, single sample values, and background values were below the action limits, indicating no contamination was found.

Y - Representative floor plans, sketches, and photographs were available.

Y - Deviation from survey plans and objectives were documented.

Y - Extent of remediation actions documented.

Y - All selected survey units passed D&D tests; units are recommended for unrestricted release.

Y - Additional Checks/Data passed D&D tests; unit is recommended for unrestricted release.

Notes: Tests included complying with applicable elements of the MARSSIM Final Status Survey checklist, mean-value and single-value comparisons of survey-unit data to action limits (DCGLs), mean-value comparison to background, completion of required monitoring, and satisfactory scan monitoring results.

Quality Assurance Leader: Schleurious L. Gaiter, LCDR, MSC, USN

Table 12-4-2A. Final Status Survey Summary For Direct Readings of Impacted Survey Units Using a Gas Proportional Counter

DATA CONVERSION WAS PERFORMED AS DESCRIBED BELOW

Building Number: Rockville Annex

Monitoring date(s): 4/14/00

MARSSIM formula 6-4:

$$\frac{dpm}{(100\ cm^2)} = \frac{(C_s/T_s) - (C_b/T_b)}{(E_i \times (A/100))}$$

where, A=126 cm^2, E_i = instrument efficiency = 0.15, sample and background count times = T_s = T_b= 1 minute, C_s = sample counts during time T_s, and C_b = background counts during time, T_b

Notes: Negative values of the calculated dpm were set equal to zero. CPM = cpm reading obtained using the gas proportional counter; DPM = calculated dpm/100 cm^2 value.

SAMPLE NUMBER	ROOM NUMBER: A110		ROOM NUMBER: A111		ROOM NUMBER: A113	
	CPM	DPM	CPM	DPM	CPM	DPM
1	268	185	221	0	266	228
2	249	85	237	0	255	169
3	221	0	245	0	238	79
4	239	32	255	37	263	212
5	238	26	297	259	261	201
6	269	190	264	85	245	116
7	262	153	250	11	237	74
8	221	0	233	0	226	16
9	247	74	251	16	207	0
10	222	0	245	0	249	138
11			225	0	253	159
AVERAGE, DPM	75		37		127	
STANDARD DEVIATION, DPM	77		78		77	
MAXIMUM VALUE, DPM	190		259		228	
BACKGROUND, CPM	233		248		223	
ACTION LIMIT	2,000		2,000		2,000	

Table 12-4-2B. Final Status Survey Summary For Direct Readings of Impacted Survey Units Using a Gas Proportional Counter

DATA CONVERSION WAS PERFORMED AS DESCRIBED IN TABLE 12-4-2A

Building Number: Rockville Annex

Monitoring date(s): 4/14/00

SAMPLE NUMBER	ROOM NUMBER: A115		ROOM NUMBER: A118		ROOM NUMBER: A124	
	CPM	DPM	CPM	DPM	CPM	DPM
1	322	365	198	0	180	0
2	315	328			207	0
3	256	16			188	0
4	258	26			201	0
5	310	302				
6	321	360				
7	309	296				
8	307	286				
9	297	233				
10	292	206				
11	307	286				
12	324	376				
13						
14						
AVERAGE, DPM	257		0		0	
STANDARD DEVIATION, DPM	121				0	
MAXIMUM VALUE, DPM	376		0		0	
BACKGROUND, CPM	253		220		207	
ACTION LIMIT	2,000		2,000		2,000	

Table 12-4-3A. Final Status Survey Summary For Direct Readings of Impacted Survey Units Using a Gas Proportional Counter

DATA CONVERSION WAS PERFORMED AS DESCRIBED IN TABLE 12-4-2A

Building Number: Rockville Annex

Monitoring date(s): 4/14/00

SAMPLE NUMBER	ROOM NUMBER: A126		ROOM NUMBER: A127		ROOM NUMBER: A128	
	CPM	DPM	CPM	DPM	CPM	DPM
1	229	116	216	48	235	0
2	207	0	233	138	242	0
3	241	180	229	116	263	63
4	213	32	234	143	233	0
5	211	21	275	360	249	0
6	222	79			252	5
7	262	291			250	0
8	237	159			239	0
9					234	0
10					269	95
11					260	48
12					269	95
13					248	0
14					264	69
AVERAGE, DPM	110		161		27	
STANDARD DEVIATION, DPM	98		118		38	
MAXIMUM VALUE, DPM	291		360		95	
BACKGROUND, CPM	207		202		251	
ACTION LIMIT	2,000		2,000		2,000	

Table 12-4-3B. Final Status Survey Summary For Direct Readings of Impacted Survey Units Using a Gas Proportional Counter

DATA CONVERSION WAS PERFORMED AS DESCRIBED IN TABLE 12-4-2A

Building Number: Rockville Annex

Monitoring date(s): 4/14/00

SAMPLE NUMBER	ROOM NUMBER: A201		ROOM NUMBER: A213		ROOM NUMBER: A213B	
	CPM	DPM	CPM	DPM	CPM	DPM
1	318	254	247	190	269	0
2	333	333	257	243	269	0
3	256	0	227	85	282	0
4	354	444	230	101	323	185
5	306	190	361	794		
6	234	0				
7						
8						
9						
10						
11						
12						
13						
14						
AVERAGE, DPM	204		283		46	
STANDARD DEVIATION, DPM	179		293		93	
MAXIMUM VALUE, DPM	444		794		185	
BACKGROUND, CPM	270		211		288	
ACTION LIMIT	2,000		2,000		2,000	

Table 12-4-4A. Final Status Survey Summary For Direct Readings of Impacted Survey Units Using a Gas Proportional Counter

DATA CONVERSION WAS PERFORMED AS DESCRIBED IN TABLE 12-4-2A

Building Number: Rockville Annex

Monitoring date(s): 4/14/00

SAMPLE NUMBER	ROOM NUMBER: 218		ROOM NUMBER: A219		ROOM NUMBER: A220	
	CPM	DPM	CPM	DPM	CPM	DPM
1	245	127	251	206	218	21
2	201	0	224	63	277	333
3	233	63	236	127	220	32
4	208	0	223	58	231	90
5	218	0	225	69	274	317
6	214	0	206	0	246	169
7			247	185	244	159
8			231	101	231	90
9			222	53	230	85
10			226	74	244	159
11			231	101		
12			222	53		
13			296	444		
14			269	302		
15			244	169		
16			230	95		
AVERAGE, DPM	32		131		146	
STANDARD DEVIATION, DPM	53		112		108	
MAXIMUM VALUE, DPM	127		444		333	
BACKGROUND, CPM	221		212		214	
ACTION LIMIT	2,000		2,000		2,000	

Table 12-4-4B. Final Status Survey Summary For Direct Readings of Impacted Survey Units Using a Gas Proportional Counter

DATA CONVERSION WAS PERFORMED AS DESCRIBED IN TABLE 12-4-2A

Building Number: Rockville Annex

Monitoring date(s): 4/14/00

SAMPLE NUMBER	ROOM NUMBER: A221		ROOM NUMBER: Annex Rad Waste Locker			
	CPM	DPM	CPM	DPM		
1	289	138	230	0		
2	294	164	300	53		
3	281	95	277	0		
4	286	122	318	148		
5	295	169	283	0		
6			320	159		
7			256	0		
8			286	0		
9						
10						
11						
12						
13						
14						
AVERAGE, DPM	138		45			
STANDARD DEVIATION, DPM	31		69			
MAXIMUM VALUE, DPM	169		159			
BACKGROUND, CPM	263		290			
ACTION LIMIT	2,000		2,000		2,000	

Table 12-4-5. Annex 201 - Final Status Survey Summary for RANDOM STATISTICAL SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 201				
Survey Date: 2/8/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	16	11	32	14
2	22	11	14	8
3	10	7	7	9
4	18	12	7	12
5	11	13	9	6
6	25	9	23	10
7	0	10	21	15
8	13	9	22	19
9	21	18	8	8
10	21	6	29	9
11	19	11	8	6
12	21	5	18	11
13	18	4	18	11
14	17	12	6	13
15	13	10	11	24
16	14	10	11	6
17	12	13	11	13
18	10	8	14	18
19	21	11	24	6
20	5	11	25	20
21	12	10	20	14
Average DPM	15	10	16	12
Standard Deviation, DPM	6	3	8	5
Maximum DPM	25	18	32	24
Action Limit, DPM			700	700

Table 12-4-6. Annex 201 - Final Status Survey Summary for ADDITIONAL SELECT SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 201				
Survey Date: 2/8/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	16	11	3	10
2	22	11	23	7
3	10	7	11	19
4	18	12	8	14
5	11	13	14	5
6	25	9	13	14
7	0	10	9	17
8	13	9	10	12
9	21	18	12	9
10	21	6	26	4
11	19	11	6	7
12	21	5	17	13
13	18	4	6	6
14	17	12	11	14
15	13	10		
16	14	10		
17	12	13		
18	10	8		
19	21	11		
20	5	11		
21	12	10		
Average DPM	15	10	12	11
Standard Deviation, DPM	6	3	6	5
Maximum DPM	25	18	26	19
Action Limit, DPM			700	700

Figure 12-4-1: Grid Map for Rockville Annex, Room 201
Survey date: 2/8/00
Survey results: background < 25 DPM; H-3 and C-14 < 32 DPM
R1-R21 = random statistical sample locations
C1-C13 = additional select sample locations

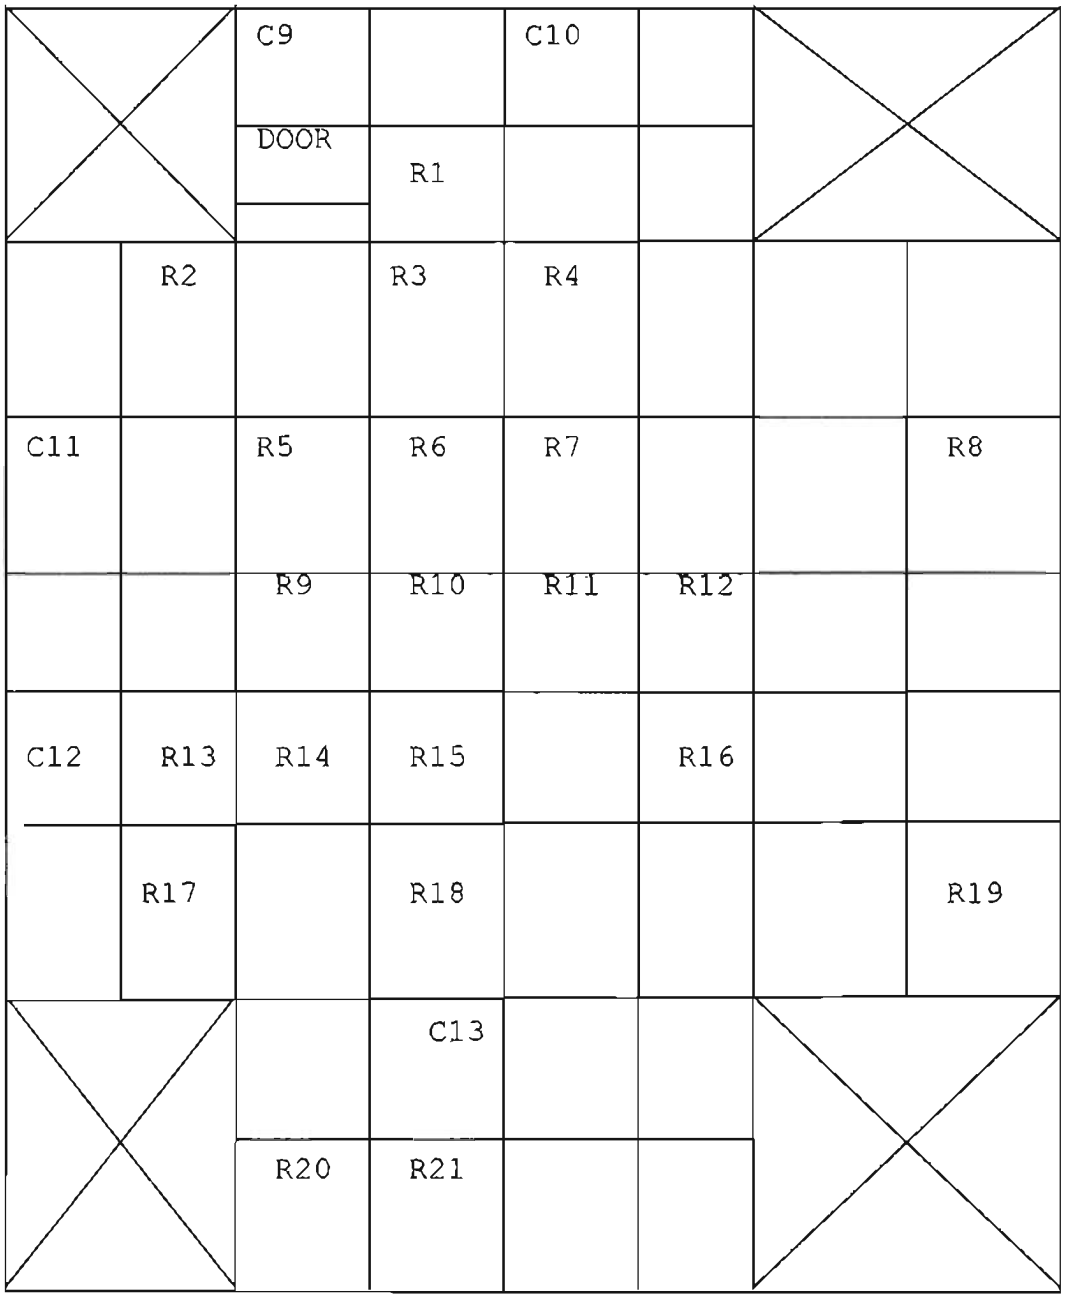

Table 12-4-7. Annex 213-1 - Final Status Survey Summary for RANDOM STATISTICAL SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 213-1				
Survey Date: 2/8/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	16	11	12	8
2	22	11	57	16
3	10	7	0	15
4	18	12	6	10
5	11	13	0	16
6	25	9	34	10
7	0	10	16	9
8	13	9	34	12
9	21	18	11	11
10	21	6	6	15
11	19	11	25	10
12	21	5	0	12
13	18	4	11	13
14	17	12	42	9
15	13	10	36	11
16	14	10	0	20
17	12	13	21	13
18	10	8	9	10
19	21	11	17	9
20	5	11	10	13
21	12	10	1	19
Average DPM	15	10	17	12
Standard Deviation, DPM	6	3	16	3
Maximum DPM	25	18	57	20
Action Limit, DPM			700	700

Table 12-4-8. Annex 213-1 - Final Status Survey Summary for ADDITIONAL SELECT SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 213-1				
Survey Date: 2/8/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	16	11	0	10
2	22	11	17	15
3	10	7	11	13
4	18	12	16	10
5	11	13	20	4
6	25	9	11	8
7	0	10	21	6
8	13	9	18	8
9	21	18	11	3
10	21	6	11	19
11	19	11	2	16
12	21	5	0	19
13	18	4	8	21
14	17	12		
15	13	10		
16	14	10		
17	12	13		
18	10	8		
19	21	11		
20	5	11		
21	12	10		
Average DPM	15	10	12	11
Standard Deviation, DPM	6	3	6	5
Maximum DPM	25	18	26	19
Action Limit, DPM			700	700

Figure 12-4-2: Grid Map for Rockville Annex, Room 213-1
Survey date: 2/8/00
Survey results: background < 25 DPM; H-3 and C-14 < 57 DPM
R1-R21 = random statistical sample locations
C1-C18 = additional select sample locations

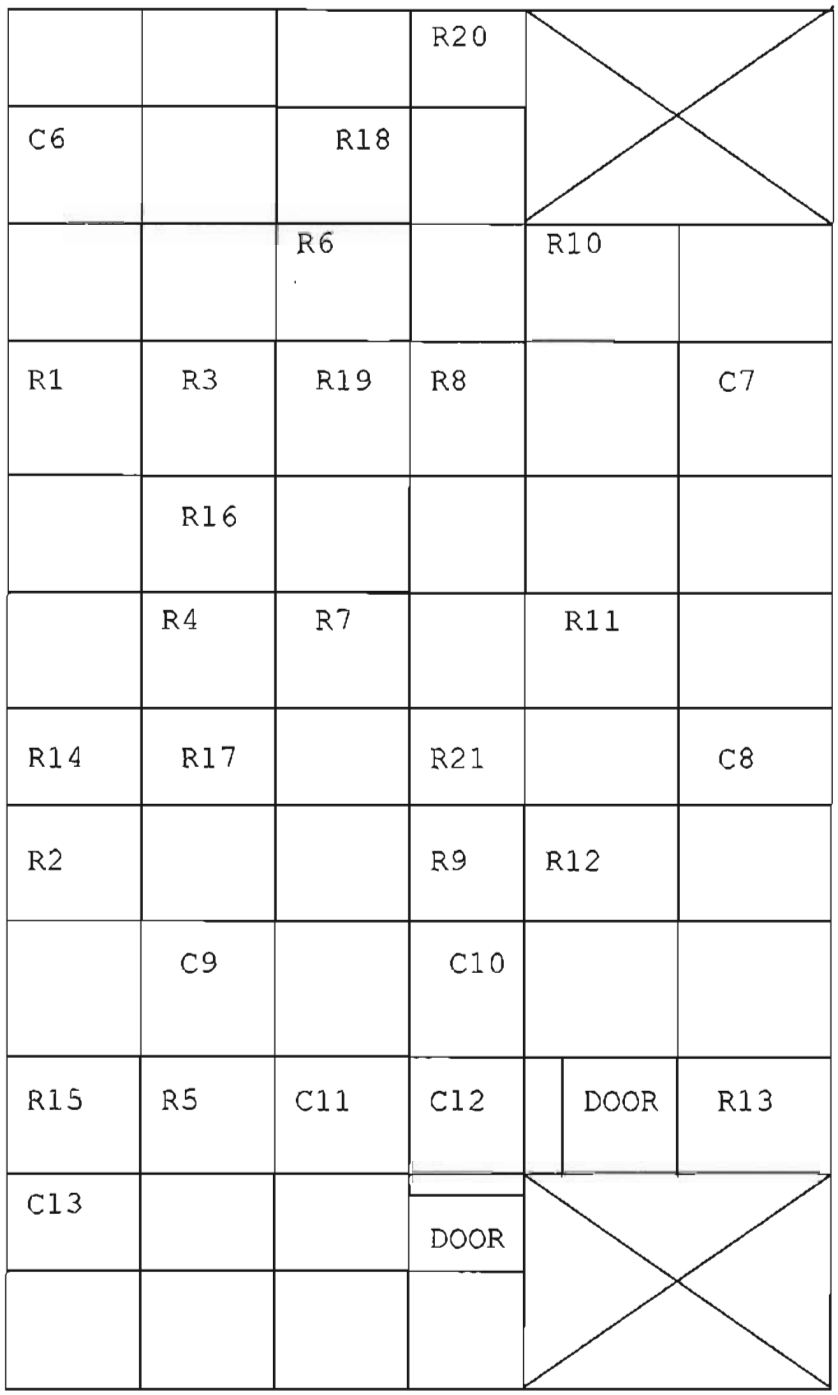

Table 12-4-9. Annex 213-2 - Final Status Survey Summary for RANDOM STATISTICAL SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 213-2				
Survey Date: 2/8/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	16	11	9	10
2	22	11	16	6
3	10	7	12	13
4	18	12	22	5
5	11	13	13	10
6	25	9	0	18
7	0	10	0	17
8	13	9	16	23
9	21	18	7	17
10	21	6	8	4
11	19	11	5	15
12	21	5	4	14
13	18	4	0	19
14	17	12	6	12
15	13	10	26	9
16	14	10	17	8
17	12	13	0	10
18	10	8	0	10
19	21	11	0	20
20	5	11	5	11
21	12	10	0	13
Average DPM	15	10	8	13
Standard Deviation, DPM	6	3	8	5
Maximum DPM	25	18	26	23
Action Limit, DPM			700	700

Table 12-4-10. Annex 213-2 - Final Status Survey Summary for ADDITIONAL SELECT SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 213-2				
Survey Date: 2/8/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	16	11	1	9
2	22	11	4	10
3	10	7	7	9
4	18	12	0	8
5	11	13	22	5
6	25	9	15	12
7	0	10	24	5
8	13	9	14	12
9	21	18		
10	21	6		
11	19	11		
12	21	5		
13	18	4		
14	17	12		
15	13	10		
16	14	10		
17	12	13		
18	10	8		
19	21	11		
20	5	11		
21	12	10		
Average DPM	15	10	11	9
Standard Deviation, DPM	6	3	9	3
Maximum DPM	25	18	24	12
Action Limit, DPM			700	700

Figure 12-4-3: Grid Map for Rockville Annex, Room 213-2
Survey date: 2/8/00
Survey results: background < 25 DPM; H-3 and C-14 < 26 DPM
R1-R21 = random statistical sample locations
C1-C8 = additional select sample locations

		R1		R2	
		R3	R4		R5
	R6			C6	
		R7		R8	
R9	R10	C8		R11	
R12			C9		R13
R14		R15		R16	
			R17		
R18	R19		C10		C11
R20	R21			C12	
		C13		C14	

Table 12-4-11. Annex 213A - Final Status Survey Summary for 100% Coverage				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 213A				
Survey Date: 2/17/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	5	14	2	6
2	6	5	1	9
3	9	13	0	7
4	13	8	3	7
5	3	8	9	5
6	7	4	7	10
7	9	4	5	19
8	1	7	4	8
9	11	9	0	15
10	0	8	0	14
11	0	11	3	14
12	10	10	14	9
13	8	10	13	8
14	3	8	2	5
15	3	10	6	7
16	14	6	3	11
17	13	8	4	7
18	13	11	3	11
19	9	6	10	8
20	5	15	9	4
21	9	15	4	13
22			7	14
23			4	21
24			4	14
25			0	12
26			8	3
27			9	11
28			0	12
29			0	12
30			15	11
31			3	8
32			3	11
33			14	13

34			17	7
35			1	9
36			4	5
37			15	12
38			0	4
39			1	9
40			4	16
41			0	1
42			0	4
43			1	9
44			11	9
45			25	2
46			11	18
Average DPM	7	9	6	10
Standard Deviation, DPM	4	3	6	4
Maximum DPM	14	15	25	21
Action Limit, DPM			700	700

Table 12-4-12. Annex 213A - Final Status Survey Summary for ADDITIONAL SELECT SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 213A				
Survey Date: 2/17/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	5	14	68	9
2	6	5	21	10
3	9	13	6	9
4	13	8	25	9
5	3	8	3	7
6	7	4	52	4
7	9	4	7	8
8	1	7	14	7
9	11	9	1	5
10	0	8	6	12
11	0	11		
12	10	10		
13	8	10		
14	3	8		
15	3	10		
16	14	6		
17	13	8		
18	13	11		
19	9	6		
20	5	15		
21	9	15		
Average DPM	7	9	20	8
Standard Deviation, DPM	4	3	23	2
Maximum DPM	14	15	68	12
Action Limit, DPM			700	700

Figure 12-4-4: Grid Map for Rockville Annex, Room 213A
Survey date: 2/17/00
Survey results: background < 15 DPM; H-3 and C-14 < 19 DPM
R1-R45 = random statistical sample locations
C1-C5 = additional select sample locations

		R33	R31		
		R34	R32		
R1	R2	R35	R40	R30	R29
R3	R4	R36	R41	R28	R27
R5	R6	R37	R42	R26	R25
R7	R8	R38	R43	R24	R23
R9	R10	R39	R44	R22	R21
R11	R12	R45	R46	R20	R19
R13	R14	R45	R46		
		R16	R18		
		R15	R17		

Table 12-4-13. Annex 213B - Final Status Survey Summary for 100%-COVERAGE (SAMPLES #1-#44)				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 213B				
Survey Date: 2/15/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	24	16	3	23
2	12	5	5	1
3	30	8	13	5
4	22	2	23	7
5	13	6	7	8
6	27	8	1	7
7	23	3	9	12
8	17	7	8	6
9	27	7	8	9
10	8	9	0	15
11	28	4	3	11
12	17	11	9	10
13	8	7	8	7
14	11	7	13	14
15	17	12	18	11
16	16	8	5	11
17	22	4	29	7
18	14	15	0	11
19	31	7	17	6
20	6	7	16	5
21	13	9	14	9
22			3	17
23			9	9
24			0	18
25			3	17
26			11	12
27			14	8
28			16	8
29			8	14
30			13	9
31			8	8
32			11	12
33			0	15

34			12	8
35			10	11
36			2	6
37			13	9
38			7	10
39			0	16
40			5	12
41			19	3
42			2	16
43			8	17
44			0	13
Average DPM	18	8	9	11
Standard Deviation, DPM	8	4	7	4
Maximum DPM	31	16	29	23
Action Limit, DPM			700	700

Table 12-4-14. Annex 213B - Final Status Survey Summary for ADDITIONAL SELECT SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 213B				
Survey Date: 2/15/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	24	16	9	14
2	12	5	4	11
3	30	8	17	6
4	22	2	12	8
5	13	6	12	6
6	27	8	49	7
7	23	3	13	12
8	17	7	4	6
9	27	7	11	9
10	8	9	21	11
11	28	4		
12	17	11		
13	8	7		
14	11	7		
15	17	12		
16	16	8		
17	22	4		
18	14	15		
19	31	7		
20	6	7		
21	13	9		
Average DPM	18	8	15	9
Standard Deviation, DPM	8	4	13	3
Maximum DPM	31	16	49	14
Action Limit, DPM			700	700

Figure 12-4-5: Grid Map for Rockville Annex, Room 213B
Survey date: 2/15/00
Survey results: background < 31 DPM; H-3 and C-14 < 49 DPM
R1-R44 = random statistical sample locations
C1-C10 = additional select sample locations

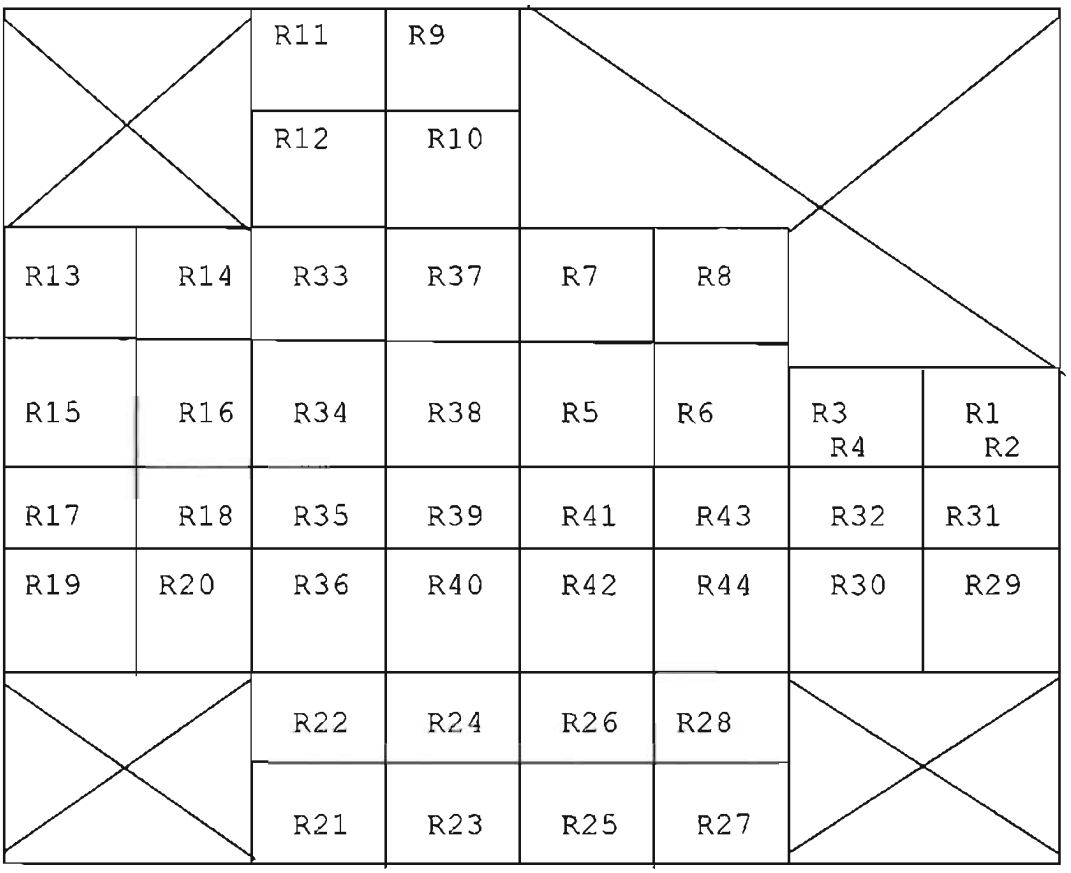

Table 12-4-15. Annex 218 - Final Status Survey Summary for 100%-COVERAGE (SAMPLES #1-#38)				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 218				
Survey Date: 2/15/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	24	16	11	4
2	12	5	0	12
3	30	8	8	14
4	22	2	28	9
5	13	6	12	13
6	27	8	7	6
7	23	3	13	12
8	17	7	7	15
9	27	7	18	14
10	8	9	17	10
11	28	4	10	8
12	17	11	13	5
13	8	7	22	7
14	11	7	10	7
15	17	12	12	17
16	16	8	8	10
17	22	4	5	18
18	14	15	0	10
19	31	7	14	2
20	6	7	19	11
21	13	9	17	9
22			5	9
23			24	8
24			19	6
25			9	6
26			14	8
27			4	10
28			10	11
29			8	9
30			7	9
31			9	14
32			18	12
33			6	15

34			5	12
35			11	17
36			6	6
37			18	8
38			4	9
Average DPM	18	8	11	10
Standard Deviation, DPM	8	4	6	4
Maximum DPM	31	16	28	18
Action Limit, DPM			700	700

Table 12-4-16. Annex 218 - Final Status Survey Summary for ADDITIONAL SELECT SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 218				
Survey Date: 2/15/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	24	16	6	15
2	12	5	6	15
3	30	8	12	3
4	22	2	15	5
5	13	6	3	14
6	27	8		
7	23	3		
8	17	7		
9	27	7		
10	8	9		
11	28	4		
12	17	11		
13	8	7		
14	11	7		
15	17	12		
16	16	8		
17	22	4		
18	14	15		
19	31	7		
20	6	7		
21	13	9		
Average DPM	18	8	8	10
Standard Deviation, DPM	8	4	5	6
Maximum DPM	31	16	15	15
Action Limit, DPM			700	700

Figure 12-4-6: Grid Map for Rockville Annex, Room 218
Survey date: 2/15/00
Survey results: background < 31 DPM; H-3 and C-14 < 28 DPM
R1-R38 = random statistical sample locations
C1-C5 = additional select sample locations

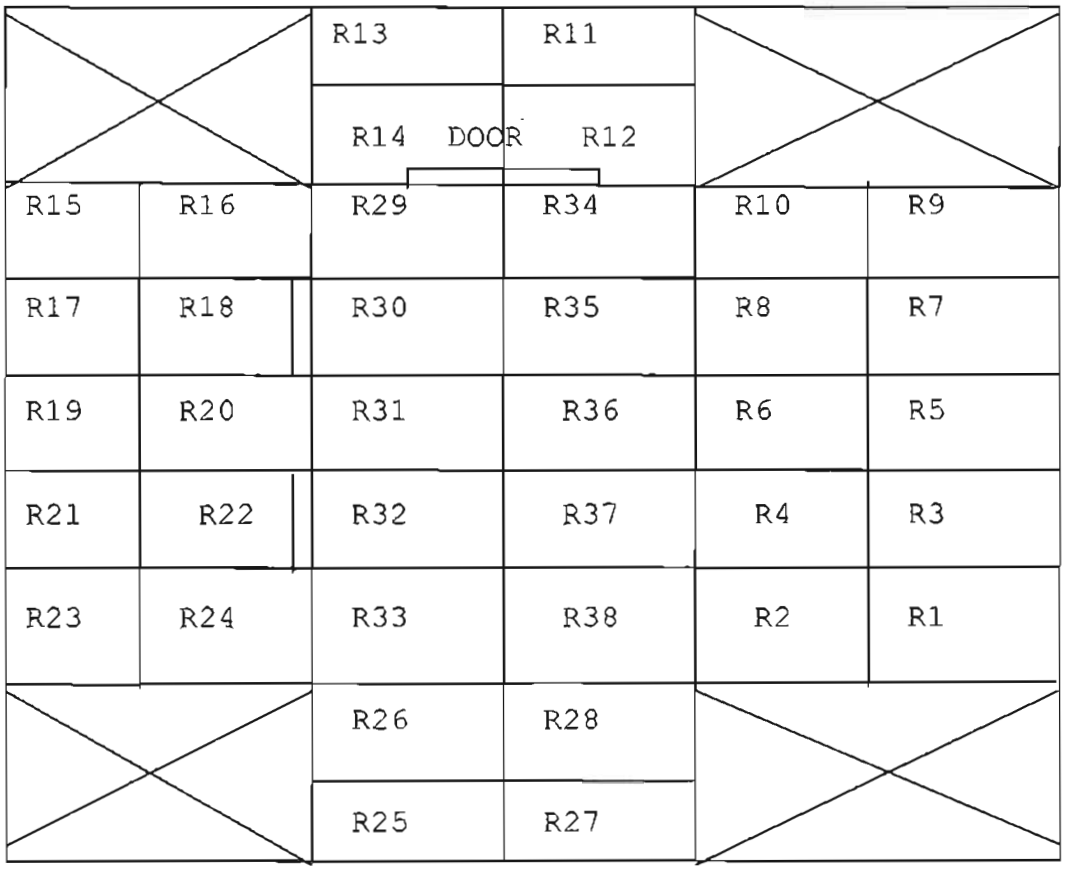

Table 12-4-17. Annex 218A - Final Status Survey Summary for 100%-COVERAGE (SAMPLES #1-#27)				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 218A				
Survey Date: 2/15/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination; Action Limit = 700 dpm				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	24	16	8	12
2	12	5	18	11
3	30	8	20	12
4	22	2	13	15
5	13	6	7	14
6	27	8	14	8
7	23	3	6	11
8	17	7	13	16
9	27	7	6	11
10	8	9	14	7
11	28	4	20	14
12	17	11	4	8
13	8	7	14	7
14	11	7	2	6
15	17	12	13	12
16	16	8	25	13
17	22	4	11	10
18	14	15	15	9
19	31	7	14	7
20	6	7	7	14
21	13	9	27	7
22			40	5
23			0	14
24			0	10
25			1	9
26			13	13
27			26	14
Average DPM	18	8	13	11
Standard Deviation, DPM	8	4	9	3
Maximum DPM	31	16	40	16

Table 12-4-18. Annex 218A - Final Status Survey Summary for ADDITIONAL SELECT SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 218A				
Survey Date: 2/15/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	24	16	0	10
2	12	5	18	13
3	30	8	8	12
4	22	2	21	13
5	13	6	12	8
6	27	8		
7	23	3		
8	17	7		
9	27	7		
10	8	9		
11	28	4		
12	17	11		
13	8	7		
14	11	7		
15	17	12		
16	16	8		
17	22	4		
18	14	15		
19	31	7		
20	6	7		
21	13	9		
Average DPM	18	8	12	11
Standard Deviation, DPM	8	4	8	2
Maximum DPM	31	16	21	13
Action Limit, DPM			700	700

Figure 12-4-7: Grid Map for Rockville Annex, Room 218A
Survey date: 2/15/00
Survey results: background < 31 DPM; H-3 and C-14 < 40 DPM
R1-R27 = random statistical sample locations
C1-C5 = additional select sample locations

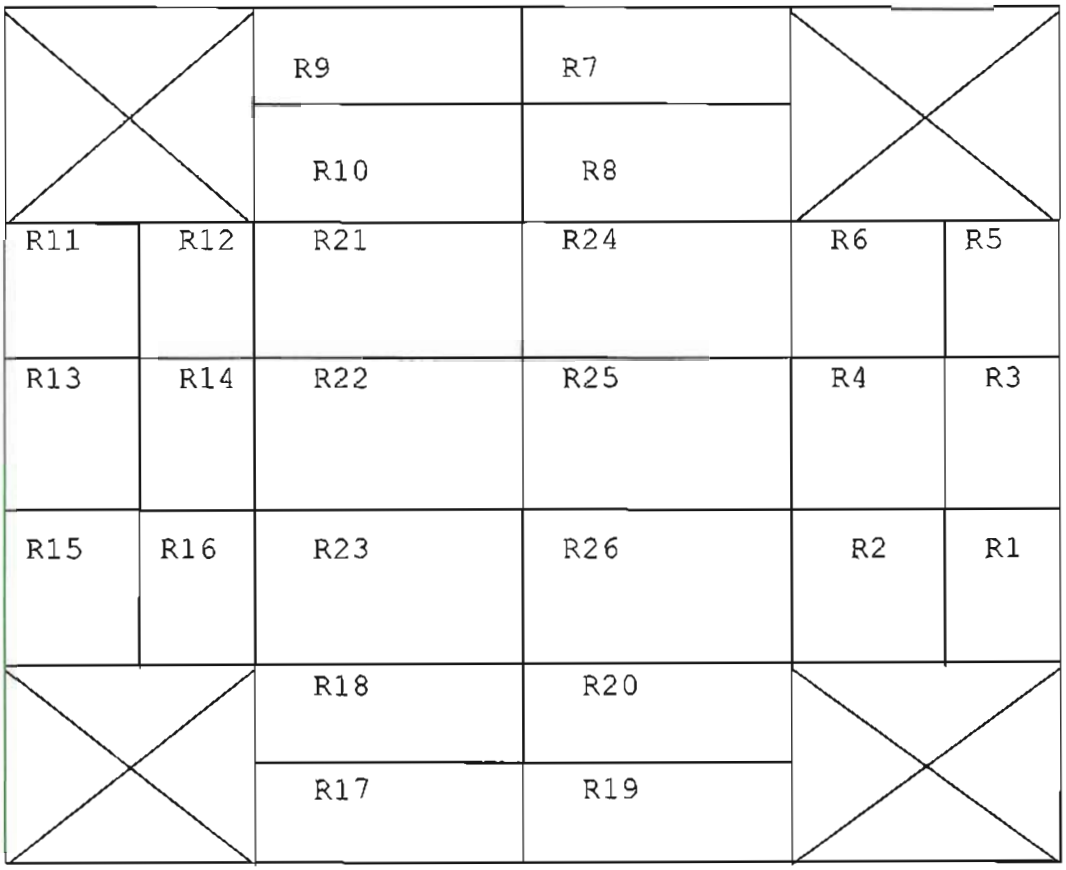

Table 12-4-19. Annex 218B – Final Status Survey Summary for 100%-COVERAGE (SAMPLES #1-#27)				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 218B				
Survey Date: 2/15/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination; Action Limit = 700 dpm				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	24	16	1	14
2	12	5	12	12
3	30	8	2	13
4	22	2	4	6
5	13	6	0	12
6	27	8	0	17
7	23	3	6	9
8	17	7	7	9
9	27	7	15	9
10	8	9	10	29
11	28	4	8	8
12	17	11	15	5
13	8	7	11	8
14	11	7	2	19
15	17	12	8	9
16	16	8	3	14
17	22	4	2	10
18	14	15	7	13
19	31	7	9	10
20	6	7	8	12
21	13	9	1	8
22			7	7
23			6	7
24			7	14
25			10	4
26			2	5
27			7	12
Average DPM	18	8	6	11
Standard Deviation, DPM	8	4	4	5
Maximum DPM	31	16	15	29

Table 12-4-20. Annex 218B - Final Status Survey Summary for ADDITIONAL SELECT SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 218B				
Survey Date: 2/15/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	24	16	16	17
2	12	5	1	9
3	30	8	5	8
4	22	2	10	19
5	13	6	12	10
6	27	8		
7	23	3		
8	17	7		
9	27	7		
10	8	9		
11	28	4		
12	17	11		
13	8	7		
14	11	7		
15	17	12		
16	16	8		
17	22	4		
18	14	15		
19	31	7		
20	6	7		
21	13	9		
Average DPM	18	8	9	13
Standard Deviation, DPM	8	4	6	5
Maximum DPM	31	16	16	19
Action Limit, DPM			700	700

Figure 12-4-8: Grid Map for Rockville Annex, Room 218B
Survey date: 2/15/00
Survey results: background < 31 DPM; H-3 and C-14 < 19 DPM
R1-R27 = random statistical sample locations
C1-C5 = additional select sample locations

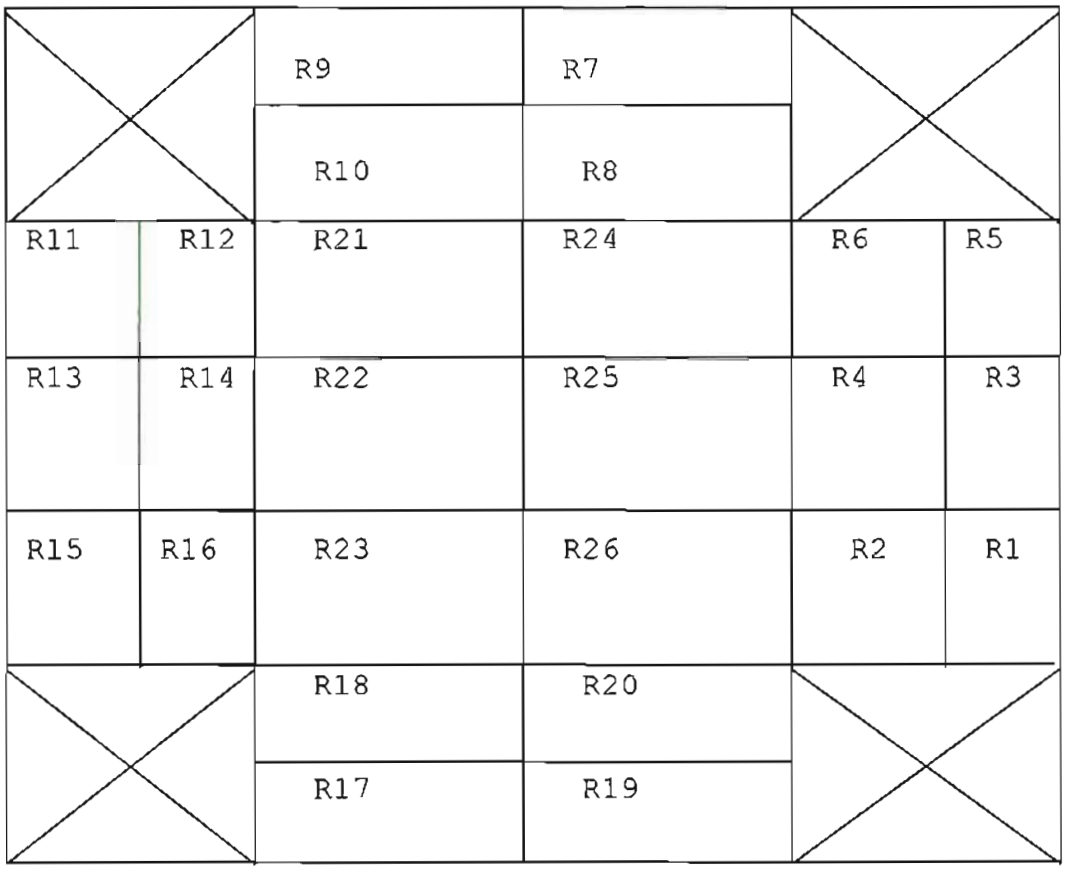

Table 12-4-21. Annex 219-1 - Final Status Survey Summary for RANDOM STATISTICAL SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 219-1				
Survey Date: 2/3/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	17	12	19	10
2	13	20	6	25
3	5	12	38	11
4	15	11	17	16
5	12	9	23	16
6	11	12	10	3
7	19	10	37	3
8	17	12	35	11
9	33	8	14	9
10	57	5	32	20
11	18	9	13	2
12	34	8	11	8
13	11	20	28	10
14	19	11	20	6
15	15	14	10	16
16	17	9	26	2
17	19	9	26	10
18	5	24	25	13
19	8	6	34	6
20	18	41	117	8
21	15	8	12	19
Average DPM	18	13	26	11
Standard Deviation, DPM	11	8	23	6
Maximum DPM	57	41	117	25
Action Limit, DPM			700	700

Table 12-4-22. Annex 219-1 - Final Status Survey Summary for ADDITIONAL SELECT SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 219-1				
Survey Date: 2/3/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	17	12	19	10
2	13	20	34	2
3	5	12	46	12
4	15	11	30	4
5	12	9	14	11
6	11	12	34	2
7	19	10	40	12
8	17	12	17	4
9	33	8	4	11
10	57	5	39	6
11	18	9	10	20
12	34	8	16	6
13	11	20	25	5
14	19	11	71	27
15	15	14	27	6
16	17	9	12	13
17	19	9		
18	5	24		
19	8	6		
20	18	41		
21	15	8		
Average DPM	18	13	27	9
Standard Deviation, DPM	11	8	17	7
Maximum DPM	57	41	71	27
Action Limit, DPM			700	700

Figure 12-4-9: Grid Map for Rockville Annex, Room 219-1
Survey date: 2/3/00
Survey results: background < 57 DPM; H-3 and C-14 < 117 DPM
R1-R21 = random statistical sample locations
C1-C16 = additional select sample locations

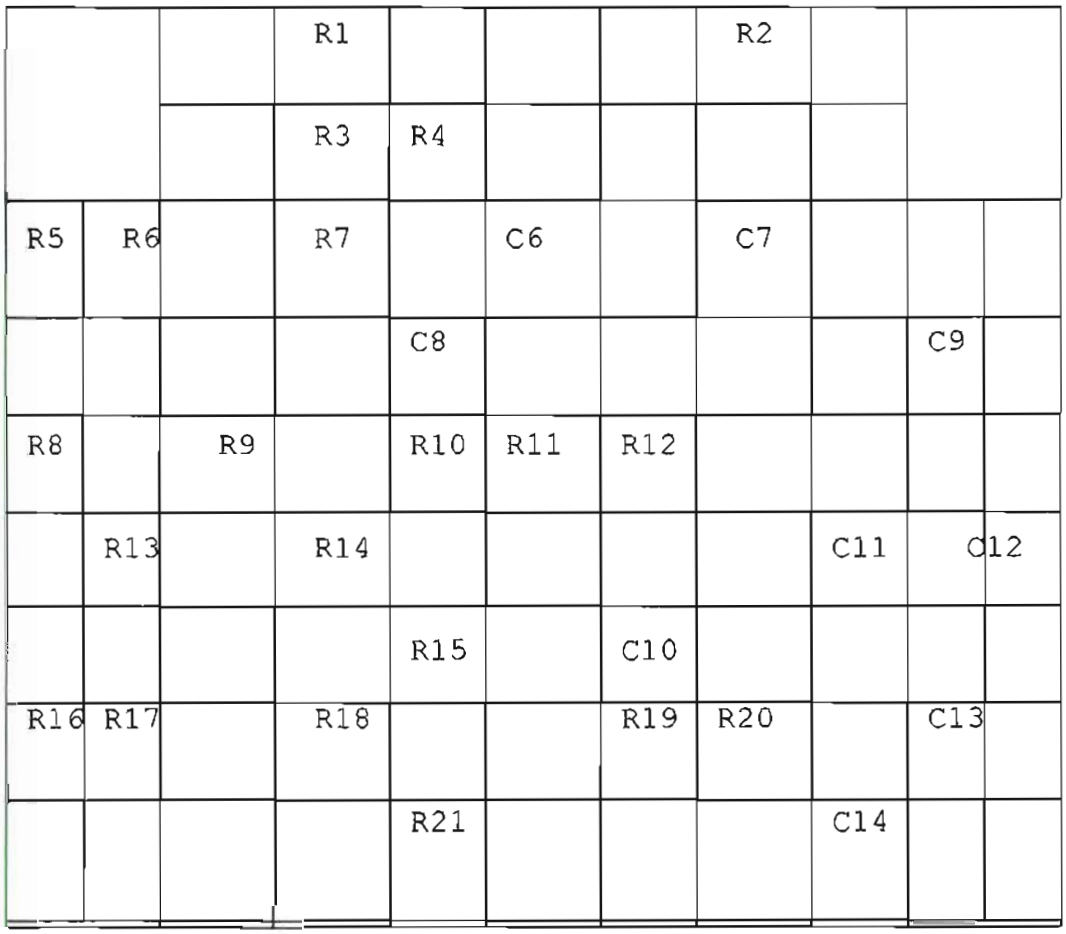

C15 = SINK 1
C16 = SINK 2

Table 12-4-23. Annex 219-2 - Final Status Survey Summary for RANDOM STATISTICAL SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 219-2				
Survey Date: 2/3/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	17	12	26	10
2	13	20	19	13
3	5	12	16	10
4	15	11	16	21
5	12	9	18	7
6	11	12	51	14
7	19	10	9	11
8	17	12	0	13
9	33	8	11	11
10	57	5	25	16
11	18	9	20	18
12	34	8	3	15
13	11	20	45	12
14	19	11	21	17
15	15	14	25	9
16	17	9	28	9
17	19	9	53	2
18	5	24	33	5
19	8	6	27	7
20	18	41	47	16
21	15	8	12	6
Average DPM	18	13	24	12
Standard Deviation, DPM	11	8	15	5
Maximum DPM	57	41	53	21
Action Limit, DPM			700	700

Table 12-4-24. Annex 219-2 - Final Status Survey Summary for ADDITIONAL SELECT SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 219-2				
Survey Date: 2/3/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	17	12	21	13
2	13	20	15	12
3	5	12	11	4
4	15	11	15	9
5	12	9	17	6
6	11	12	46	5
7	19	10	27	14
8	17	12	47	14
9	33	8	7	21
10	57	5	7	16
11	18	9	35	8
12	34	8	40	14
13	11	20	10	8
14	19	11	2	11
15	15	14	22	21
16	17	9	15	8
17	19	9	28	10
18	5	24	41	4
19	8	6		
20	18	41		
21	15	8		
Average DPM	18	13	23	11
Standard Deviation, DPM	11	8	14	5
Maximum DPM	57	41	47	21
Action Limit, DPM			700	700

Figure 12-4-10: Grid Map for Rockville Annex, Room 219-2
Survey date: 2/3/00
Survey results: background < 57 DPM; H-3 and C-14 < 53 DPM
R1-R21 = random statistical sample locations
C1-C18 = additional select sample locations

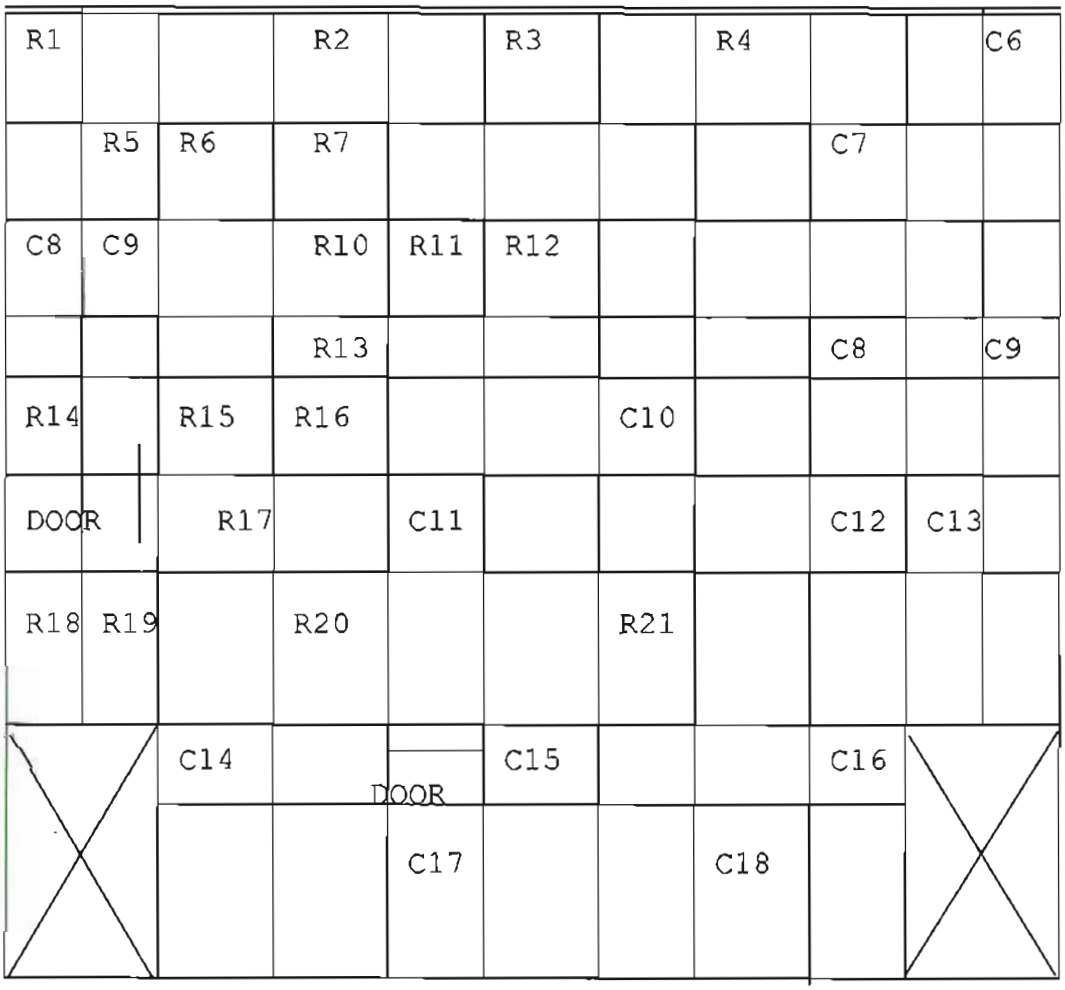

Table 12-4-25. Annex 219A - Final Status Survey Summary for RANDOM STATISTICAL SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 219A				
Survey Date: 2/3/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	17	12	25	9
2	13	20	40	4
3	5	12	17	10
4	15	11	25	20
5	12	9	60	2
6	11	12	41	8
7	19	10	27	10
8	17	12	7	12
9	33	8	18	10
10	57	5	58	8
11	18	9	32	11
12	34	8	29	7
13	11	20	34	12
14	19	11	36	5
15	15	14	46	8
16	17	9	50	19
17	19	9	33	9
18	5	24	66	1
19	8	6	22	17
20	18	41	7	16
21	15	8	38	14
Average DPM	18	13	34	10
Standard Deviation, DPM	11	8	16	5
Maximum DPM	57	41	66	20
Action Limit, DPM			700	700

Table 12-4-26. Annex 219A - Final Status Survey Summary for ADDITIONAL SELECT SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 219A				
Survey Date: 2/3/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	17	12	17	7
2	13	20	13	11
3	5	12	19	14
4	15	11	18	12
5	12	9	52	0
6	11	12	24	10
7	19	10	80	6
8	17	12	22	8
9	33	8	56	16
10	57	5	24	20
11	18	9	18	15
12	34	8	21	52
13	11	20	57	54
14	19	11	50	15
15	15	14	18	13
16	17	9	33	6
17	19	9	15	30
18	5	24	25	13
19	8	6	20	10
20	18	41	44	16
21	15	8	63	7
22			59	9
23			13	12
Average DPM	18	13	33	15
Standard Deviation, DPM	11	8	20	13
Maximum DPM	57	41	80	54
Action Limit, DPM			700	700

Figure 12-4-11: Grid Map for Rockville Annex, Room 219A
Survey date: 2/3/00
Survey results: background < 57 DPM; H-3 and C-14 < 80 DPM
R1-R21 = random statistical sample locations
C1-C23 = additional select sample locations

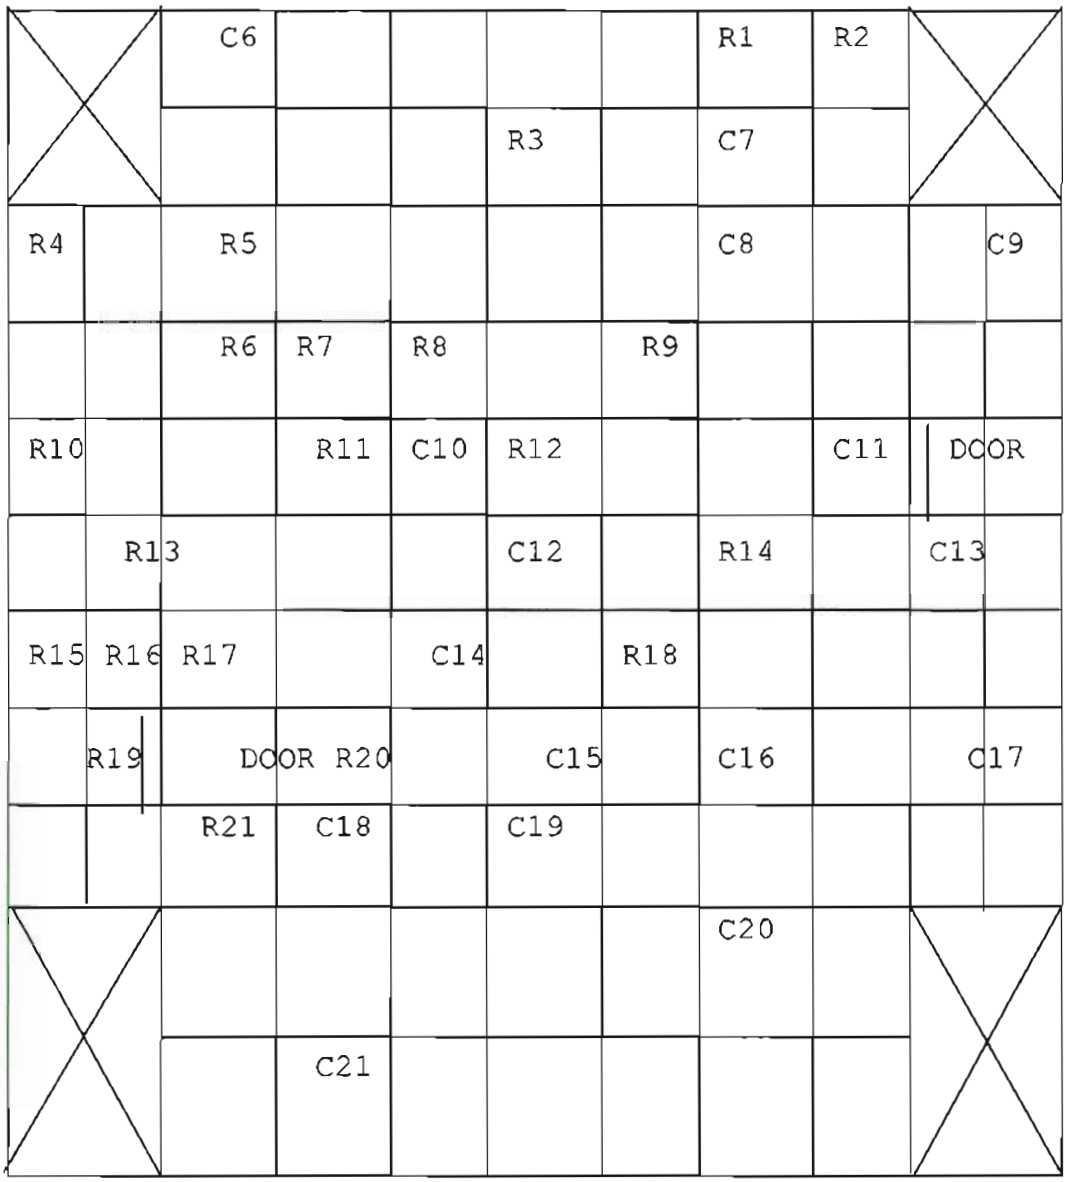

Table 12-4-27. Annex 219B – Final Status Survey Summary for RANDOM STATISTICAL SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 219B				
Survey Date: 2/3/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	12	14	71	93
2	4	19	44	83
3	33	13	44	104
4	37	20	22	10
5	49	15	37	5
6	8	13	13	18
7	16	20	68	5
8	21	17	14	11
9	32	8	27	3
10	25	24	1	13
11	20	11	31	14
12	21	7	44	38
13	23	35	2	15
14	18	13	1	16
15	25	9	21	10
16	15	17	13	15
17	17	11	17	39
18	14	48	70	14
19	22	11	17	42
20	16	12	31	21
21	10	19	36	19
Average DPM	21	17	30	28
Standard Deviation, DPM	10	9	21	29
Maximum DPM	49	48	71	104
Action Limit, DPM			700	700

Table 12-4-28. Annex 219B - Final Status Survey Summary for ADDITIONAL SELECT SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 219B				
Survey Date: 2/3/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	12	14	33	20
2	4	19	33	7
3	33	13	57	11
4	37	20	31	15
5	49	15	23	11
6	8	13	37	15
7	16	20	13	12
8	21	17	61	5
9	32	8	34	11
10	25	24	29	10
11	20	11	30	16
12	21	7	19	11
13	23	35	17	16
14	18	13	14	13
15	25	9	24	14
16	15	17	25	9
17	17	11	16	16
18	14	48	42	22
19	22	11	42	17
20	16	12		
21	10	19		
Average DPM	21	17	31	13
Standard Deviation, DPM	10	9	13	4
Maximum DPM	49	48	61	22
Action Limit, DPM			700	700

Table 12-4-29. Annex 219B - Final Status Survey Summary for QUALITY CONTROL SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 219B				
QUALITY CONTROL SAMPLES				
Survey Date: 2/3/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	12	14	2	12
2	4	19	8	4
3	33	13	13	13
4	37	20	4	8
5	49	15	14	40
6	8	13	9	1
7	16	20	2	21
8	21	17	9	8
9	32	8	6	7
10	25	24	9	13
11	20	11	11	15
12	21	7	0	7
13	23	35	4	14
14	18	13	10	12
15	25	9	7	44
16	15	17	15	14
17	17	11	10	16
18	14	48		
19	22	11		
20	16	12		
21	10	19		
Average DPM	21	17	8	15
Standard Deviation, DPM	10	9	4	11
Maximum DPM	49	48	15	44
Action Limit, DPM			700	700

Figure 12-4-12: Grid Map for Rockville Annex, Room 219B
Survey date: 2/7/00
Survey results: background < 49 DPM; H-3 and C-14 < 71 DPM
R1-R21 = random statistical sample locations
C1-C19 = additional select sample locations

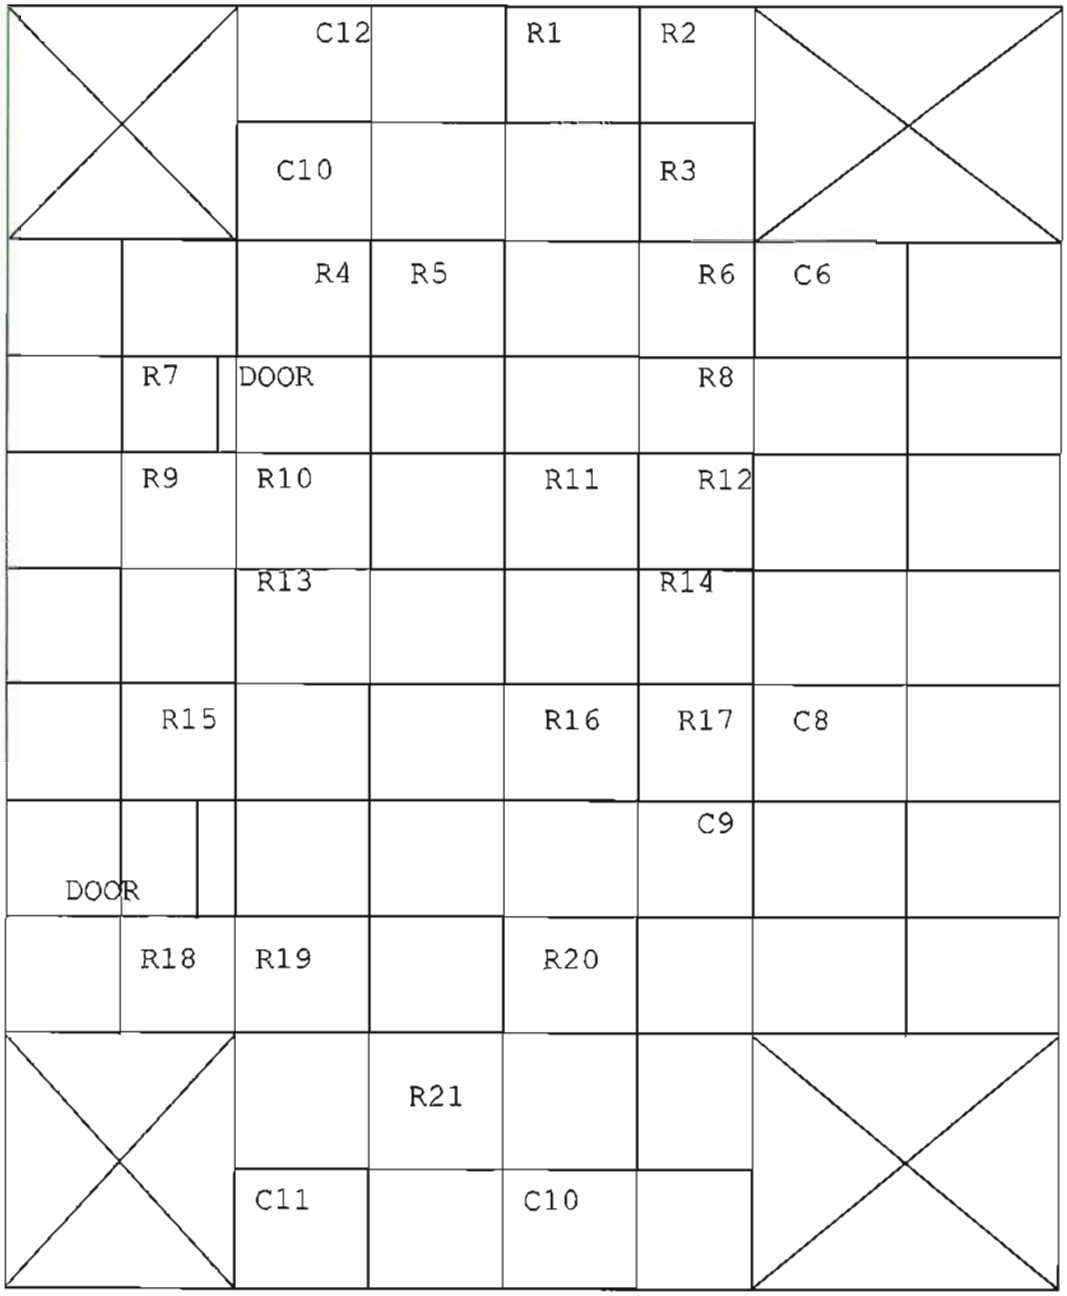

Table 12-4-30. Annex 220-1 - Final Status Survey Summary for RANDOM STATISTICAL SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 220-1				
Survey Date: 2/2/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	24	8	15	25
2	34	13	13	8
3	40	11	11	11
4	26	9	8	9
5	15	18	90	2
6	13	15	44	8
7	13	10	50	7
8	10	36	32	7
9	53	27	0	34
10	8	17	5	22
11	17	18	19	15
12	22	4	8	8
13	25	10	77	14
14	15	21	19	32
15	21	6	46	17
16	16	8	41	14
17	17	10	24	23
18	8	4	23	7
19	3	29	25	13
20	23	10	43	2
21	12	10	41	10
Average DPM	20	14	30	14
Standard Deviation, DPM	12	8	23	9
Maximum DPM	53	36	90	34
Action Limit, DPM			700	700

Table 12-4-31. Annex 220-1 - Final Status Survey Summary for ADDITIONAL SELECT SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 220-1				
Survey Date: 2/2/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	24	8	34	5
2	34	13	39	49
3	40	11	29	13
4	26	9	126	0
5	15	18	19	15
6	13	15	35	7
7	13	10	8	10
8	10	36	17	10
9	53	27	87	10
10	8	17	18	9
11	17	18	25	8
12	22	4	19	9
13	25	10		
14	15	21		
15	21	6		
16	16	8		
17	17	10		
18	8	4		
19	3	29		
20	23	10		
21	12	10		
Average DPM	20	14	38	12
Standard Deviation, DPM	12	8	34	12
Maximum DPM	53	36	126	49
Action Limit, DPM			700	700

Figure 12-4-13: Grid Map for Rockville Annex, Room 220-1
Survey date: 2/3/00
Survey results: background < 53 DPM; H-3 and C-14 < 126 DPM
R1-R21 = random statistical sample locations
C1-C12 = additional select sample locations

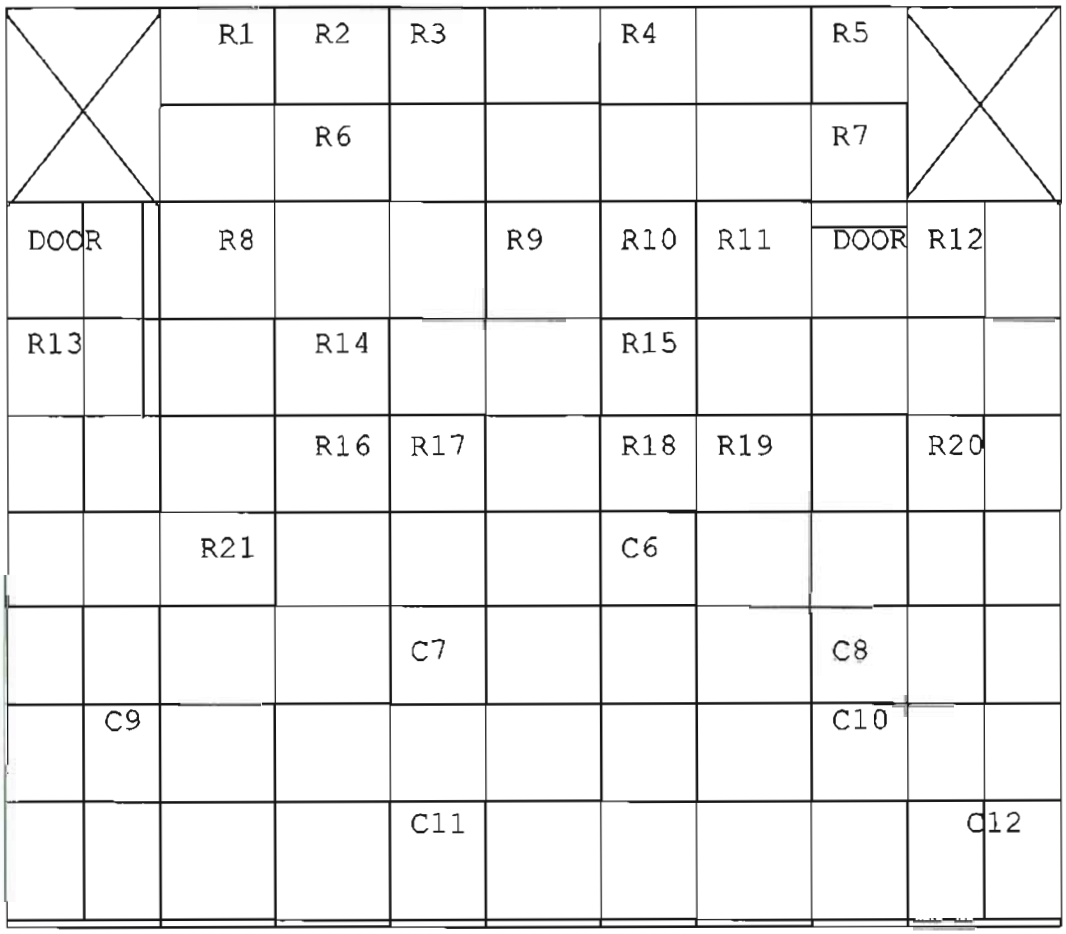

Table 12-4-32. Annex 220-2 - Final Status Survey Summary for RANDOM STATISTICAL SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 220-2				
Survey Date: 2/2/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	24	8	10	8
2	34	13	10	6
3	40	11	15	9
4	26	9	22	6
5	15	18	11	6
6	13	15	2	5
7	13	10	14	11
8	10	36	19	5
9	53	27	10	13
10	8	17	3	14
11	17	18	13	4
12	22	4	0	19
13	25	10	7	6
14	15	21	0	10
15	21	6	12	11
16	16	8	0	15
17	17	10	18	10
18	8	4	14	27
19	3	29	26	15
20	23	10	7	12
21	12	10	9	3
Average DPM	20	14	11	10
Standard Deviation, DPM	12	8	7	6
Maximum DPM	53	36	26	27
Action Limit, DPM			700	700

Table 12-4-33. Annex 220-2 - Final Status Survey Summary for ADDITIONAL SELECT SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 220-2				
Survey Date: 2/2/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	24	8	0	10
2	34	13	0	15
3	40	11	14	11
4	26	9	17	7
5	15	18	19	18
6	13	15	5	11
7	13	10	7	21
8	10	36	14	22
9	53	27	4	12
10	8	17	3	43
11	17	18	6	14
12	22	4	4	62
13	25	10	21	33
14	15	21	11	15
15	21	6	23	73
16	16	8	5	15
17	17	10	21	5
18	8	4	6	13
19	3	29	20	35
20	23	10		
21	12	10		
Average DPM	20	14	11	23
Standard Deviation, DPM	12	8	8	19
Maximum DPM	53	36	23	73
Action Limit, DPM			700	700

Figure 12-4-14: Grid Map for Rockville Annex, Room 220-2
Survey date: 2/2/00
Survey results: background < 53 DPM; H-3 and C-14 < 73 DPM
R1-R21 = random statistical sample locations
C1-C19 = additional select sample locations

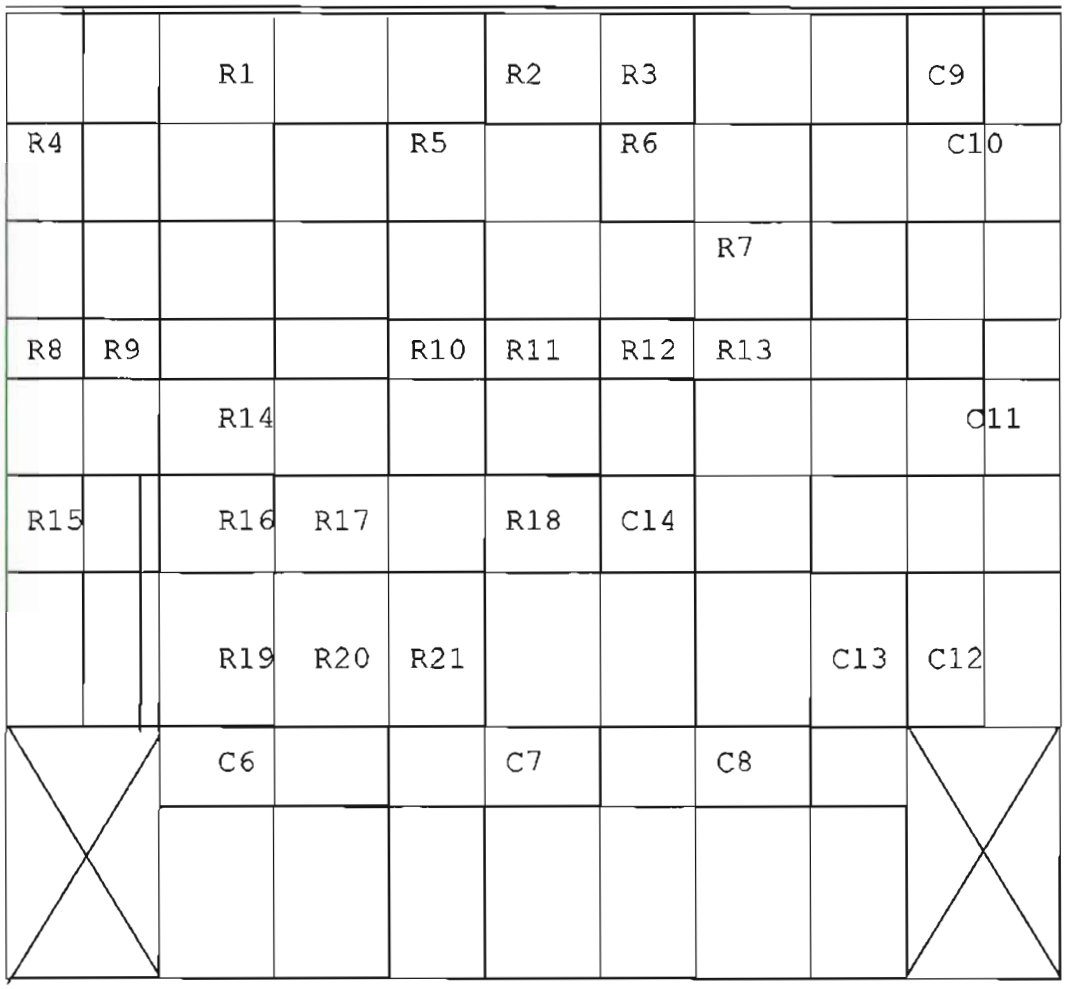

Table 12-4-34. Annex 220-3 - Final Status Survey Summary for 100% Coverage				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 220-3				
Survey Date: 2/2/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	24	8	17	9
2	34	13	15	9
3	40	11	14	10
4	26	9	19	6
5	15	18	13	6
6	13	15	13	13
7	13	10	22	10
8	10	36	43	5
9	53	27	0	19
10	8	17	8	8
11	17	18	23	7
12	22	4	42	7
13	25	10	19	6
14	15	21	13	16
15	21	6	14	6
16	16	8	16	6
17	17	10	9	13
18	8	4	7	10
19	3	29	18	13
20	23	10	12	35
21	12	10		
Average DPM	20	14	17	11
Standard Deviation, DPM	12	8	10	7
Maximum DPM	53	36	43	35
Action Limit, DPM			700	700

Table 12-4-35. Annex 220-3 - Final Status Survey Summary for ADDITIONAL SELECT SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 220-3				
Survey Date: 2/2/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	24	8	6	13
2	34	13	18	17
3	40	11	48	9
4	26	9	69	8
5	15	18	8	6
6	13	15	16	13
7	13	10	11	6
8	10	36	0	15
9	53	27	26	9
10	8	17		
11	17	18		
12	22	4		
13	25	10		
14	15	21		
15	21	6		
16	16	8		
17	17	10		
18	8	4		
19	3	29		
20	23	10		
21	12	10		
Average DPM	20	14	22	11
Standard Deviation, DPM	12	8	22	4
Maximum DPM	53	36	69	17
Action Limit, DPM			700	700

Figure 12-4-15: Grid Map for Rockville Annex, Room 220-3
Survey date: 2/2/00
Survey results: background < 53 DPM; H-3 and C-14 < 69 DPM
R1-R21 = random statistical sample locations
C1-C9 = additional select sample locations

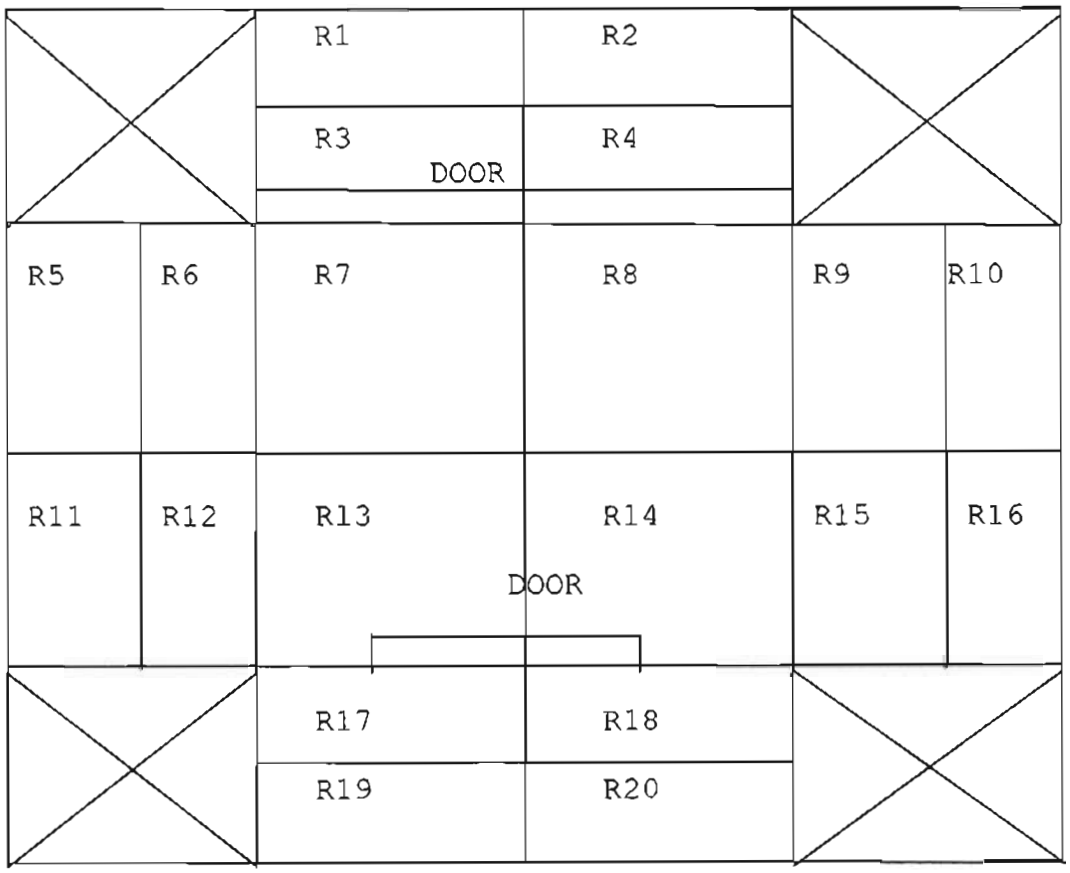

Table 12-4-36. Annex 221 - Final Status Survey Summary for RANDOM STATISTICAL SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 221				
Survey Date: 2/1/00 (1440-1530)		Count Times: 1 minute		
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	49	8	20	24
2	21	12	10	22
3	20	7	17	51
4	5	18	35	28
5	43	30	41	45
6	5	24	22	10
7	14	29	15	10
8	10	22	24	96
9	20	13	20	33
10	8	22	9	8
11	22	17	30	32
12	13	22	50	11
13	18	15	24	26
14	15	26	5	23
15	30	13	20	11
16	45	76	28	20
17	27	54	47	30
18	16	33	19	20
19	20	17	32	8
20	11	34	11	19
21	19	42	12	10
Average DPM	21	25	23	26
Standard Deviation, DPM	12	16	12	20
Maximum DPM	49	76	50	96
Action Limit, DPM			700	700

Table 12-4-37. Annex 221 - Final Status Survey Summary for ADDITIONAL SELECT SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 221				
Survey Date: 2/3/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	49	8	38	336
2	21	12	20	17
3	20	7	87	13
4	5	18	52	26
5	43	30	45	298
6	5	24		
7	14	29		
8	10	22		
9	20	13		
10	8	22		
11	22	17		
12	13	22		
13	18	15		
14	15	26		
15	30	13		
16	45	76		
17	27	54		
18	16	33		
19	20	17		
20	11	34		
21	19	42		
Average DPM	21	25	48	138
Standard Deviation, DPM	12	16	25	164
Maximum DPM	49	76	87	336
Action Limit, DPM		0	700	700

Figure 12-4-16: Grid Map for Rockville Annex, Room 221
Survey date: 2/2/00
Survey results: background < 53 DPM; H-3 and C-14 < 69 DPM
R1-R21 = random statistical sample locations
C1-C9 = additional select sample locations

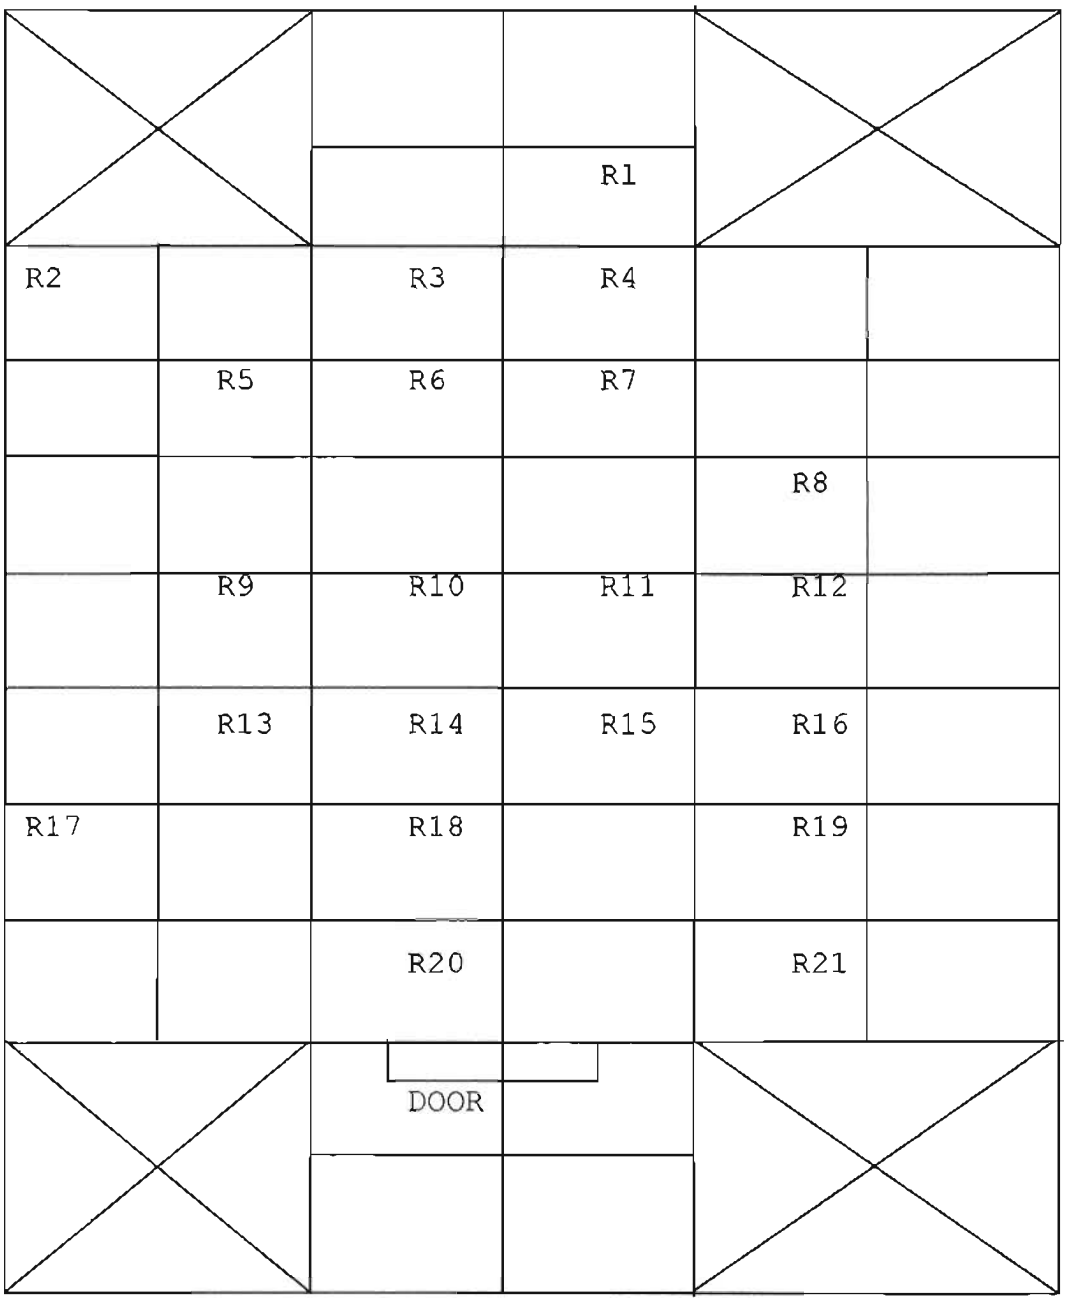

XII. APPENDIX E

Appendix E-5. ROCKVILLE ANNEX, FIRST FLOOR IMPACTED CLASS 3 AREAS AND OTHER AREAS

- Location: NMRC Rockville Annex, First Floor Impacted Class 3 Areas and Other Areas

- Monitoring Date(s): 8, 11, 14, 16, 17 Feb 00; and 28 Mar 00

- Radioactive Contaminants of Concern: Beta- and gamma-radiation emitters, Tritium (H-3), Carbon-14 (C-14), Phosphorus-32 (P-32), Sulfur-35 (S-35), and Chromium-51 (Cr-51).

- Minimum Control Beta Swipe Locations (performed for every survey unit): (1) floor at door in room; (2) floor at door outside room; (3) doorknob in room; (4) doorknob outside room; and (5) light switch inside room.

- Survey Instrument Information:
  - Beta meters -- serial numbers (background CPM): 11030 (<100CPM), 54537 (<100 CPM)
  - Gamma meters -- serial numbers (background CPM): 114886 (<300 CPM), 121730 (<200 CPM), 121886 (<300 CPM)
  - Liquid Scintillation Counter: Packard 2500TR, S/N 403848

- Radiation-detection Action Limits:
  - 2 to 3 times background for beta and gamma scans
  - 500 - 700 dpm or higher for either H-3 or C-14 beta swipes counted using a liquid scintillation counter

- Summary of Radiological Scans and Swipe Results:
  - Background level for all beta and gamma scans
  - All H-3 and C-14 beta swipe results below Action Limits

- Contamination and Remedial Actions: In laboratory 115, swipe results revealed residual tritium (H-3) contamination in a two-basin sink that was designated for disposing aqueous, radioactive liquid waste. Decontamination efforts included the removal of plumbing fixtures and pipes underneath the sink basin, extending from the sink drain to the wall connection. The removed fixtures and piping were disposed as radioactive waste. Decontamination efforts were completed for the remaining stub section of drainpipe beneath the sink. After several iterations of decontamination efforts, the final swipe results for the inside surface of the cut-off drainpipe were on the order of 3,000 to 6,000 dpm. Remediation surveys for adjacent areas within the survey unit yielded satisfactory results. The results revealed that decontamination efforts for the sink were successful, resulting in background-level swipe results. The residual-contamination level on the inside surface of the drainpipe stub (3×10^3 to 6×10^3 dpm) was approximately 20,000 times lower than the regulatory limit for residual tritium contamination (1.2×10^8 dpm). The residual-contamination levels for the sink and drainpipe stub meet the regulatory-release criteria for unrestricted use.

- Conclusion: The radiological monitoring results for all survey units addressed in this section meet the criteria for release for unrestricted use.

TABLE 12-5-1. RADIOLOGICAL FINAL STATUS SURVEY SUMMARIES
NMRC Rockville Annex
First Floor Impacted Class 3 Areas and Other Areas

Date	Room number or area (Survey Unit)	Beta and/or Gamma Scan Monitoring (check if yes)	Maximum Background beta (H-3 or C-14) swipe result (DPM)	Maximum Random or Control beta (H-3 or C-14) swipe result (DPM)	Recommend Survey Unit for radiological clearance (Y/N)
2/14/00	110-1	Y	78	183	Y
2/14/00	110-2	Y	78	102	Y
2/11/00	110A	Y	52	561	Y
2/11/00	110B	Y	52	294	Y
2/16/00	111	Y	87	330	Y
2/17/00	112	Y	316	25	Y
2/17/00	113	Y	316	128	Y
2/11/00	114	Y	52	174	Y
2/16/00	115	Y	87	18	N
2/11/00	123	Y	52	48	Y
2/17/00	124	Y	316	111	Y
2/17/00	125	Y	316	20	Y
2/14/00	126	Y	78	73	Y
2/11/00	127	Y	52	152	Y
2/14/00	128-1	Y	78	33	Y
2/14/00	128-2	Y	78	144	Y
2/14/00	1st Floor Hallways	Y	127	54	Y
2/22/00	2nd Floor Hallways	Y	42	76	Y
2/10/00	Stair A	Y	53	50	Y
3/28/00	Stair B	Y	33	48	Y
3/28/00	Loading Dock Area	Y	33	167	Y
3/28/00	Loading Dock Storage	Y	10	18	Y
3/28/00	Hall Storage Closet (near RWL)	Y	33	32	Y
2/22/00	Radiation Waste Locker (RWL)	Y	42	337	Y
3/28/00		Y	33	47	Y

Quality Assurance Checklist

Building number or location: NMRC Rockville Annex, First Floor Impacted Areas and Other Areas
Monitoring Date(s): 9, 11, 14, 16, 17, 22 Feb 00; 28 Mar 00

Y - Appropriate and satisfactory daily and weekly calibration checks were completed for the selected survey monitoring equipment and instruments.

Y - Selected meters with current calibrations for the isotopes of concern.

Y - Survey maps or floor plans (for all survey units) and grid maps (for known RAM-use areas) were available.

Y - Background checks were performed when impacted areas were monitored.

Y - For known RAM-use survey units, additional checks were performed (workbenches, shelves, sinks, basins, traps, floor at sinks and entrances, wall at hoods and sinks, and/or other areas as deemed appropriate).

Y - Mean values, single sample values, and background values were below the action limits, indicating no contamination was found.

Y - Representative floor plans, sketches, and photographs were available.

Y - Deviation from survey plans and objectives were documented.

Y - Extent of remediation actions documented.

Y - All selected survey units passed D&D tests; units are recommended for unrestricted release.

Y - Additional Checks/Data passed D&D tests; unit is recommended for unrestricted release.

Notes: Tests included complying with applicable elements of the MARSSIM Final Status Survey checklist, mean-value and single-value comparisons of survey-unit data to action limits (DCGLs), mean-value comparison to background, completion of required monitoring, and satisfactory scan monitoring results.

Quality Assurance Leader: Schleurious L. Gaiter, LCDR, MSC, USN

Table 12-5-2. Annex 110-1 - Final Status Survey Summary for RANDOM STATISTICAL SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 110-1				
Survey Date: 2/14/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	28	2	49	4
2	47	19	32	11
3	78	3	14	6
4	35	15	36	4
5	41	10	125	9
6	57	2	22	11
7	52	9	10	18
8	72	7	78	2
9	24	12	47	9
10	44	8	55	4
11	45	5	150	4
12	66	12	42	12
13	62	5	47	8
14	38	9	72	7
15	38	9	118	10
16	33	10	42	6
17	27	8	33	5
18	15	10	21	6
19	41	6	11	4
20	42	5	20	4
21	11	18	41	7
Average DPM	43	9	51	7
Standard Deviation, DPM	17	5	38	4
Maximum DPM	78	19	150	18
Action Limit, DPM			700	700

Table 12-5-3. Annex 110-1 - Final Status Survey Summary for ADDITIONAL SELECT SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 110-1				
Survey Date: 2/14/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	28	2	9	6
2	47	19	69	11
3	78	3	93	5
4	35	15	33	4
5	41	10	89	0
6	57	2	32	9
7	52	9	37	14
8	72	7	183	0
9	24	12	27	8
10	44	8	68	7
11	45	5	19	10
12	66	12	36	4
13	62	5	36	17
14	38	9	165	0
15	38	9	36	6
16	33	10		
17	27	8		
18	15	10		
19	41	6		
20	42	5		
21	11	18		
Average DPM	43	9	62	7
Standard Deviation, DPM	17	5	52	5
Maximum DPM	78	19	183	17
Action Limit, DPM			700	700

Figure 12-5-1: Grid Map for Rockville Annex, Room 110-1
Survey date: 2/14/00
Survey results: background < 78 DPM; H-3 and C-14 < 183 DPM
R1-R21 = random statistical sample locations
C1-C15 = additional select sample locations

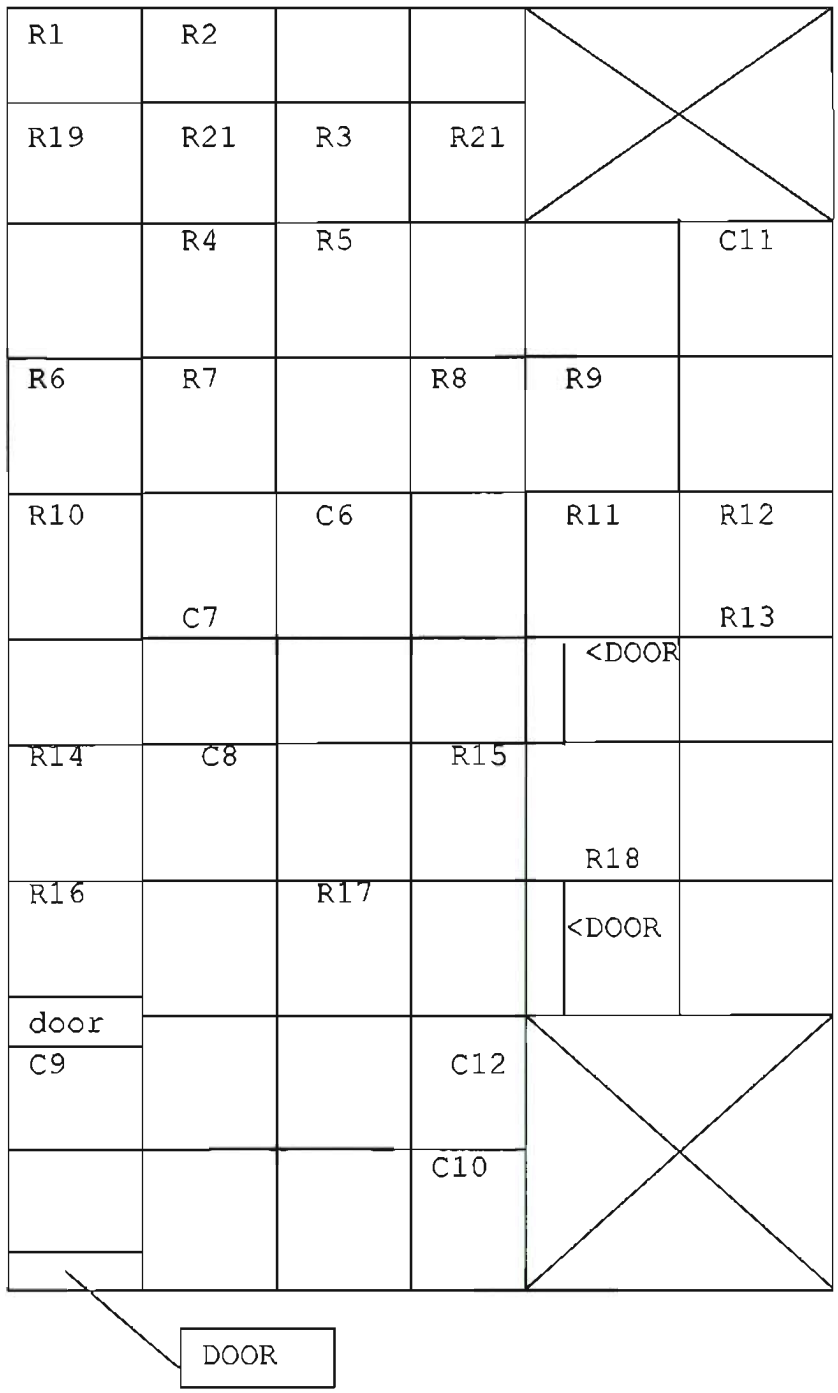

Table 12-5-4. Annex 110-2 - Final Status Survey Summary for RANDOM STATISTICAL SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 110-2				
Survey Date: 2/14/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	28	2	44	12
2	47	19	16	9
3	78	3	29	8
4	35	15	43	9
5	41	10	81	4
6	57	2	48	5
7	52	9	26	18
8	72	7	32	12
9	24	12	19	6
10	44	8	34	23
11	45	5	19	7
12	66	12	35	12
13	62	5	18	7
14	38	9	5	15
15	38	9	31	11
16	33	10	93	9
17	27	8	42	7
18	15	10	84	9
19	41	6	34	4
20	42	5	27	14
21	11	18	56	9
Average DPM	43	9	39	10
Standard Deviation, DPM	17	5	23	5
Maximum DPM	78	19	93	23
Action Limit, DPM			700	700

Table 12-5-5. Annex 110-2 - Final Status Survey Summary for ADDITIONAL SELECT SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 110-2				
Survey Date: 2/14/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	28	2	102	11
2	47	19	27	7
3	78	3	11	8
4	35	15	22	11
5	41	10	63	10
6	57	2	14	8
7	52	9	85	3
8	72	7	16	5
9	24	12	20	8
10	44	8	13	11
11	45	5	15	9
12	66	12	25	11
13	62	5	11	10
14	38	9	21	2
15	38	9	29	5
16	33	10	52	10
17	27	8	41	12
18	15	10	21	14
19	41	6	15	14
20	42	5		
21	11	18		
Average DPM	43	9	32	9
Standard Deviation, DPM	17	5	26	3
Maximum DPM	78	19	102	14
Action Limit, DPM			700	700

Figure 12-5-2: Grid Map for Rockville Annex, Room 110-2
Survey date: 2/14/00
Survey results: background < 78 DPM; H-3 and C-14 < 102 DPM
R1-R21 = random statistical sample locations
C1-C21 = additional select sample locations

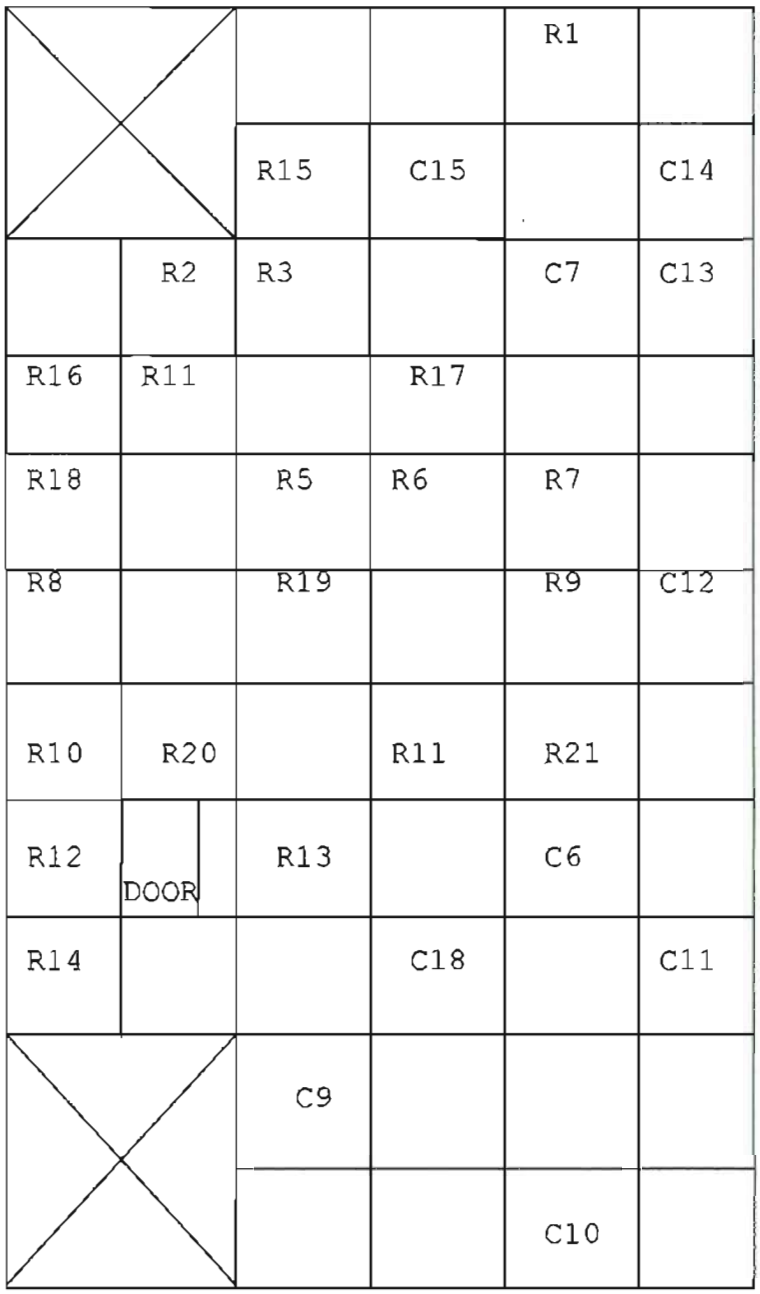

Table 12-5-6. Annex 110A - Final Status Survey Summary for RANDOM STATISTICAL SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 110A				
Survey Date: 2/11/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	31	1	25	9
2	19	5	77	0
3	49	15	122	2
4	42	2	150	4
5	11	7	71	6
6	45	5	42	11
7	32	3	198	0
8	30	6	66	8
9	31	8	293	0
10	23	7	64	1
11	20	7	30	9
12	19	12	75	0
13	14	11	251	4
14	27	2	478	0
15	26	15	15	8
16	25	8	183	0
17	9	11	158	0
18	12	15	23	2
19	52	9	94	4
20	29	11	125	10
21	46	6	42	4
Average DPM	28	8	123	4
Standard Deviation, DPM	13	4	112	4
Maximum DPM	52	15	478	11
Action Limit, DPM			700	700

Table 12-5-7. Annex 110A - Final Status Survey Summary for ADDITIONAL SELECT SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 110A				
Survey Date: 2/11/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	31	1	167	0
2	19	5	75	9
3	49	15	561	0
4	42	2	284	0
5	11	7	98	2
6	45	5	89	7
7	32	3	14	14
8	30	6	23	6
9	31	8	72	1
10	23	7	38	13
11	20	7		
12	19	12		
13	14	11		
14	27	2		
15	26	15		
16	25	8		
17	9	11		
18	12	15		
19	52	9		
20	29	11		
21	46	6		
Average DPM	28	8	142	5
Standard Deviation, DPM	13	4	167	5
Maximum DPM	52	15	561	14
Action Limit, DPM			700	700

Figure 12-5-3: Grid Map for Rockville Annex, Room 110A
Survey date: 2/11/00
Survey results: background < 52 DPM; H-3 and C-14 < 561 DPM
R1-R21 = random statistical sample locations
C1-C10 = additional select sample locations

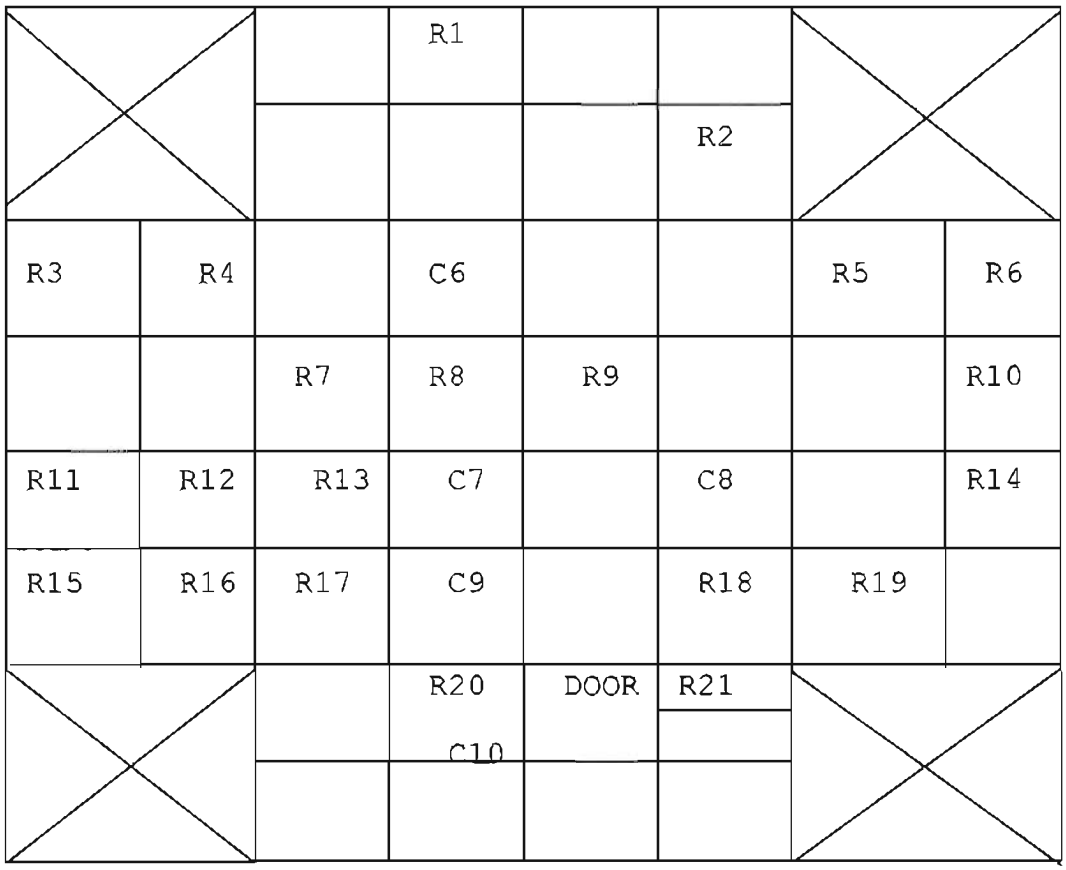

Table 12-5-8. Annex 110B - Final Status Survey Summary for RANDOM STATISTICAL SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 110B				
Survey Date: 2/11/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	31	1	26	12
2	19	5	93	8
3	49	15	105	8
4	42	2	10	14
5	11	7	85	7
6	45	5	107	5
7	32	3	63	11
8	30	6	61	7
9	31	8	56	8
10	23	7	64	8
11	20	7	51	7
12	19	12	59	11
13	14	11	98	1
14	27	2	59	5
15	26	15	134	8
16	25	8	79	11
17	9	11	46	4
18	12	15	104	1
19	52	9	52	11
20	29	11	83	1
21	46	6	32	11
Average DPM	28	8	70	8
Standard Deviation, DPM	13	4	30	4
Maximum DPM	52	15	134	14
Action Limit, DPM			700	700

Table 12-5-9. Annex 110B - Final Status Survey Summary for ADDITIONAL SELECT SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 110B				
Survey Date: 2/11/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	31	1	134	0
2	19	5	132	3
3	49	15	294	0
4	42	2	270	0
5	11	7	123	3
6	45	5	87	7
7	32	3	66	11
8	30	6	24	14
9	31	8	101	10
10	23	7	14	6
11	20	7		
12	19	12		
13	14	11		
14	27	2		
15	26	15		
16	25	8		
17	9	11		
18	12	15		
19	52	9		
20	29	11		
21	46	6		
Average DPM	28	8	125	5
Standard Deviation, DPM	13	4	93	5
Maximum DPM	52	15	294	14
Action Limit, DPM			700	700

Figure 12-5-4: Grid Map for Rockville Annex, Room 110B
Survey date: 2/11/00
Survey results: background < 52 DPM; H-3 and C-14 < 294 DPM
R1-R21 = random statistical sample locations
C1-C10 = additional select sample locations

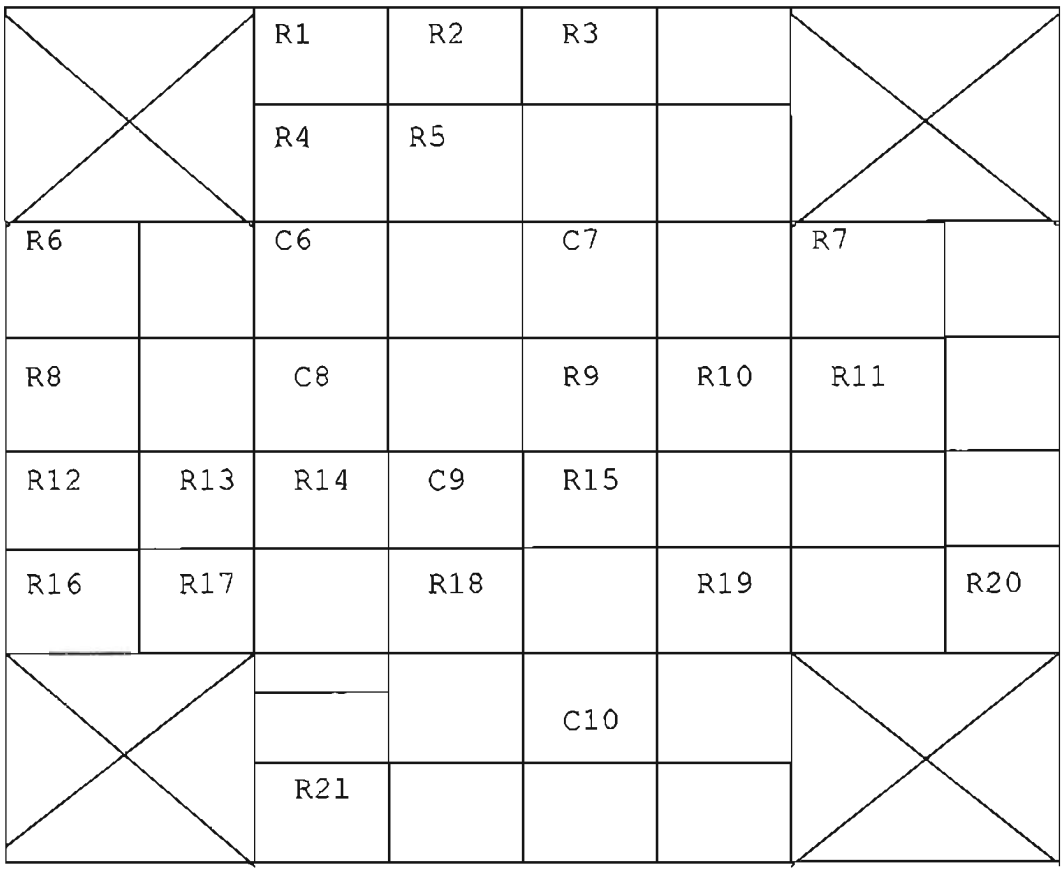

Table 12-5-10. Annex 111 - Final Status Survey Summary for RANDOM STATISTICAL SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 111				
Survey Date: 2/16/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	87	3	16	9
2	66	8	38	7
3	42	10	29	14
4	51	7	330	0
5	43	5	4	13
6	34	4	35	6
7	54	6	48	9
8	50	13	87	17
9	74	0	92	5
10	63	9	12	12
11	44	6	18	6
12	18	9	31	10
13	37	9	41	4
14	25	9	48	10
15	24	15	47	3
16	15	10	17	9
17	16	9	12	9
18	26	4	18	6
19	33	11	32	8
20	15	4	26	10
21	23	5	1	16
Average DPM	40	7	47	9
Standard Deviation, DPM	20	4	69	4
Maximum DPM	87	15	330	17
Action Limit, DPM			700	700

Table 12-5-11. Annex 111 - Final Status Survey Summary for ADDITIONAL SELECT SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 111				
Survey Date: 2/16/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	87	3	20	9
2	66	8	12	12
3	42	10	12	9
4	51	7	12	6
5	43	5	22	14
6	34	4	10	8
7	54	6	18	11
8	50	13	14	11
9	74	0	13	10
10	63	9	19	7
11	44	6	58	4
12	18	9	68	7
13	37	9	8	17
14	25	9	42	8
15	24	15	6	8
16	15	10	17	6
17	16	9	26	7
18	26	4	30	12
19	33	11	25	7
20	15	4	34	9
21	23	5	77	8
22			9	8
23			26	15
24			13	7
25			23	3
Average DPM	40	7	25	9
Standard Deviation, DPM	20	4	19	3
Maximum DPM	87	15	77	17
Action Limit, DPM			700	700

Figure 12-5-5: Grid Map for Rockville Annex, Room 111
Survey date: 2/16/00
Survey results: background < 87 DPM; H-3 and C-14 < 330 DPM
R1-R21 = random statistical sample locations
C1-C25 = additional select sample locations

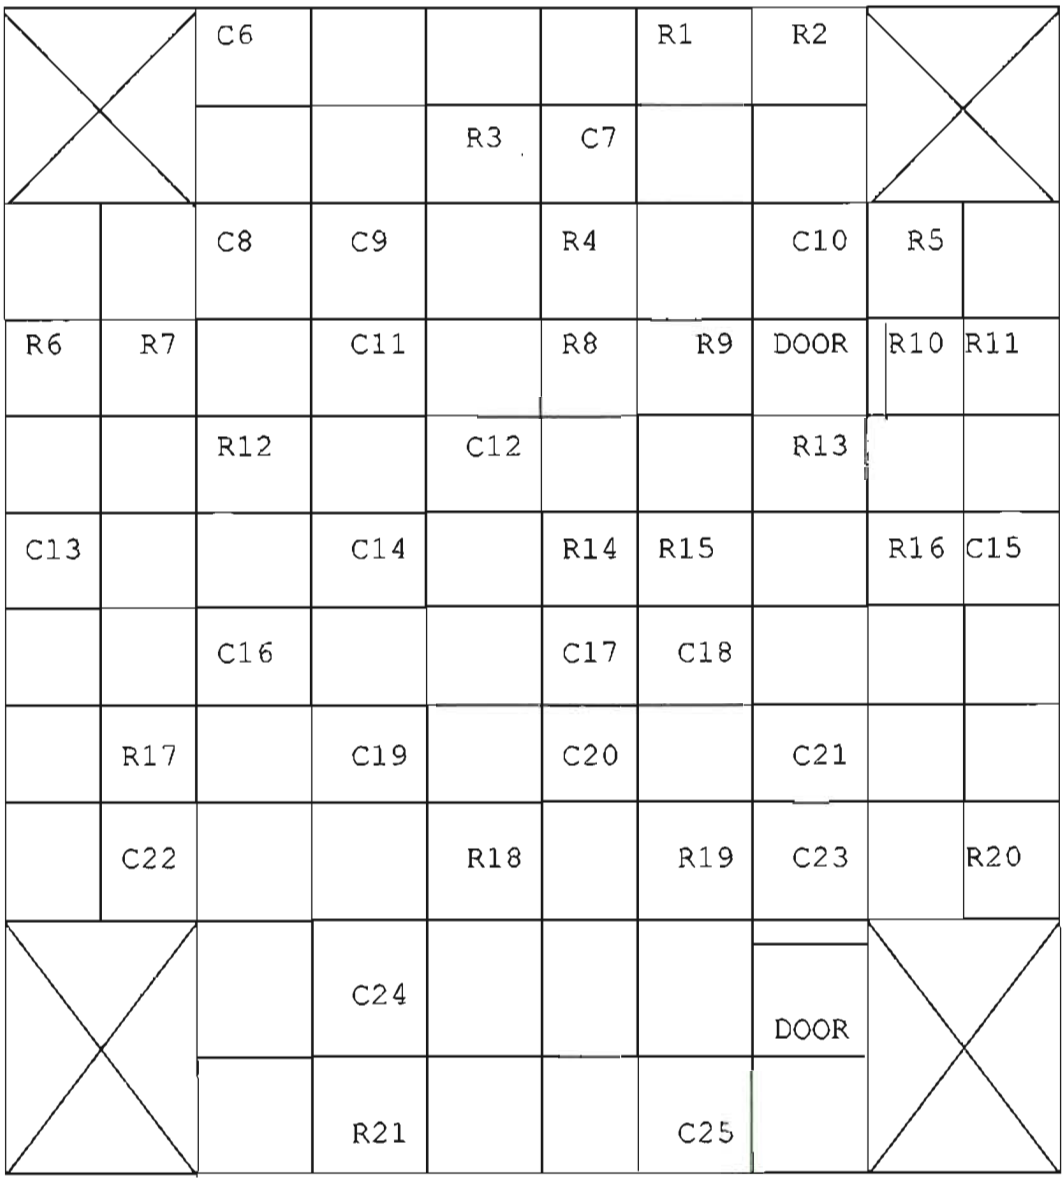

Table 12-5-12. Annex 112 - Final Status Survey Summary for RANDOM STATISTICAL SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 112				
Survey Date: 2/17/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	28	17	6	8
2	6	6	11	14
3	16	3	0	15
4	33	15	25	6
5	37	6	16	11
6	16	6	3	8
7	242	0	5	5
8	11	11	18	8
9	58	10	9	11
10	124	7	3	7
11	55	6	17	12
12	31	3	8	15
13	181	0	15	5
14	118	13	3	8
15	22	10	12	10
16	180	1	5	13
17	316	0	12	15
18	65	0	9	13
19	19	16	2	8
20	85	4	0	10
21	53	9	0	10
22			20	7
23			12	13
24			16	9
25			12	7
26			8	17
Average DPM	81	7	10	10
Standard Deviation, DPM	84	5	7	3
Maximum DPM	316	17	25	17
Action Limit, DPM			700	700

Table 12-5-13. Annex 112 - Final Status Survey Summary for ADDITIONAL SELECT SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 112				
Survey Date: 2/17/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	28	17	0	16
2	6	6	8	8
3	16	3	25	5
4	33	15	11	8
5	37	6	21	13
6	16	6		
7	242	0		
8	11	11		
9	58	10		
10	124	7		
11	55	6		
12	31	3		
13	181	0		
14	118	13		
15	22	10		
16	180	1		
17	316	0		
18	65	0		
19	19	16		
20	85	4		
21	53	9		
Average DPM	81	7	13	10
Standard Deviation, DPM	84	5	10	4
Maximum DPM	316	17	25	16
Action Limit, DPM			700	700

Figure 12-5-6: Grid Map for Rockville Annex, Room 112
Survey date: 2/17/00
Survey results: background < 316 DPM; H-3 and C-14 < 25 DPM
R1-R26 = random statistical sample locations
C1-C5 = additional select sample locations

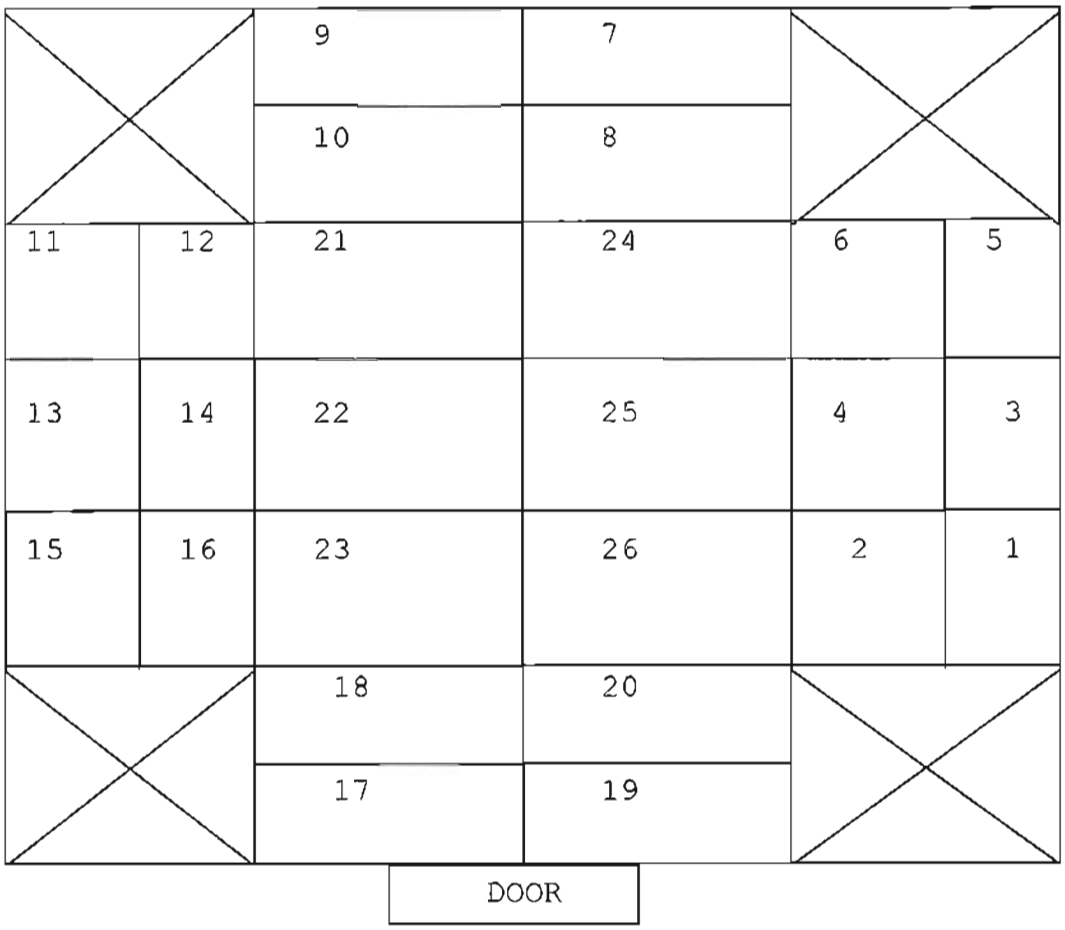

Table 12-5-14. Annex 113 - Final Status Survey Summary for 100% Coverage				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 113				
Survey Date: 2/17/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	28	17	5	8
2	6	6	6	12
3	16	3	3	10
4	33	15	0	10
5	37	6	6	6
6	16	6	15	13
7	242	0	12	10
8	11	11	9	16
9	58	10	11	9
10	124	7	3	8
11	55	6	0	11
12	31	3	11	7
13	181	0	11	13
14	118	13	5	11
15	22	10	6	9
16	180	1	7	2
17	316	0	3	11
18	65	0	13	15
19	19	16	11	9
20	85	4	11	15
21	53	9	6	12
22			24	7
23			5	11
24			7	13
25			4	11
26			15	13
27			0	10
28			2	11
29			3	14
30			4	10
31			6	7
32			13	10

33			9	14
34			22	16
35			2	6
36			0	13
37			6	12
38			13	11
39			6	12
40			9	10
41			15	9
42			9	15
43			16	11
44			24	8
45			6	9
46			128	9
47			20	19
48			29	6
49			0	13
50			17	8
51			0	12
52			18	15
Average DPM	81	7	11	11
Standard Deviation, DPM	84	5	18	3
Maximum DPM	316	17	128	19
Action Limit, DPM			700	700

Table 12-5-15. Annex 113 - Final Status Survey Summary for ADDITIONAL SELECT SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 113				
Survey Date: 2/17/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	28	17	4	12
2	6	6	17	7
3	16	3	18	5
4	33	15	12	10
5	37	6	0	14
6	16	6	9	10
7	242	0	9	2
8	11	11	5	7
9	58	10	5	7
10	124	7	15	8
11	55	6		
12	31	3		
13	181	0		
14	118	13		
15	22	10		
16	180	1		
17	316	0		
18	65	0		
19	19	16		
20	85	4		
21	53	9		
Average DPM	81	7	9	8
Standard Deviation, DPM	84	5	6	3
Maximum DPM	316	17	18	14
Action Limit, DPM			700	700

Figure 12-5-7: Grid Map for Rockville Annex, Room 113
Survey date: 2/17/00
Survey results: background < 316 DPM; H-3 and C-14 < 128 DPM
R1-R52 = random statistical sample locations
C1-C10 = additional select sample locations

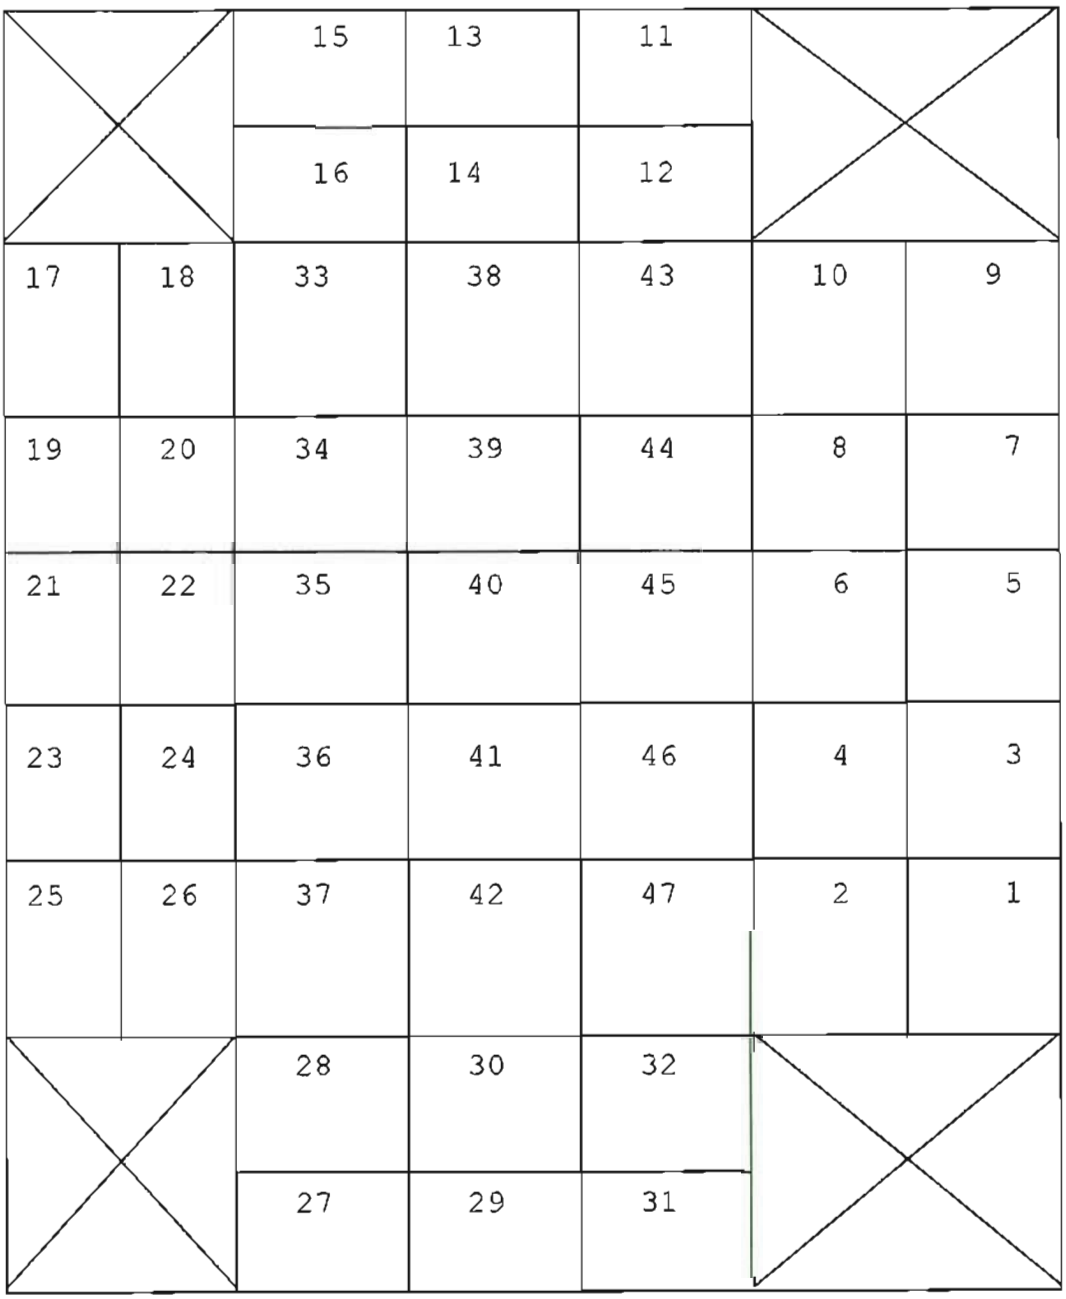

Table 12-5-16. Annex 114 - Final Status Survey Summary for RANDOM STATISTICAL SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 114				
Survey Date: 2/11/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	31	1	12	5
2	19	5	8	9
3	49	15	11	7
4	42	2	19	15
5	11	7	5	11
6	45	5	0	8
7	32	3	11	11
8	30	6	26	7
9	31	8	48	12
10	23	7	10	13
11	20	7	13	10
12	19	12	44	14
13	14	11	106	0
14	27	2	79	7
15	26	15	8	9
16	25	8	62	10
17	9	11	64	2
18	12	15	24	7
19	52	9	12	15
20	29	11	14	21
21	46	6	69	4
Average DPM	28	8	31	9
Standard Deviation, DPM	13	4	29	5
Maximum DPM	52	15	106	21
Action Limit, DPM			700	700

Table 12-5-17. Annex 114 - Final Status Survey Summary for ADDITIONAL SELECT SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 114				
Survey Date: 2/11/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	31	1	73	9
2	19	5	174	0
3	49	15	42	8
4	42	2	48	9
5	11	7	33	2
6	45	5	51	8
7	32	3	45	15
8	30	6	119	4
9	31	8	45	2
10	23	7	40	10
11	20	7	19	7
12	19	12	43	9
13	14	11	109	5
14	27	2	112	9
15	26	15		
16	25	8		
17	9	11		
18	12	15		
19	52	9		
20	29	11		
21	46	6		
Average DPM	28	8	68	7
Standard Deviation, DPM	13	4	44	4
Maximum DPM	52	15	174	15
Action Limit, DPM			700	700

Figure 12-5-8: Grid Map for Rockville Annex, Room 114
Survey date: 2/11/00
Survey results: background < 52 DPM; H-3 and C-14 < 174 DPM
R1-R21 = random statistical sample locations
C1-C14 = additional select sample locations

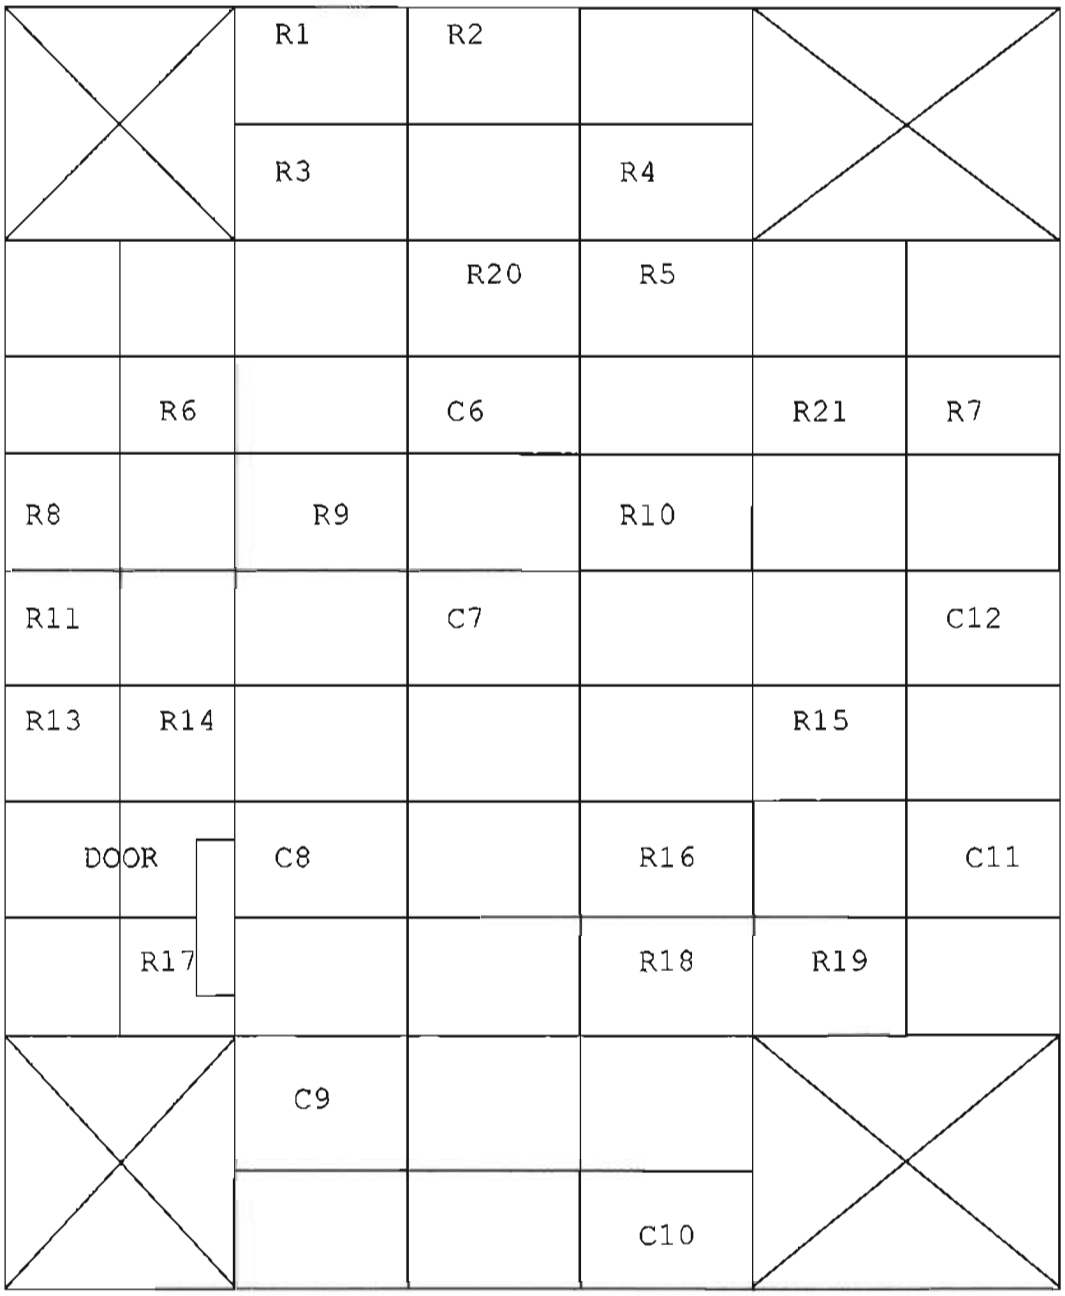

Table 12-5-18. Annex 115 - Final Status Survey Summary for RANDOM STATISTICAL SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 115				
Survey Date: 2/16/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	87	3	16	9
2	66	8	9	17
3	42	10	12	5
4	51	7	16	11
5	43	5	8	9
6	34	4	7	19
7	54	6	17	9
8	50	13	6	9
9	74	0	7	11
10	63	9	4	20
11	44	6	15	7
12	18	9	18	8
13	37	9	8	7
14	25	9	12	16
15	24	15	16	9
16	15	10	11	4
17	16	9	7	9
18	26	4	0	10
19	33	11	13	15
20	15	4	15	7
21	23	5	15	5
Average DPM	40	7	11	10
Standard Deviation, DPM	20	4	5	5
Maximum DPM	87	15	18	20
Action Limit, DPM			700	700

Table 12-5-19. Annex 115 - Final Status Survey Summary for ADDITIONAL SELECT SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 115				
Survey Date: 2/16/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	87	3	17	16
2	66	8	12	13
3	42	10	9	8
4	51	7	9	8
5	43	5	8	16
6	34	4	7	8
7	54	6	25	13
8	50	13	0	11
9	74	0	16	9
10	63	9	24	6
11	44	6	35	4
12	18	9	9	3
13	37	9	5	17
14	25	9	19	10
15	24	15	0	20
16	15	10	17	14
17	16	9	16	8
18	26	4	8	7
19	33	11	14	12
20	15	4	16	4
21	23	5	19	8
22			21	9
23			22	11
24			33	8
25			8	12
26			8	13
27			18	0
28			4	13
29			27	9
30			9	6
31			12	5
32			7	8

33			10	8
34			13	17
35			8	12
36			17	14
37			11	16
38			5	22
39			37	6
40 HOT SINK, RIGHT			75003	0
41 HOT SINK, LEFT			997	17
42			39	11
43			77	8
44			54	12
Average DPM	40	7	1744	10
Standard Deviation, DPM	20	4	11302	5
Maximum DPM	87	15	75003	22
Action Limit, DPM			700	700

Figure 12-5-9: Grid Map for Rockville Annex, Room 115
Survey date: 2/16/00
Survey results: background < 87 DPM; H-3 and C-14 < 18 DPM
R1-R21 = random statistical sample locations
C1-C40 = additional select sample locations

		R1	R2		R3		R4			
		R5			R6			C6		
R7	R8		C7		R9		C8		C9	
		R10		C10		C11		C12		
	C13	R11	R12			R13	R14		C14	
R15			C15			R16		C16	C17	
	R17	C18			R18		C19		C20	
C21		R19	C22	C23		C24		C25	C26	
	C27		C28		R20		C29		C30	
		R21		C31		C32				
			C33		C34		C35			

Table 12-5-20. Annex 115 HOT SINK - Final Status Survey Summary for selected location PRE-DECONTAMINATION EFFORTS		
Building: NMRC Rockville Annex		
Survey Unit or Room Number: 115		
Survey Date: 2/11/00	Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination		
Sample Description	H-3 (dpm)	C-14 (dpm)
C1 **Pre-decon** samples #C1-C12 right inner sink wall	347	4
C2 **Pre-decon** left inner sink wall	700	19
C3 **Pre-decon** rear inner sink wall	621	11
C4 **Pre-decon** front inner sink wall	391	7
C5 **Pre-decon** basin	2883	0
C6 **Pre-decon** upper right edge	160	2
C7 **Pre-decon** upper left edge	205	0
C8 **Pre-decon** upper front edge	203	2
C9 **Pre-decon** upper back edge	153	8
C10 **Pre-decon** basin drain, 3 inches below rim	2892	0
C11 **Pre-decon** basin drain, 1 inch below rim	642	7
C12 **Pre-decon** basin drain at rim surface	1009	0
C13 **Post-decon** right inner sink wall	74	5
C14 **Post-decon** left inner sink wall	43	9
C15 **Post-decon** rear inner sink wall	104	1
C16 **Post-decon** front inner sink wall	67	3
C17 **Post-decon** basin	1161	0
C18 **Post-decon** upper right edge	172	3
C19 **Post-decon** upper left edge	51	13
C20 **Post-decon** upper front edge	58	15
C21 **Post-decon** upper back edge	77	8
C22 **Post-decon** basin drain, 3 inches below rim	2795	10
C23 **Post-decon** basin drain, 1 inch below rim	110	10
C24 **Post-decon** basin drain at rim surface	183	2
Average DPM		
Standard Deviation, DPM		
Maximum DPM		
Action Limit, DPM	700	700

Table 12-5-21a. Annex 115 HOT SINK - Final Status Survey Summary for selected location POST-REMOVAL OF DRAIN PIPING BENEATH SINK		
Building: NMRC Rockville Annex		
Survey Unit or Room Number: 115		
Survey Date: 2/11/00	Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination		
Sample Description	H-3 (dpm)	C-14 (dpm)
C1 pre-decon left (L) drain pipe, inner surface	8158	13
C2 pre-decon L drain pipe, outer surface	429	0
C3 pre-decon right (R) drain pipe, inner	38924	0
C4 pre-decon R drain pipe, outer	660	11
C5 post-decon L drain pipe, inner surface	61185	399
C6 post-decon L drain pipe, outer surface	722	6
C7 post-decon R drain pipe, inner	100	20
C8 pre-decon R drain pipe, outer	51263	269
C9 floor at sink	305	6
C10 right sink basin, inner drain	612	9
C11 right sink basin	1109	10
C12 left sink basin, inner drain	69	0
C13 left sink basin	332	17
C14 corner of center bench near sink	14	18
C15 floor at door	8	10
C16 right shelf beneath sink	114	20
C17 left shelf beneath sink	106	11
C18 post-decon right sink basin drain	194	29
C19 post-decon left sink basin drain	7	9
C20 post-decon right sink basin	169	11
C21 post-decon left sink basin	32	12
C22 floor at bench and sink	120	10
Average DPM	7483	40
Standard Deviation, DPM	17894	97
Maximum DPM	61185	399
Action Limit, DPM	700	700

Table 12-5-21b. Annex 115 HOT SINK - Final Status Survey Summary for selected location POST-REMOVAL OF DRAIN PIPING BENEATH SINK		
Building: NMRC Rockville Annex		
Survey Unit or Room Number: 115		
Survey Date: 5/12/00	Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination		
Sample Description or Location	H-3 (dpm)	C-14 (dpm)
Pre-Decontamination Results		
Floor at sink	935	14
Floor at door	257	19
Shelf beneath sink	542	0
Outer surface of drainpipe after cutting to stub length	270	0
Post-Decontamination (Initial Effort)		
Outer surface of drainpipe stub	316	0
Outer surface of drainpipe stub	219	1
Inner surface of drainpipe stub	35352	0
Inner surface of drainpipe stub	12621	0
Post-Decontamination (Second Effort)		
Outer surface of drainpipe stub	255	6
Outer surface of drainpipe stub	182	8
Inner surface of drainpipe stub	9499	0
Inner surface of drainpipe stub	5818	0
Post-Decontamination (Final Effort)		
Outer surface of drainpipe stub	411	3
Outer surface of drainpipe stub	72	8
Inner surface of drainpipe stub	5600	0
Inner surface of drainpipe stub	2454	10
Floor at sink	46	10
Floor at door	109	7
Shelf beneath sink	20	13
Wall at drainpipe stub	85	7
Regulatory Screening Levels for Unrestricted Release	1.2e+08	3.7e+06

Table 12-5-22. Annex 123 - Final Status Survey Summary for RANDOM STATISTICAL SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 123				
Survey Date: 2/11/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	31	1	28	15
2	19	5	25	5
3	49	15	15	11
4	42	2	15	5
5	11	7	7	21
6	45	5	21	7
7	32	3	31	9
8	30	6	14	12
9	31	8	40	12
10	23	7	20	15
11	20	7	5	11
12	19	12	22	13
13	14	11	21	12
14	27	2	13	14
15	26	15	19	9
16	25	8	22	5
17	9	11	26	10
18	12	15	12	7
19	52	9	20	12
20	29	11	48	7
21	46	6	19	15
Average DPM	28	8	21	11
Standard Deviation, DPM	13	4	10	4
Maximum DPM	52	15	48	21
Action Limit, DPM			700	700

Table 12-5-23. Annex 123 - Final Status Survey Summary for ADDITIONAL SELECT SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 123				
Survey Date: 2/11/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	31	1	14	11
2	19	5	18	15
3	49	15	14	13
4	42	2	5	9
5	11	7	26	4
6	45	5	8	10
7	32	3	40	6
8	30	6	18	11
9	31	8	11	19
10	23	7	11	11
11	20	7	25	12
12	19	12	35	5
13	14	11	14	17
14	27	2	24	13
15	26	15		
16	25	8		
17	9	11		
18	12	15		
19	52	9		
20	29	11		
21	46	6		
Average DPM	28	8	19	11
Standard Deviation, DPM	13	4	10	4
Maximum DPM	52	15	40	19
Action Limit, DPM			700	700

Figure 12-5-10: Grid Map for Rockville Annex, Room 123
Survey date: 2/11/00
Survey results: background < 52 DPM; H-3 and C-14 < 48 DPM
R1-R21 = random statistical sample locations
C1-C14 = additional select sample locations

		R2	R6		R11		
			R7				
		R3			R12	R15	R16
	C6		R8	R9	R13		
R1		R4		C7		C8	
R19			C9		R20	R21	R17
		R5			R14		R18
		C10		R10			

Table 12-5-24. Annex 124 - Final Status Survey Summary for 100% Coverage				
Building: Rockville Annex		Room Number: 124		
Survey Date: 2/17/00		Count Times: 1 minute		
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	28	17	19	14
2	6	6	7	10
3	16	3	6	12
4	33	15	18	4
5	37	6	17	5
6	16	6	3	7
7	242	0	8	8
8	11	11	12	12
9	58	10	10	8
10	124	7	8	20
11	55	6	0	8
12	31	3	8	10
13	181	0	0	10
14	118	13	9	9
15	22	10	3	8
16	180	1	6	8
17	316	0	1	17
18	65	0	9	4
19	19	16	1	18
20	85	4	7	6
21	53	9	16	6
22			21	0
23			0	5
24			0	17
25			9	17
26			25	6
27			7	12
Average DPM	81	7	9	10
Standard Deviation, DPM	84	5	7	5
Maximum DPM	316	17	25	20
Action Limit, DPM			700	700

Table 12-5-25. Annex 124 - Final Status Survey Summary for ADDITIONAL SELECT SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 124				
Survey Date: 2/17/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	28	17	18	4
2	6	6	12	9
3	16	3	11	14
4	33	15	13	16
5	37	6	111	5
6	16	6		
7	242	0		
8	11	11		
9	58	10		
10	124	7		
11	55	6		
12	31	3		
13	181	0		
14	118	13		
15	22	10		
16	180	1		
17	316	0		
18	65	0		
19	19	16		
20	85	4		
21	53	9		
Average DPM	81	7	33	10
Standard Deviation, DPM	84	5	44	5
Maximum DPM	316	17	111	16
Action Limit, DPM			700	700

Figure 12-5-11: Grid Map for Rockville Annex, Room 124
Survey date: 2/17/00
Survey results: background < 316 DPM; H-3 and C-14 < 111 DPM
R1-R27 = random statistical sample locations
C1-C5 = additional select sample locations

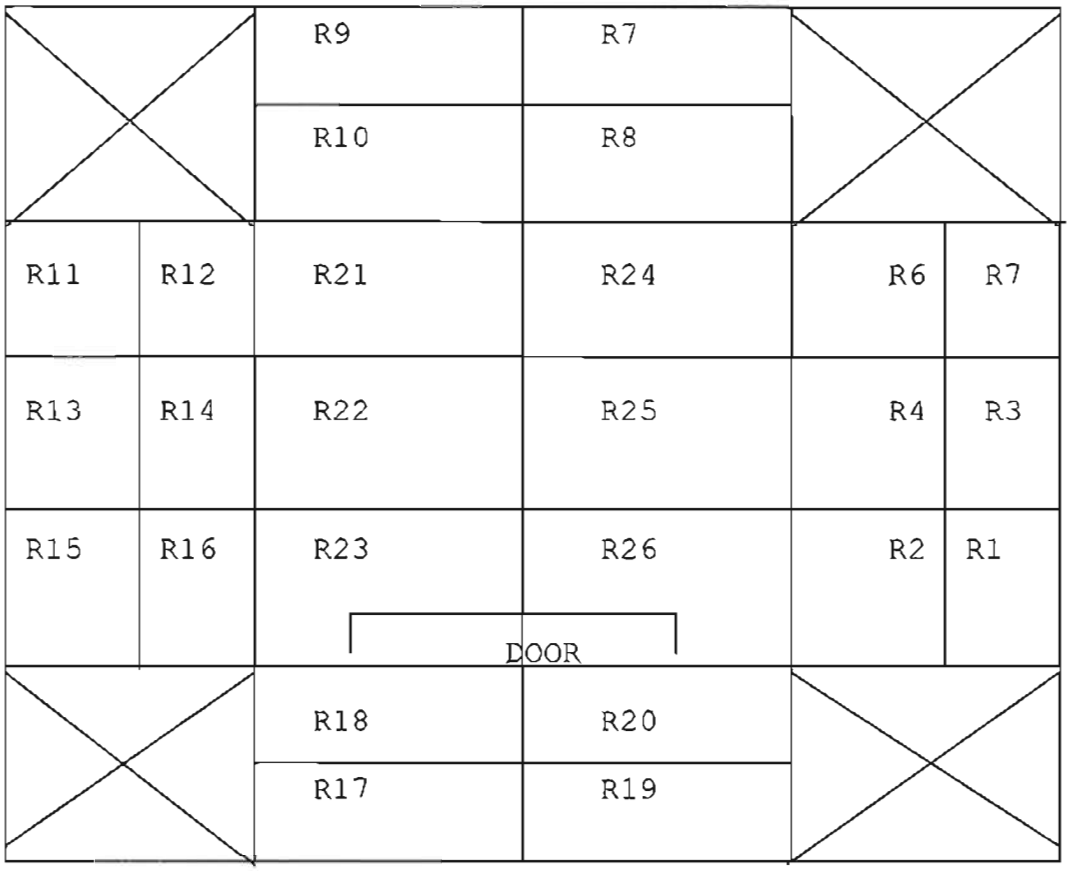

R27 = COUNTER TOP

Table 12-5-26. Annex 125 - Final Status Survey Summary for 100% Coverage				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 125				
Survey Date: 2/17/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	28	17	14	10
2	6	6	13	0
3	16	3	10	10
4	33	15	5	13
5	37	6	18	6
6	16	6	13	8
7	242	0	2	12
8	11	11	13	9
9	58	10	19	5
10	124	7	12	4
11	55	6	4	6
12	31	3	17	6
13	181	0	6	7
14	118	13	6	7
15	22	10	13	8
16	180	1	5	9
17	316	0	12	4
18	65	0	6	8
19	19	16	10	9
20	85	4	6	12
21	53	9	20	13
22			13	7
23			0	13
24			5	6
25			18	5
26			0	10
Average DPM	81	7	10	8
Standard Deviation, DPM	84	5	6	3
Maximum DPM	316	17	20	13
Action Limit, DPM			700	700

Table 12-5-27. Annex 125 - Final Status Survey Summary for ADDITIONAL SELECT SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 125				
Survey Date: 2/17/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	28	17	16	6
2	6	6	20	13
3	16	3	5	15
4	33	15	12	9
5	37	6	11	12
6	16	6		
7	242	0		
8	11	11		
9	58	10		
10	124	7		
11	55	6		
12	31	3		
13	181	0		
14	118	13		
15	22	10		
16	180	1		
17	316	0		
18	65	0		
19	19	16		
20	85	4		
21	53	9		
Average DPM	81	7	13	11
Standard Deviation, DPM	84	5	6	4
Maximum DPM	316	17	20	15
Action Limit, DPM			700	700

Figure 12-5-12: Grid Map for Rockville Annex, Room 125
Survey date: 2/17/00
Survey results: background < 316 DPM; H-3 and C-14 < 20 DPM
R1-R26 = random statistical sample locations
C1-C5 = additional select sample locations

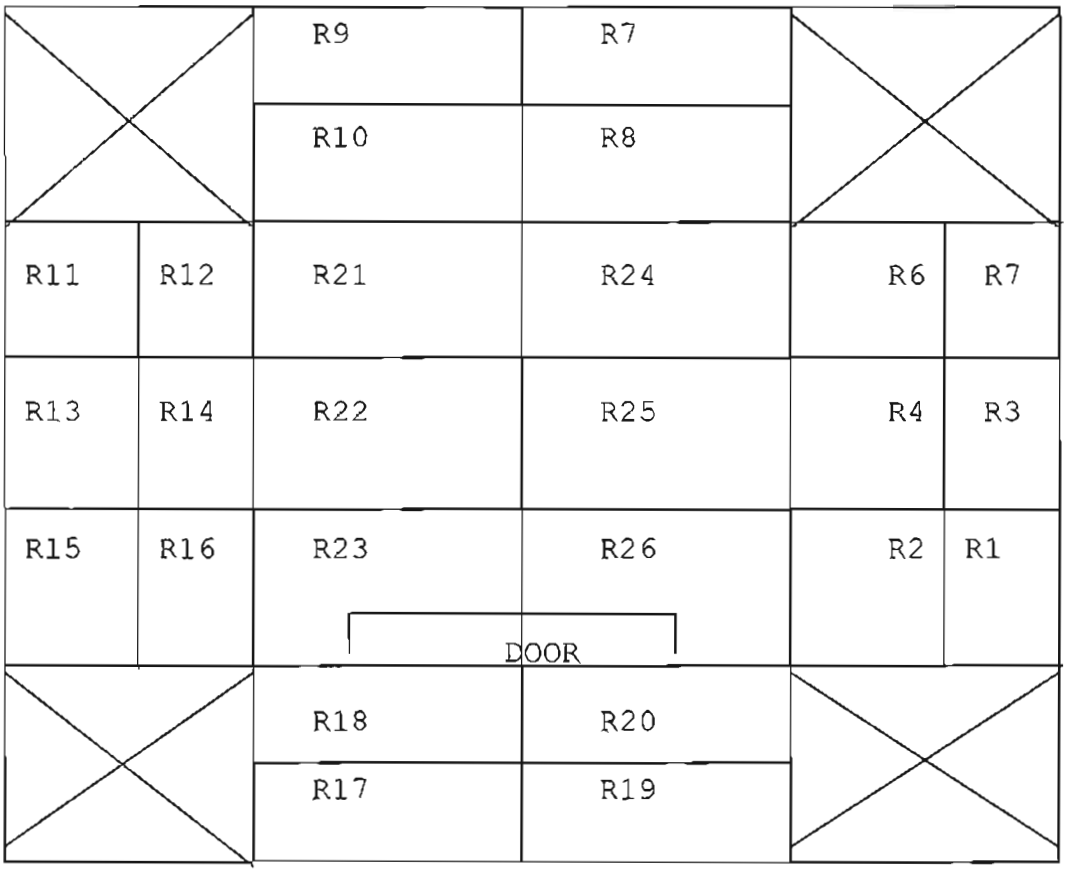

Table 12-5-28. Annex 126 - Final Status Survey Summary for RANDOM STATISTICAL SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 126				
Survey Date: 2/14/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	28	2	6	13
2	47	19	32	8
3	78	3	8	17
4	35	15	2	10
5	41	10	19	13
6	57	2	11	13
7	52	9	13	13
8	72	7	20	4
9	24	12	2	17
10	44	8	14	5
11	45	5	10	17
12	66	12	13	8
13	62	5	13	13
14	38	9	8	8
15	38	9	9	8
16	33	10	15	10
17	27	8	11	12
18	15	10	0	10
19	41	6	13	9
20	42	5	27	5
21	11	18	8	6
Average DPM	43	9	12	10
Standard Deviation, DPM	17	5	8	4
Maximum DPM	78	19	32	17
Action Limit, DPM			700	700

Table 12-5-29. Annex 126 - Final Status Survey Summary for ADDITIONAL SELECT SAMPLES				
Building: Rockville Annex		Room Number: 126		
Survey Date: 2/14/00		Count Times: 1 minute		
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	28	2	13	7
2	47	19	10	14
3	78	3	14	10
4	35	15	15	5
5	41	10	23	6
6	57	2	25	4
7	52	9	0	9
8	72	7	17	10
9	24	12	25	13
10	44	8	5	10
11	45	5	3	8
12	66	12	13	11
13	62	5	6	11
14	38	9	3	8
15	38	9	1	7
16	33	10	19	5
17	27	8	12	9
18	15	10	14	10
19	41	6	5	6
20	42	5	7	6
21	11	18	15	4
22			5	9
23			4	10
24			23	14
25			2	12
26			8	21
27			0	19
28			0	18
29			73	9
Average DPM	43	9	12	10
Standard Deviation, DPM	17	5	14	4
Maximum DPM	78	19	73	21
Action Limit, DPM			700	700

Figure 12-5-13: Grid Map for Rockville Annex, Room 126
Survey date: 2/14/00
Survey results: background < 78 DPM; H-3 and C-14 < 73 DPM
R1-R21 = random statistical sample locations
C1-C29 = additional select sample locations

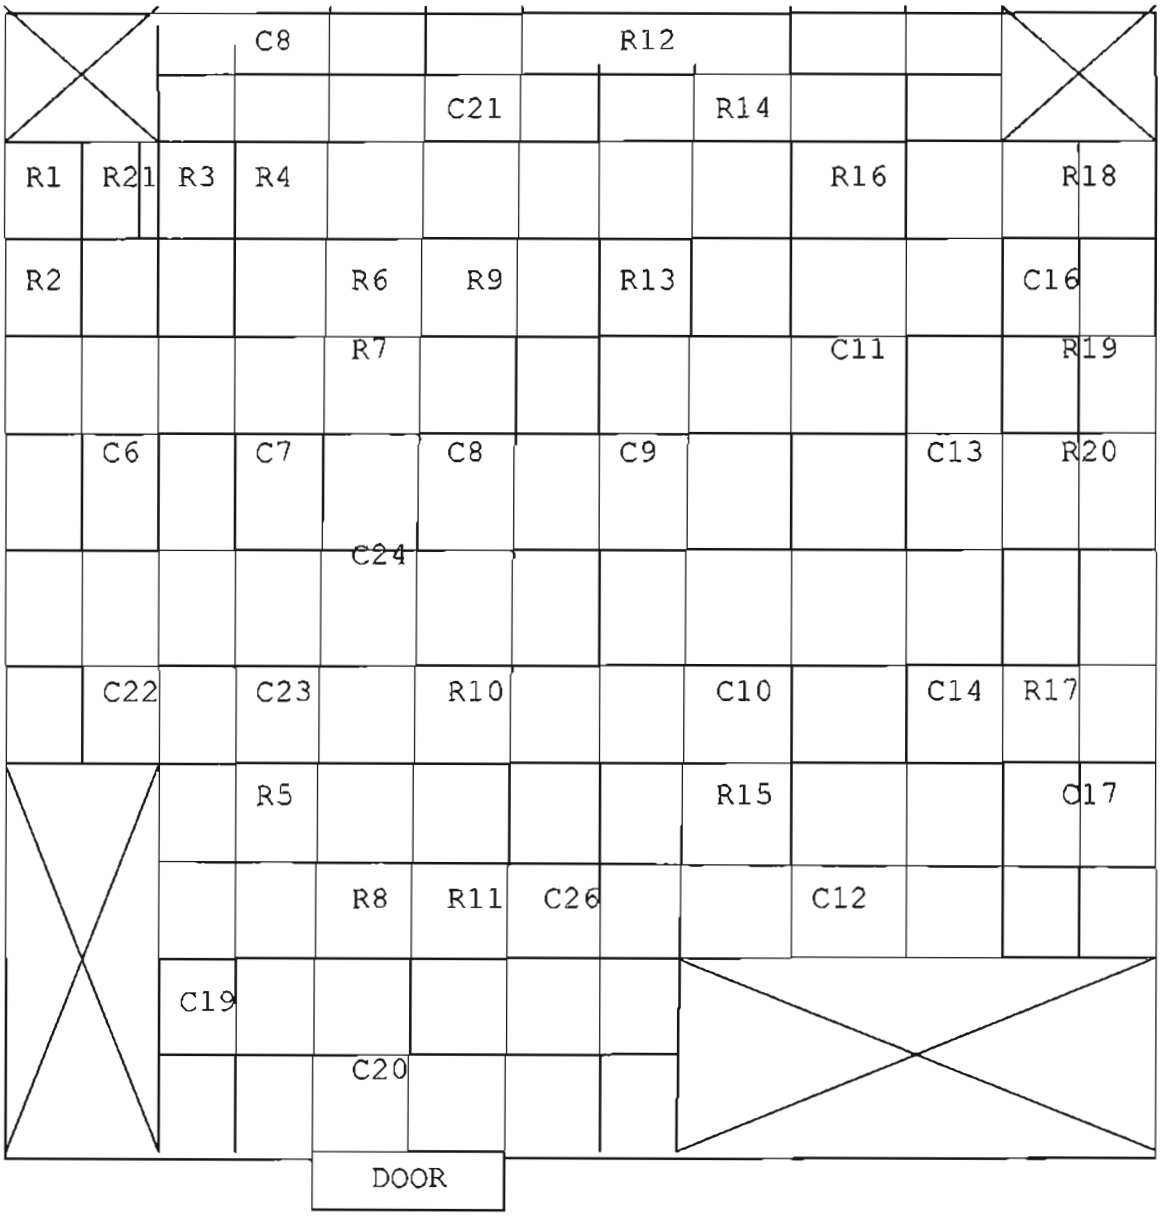

Table 12-5-30. Annex 127 - Final Status Survey Summary for RANDOM STATISTICAL SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 127				
Survey Date: 2/11/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	31	1	9	10
2	19	5	31	8
3	49	15	3	17
4	42	2	31	11
5	11	7	17	5
6	45	5	6	9
7	32	3	40	7
8	30	6	67	5
9	31	8	12	5
10	23	7	46	5
11	20	7	33	6
12	19	12	57	6
13	14	11	26	7
14	27	2	35	10
15	26	15	0	19
16	25	8	22	7
17	9	11	2	17
18	12	15	33	9
19	52	9	36	11
20	29	11	24	3
21	46	6	20	4
Average DPM	28	8	26	9
Standard Deviation, DPM	13	4	18	4
Maximum DPM	52	15	67	19
Action Limit, DPM			700	700

Table 12-5-31. Annex 127 - Final Status Survey Summary for ADDITIONAL SELECT SAMPLES

Survey Date: 2/11/00	Count Times: 1 minute
Building: NMRC Rockville Annex	Survey Unit or Room Number: 128-1

Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination

Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	31	1	152	0
2	19	5	131	4
3	49	15	132	5
4	42	2	67	6
5	11	7	38	5
6	45	5	23	16
7	32	3	42	3
8	30	6	24	12
9	31	8	43	6
10	23	7	65	12
11	20	7	28	5
12	19	12	17	6
13	14	11	37	6
14	27	2	36	3
15	26	15	43	9
16	25	8	49	10
17	9	11	12	10
18	12	15	12	13
19	52	9	29	10
20	29	11	31	5
21	46	6	9	3
22			26	7
23			21	14
24			0	12
25			24	9
26			14	9
27			24	9
28			38	10
29			43	5
30			32	14
Average DPM	28	8	41	8
Standard Deviation, DPM	13	4	36	4
Maximum DPM	52	15	152	16
Action Limit, DPM			700	700

Figure 12-5-14: Grid Map for Rockville Annex, Room 127
Survey date: 2/11/00
Survey results: background < 52 DPM; H-3 and C-14 < 152 DPM
R1-R21 = random statistical sample locations
C1-C32 = additional select sample locations

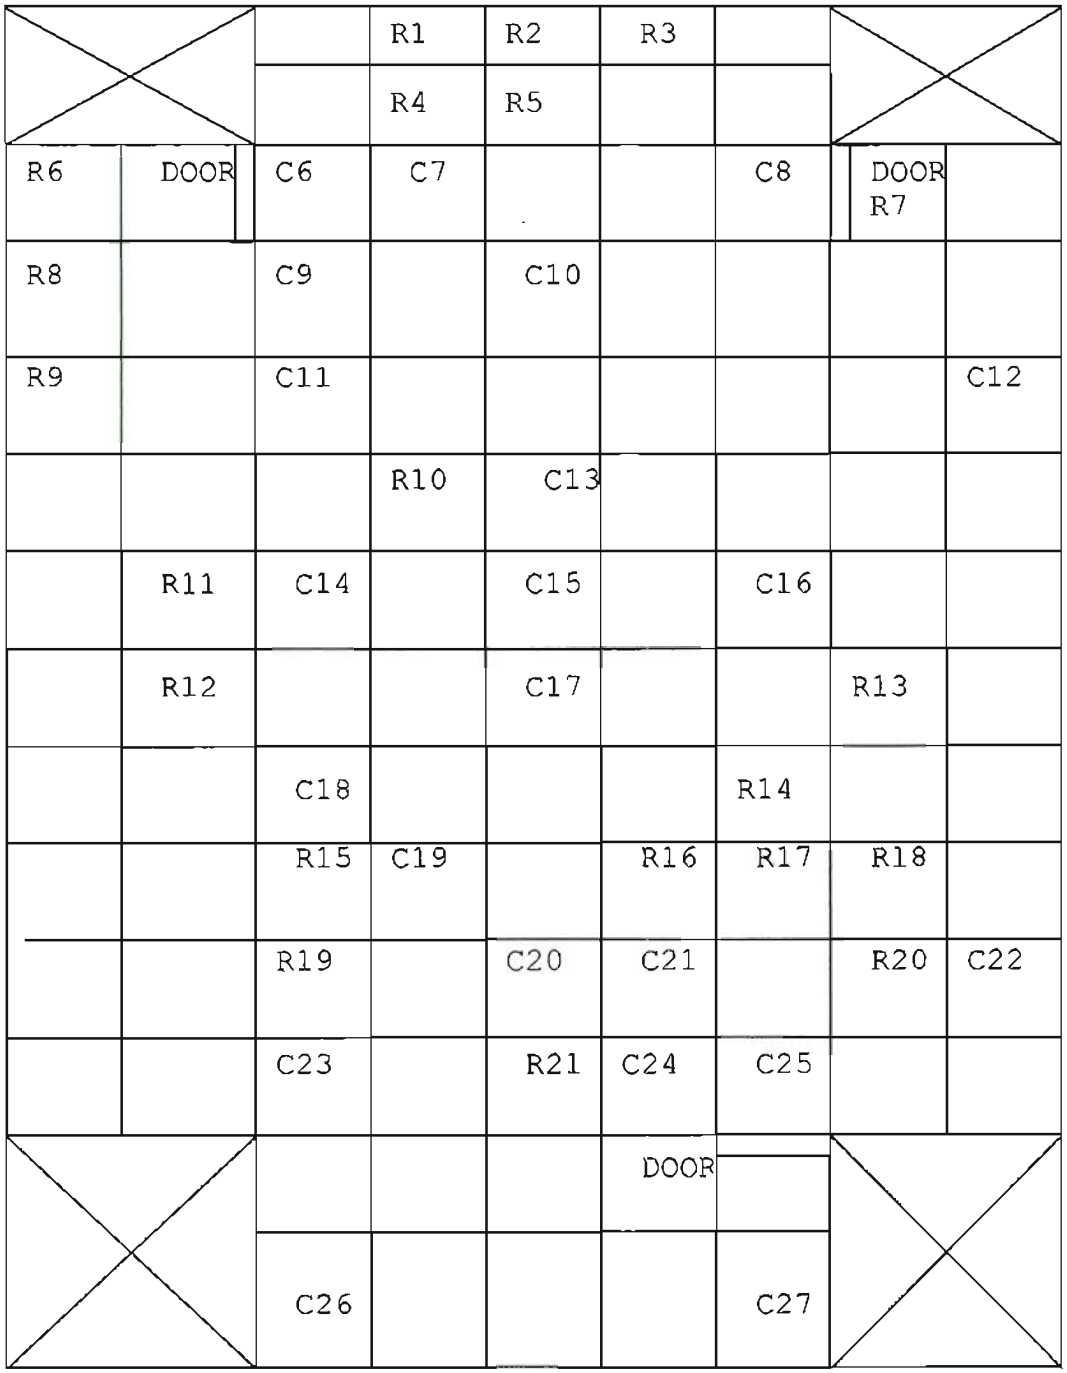

Table 12-5-32. Annex 128-1 - Final Status Survey Summary for RANDOM STATISTICAL SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 128-1				
Survey Date: 2/14/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	28	2	5	9
2	47	19	0	10
3	78	3	15	14
4	35	15	6	18
5	41	10	15	6
6	57	2	5	12
7	52	9	17	6
8	72	7	10	4
9	24	12	7	16
10	44	8	23	11
11	45	5	16	16
12	66	12	6	16
13	62	5	13	16
14	38	9	14	9
15	38	9	27	8
16	33	10	18	16
17	27	8	25	12
18	15	10	21	9
19	41	6	10	14
20	42	5	10	10
21	11	18	18	6
Average DPM	43	9	13	11
Standard Deviation, DPM	17	5	7	4
Maximum DPM	78	19	27	18
Action Limit, DPM			700	700

Table 12-5-33. Annex 128-1 - Final Status Survey Summary for ADDITIONAL SELECT SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 128-1				
Survey Date: 2/14/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	28	2	11	8
2	47	19	5	12
3	78	3	33	12
4	35	15	10	15
5	41	10	19	11
6	57	2	17	6
7	52	9	3	17
8	72	7	7	10
9	24	12	9	8
10	44	8	23	14
11	45	5	24	9
12	66	12	11	5
13	62	5	9	14
14	38	9		
15	38	9		
16	33	10		
17	27	8		
18	15	10		
19	41	6		
20	42	5		
21	11	18		
Average DPM	43	9	14	11
Standard Deviation, DPM	17	5	9	4
Maximum DPM	78	19	33	17
Action Limit, DPM			700	700

Figure 12-5-15: Grid Map for Rockville Annex, Room 128-1
Survey date: 2/14/00
Survey results: background < 78 DPM; H-3 and C-14 < 33 DPM
R1-R21 = random statistical sample locations
C1-C13 = additional select sample locations

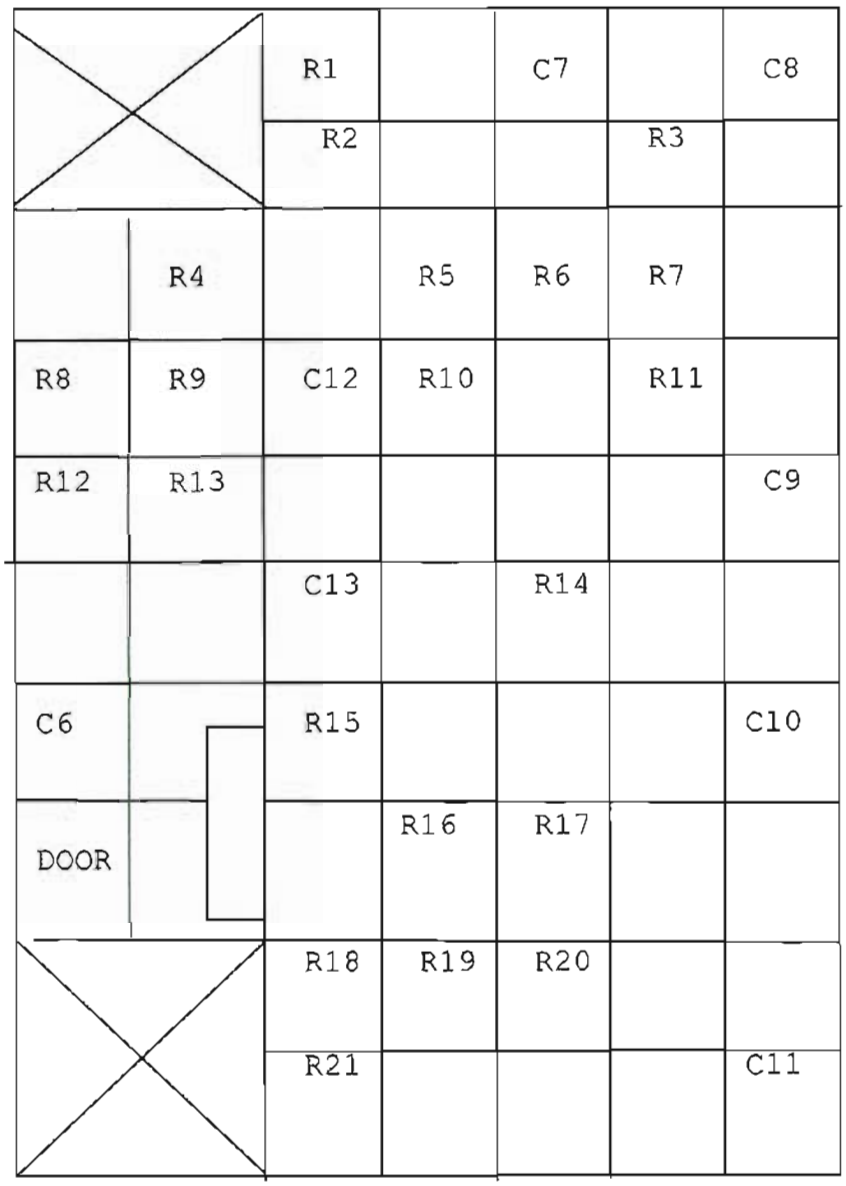

Table 12-5-34. Annex 128-2 - Final Status Survey Summary for RANDOM STATISTICAL SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 128-2				
Survey Date: 2/14/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	28	2	22	6
2	47	19	22	13
3	78	3	28	9
4	35	15	14	11
5	41	10	12	5
6	57	2	19	9
7	52	9	53	9
8	72	7	12	8
9	24	12	57	13
10	44	8	31	12
11	45	5	43	7
12	66	12	51	5
13	62	5	144	5
14	38	9	20	15
15	38	9	40	12
16	33	10	49	14
17	27	8	26	12
18	15	10	21	6
19	41	6	55	21
20	42	5	14	8
21	11	18	12	13
Average DPM	43	9	35	10
Standard Deviation, DPM	17	5	29	4
Maximum DPM	78	19	144	21
Action Limit, DPM			700	700

Table 12-5-35. Annex 128-2 - Final Status Survey Summary for ADDITIONAL SELECT SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 128-2				
Survey Date: 2/14/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	28	2	7	10
2	47	19	74	7
3	78	3	27	7
4	35	15	23	3
5	41	10	5	9
6	57	2	8	9
7	52	9	4	11
8	72	7	0	23
9	24	12	16	17
10	44	8	0	13
11	45	5	1	8
12	66	12	22	9
13	62	5	20	7
14	38	9	12	7
15	38	9	7	7
16	33	10		
17	27	8		
18	15	10		
19	41	6		
20	42	5		
21	11	18		
Average DPM	43	9	15	10
Standard Deviation, DPM	17	5	19	5
Maximum DPM	78	19	74	23
Action Limit, DPM			700	700

Figure 12-5-16: Grid Map for Rockville Annex, Room 128-2
Survey date: 2/14/00
Survey results: background < 78 DPM; H-3 and C-14 < 144 DPM
R1-R21 = random statistical sample locations
C1-C15 = additional select sample locations

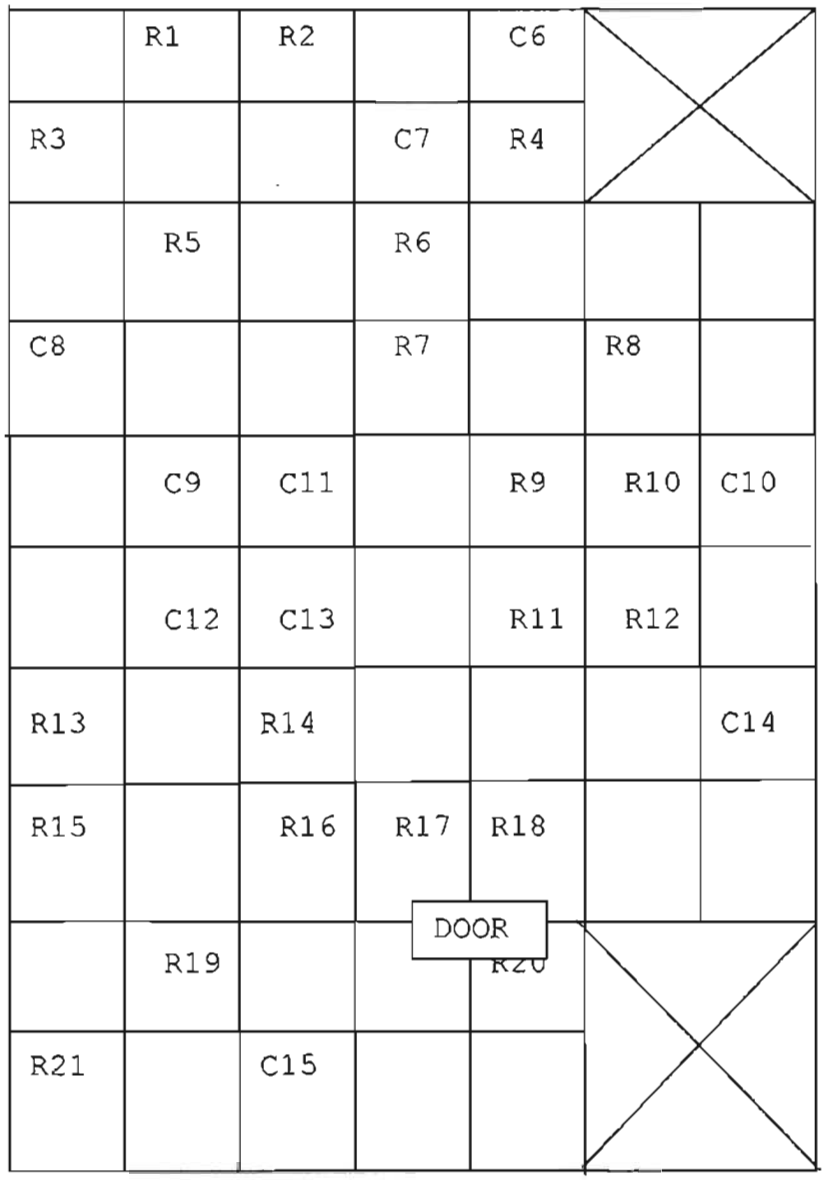

Table 12-5-36. Annex 1ST Floor Hallway - Final Status Survey Summary for SELECT SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 1ST Floor Hallway				
Survey Date: 3/28/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	57	6	17	10
2	51	4	2	11
3	127	2	19	10
4	118	3	12	8
5	70	7	13	7
6	69	3	12	15
7	33	4	12	9
8	40	6	6	14
9	70	5	11	9
10	80	4	6	11
11	46	5	6	7
12	64	7	5	8
13	42	14	8	9
14	34	5	2	12
15	32	8	6	14
16	34	8	4	7
17	31	7	20	10
18	20	8	4	8
19	34	6	13	8
20	47	6	10	6
21	28	3	11	4
22			36	10
23			23	13
24			26	12
25			10	14
26			20	10
27			34	10
28			54	5
29			9	12
30			43	9
31			14	6
32			39	8

33			23	8
34			14	9
35			19	7
36			0	15
37			11	20
38			6	13
39			26	14
40			4	8
41			25	5
42			27	8
43			17	10
44			34	7
45			1	9
46			3	14
47			10	6
48			5	9
49			0	21
50			18	8
51			17	7
Average DPM	54	6	15	10
Standard Deviation, DPM	28	3	12	4
Maximum DPM	127	14	54	21
Action Limit, DPM			700	700

Figure 12-5-17: Grid Map for Rockville Annex, First Floor halls (sectioned as parts A, B and G)
Survey date: 2/22/00
Survey results: background < 127 DPM; H-3 and C-14 < 54 DPM
C1-C51 = Control or selected sample locations

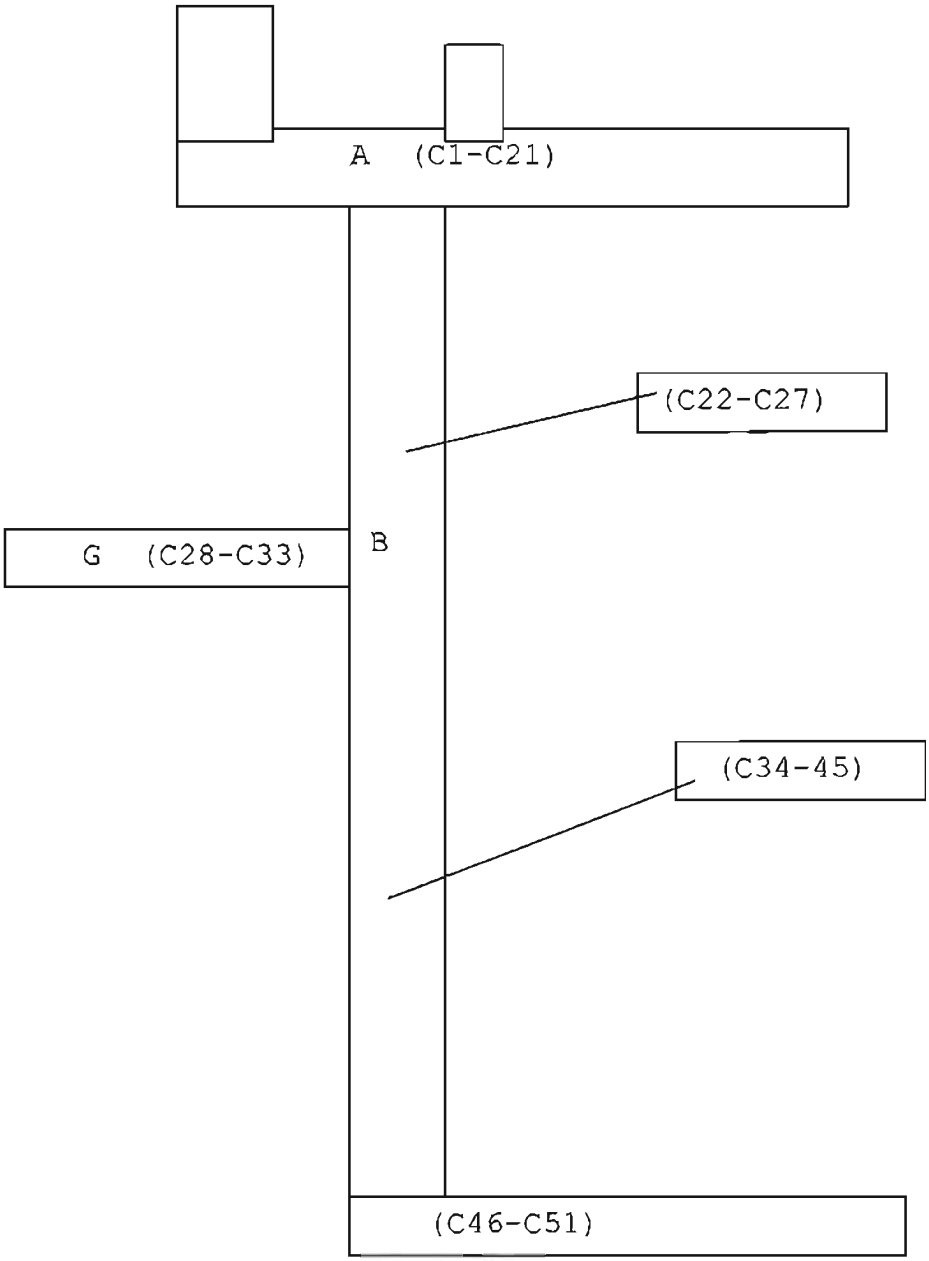

Table 12-5-37. Annex 2nd Floor Hallway - Final Status Survey Summary for SELECT SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: 2ND Floor Hallway				
Survey Date: 2/22/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	33	5	13	13
2	3	14	5	8
3	18	6	2	12
4	42	11	10	12
5	24	8	16	9
6	27	4	15	10
7	8	13	14	12
8	14	10	11	5
9	18	6	3	17
10	12	15	13	4
11	11	12	15	8
12	8	7	3	8
13	12	8	17	10
14	31	12	3	11
15	30	9	8	7
16	11	6	8	6
17	38	0	17	10
18	10	13	22	6
19	4	11	12	4
20	24	7	13	4
21	19	5	13	5
22			3	14
23			0	16
24			12	14
25			8	10
26			13	3
27			9	14
28			28	11
29			5	6
30			8	8
31			7	17

32			4	6
33			6	13
34			19	14
35			0	17
36			12	8
37			9	8
38			3	14
39			14	7
40			16	6
41			33	1
42			33	10
43			18	8
44			3	14
45			0	12
46			0	11
47			0	15
48			15	13
49			7	10
50			8	14
51			11	16
52			8	8
53			38	17
54			10	11
55			10	12
56			0	17
57			8	8
58			1	8
59			20	20
60			10	8
61			18	18
62			18	19
63			0	27
64			1	36
65			43	47
66			76	65
67			5	11
Average DPM	19	9	12	13
Standard Deviation, DPM	11	4	12	10
Maximum DPM	42	15	76	65
Action Limit, DPM			700	700

Table 12-5-38. Annex Stair A - Final Status Survey Summary for CONTROL AND SELECTED SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: Stair A				
Survey Date: 2/9/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	24	5	14	15
2	10	12	18	11
3	25	13	50	8
4	22	12	11	14
5	8	53	8	12
6	29	6	22	9
7	17	18	9	10
8	8	15	23	5
9	11	10	7	13
10	7	13	13	14
11	6	17	16	10
12	18	9	16	11
13	7	13	22	12
14	25	22		
15	19	9		
16	16	8		
17	25	15		
18	21	11		
19	8	10		
20	25	12		
21	28	10		
Average DPM	17	14	18	11
Standard Deviation, DPM	8	10	11	3
Maximum DPM	29	53	50	15
Action Limit, DPM			700	700

Table 12-5-39. Annex Stair B - Final Status Survey Summary for CONTROL AND SELECTED SAMPLES				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: Stair B				
Survey Date: 3/28/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	0	5	11	5
2	5	10	25	4
3	19	4	6	10
4	0	13	20	15
5	13	5	17	6
6	0	6	8	2
7	33	14	0	9
8	15	0	34	17
9	24	7	0	12
10	8	8	37	7
11	22	12	43	4
12	0	16	0	12
13	4	10	0	18
14	0	8	0	18
15	16	6	0	3
16	29	5	48	12
17	0	10	0	15
18	15	7	0	16
19	0	28	22	2
20	9	5	6	18
21	14	5	35	10
22			12	11
23			32	16
24			0	15
25			9	14
26			0	19
27			8	5
28			0	24
29			0	12
30			20	2
31			1	18

32			0	12
33			0	13
34			0	13
35			21	8
Average DPM	11	9	12	11
Standard Deviation, DPM	10	6	15	6
Maximum DPM	33	28	48	24
Action Limit, DPM			700	700

Table 12-5-40. Annex Loading Dock Area - Final Status Survey Summary for 100% SAMPLING				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: Loading Dock Area				
Survey Date: 3/28/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	0	5	167	0
2	5	10	106	1
3	19	4	24	11
4	0	13	24	14
5	13	5	56	2
6	0	6	9	12
7	33	14	51	2
8	15	0	17	11
9	24	7	18	6
10	8	8	17	6
11	22	12	6	2
12	0	16	31	3
13	4	10	0	12
14	0	8	7	14
15	16	6	0	6
16	29	5	0	6
17	0	10	30	4
18	15	7	15	11
19	0	28	22	6
20	9	5	32	0
21	14	5	13	4
22			52	1
23			0	9
24			10	11
25			0	6
26			0	20
27			6	5
28			10	7
29			4	5
30			0	7
31			3	16
32			0	8

33			0	11
34			0	3
35			0	17
36			11	12
37			14	9
38			6	2
39			15	4
40			7	7
41			0	8
42			0	13
43			0	8
44			0	11
45			19	6
46			13	6
47			7	0
48			4	7
49			0	23
50			0	5
51			0	15
52			0	23
53			3	16
54			13	9
55			0	17
56			2	12
57			13	11
58			0	8
59			0	11
60			0	9
61			4	10
62			19	11
63			2	15
64			4	16
65			10	11
Average DPM	11	9	14	9
Standard Deviation, DPM	10	6	26	5
Maximum DPM	33	28	167	23
Action Limit, DPM			700	700

Figure 12-5-18: Grid Map for Rockville Annex, Loading Dock Area
Survey date: 3/28/00
Survey results: background < 33 DPM; H-3 and C-14 < 167 DPM
C1-C65 = select sample locations

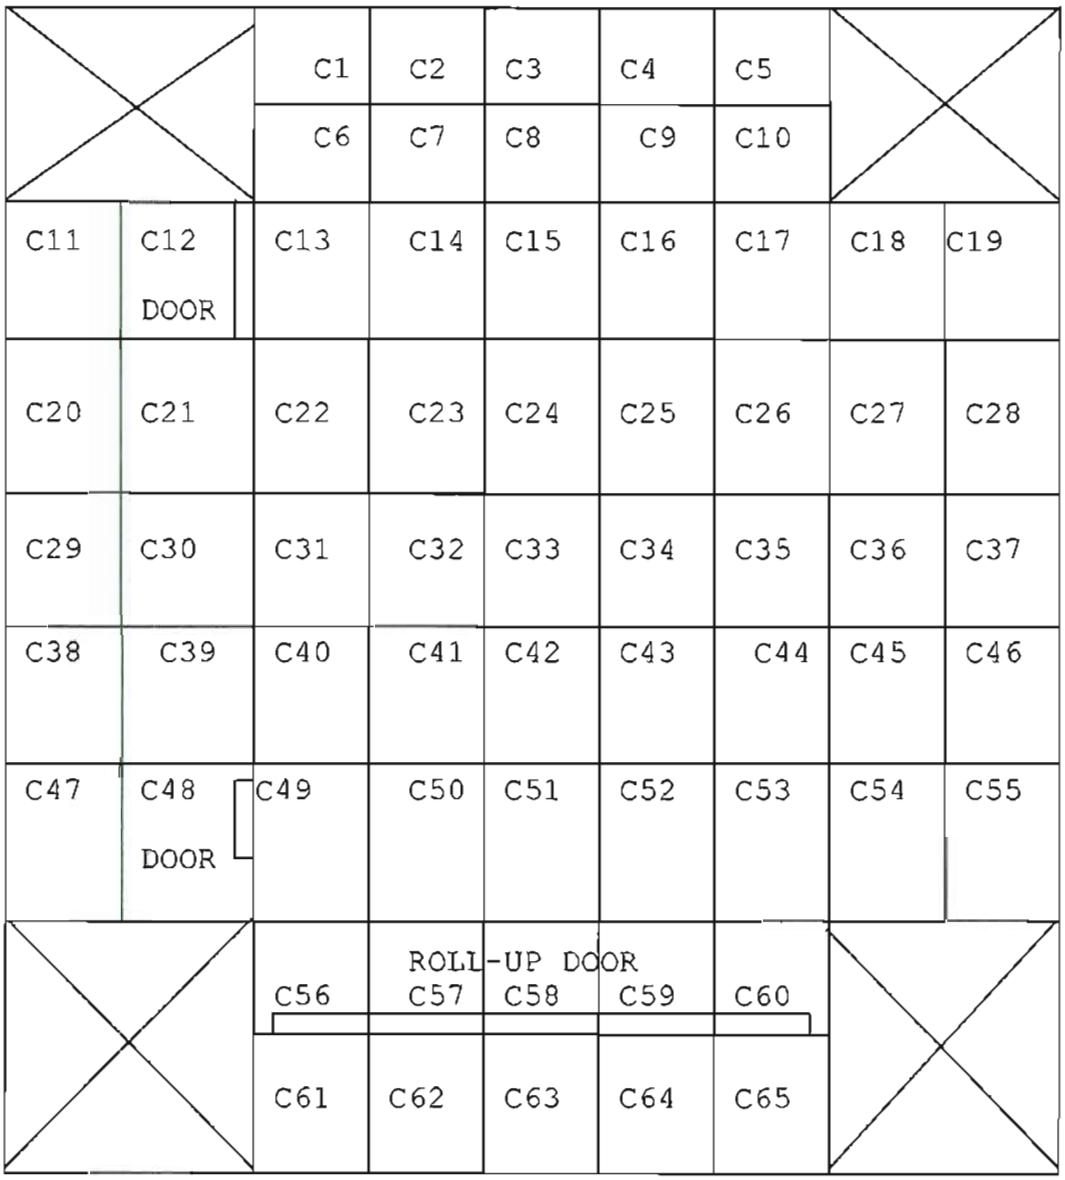

Table 12-5-41. Annex Loading Dock Storage - Final Status Survey Summary for 100% SAMPLING				
Survey Unit: NMRC Rockville Annex Loading Dock Storage				
Survey Date: 3/28/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	0	5	3	7
2	5	10	16	11
3	19	4	12	11
4	0	13	10	9
5	13	5	10	7
6	0	6	0	20
7	33	14	14	2
8	15	0	1	14
9	24	7	13	8
10	8	8	0	0
11	22	12	11	11
12	0	16	80	7
13	4	10	13	2
14	0	8	18	1
15	16	6	2	10
16	29	5	26	4
17	0	10	11	5
18	15	7	0	14
19	0	28	23	4
20	9	5	0	10
21	14	5	10	7
22			0	7
23			6	17
24			19	11
25			21	0
26			15	9
27			19	7
28			68	0
Average DPM	11	9	15	8
Standard Deviation, DPM	10	6	18	5
Maximum DPM	33	28	80	20
Action Limit, DPM			700	700

Figure 12-5-19: Grid Map for Rockville Annex, Loading Dock Storage Room
Survey date:
Survey results: background < 33 DPM; H-3 and C-14 < 80 DPM
C1-C28 = select sample locations

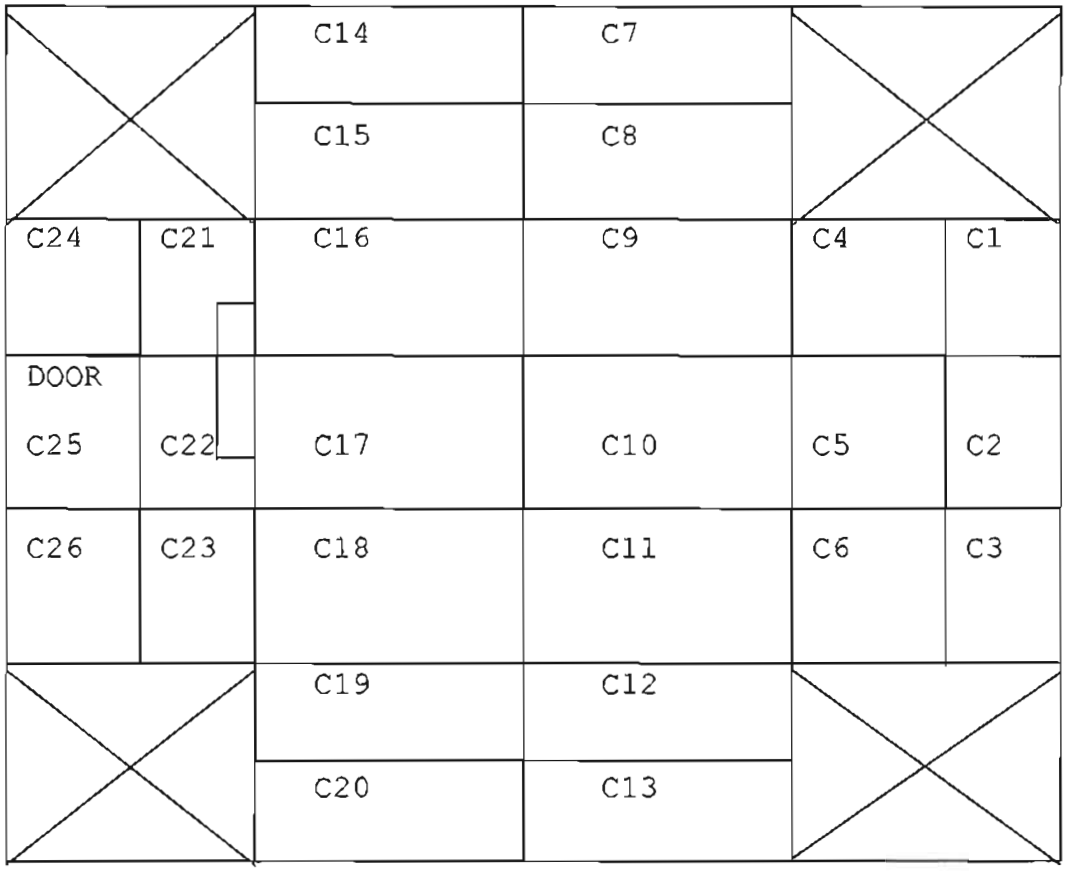

Table 12-5-42. Annex Radiation Waste Locker - Final Status Survey Summary for 100% SAMPLING (INITIAL EFFORT)				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: Radiation Waste Locker				
Survey Date: 2/22/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	33	5	16	10
2	3	14	33	7
3	18	6	67	8
4	42	11	337	0
5	24	8	109	0
6	27	4	28	13
7	8	13	56	5
8	14	10	161	9
9	18	6	243	6
10	12	15	97	5
11	11	12	27	8
12	8	7	34	7
13	12	8	102	0
14	31	12	69	1
15	30	9	84	4
16	11	6	32	7
17	38	0	41	9
18	10	13	139	3
19	4	11	69	2
20	24	7	27	2
21	19	5	88	10
22			54	9
23			163	9
24			96	6
25			45	10
26			84	10
27			128	2
28			126	10
29			34	7
30			33	6
31			25	9
32			25	12

33			14	9
34			17	16
35			18	13
36			9	10
37			23	11
38			40	12
39			23	7
40			27	7
41			7	9
42			19	8
43			37	7
44			20	13
45			25	9
46			22	7
47			12	8
48			13	4
49			8	6
50			22	14
51			29	9
52			18	7
53			12	8
54			13	4
55			30	3
56			30	3
57			31	15
58			25	13
59			24	6
60			13	11
61			19	6
62			33	8
63			18	7
64			27	3
65			29	10
66			23	14
67			33	9
68			13	17
69			12	10
70			25	7
71			27	12
72			49	6
73			32	14

74			18	9
Average DPM	19	9	49	8
Standard Deviation, DPM	11	4	55	4
Maximum DPM	42	15	337	17
Action Limit, DPM			700	700

Table 12-5-43. Annex Radiation Waste Locker - Final Status Survey Summary for 100% SAMPLING (POST-DECONTAMINATION EFFORT)				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: Radiation Waste Locker				
Survey Date: 3/28/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	0	5	11	9
2	5	10	13	2
3	19	4	19	13
4	0	13	40	5
5	13	5	35	5
6	0	6	13	6
7	33	14	42	5
8	15	0	20	4
9	24	7	26	0
10	8	8	18	6
11	22	12	34	5
12	0	16	17	4
13	4	10	25	6
14	0	8	21	6
15	16	6	41	25
16	29	5	47	10
17	0	10	33	8
18	15	7	27	10
19	0	28	18	0
20	9	5	28	8
21	14	5	31	3
22			22	15
23			46	12
24			14	4
25			28	10
26			32	3
Average DPM	11	9	27	7
Standard Deviation, DPM	10	6	11	5
Maximum DPM	33	28	47	25
Action Limit, DPM			700	700

Figure 12-5-20: Grid Map for Rockville Annex, Radioactive Waste Locker (RWL)
Survey date: 3/28/00 (POST DECONTAMINATION; 100% SAMPLING)
Survey results: background < 33 DPM; H-3 and C-14 < 47 DPM
C1-C26 = select sample locations

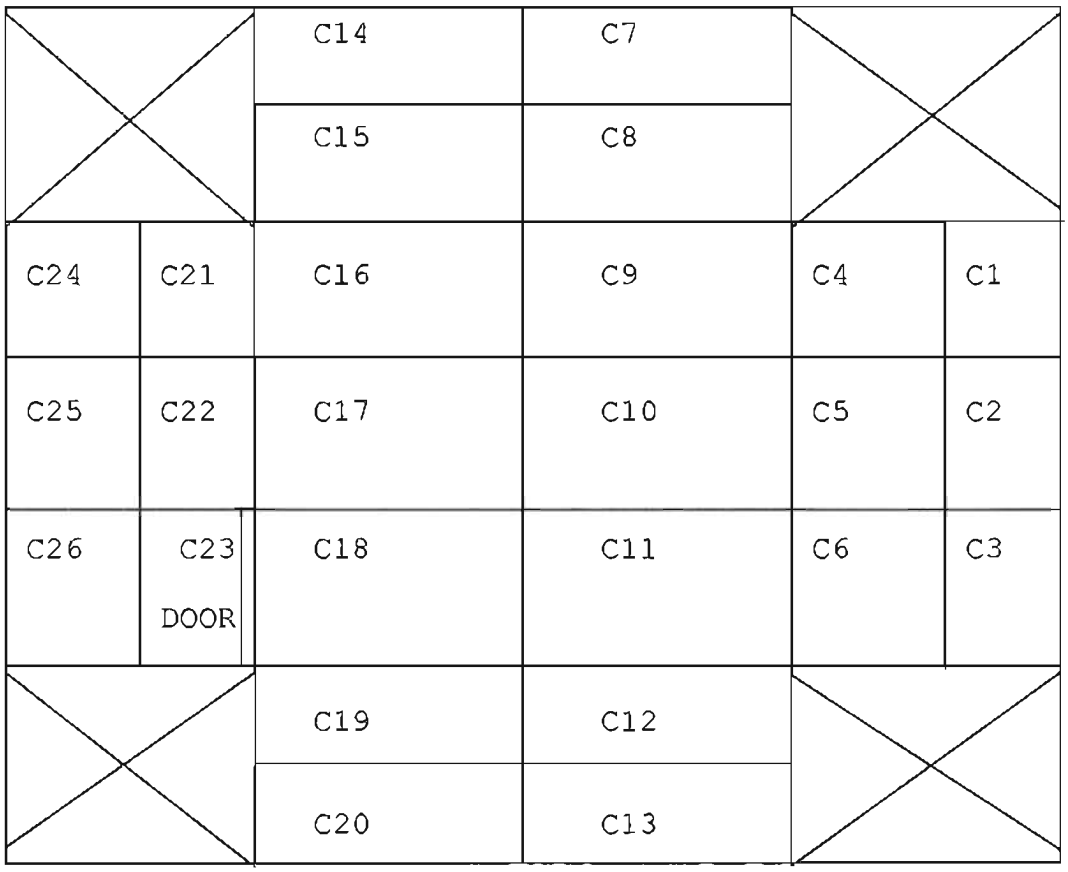

Table 12-5-44. Annex Storage Closet (behind RWL) - Final Status Survey Summary for 100% Coverage				
Building: NMRC Rockville Annex				
Survey Unit or Room Number: Storage Closet (near room 118)				
Survey Date: 3/28/00			Count Times: 1 minute	
Liquid Scintillation Swipe Results for Background, H-3 and C-14 Analyses for Residual Contamination				
Sample Number	DPM, Background		DPM, H-3	DPM, C-14
	H-3	C-14		
1	0	5	1	18
2	5	10	0	8
3	19	4	14	12
4	0	13	32	8
5	13	5	5	10
6	0	6	0	5
7	33	14	2	12
8	15	0	4	7
9	24	7	3	10
10	8	8	22	4
11	22	12	13	9
12	0	16	22	1
13	4	10	6	17
14	0	8	13	11
15	16	6	31	3
16	29	5	16	4
17	0	10	20	1
18	15	7	18	9
19	0	28	17	11
20	9	5	0	18
21	14	5	14	14
Average DPM	11	9	12	9
Standard Deviation, DPM	10	6	10	5
Maximum DPM	33	28	32	18
Action Limit, DPM			700	700
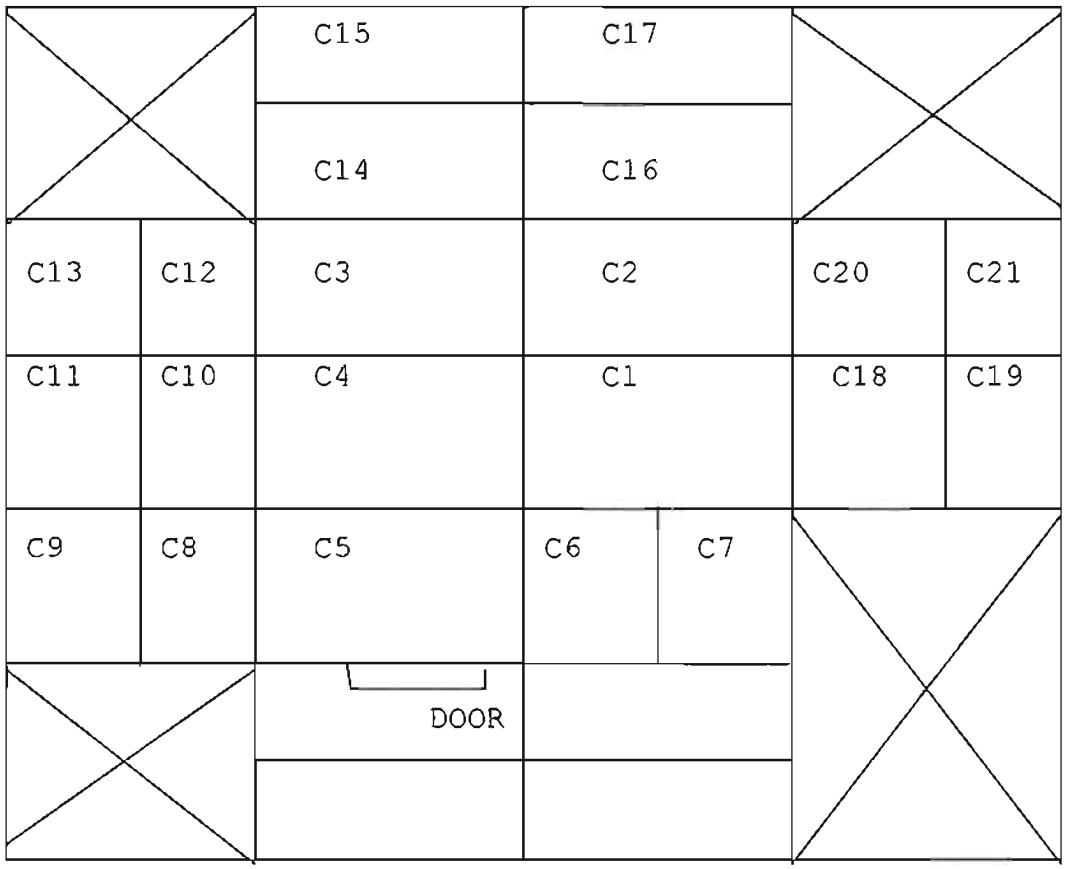
Figure 12-5-21: Grid Map for Rockville Annex, Hall Closet (near room 118)
Survey date: 3/28/00
Survey results: background < 33 DPM; H-3 and C-14 < 32 DPM
R1-R21 = random statistical sample locations
