PMBelCOL PEmails

From: Stephanie Coffin
Sent: Friday, May 08, 2009 8:28 AM
To: Jeffrey Cruz; Thomas Kevern
Cc: BelCol Resource; VogtleCOL Resource; HarrisCOL Resource; LevyCOL Resource; SummerCOL Resource
Subject: FW: ACRS slides
Attachments: 20090507 NRC ACRS Presentation Final.pdf

FYI

Tom - Glad you were there yesterday afternoon. Steph

From: Richard Grumbir [mailto:richard.grumbir@excelservices.com]
Sent: Wednesday, May 06, 2009 9:37 AM
To: Stephanie Coffin
Cc: 'Hastings, Peter S'; 'Eddie R Grant'
Subject: ACRS slides

Stephanie, attached are the ACRS slides for tomorrow. We are having 35 copies made and Eddie will be delivering them to you around noon.

Richard Grumbir

AP1000 COL Project Manager
NuStart Energy Development
richard.grumbir@excelservices.com
rgrumbir@gmail.com (alternate)
256-308-1770 home office
256-309-8974 cell/BB
256-308-1771 fax

Hearing Identifier: Bellefonte_COL_Public_EX
Email Number: 1530

Mail Envelope Properties (3AF7DEF82ADA8944AD8247B7ED7FD651968D3882F7)

Subject: FW: ACRS slides
Sent Date: 5/8/2009 8:28:06 AM
Received Date: 5/8/2009 8:28:10 AM
From: Stephanie Coffin

Created By: Stephanie.Coffin@nrc.gov

Recipients:
"BelCol Resource" <BelCol.Resource@nrc.gov>
Tracking Status: None
"VogtleCOL Resource" <VogtleCOL.Resource@nrc.gov>
Tracking Status: None
"HarrisCOL Resource" <HarrisCOL.Resource@nrc.gov>
Tracking Status: None
"LevyCOL Resource" <LevyCOL.Resource@nrc.gov>
Tracking Status: None
"SummerCOL Resource" <SummerCOL.Resource@nrc.gov>
Tracking Status: None
"Jeffrey Cruz" <Jeffrey.Cruz@nrc.gov>
Tracking Status: None
"Thomas Kevern" <Thomas.Kevern@nrc.gov>
Tracking Status: None

Post Office: HQCLSTR01.nrc.gov

Files	**Size**	**Date & Time**
MESSAGE	748	5/8/2009 8:28:10 AM
20090507 NRC ACRS Presentation Final.pdf	849449	

Options
Priority: Standard
Return Notification: No
Reply Requested: No
Sensitivity: Normal
Expiration Date:
Recipients Received:

NuStart Energy sm

AP1000 DCD/R-COLA Integration, Development, and Standardization

AP1000 Design-Centered Work Group Presentation to ACRS May 7, 2009

Peter Hastings, NuStart — ***AP1000 DCWG Lead***
Rob Sisk, Westinghouse — ***Manager, AP1000 Licensing & Customer Interface***
Eddie Grant, NuStart — ***AP1000 R-COLA Licensing***

NuStart Energy Development, LLC - All Rights Reserved

NuStart Energy℠

AP1000 DCWG

Duke Energy®

SCE&G® A SCANA COMPANY

SOUTHERN COMPANY

AP1000 Westinghouse

Progress Energy

FPL.

TVA

Bellefonte 3&4 | Lee Nuclear 1&2 | Summer 2&3 | Vogtle 3&4 | Harris 2&3 | Levy 1&2 | Turkey Point 6&7

AP1000 Design Center

- **High level of standardization**
- **Design with significant finality**
- **Integration of DCD and COL applications through incorporation by reference**
- **Explicit identification of standard and site-specific information**
- **Status**
  - Design Certification amendment request under review
  - Six COL applications under review (each for two units), additional application expected in June
  - COL applications reference AP1000, as being amended
  - Reference/Subsequent COLA (R-COLA/S-COLA) approach being used for standard content

Use of Standard Content

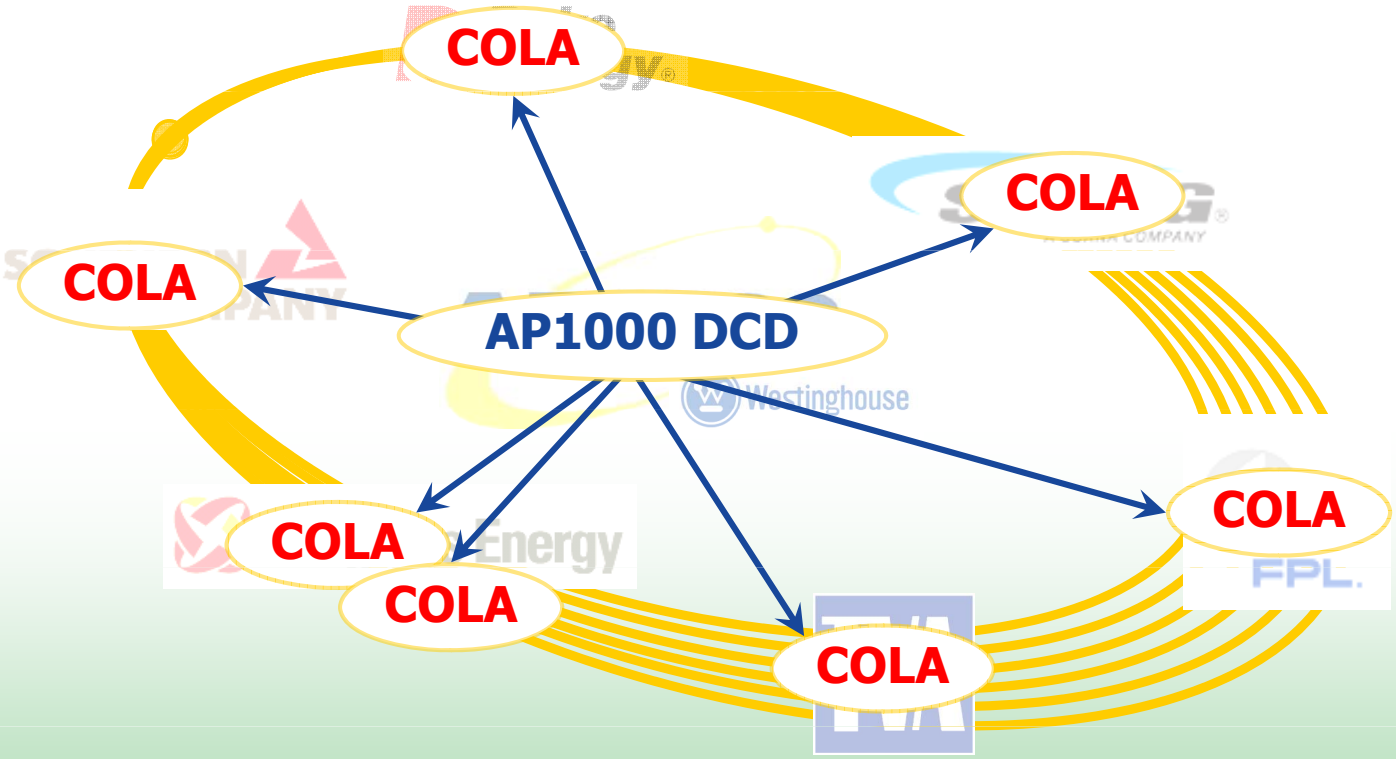

Bellefonte 3&4 Lee Nuclear 1&2 Summer 2&3 Vogtle 3&4 Harris 2&3 Levy 1&2 Turkey Point 6&7

Use of Standard Content (cont'd)

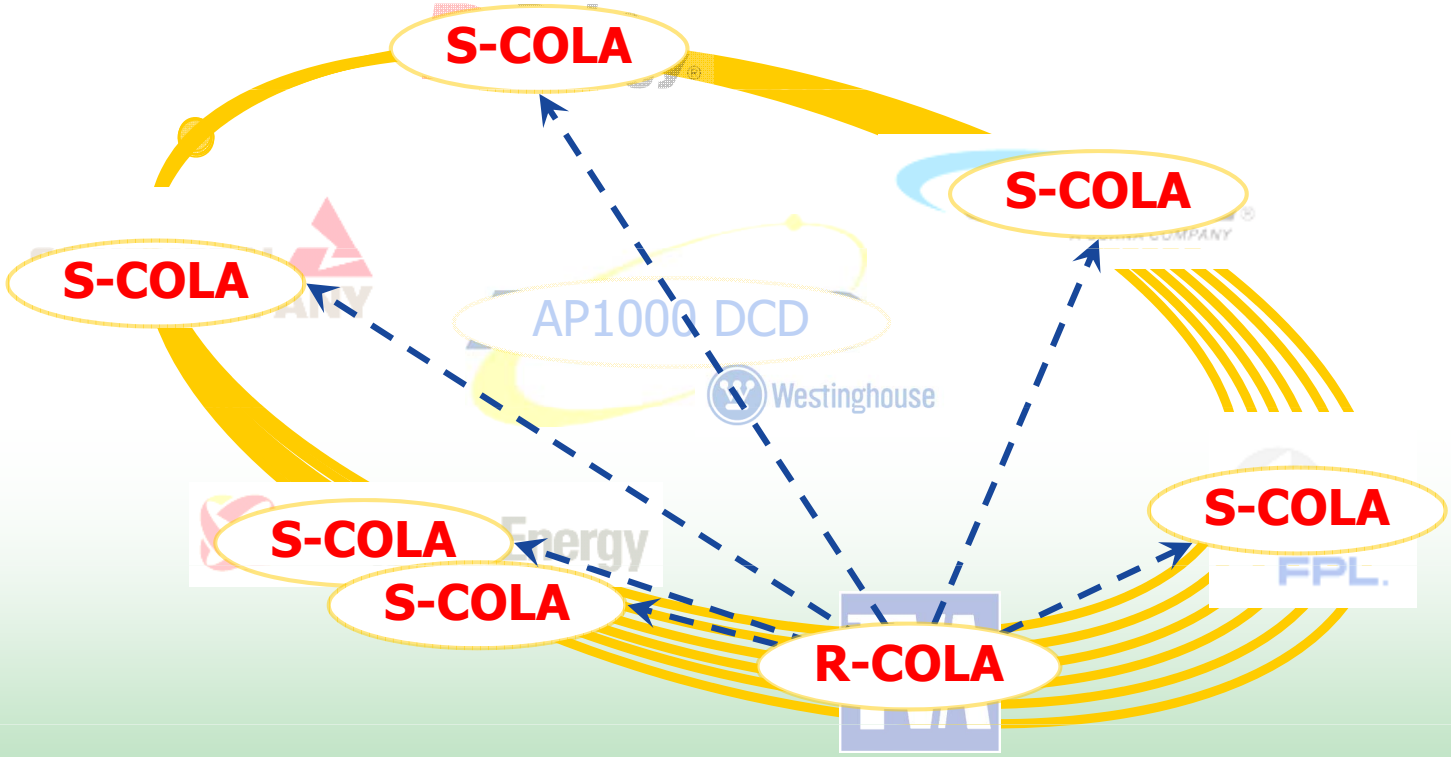

Bellefonte 3&4 | Lee Nuclear 1&2 | Summer 2&3 | Vogtle 3&4 | Harris 2&3 | Levy 1&2 | Turkey Point 6&7

R-COLA Transition

- **Change in dockets to facilitate resource alignment**
- **No change in DCWG structure**
- **SER with Open Items issued on Bellefonte**
- **STD Open Items to be closed on Vogtle**
- **Handling site-specific issues**
  - Bellefonte site-specific issues addressed in Bellefonte SER with Open Items
  - ACRS review and closure on Bellefonte (as with any other S-COLA)
  - Early Site Permit addressed majority of significant site-specific issues for Vogtle
- **Timing of transition closely coordinated with NRC Staff**

Overview of the AP1000 Certified Design Amendment

- AP1000 Design (Rev 15) was certified on January 27, 2006
  - 10CFR52 Appendix D – AP1000 Design (certified)
  - Preceded by 10CFR52 Appendix C – AP600 Design (certified) and 10CFR52 Appendix B – System 80+ Design (certified)

- An Amendment to the certified design was submitted May 26, 2007
  - Augmented in Sept 22, 2008
  - Consistent with 10CFR52.63 requirements

- Purpose of the Amendment:
  - Address COL Information items
  - Address Design Acceptance Criteria
  - Address NRC requirements
  - Enhance Standardization
  - Design Maturity
  - Incorporate Design Improvements

Amendment Overview

- AP1000 amendment builds on the certified design
  - Much of certified design as documented in the DCD remains unchanged
- Key review issues:
  - Address developing security requirements
  - DAC (I&C, HFE, Piping)
  - Containment sump and downstream effects
  - Structural design and seismic analyses
  - Control room ventilation
  - Enhanced Integrated Head Package
  - ASTRUM
  - Addressed non-plant-specific Technical Specification
- Conclusions of the AP1000 safety analysis remain unchanged

First AP1000 Plants Being Constructed in China

Contracts signed for first four units:

- Two units at Sanmen
- Two units at Haiyang

Contracts signed in July 2007

First unit (Sanmen 1):

Groundbreaking in Feb 2008

First concrete in March 2009

Fuel loading in May 2013

Operational in November 2013

Haiyang schedule 6 months behind Sanmen

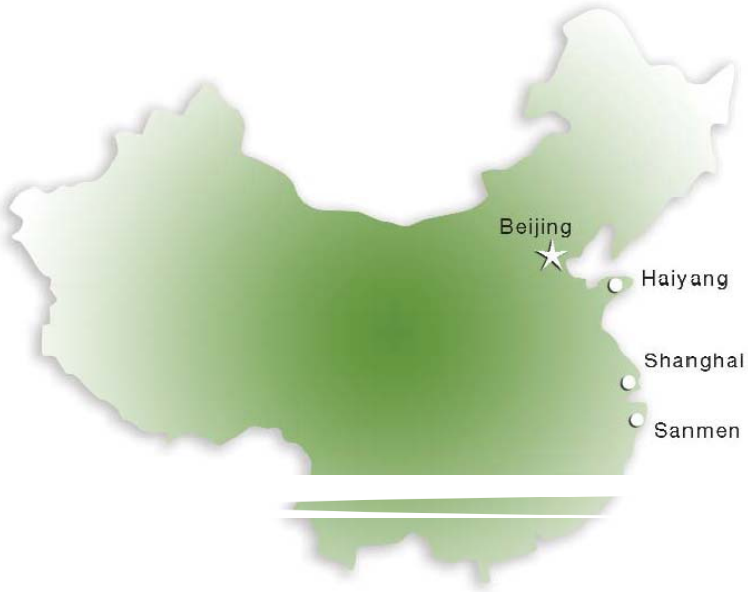

AP1000 Projects in the United States

EPC contracts in place for 6 units:

Operational:

Southern Co.

Vogtle 3, 4 2016, 2017

SCE&G

VC Summer 2, 3 2016, 2019

Progress Energy

Levy County 1, 2 2018-2020*

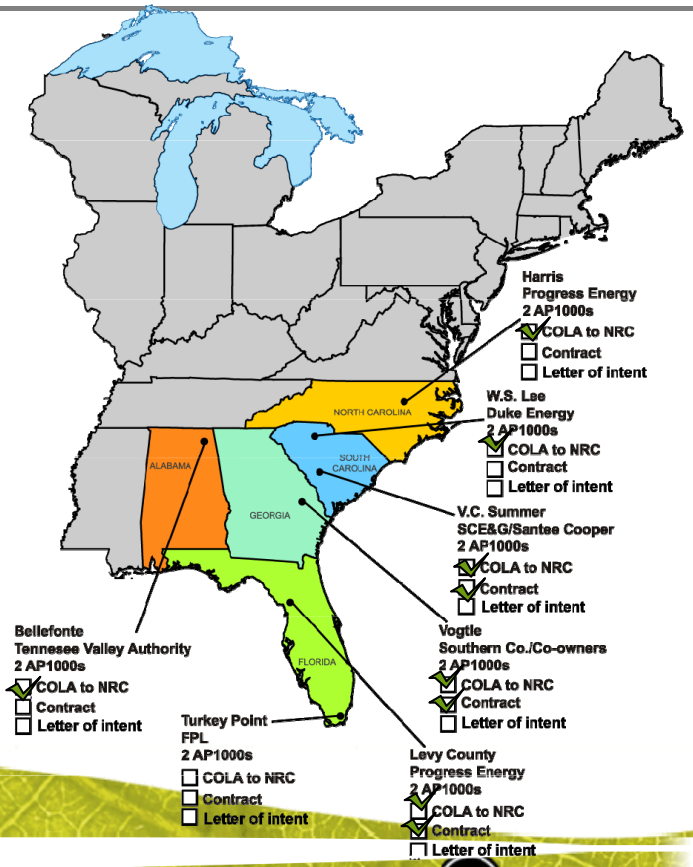

Closing Remarks

- Westinghouse is working to address the NRC's concerns on a schedule to support the ACRS meetings:
  - July 23 &24
  - Oct 6 & 7
  - November 19 & 20
- AP1000 Design was certified on January 27, 2006.
  - Built on the Review and Approval of AP600
  - The amendment process incorporated two revisions (Rev 16 & 17)
  - A conforming revision (Rev 18) is anticipated to support rulemaking
- Focus is on reviewing changes to the certified design
  - Recognizing Design Finality applies (10CFR52.63)
- Westinghouse is ready to present the AP1000 amended design to the ACRS!

Combined License (COL) Application

- Cover Letter, Affidavits, etc. ("Part 0")
- Part 1 – General & Administrative Information
- Part 2 – Final Safety Analysis Report
- Part 3 – Environmental Report
- Part 4 – Plant Specific Technical Specifications
- Part 5 – Emergency Planning Information
- Part 6 – Limited Work Authorization Information
- Part 7 – Departures & Exemption Requests
- Part 8 – Safeguards Information
- Part 9 – Other Withheld Information
- Part 10 – Proposed License Conditions, including ITAAC
- Part 11 – Other Documents (e.g., QAPD)

DCD/R-COLA Integration in Part 2

- **Incorporation by Reference (IBR):** majority of DCD IBR'd into COLA (and not repeated)
- **S-COLAs includes standard content reflected in R-COLA**
- **FSAR content labeled explicitly with Left Margin Annotations (LMAs) as STD or site-specific (BLN):**
  - COL Information Items:
    - STD COL #.#-# or BLN COL #.#-#
  - Departures from DCD:
    - STD DEP #.#-# or BLN DEP #.#-#
  - Supplemental Information:
    - STD SUP #.#-# or BLN SUP #.#-#

Left Margin Annotations (FSAR)

MARGIN NOTATION	DEFINITION AND USE
STD DEP X.Y.Z-#	FSAR information that **departs from the generic DCD** and is common for parallel applicants. Each Standard Departure is numbered separately at an appropriate level.
NPP DEP X.Y.Z-#	FSAR information that **departs from the generic DCD** and is plant specific. NPP is replaced with a plant specific identifier.
STD COL X.Y-#	FSAR information that addresses a DCD **Combined License Information item** and is common to other COL applicants. Each COL item is numbered as identified in DCD Table 1.8-2.
NPP COL X.Y-#	FSAR information that addresses a DCD **Combined License Information item** and is plant specific. NPP is replaced with a plant specific identifier.
STD SUP X.Y-#	FSAR information that **supplements** the material in the DCD and is common to other COL applicants. Each SUP item is numbered separately at an appropriate subsection level.
NPP SUP X.Y-#	FSAR information that **supplements** the material in the DCD and is plant specific. NPP is replaced with a plant specific identifier. Each SUP item is numbered separately at an appropriate subsection level.
NPP CDI or **STD CDI**	FSAR information that addresses **DCD Conceptual Design Information (CDI)**. Replacement design information is generally plant specific; however, some may be common to other applicants. NPP is replaced with a plant specific identifier. STD is used if it is common. CDI information replacements are not numbered.
DCD	FSAR information that **duplicates material in the DCD**. Such information from the DCD is repeated in the FSAR only in instances determined necessary to provide contextual clarity.

DCD/R-COLA Integration (other Parts)

- **Part 4 – Plant Specific Technical Specifications**
  - Generic TS repeated to provide full, clean copy
  - Plant specific information included

- **Part 7 – Departures and Exemptions**
  - Tier 1 and GTS departures require exemptions
  - Tier 2* departures require NRC approval
  - Tier 2 departures require evaluation ~ 50.59
    - Some require NRC approval

DCD/R-COLA Integration (other Parts)

- **Part 10 – Proposed License Conditions**
  - ITAAC (IBR of DCD Tier 1 ITAAC)
    - Adds Security, Plant Specific, Emergency Planning
  - Holder items
    - COL Info Items that can't be completed prior to COL issuance (e.g., as-built or startup testing)
  - Program implementation milestones
  - Program readiness (for inspections)
  - Other items typical for Operating Licenses
    - Security program revision process
    - Startup testing change reporting
    - Environmental Protection Plan (Nonradiological)

FSAR Standardization examples

Sect.	IBR	STD	PS
1.1	IBR	X	X
1.2	IBR		X
1.3	IBR		
1.4	IBR		X
1.5	IBR		
1.6	IBR	X	
1.7	IBR		X
1.8	IBR	X	X
1.9	IBR	X	X
1.10	(New)	X	X
1A	IBR	X	

Chapter	% STD	Chapter	% STD
1	75	11	40
2	0	12	70
3	80	13	30
4	100	14	90
5	100	15	75
6	80	16	75
7	80	17	60
8	75	18	90
9	60	19	100
10	50	FSAR	20/70

R-COLA Standard Material Summary

- **DCD Incorporated by Reference**
  - Part 2 – FSAR
  - Part 10 – Proposed License Conditions
- **Part 4 – Technical Specifications**
- **Many Program Descriptions in FSAR**
  - NEI Templates (examples)
    - RP, Training, ALARA, Maintenance, PCP, ODCM
  - Others such as ISI, IST, CLRT
  - Procedural information
- **Many COL Information Item closures**
- **Much of the Supplemental material**
- **Standard methods used**
  - Examples - PSHA, Cost-benefit analyses
