APPENDIX F.3

SOIL MOISTURE-DENSITY AND CALIFORNIA BEARING RATIO TESTS

NORTH ANNA COL

DATA REPORT REV. 0
JANUARY 23, 2007

MACTEC PROJECT NO. 6468-06-1472

COMPACTION TEST REPORT/ ASTM D-1557-02

Curve No.: TP-1-1

Project No.: 6468061472 **Date:** 12/1/06

Project: NORTH ANNA COL PROJECT

Location: TEST PIT No 1 23f 1/22/07

Elev./Depth: 0-1.5' **Sample No.** TP-1-1

Remarks: ND= NOT DETERMINED

MATERIAL DESCRIPTION

Description: Brown red silty sandy clay(VISUAL)

Classifications - **USCS:** ND **AASHTO:** ND

Nat. Moist. = 23.4 %

Liquid Limit = ND


% > No.4 = 0.9 %

Sp.G. = ND

Plasticity Index = ND

% < No.200 = ND %

TEST RESULTS
Maximum dry density = 108.7 pcf
Optimum moisture = 17.6 %

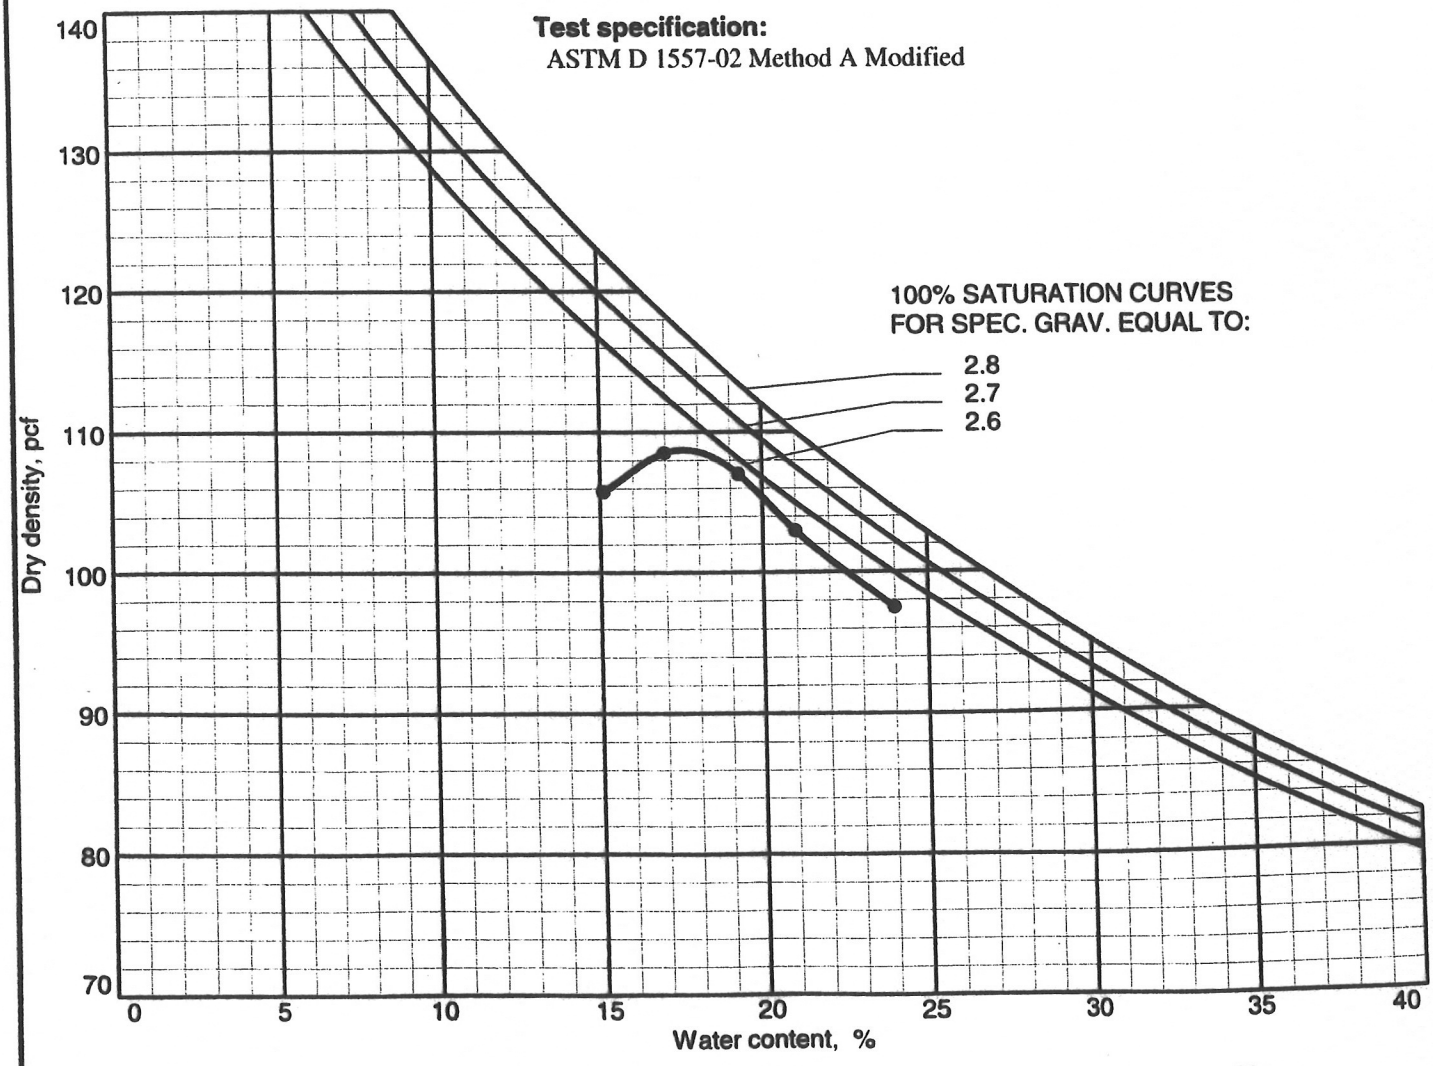

Figure

MOISTURE DENSITY TEST DATA


Client: Dominion Nuclear North Anna
Project: NORTH ANNA COL PROJECT
Project Number: 6468061472

Specimen Data

Source: TEST PIT 1
Sample No.: TP-1-1
Elev. or Depth: 0-1.5' **Sample Length(in./cm.):** 18
Location:
Description: Brown red silty sandy clay(VISUAL)
Liquid Limit: ND **Plasticity Index:** ND **Natural Moisture:** 23.4
Date: 12/1/06 **USCS Classification:** ND **AASHTO Classification:** ND
Testing Remarks: ND= NOT DETERMINED
Percent retained on No.4 sieve: 0.9
Percent passing No. 200 sieve: ND **Specific gravity:** ND

Test Data And Results For Curve TP-1-1

Type of test: ASTM D 1557-02 Method A Modified
Mold Dia.: 4.00 in. **Hammer Wt.:** 10 lb. **Drop:** 18 in.
Layers: five **Blows per Layer:** 25

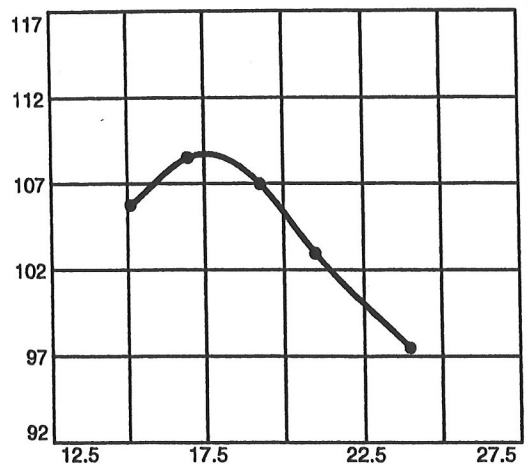

POINT NO.	1	2	3	4	5
WM + WS	3979.1	3989.0	3943.2	3887.1	3900.0
WM	2060.0	2060.0	2060.0	2060.0	2060.0
WW+T	522.90	568.30	572.70	569.40	531.20
WD+T	448.30	478.00	474.90	461.10	463.70
TARE	9.10	9.40	9.20	9.50	16.90
MOIST	17.0	19.3	21.0	24.0	15.1
MOISTURE	17.0	19.3	21.0	24.0	15.1
DRY DEN	108.5	107.0	102.9	97.5	105.7

Max dry den= 108.7 pcf **Opt moisture=** 17.6 %

COMPACTION TEST REPORT/ ASTM D-1557-02

Curve No.: TP-1-2

Project No.: 6468061472 **Date:** 12/1/06

Project: NORTH ANNA COL PROJECT

Location: TEST PIT No 1 RBJ 1/23/07

Elev./Depth: 1.5-4' **Sample No.** TP-1-2

Remarks: ND = NOT DETERMINED

MATERIAL DESCRIPTION

Description: Yellow brown slightly silty sandy clay (VISUAL)

Classifications - **USCS:** ND **AASHTO:** ND

Nat. Moist. = 22.6 %

Liquid Limit = ND


% > No.4 = 100.0 %

Sp.G. = ND

Plasticity Index = ND

% < No.200 = ND %

TEST RESULTS
Maximum dry density = 108.8 pcf
Optimum moisture = 17.1 %

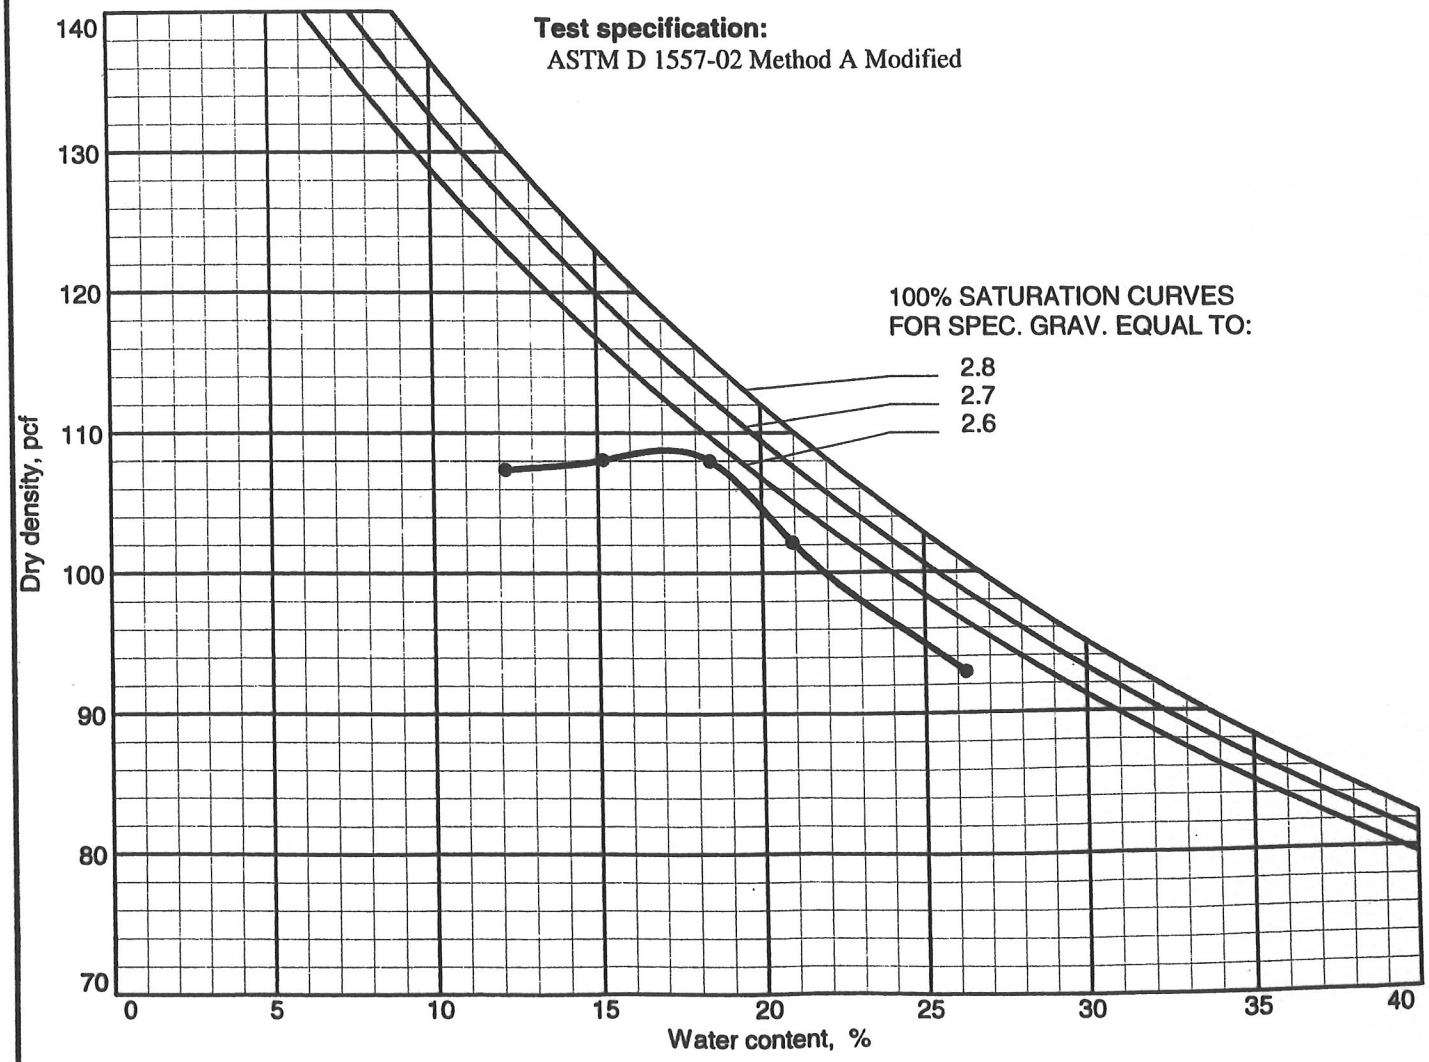

Figure

MOISTURE DENSITY TEST DATA


Client: Dominion Nuclear North Anna
Project: NORTH ANNA COL PROJECT
Project Number: 6468061472

Specimen Data

Source: TEST PIT 1
Sample No.: TP-1-2
Elev. or Depth: 1.5-4' **Sample Length(in./cm.):** 2.5
Location:
Description: Yellow brown slightly silty sandy clay (VISUAL)
Liquid Limit: ND **Plasticity Index:** ND **Natural Moisture:** 22.6
Date: 12/1/06 **USCS Classification:** ND **AASHTO Classification:** ND
Testing Remarks: ND = NOT DETERMINED
Percent retained on No.4 sieve: 100.0
Percent passing No. 200 sieve: ND **Specific gravity:** ND

Test Data And Results For Curve TP-1-2

Type of test: ASTM D 1557-02 Method A Modified
Mold Dia.: 4.00 in. **Hammer Wt.:** 10 lb. **Drop:** 18 in.
Layers: five **Blows per Layer:** 25

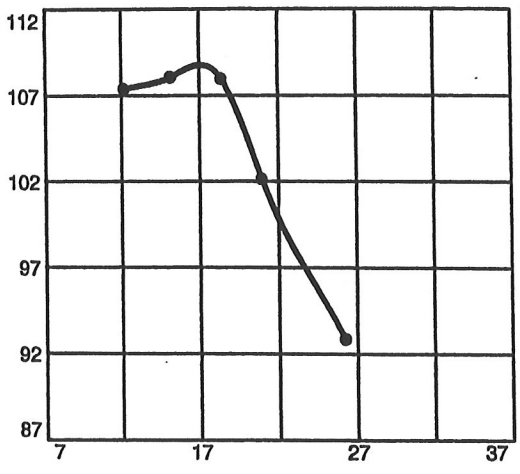



POINT NO.	1	2	3	4	5
WM + WS	3881.2	3993.4	3928.0	3832.7	3941.6
WM	2060.0	2060.0	2060.0	2060.0	2060.0
WW+T	530.70	511.80	529.00	584.50	544.80
WD+T	473.00	433.60	438.80	464.80	473.00
TARE	0.00	9.40	8.20	9.10	0.00
MOIST	12.2	18.4	20.9	26.3	15.2
MOISTURE	12.2	18.4	20.9	26.3	15.2
DRY DEN	107.4	108.0	102.2	92.9	108.1


Max dry den= 108.8 pcf **Opt moisture=** 17.1 %

BEARING RATIO TEST REPORT

ASTM D 1883-~~99~~05 LBS 1/23/07

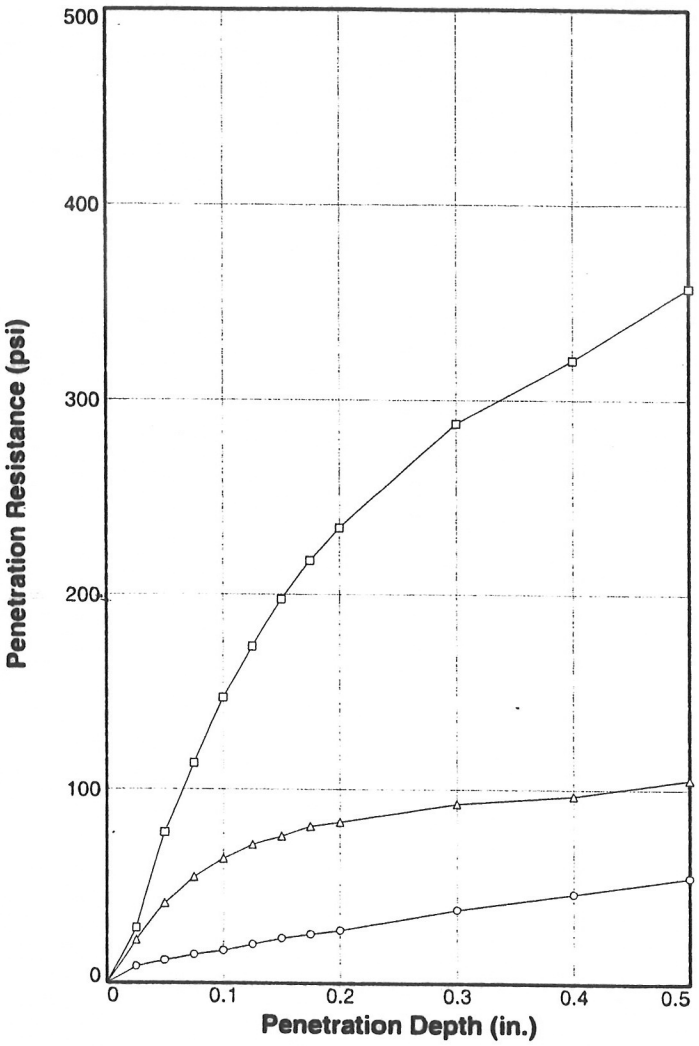

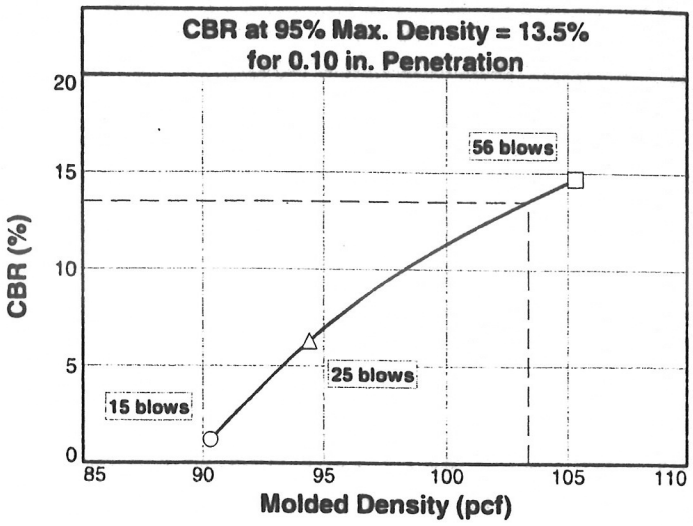

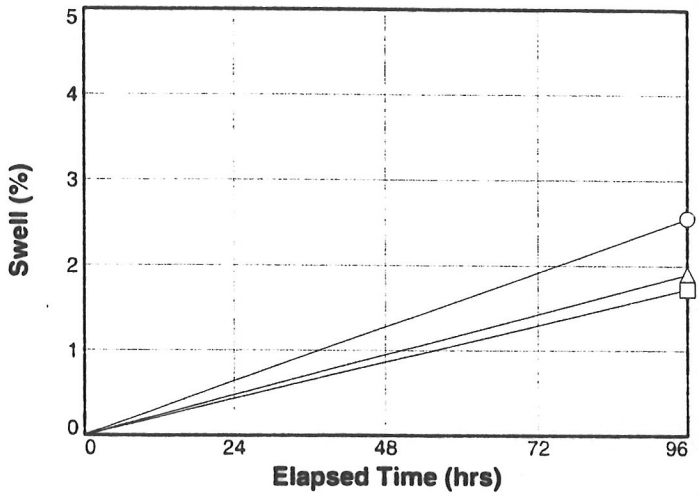

	Molded			Soaked			CBR (%)		Linearity Correction (in.)	Surcharge (lbs.)	Max. Swell (%)
	Density (pcf)	Percent of Max. Dens.	Moisture (%)	Density (pcf)	Percent of Max. Dens.	Moisture (%)	0.10 in.	0.20 in.			
1 ○	90.3	83	17.0	88.1	81	25.2	1.2	1.6	-0.048	10.01	2.6
2 △	94.4	86.8	17.0	92.6	85.2	22.8	6.3	5.5	-0.003	10.03	1.9
3 □	105.3	96.8	17.2	103.5	95.2	19.4	14.7	15.6	0.000	10.01	1.7

Material Description	USCS	Max. Dens. (pcf)	Optimum Moisture (%)	LL	PI
Yellow brown slightly silty sandy clay (VISUAL)	ND	108.8	17.1	ND	ND

Project No: 6468061472

Project: NORTH ANNA COL PROJECT

Source of Sample: TEST PIT 1 **Depth:** 1.5-4'

Sample Number: TP-1-2

Date:

Test Description/Remarks:

Tested in accordance with ASTM D-1883, section 7.1.2

BEARING RATIO TEST REPORT

MACTEC, Inc.

Figure _____

BEARING RATIO TESTING RESULTS
(ASTM D 1883-99(05) 1/23/07 LBJ

Date:
Project No.: 6468061472
Project: NORTH ANNA COL PROJECT
Location: TEST PIT 1
Depth: 1.5-4' **Sample Number:** TP-1-2
Material Description: Yellow brown slightly silty sandy clay (VISUAL)
USCS Classification: ND
Liquid Limit: ND **Plasticity Index:** ND

Test Description: Tested in accordance with ASTM D-1883, section 7.1.2
Maximum Dry Density: 108.8 **Optimum Moisture Content:** 17.1
Testing Remarks:

Sample 1 (15 Blows; Surcharge: 10.01 lbs.)

Water Content

Wt. Wet Soil+Tare, gms. 518.2 | Wt. Soil+Tare, gms. 442.8 | Wt. Tare, gms. 0 | Moisture, % 17.0

Unit Weight

Wt. Mold+Soil, gms. 7782 | Wt. Mold, gms. 4188 | Ht. Soil, in. 4.581 | Density, pcf 90.3

Swell Data


Elapsed Time, hrs.	Dial Reading in. x 1,000	Swell %
0	154	0.0
96	271	2.6

Final Water Content

	Wt. Wet Soil+Tare, gms.	Dry Soil+Tare	Tare	Moisture, %
Top	513.8	406.7	9.0	26.9
Middle	568.5	460.6	17.0	24.3
Bottom	568.5	460.6	17.0	24.3

Penetration Test Data

Pen. in.	Dial Reading in. x 1,000	Stress psi	CBR %
0.0	0	0.0	
0.025	8	8.4	
0.05	11	11.6	
0.075	14	14.7	
0.1	16	16.8	1.2
0.125	19	20.0	
0.15	22	23.1	
0.175	24	25.2	
0.2	26	27.3	1.6
0.3	36	37.8	1.7
0.4	44	46.2	1.8
0.5	52	54.6	1.9

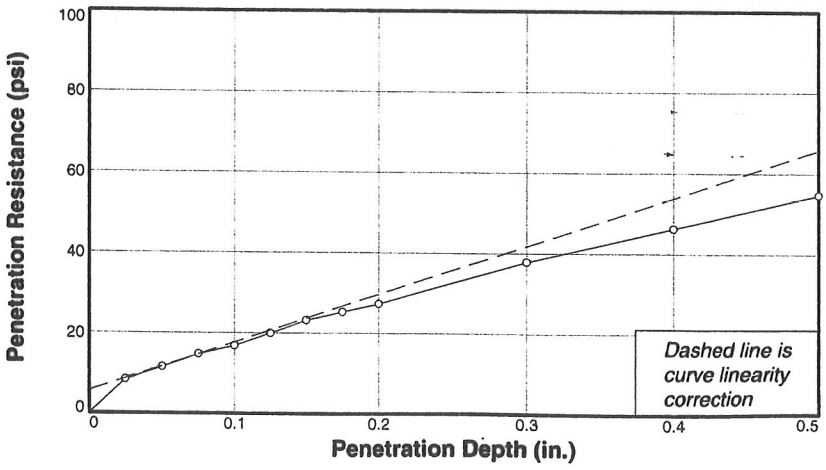

Sample 2 (25 Blows; Surcharge: 10.03 lbs.)

Water Content

Wt. Wet Soil+Tare, gms. 371.1 | Wt. Soil+Tare, gms. 317.2 | Wt. Tare, gms. 0 | Moisture, % 17.0

Unit Weight

Wt. Mold+Soil, gms. 7974 | Wt. Mold, gms. 4218 | Ht. Soil, in. 4.582 | Density, pcf 94.4

Swell Data


Elapsed Time, hrs.	Dial Reading in. x 1,000	Swell %
0	90	0.0
96	177	1.9

Final Water Content

	Wt. Wet Soil+Tare, gms.	Dry Soil+Tare	Tare	Moisture, %
Top	551.4	447.4	17.1	24.2
Middle	559.9	461.2	17.1	22.2
Bottom	559.2	461.2	17.1	22.1

Penetration Test Data

Pen. in.	Dial Reading in. x 1,000	Stress psi	CBR %
0.0	0	0.0	
0.025	21	22.1	
0.05	39	41.0	
0.075	52	54.6	
0.1	61	64.1	6.3
0.125	68	71.4	
0.15	72	75.6	
0.175	77	80.9	
0.2	79	83.0	5.5
0.3	88	92.4	4.9
0.4	92	96.6	4.2
0.5	100	105.0	4.0

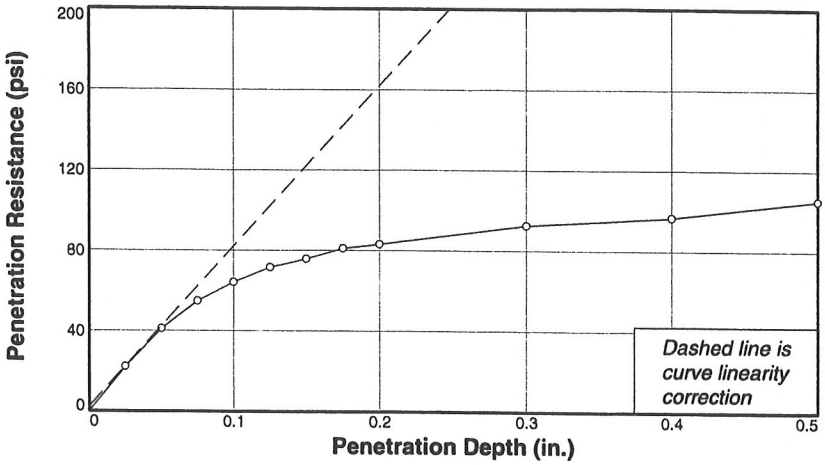

Sample 3 (56 Blows; Surcharge: 10.01 lbs.)

Water Content

Wt. Wet Soil+Tare, gms. 414.3 | Wt. Soil+Tare, gms. 353.5 | Wt. Tare, gms. 0 | Moisture, % 17.2

Unit Weight

Wt. Mold+Soil, gms. 8382 | Wt. Mold, gms. 4188 | Ht. Soil, in. 4.578 | Density, pcf 105.3

Swell Data


Elapsed Time, hrs.	Dial Reading in. x 1,000	Swell %
0	473	0.0
96	552	1.7

Final Water Content

	Wt. Wet Soil+Tare, gms.	Dry Soil+Tare	Tare	Moisture, %
Top	533.9	443.6	17	21.2
Middle	542.6	459.8	13.9	18.6
Bottom	542.6	459.8	13.9	18.6

Penetration Test Data

Pen. in.	Dial Reading in. x 1,000	Stress psi	CBR %
0.0	0	0.0	
0.025	27	28.4	
0.05	74	77.7	
0.075	108	113.5	
0.1	140	147.1	14.7
0.125	165	173.3	
0.15	188	197.5	
0.175	207	217.4	
0.2	223	234.3	15.6
0.3	274	287.8	15.1
0.4	305	320.4	13.9
0.5	340	357.2	13.7

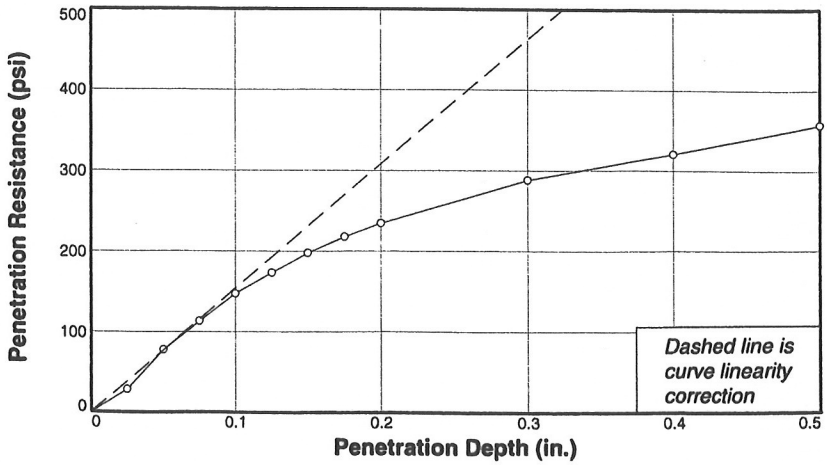

COMPACTION TEST REPORT/ ASTM D-1557-02

Curve No.: TP-2

Project No.: 6468061472 **Date:** 12/2/06

Project: NORTH ANNA COL PROJECT

Location: TEST PIT NO 2 LBS 1/22/07

Elev./Depth: 0-3.8 **Sample No.** TP-2

Remarks: ND= NOT DETERMINED

MATERIAL DESCRIPTION

Description: Brown slightly silty sandy clay

Classifications - **USCS:** ND **AASHTO:** ND

Nat. Moist. = 22.6 %

Liquid Limit = ND

% > No.4 = 0.0 %


Sp.G. = ND

Plasticity Index = ND

% < No.200 = ND %

TEST RESULTS
Maximum dry density = 100.4 pcf
Optimum moisture = 22.3 %

Test specification:
ASTM D 1557-02 Method A Modified

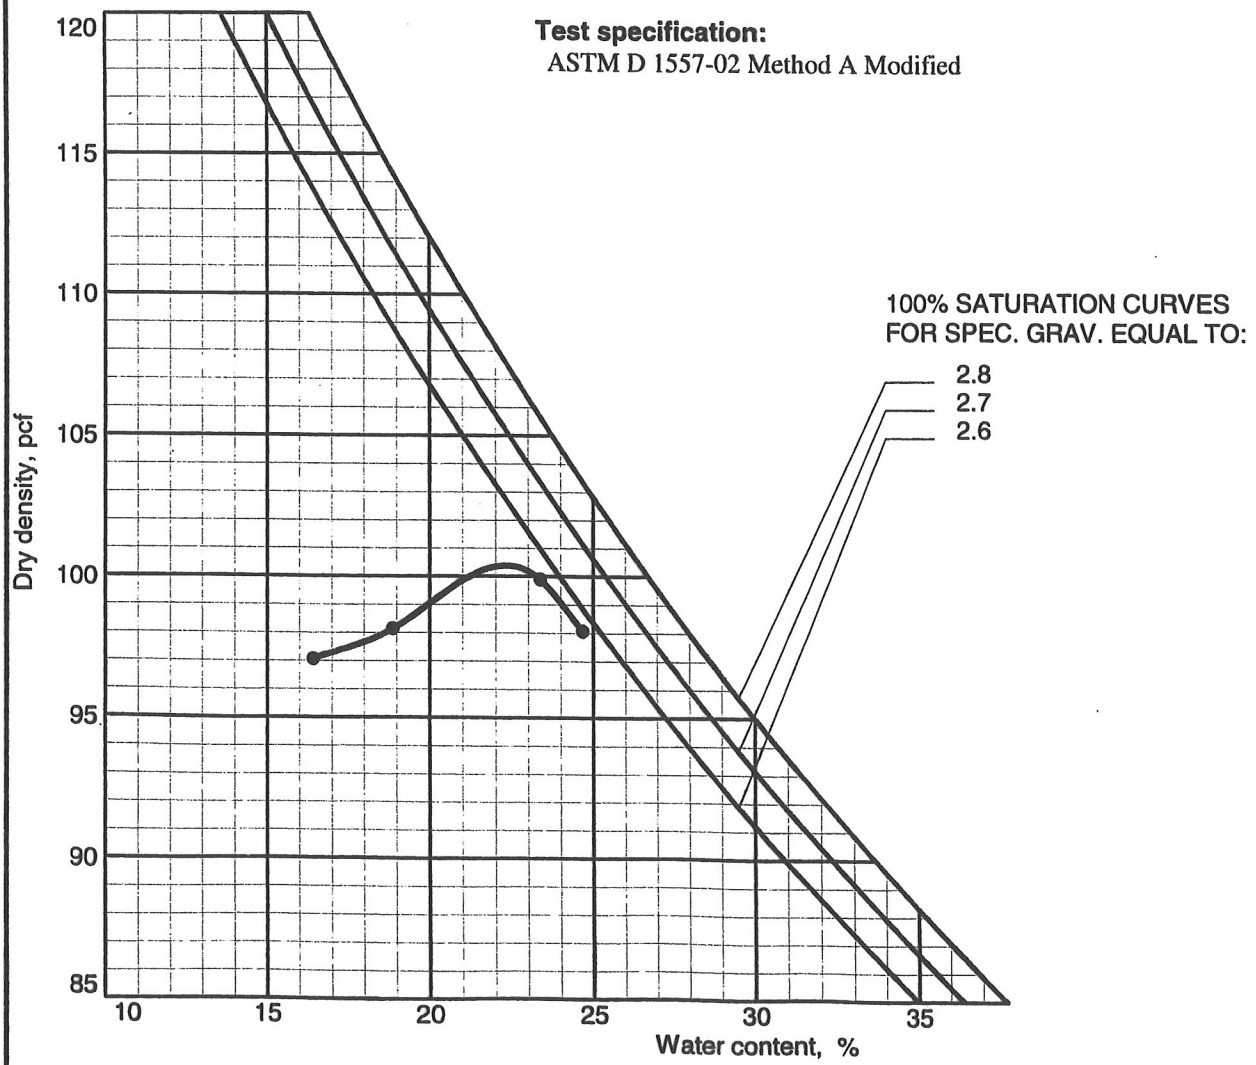

Figure

MACTEC, Inc.

MOISTURE DENSITY TEST DATA


Client: Dominion Nuclear North Anna
Project: NORTH ANNA COL PROJECT
Project Number: 6468061472

Specimen Data

Source: TEST PIT 2
Sample No.: TP-2
Elev. or Depth: 0-3.8 **Sample Length(in./cm.):** 3.8
Location:
Description: Brown slightly silty sandy clay
Liquid Limit: ND **Plasticity Index:** ND **Natural Moisture:** 22.6
Date: 12/2/06 **USCS Classification:** ND **AASHTO Classification:** ND
Testing Remarks: ND= NOT DETERMINED
Percent retained on No.4 sieve: 0.0
Percent passing No. 200 sieve: ND **Specific gravity:** ND

Test Data And Results For Curve TP-2

Type of test: ASTM D 1557-02 Method A Modified
Mold Dia.: 4.00 in. **Hammer Wt.:** 10 lb. **Drop:** 18 in.
Layers: five **Blows per Layer:** 25

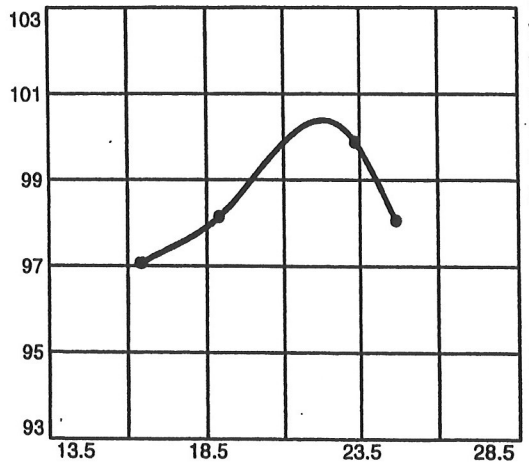



POINT NO.	1	2	3	4
WM + WS	3768.3	3824.0	3922.8	3908.3
WM	2060.0	2060.0	2060.0	2060.0
WW+T	558.50	529.70	565.20	544.80
WD+T	481.70	447.00	459.90	438.80
TARE	13.90	9.20	9.10	9.20
MOIST	16.4	18.9	23.4	24.7
MOISTURE	16.4	18.9	23.4	24.7
DRY DEN	97.1	98.1	99.9	98.1


Max dry den= 100.4 pcf **Opt moisture=** 22.3 %

BEARING RATIO TEST REPORT

ASTM D 1883-99 05 usy 1/23/07

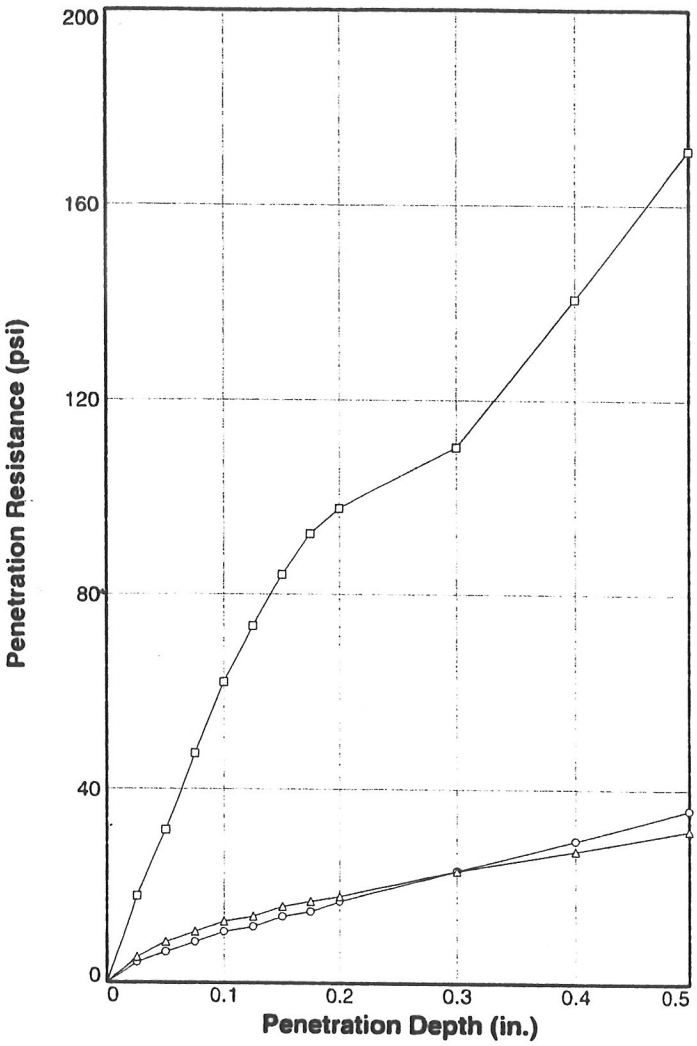

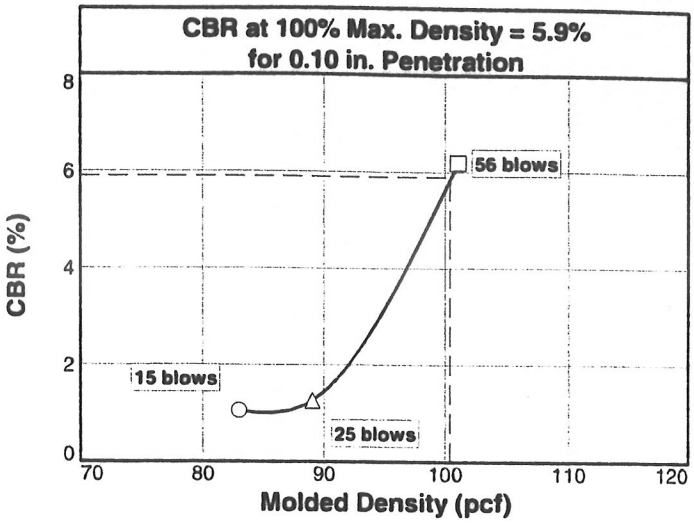

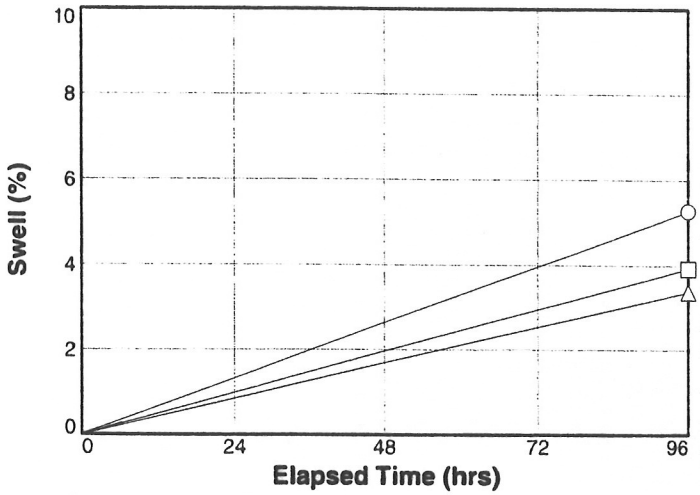

	Molded			Soaked			CBR (%)		Linearity Correction (in.)	Surcharge (lbs.)	Max. Swell (%)
	Density (pcf)	Percent of Max. Dens.	Moisture (%)	Density (pcf)	Percent of Max. Dens.	Moisture (%)	0.10 in.	0.20 in.			
1 ○	83.0	82.7	22.8	78.8	78.5	36.8	1.1	1.1	0.000	10.0	5.3
2 △	89.1	88.7	22.0	86.2	85.8	37.1	1.3	1.2	0.000	10.0	3.4
3 □	101.0	100.6	22.0	97.2	96.8	30.0	6.2	6.5	0.000	10.0	3.9

Material Description	USCS	Max. Dens. (pcf)	Optimum Moisture (%)	LL	PI
Brown slightly silty sandy clay	ND	100.4	22.3	ND	ND

Project No: 6468061472

Project: NORTH ANNA COL PROJECT

Source of Sample: TEST PIT 2 **Depth:** 0-3.8

Sample Number: TP-2

Date: 11/15/06

Test Description/Remarks:

Tested in accordance with ASTM D-1883-05, Section 7.1.2
ND = NOT DETERMINED.

BEARING RATIO TEST REPORT

MACTEC, Inc.

Figure _____

BEARING RATIO TESTING RESULTS
(ASTM D 1883-99) 05 2133 1/23/07

Date:	11/15/06		
Project No.:	6468061472		
Project:	NORTH ANNA COL PROJECT		
Location:	TEST PIT 2		
Depth:	0-3.8	**Sample Number:**	TP-2
Material Description:	Brown slightly silty sandy clay		
USCS Classification:	ND		
Liquid Limit:	ND	**Plasticity Index:**	ND

Test Description:

Maximum Dry Density:	100.4	**Optimum Moisture Content:**	22.3
Testing Remarks:	Tested in accordance with ASTM D-1883-05, Section 7.1.2 ND = NOT DETERMINED.		

Sample 1 (15 Blows; Surcharge: 10.0 lbs.)

Water Content

Wt. Wet Soil+Tare, gms.	Wt. Soil+Tare, gms.	Wt. Tare, gms.	Moisture, %
794.4	653.05	33.9	22.8

Unit Weight

Wt. Mold+Soil, gms.	Wt. Mold, gms.	Ht. Soil, in.	Density, pcf
7664	4196	4.585	83.0

Swell Data


Elapsed Time, hrs.	Dial Reading in. x 1,000	Swell %
0	130	0.0
96	372	5.3

Final Water Content

	Wt. Wet Soil+Tare, gms.	Dry Soil+Tare	Tare	Moisture, %
Top	536.2	389.2	17.2	39.5
Middle	580.6	433.1	16.4	35.4
Bottom	580.6	433.1	16.4	35.4

Penetration Test Data

Pen. in.	Dial Reading in. x 1,000	Stress psi	CBR %
0.0	0	0.0	
0.025	4	4.2	
0.05	6	6.3	
0.075	8	8.4	
0.1	10	10.5	1.1
0.125	11	11.6	
0.15	13	13.7	
0.175	14	14.7	
0.2	16	16.8	1.1
0.3	22	23.1	1.2
0.4	28	29.4	1.3
0.5	34	35.7	1.4

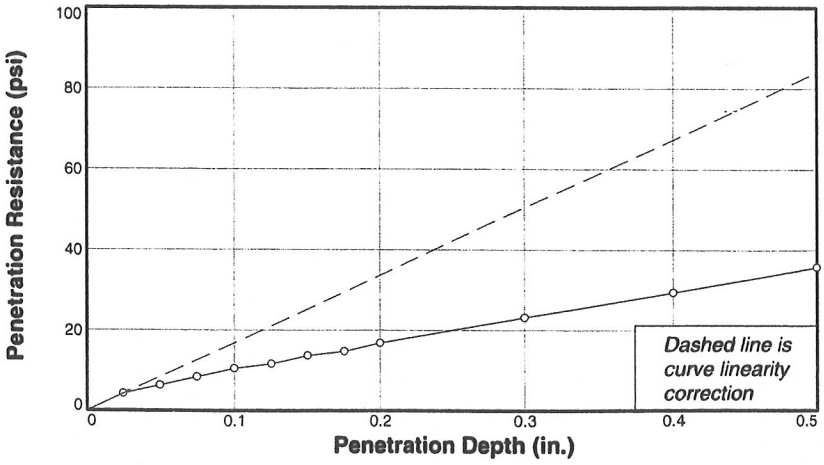

Sample 2 (25 Blows; Surcharge: 10.0 lbs.)

Water Content

Wt. Wet Soil+Tare, gms. 476.1 | Wt. Soil+Tare, gms. 393.2 | Wt. Tare, gms. 17.2 | **Moisture, % 22.0**

Unit Weight

Wt. Mold+Soil, gms. 7862 | Wt. Mold, gms. 4156 | Ht. Soil, in. 4.594 | **Density, pcf 89.1**

Swell Data


Elapsed Time, hrs.	Dial Reading in. x 1,000	Swell %
0	95	0.0
96	250	3.4

Final Water Content

	Wt. Wet Soil+Tare, gms.	Dry Soil+Tare	Tare	Moisture, %
Top	522.6	372.1	6.7	41.2
Middle	574.2	429.4	17.1	35.1
Bottom	574.2	429.4	17.1	35.1

Penetration Test Data

Pen. in.	Dial Reading in. x 1,000	Stress psi	CBR %
0.0	0	0.0	
0.025	5	5.3	
0.05	8	8.4	
0.075	10	10.5	
0.1	12	12.6	1.3
0.125	13	13.7	
0.15	15	15.8	
0.175	16	16.8	
0.2	17	17.9	1.2
0.3	22	23.1	1.2
0.4	26	27.3	1.2
0.5	30	31.5	1.2

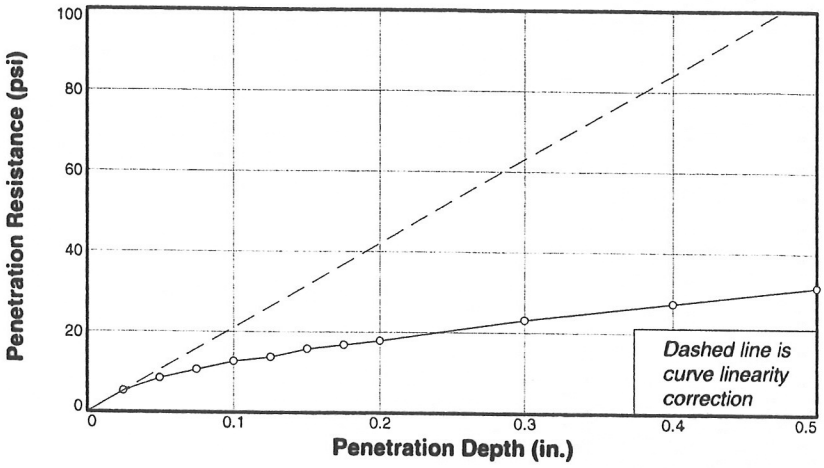

Sample 3 (56 Blows; Surcharge: 10.0 lbs.)

Water Content

Wt. Wet Soil+Tare, gms. 462 | Wt. Soil+Tare, gms. 384.7 | Wt. Tare, gms. 33.7 | **Moisture, % 22.0**

Unit Weight

Wt. Mold+Soil, gms. 8360 | Wt. Mold, gms. 4166 | Ht. Soil, in. 4.583 | **Density, pcf 101.0**

Swell Data

Elapsed Time, hrs.	Dial Reading in. x 1,000	Swell %
0	83	0.0
96	263	3.9

Final Water Content

	Wt. Wet Soil+Tare, gms.	Dry Soil+Tare	Tare	Moisture, %
Top	542.4	411.8	9.3	32.4
Middle	545.9	427.9	16.9	28.7
Bottom	545.9	427.9	16.9	28.7

Penetration Test Data

Pen. in.	Dial Reading in. x 1,000	Stress psi	CBR %
0.0	0	0.0	
0.025	17	17.9	
0.05	30	31.5	
0.075	45	47.3	
0.1	59	62.0	6.2
0.125	70	73.5	
0.15	80	84.0	
0.175	88	92.4	
0.2	93	97.7	6.5
0.3	105	110.3	5.8
0.4	134	140.8	6.1
0.5	163	171.2	6.6

