Figure 8-1
Preliminary Reclamation Schedule

ID	Task Name
1	Excavate and Treat Material Under Cell Footprint
2	Recover and Treat Impacted Groundwater Encountered
3	**Sequoyah Facility Reclamation**
4	NRC Approval of Reclamation Plan
5	Construct Disposal Cell Base and Dike
6	Collect and Treat Stormwater
7	Dismantle Process Equipment
8	Dismantle/Demolish Structures
9	Demolish Concrete Floors, Foundations and Storage Pads
10	Size Reduction/Compaction of Structures, Systems and Components
11	Remove and Treat Sludges and Sediments
12	Remove Clay Liners/Soils Under Impoundments
13	Excavate Contaminated Soils Outside the Cell Footprints
14	Conduct Final Status Survey
15	Complete Capping and Closure of Cell
16	Backfill Excavations to a Finished Grade and Revegetate
17	Monitor Cell Performance
18	Establish Fenced Institutional Control Boundary
19	Transfer Title to DOE
20	Termination of SUB-1010

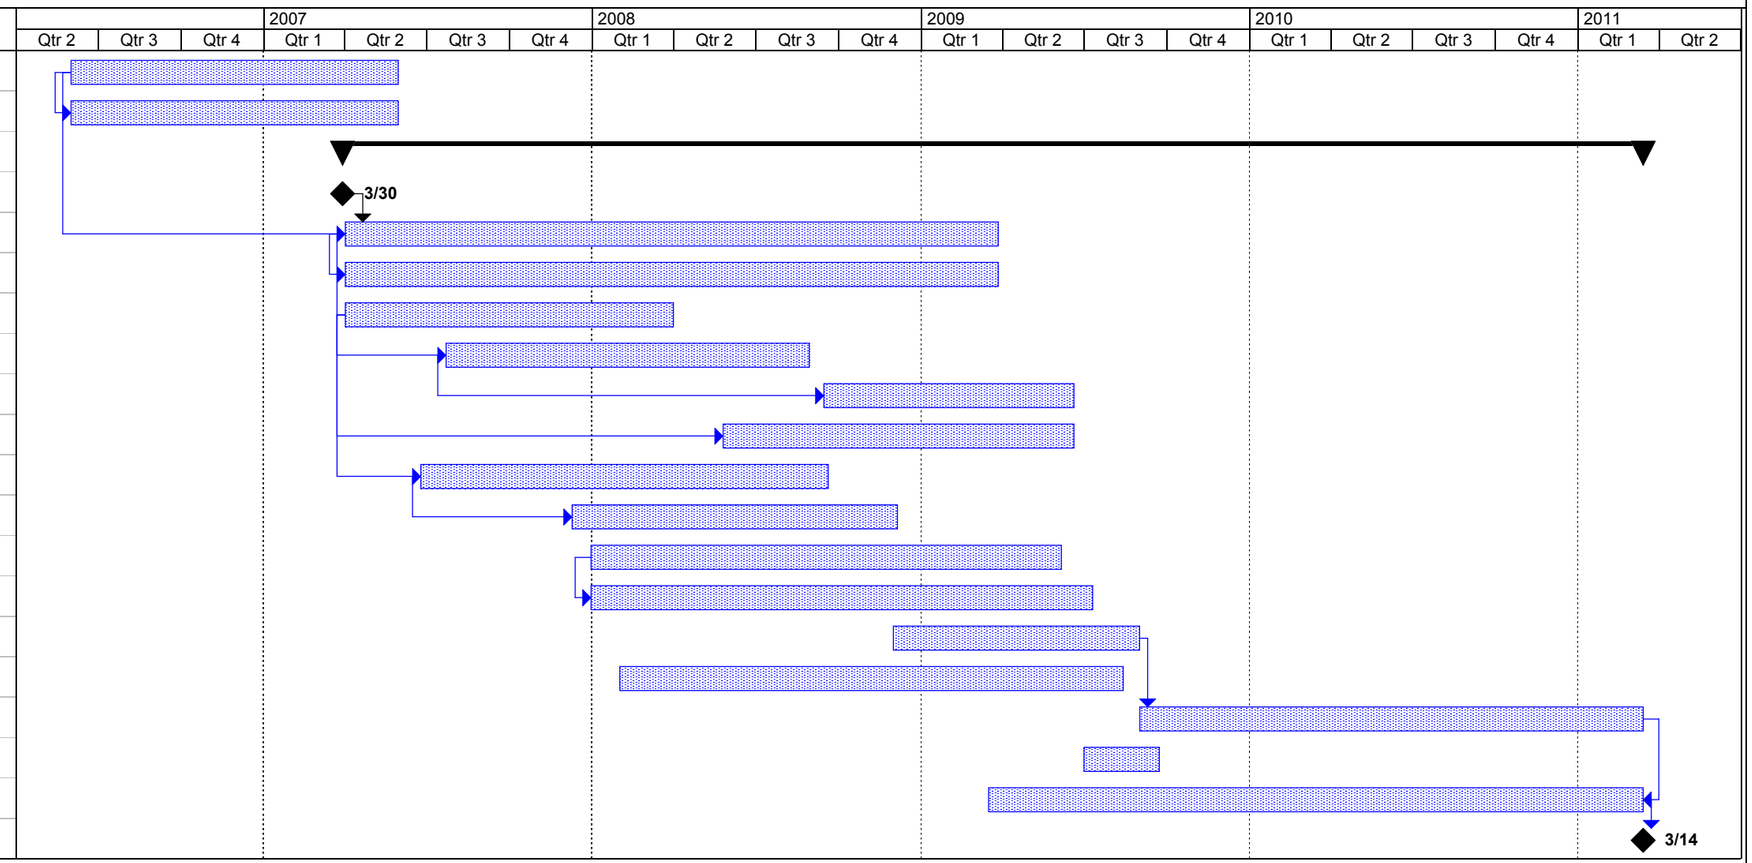

Project: Figure 8-1
Date: Dec 2005

Task | Split | Milestone | Summary
