Blazer

SERVING THE
PLANT VOGTLE COMMUNITY

Bulk Rate
U.S. Postage
PAID
Waynesboro, GA 30830
Permit No. 15

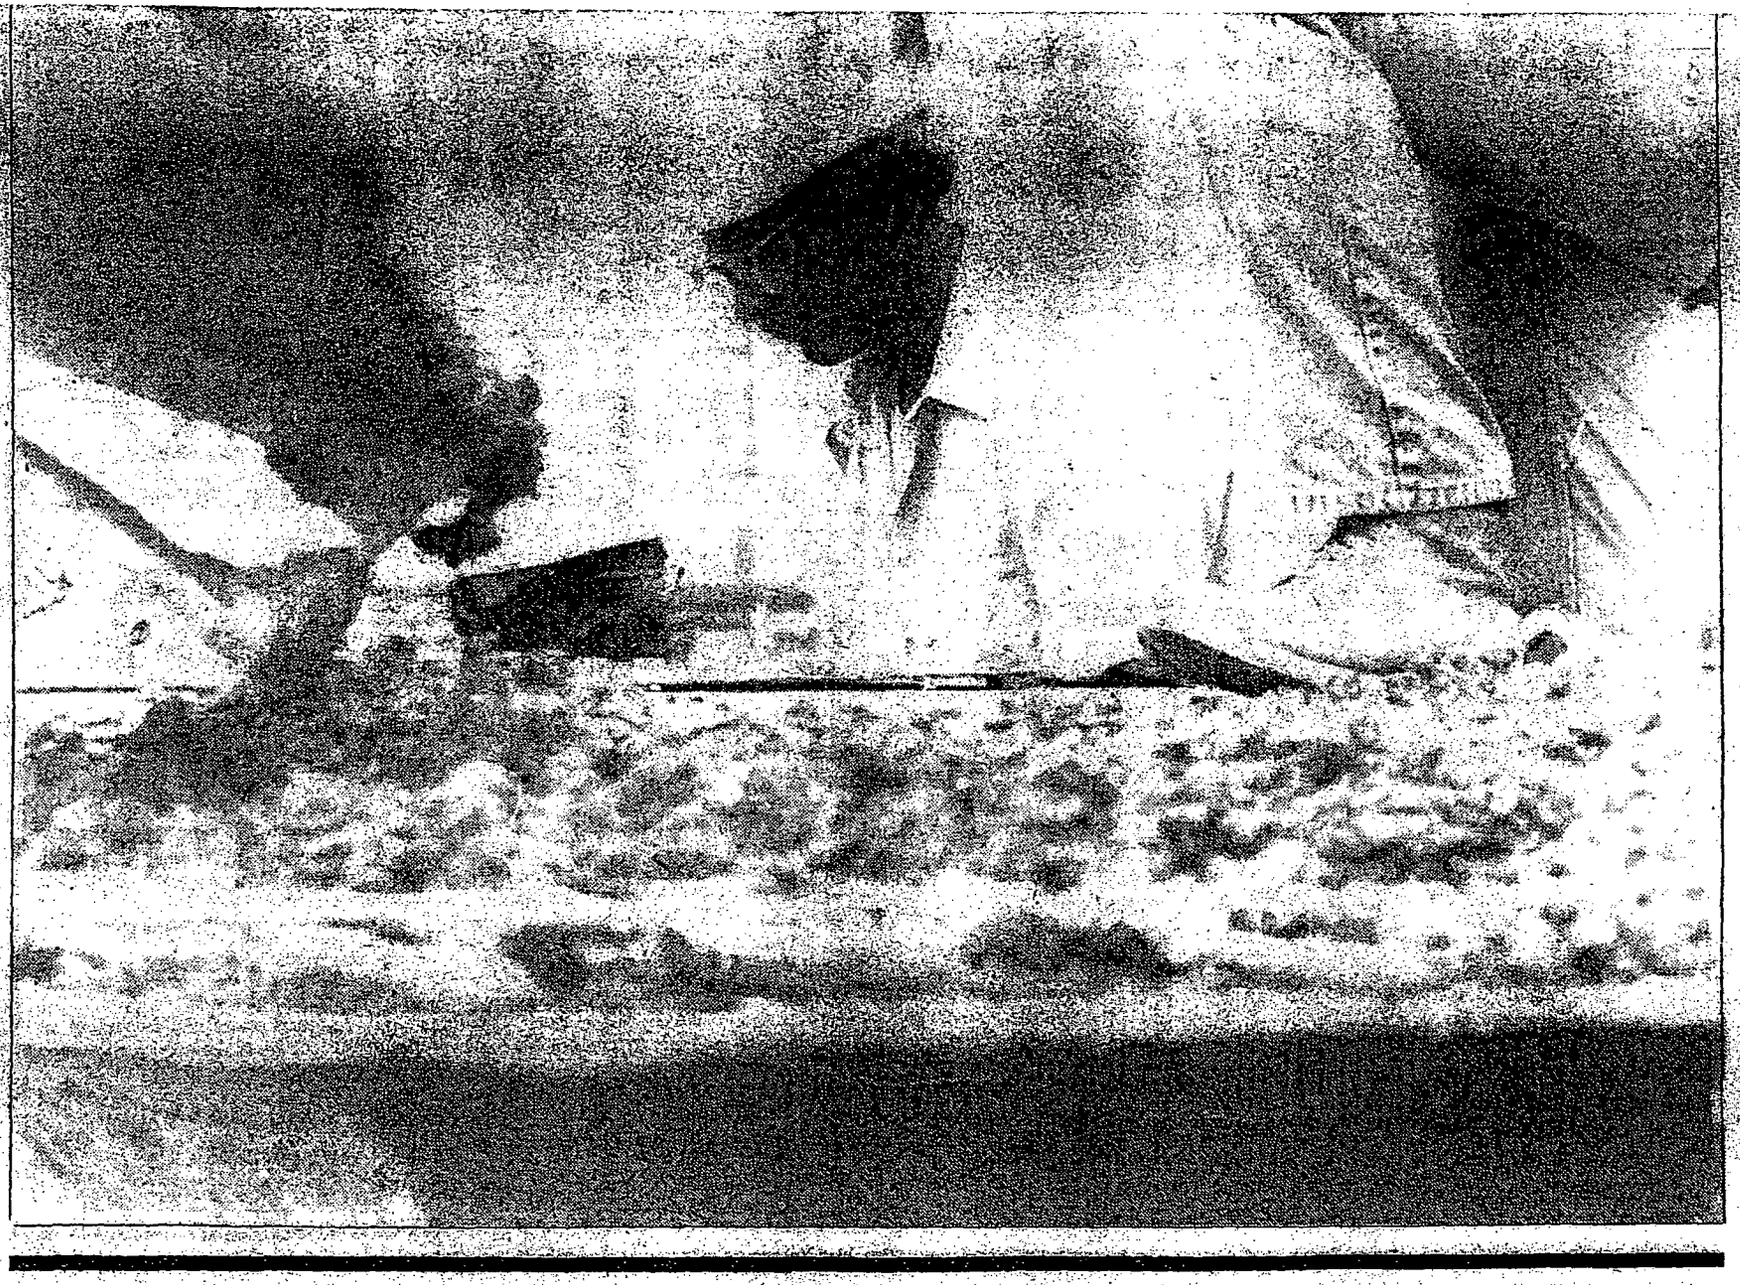

VOLUME 5, NUMBER 12 610 ACADEMY AVENUE, WAYNESBORO, GEORGIA 30830 SATURDAY, JUNE 7, 1986

related items, the tournament doesn't draw a lot of expert fishermen. What it does draw is a lot of parent-child teams looking for a good day's fishing, a little bit of fun and a lot of togetherness.

The tournament begins at 8 a.m. and ends at 5 p.m., but anyone [illegible] take part may register and begin fishing anytime during the day. [illegible]

The Vogtle Report

PROJECT MANPOWER
Jobsite Staffing as of March 23

		CHANGE FROM Feb. 23
Nuclear Construction		
GPC, Subcontractors and Construction Support (BPC)	1,043	—19
Contractors Staff	1,627	—19
Westinghouse Staff	132	N/C
Contractors Craft	7,168	—51
Westinghouse Craft	254	+2
Other Nuclear Construction Support		
Specialty Contractor Staff	56	+19
Specialty Contractor Craft	140	+40
PPG	701	+86
Total Construction/Construction Support	11,121	+57
Subtotal Nuclear Operations	2,047	+176
Subtotal Project Services	606	+84
Oglethorpe Power	4	N/C
Total Jobsite Manpower	13,778	+317
Bechtel LA/SCS	476	—42
TOTAL PROJECT STAFFING	14,254	+275
Prudency	0	0

BULK QUANTITY INSTALLATION
Through March 1986

Commodity	Percent Complete
UNIT 1	
Concrete (CY)	100
Backfill (CY)	95
Large Pipe (LF)	99
Large Hangers (EA)	96
Small Pipe (LF)	94
Small Hangers (EA)	81
Tubing Hangers (EA)	56
Tubing (LF)	86
HVAC Duct (LB)	97
Cable Tray (LF)	99
Conduit — PVC (LF)	91
Conduit — Rigid (LF)	94
Wire & Cable (LF)	91
Terminations (EA)	69
Pullman Instruments (EA)	89
Cleveland Instruments (EA)	98
Coatings (SF)	87
UNIT 2	
Concrete (CY)	87
Large Pipe (LF)	68
Large Hangers (EA)	22
* Small Pipe (LF)	15
** Small Hangers (EA)	2
HVAC Duct (LB)	25
Cable Tray (LF)	29
Conduit — PVC (LF)	59
Conduit — Rigid (LF)	16
Wire & Cable (LF)	
Terminations (EA)	
Coatings (SF)	
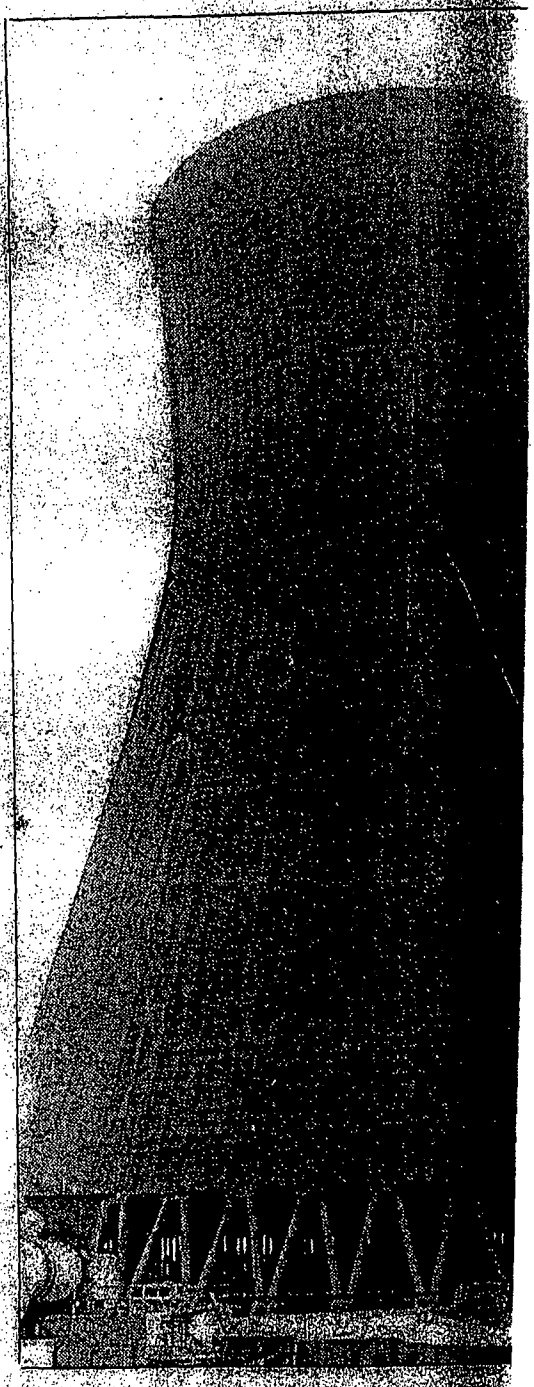
* Includes tubing
** Includes tubing hangers
