

March 7, 2000

MEMORANDUM TO: John Zwolinski, Director
Division of Licensing Project Management

THRU: Elinor Adensam, Director */RA/*
Project Directorate I
Division of Licensing Project Management

FROM: Richard Croteau, Project Manager */RA/*
Project Directorate I
Division of Licensing Project Management

SUBJECT: REPORT ON THE STATUS OF OPEN TIAs ASSIGNED TO NRR

The attached graphs and tables give the status of open TIAs assigned to NRR as of February 29, 2000. The first graph shows the status of total TIAs, those opened and closed. The second graph shows age of inventory. The first table gives summary data. Table 2 lists open TIAs by age, Table 3 shows closed TIAs. Attachment 1 lists open TIAs by plant name and gives details on issues and on delays in resolving them. TIAs completed since the last report are also shown. This update was provided by the project managers. The applicable review branches were given an opportunity to comment.

The office letter goal for FY2000 is to complete 95% of the TIAs by the original due date. Since the last status report, three TIAs have been completed (see Table 3). One of these (DC Cook MA7376/7) was not completed by the original due date negotiated with the region. For FY2000, NRR completed 19 of 21 within the original agreed-upon date for 90%.

There were no new TIAs. Of the 9 open TIAs, the following divisions are the current action holder: DSSA - 3, DE - 2, DIPM - 1, DRIP - 2 and DLPM - 3. Some TIAs may have more than one action holder.

cc w/atts: See next page

March 7, 2000

MEMORANDUM TO: John Zwolinski, Director
Division of Licensing Project Management

THRU: Elinor Adensam, Director */RA/*
Project Directorate
Division of Licensing Project Management

FROM: Richard Croteau, Project Manager */RA/*
Project Directorate I
Division of Licensing Project Management

SUBJECT: REPORT ON THE STATUS OF OPEN TIAs ASSIGNED TO NRR

The attached graphs and tables give the status of open TIAs assigned to NRR as of February 29, 2000. The first graph shows the status of total TIAs, those opened and closed. The second graph shows age of inventory. The first table gives summary data. Table 2 lists open TIAs by age, Table 3 shows closed TIAs. Attachment 1 lists open TIAs by plant name and gives details on issues and on delays in resolving them. TIAs completed since the last report are also shown. This update was provided by the project managers. The applicable review branches were given an opportunity to comment.

The office letter goal for FY2000 is to complete 95% of the TIAs by the original due date. Since the last status report, three TIAs have been completed (see Table 3). One of these (DC Cook MA7376/7) was not completed by the original due date negotiated with the region. For FY2000, NRR completed 19 of 21 within the original agreed-upon date for 90%.

There were no new TIAs. Of the 9 open TIAs, the following divisions are the current action holder: DSSA - 3, DE - 2, DIPM - 1, DRIP - 2 and DLPM - 3. Some TIAs may have more than one action holder.

cc w/atts: See next page

DOCUMENT NAME: C:\Feb2000TIA.WPD

**To receive a copy of this document, indicate in the box: "C" = Copy without attachment/enclosure
"E" = Copy with attachment/enclosure "N" = No copy**


OFFICE	PM/PDI	E	PD/PDI	
NAME	RCroteau		EAdensam	
DATE	03/7/00		03/7/00	

Official Record Copy


cc w/attachments:

S. Collins
R. Zimmerman
B. Sheron
J. Johnson
T.P. Gwynn, RIV
J. Caldwell, RIII
B. Mallett, RII
C. Casto, RII
J. Wiggins, RI
R. Blough, RI
L. Plisco, RII
G. Grant, RIII
K. Brockman, RIV
W. Lanning, RI
J. Grobe, RIII
A. Howell, RIV
NRR BCs, SCs and PDs (by e-mail)
G. Holahan
J. Strosnider
B. Boger
D. Matthews
S. Black
M. Oprendeck, RI
J. Barnes, RII
R. Lanksbury, RIII
L. Yandell, RIV
M. Gamberoni

TIA STATUS

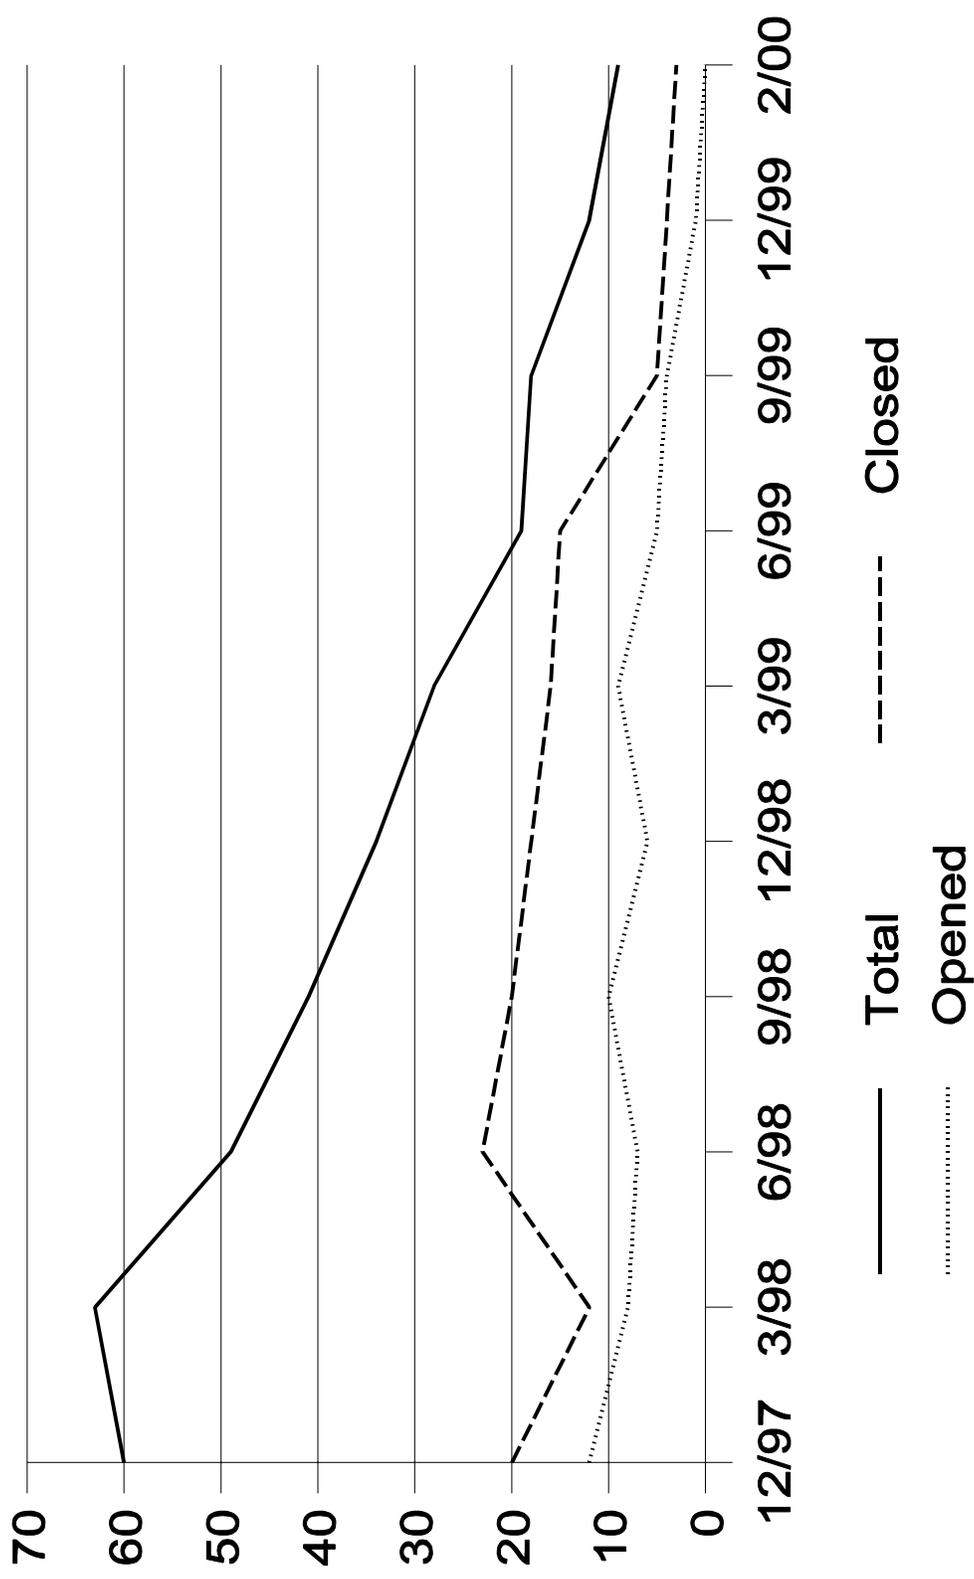

Average and Median Age of TIA Inventory

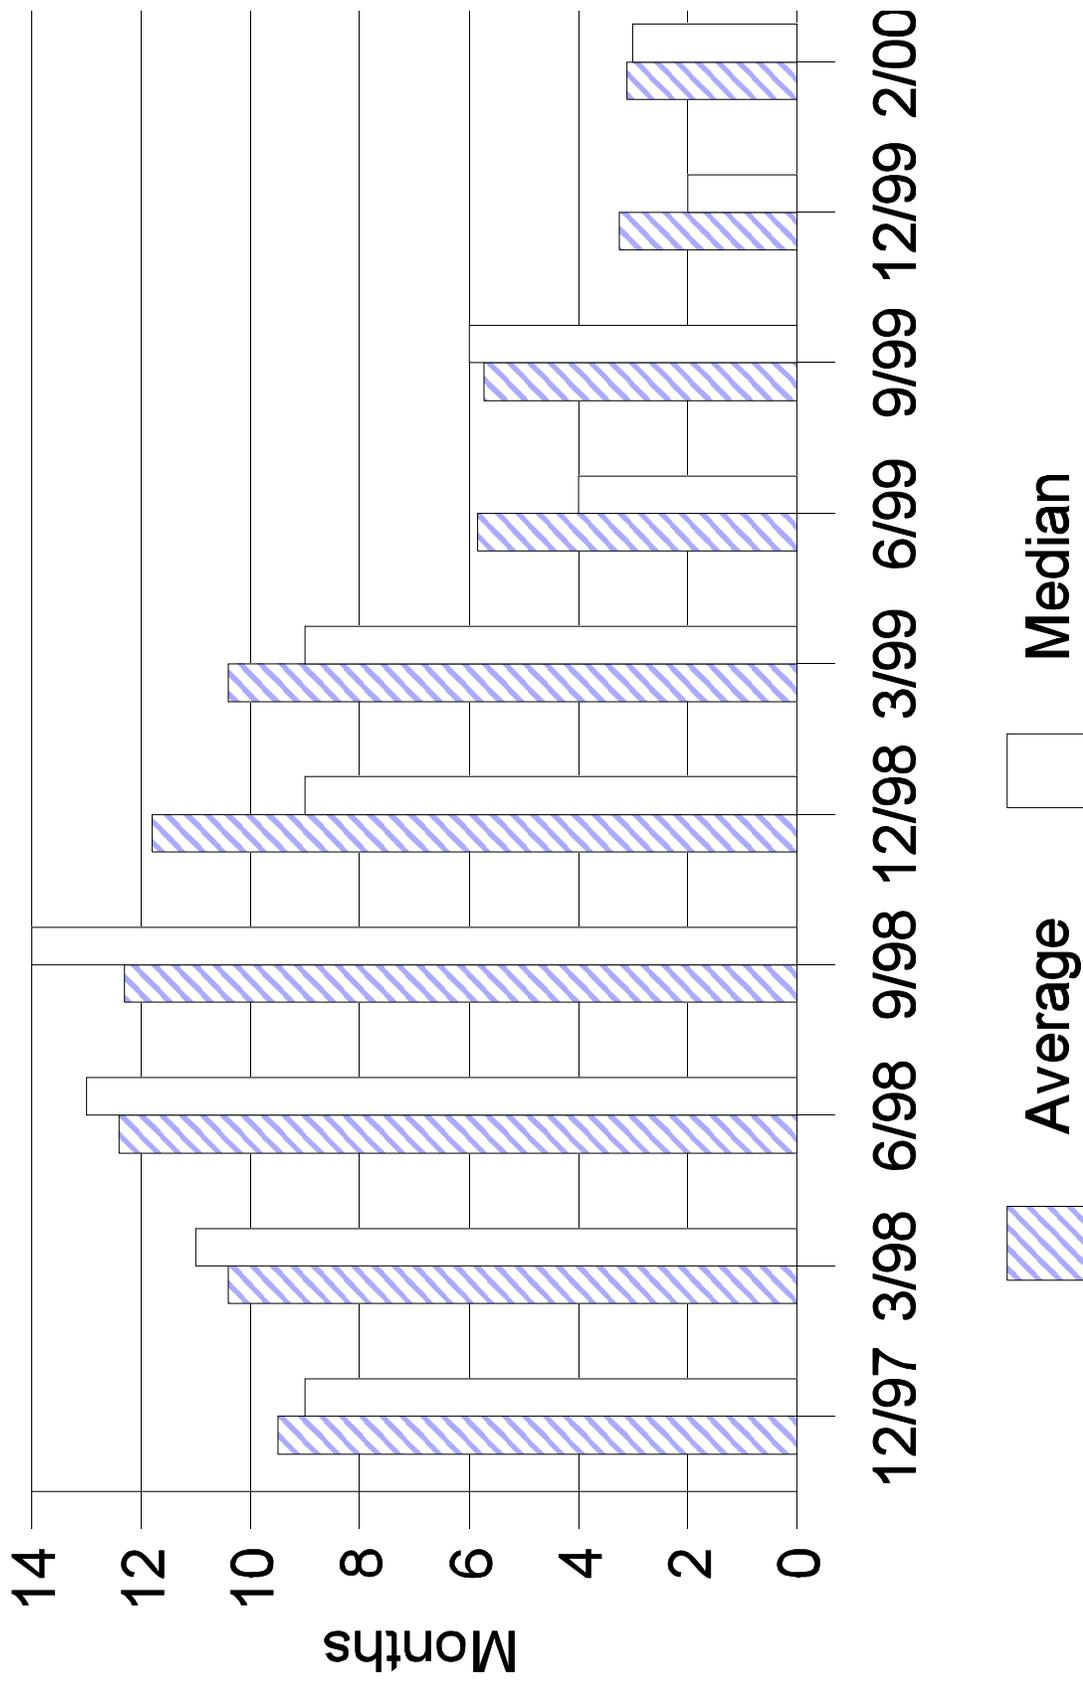

**TABLE 1 - SUMMARY DATA
AS OF FEBRUARY 29, 2000**

	New TIAs		Closed TIAs		Late TIAs FY-00	Total Inventory	Percent by Original Due Date
	FEB-00	FY-00	FEB-00	FY-00			
Region I	0	3	0	4	0	1	
Region II	0	3	0	5	1	3	
Region III	0	4	1	8	1	3	
Region IV	0	1	2	4	0	2	
Total	0	11	3	21	0	9	

* Operating Plan Goal is to complete 95% by originally agreed-upon date

Table 2

OPEN TIAs ASSIGNED TO NRR (by age)

TIA NO.	TAC NO.	DATE OF INITIAL REQUEST	EXPECTED COMPLETION DATE	AGE (Months)	PLANT	HOURS BILLED TO DATE
99-13	MA6662	9/21/99	3/31/00	5	BRUNSWICK	19.5
99-21	MA6664	9/27/99	3/27/00	5	WATERFORD	89.5
99-29	MA6907	10/22/99	2/11/00 - Late	4	KEWAUNEE	187.5
99-23	MA7122	11/3/99	5/15/00	3	WATERFORD 3	89.5
99-24	MA7247	11/23/99	5/23/00	3	BRUNSWICK 1	22
99-28	MA7235	11/23/99	2/15/00 - Late	3	HARRIS	128.5
2000-01	MA7271	12/8/99	6/8/00	2	GINNA	129.5
99-30	MA7367	12/9/99	7/1/00	2	MONTICELLO	3
99-32	MA7943	1/4/00	6/15/00	1	PALISADES	54.5
			AGE (Mos)	3.11	AVE Hours Billed	80.39

**TABLE 3
CLOSED TIAs ASSIGNED TO NRR - FY00 YTD**

TIA NO.	TAC NO.	DATE OF INITIAL REQUEST	DATE COMPLETED (w/i, due date)	AGE (Months)	PLANT	HOURS BILLED
99-26	MA6277	12/24/96	11/5/99	35	VERMONT YANKEE	11
99-27	MA6346/7	8/6/98	12/20/99	16	PEACH BOTTOM	21
98-09	MA2427/8	8/24/98	11/30/99	15	DRESDEN 2/3	460.2
98-11	MA4397/8	12/8/98	1/27/00 - Late	13	FARLEY	358.5
98-08	MA4165	11/2/98	10/6/99	11	WNP-2	74
98-11	MA4550/1	12/15/98	10/12/99	10	PT. BEACH 1/2	122
99-01	MA4729	1/26/99	11/3/99	10	PALISADES	169.9
99-01	MA4655/6	1/26/99	11/29/99	10	ST. LUCIE 1/2	355
99-03	MA4887/8	2/19/99	12/30/99	10	DC COOK 1/2	1
99-02	MA4999	2/25/99	12/13/99	9	SEQUOYAH 1	269
99-25	MA5040	2/17/99	11/17/99	9	VERMONT YANKEE	21.5
99-18	MA6004/5	6/21/99	2/22/00	8	ARKANSAS 1/2	146.7
99-03	MA5130/1	3/23/99	11/24/99	8	MCGUIRE 1/2	243.6
99-17	MA5408	5/4/99	2/14/00	8	WNP2	173
99-02	MA5115	3/23/99	10/29/99	7	DUANE ARNOLD	132.5
99-15	MA5688/9	6/21/99	12/15/99	5	ARKANSAS 1/2	147
99-06	MA5648	6/2/99	10/29/99	4	PERRY 1	70
99-31	MA7376/7	11/29/99	2/29/00 - Late	3	DC COOK	215
99-22	MA6455/6	10/8/99	1/28/00	3	FARLEY 1/2	83.5
99-20	MA6463	9/7/99	11/30/99	2	PERRY	15
	MA6381	9/15/99	11/15/99	2	OYSTER CREEK	78
			AGE (Mos)	9.43	AVE Hours Billed	150.83

Note: Completion dates are within the original agreed-upon date unless otherwise noted

RECENTLY CLOSED AND OPEN TIAs ASSIGNED TO NRR (by Plant Name)

PLANT	TIA NO.	TAC #	TITLE	MEMO DATE	TARGET COMPL. DATE	SE PROVIDED BY	CURRENT ACTION HOLDER	MEETING DUE DATE DEPENDS ON	STATUS/ OTHER REMARKS
ARKANSAS 1/2	99-18	MA6004/5	ANO Site Assembly/Evacuation	6/21/99	2/22/00C	IOHB - E. Fox	Complete	Complete	Complete
BRUNSWICK	99-13	MA6662	Dose calculation bypass leakage - control room and offsite	9/21/99	3/31/00	SPSB - J. Hays	SPSB	SPSB	Due date negotiated w/Reg
BRUNSWICK 1	99-24	MA7247	Rx pressure vessel heatup and cooldown curves	11/23/99	5/23/00	EMCB - M. Mitchell	EMCB DLPM Licensee	EMCB DLPM Licensee	Awaiting Licensee RAI Response
DC COOK 1/2	99-31	MA7376/7	Acceptability of non-safety cables	11/29/99	2/29/00C Late	EEIB - D. Thatcher	Complete	Complete	Complete (Late)
GINNA	00-01	MA7271	Operability of Check Valve	12/8/99	6/8/00	EMEB 1/24/00C SRXB 5/30/00T	SRXB	SRXB	Working. EMEB input to SRXB provided 1/24/00
HARRIS	99-28	MA7235	Resolution of Harris pilot fire protection inspection fire barrier qualification issues.	11/23/99	2/15/00 Late	SPLB	SPLB DLPM Region	SPLB DLPM Region	Draft response sent to region 2/17/00. Resolving comments and negotiating new due date.
KEWAUNEE	99-29	MA6907	PIV surveillance.	10/22/99	2/11/00 Late	RTSB - J. Foster	RTSB ADTP ADIP	RTSB ADTP ADIP	NRR management reviewing staff recommendations
MONTICELLO	99-30	MA7367	Reportability of RCIC Inoperability	12/9/99	7/1/00	RGEB - D. Allison	RGEB	RGEB	Due date negotiated w/Reg.
PALISADES	99-32	MA7943	Use of Non-EQ Cables in Containment	1/4/00	6/15/00	EEIB-J. Knox 5/1/00T	EEIB	EEIB	Due date negotiated w/Reg.

PLANT	TIA NO.	TAC #	TITLE	MEMO DATE	TARGET COMPL. DATE	SE PROVIDED BY	CURRENT ACTION HOLDER	MEETING DUE DATE DEPENDS ON	STATUS/ OTHER REMARKS
WATERFORD	99-21	MA6664	Auditor Independence Eval	9/27/99	3/27/00	IQMB	IQMB	IQMB	
WATERFORD	99-23	MA7122	Adequacy of automatic resequencing of non-safety related electrical loads to class 1E buses.	11/3/99	5/15/00	EEIB - A. Pal	DLPM Licensee	DLPM Licensee	Due date negotiated w/reg. RAI with Licensee.
WNP-2	99-17	MA5408	Iodine Release fraction calculation	5/4/99	2/14/00C	SPSB - Mark Blumberg 1/24/00C	Compete	Compete	Compete
