


Kaiser Aluminum & Chemical Corporation


| ID | Task Name | Start | Duration | 1999 | | 2000 | | 2001 | | 2002 | | 2003 | | 2004 | | 2005 | | 2006 | | 2007 | | 200 | |
|----|---|-----------------|-----------------|------|----|------|----|------|----|------|----|------|----|------|----|------|----|------|----|------|----|-----|----|
| | | | | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 |
| 1 | Review Phase 1 RAI | 06/10/99 | 0 days | | | | | | | | | | | | | | | | | | | | |
| 2 | Kaiser prepares response to RAI | 06/11/99 | 37 days | | | | | | | | | | | | | | | | | | | | |
| 3 | NRC reviews response to RAI | 08/03/99 | 1 day | | | | | | | | | | | | | | | | | | | | |
| 4 | FRN - EA-FONSI | 09/09/99 | 134 days | | | | | | | | | | | | | | | | | | | | |
| 5 | PM - Draft FRN | 09/09/99 | 90 days | | | | | | | | | | | | | | | | | | | | |
| 6 | LA - Review of FRN | 01/13/00 | 3 days | | | | | | | | | | | | | | | | | | | | |
| 7 | Concurrence | 01/18/00 | 25 days | | | | | | | | | | | | | | | | | | | | |
| 8 | Publish FRN | 03/08/00 | 5 days | | | | | | | | | | | | | | | | | | | | |
| 9 | Approve Phase 1 RP | 04/04/00 | 0 days | | | | | | | | | | | | | | | | | | | | |
| 10 | Phase 1 Site Decommissioning | 04/04/00 | 324 days | | | | | | | | | | | | | | | | | | | | |
| 11 | Pre-cleanup staging activities | 04/04/00 | 128 days | | | | | | | | | | | | | | | | | | | | |
| 12 | Kaiser Performs Cleanup | 09/29/00 | 136 days | | | | | | | | | | | | | | | | | | | | |
| 13 | Region in process confirmatory survey | 02/26/01 | 30 days | | | | | | | | | | | | | | | | | | | | |
| 14 | Kaiser prepare FSSR | 04/09/01 | 60 days | | | | | | | | | | | | | | | | | | | | |
| 15 | Review Final Site Survey Report (FSSR) | 07/02/01 | 164 days | | | | | | | | | | | | | | | | | | | | |
| 16 | FSSR - Acceptance Review | 07/02/01 | 88 days | | | | | | | | | | | | | | | | | | | | |
| 17 | PM - Acceptance Review | 07/02/01 | 12 days | | | | | | | | | | | | | | | | | | | | |
| 18 | Reject FSSR | 07/17/01 | 0 days | | | | | | | | | | | | | | | | | | | | |
| 19 | Kaiser revises FSSR | 07/18/01 | 30 days | | | | | | | | | | | | | | | | | | | | |
| 20 | PM Acceptance Review | 08/29/01 | 30 days | | | | | | | | | | | | | | | | | | | | |
| 21 | PM - Draft Letter | 10/10/01 | 5 days | | | | | | | | | | | | | | | | | | | | |
| 22 | Concurrence | 10/17/01 | 10 days | | | | | | | | | | | | | | | | | | | | |

Kaiser Aluminum & Chemical Corporation

| ID | Task Name | Start | Duration | 1999 | | 2000 | | 2001 | | 2002 | | 2003 | | 2004 | | 2005 | | 2006 | | 2007 | | 200 | |
|----|--|-----------------|-----------------|------|----|------|----|------|----|------|----|------|----|------|----|------|----|------|----|------|----|-----|----|
| | | | | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 |
| 23 | Issue letter to Kaiser | 10/31/01 | 1 day | | | | | | | | | | | | | | | | | | | | |
| 24 | FSSR - Technical Review | 11/01/01 | 76 days | | | | | | | | | | | | | | | | | | | | |
| 25 | PM - Technical Review | 11/01/01 | 60 days | | | | | | | | | | | | | | | | | | | | |
| 26 | PM - Draft Letter | 01/24/02 | 5 days | | | | | | | | | | | | | | | | | | | | |
| 27 | Concurrence | 01/31/02 | 10 days | | | | | | | | | | | | | | | | | | | | |
| 28 | Issue letter to Kaiser | 02/14/02 | 1 day | | | | | | | | | | | | | | | | | | | | |
| 29 | Off-site Acceptable for Release | 02/15/02 | 1 day | | | | | | | | | | | | | | | | | | | | |
| 30 | Phase II DP - Review | 05/25/01 | 345 days | | | | | | | | | | | | | | | | | | | | |
| 31 | DP - Acceptance Review | 05/25/01 | 53 days | | | | | | | | | | | | | | | | | | | | |
| 32 | Receive DP | 05/25/01 | 0 days | | | | | | | | | | | | | | | | | | | | |
| 33 | PM - Acceptance Review | 05/25/01 | 47 days | | | | | | | | | | | | | | | | | | | | |
| 34 | PM - Draft Letter | 07/31/01 | 3 days | | | | | | | | | | | | | | | | | | | | |
| 35 | Concurrence | 08/03/01 | 2 days | | | | | | | | | | | | | | | | | | | | |
| 36 | Issue letter to Kaiser | 08/07/01 | 1 day | | | | | | | | | | | | | | | | | | | | |
| 37 | Publish Federal Register Notice (FRN) | 09/17/01 | 23 days | | | | | | | | | | | | | | | | | | | | |
| 38 | PM - Draft FRN | 09/17/01 | 5 days | | | | | | | | | | | | | | | | | | | | |
| 39 | LA - Review of FRN | 09/24/01 | 3 days | | | | | | | | | | | | | | | | | | | | |
| 40 | Concurrence | 09/27/01 | 10 days | | | | | | | | | | | | | | | | | | | | |
| 41 | Publish FRN | 10/11/01 | 5 days | | | | | | | | | | | | | | | | | | | | |
| 42 | Phase II DP - Technical Review | 08/08/01 | 134 days | | | | | | | | | | | | | | | | | | | | |
| 43 | Develop Review Plan | 08/08/01 | 24 days | | | | | | | | | | | | | | | | | | | | |
| 44 | PM - Prepare Task Plan | 08/08/01 | 8 days | | | | | | | | | | | | | | | | | | | | |




| ID | Task Name | Start | Duration | 1999 | | 2000 | | 2001 | | 2002 | | 2003 | | 2004 | | 2005 | | 2006 | | 2007 | | 2008 |
|----|---------------------------------------|-----------------|-----------------|------|----|------|----|------|----|------|----|------|----|------|----|------|----|------|----|------|----|------|
| | | | | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 |
| 45 | SL - Review Task Plan | 08/20/01 | 5 days | | | | | | | | | | | | | | | | | | | |
| 46 | PM - Prepare TAR | 08/27/01 | 5 days | | | | | | | | | | | | | | | | | | | |
| 47 | TAR concurrence | 09/03/01 | 5 days | | | | | | | | | | | | | | | | | | | |
| 48 | Issue TAR | 09/10/01 | 1 day | | | | | | | | | | | | | | | | | | | |
| 49 | Evaluate Decommissioning Plan | 09/11/01 | 110 days | | | | | | | | | | | | | | | | | | | |
| 50 | Review SRP 1 - Executive Summary | 09/11/01 | 5 days | | | | | | | | | | | | | | | | | | | |
| 51 | Review SRP 2 - Facility Operating Hi | 09/18/01 | 5 days | | | | | | | | | | | | | | | | | | | |
| 52 | Review SRP 3 - Facility Description | 09/25/01 | 5 days | | | | | | | | | | | | | | | | | | | |
| 53 | Review SRP 4 - Facility Radiological | 10/02/01 | 5 days | | | | | | | | | | | | | | | | | | | |
| 54 | Review SRP 5 - Dose Assessment | 09/11/01 | 90 days | | | | | | | | | | | | | | | | | | | |
| 55 | Review SRP 6 - Alternatives Analysis | 10/09/01 | 5 days | | | | | | | | | | | | | | | | | | | |
| 56 | Review SRP 7 - ALARA | 10/16/01 | 10 days | | | | | | | | | | | | | | | | | | | |
| 57 | Review SRP 8 - Planned Decom Acti | 10/30/01 | 10 days | | | | | | | | | | | | | | | | | | | |
| 58 | Review SRP 9 - Project Management | 11/13/01 | 5 days | | | | | | | | | | | | | | | | | | | |
| 59 | Review SRP 10 - Health & Safety Pla | 11/20/01 | 10 days | | | | | | | | | | | | | | | | | | | |
| 60 | Review SRP 11 - Envir. Monitoring PI | 12/04/01 | 10 days | | | | | | | | | | | | | | | | | | | |
| 61 | Review SRP 12 - Rad Waste Mgnt | 12/18/01 | 5 days | | | | | | | | | | | | | | | | | | | |
| 62 | Review SRP 13 - QA Program | 12/25/01 | 5 days | | | | | | | | | | | | | | | | | | | |
| 63 | Review SRP 14 - Radiation Surveys | 01/01/02 | 10 days | | | | | | | | | | | | | | | | | | | |
| 64 | Review SRP 15 - Financial Assuranc | 01/15/02 | 15 days | | | | | | | | | | | | | | | | | | | |
| 65 | Review SRP 16 - Restricted Use | 02/05/02 | 5 days | | | | | | | | | | | | | | | | | | | |
| 66 | Develop RAI / Resolve Comments | 02/12/02 | 112 days | | | | | | | | | | | | | | | | | | | |




Kaiser Aluminum & Chemical Corporation

| ID | Task Name | Start | Duration | 1999 | | 2000 | | 2001 | | 2002 | | 2003 | | 2004 | | 2005 | | 2006 | | 2007 | | 200 | |
|----|---------------------------------------|-----------------|-----------------|------|----|------|----|------|----|------|----|------|----|------|----|------|----|------|----|------|----|-----|----|
| | | | | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 |
| 67 | Develop TER | 02/12/02 | 35 days | | | | | | | | | | | | | | | | | | | | |
| 68 | Review TER | 04/02/02 | 5 days | | | | | | | | | | | | | | | | | | | | |
| 69 | Meet with Kaiser to discuss concerns | 04/09/02 | 1 day | | | | | | | | | | | | | | | | | | | | |
| 70 | Draft questions/comments | 04/10/02 | 10 days | | | | | | | | | | | | | | | | | | | | |
| 71 | Review questions/comments | 04/24/02 | 10 days | | | | | | | | | | | | | | | | | | | | |
| 72 | Issue comment letter | 05/08/02 | 1 day | | | | | | | | | | | | | | | | | | | | |
| 73 | Kaiser review RAI | 05/09/02 | 45 days | | | | | | | | | | | | | | | | | | | | |
| 74 | Review Kaiser response to RAI | 07/11/02 | 5 days | | | | | | | | | | | | | | | | | | | | |
| 75 | Prepare EA - SER - FONSI | 07/18/02 | 46 days | | | | | | | | | | | | | | | | | | | | |
| 76 | Prepare draft EA, SER, FONSI | 07/18/02 | 30 days | | | | | | | | | | | | | | | | | | | | |
| 77 | Review draft EA, SER, FONSI | 08/29/02 | 10 days | | | | | | | | | | | | | | | | | | | | |
| 78 | Revise draft EA, SER, FONSI | 09/12/02 | 3 days | | | | | | | | | | | | | | | | | | | | |
| 79 | Finalize EA, SER, FONSI | 09/17/02 | 1 day | | | | | | | | | | | | | | | | | | | | |
| 80 | Publish FRN | 09/18/02 | 1 day | | | | | | | | | | | | | | | | | | | | |
| 81 | Approve Phase 2 DP | 09/19/02 | 1 day | | | | | | | | | | | | | | | | | | | | |
| 82 | Site Decommissioning | 09/20/02 | 936 days | | | | | | | | | | | | | | | | | | | | |
| 83 | Kaiser performs cleanup | 09/20/02 | 700 days | | | | | | | | | | | | | | | | | | | | |
| 84 | Region in-process confirmatory survey | 05/27/05 | 30 days | | | | | | | | | | | | | | | | | | | | |
| 85 | Kaiser prepares FSSR | 07/08/05 | 30 days | | | | | | | | | | | | | | | | | | | | |
| 86 | Review FSSR | 08/19/05 | 176 days | | | | | | | | | | | | | | | | | | | | |
| 87 | FSSR - Acceptance Review | 08/19/05 | 19 days | | | | | | | | | | | | | | | | | | | | |
| 88 | PM - acceptance review | 08/19/05 | 5 days | | | | | | | | | | | | | | | | | | | | |

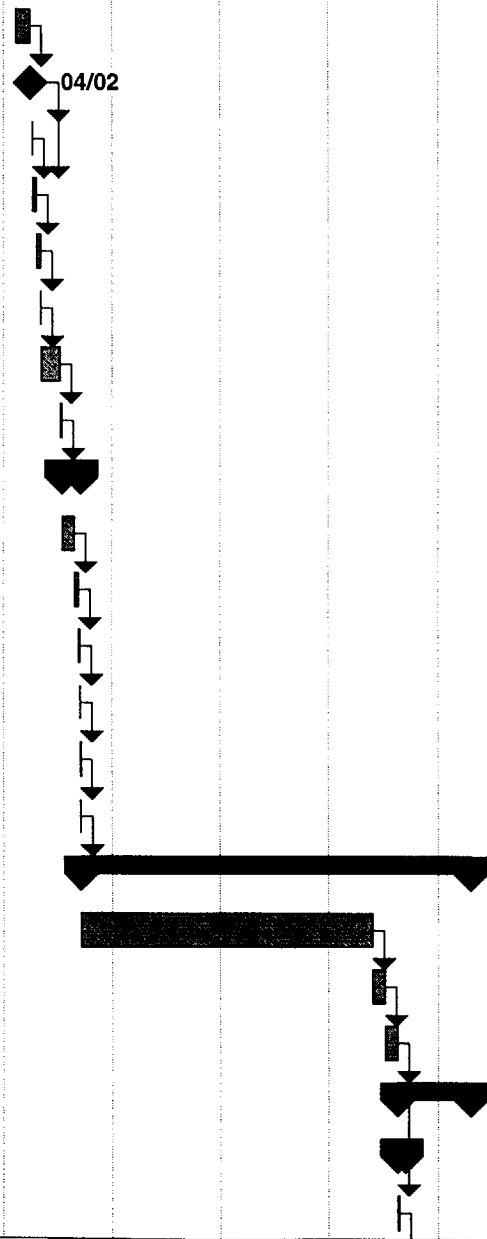

Kaiser Aluminum & Chemical Corporation

| ID | Task Name | Start | Duration | 1999 | | 2000 | | 2001 | | 2002 | | 2003 | | 2004 | | 2005 | | 2006 | | 2007 | | 200 |
|-----|---|-----------------|-----------------|------|----|------|----|------|----|------|----|------|----|------|----|------|----|------|----|------|----|-----|
| | | | | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 |
| 89 | PM - draft letter | 08/26/05 | 3 days | | | | | | | | | | | | | | | | | | | |
| 90 | Concurrence | 08/31/05 | 10 days | | | | | | | | | | | | | | | | | | | |
| 91 | Issue letter to Kaiser | 09/14/05 | 1 day | | | | | | | | | | | | | | | | | | | |
| 92 | FSSR - Technicial review | 09/15/05 | 156 days | | | | | | | | | | | | | | | | | | | |
| 93 | PM - technicial review | 09/15/05 | 60 days | | | | | | | | | | | | | | | | | | | |
| 94 | Complete FSSR review | 12/07/05 | 0 days | | | | | | | | | | | | | | | | | | | |
| 95 | Develop FSSR TER and FSSR RAI | 12/08/05 | 30 days | | | | | | | | | | | | | | | | | | | |
| 96 | Kaiser prepares response to RAI | 01/19/06 | 30 days | | | | | | | | | | | | | | | | | | | |
| 97 | NRC reviews response to RAI | 03/02/06 | 20 days | | | | | | | | | | | | | | | | | | | |
| 98 | PM - draft letter | 03/30/06 | 5 days | | | | | | | | | | | | | | | | | | | |
| 99 | Concurrence | 04/06/06 | 10 days | | | | | | | | | | | | | | | | | | | |
| 100 | Issue letter to Kaiser | 04/20/06 | 1 day | | | | | | | | | | | | | | | | | | | |
| 101 | Site acceptable for release | 04/21/06 | 1 day | | | | | | | | | | | | | | | | | | | |
| 102 | Remove Site From SDMP | 04/24/06 | 88 days | | | | | | | | | | | | | | | | | | | |
| 103 | Prepare Commission Paper | 04/24/06 | 33 days | | | | | | | | | | | | | | | | | | | |
| 104 | PM - prepare Commission Paper Outline | 04/24/06 | 3 days | | | | | | | | | | | | | | | | | | | |
| 105 | Management review | 04/27/06 | 5 days | | | | | | | | | | | | | | | | | | | |
| 106 | PM - draft Commission Paper | 05/04/06 | 15 days | | | | | | | | | | | | | | | | | | | |
| 107 | Concurrence | 05/25/06 | 10 days | | | | | | | | | | | | | | | | | | | |
| 108 | Prepare FRN to remove site from SDMP | 06/08/06 | 18 days | | | | | | | | | | | | | | | | | | | |
| 109 | PM - draft FRN | 06/08/06 | 5 days | | | | | | | | | | | | | | | | | | | |
| 110 | LA - review FRN | 06/15/06 | 3 days | | | | | | | | | | | | | | | | | | | |



Kaiser Aluminum & Chemical Corporation

| ID | Task Name | Start | Duration | 1999 | | 2000 | | 2001 | | 2002 | | 2003 | | 2004 | | 2005 | | 2006 | | 2007 | | 200 |
|-----|---|-----------------|----------------|------|----|------|----|------|----|------|----|------|----|------|----|------|----|------|----|------|----|-----|
| | | | | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 | H2 | H1 |
| 111 | Concurrence | 06/20/06 | 10 days | | | | | | | | | | | | | | | | | | | |
| 112 | Prepare Letters to State & EPA | 07/04/06 | 15 days | | | | | | | | | | | | | | | | | | | |
| 113 | PM - draft letter to State/EPA | 07/04/06 | 5 days | | | | | | | | | | | | | | | | | | | |
| 114 | Concurrence | 07/11/06 | 10 days | | | | | | | | | | | | | | | | | | | |
| 115 | Issue Commission Paper | 07/25/06 | 1 day | | | | | | | | | | | | | | | | | | | |
| 116 | Commission Review | 07/26/06 | 15 days | | | | | | | | | | | | | | | | | | | |
| 117 | Publish FRN & issue letters | 08/16/06 | 5 days | | | | | | | | | | | | | | | | | | | |
| 118 | Release site | 08/23/06 | 1 day | | | | | | | | | | | | | | | | | | | |

