

August 17, 2012

Dominion 6/7/2012

North Anna 3 COLA

Meeting Presentation:


US – APWR DCWG

Licensing Actions

This schedule graphic contains public information about the NRC review schedules for the three US-APWR DCWG licensing actions and Dominion's assumptions regarding those activities.

Note: Issuance of the R-COL and S-COL is staggered one and two months, respectively, after issuance of the DCD

**US-APWR DCWG Licensing Actions**

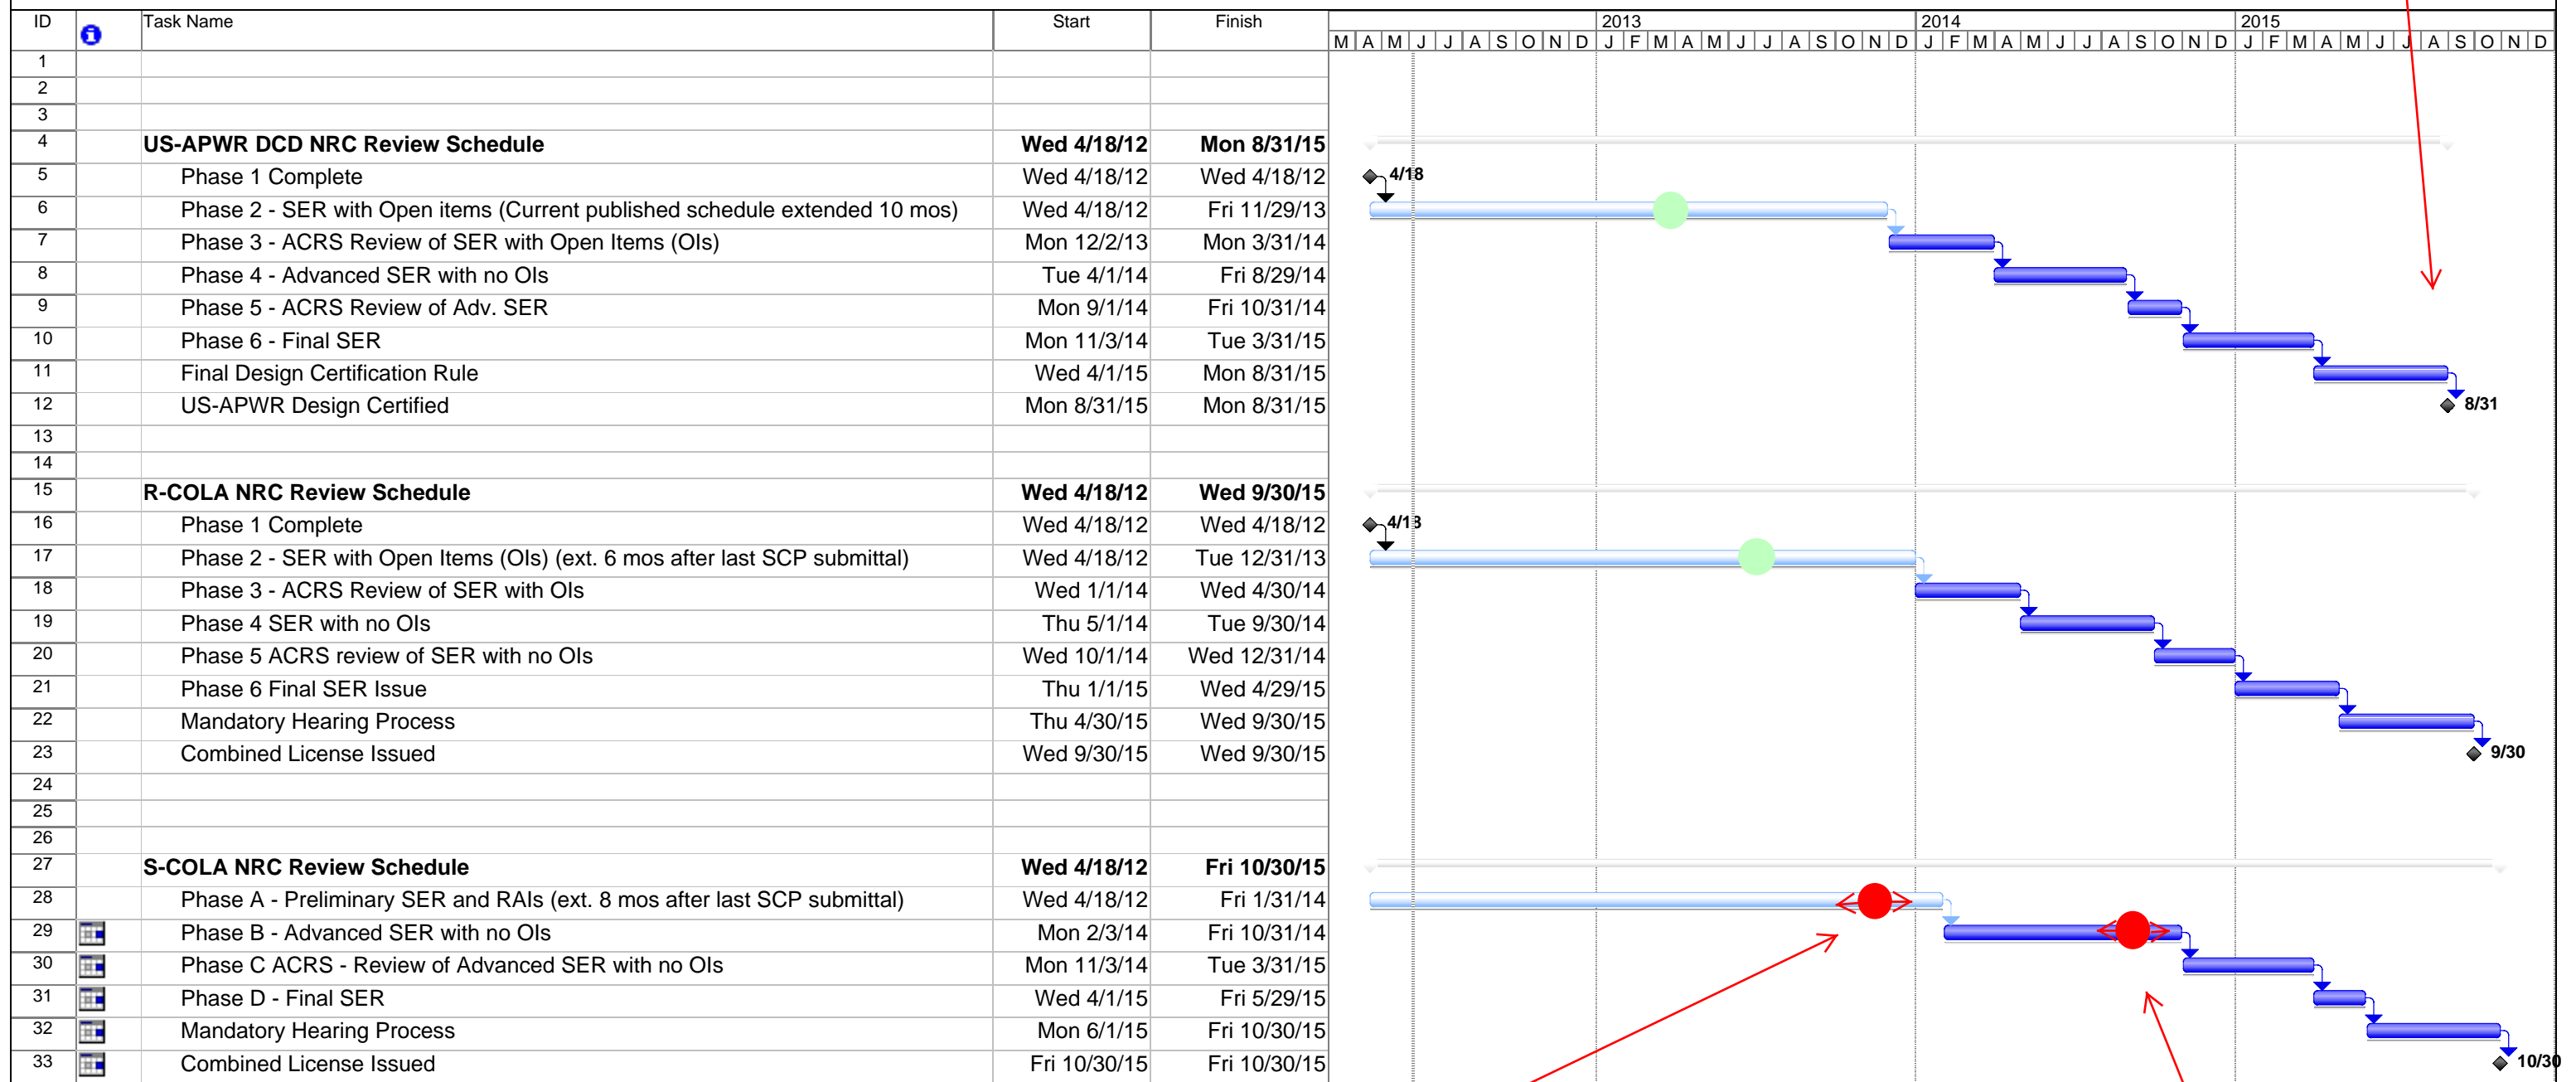

Project: 052212 USAPWR DCWG Lic Date: Tue 6/5/12

Task: [Blue Bar] Progress [Grey Bar] Summary [Grey Bar] External Tasks [Grey Bar] Deadline [Green Arrow]

Split: [Dotted Bar] Milestone [Diamond] Project Summary [Grey Bar] External Milestone [Diamond]

**Legend:**  
 Red Ball - Indicates target timeframe for S-COLA revision  
 Green Ball - Indicates planned DCD or R-COLA revision  
 Light Blue Line - Current NRC review phase  
 Dark Blue Line - Later NRC review phases. Phase durations consistent with latest published schedules.

A S-COLA revision targeted in late 2013 is proposed in order to:  
 \* Maximize the opportunity to incorporate new or revised information driven by DCD Rev. 4 (planned for submittal in March 2013)  
 \* Reflect the results of NRC's review of Dominion's various seismic closure plan (SCP) submittals scheduled from July 2012 to May 2013  
 \* Incorporate the results of Dominion responses to NRC SCP-related RAIs

This COLA revision would serve as the basis for entry into Phase B

A S-COLA revision targeted in late Summer or early Fall 2014 is proposed in order to:  
 \* Reflect the resolution of the open items dispositioned during the Phase B NRC review  
 \* Provide adequate time for NRC to conduct confirmatory reviews of any outstanding items that NRC would expect to see in the S-COLA revision

This COLA revision would serve as the basis for entry into Phase C
