



U.S.NRC

UNITED STATES NUCLEAR REGULATORY COMMISSION

Protecting People and the Environment

**CIP Public Meeting
October 1, 2018**

Vogtle Readiness Group (VRG) Update

Ayo Ayegbusi

Victor Hall

NRO/DCIP

Vogtle Readiness Group

- VRG serves as the focal point for project status and for coordination among Region II, NRO, NRR, NSIR, and OGC through commercial operation of Vogtle Units 3 and 4. Oversee the Vogtle Units 3 and 4 Transition to Operations
- In addition, the VRG serves as the hub for communications with the Commission, the Executive Director for Operations and its office direct reports, the licensee, and other external stakeholders
- Identify and resolve any licensing, inspection, or regulatory challenges or gaps that could impact the schedule for completion of Vogtle Units 3 and 4.

Integrated Project Plan


- VRG directed the formation of an internal NRC working group to develop an Integrated Project Plan (IPP) scheduling tool
- The IPP lists the regulatory milestones for the transition of Vogtle’s construction to operations

Integrated Project Plan

- The tool will allow the working group to map the milestones' inter-dependencies and ties to NRC's inspection schedule
- The VRG will use the IPP to track scheduled activities and identify potential critical path areas related to the completion of construction

Integrated Project Plan

- Innovative and technology driven
 - First of a kind at NRC
 - Uses Primavera software
- Enhances communication
 - Internal and external
- Reduces project risks
 - NRC internal processes are known
 - Increases stakeholder confidence

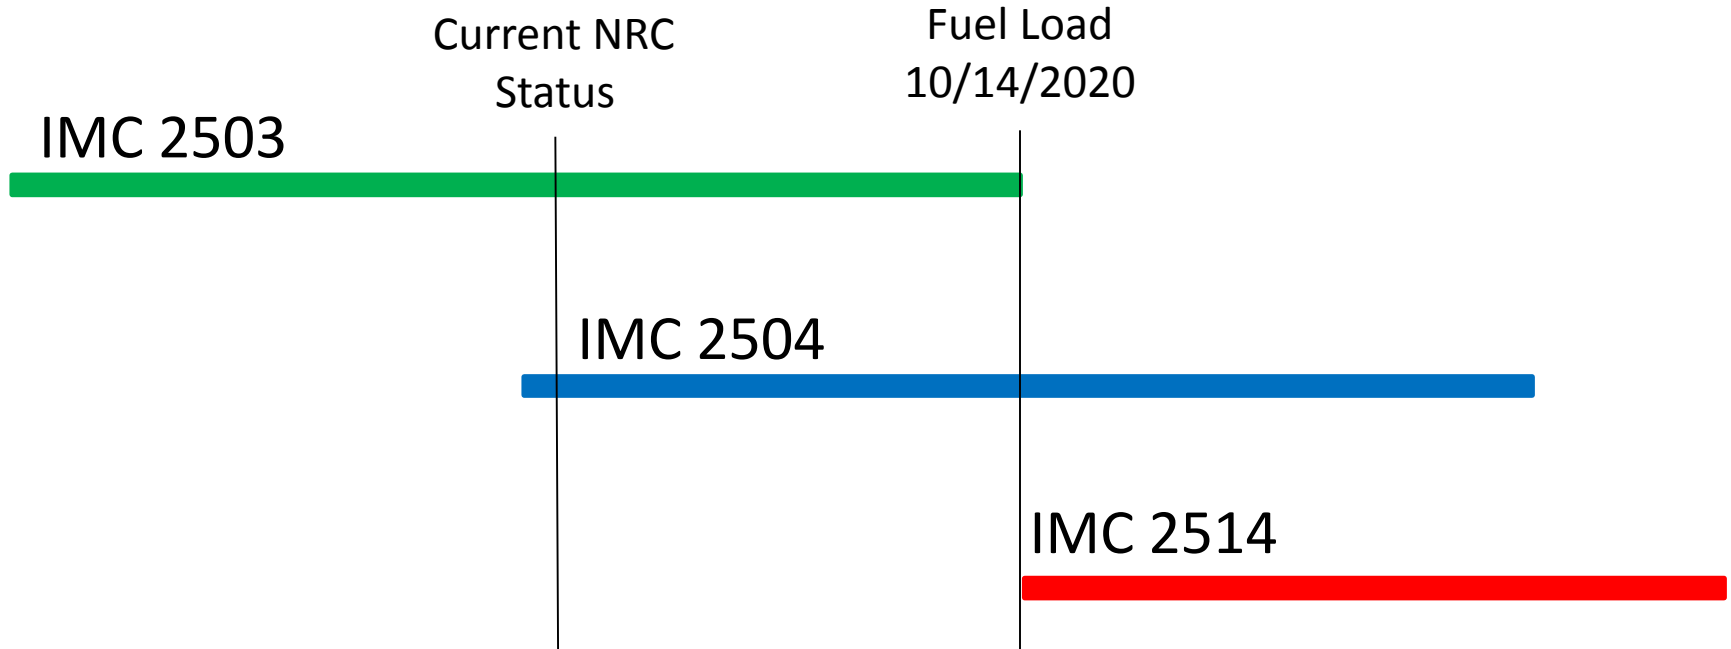

Upcoming NRC Schedule Items

- Continue to inspect construction activities
- Finalize 103(g) sequence of events
- Continue implementation of IMC 2504
- Complete development of IMC 2514

Questions?
